ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(पूर्ववर्ती पावर सिस्टम ऑपरेशन कार्पोरेशन लिमिटेड)
GRID CONTROLLER OF INDIA LIMITED
(Formerly known as Power System Operation Corporation Limited)
CIN: U40105DL2009GOI188682 | राष्ट्रीय भार प्रेषण केंद्र: प्रथम तल, बी-9, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली – 110016
National Load Dispatch Centre: First Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi – 110016

संदर्भ संख्या:- **GRID-INDIA/NLDC/MR/** दिनांक: **24.05.2024**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट **– अप्रैल 2024**

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, **अप्रैल 2024** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

Sd/-
एस. बनर्जी
मुख्य महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्न: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 मुख्य महाप्रबंधक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Chief General Manager, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



अप्रैल 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह अप्रैल 2024 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF APRIL -2024


पृष्ठसूची CONTENTS

1	माह अप्रैल 2024 की सारांश रिपोर्ट Summary of report for the month of APRIL 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	30 अप्रैल के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 30-APRIL (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अप्रैल 2023 से तुलना Energy requirement and met comparison with APRIL 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अप्रैल 2023 से तुलना Peak demand requirement and met comparison with APRIL 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-39
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	40-42
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	43
18	पावर मार्केट की सूचना Power market information	44-49
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	50-52
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	53-63
21	नए कमीशंड पारेषण तत्व New elements commissioned	64
22	विभव रूपरेखा Voltage profile	65
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह अप्रैल 2024 तक All Time Highest (Demand & Energy) figures: Till APRIL 2024	66
24	अप्रैल 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for APRIL 2024	67

1. SUMMARY OF REPORT FOR THE MONTH OF APRIL-2024


EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

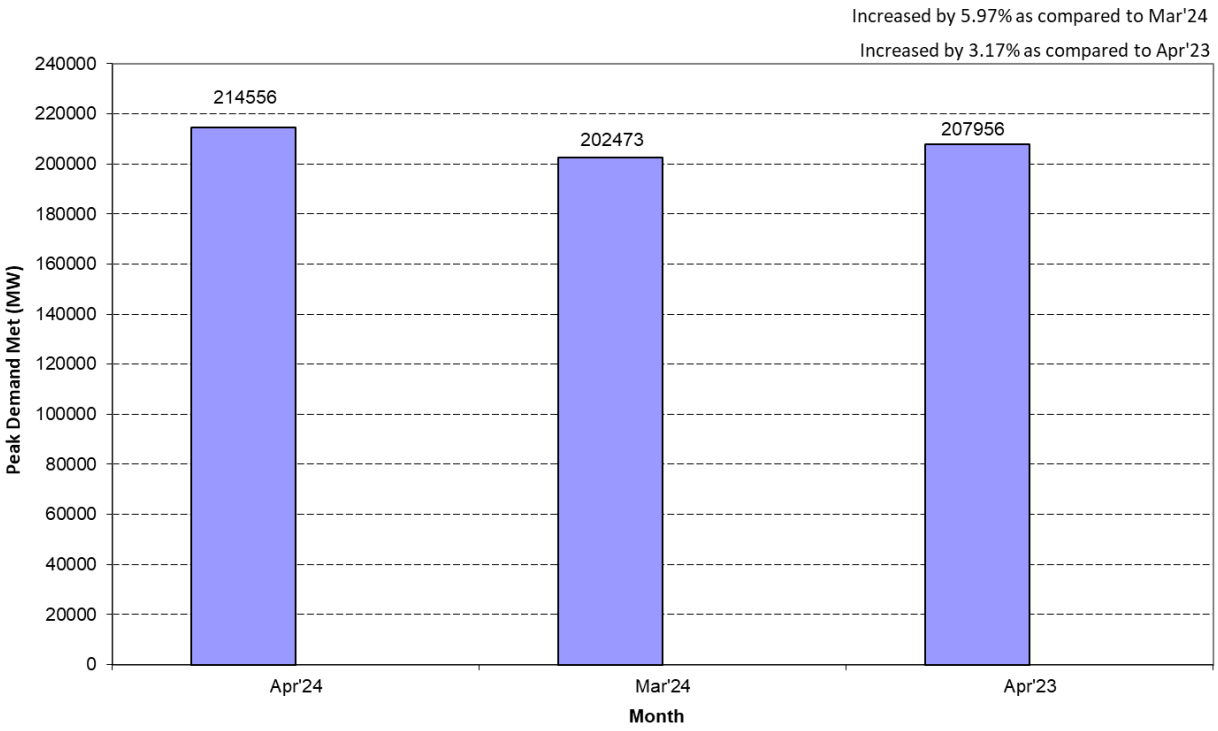


Frequency within IEGC Band

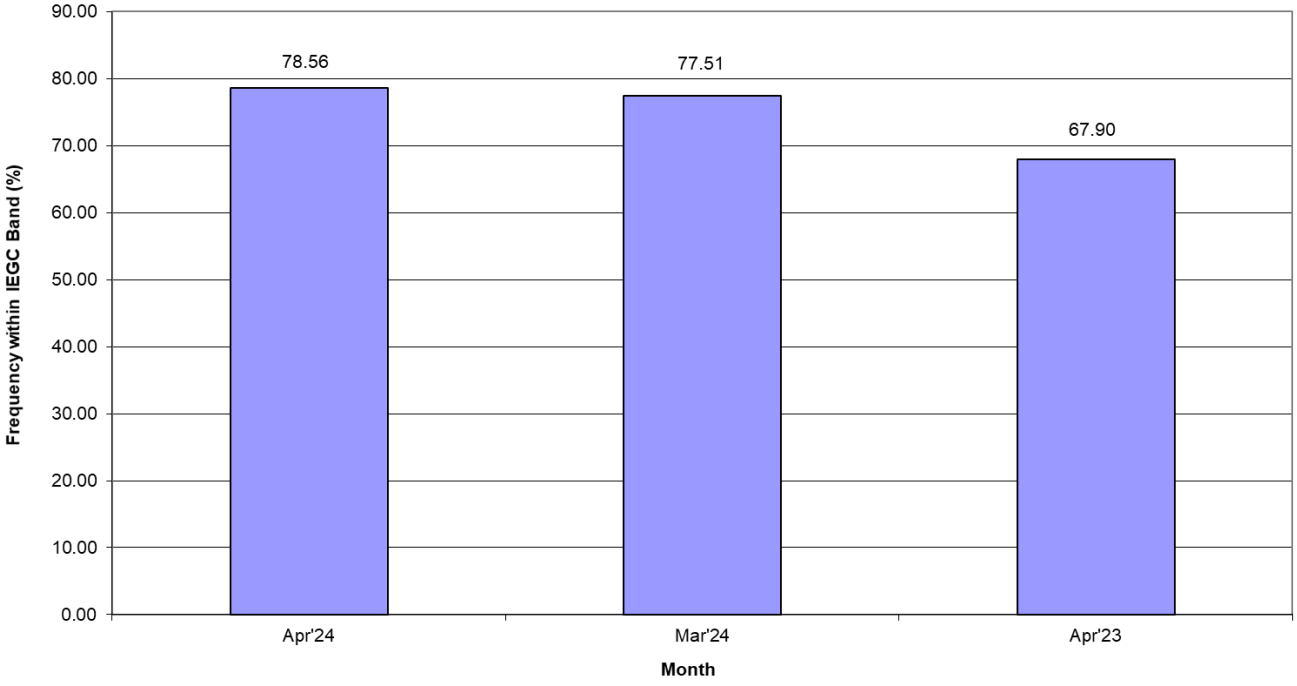


ENERGY MET AT NATIONAL LEVEL (MU)

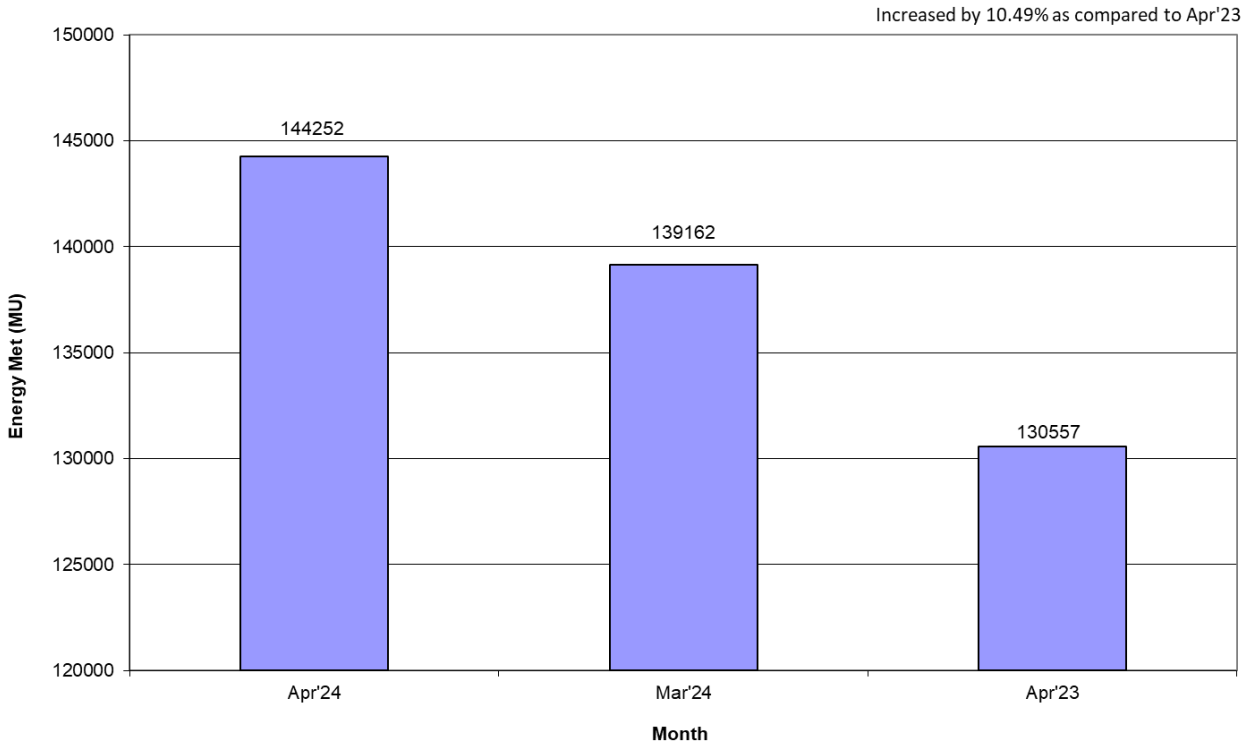


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

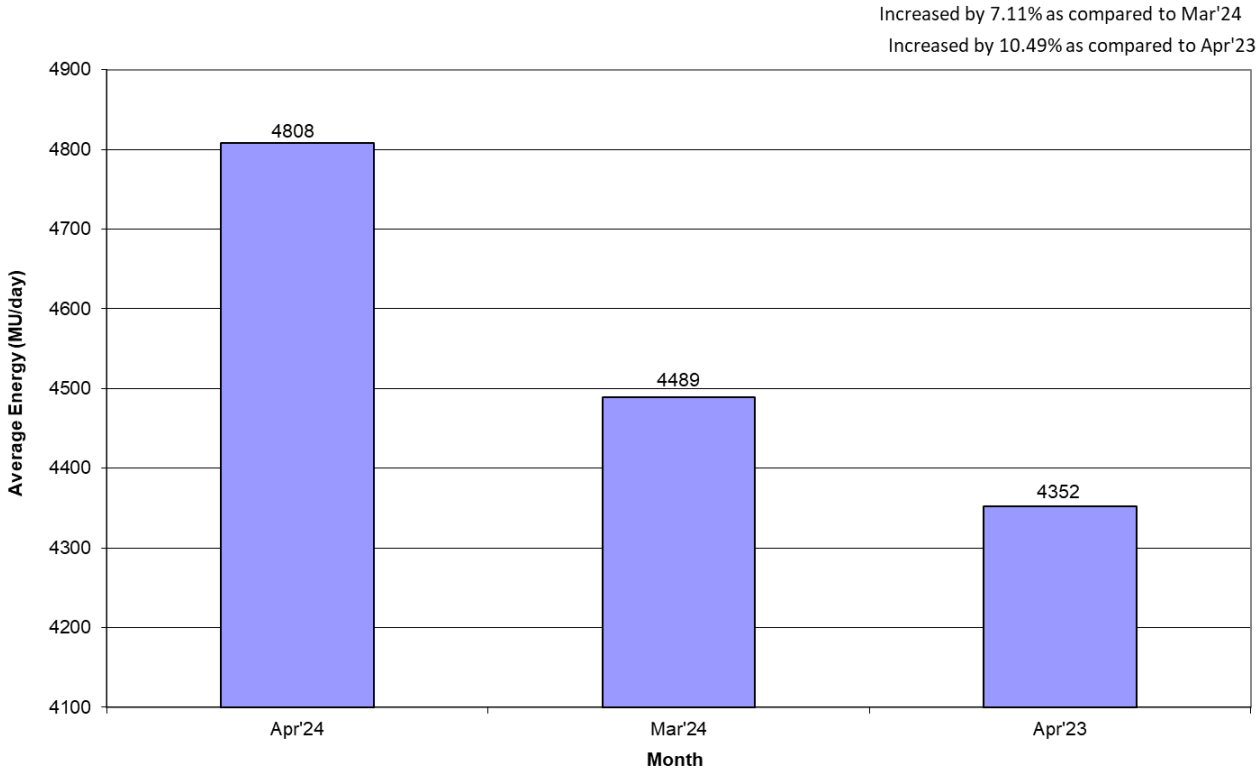


HYDRO GENERATION AT NATIONAL LEVEL (MU)

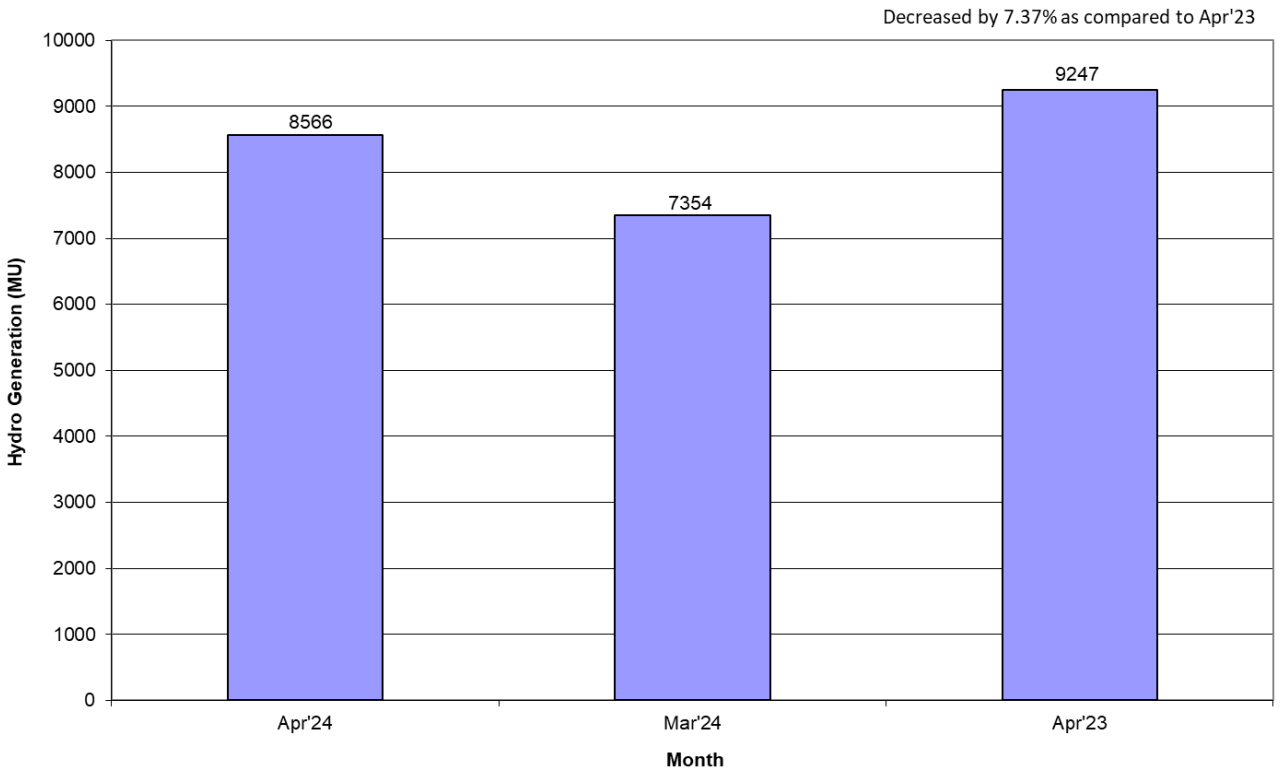


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

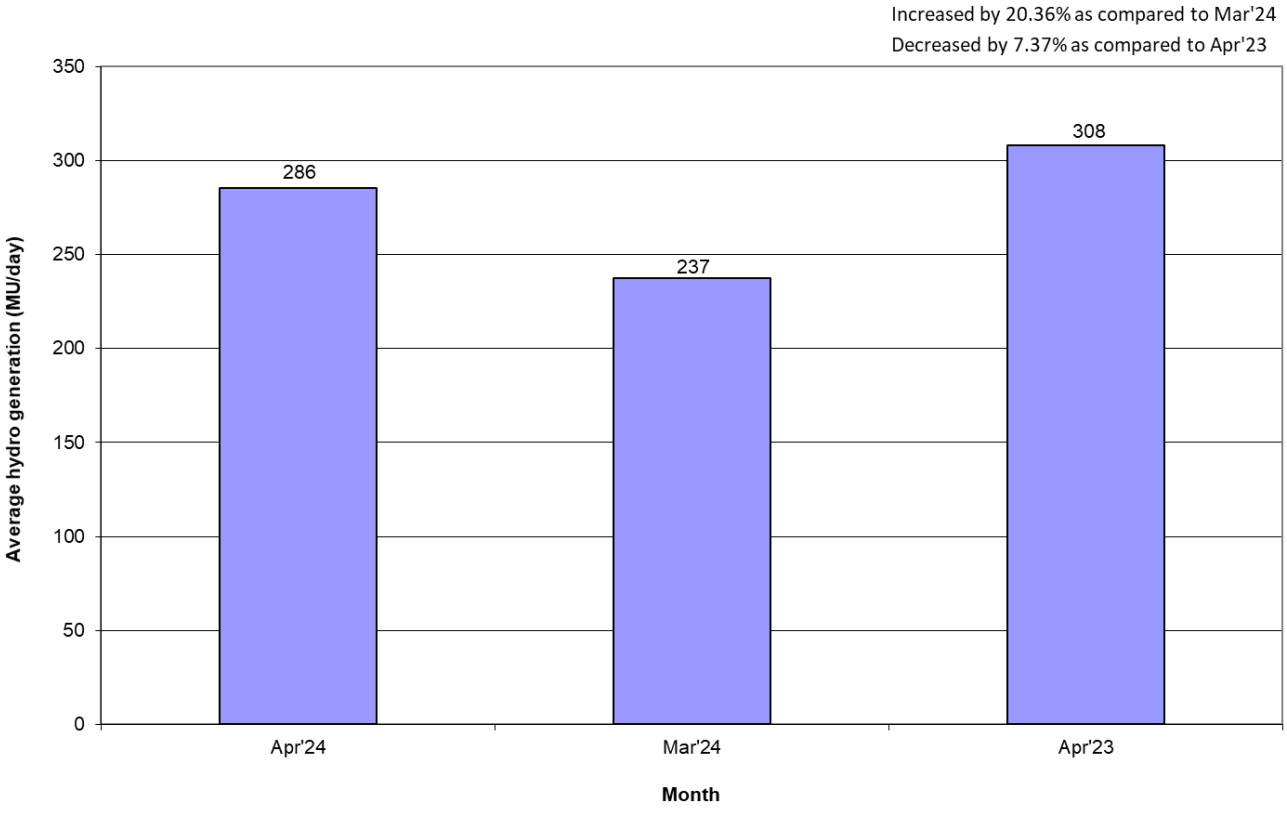


WIND GENERATION AT NATIONAL LEVEL (MU)

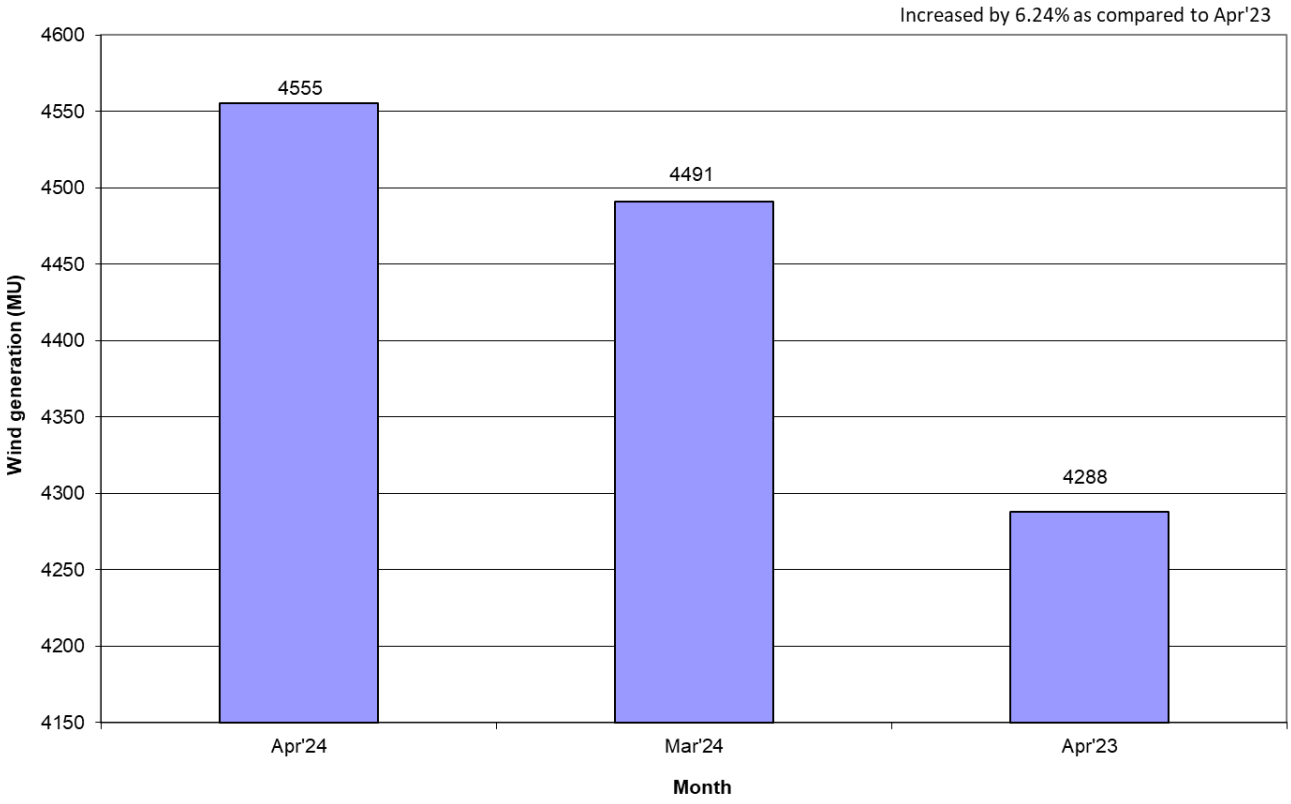


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

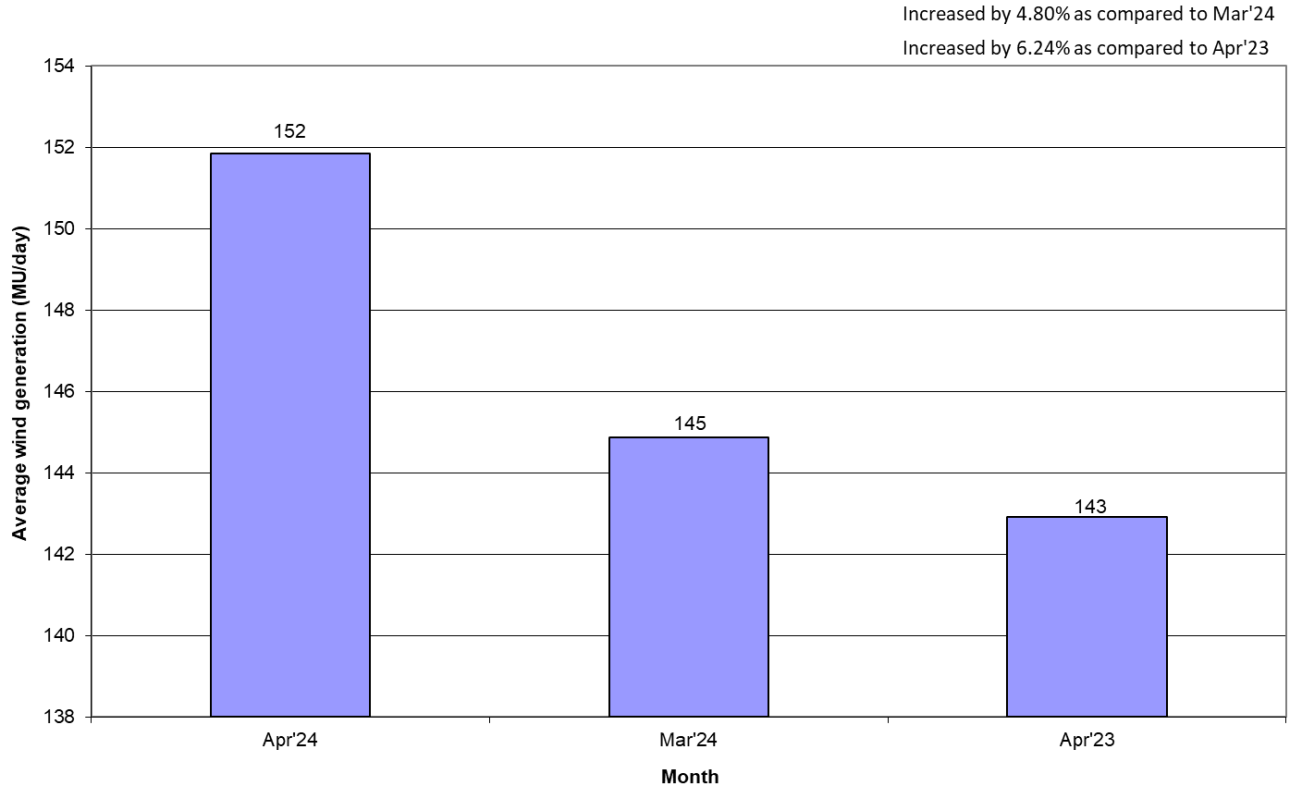

SOLAR GENERATION AT NATIONAL LEVEL (MU)

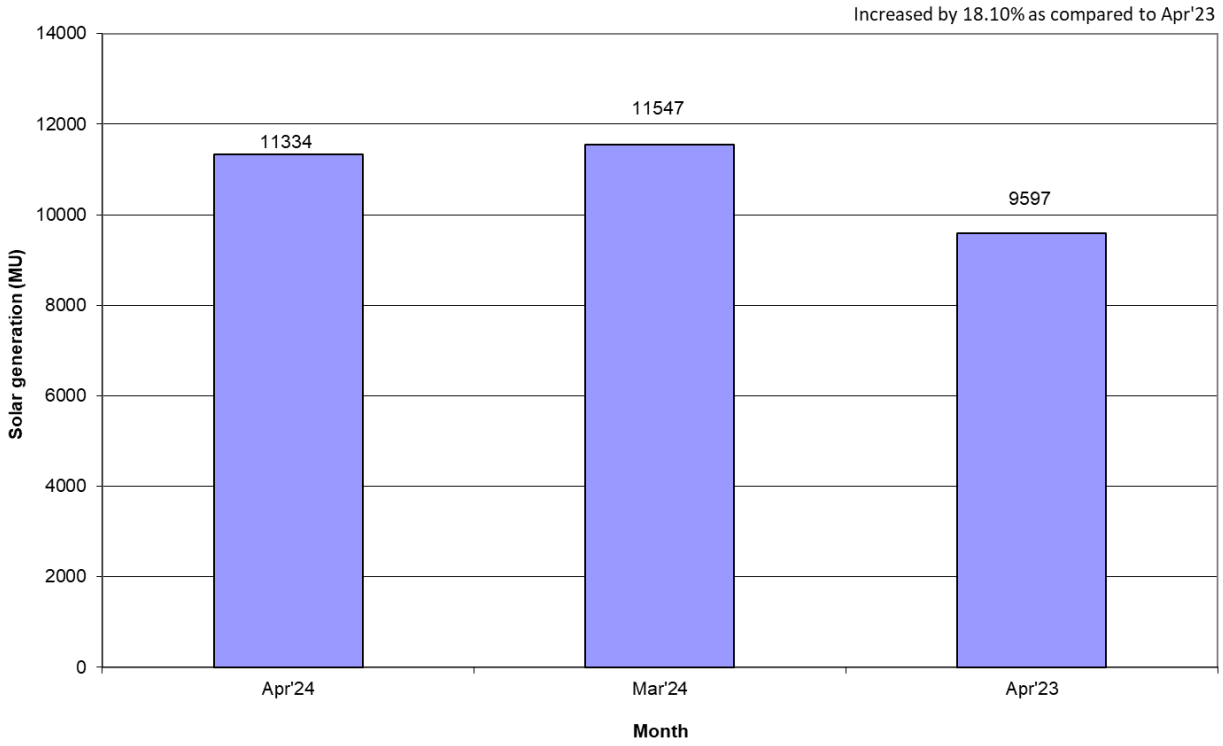

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

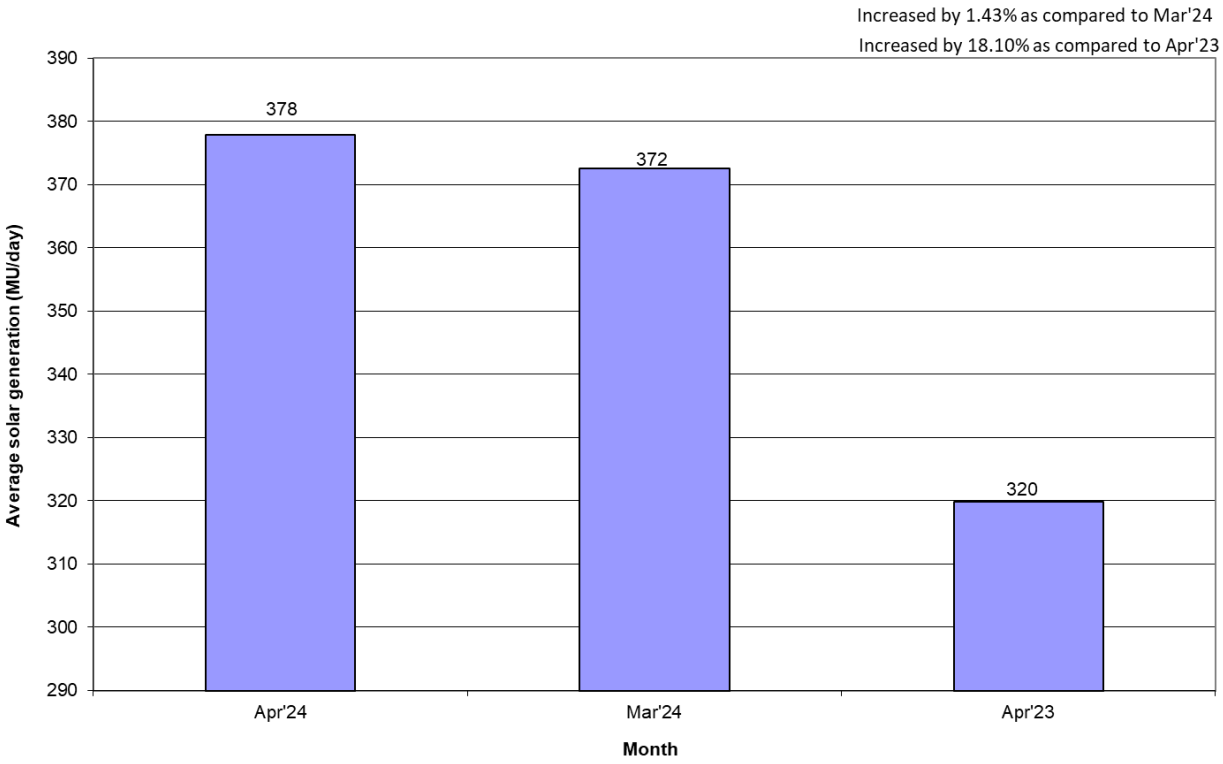

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 30.04.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56951	1580	5995	0	64526	1620	20830	38652	125628
2	WR	74663	1400	10806	0	86869	3240	7563	49144	146816
3	SR	49717	3640	6272	434	60063	3320	11827	54329	129539
4	ER	28690	0	80	0	28770	0	4764	2010	35544
5	NER	949	0	1665	36	2650	0	1944	576	5170
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	210969	6620	24818	589	242997	8180	46928	144752	442857

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति

EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: अप्रैल 2024 MONTH:- APR 2024


सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Apr-24	52106	62332	52587	26044	2558	195627
2-Apr-24	53540	63663	53256	26001	2713	199173
3-Apr-24	54769	64359	53970	27483	2850	203431
4-Apr-24	55165	65135	53789	27064	2794	203947
5-Apr-24	55788	65282	53981	28505	2781	206337
6-Apr-24	56083	64828	53736	27771	2921	205339
7-Apr-24	53488	60789	50474	23968	2604	191323
8-Apr-24	56130	63099	53079	25000	3018	200326
9-Apr-24	57331	61008	50775	25995	3027	198136
10-Apr-24	56130	60622	51883	26063	2808	197506
11-Apr-24	55375	60471	50805	24123	2905	193679
12-Apr-24	57612	59856	50664	25626	2938	196696
13-Apr-24	54178	60218	49716	24633	2886	191631
14-Apr-24	52970	59883	47033	25674	2922	188482
15-Apr-24	57516	64331	52555	27916	3031	205349
16-Apr-24	58592	64718	53642	28330	2781	208063
17-Apr-24	57634	63551	53884	26336	2545	203950
18-Apr-24	58237	66509	52748	27713	2778	207985
19-Apr-24	59035	66236	50476	28982	2480	207209
20-Apr-24	59825	62914	51661	28374	2539	205313
21-Apr-24	57516	61291	48322	27285	2704	197118
22-Apr-24	61273	62114	52840	27217	2903	206347
23-Apr-24	56334	61642	52771	27713	3004	201464
24-Apr-24	61310	64278	52978	27735	2957	209258
25-Apr-24	62731	65747	54098	28029	3088	213693
26-Apr-24	58090	63194	53203	28371	2838	205696
27-Apr-24	62001	65382	53625	28098	2876	211982
28-Apr-24	61382	62745	50700	27854	2425	205106
29-Apr-24	61003	66793	54798	28465	3005	214064
30-Apr-24	61837	66392	54581	28957	2789	214556
उच्चतम MAXIMUM	62731	66793	54798	28982	3088	214556
निम्नतम MINIMUM	52106	59856	47033	23968	2425	188482
औसत AVERAGE	57499	63313	52288	27044	2816	202960
अब तक का उच्चतम All Time Max.	76274	**66793**	**54798**	**28982**	3510	215592
दिनांक Date	04.09.23	**29.04.24**	**29.04.24**	**19.04.24**	12.08.22	28.08.23

नोट : सभी आंकड़े 2000 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND (2000hrs) MET DURING THE MONTH OF APRIL 2024

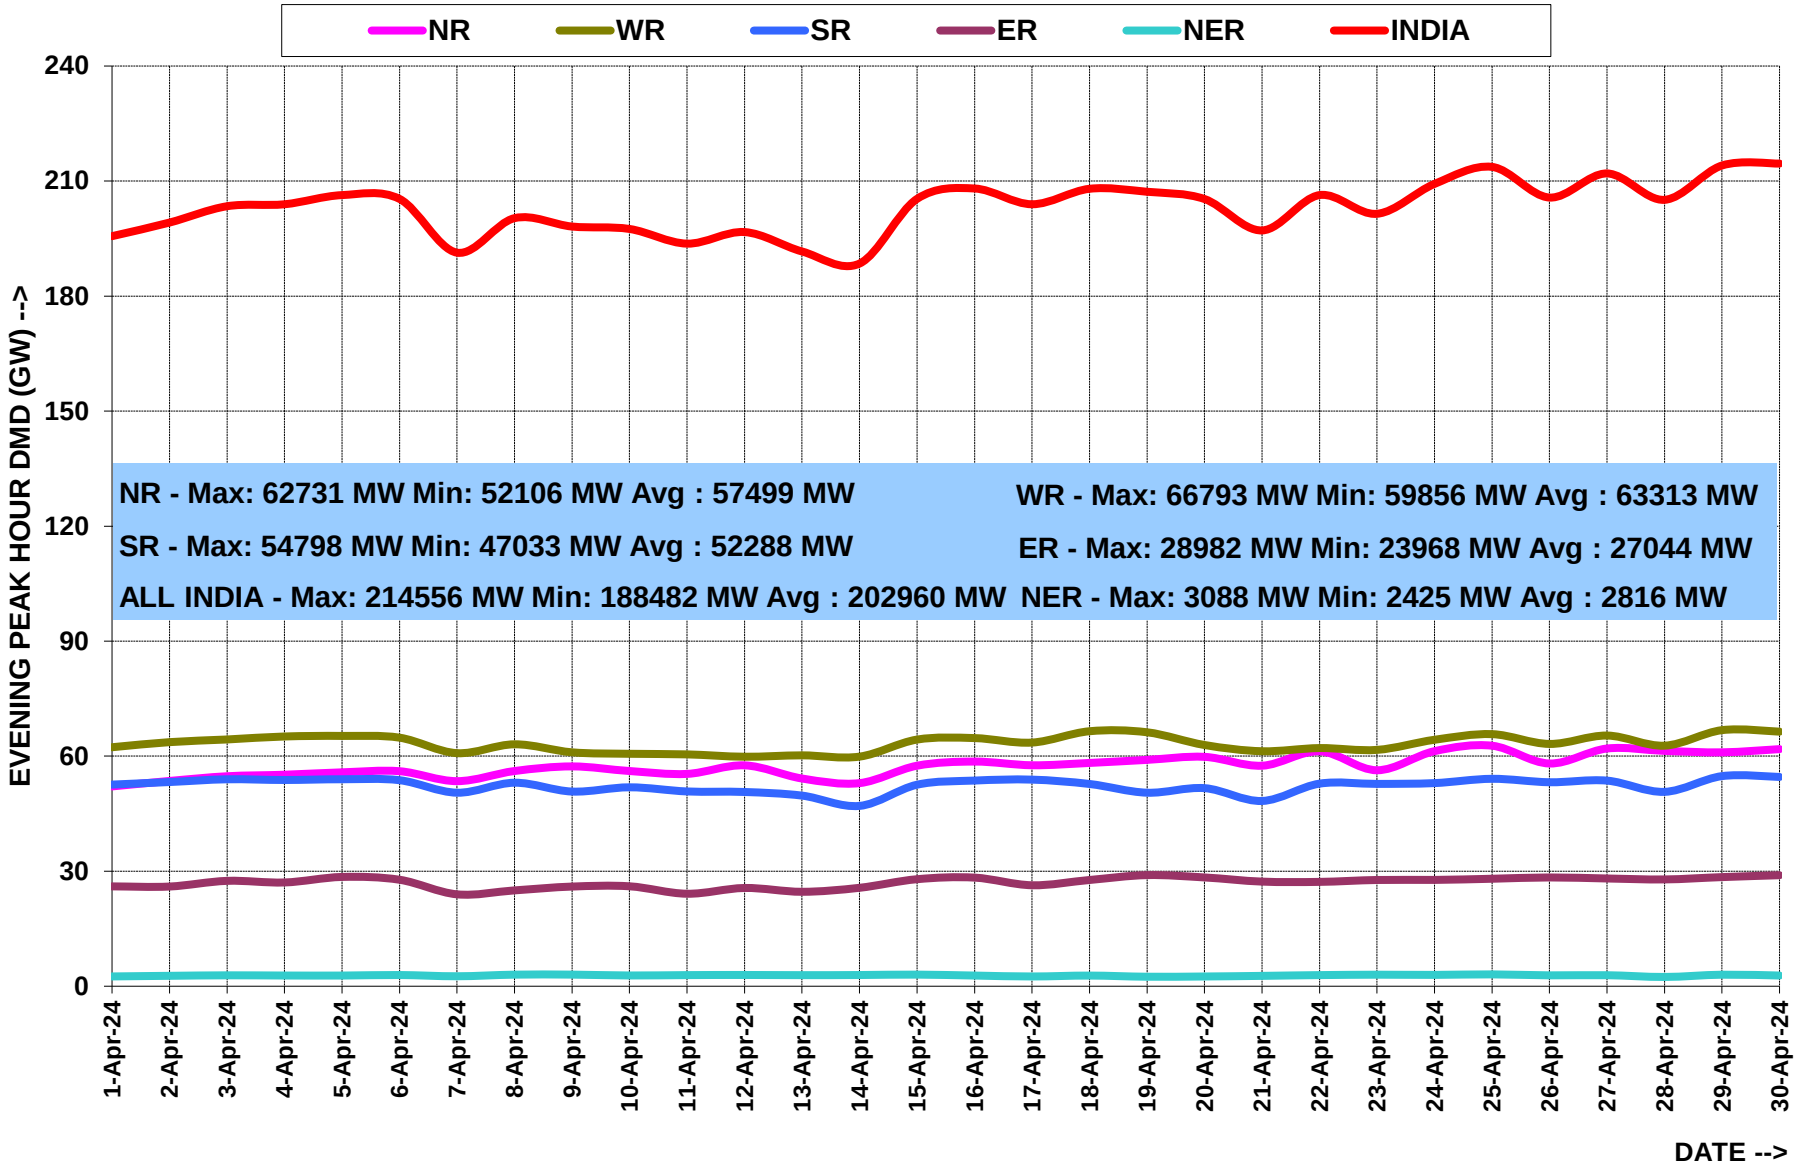


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: अप्रैल 2024 MONTH:- APR 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Apr-24	1127	1523	1369	560	43	4622
02-Apr-24	1148	1555	1397	574	49	4722
03-Apr-24	1184	1572	1406	588	51	4800
04-Apr-24	1206	1588	1409	609	52	4864
05-Apr-24	1226	1588	1416	624	56	4910
06-Apr-24	1210	1587	1402	629	54	4883
07-Apr-24	1153	1529	1343	574	51	4650
08-Apr-24	1191	1549	1375	546	56	4717
09-Apr-24	1230	1525	1342	552	56	4706
10-Apr-24	1222	1523	1345	574	57	4720
11-Apr-24	1216	1493	1346	540	56	4650
12-Apr-24	1235	1483	1335	540	58	4651
13-Apr-24	1209	1463	1281	567	57	4578
14-Apr-24	1130	1458	1225	572	55	4441
15-Apr-24	1217	1554	1310	612	58	4751
16-Apr-24	1238	1587	1352	630	54	4861
17-Apr-24	1213	1599	1375	618	50	4854
18-Apr-24	1241	1615	1368	631	51	4907
19-Apr-24	1261	1628	1288	635	51	4864
20-Apr-24	1284	1596	1279	637	48	4844
21-Apr-24	1237	1534	1236	622	50	4679
22-Apr-24	1299	1545	1298	629	55	4826
23-Apr-24	1285	1555	1322	623	58	4843
24-Apr-24	1303	1559	1336	624	57	4879
25-Apr-24	1347	1602	1355	630	57	4990
26-Apr-24	1346	1593	1342	656	57	4994
27-Apr-24	1352	1602	1354	652	56	5016
28-Apr-24	1332	1553	1301	638	50	4873
29-Apr-24	1364	1613	1369	653	52	5051
30-Apr-24	1357	1635	1393	667	56	5108
कुल TOTAL	37363	46804	40266	18207	1613	144252
उच्चतम MAXIMUM	1364	1635	1416	667	58	5108
निम्नतम MINIMUM	1127	1458	1225	540	43	4441
औसत AVERAGE	1245	1560	1342	607	54	4808
संचयी 2024-25 Cumulative 2024-25	37363	46804	40266	18207	1613	144252
अब तक का उच्चतम All Time Max.	1796	**1635**	**1416**	**667**	72	5224
दिनांक Date	04.09.23	**30.04.24**	**05.04.24**	**30.04.24**	15.09.23	02.09.23

ENERGY MET DURING THE MONTH OF APRIL' 2024

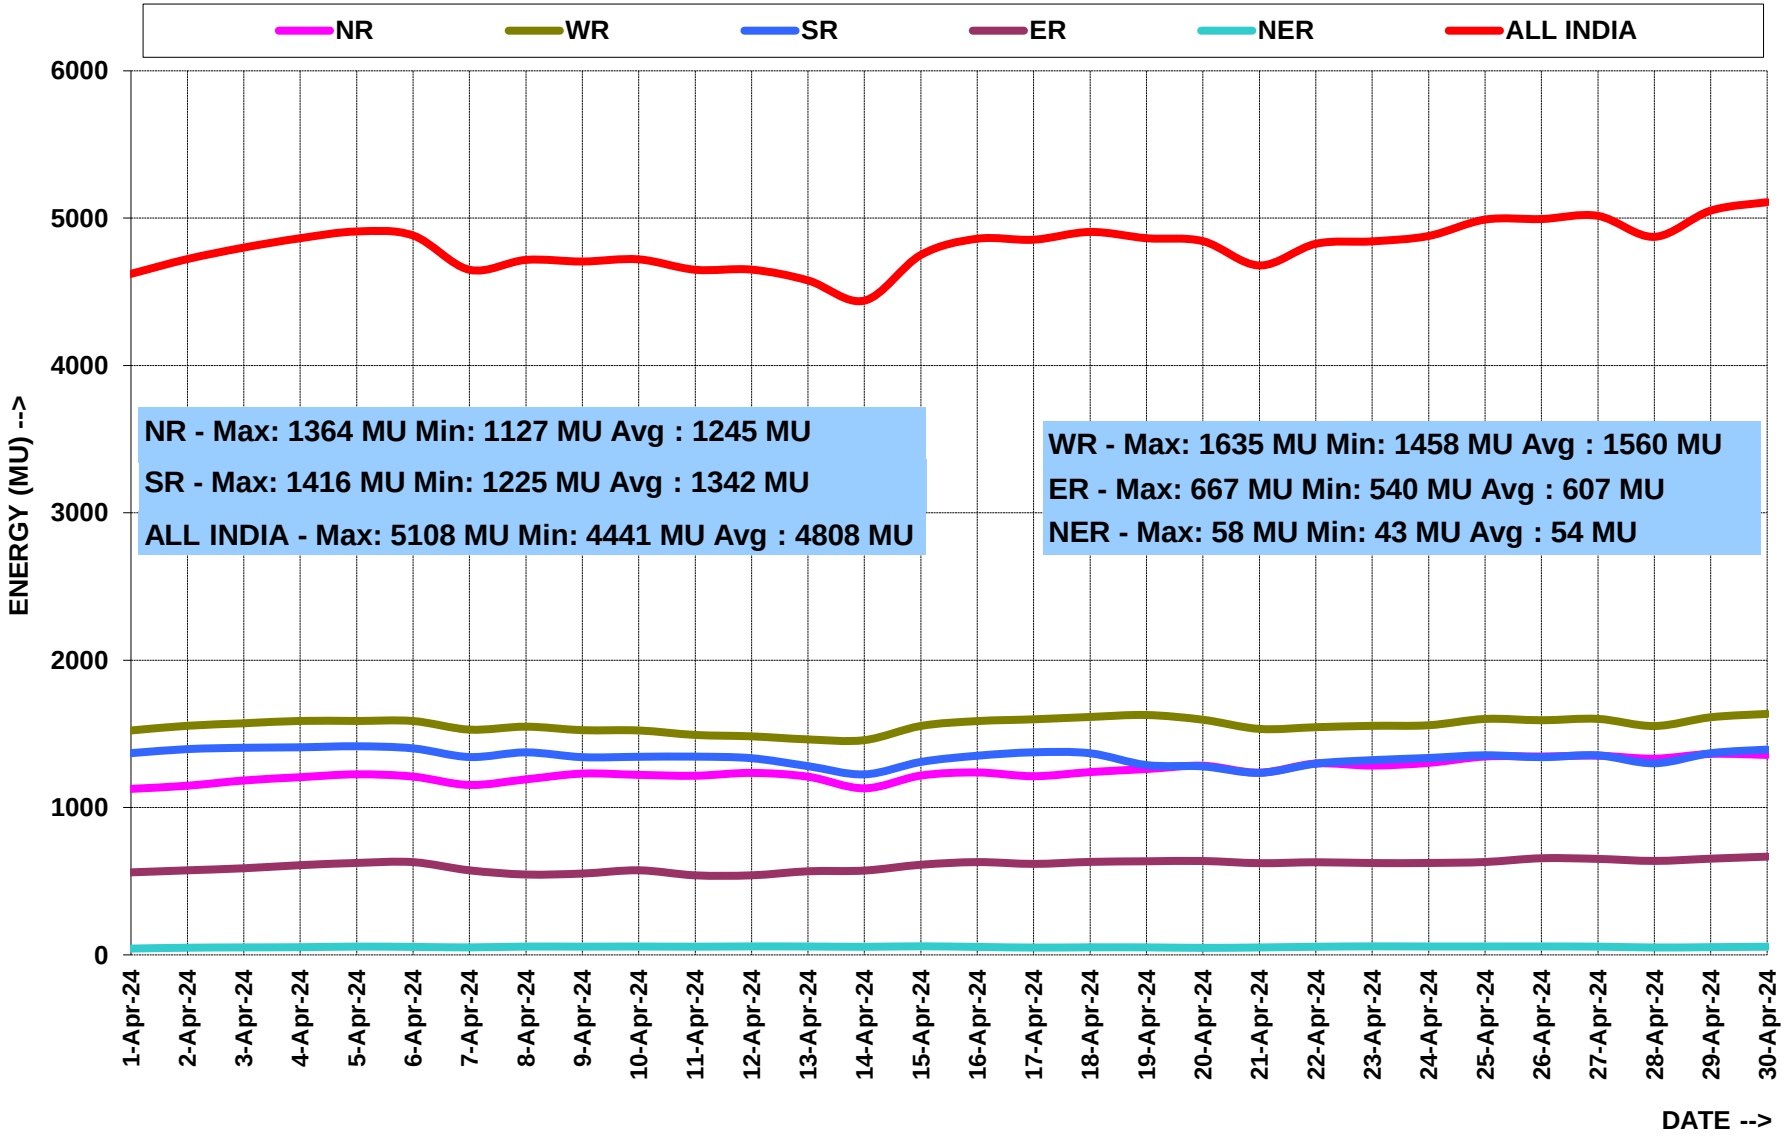

5. वर्ष 2024-25 के लिए आवृति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	2024-25 (upto Apr)	All India Grid	0.43	6.44	1.33		50.43	49.55	4.10

5.1 अप्रैल 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR APRIL 2024


फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Apr-24	7.26	65.60	27.14		50.29	49.78	50.01	0.07
	02-Apr-24	7.79	76.33	15.88		50.25	49.74	49.99	0.04
	03-Apr-24	10.13	78.36	11.52		50.20	49.68	49.98	0.05
	04-Apr-24	10.00	78.96	11.04		50.26	49.73	49.98	0.04
	05-Apr-24	10.98	72.03	16.99		50.38	49.74	50.00	0.06
	06-Apr-24	3.15	82.38	14.47		50.25	49.55	50.00	0.03
	07-Apr-24	2.45	80.07	17.48		50.26	49.78	50.01	0.03
	08-Apr-24	1.46	82.16	16.38		50.24	49.86	50.01	0.03
	09-Apr-24	8.99	81.05	9.95		50.25	49.71	49.98	0.04
	10-Apr-24	2.19	84.80	13.01		50.27	49.81	50.00	0.03
	11-Apr-24	5.05	88.83	6.12		50.14	49.81	49.98	0.02
	12-Apr-24	4.03	81.47	14.50		50.30	49.73	50.00	0.03
	13-Apr-24	11.79	72.63	15.58		50.28	49.74	49.98	0.06
	14-Apr-24	7.25	78.24	14.51		50.34	49.76	49.99	0.04
	15-Apr-24	13.19	70.91	15.89		50.28	49.64	49.98	0.07
	16-Apr-24	0.61	82.44	16.94		50.23	49.85	50.01	0.02
	17-Apr-24	3.31	78.55	18.14		50.30	49.82	50.01	0.03
	18-Apr-24	5.81	71.61	22.58		50.43	49.65	50.01	0.05
	19-Apr-24	4.66	71.64	23.69		50.37	49.79	50.02	0.05
	20-Apr-24	5.86	75.25	18.89		50.28	49.68	50.00	0.04
	21-Apr-24	4.91	86.49	8.60		50.20	49.79	49.99	0.03
	22-Apr-24	3.80	79.03	17.18		50.24	49.78	50.01	0.03
	23-Apr-24	0.58	74.05	25.37		50.24	49.86	50.02	0.03
	24-Apr-24	3.82	84.14	12.04		50.25	49.82	50.00	0.03
	25-Apr-24	4.13	82.62	13.25		50.32	49.80	50.00	0.03
	26-Apr-24	2.19	80.61	17.20		50.20	49.80	50.01	0.02
	27-Apr-24	5.24	85.80	8.96		50.20	49.73	49.99	0.03
	28-Apr-24	3.67	74.57	21.76		50.29	49.82	50.02	0.04
	29-Apr-24	1.61	85.02	13.37		50.17	49.84	50.00	0.02
	30-Apr-24	1.70	71.09	27.21		50.31	49.85	50.02	0.03

6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: अप्रैल 2024 MONTH:- APR 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Apr-24	154	24	58	20	15	271
02-Apr-24	136	31	66	25	12	271
03-Apr-24	134	38	72	24	13	280
04-Apr-24	130	40	73	25	12	279
05-Apr-24	129	43	72	23	12	279
06-Apr-24	126	46	62	28	14	275
07-Apr-24	127	36	49	18	15	245
08-Apr-24	127	33	58	18	14	251
09-Apr-24	129	27	52	19	12	239
10-Apr-24	138	27	45	17	9	236
11-Apr-24	137	26	50	16	9	238
12-Apr-24	132	27	40	16	10	223
13-Apr-24	139	24	42	19	10	233
14-Apr-24	145	27	38	21	9	241
15-Apr-24	157	46	52	25	10	289
16-Apr-24	183	51	65	25	9	333
17-Apr-24	169	38	57	33	11	308
18-Apr-24	166	41	51	30	13	301
19-Apr-24	165	47	47	31	14	304
20-Apr-24	172	39	38	29	11	288
21-Apr-24	170	38	37	30	13	288
22-Apr-24	165	46	39	28	11	289
23-Apr-24	167	42	44	24	11	287
24-Apr-24	167	44	52	24	11	299
25-Apr-24	174	50	57	24	10	315
26-Apr-24	177	62	46	24	10	319
27-Apr-24	188	62	63	28	11	352
28-Apr-24	194	52	56	26	10	337
29-Apr-24	181	59	64	29	11	345
30-Apr-24	197	54	56	30	14	352
कुल TOTAL	4674	1218	1600	728	346	8566
उच्चतम MAXIMUM	197	62	73	33	15	352
निम्नतम MINIMUM	126	24	37	16	9	223
औसत AVERAGE	156	41	53	24	12	286
संचयी 2024-25 Cumulative 2024-25	4674	1218	1600	728	346	8566
अब तक का उच्चतम All Time Max.	443	167	208	157	41	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	29.08.23	30.08.22

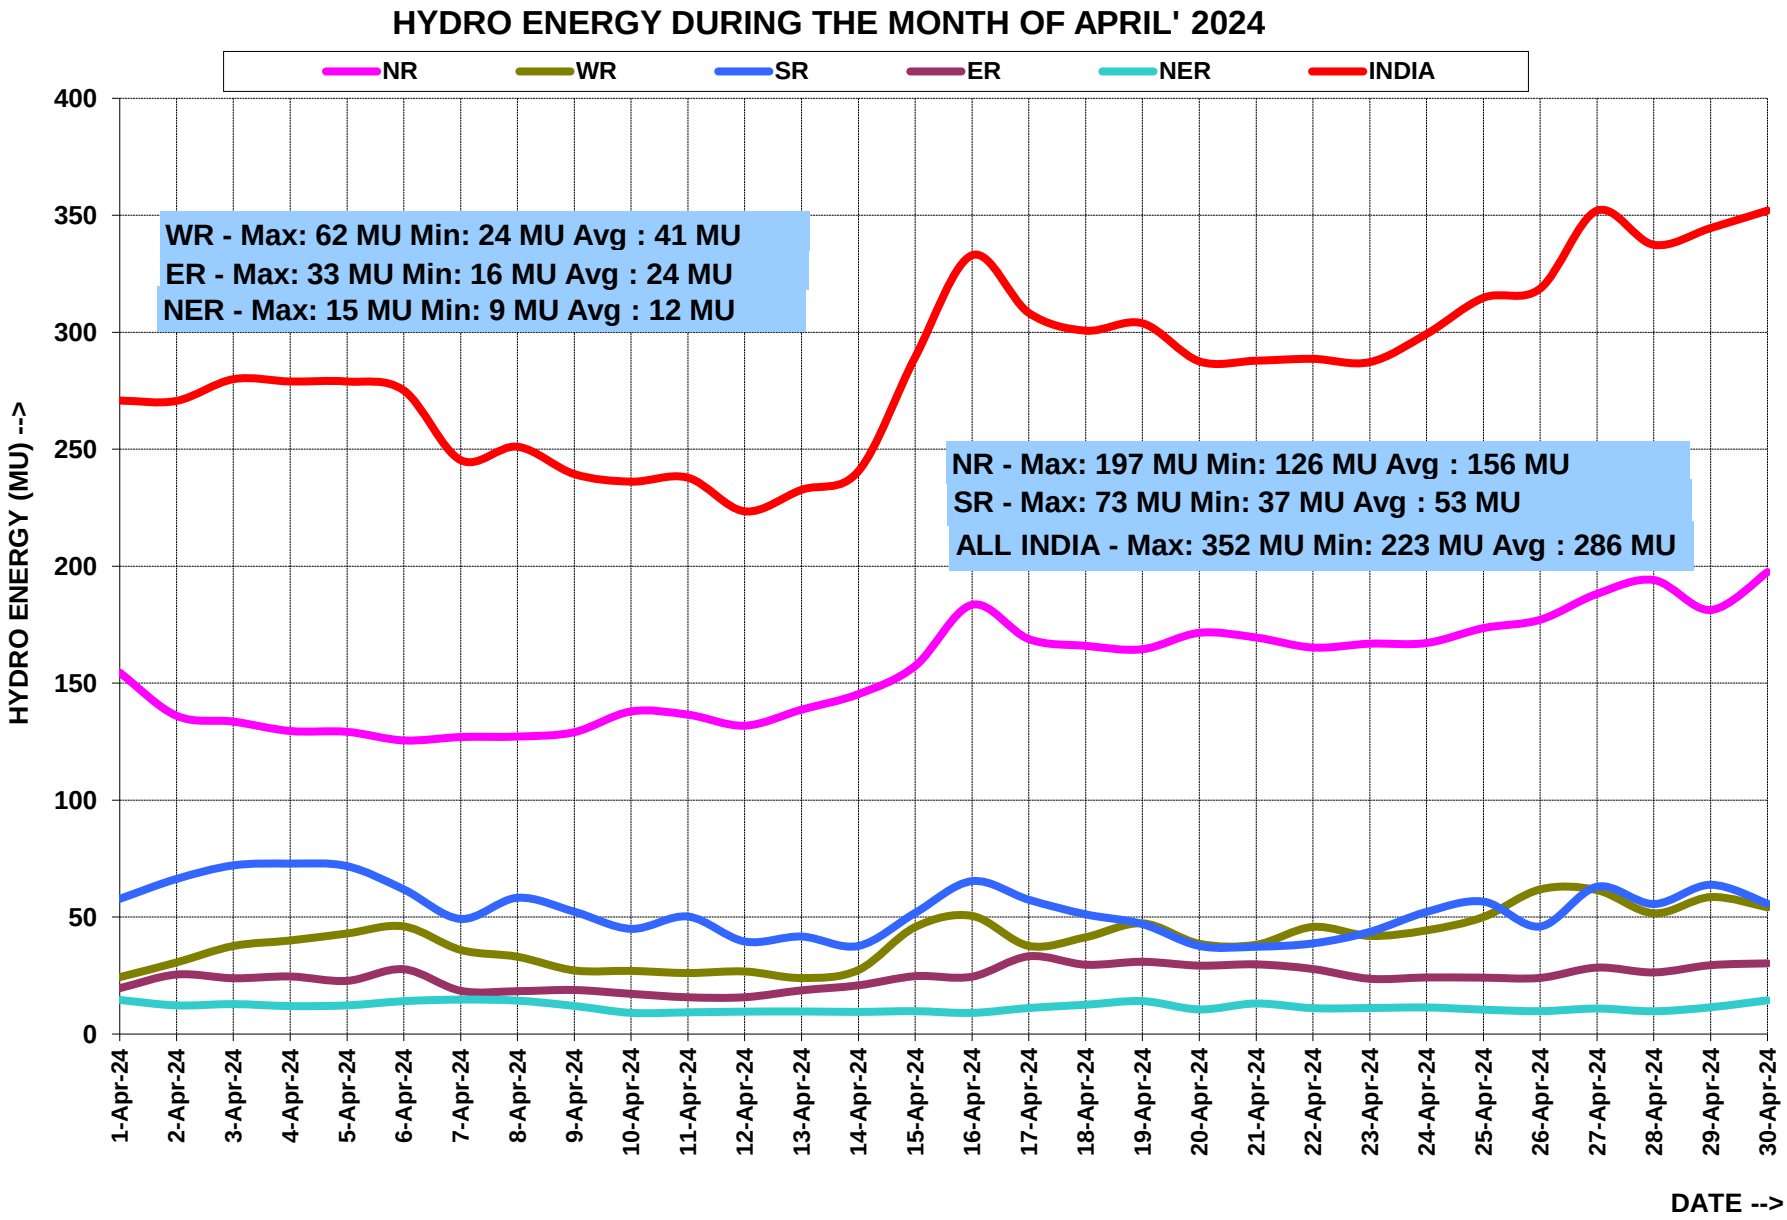
HYDRO ENERGY DURING THE MONTH OF APRIL' 2024
NR
WR
SR
ER
NER
INDIA
WR - Max: 62 MU Min: 24 MU Avg : 41 MU
ER - Max: 33 MU Min: 16 MU Avg : 24 MU
NER - Max: 15 MU Min: 9 MU Avg : 12 MU
NR - Max: 197 MU Min: 126 MU Avg : 156 MU
SR - Max: 73 MU Min: 37 MU Avg : 53 MU
ALL INDIA - Max: 352 MU Min: 223 MU Avg : 286 MU
HYDRO ENERGY (MU) -->
400
350
300
250
200
150
100
50
0
1-Apr-24
2-Apr-24
3-Apr-24
4-Apr-24
5-Apr-24
6-Apr-24
7-Apr-24
8-Apr-24
9-Apr-24
10-Apr-24
11-Apr-24
12-Apr-24
13-Apr-24
14-Apr-24
15-Apr-24
16-Apr-24
17-Apr-24
18-Apr-24
19-Apr-24
20-Apr-24
21-Apr-24
22-Apr-24
23-Apr-24
24-Apr-24
25-Apr-24
26-Apr-24
27-Apr-24
28-Apr-24
29-Apr-24
30-Apr-24
DATE -->

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: अप्रैल 2024 MONTH:- APR 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Apr-24	14	89	28	----------	----------	131
02-Apr-24	6	89	34	----------	----------	129
03-Apr-24	17	98	37	----------	----------	153
04-Apr-24	15	87	31	----------	----------	132
05-Apr-24	13	130	36	----------	----------	180
06-Apr-24	4	114	33	----------	----------	151
07-Apr-24	7	89	52	----------	----------	149
08-Apr-24	6	73	49	----------	----------	127
09-Apr-24	8	86	56	----------	----------	150
10-Apr-24	15	97	56	----------	----------	169
11-Apr-24	19	76	44	----------	----------	139
12-Apr-24	25	66	67	----------	----------	157
13-Apr-24	25	77	40	----------	----------	142
14-Apr-24	13	70	46	----------	----------	129
15-Apr-24	15	54	66	----------	----------	135
16-Apr-24	19	55	37	----------	----------	111
17-Apr-24	13	64	38	----------	----------	115
18-Apr-24	34	98	46	----------	----------	178
19-Apr-24	61	115	52	----------	----------	228
20-Apr-24	16	115	58	----------	----------	189
21-Apr-24	11	99	25	----------	----------	135
22-Apr-24	11	120	43	----------	----------	174
23-Apr-24	10	91	35	----------	----------	136
24-Apr-24	14	78	43	----------	----------	135
25-Apr-24	24	80	38	----------	----------	142
26-Apr-24	41	100	36	----------	----------	177
27-Apr-24	19	77	38	----------	----------	134
28-Apr-24	8	101	38	----------	----------	147
29-Apr-24	28	113	35	----------	----------	177
30-Apr-24	23	134	47	----------	----------	203
कुल TOTAL	535	2734	1286	----------	----------	4555
उच्चतम MAXIMUM	61	134	67	----------	----------	228
निम्नतम MINIMUM	4	54	25	----------	----------	111
औसत AVERAGE	18	91	43	----------	----------	152
संचयी 2024-25 Cumulative 2024-25	535	2734	1286	----------	----------	4555
अब तक का उच्चतम All Time Max.	86	273	298	----------	----------	611
दिनांक Date	07.08.23	07.08.23	21.07.23	----------	----------	02.08.23

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन

SOLAR GENERATION AT NATIONAL LEVEL

माह: अप्रैल 2024 MONTH:- APR 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Apr-24	156	85	141	3.4	0.9	386
02-Apr-24	155	80	134	3.7	1.3	373
03-Apr-24	148	82	130	3.0	1.3	364
04-Apr-24	149	71	139	3.0	1.0	363
05-Apr-24	119	75	140	3.2	1.0	338
06-Apr-24	162	85	137	3.0	1.2	387
07-Apr-24	164	81	135	2.2	1.1	383
08-Apr-24	168	87	139	2.2	0.9	397
09-Apr-24	136	82	138	2.0	1.2	360
10-Apr-24	146	76	137	2.5	1.0	362
11-Apr-24	151	78	131	1.3	1.1	362
12-Apr-24	141	83	119	2.6	1.1	346
13-Apr-24	114	84	118	2.8	1.2	320
14-Apr-24	130	75	137	2.8	1.1	346
15-Apr-24	126	83	140	3.3	1.1	354
16-Apr-24	168	90	143	3.0	0.6	404
17-Apr-24	140	88	129	3.3	1.0	361
18-Apr-24	118	92	125	3.1	0.9	338
19-Apr-24	169	90	120	3.9	0.7	384
20-Apr-24	161	92	107	3.6	0.8	363
21-Apr-24	158	91	112	3.4	1.2	366
22-Apr-24	171	90	131	2.8	1.1	396
23-Apr-24	175	96	144	3.7	1.1	419
24-Apr-24	170	98	141	3.3	1.3	413
25-Apr-24	170	99	137	3.4	1.3	411
26-Apr-24	175	87	138	3.6	1.3	404
27-Apr-24	168	92	140	3.8	1.1	405
28-Apr-24	160	95	137	3.2	0.9	395
29-Apr-24	172	93	135	3.3	1.2	405
30-Apr-24	184	103	135	3.6	1.2	426
00-Jan-00	0	0	0	0.0	0.0	0
कुल TOTAL	4624	2601	3986	92	32	11334
उच्चतम MAXIMUM	184	103	144	3.9	1.3	426
निम्नतम MINIMUM	114	71	107	1.3	0.6	320
औसत AVERAGE	154	87	133	3.1	1.1	378
संचयी 2024-25 Cumulative 2024-25	4624	2601	3986	92	32.2	11334
अब तक का उच्चतम All Time Max.	**184**	**103**	149	6.7	2.4	**426**
दिनांक Date	**30.04.24**	**30.04.24**	31.03.24	23.03.23	22.06.22	**30.04.24**

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति

DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: अप्रैल 2024 MONTH:- APR 2024

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL		विभिन्नता फ़ैक्टर Diversity Factor*
01-Apr-24	54484	68206	66219	26742	2730	207269		1.054
02-Apr-24	55353	69135	66222	26880	2892	209499		1.052
03-Apr-24	56505	69479	66523	27488	2934	212896		1.047
04-Apr-24	56792	70519	66355	27969	2933	216469		1.037
05-Apr-24	57331	70225	66967	28996	3050	218365		1.038
06-Apr-24	57746	71056	66723	28851	3137	215883		1.054
07-Apr-24	54757	67050	61531	28451	2763	204312		1.050
08-Apr-24	57789	70670	65439	25672	3119	209699		1.062
09-Apr-24	58089	68984	63042	26632	3196	208147		1.057
10-Apr-24	56606	69639	64228	26760	3069	209647		1.051
11-Apr-24	56226	67089	63544	25312	3055	204821		1.051
12-Apr-24	58086	66769	63388	26033	3121	206122		1.055
13-Apr-24	54603	66099	61130	26900	3053	201608		1.050
14-Apr-24	53415	65235	56487	27001	2940	195636		1.048
15-Apr-24	58014	70696	62111	29002	3186	210339		1.060
16-Apr-24	59234	71660	64376	29377	2983	214955		1.059
17-Apr-24	59234	71660	64376	29377	2983	214955		1.059
18-Apr-24	58831	72684	65684	29074	2964	214072		1.071
19-Apr-24	59172	73980	60161	29739	2754	214645		1.052
20-Apr-24	61026	71514	60434	29818	2739	212500		1.061
21-Apr-24	57905	68427	56806	29404	2787	209885		1.026
22-Apr-24	61890	70023	63028	29230	3080	213853		1.063
23-Apr-24	58127	71160	62449	29120	3166	211877		1.057
24-Apr-24	61821	71622	63086	29912	3005	218109		1.052
25-Apr-24	63130	72993	64128	29913	3206	222006		1.051
26-Apr-24	60232	71129	62913	30772	3125	217029		1.051
27-Apr-24	62385	73620	64064	30480	3279	222968		1.049
28-Apr-24	62339	69367	59745	30315	2585	214119		1.048
29-Apr-24	61820	73261	65443	30661	3179	223110		1.050
30-Apr-24	62789	73936	66470	31895	3059	224181		1.062
उच्चतम MAXIMUM	63130	73980	66967	31895	3279	224181		1.071
निम्नतम MINIMUM	53415	65235	56487	25312	2585	195636		1.026
औसत AVERAGE	58524	70263	63436	28593	3002	212632		1.053
अब तक का उच्चतम All Time Max.	81220	74799	68735	**31895**	3712	239978		
दिनांक Date	04.09.23	29.01.24	13.03.24	**30.04.24**	04.09.23	01.09.23		


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 30 APRIL (MAXIMUM DEMAND MET)

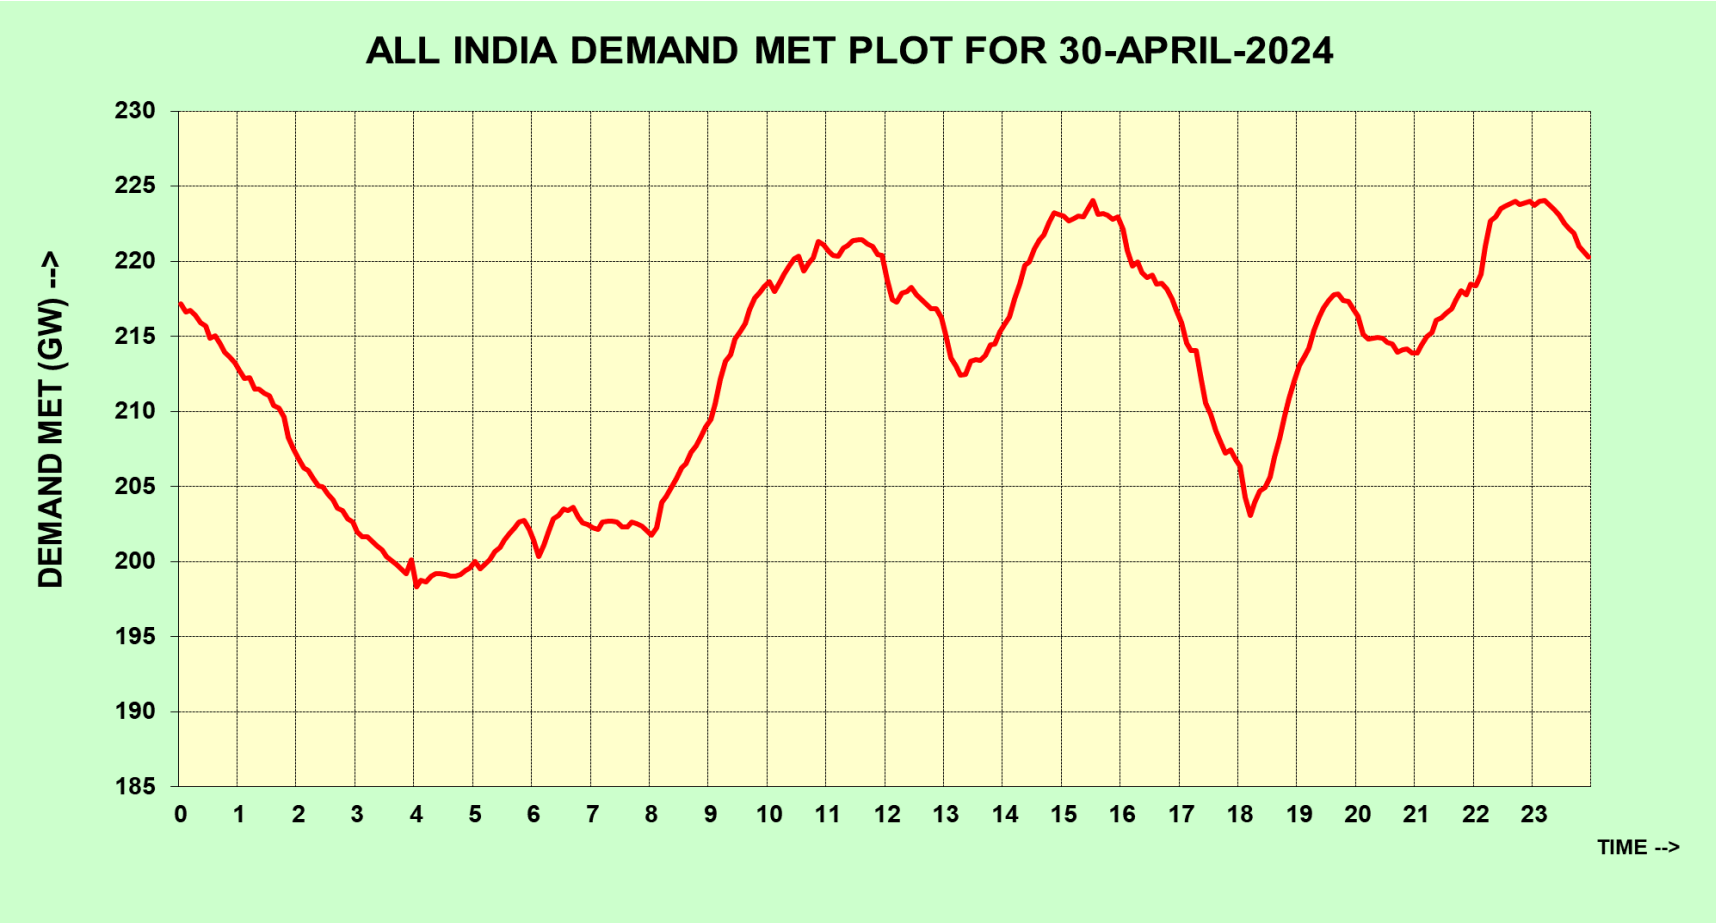

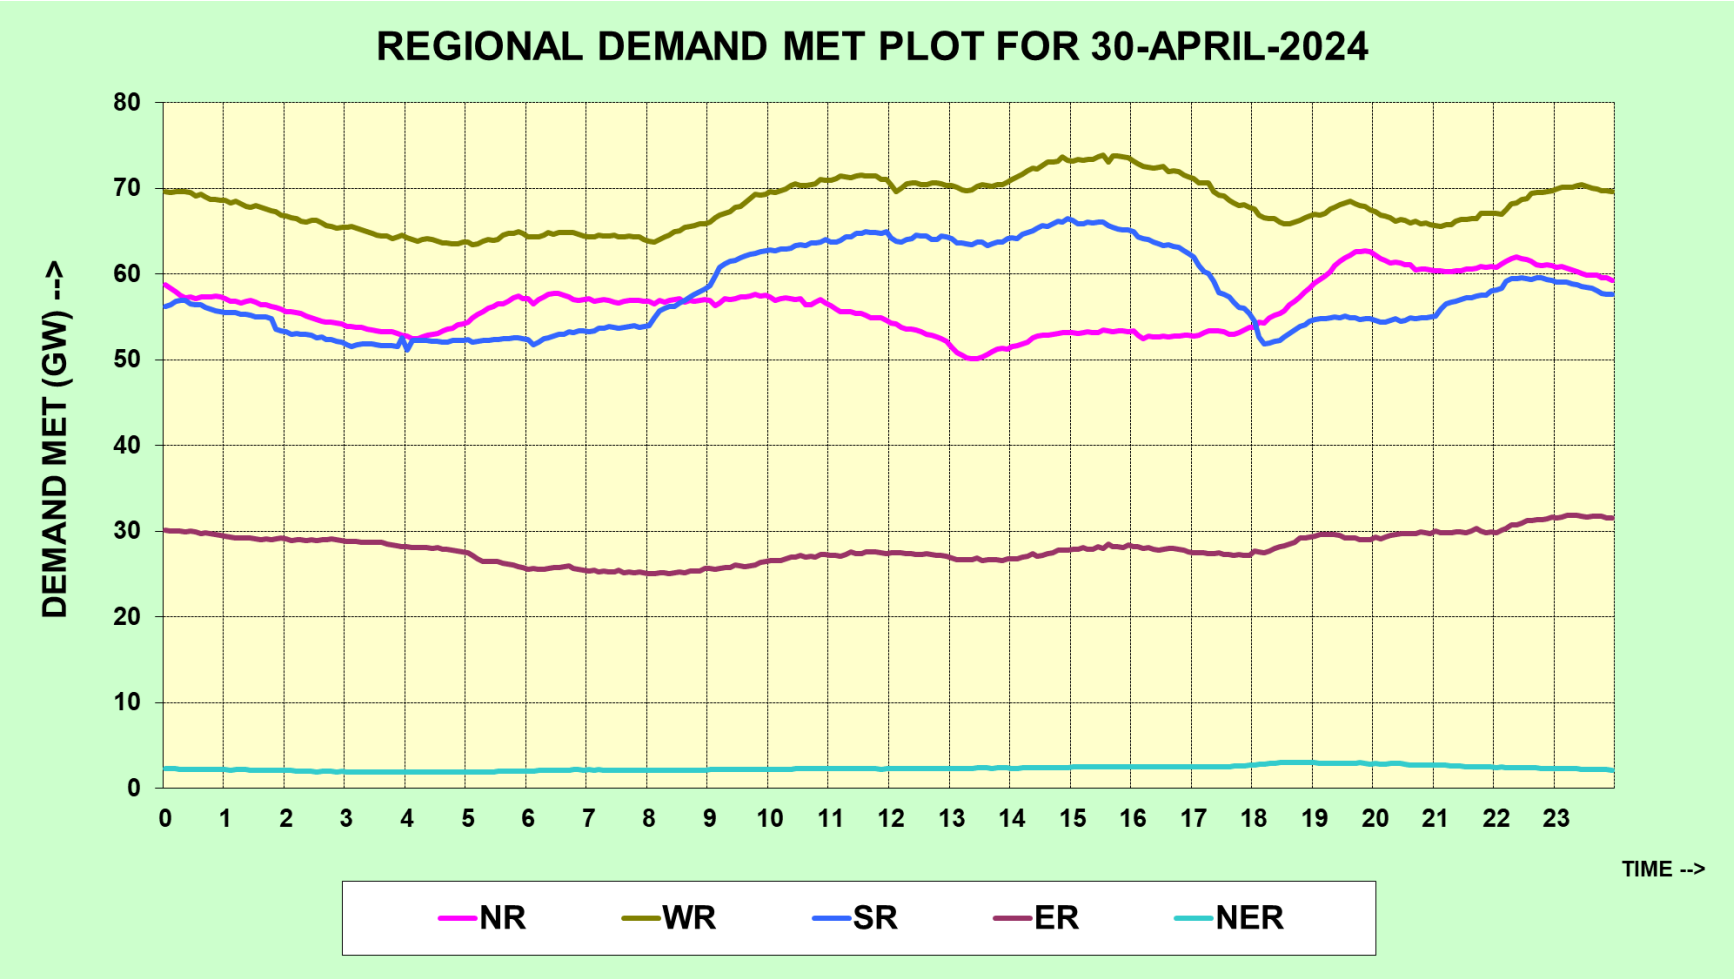
REGIONAL DEMAND MET PLOT FOR 30-APRIL-2024
DEMAND MET (GW) -->
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

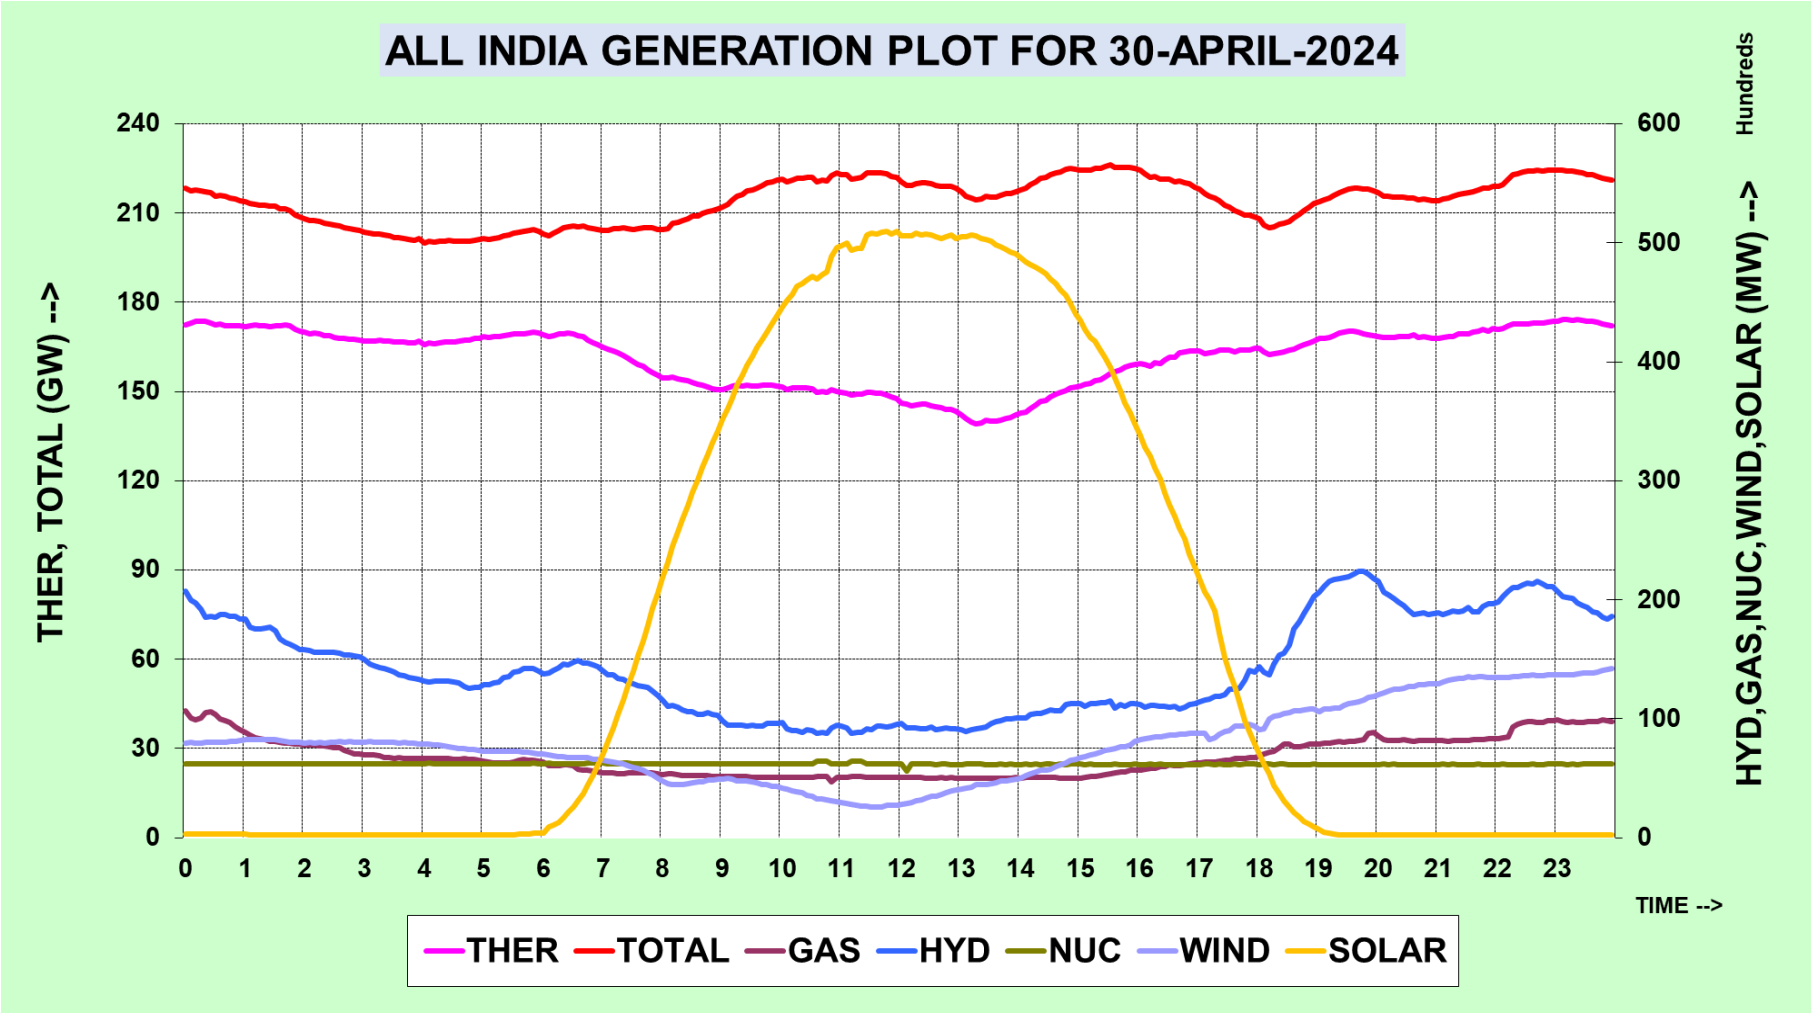
ALL INDIA GENERATION PLOT FOR 30-APRIL-2024
THER, TOTAL (GW) -->
HYD,GAS,NUC,WIND,SOLAR (MW) -->
Hundreds
240
210
180
150
120
90
60
30
0
600
500
400
300
200
100
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
THER TOTAL GAS HYD NUC WIND SOLAR

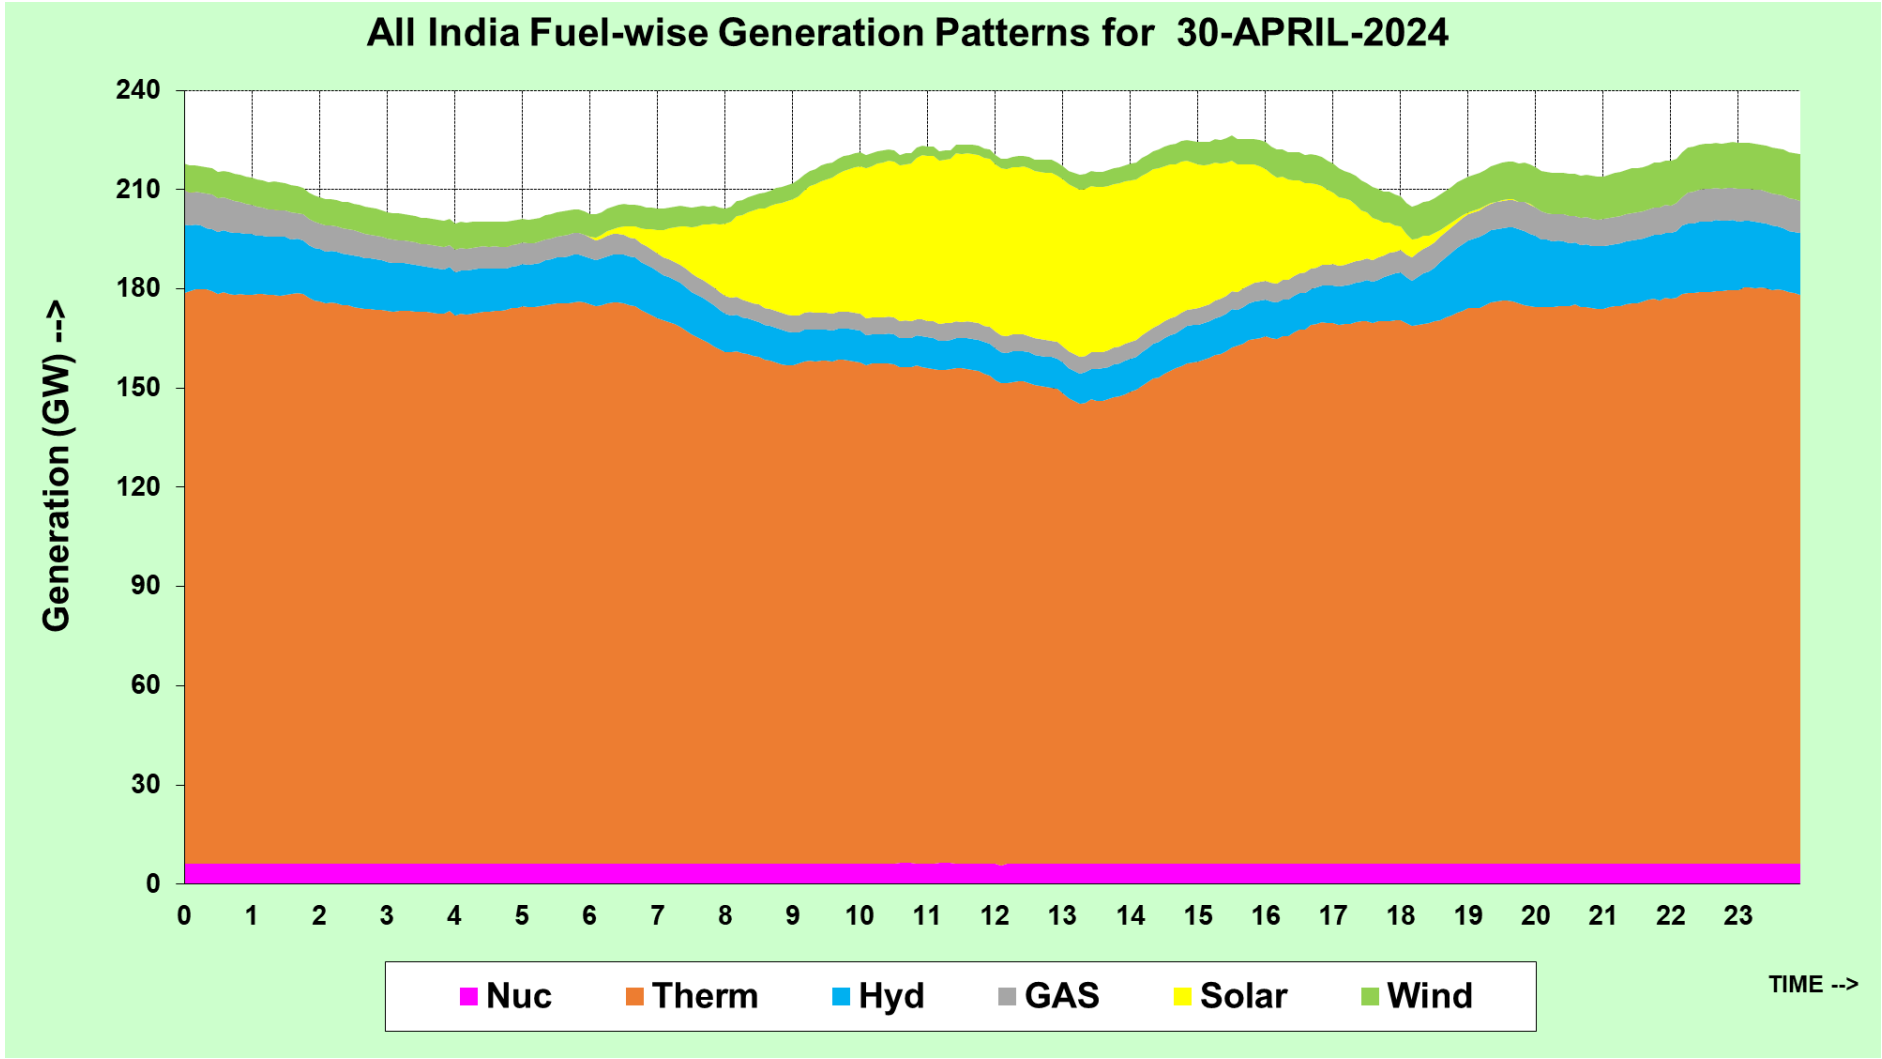
All India Fuel-wise Generation Patterns for 30-APRIL-2024
Generation (GW) -->
240
210
180
150
120
90
60
30
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Nuc
Therm
Hyd
GAS
Solar
Wind

30 अप्रैल 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 30 APRIL 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	216614		**12:05**	217419
00:20	215925		**12:20**	218000
00:35	215035		**12:35**	217450
00:50	213596		**12:50**	216852
01:05	212215		**13:05**	213571
01:20	211479		**13:20**	212459
01:35	210372		**13:35**	213380
01:50	208275		**13:50**	214501
02:05	206248		**14:05**	216266
02:20	205013		**14:20**	219757
02:35	204133		**14:35**	221423
02:50	202850		**14:50**	223217
03:05	201662		**15:05**	222677
03:20	201046		**15:20**	222981
03:35	200052		**15:35**	223094
03:50	199215		**15:50**	222794
04:05	198758		**16:05**	220720
04:20	199187		**16:20**	219228
04:35	199019		**16:35**	218496
04:50	199421		**16:50**	217498
05:05	199500		**17:05**	214568
05:20	200694		**17:20**	212112
05:35	201867		**17:35**	208698
05:50	202761		**17:50**	207428
06:05	200353		**18:05**	204288
06:20	202867		**18:20**	204728
06:35	203388		**18:35**	206933
06:50	202596		**18:50**	210870
07:05	202132		**19:05**	213671
07:20	202692		**19:20**	216306
07:35	202322		**19:35**	217763
07:50	202386		**19:50**	217344
08:05	202249		**20:05**	215121
08:20	204939		**20:20**	214952
08:35	206498		**20:35**	214462
08:50	208267		**20:50**	214155
09:05	210476		**21:05**	214419
09:20	213757		**21:20**	216070
09:35	215850		**21:35**	216827
09:50	217917		**21:50**	217789
10:05	218001		**22:05**	219139
10:20	219697		**22:20**	222930
10:35	219333		**22:35**	223821
10:50	221305		**22:50**	223865
11:05	220363		**23:05**	223998
11:20	221060		**23:20**	223472
11:35	221452		**23:35**	222194
11:50	220453		**23:50**	220645
Maximum Demand of 224181 MW met@22:42 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - APRIL 2024

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	131	131	0	0.0	258	258	0	0.0
	Delhi	95	95	0.0	2843	2843	0	0.0	5447	5447	0	0.0
	Haryana	156	156	0.0	4671	4671	0	0.0	9502	9502	0	0.0
	Himachal Pradesh	31	31	0.0	943	942	-1	-0.1	1819	1819	0	0.0
	J&K(UT) and Ladakh(UT)	51	50	-0.3	1521	1511	-10	-0.6	2924	2924	0	0.0
	Punjab	154	154	0.0	4610	4610	0	0.0	10061	10061	0	0.0
	Rajasthan	271	271	-0.2	8142	8137	-5	-0.1	14283	14283	0	0.0
	Uttar Pradesh	436	436	0.0	13093	13093	0	0.0	25462	25462	0	0.0
	Uttarakhand	44	43	0.0	1306	1305	-1	-0.1	2357	2357	0	0.0
	Railway	4	4	0.0	119	119	0	0.0	220	220	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	5	5	0	0.0
	TOTAL	1246	1245	-0.6	37381	37363	-17	0.0	62884	62884	0	0.0
WR	Gujarat	467	467	0.0	14015	14015	0	0.0	23933	23916	-17	-0.1
	Madhya Pradesh	267	267	-0.7	8018	7998	-20	-0.2	13151	13151	0	0.0
	Chhattisgarh	133	133	0.0	3978	3976	-1	0.0	6367	6347	-20	-0.3
	Maharashtra	618	618	-0.1	18528	18526	-2	0.0	28924	28924	0	0.0
	Goa	16	16	0.0	480	479	0	-0.1	803	803	0	0.0
	DNHDDPDCL	29	29	0.0	864	864	0	0.0	1292	1292	0	0.0
	AMNSIL	19	19	0.0	571	571	0	0.0	922	922	0	0.0
	BALCO	12	12	0.0	374	374	0	0.0	526	526	0	0.0
	TOTAL	1561	1560	-0.8	46828	46804	-24	-0.1	73511	73511	0	0.0
SR	Andhra Pradesh	245	245	0.0	7347	7347	0	0.0	13418	13418	0	0.0
	Telangana	243	243	0.2	7293	7298	5	0.1	13884	13884	0	0.0
	Karnataka	315	315	0.2	9457	9462	6	0.1	16985	16985	0	0.0
	Kerala	106	106	0.1	3189	3191	2	0.1	5646	5646	0	0.0
	Tamil Nadu	421	422	0.2	12641	12649	7	0.1	20701	20701	0	0.0
	Puducherry	11	11	0.0	320	320	0	0.1	517	517	0	0.0
	TOTAL	1342	1342	0.7	40247	40267	20	0.1	66986	66986	0	0.0
ER	Bihar	129	128	-0.9	3871	3844	-27	-0.7	7051	7051	0	0.0
	Jharkhand	44	43	-1.0	1312	1284	-29	-2.2	2187	2187	0	0.0
	DVC	73	73	0.0	2199	2199	0	0.0	3551	3551	0	0.0
	Odisha	130	130	0.0	3901	3901	0	0.0	6860	6860	0	0.0
	West Bengal	234	234	0.0	7027	7027	0	0.0	12756	12756	0	0.0
	Sikkim	2	2	0.0	47	47	0	0.0	105	105	0	0.0
	Railways_ER ISTS	0	0	0.0	4	4	0	0.0	18	18	0	0.0
	TOTAL	612	610	-1.9	18361	18305	-56	-0.3	31890	31890	0	0.0
NER	Arunachal Pradesh	2	2	0.0	75	75	0	0.0	185	185	0	0.0
	Assam	33	33	0.0	994	994	0	0.0	2012	2012	0	0.0
	Manipur	3	3	0.0	85	85	0	0.0	214	214	0	0.0
	Meghalaya	6	6	0.0	166	166	0	0.0	408	408	0	0.0
	Mizoram	2	2	0.0	56	56	0	0.0	130	130	0	0.0
	Nagaland	2	2	0.0	67	67	0	0.0	166	166	0	0.0
	Tripura	6	6	0.0	167	167	0	0.0	363	363	0	0.0
	TOTAL	54	54	0.0	1608	1608	0	0.0	3281	3281	0	0.0
ALL INDIA		4814	4812	-2.6	144424	144348	-77	-0.1				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF APRIL 2024 vs APRIL 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Apr-23	Apr-24	Difference	% Change	Average MU/day for Apr-24	Apr-23	Apr-24	Difference	% Change	Average MU/day for Apr-24
NR	Chandigarh	121	131	9	8	4	121	131	9	8	4
	Delhi	2553	2843	290	11	95	2553	2843	290	11	95
	Haryana	4226	4671	445	11	156	4195	4671	477	11	156
	Himachal Pradesh	918	943	25	3	31	914	942	27	3	31
	J&K(UT) and Ladakh(UT)	1695	1521	-174	-10	51	1675	1511	-164	-10	50
	Punjab	4199	4610	411	10	154	4194	4610	416	10	154
	Rajasthan	7402	8142	740	10	271	7359	8137	778	11	271
	Uttar Pradesh	11099	13093	1994	18	436	11083	13093	2011	18	436
	Uttarakhand	1222	1306	84	7	44	1207	1305	98	8	43
	Railway/NFL	98	121	23	23	4	98	121	23	23	4
	TOTAL	33534	37381	3847	11	1246	33399	37363	3964	12	1245
WR	Gujarat	12977	14015	1038	8	467	12977	14015	1038	8	467
	Madhya Pradesh	7170	8018	849	12	267	7170	7998	829	12	267
	Chhattisgarh	3442	3978	536	16	133	3435	3976	541	16	133
	Maharashtra	16846	18528	1682	10	618	16844	18526	1682	10	618
	Goa	443	480	37	8	16	442	479	37	8	16
	DNHDDPDCL	859	864	5	1	29	859	864	5	1	29
	AMNSIL	541	571	30	6	19	541	571	30	6	19
	BALCO	371	374	3	1	12	371	374	3	1	12
	TOTAL	42649	46828	4178	10	1561	42640	46804	4164	10	1560
SR	Andhra Pradesh	7011	7347	336	5	245	6946	7347	401	6	245
	Telangana	7111	7293	182	3	243	7034	7298	264	4	243
	Karnataka	8710	9457	747	9	315	8631	9462	831	10	315
	Kerala	2792	3189	397	14	106	2765	3191	426	15	106
	Tamil Nadu	11377	12641	1265	11	421	11272	12649	1377	12	422
	Puducherry	297	320	23	8	11	294	320	26	9	11
	TOTAL	37297	40247	2950	8	1342	36942	40267	3325	9	1342
ER	Bihar	3400	3871	471	14	129	3372	3844	472	14	128
	Jharkhand	1031	1312	281	27	44	970	1284	314	32	43
	DVC	2289	2199	-90	-4	73	2289	2199	-90	-4	73
	Odisha	3501	3901	400	11	130	3501	3901	400	11	130
	West Bengal	5907	7027	1120	19	234	5901	7027	1126	19	234
	Sikkim	42	47	4	11	2	42	47	4	11	2
	Railways_ER ISTS	1	4	3	353	0	1	4	3	353	0
	TOTAL	16171	18361	2190	14	612	16076	18305	2229	14	610
NER	Arunachal Pradesh	81	75	-6	-7	2	81	75	-6	-7	2
	Assam	913	994	81	9	33	911	994	83	9	33
	Manipur	78	85	7	8	3	78	85	7	9	3
	Meghalaya	193	166	-27	-14	6	153	166	13	9	6
	Mizoram	53	56	3	6	2	53	56	3	6	2
	Nagaland	65	67	2	3	2	65	67	2	3	2
	Tripura	150	167	17	11	6	150	167	17	11	6
	TOTAL	1532	1608	76	5	54	1490	1608	119	8	54
ALL INDIA		131183	144424	13242	10	4814	130547	144348	13801	11	4812

13. DEMAND COMPARISON OF APRIL 2024 vs APRIL 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Apr-23	Apr-24	Difference	% Change	Apr-23	Apr-24	Difference	% Change
NR	Chandigarh	252	258	6	2.4	252	258	6	2.4
	Delhi	5465	5447	-18	-0.3	5422	5447	25	0.5
	Haryana	8345	9502	1157	13.9	8345	9502	1157	13.9
	Himachal Pradesh	1809	1819	10	0.6	1809	1819	10	0.6
	J&K(UT) and Ladakh(UT)	2890	2924	34	1.2	2890	2924	34	1.2
	Punjab	8143	10061	1918	23.6	8143	10061	1918	23.6
	Rajasthan	13766	14283	517	3.8	13766	14283	517	3.8
	Uttar Pradesh	23473	25462	1989	8.5	23473	25462	1989	8.5
	Uttarakhand	2228	2357	129	5.8	2228	2357	129	5.8
	Railway/NFL	187	225	38	20.4	187	225	38	20.4
WR	Gujarat	21627	23933	2306	11	21627	23916	2289	10.6
	Madhya Pradesh	12402	13151	749	6	12402	13151	749	6.0
	Chhattisgarh	5642	6367	725	13	5642	6347	705	12.5
	Maharashtra	28584	28924	340	1	28584	28924	340	1.2
	Goa	759	803	43	6	759	803	43	5.7
	DNHDDPDCL	1271	1292	21	1.7	1271	1292	21	1.7
	AMNSIL	895	922	27	3.0	895	922	27	3.0
	BALCO	522	526	4	0.7	522	526	4	0.7
SR	Andhra Pradesh	12494	13418	924	7.4	12494	13418	924	7.4
	Telangana	14517	13884	-633	-4.4	14499	13884	-615	-4.2
	Karnataka	16110	16985	875	5.4	16110	16985	875	5.4
	Kerala	5028	5646	618	12.3	5024	5646	621	12.4
	Tamil Nadu	19387	20701	1314	6.8	19387	20701	1314	6.8
	Puducherry	474	517	43	9.1	474	517	43	9.1
ER	Bihar	6820	7051	231	3.4	6456	7051	595	9.2
	Jharkhand	1857	2187	330	17.8	1857	2187	330	17.8
	DVC	3751	3551	-200	-5.3	3751	3551	-200	-5.3
	Odisha	7192	6860	-332	-4.6	7192	6860	-332	-4.6
	West Bengal	11868	12756	888	7.5	11868	12756	888	7.5
	Sikkim	105	105	0	0.0	105	105	0	0.0
	Railways_ER ISTS	11	18	7	58.0	11	18	7	58.0
NER	Arunachal Pradesh	155	185	30	19.4	155	185	30	19.4
	Assam	2013	2012	-1	-0.1	2013	2012	-1	-0.1
	Manipur	213	214	1	0.6	213	214	1	0.6
	Meghalaya	336	408	72	21.5	336	408	72	21.5
	Mizoram	127	130	3	2.5	127	130	3	2.5
	Nagaland	150	166	16	10.6	150	166	16	10.6
	Tripura	338	363	26	7.6	338	363	26	7.6

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - APRIL 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	133.05	133.09	0.04	0.03	4.44	4.44	0.00
	Delhi	2510.77	2529.27	18.50	0.74	83.69	84.31	0.62
	Haryana	2881.37	2857.14	-24.23	-0.84	96.05	95.24	-0.81
	Himachal Pradesh	503.10	509.91	6.81	1.35	16.77	17.00	0.23
	J&K(UT) and Ladakh(UT)	1122.60	1123.88	1.28	0.11	37.42	37.46	0.04
	Punjab	1397.27	1341.67	-55.60	-3.98	46.58	44.72	-1.85
	Rajasthan	1814.42	1793.67	-20.75	-1.14	60.48	59.79	-0.69
	Uttar Pradesh	4996.46	5017.65	21.19	0.42	166.55	167.26	0.71
	Uttarakhand	752.60	741.52	-11.08	-1.47	25.09	24.72	-0.37
	Railway	111.87	118.67	6.80	6.08	3.73	3.96	0.23
	NFL	2.28	2.29	0.02	0.69	0.08	0.08	0.00
	Total	16225.79	16168.77	-57.02	-0.35	540.86	538.96	-1.90
WR	Gujarat	5142.29	5078.54	-63.75	-1.24	171.41	169.28	-2.13
	Madhya Pradesh	4276.78	4149.17	-127.61	-2.98	142.56	138.31	-4.25
	Chhattisgarh	2240.85	2222.73	-18.12	-0.81	74.70	74.09	-0.60
	Maharashtra	6201.72	6097.60	-104.12	-1.68	206.72	203.25	-3.47
	Goa	475.24	472.12	-3.11	-0.65	15.84	15.74	-0.10
	DNHDDPDCL	864.13	864.29	0.16	0.02	28.80	28.81	0.01
	AMNSIL	197.05	203.95	6.90	3.50	6.57	6.80	0.23
	BALCO*	376.01	374.10	-1.91	-0.51	12.53	12.47	-0.06
	Total	19774.07	19462.51	-311.56	-1.58	659.14	648.75	-10.39
SR	Andhra Pradesh	2435.41	2417.52	-17.89	-0.73	81.18	80.58	-0.60
	Telangana	3641.24	3632.89	-8.35	-0.23	121.37	121.10	-0.28
	Karnataka	4408.32	4425.78	17.46	0.40	146.94	147.53	0.58
	Kerala	2519.91	2562.53	42.62	1.69	84.00	85.42	1.42
	Tamil Nadu	8103.44	8016.59	-86.85	-1.07	270.11	267.22	-2.90
	Puducherry	309.17	302.30	-6.87	-2.22	10.31	10.08	-0.23
	Goa (SR)	110.21	76.38	-33.83	-30.70	3.67	2.55	-1.13
	Total	21527.70	21433.99	-93.71	-0.44	717.59	714.47	-3.12
ER	Bihar	3540.50	3530.86	-9.64	-0.27	118.02	117.70	-0.32
	Jharkhand	906.02	920.60	14.58	1.61	30.20	30.69	0.49
	DVC	-1176.34	-1167.14	9.19	-0.78	-39.21	-38.90	0.31
	Odisha	1504.28	1491.29	-12.99	-0.86	50.14	49.71	-0.43
	West Bengal	2804.49	2754.23	-50.27	-1.79	93.48	91.81	-1.68
	Sikkim	47.01	46.61	-0.39	-0.83	1.57	1.55	-0.01
	Railways_ER ISTS	4.01	3.89	-0.12	-3.00	0.13	0.13	0.00
	Total	7629.97	7580.33	-49.64	-0.65	254.33	252.68	-1.65
NER	Arunachal Pradesh	79.02	72.14	-6.88	-8.71	2.63	2.40	-0.23
	Assam	799.60	805.05	5.45	0.68	26.65	26.84	0.18
	Manipur	87.04	84.64	-2.40	-2.76	2.90	2.82	-0.08
	Meghalaya	129.59	124.85	-4.74	-3.66	4.32	4.16	-0.16
	Mizoram	53.23	46.57	-6.66	-12.51	1.77	1.55	-0.22
	Nagaland	69.79	66.56	-3.23	-4.63	2.33	2.22	-0.11
	Tripura	164.07	174.35	10.28	6.27	5.47	5.81	0.34
	Total	1382.34	1374.16	-8.18	-0.59	46.08	45.81	-0.27
All India Total		66539.87	66019.76	-520.11	-0.78	2218.00	2200.66	-17.34

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	Fin. Year 2024-25
Name of Line		
Import of NR from WR (WR-NR)		
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	**529.65**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	**157.44**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	**304.53**
WR-NR 765 kV Satna-Orai	535.85	**535.85**
WR-NR 765 kV Gwalior-Orai	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	**1525.63**
WR - NR HVDC Vindhyachal	0.00	**0.00**
WR - NR 400 kV Zerda Kankroli	0.00	**0.00**
WR - NR 400 kV Zerda Bhinmal	0.00	**0.00**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	**0.00**
WR - NR 220 kV Bhanpura - Ranpur	55.64	**55.64**
WR - NR 220 kV Bhanpura - Modak	69.87	**69.87**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	**0.00**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	**717.97**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	**0.67**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	**1373.47**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	**0.00**
Total WR - NR	**5270.72**	**5270.72**
Export of NR to WR (NR-WR)		
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	**10.49**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	**0.00**

	Apr'24	Fin. Year 2024-25
Name of Line		
NR - WR 765 kV Satna-Orai	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	**245.97**
NR - WR HVDC Champa- Kurukshetra	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	**259.46**
NR - WR 400 kV Zerda Kankroli	240.09	**240.09**
NR - WR 400 kV Zerda Bhinmal	8.05	**8.05**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	**159.07**
NR - WR 220 kV Bhanpura - Ranpur	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	**59.69**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	**609.68**
NR - WR HVDC Mundra - Mohindergarh	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	**463.90**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	**139.03**
Total NR - WR	**2195.43**	**2195.43**

	Apr'24	Fin. Year 2024-25
Name of Line		
Import of NR from ER (ER-NR)		
ER - NR 765 kV Sasaram - Fatehpur	111.08	**111.08**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	**50.67**
ER - NR 765 kV Gaya - Balia	213.79	**213.79**
ER - NR HVDC Alipurduar - Agra	0.00	**0.00**
ER-NR 400 kV Patna - Balia D/C	192.05	**192.05**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	**3.14**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	**0.00**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	**63.12**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	**3.31**
ER - NR 400 kV Sasaram -Varanasi	41.13	**41.13**
ER - NR 400 kV Sasaram -Allahabad	0.13	**0.13**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	**26.02**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	**2.88**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	**0.00**
ER - NR 132 kV Rihand - Garhwa	0.00	**0.00**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	**44.01**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	**2.89**
Total ER-NR	**754.22**	**754.22**
Import of NR from NER (NER-NR)		
NER-NR HVDC Biswanath Chariali - Agra	0.00	**0.00**
Total NER - NR	**0.00**	**0.00**
Export of NR to ER (NR-ER)		
NR - ER 765 kV Sasaram - Fatehpur	0.00	**0.00**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	**65.96**
NR - ER 765 kV Gaya - Balia	0.00	**0.00**

	Apr'24	Fin. Year 2024-25
Name of Line		
NR - ER HVDC Alipurduar - Agra	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	**87.39**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	**148.68**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	**0.29**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	**19.06**
NR - ER 400 kV Sasaram -Varanasi	0.00	**0.00**
NR - ER 400 kV Sasaram -Allahabad	10.41	**10.41**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	**0.00**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	**1.44**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	**0.00**
ER - NR 132 kV Rihand - Garhwa	18.99	**18.99**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	**0.00**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	**0.00**
Total NR - ER	**352.22**	**352.22**
Export of NR to NER (NER-NR)		
NR-NER HVDC Biswanath Chariali - Agra	433.33	**433.33**
Total NR - NER	**433.33**	**433.33**

	Apr'24	Fin. Year 2024-25
Name of Line		
Export of WR to ER (WR-ER)		
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	**388.72**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	**721.67**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	**0.05**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	**51.26**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	**3.12**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	**8.86**
WR - ER 220 kV Raigarh - Budhipadar	7.90	**7.90**
Total WR - ER	**1181.58**	**1181.58**
Import of WR from ER (ER - WR)		
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	**48.43**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	**2.75**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	**376.32**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	**22.01**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	**195.37**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	**1.27**
ER - WR 220 kV Raigarh - Budhipadar	15.69	**15.69**
Total ER - WR	**661.85**	**661.85**
Export of ER to NER (ER - NER)		
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	**20.06**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	**16.74**
ER - NER 220 kV Birpara - Salakati D/C	2.74	**2.74**
Total ER - NER	**39.54**	**39.54**
Import of ER from NER (NER - ER)		
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	**79.80**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	**164.15**

	Apr'24	Fin. Year 2024-25
Name of Line		
NER - ER 220 kV Birpara - Salakati D/C	18.58	**18.58**
Total NER - ER	**262.52**	**262.52**
Export of ER to SR (ER - SR)		
ER - SR HVDC Gazuwaka	413.69	**413.69**
ER - SR HVDC Talchar - Kolar	1069.04	**1069.04**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	**1640.93**
Total ER - SR	**3123.66**	**3123.66**
Import of ER from SR (SR - ER)		
SR - ER HVDC Gazuwaka	0.00	**0.00**
SR - ER HVDC Talchar - Kolar	0.00	**0.00**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	**0.00**
Total SR - ER	**0.00**	**0.00**

	Apr'24	Fin. Year 2024-25
Name of Line		
Export of WR to SR (WR-SR)		
WR - SR HVDC Bhadrawati	601.92	**601.92**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	**802.05**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	**1407.32**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	**0.00**
WR-SR HVDC Raigarh-Pugalur	2668.37	**2668.37**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	**73.01**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	**43.06**
WR-SR 765 kV Warora - Warangal D/C	1603.13	**1603.13**
Total WR - SR	**7198.86**	**7198.86**
Import of WR from SR (SR - WR)		
SR - WR HVDC Bhadrawati	2.36	**2.36**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	**0.55**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	**0.00**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	**429.02**
SR-WR HVDC Pugalur-Raigarh	0.00	**0.00**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	**0.00**
SR-WR 765 kV Warangal - Warora D/C	0.00	**0.00**
Total SR - WR	**431.93**	**431.93**
TOTAL ALL INDIA	**21906**	**21906**
***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**		

15.1 Import-Export of NR with WR during April 2024

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Apr-24	5.73	5.04	0.70	16.58	0.00	47.59	0.00	0.00		0.00	1.71	2.21	0.00	0.00	14.58	0.00	31.76	0.00	**125.90**
2-Apr-24	8.72	8.74	5.16	17.83	0.00	45.80	0.00	0.00		0.00	1.71	2.49	0.00	0.00	21.09	0.00	35.28	0.00	**146.82**
3-Apr-24	9.85	5.33	3.97	16.87	0.00	44.50	0.00	0.00		0.00	1.70	2.48	0.00	0.00	29.06	0.00	38.98	0.00	**152.74**
4-Apr-24	9.60	7.05	4.20	16.97	0.00	48.76	0.00		0.00	0.00	1.71	2.42	0.00	0.00	24.23	0.00	44.27		**159.21**
5-Apr-24	15.35	6.95	8.12	17.60	0.00	48.15	0.00	0.00		0.00	1.75	2.34	0.00	0.00	24.23	0.00	46.21		**170.70**
6-Apr-24	14.14	0.00	4.61	16.61	0.00	45.32	0.00	0.00		0.00	1.58	2.40	0.00	0.00	24.22	0.00	41.15		**150.03**
7-Apr-24	11.84	0.00	4.22	16.36	0.00	48.30	0.00	0.00		0.00	1.55	2.46	0.00	0.00	17.46	0.67	38.05	0.00	**140.91**
8-Apr-24	16.02	5.75	6.57	18.59	0.00	46.80	0.00	0.00		0.00	1.62	2.49	0.00	0.00	14.25	0.00	35.44	0.00	**147.53**
9-Apr-24	18.94	13.17	14.90	20.56	0.00	47.80	0.00	0.00		0.00	1.73	2.35	0.00	0.00	19.41	0.00	41.54	0.00	**180.40**
10-Apr-24	20.14	9.59	12.82	20.32	0.00	40.79	0.00	0.00		0.00	1.74	2.45	0.00	0.00	19.41	0.00	42.87	0.00	**170.13**
11-Apr-24	15.92	7.36	9.26	18.91	0.00	47.58	0.00	0.00		0.00	1.60	2.40	0.00	0.00	18.78	0.00	38.91	0.00	**160.72**
12-Apr-24	16.67	9.54	9.68	19.98	0.00	57.83	0.00	0.00		0.00	1.77	2.24	0.00	0.00	15.71	0.00	35.76	0.00	**169.18**
13-Apr-24	21.72	14.38	14.60	20.46	0.00	59.23	0.00	0.00	0.00	0.00	1.66	2.23	0.00	0.00	15.30	0.00	44.33	0.00	**193.91**
14-Apr-24	18.34	9.01	11.76	17.38	0.00	47.82	0.00	0.00		0.00	1.78	2.39	0.00	0.00	21.79	0.00	46.42	0.00	**176.69**
15-Apr-24	23.60	13.15	18.00	18.86	0.00	36.28	0.00	0.00		0.00	1.88	2.33	0.00	0.00	16.73	0.00	49.85	0.00	**180.68**
16-Apr-24	18.95	2.52	13.66	17.04	0.00	34.72	0.00	0.00		0.00	1.92	2.52	0.00	0.00	13.51	0.00	49.76	0.00	**154.60**
17-Apr-24	17.08	3.75	9.91	17.23	0.00	38.06	0.00	0.00		0.00	1.92	2.29	0.00	0.00	23.01	0.00	41.98	0.00	**155.23**
18-Apr-24	21.52	3.05	10.93	18.70	0.00	47.51	0.00	0.00		0.00	1.96	2.28	0.00	0.00	18.80	0.00	41.35	0.00	**166.10**
19-Apr-24	17.92	0.00	8.07	17.58	0.00	46.67	0.00	0.00		0.00	1.92	2.25	0.00	0.00	27.43	0.00	47.44	0.00	**169.28**
20-Apr-24	24.88	5.48	16.04	19.81	0.00	47.58	0.00	0.00		0.00	1.97	2.16	0.00	0.00	29.76	0.00	52.78	0.00	**200.46**
21-Apr-24	21.85	1.46	14.15	18.88	0.00	46.69	0.00	0.00		0.00	1.89	2.37	0.00	0.00	24.22	0.00	50.91	0.00	**182.42**
22-Apr-24	28.50	4.10	16.73	19.95	0.00	50.35	0.00	0.00		0.00	1.94	2.30	0.00	0.00	24.22	0.00	54.80	0.00	**202.89**
23-Apr-24	19.49	4.77	12.01	18.11	0.00	71.87	0.00	0.00		0.00	1.95	2.35	0.00	0.00	23.95	0.00	50.32	0.00	**204.82**
24-Apr-24	19.67	6.75	11.44	18.02	0.00	69.80	0.00	0.00		0.00	2.05	2.26	0.00	0.00	24.22	0.00	52.06	0.00	**206.27**
25-Apr-24	19.62	5.10	10.99	18.27	0.00	70.68	0.00	0.00		0.00	2.05	2.36	0.00	0.00	36.25	0.00	52.44	0.00	**217.76**
26-Apr-24	21.05	0.00	12.05	15.29	0.00	70.50	0.00	0.00		0.00	2.10	2.11	0.00	0.00	33.92	0.00	54.65	0.00	**211.67**
27-Apr-24	16.96	1.28	9.06	15.32	0.00	69.38	0.00	0.00		0.00	2.17	2.19	0.00	0.00	36.35	0.00	54.02	0.00	**206.73**
28-Apr-24	19.28	1.77	10.99	15.92	0.00	59.90	0.00	0.00		0.00	2.08	2.38	0.00	0.00	34.21	0.00	55.94	0.00	**202.47**
29-Apr-24	18.66	2.35	10.88	16.35	0.00	47.16	0.00	0.00		0.00	2.13	2.10	0.00	0.00	32.01	0.00	51.05	0.00	**182.69**
30-Apr-24	17.64	0.00	9.05	15.50	0.00	42.21	0.00	0.00		0.00	2.10	2.27	0.00	0.00	39.86	0.00	53.15	0.00	**181.78**
Total	**529.65**	**157.44**	**304.53**	**535.85**	**0.00**	**1525.63**	**0.00**	**0.00**	**0.00**	**0.00**	**55.64**	**69.87**	**0.00**	**0.00**	**717.97**	**0.67**	**1373.47**	**0.00**	**5270.72**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during April 2024

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Apr-24	0.00	0.00	0.00	0.00	8.81	0.00	6.07	7.40		5.14	0.00	0.00	2.54	21.58	0.00	17.45	0.00	7.20	**76.19**
2-Apr-24	0.00	0.00	0.00	0.00	9.79	0.00	6.01	7.79		6.51	0.00	0.00	2.32	22.34	0.00	17.06	0.00	5.08	**76.90**
3-Apr-24	0.00	0.00	0.00	0.00	8.88	0.00	6.06	7.33		7.20	0.00	0.00	2.13	22.53	0.00	16.77	0.00	0.00	**70.90**
4-Apr-24	0.00	0.00	0.00	0.00	9.44	0.00	6.14		8.05	6.65	0.00	0.00	2.10	22.51	0.00	20.13	0.00		**75.02**
5-Apr-24	0.00	0.00	0.00	0.00	8.84	0.00	6.65	4.35		5.59	0.00	0.00	1.67	22.37	0.00	6.85	0.00		**56.32**
6-Apr-24	0.00	0.51	0.00	0.00	7.71	0.00	6.06	7.10		8.68	0.00	0.00	1.81	22.54	0.00	13.43	0.00		**67.84**
7-Apr-24	0.00	0.12	0.00	0.00	8.75	0.00	6.07	8.67		9.25	0.00	0.00	2.12	22.22	0.00	19.52	0.00	0.00	**76.72**
8-Apr-24	0.00	0.00	0.00	0.00	9.40	0.00	7.14	10.84		7.49	0.00	0.00	1.94	22.31	0.00	21.35	0.00	6.23	**86.70**
9-Apr-24	0.00	0.00	0.00	0.00	9.24	0.00	9.09	8.95		3.85	0.00	0.00	1.42	21.88	0.00	13.87	0.00	4.64	**72.94**
10-Apr-24	0.00	0.00	0.00	0.00	8.90	0.00	9.52	10.00		5.05	0.00	0.00	1.50	22.19	0.00	17.00	0.00	5.21	**79.37**
11-Apr-24	0.00	0.00	0.00	0.00	9.24	0.00	8.51	11.99		5.50	0.00	0.00	1.69	22.52	0.00	24.28	0.00	5.01	**88.74**
12-Apr-24	0.00	0.00	0.00	0.00	9.32	0.00	9.44	11.40		4.06	0.00	0.00	1.62	22.07	0.00	22.76	0.00	4.01	**84.68**
13-Apr-24	0.00	0.00	0.00	0.00	10.44	0.00	7.27	8.46	0.00	0.32	0.00	0.00	1.29	22.47	0.00	15.62	0.00	1.53	**67.40**
14-Apr-24	0.00	0.00	0.00	0.00	9.91	0.00	7.26	10.08		2.81	0.00	0.00	1.62	10.60	0.00	20.72	0.00	3.62	**66.62**
15-Apr-24	0.00	0.00	0.00	0.00	11.22	0.00	8.44	9.35		1.57	0.00	0.00	1.48	10.90	0.00	20.00	0.00	2.32	**65.28**
16-Apr-24	0.00	0.00	0.00	0.00	8.08	0.00	12.18	9.05		5.26	0.00	0.00	2.15	10.78	0.00	18.75	0.00	4.58	**70.83**
17-Apr-24	0.00	0.00	0.00	0.00	8.88	0.00	12.13	8.50		5.73	0.00	0.00	3.03	10.78	0.00	15.57	0.00	5.25	**69.87**
18-Apr-24	0.00	0.00	0.00	0.00	7.80	0.00	12.10	5.64		4.25	0.00	0.00	2.51	12.04	0.00	6.10	0.00	4.58	**55.02**
19-Apr-24	0.00	4.32	0.00	0.00	5.00	0.00	12.15	9.04		6.85	0.00	0.00	2.23	21.35	0.00	11.74	0.00	8.22	**80.90**
20-Apr-24	0.00	0.00	0.00	0.00	7.92	0.00	12.17	6.52		2.15	0.00	0.00	1.93	22.25	0.00	9.85	0.00	2.40	**65.19**
21-Apr-24	0.00	0.00	0.00	0.00	7.66	0.00	10.06	6.37		3.86	0.00	0.00	1.37	21.81	0.00	8.93	0.00	4.40	**64.46**
22-Apr-24	0.00	0.00	0.00	0.00	7.35	0.00	6.05	5.66		3.17	0.00	0.00	1.07	22.31	0.00	6.39	0.00	4.14	**56.14**
23-Apr-24	0.00	0.00	0.00	0.00	6.54	0.00	7.02	7.45		4.35	0.00	0.00	2.18	22.06	0.00	12.57	0.00	6.63	**68.80**
24-Apr-24	0.00	0.00	0.00	0.00	7.19	0.00	8.67	7.95		4.45	0.00	0.00	2.21	22.43	0.00	14.12	0.00	6.82	**73.84**
25-Apr-24	0.00	0.00	0.00	0.00	7.15	0.00	12.16	9.20		5.50	0.00	0.00	2.44	22.34	0.00	19.17	0.00	7.65	**85.61**
26-Apr-24	0.00	3.27	0.00	0.00	5.36	0.00	12.06	9.56		7.61	0.00	0.00	1.95	22.38	0.00	15.34	0.00	9.10	**86.63**
27-Apr-24	0.00	0.00	0.00	0.00	6.98	0.00	2.65	9.40		6.44	0.00	0.00	2.42	22.51	0.00	18.53	0.00	7.60	**76.53**
28-Apr-24	0.00	0.00	0.00	0.00	6.89	0.00	11.69	6.49		5.51	0.00	0.00	2.24	22.22	0.00	12.88	0.00	6.75	**74.67**
29-Apr-24	0.00	0.00	0.00	0.00	7.35	0.00	6.47	8.92		6.55	0.00	0.00	2.33	21.39	0.00	16.94	0.00	7.03	**76.98**
30-Apr-24	0.00	2.27	0.00	0.00	5.93	0.00	12.17	6.63		7.72	0.00	0.00	2.38	22.00	0.00	10.21	0.00	9.03	**78.34**
Total	**0.00**	**10.49**	**0.00**	**0.00**	**245.97**	**0.00**	**259.46**	**240.09**	**8.05**	**159.07**	**0.00**	**0.00**	**59.69**	**609.68**	**0.00**	**463.90**	**0.00**	**139.03**	**2195.43**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during April 2024

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Apr-24	6.75	7.21	6.38		5.50	2.29	0.00	3.86	0.21	1.33	0.00	1.30			0.00	2.13		36.96	0.00	0.00
2-Apr-24	5.20	4.98	6.40		5.40	0.19	0.00	2.40	0.00	1.10	0.00	0.70	0.96			1.45		28.78	0.00	0.00
3-Apr-24	3.98	1.33	6.74		3.60	0.00	0.00	1.10	0.00	1.77	0.00	2.95				0.51		21.98	0.00	0.00
4-Apr-24	3.08	0.00	7.05		2.65	0.00	0.00	0.29	0.00	1.97	0.00	1.15			0.00	0.49		16.68	0.00	0.00
5-Apr-24	3.22	0.00	7.08		2.16	0.00	0.00	0.11	0.00	1.96	0.00	1.35			0.00	0.04		15.92	0.00	0.00
6-Apr-24	2.75	0.00	7.40		2.15	0.00	0.00	0.00	0.00	1.78	0.00	1.04			0.00	0.63		15.75	0.00	0.00
7-Apr-24	3.72	0.35	8.71		6.25	0.00	0.00	1.40	0.00	1.51	0.00	1.01			0.00	0.38		23.33	0.00	0.00
8-Apr-24	5.35	4.83	7.71		10.54	0.00	0.00	3.59	0.37	0.95	0.00	1.28			0.00	1.47		36.09	0.00	0.00
9-Apr-24	6.96	6.99	8.73		12.56	0.10	0.00	3.10	0.66	0.60	0.01	1.10			0.00	3.40		44.21	0.00	0.00
10-Apr-24	6.52	4.59	8.12		9.82	0.00	0.00	2.65	0.38	0.80	0.00	0.90	0.00		0.00	2.58		36.36	0.00	0.00
11-Apr-24	6.10	4.68	8.12		9.09	0.23	0.00	3.23	0.40	1.22	0.00	0.62			0.00	2.44		36.13	0.00	0.00
12-Apr-24	7.25	10.47	10.01		9.85	0.33	0.00	3.87	0.73	0.98	0.00	0.92	0.48		0.00	2.72		47.61	0.00	0.00
13-Apr-24	6.41	5.24	9.02		8.86	0.00	0.00	3.22	0.54	1.16	0.00	0.66			0.00	2.24		37.35	0.00	0.00
14-Apr-24	2.54	0.00	6.99		5.09	0.00	0.00	1.53	0.00	1.41	0.00	0.67	0.00		0.00	0.99		19.22	0.00	0.00
15-Apr-24	4.13	0.00	7.11		6.99	0.00	0.00	2.07	0.00	1.41	0.00	0.90			0.00	0.30		22.91	0.00	0.00
16-Apr-24	1.61	0.00	4.83		4.48	0.00	0.00	1.14	0.00	1.68	0.00	0.02				0.95		14.71	0.00	0.00
17-Apr-24	3.50	0.00	5.05		7.29	0.00	0.00	2.67	0.00	1.20	0.00	0.50				1.69		21.90	0.00	0.00
18-Apr-24	3.36	0.00	4.98		6.93	0.00	0.00	1.53	0.00	1.40	0.00	0.62	0.00		0.00	1.79		20.61	0.00	0.00
19-Apr-24	2.57	0.00	6.08		6.19	0.00	0.00	1.06	0.00	1.28	0.00	1.42	0.00		0.00	1.81		20.41		0.00
20-Apr-24	3.60	0.00	7.45		8.52	0.00	0.00	3.20	0.00	0.99	0.12	0.68			0.00	2.40	0.34	27.30	0.00	0.00
21-Apr-24	2.74	0.00	5.96		7.40	0.00	0.00	3.51	0.00	1.22	0.00	0.48	0.48		0.00	1.99	0.92	24.70	0.00	0.00
22-Apr-24	3.67	0.00	6.81		6.35	0.00	0.00	2.36	0.00	1.13	0.00	0.48	0.00		0.00	1.78	0.35	22.93	0.00	0.00
23-Apr-24	2.52	0.00	7.06		5.01	0.00	0.00	2.94	0.00	1.52	0.00	0.35			0.00	1.81	0.05	21.26	0.00	0.00
24-Apr-24	3.06	0.00	7.85		5.95	0.00	0.00	2.60	0.00	1.18	0.00	0.55	0.00		0.00	1.86		23.05	0.00	0.00
25-Apr-24	3.40	0.00	7.17		7.20	0.00	0.00	2.94	0.00	1.27	0.00	0.93			0.00	1.80	0.60	25.31	0.00	0.00
26-Apr-24	0.66	0.00	8.36		5.60	0.00	0.00	0.54	0.00	1.58	0.00	0.52	0.48		0.00	0.68	0.15	18.57	0.00	0.00
27-Apr-24	1.47	0.00	6.12		4.15	0.00	0.00	0.52	0.02	1.61	0.00	0.42	0.48		0.00	0.60	0.48	15.87	0.00	0.00
28-Apr-24	1.37	0.00	5.69		4.58	0.00	0.00	1.79		1.50	0.00	0.73			0.00	1.01	0.00	16.67	0.00	0.00
29-Apr-24	1.99	0.00	8.24		8.34	0.00	0.00	3.40		1.71	0.00	0.96	0.00		0.00	1.81	0.00	26.45	0.00	0.00
30-Apr-24	1.60	0.00	6.57		3.55	0.00	0.00	0.50		1.91	0.00	0.81	0.00		0.00	0.26	0.00	15.20	0.00	0.00
Total	**111.08**	**50.67**	**213.79**	**0.00**	**192.05**	**3.14**	**0.00**	**63.12**	**3.31**	**41.13**	**0.13**	**26.02**	**2.88**	**0.00**	**0.00**	**44.01**	**2.89**	**754.22**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.2 Import-Export of NR with ER & NER during April 2024

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Apr-24	0.00	0.00	0.00		0.00	0.00	1.39	0.00	0.00	0.00	0.22	0.00			0.00	0.00		**1.61**	17.08	**17.08**
2-Apr-24	0.00	0.00	0.00		0.00	0.00	2.99	0.00	0.79	0.00	0.30	0.00	0.00			0.00		**4.08**	13.02	**13.02**
3-Apr-24	0.00	0.00	0.00		0.00	2.87	4.83	0.00	1.76	0.00	0.62	0.00				0.00		**10.08**	11.45	**11.45**
4-Apr-24	0.00	1.06	0.00		0.00	4.66	5.62	0.00	1.56	0.00	0.90	0.00			0.76	0.00		**14.56**	9.77	**9.77**
5-Apr-24	0.00	1.15	0.00		0.00	4.86	6.13	0.00	2.40	0.00	0.90	0.00			0.82	0.00		**16.26**	16.10	**16.10**
6-Apr-24	0.00	1.25	0.00		0.00	4.05	5.20	0.29	2.19	0.00	0.64	0.00			0.85	0.00		**14.47**	17.16	**17.16**
7-Apr-24	0.00	0.00	0.00		0.00	1.73	3.65	0.00	0.40	0.00	0.32	0.00			0.82	0.00		**6.92**	16.64	**16.64**
8-Apr-24	0.00	0.00	0.00		0.00	0.56	3.10	0.00	0.00	0.00	0.32	0.00			0.57	0.00		**4.55**	15.39	**15.39**
9-Apr-24	0.00	0.00	0.00		0.00	0.00	3.05	0.00	0.00	0.00	0.00	0.00			0.79	0.00		**3.84**	9.94	**9.94**
10-Apr-24	0.00	0.00	0.00		0.00	2.65	4.95	0.00	0.00	0.00	0.18	0.00	0.00		0.89	0.00		**8.67**	12.00	**12.00**
11-Apr-24	0.00	0.00	0.00		0.00	0.00	3.04	0.00	0.00	0.00	0.11	0.00			0.89	0.00		**4.04**	15.98	**15.98**
12-Apr-24	0.00	0.00	0.00		0.00	0.00	2.82	0.00	0.00	0.00	0.17	0.00	0.00		0.68	0.00		**3.67**	16.74	**16.74**
13-Apr-24	0.00	0.00	0.00		0.00	1.09	3.65	0.00	0.00	0.00	0.01	0.00			0.27	0.00		**5.02**	16.87	**16.87**
14-Apr-24	0.00	2.37	0.00		0.00	3.15	4.93	0.00	0.82	0.00	0.25	0.00	0.00		0.83	0.00		**12.35**	15.54	**15.54**
15-Apr-24	0.00	2.62	0.00		0.00	3.33	4.85	0.00	0.39	0.00	0.29	0.00			0.79	0.00		**12.27**	14.35	**14.35**
16-Apr-24	0.00	8.16	0.00		0.00	5.44	6.20	0.00	1.51	0.00	0.65	0.00				0.00		**21.96**	9.60	**9.60**
17-Apr-24	0.00	3.20	0.00		0.00	2.95	3.59	0.00	0.57	0.00	0.07	0.00				0.00		**10.38**	9.46	**9.46**
18-Apr-24	0.00	2.40	0.00		0.00	4.01	4.34	0.00	1.18	0.00	0.35	0.00	0.48		0.68	0.00		**13.44**	8.60	**8.60**
19-Apr-24	0.00	2.97	0.00		0.00	4.49	6.12	0.00	1.32	0.00	0.22	0.00	0.48		0.69	0.00		**16.29**		**0.00**
20-Apr-24	0.00	0.84	0.00		0.00	1.79	4.74	0.00	0.57	0.00	0.00	0.00			0.85	0.00	0.00	**8.79**	12.22	**12.22**
21-Apr-24	0.00	2.96	0.00		0.00	1.50	4.22	0.00	0.35	0.00	0.22	0.00	0.00		0.81	0.00	0.00	**10.06**	16.71	**16.71**
22-Apr-24	0.00	3.06	0.00		0.00	1.03	5.00	0.00	0.50	0.00	0.05	0.00	0.00		0.78	0.00	0.00	**10.42**	16.64	**16.64**
23-Apr-24	0.00	1.99	0.00		0.00	4.46	7.11	0.00	0.77	0.00	0.40	0.00			0.71	0.00	0.00	**15.44**	17.33	**17.33**
24-Apr-24	0.00	1.02	0.00		0.00	4.03	6.65	0.00	0.56	0.00	0.20	0.00	0.48		0.58	0.00		**13.52**	16.62	**16.62**
25-Apr-24	0.00	0.88	0.00		0.00	4.44	6.40	0.00	0.34	0.00	0.12	0.00			0.83	0.00	0.00	**13.01**	16.92	**16.92**
26-Apr-24	0.00	8.31	0.00		0.00	6.76	7.51	0.00	1.08	0.00	0.52	0.00	0.00		0.86	0.00	0.00	**25.04**	17.95	**17.95**
27-Apr-24	0.00	7.22	0.00		0.00	5.43	7.29	0.00	0.00	0.00	0.60	0.00	0.00		0.87	0.00	0.00	**21.41**	17.08	**17.08**
28-Apr-24	0.00	6.79	0.00		0.00	4.21	6.35	0.00		0.00	0.36	0.00			0.89	0.00	0.00	**18.60**	16.96	**16.96**
29-Apr-24	0.00	1.96	0.00		0.00	2.39	5.74	0.00		0.00	0.62	0.00	0.00		0.84	0.00	0.00	**11.55**	16.59	**16.59**
30-Apr-24	0.00	5.75	0.00		0.00	5.51	7.22	0.00		0.00	0.80	0.00	0.00		0.64	0.00	0.00	**19.92**	22.62	**22.62**
Total	**0.00**	**65.96**	**0.00**	**0.00**	**0.00**	**87.39**	**148.68**	**0.29**	**19.06**	**0.00**	**10.41**	**0.00**	**1.44**	**0.00**	**18.99**	**0.00**	**0.00**	**352.22**	**433.33**	**433.33**
Disclaimer:-	Blank entry if the line under outage/shutdown on corrosponding day																			

15.3 Import and Export of ER with WR & NER during April 2024

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Apr-24	2.4	17.7	0.0	0.1	0.0	0.4	0.0	**20.56**	8.4	0.1	17.6	3.5	8.3	0.0	0.7	**38.50**	0.00	0.00	0.00	**0.00**	7.76	13.87	2.44	**24.07**
2-Apr-24	2.4	22.0	0.0	0.1	0.0	0.4	0.2	**25.12**	5.6	0.1	15.8	2.7	7.5	0.1	0.3	**32.08**	0.03	0.00	0.00	**0.03**	3.69	7.17	0.89	**11.75**
3-Apr-24	6.1	23.4	0.0	0.5	0.0	0.6	0.4	**31.13**	1.3	0.0	13.6	1.4	6.7	0.3	0.2	**23.57**	0.33	0.07	0.02	**0.41**	2.78	6.47	0.54	**9.80**
4-Apr-24	12.3	23.7	0.0	0.8	0.0	2.5	0.2	**39.50**	0.0	0.0	13.2	0.4	8.1	0.0	0.3	**21.97**	0.54	0.18	0.07	**0.79**	1.87	4.23	0.29	**6.39**
5-Apr-24	17.2	27.7	0.0	2.3	0.1	1.9	0.5	**49.67**	0.0	0.0	11.1	0.0	5.8	0.0	0.1	**17.13**	0.00	0.00	0.00	**0.00**	3.65	7.71	0.70	**12.06**
6-Apr-24	13.6	32.8	0.0	1.5	0.2	0.0	1.0	**49.17**	0.0	0.0	10.7	0.1	6.5	0.0	0.0	**17.34**	0.10	0.06	0.01	**0.17**	3.22	7.44	0.65	**11.31**
7-Apr-24	5.5	25.9	0.0	0.3	0.0	0.0	0.2	**31.84**	2.3	0.0	13.9	1.4	9.5	0.0	0.2	**27.28**	0.00	0.00	0.00	**0.00**	4.15	10.07	0.90	**15.12**
8-Apr-24	1.7	19.0	0.0	0.0	0.0	0.0	0.1	**20.78**	6.6	0.0	17.8	2.7	8.7	0.0	0.3	**36.17**	0.63	0.33	0.10	**1.06**	2.78	5.57	0.41	**8.76**
9-Apr-24	4.7	14.4	0.0	0.8	0.2	0.0	0.3	**20.41**	5.6	0.1	17.3	1.9	5.1	0.0	0.3	**30.29**	1.89	1.82	0.29	**4.01**	1.15	2.80	0.13	**4.09**
10-Apr-24	4.8	20.5	0.0	0.7	0.0	0.0	0.7	**26.76**	2.8	0.0	14.9	1.3	5.8	0.0	0.2	**25.11**	2.37	2.41	0.31	**5.09**	1.14	2.62	0.10	**3.86**
11-Apr-24	1.4	21.4	0.0	0.1	0.0	0.0	0.1	**23.01**	5.3	0.0	15.5	1.7	4.7	0.0	0.9	**28.02**	0.67	0.19	0.04	**0.90**	1.91	4.38	0.29	**6.58**
12-Apr-24	3.3	21.0	0.0	0.8	0.0	0.0	0.1	**25.22**	6.1	0.0	16.9	1.6	4.0	0.0	0.6	**29.17**	0.92	0.39	0.07	**1.38**	1.67	3.94	0.22	**5.83**
13-Apr-24	2.0	12.7	0.0	0.3	0.2	0.0	0.2	**15.33**	3.5	0.1	15.0	1.0	3.5	0.0	0.3	**23.36**	0.66	0.09	0.02	**0.76**	1.84	4.35	0.28	**6.47**
14-Apr-24	12.1	18.0	0.0	1.9	0.1	0.0	0.6	**32.65**	0.2	0.0	13.1	0.3	5.9	0.0	0.3	**19.85**	0.87	0.32	0.04	**1.23**	1.79	4.12	0.28	**6.19**
15-Apr-24	20.8	24.5	0.0	3.3	0.0	0.0	1.1	**49.59**	0.0	0.1	12.0	0.0	7.2	0.0	0.0	**19.30**	1.00	0.70	0.12	**1.81**	1.11	3.19	0.20	**4.50**
16-Apr-24	23.1	26.3	0.0	3.6	0.1	0.0	0.6	**53.72**	0.0	0.1	12.2	0.1	7.3	0.0	0.2	**19.80**	2.04	2.02	0.18	**4.24**	0.84	1.96	0.20	**3.00**
17-Apr-24	15.7	29.0	0.0	1.8	0.0	0.0	0.3	**46.83**	0.6	0.1	15.0	0.6	7.0	0.0	0.6	**23.89**	0.63	1.04	0.14	**1.81**	2.84	4.69	0.48	**8.01**
18-Apr-24	13.6	27.0	0.0	1.8	0.1	0.0	0.1	**42.61**	0.0	0.0	12.4	0.2	4.6	0.0	0.5	**17.76**	1.92	2.54	0.29	**4.74**	2.07	3.87	0.36	**6.30**
19-Apr-24	13.7	35.1	0.0	1.9	0.0	0.0	0.0	**50.81**	0.0	0.0	11.0	0.3	5.7	0.0	1.0	**17.97**	0.25	0.20	0.06	**0.52**	2.37	4.47	0.55	**7.39**
20-Apr-24	17.0	31.1	0.0	2.5	0.0	0.0	0.1	**50.77**	0.0	0.0	11.4	0.1	5.7	0.0	0.6	**17.81**	0.46	0.95	0.15	**1.55**	3.02	5.92	0.96	**9.90**
21-Apr-24	15.5	29.6	0.0	2.0	0.0	0.0	0.3	**47.34**	0.0	0.0	12.5	0.1	6.7	0.0	0.5	**19.83**	0.00	0.00	0.00	**0.00**	4.05	8.28	1.22	**13.56**
22-Apr-24	18.8	24.0	0.0	2.5	0.0	0.0	0.3	**45.62**	0.0	0.1	12.5	0.0	6.4	0.0	0.7	**19.76**	0.41	0.32	0.15	**0.87**	2.88	5.33	0.59	**8.80**
23-Apr-24	17.6	20.8	0.0	2.2	0.1	0.0	0.1	**40.68**	0.0	0.0	11.7	0.1	6.6	0.0	0.9	**19.32**	1.18	1.14	0.26	**2.59**	1.93	4.02	0.26	**6.21**
24-Apr-24	16.4	18.4	0.0	1.8	0.0	0.0	0.1	**36.70**	0.0	0.1	12.1	0.2	8.4	0.1	1.0	**21.83**	0.71	0.54	0.10	**1.35**	2.21	4.52	0.43	**7.16**
25-Apr-24	15.2	17.5	0.0	1.4	0.0	0.4	0.2	**34.69**	0.0	0.2	12.2	0.3	9.9	0.3	0.8	**23.74**	0.98	0.78	0.18	**1.93**	2.12	4.41	0.39	**6.92**
26-Apr-24	26.5	17.7	0.0	4.0	0.0	0.6	0.2	**48.98**	0.0	1.4	8.8	0.0	8.2	0.1	0.5	**19.08**	0.56	0.31	0.07	**0.94**	1.82	4.13	0.43	**6.37**
27-Apr-24	21.9	22.8	0.0	2.9	0.1	0.5	0.0	**48.24**	0.0	0.2	7.1	0.0	6.6	0.0	0.7	**14.61**	0.74	0.32	0.09	**1.15**	2.40	4.80	0.62	**7.81**
28-Apr-24	22.3	28.1	0.0	3.3	0.5	0.5	0.1	**54.77**	0.0	0.0	7.0	0.0	5.8	0.1	0.9	**13.93**	0.03	0.00	0.00	**0.03**	3.11	5.96	1.17	**10.24**
29-Apr-24	20.1	33.5	0.0	2.7	0.2	0.4	0.0	**57.04**	0.0	0.0	7.2	0.0	5.2	0.0	1.2	**13.60**	0.12	0.03	0.00	**0.15**	2.91	5.33	1.10	**9.34**
30-Apr-24	21.0	36.1	0.0	3.4	0.9	0.6	0.0	**62.04**	0.0	0.0	4.9	0.0	4.1	0.0	0.8	**9.79**	0.02	0.00	0.00	**0.02**	4.70	8.53	1.50	**14.73**
Total	**388.72**	**721.67**	**0.05**	**51.26**	**3.12**	**8.86**	**7.90**	**1181.58**	**48.43**	**2.75**	**376.32**	**22.01**	**195.37**	**1.27**	**15.69**	**661.85**	**20.06**	**16.74**	**2.74**	**39.54**	**79.80**	**164.15**	**18.58**	**262.52**

Date	15.4 Import and Export of SR with ER & WR during April 2024																							
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)								
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Apr-24	14.85	36.16	57.98	**108.99**	0.00	0.00	0.00	**0.00**	20.29	30.24	59.32	0.00	119.78	2.56	0.00	61.43	**293.62**	0.00	0.00	0.00	12.81	0.00	0.00	0.00	0.00	**12.81**
2-Apr-24	15.22	36.16	56.60	**107.98**	0.00	0.00	0.00	**0.00**	22.22	30.57	52.68	0.00	121.75	2.51	0.00	60.90	**290.63**	0.00	0.00	0.00	14.23	0.00	0.00	0.00	0.00	**14.23**
3-Apr-24	12.51	36.14	54.41	**103.06**	0.00	0.00	0.00	**0.00**	24.17	30.35	50.55	0.00	114.83	2.54	0.00	57.92	**280.36**	0.00	0.00	0.00	17.51	0.00	0.00	0.00	0.00	**17.51**
4-Apr-24	13.68	36.17	56.41	**106.26**	0.00	0.00	0.00	**0.00**	19.67	35.21	56.00	0.00	96.47	2.62	0.57	60.33	**270.87**	0.00	0.00	0.00	14.57	0.00	0.00	0.00	0.00	**14.57**
5-Apr-24	13.80	35.99	55.55	**105.34**	0.00	0.00	0.00	**0.00**	23.22	37.55	60.33	0.00	95.13	2.51	0.00	60.20	**278.94**	0.00	0.00	0.00	13.34	0.00	0.00	0.00	0.00	**13.34**
6-Apr-24	12.93	36.14	57.03	**106.10**	0.00	0.00	0.00	**0.00**	24.16	38.50	62.18	0.00	96.50	1.78	0.98	58.81	**282.91**	0.00	0.00	0.00	11.90	0.00	0.00	0.00	0.00	**11.90**
7-Apr-24	11.50	27.89	57.51	**96.90**	0.00	0.00	0.00	**0.00**	24.13	29.82	58.95	0.00	100.19	2.41	1.47	59.57	**276.54**	0.00	0.00	0.00	13.01	0.00	0.00	0.00	0.00	**13.01**
8-Apr-24	12.41	36.11	58.32	**106.84**	0.00	0.00	0.00	**0.00**	24.14	25.04	57.32	0.00	115.38	2.49	1.64	58.36	**284.37**	0.00	0.00	0.00	13.43	0.00	0.00	0.00	0.00	**13.43**
9-Apr-24	14.85	36.11	55.26	**106.22**	0.00	0.00	0.00	**0.00**	20.62	21.20	49.03	0.00	116.43	2.54	1.61	53.04	**264.47**	0.00	0.37	0.00	15.88	0.00	0.00	0.00	0.00	**16.25**
10-Apr-24	14.84	36.11	55.62	**106.57**	0.00	0.00	0.00	**0.00**	22.38	21.87	45.99	0.00	114.11	2.51	1.59	54.42	**262.87**	0.00	0.00	0.00	15.32	0.00	0.00	0.00	0.00	**15.32**
11-Apr-24	14.77	36.12	57.68	**108.57**	0.00	0.00	0.00	**0.00**	20.88	26.70	49.55	0.00	110.52	2.63	1.60	57.74	**269.62**	0.00	0.00	0.00	14.34	0.00	0.00	0.00	0.00	**14.34**
12-Apr-24	14.46	36.11	57.45	**108.02**	0.00	0.00	0.00	**0.00**	16.44	27.99	50.64	0.00	111.87	2.61	1.64	59.72	**270.91**	0.00	0.00	0.00	15.08	0.00	0.00	0.00	0.00	**15.08**
13-Apr-24	14.86	36.10	54.56	**105.52**	0.00	0.00	0.00	**0.00**	17.41	26.54	48.71	0.00	121.99	2.61	1.59	36.45	**255.30**	0.00	0.08	0.00	15.88	0.00	0.00	0.00	0.00	**15.96**
14-Apr-24	14.97	36.11	55.97	**107.05**	0.00	0.00	0.00	**0.00**	12.95	26.36	45.88	0.00	68.71	2.48	1.47	45.57	**203.42**	0.00	0.00	0.00	12.61	0.00	0.00	0.00	0.00	**12.61**
15-Apr-24	14.98	35.15	50.42	**100.55**	0.00	0.00	0.00	**0.00**	16.19	17.47	38.13	0.00	57.78	2.08	1.70	45.01	**178.36**	0.00	0.00	0.00	17.58	0.00	0.00	0.00	0.00	**17.58**
16-Apr-24	14.98	35.77	54.57	**105.32**	0.00	0.00	0.00	**0.00**	19.32	27.13	49.26	0.00	80.44	2.54	1.68	46.57	**226.94**	2.36	0.00	0.00	16.25	0.00	0.00	0.00	0.00	**18.61**
17-Apr-24	14.97	36.11	57.47	**108.55**	0.00	0.00	0.00	**0.00**	20.79	32.85	51.59	0.00	82.59	2.73	1.79	56.57	**248.91**	0.00	0.00	0.00	14.26	0.00	0.00	0.00	0.00	**14.26**
18-Apr-24	14.23	36.12	49.80	**100.15**	0.00	0.00	0.00	**0.00**	22.06	26.45	47.39	0.00	97.50	2.76	1.85	53.72	**251.73**	0.00	0.00	0.00	14.95	0.00	0.00	0.00	0.00	**14.95**
19-Apr-24	11.97	36.12	56.50	**104.59**	0.00	0.00	0.00	**0.00**	20.99	24.57	46.09	0.00	80.43	2.70	1.99	54.78	**231.55**	0.00	0.00	0.00	10.99	0.00	0.00	0.00	0.00	**10.99**
20-Apr-24	13.70	36.12	57.70	**107.52**	0.00	0.00	0.00	**0.00**	11.87	28.67	44.92	0.00	69.76	2.18	1.64	54.78	**213.82**	0.00	0.00	0.00	11.64	0.00	0.00	0.00	0.00	**11.64**
21-Apr-24	14.56	36.12	58.42	**109.10**	0.00	0.00	0.00	**0.00**	12.28	27.41	45.32	0.00	56.32	2.14	1.83	55.78	**201.08**	0.00	0.00	0.00	14.36	0.00	0.00	0.00	0.00	**14.36**
22-Apr-24	14.36	36.11	56.07	**106.54**	0.00	0.00	0.00	**0.00**	24.03	22.10	38.17	0.00	62.03	2.21	1.98	49.06	**199.58**	0.00	0.00	0.00	14.31	0.00	0.00	0.00	0.00	**14.31**
23-Apr-24	15.27	36.10	56.46	**107.83**	0.00	0.00	0.00	**0.00**	24.15	24.63	39.12	0.00	65.45	2.27	1.97	52.48	**210.07**	0.00	0.00	0.00	10.94	0.00	0.00	0.00	0.00	**10.94**
24-Apr-24	12.66	35.21	55.63	**103.50**	0.00	0.00	0.00	**0.00**	24.18	25.84	40.35	0.00	70.95	2.43	1.76	53.57	**219.08**	0.00	0.00	0.00	14.07	0.00	0.00	0.00	0.00	**14.07**
25-Apr-24	14.70	36.12	52.41	**103.23**	0.00	0.00	0.00	**0.00**	24.18	24.48	38.06	0.00	83.58	2.29	1.82	51.35	**225.76**	0.00	0.00	0.00	14.15	0.00	0.00	0.00	0.00	**14.15**
26-Apr-24	12.16	36.12	47.41	**95.69**	0.00	0.00	0.00	**0.00**	22.41	21.40	34.59	0.00	77.68	2.34	1.79	46.16	**206.37**	0.00	0.00	0.00	14.77	0.00	0.00	0.00	0.00	**14.77**
27-Apr-24	12.38	36.15	44.13	**92.66**	0.00	0.00	0.00	**0.00**	21.11	15.52	29.75	0.00	72.04	2.36	1.78	42.07	**184.63**	0.00	0.10	0.00	16.89	0.00	0.00	0.00	0.00	**16.99**
28-Apr-24	12.37	32.03	47.95	**92.35**	0.00	0.00	0.00	**0.00**	12.14	21.60	35.39	0.00	59.43	2.26	1.74	47.59	**180.15**	0.00	0.00	0.00	15.08	0.00	0.00	0.00	0.00	**15.08**
29-Apr-24	12.40	36.12	55.76	**104.28**	0.00	0.00	0.00	**0.00**	14.27	31.42	43.60	0.00	56.69	2.40	1.74	57.52	**207.64**	0.00	0.00	0.00	13.25	0.00	0.00	0.00	0.00	**13.25**
30-Apr-24	12.35	36.15	49.88	**98.38**	0.00	0.00	0.00	**0.00**	19.27	22.57	38.46	0.00	92.04	2.52	1.84	51.66	**228.36**	0.00	0.00	0.00	15.62	0.00	0.00	0.00	0.00	**15.62**
TOTAL	**413.69**	**1069.04**	**1640.93**	**3123.66**	**0.00**	**0.00**	**0.00**	**0.00**	**601.92**	**802.05**	**1407.32**	**0.00**	**2668.37**	**73.01**	**43.06**	**1603.13**	**7198.86**	**2.36**	**0.55**	**0.00**	**429.02**	**0.00**	**0.00**	**0.00**	**0.00**	**431.93**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 से मार्च 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
कुल Total	**86.47**	**18.58**	**346.08**	**0.00**	**694.34**	**0.00**	**0.76**	**0.00**

* Based on daily operational data

16.1 Import from neighbouring countries during April 2024

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Apr-24	1.11	0.00	0.00	0.00	0.00	1.37	0.58	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-Apr-24	1.39	0.11	0.00	0.00	0.00	1.43	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-Apr-24	0.46	0.00	0.00	0.00	0.00	0.78	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-Apr-24	0.55	0.00	0.00	0.00	0.00	0.00	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-Apr-24	0.00	0.00	0.00	0.00	0.00	0.24	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-Apr-24	0.07	0.00	0.00	0.00	0.00	0.88	0.35	0.00	0.00	0.00	0.00	0.00	0.00	0.00
7-Apr-24	0.52	0.00	0.00	0.00	0.00	0.96	0.36	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-Apr-24	0.18	0.00	0.00	0.00	0.00	0.67	0.40	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.81	0.02	0.00	0.00	0.00	0.00	0.00	0.00
10-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.60	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-Apr-24	0.00	0.00	0.00	0.00	0.00	0.00	0.79	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-Apr-24	0.00	0.00	0.00	0.00	0.00	0.26	0.64	0.02	0.00	0.00	0.00	0.00	0.00	0.00
17-Apr-24	2.75	0.48	0.00	0.00	0.00	4.52	1.01	0.14	0.00	0.00	0.00	0.00	0.00	0.00
18-Apr-24	3.30	0.35	0.00	0.00	0.00	1.87	0.85	0.09	0.00	0.00	0.00	0.00	0.00	0.00
19-Apr-24	0.73	0.00	0.00	0.00	0.00	2.66	0.91	0.06	0.00	0.00	0.00	0.00	0.00	0.00
20-Apr-24	1.56	0.00	0.00	0.00	0.00	2.18	0.67	0.00	0.00	0.00	0.00	0.00	0.00	0.00
21-Apr-24	1.58	0.00	0.00	0.00	0.00	3.23	0.91	0.00	0.00	0.00	0.00	0.00	0.00	0.00
22-Apr-24	1.25	0.00	0.00	0.00	0.00	2.69	1.10	0.07	0.00	0.00	0.00	0.00	0.00	0.00
23-Apr-24	0.50	0.00	0.00	0.00	0.00	1.21	1.07	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-Apr-24	0.75	0.00	0.00	0.00	0.00	1.37	0.92	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-Apr-24	0.00	0.00	0.00	0.00	0.13	0.81	0.79	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-Apr-24	0.00	0.00	0.00	0.00	0.34	0.55	0.79	0.00	0.00	0.00	0.00	0.00	0.00	0.00
27-Apr-24	0.00	0.00	0.00	0.00	0.31	0.51	0.79	0.00	0.00	0.00	0.00	0.00	0.00	0.00
28-Apr-24	0.00	0.00	0.00	0.00	1.31	2.27	0.79	0.14	0.00	0.00	0.00	0.00	0.00	0.00
29-Apr-24	0.00	0.00	0.00	0.00	0.90	3.53	0.79	0.25	0.00	0.00	0.00	0.00	0.00	0.00
30-Apr-24	0.00	0.00	0.00	0.00	0.00	3.89	0.79	0.10	0.00	0.00	0.00	0.00	0.00	0.00
Total	**16.70**	**0.94**	**0.00**	**0.00**	**2.99**	**37.88**	**19.63**	**0.89**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

16.2 Export to neighbouring countries during April 2024

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Apr-24	0.00	0.04	2.23	1.17	0.00	0.00	0.00	0.33	21.11	3.31	0.00	4.87	2.59	0.01
2-Apr-24	0.00	0.00	2.19	0.92	0.00	0.00	0.00	0.14	17.04	3.14	0.00	5.25	3.11	0.02
3-Apr-24	0.00	0.74	2.46	1.01	0.00	0.00	0.00	0.16	20.83	3.15	0.00	6.49	2.05	0.02
4-Apr-24	0.00	0.69	2.38	0.96	0.00	0.08	0.00	0.12	19.99	3.37	0.00	6.82	1.95	0.03
5-Apr-24	0.07	1.18	2.42	1.05	0.00	0.00	0.00	0.22	19.96	2.92	0.00	7.45	2.42	0.00
6-Apr-24	0.00	1.08	2.34	1.08	0.00	0.00	0.00	0.09	20.44	2.81	0.00	6.17	3.08	0.02
7-Apr-24	0.00	0.69	2.47	1.13	0.00	0.00	0.00	0.16	21.52	2.56	0.00	6.99	3.43	0.03
8-Apr-24	0.00	1.11	2.42	1.11	0.00	0.00	0.00	0.00	21.76	2.39	0.00	6.91	3.48	0.02
9-Apr-24	0.65	1.82	2.57	0.46	0.00	0.69	0.00	0.02	20.29	2.25	0.00	7.22	2.94	0.03
10-Apr-24	0.64	1.87	2.92	0.18	0.00	0.99	0.00	0.00	22.61	2.09	0.00	6.86	3.13	0.03
11-Apr-24	0.63	1.73	2.60	1.24	0.00	0.73	0.00	0.12	18.06	1.96	0.00	6.00	4.17	0.03
12-Apr-24	0.50	1.68	2.57	1.08	0.00	0.96	0.00	0.11	17.87	2.00	0.00	6.71	3.56	0.03
13-Apr-24	0.57	1.79	2.58	0.53	0.00	0.86	0.00	0.13	21.16	2.16	0.00	6.78	2.16	0.03
14-Apr-24	0.78	1.98	2.70	0.57	0.00	0.68	0.00	0.12	21.93	2.27	0.00	7.86	2.48	0.03
15-Apr-24	0.70	1.85	2.27	0.96	0.00	0.53	0.00	0.04	21.87	2.51	0.00	8.53	2.23	0.03
16-Apr-24	0.23	1.65	2.42	0.83	0.00	0.00	0.00	0.00	21.92	2.31	0.00	7.99	2.26	0.03
17-Apr-24	0.00	0.00	1.41	0.73	0.00	0.00	0.00	0.00	21.48	2.33	0.00	7.34	2.47	0.03
18-Apr-24	0.00	0.00	1.58	0.60	0.00	0.00	0.00	0.00	21.70	2.44	0.00	5.79	2.39	0.03
19-Apr-24	0.00	0.00	2.24	1.15	0.00	0.00	0.00	0.00	21.60	2.40	0.00	6.43	2.22	0.01
20-Apr-24	0.00	0.00	2.06	1.06	0.00	0.00	0.00	0.04	21.67	2.58	0.00	5.75	1.05	0.03
21-Apr-24	0.00	0.00	2.00	1.13	0.00	0.00	0.00	0.05	21.60	2.80	0.00	7.06	2.05	0.03
22-Apr-24	0.00	0.07	1.99	0.87	0.00	0.00	0.00	0.04	20.59	2.84	0.00	7.53	2.22	0.03
23-Apr-24	0.00	1.00	2.23	0.87	0.00	0.00	0.00	0.03	20.50	2.81	0.00	6.56	2.21	0.03
24-Apr-24	0.00	0.88	2.29	0.89	0.00	0.00	0.00	0.02	20.55	2.82	0.00	7.25	1.74	0.03
25-Apr-24	0.26	1.32	2.22	0.88	0.00	0.00	0.00	0.05	20.54	2.86	0.00	8.98	2.35	0.00
26-Apr-24	0.42	1.41	2.28	0.92	0.00	0.00	0.00	0.05	20.42	2.63	0.00	8.05	3.06	0.01
27-Apr-24	0.62	1.53	2.58	0.95	0.00	0.00	0.00	0.05	20.47	2.56	0.00	6.93	2.85	0.00
28-Apr-24	0.64	1.59	3.07	1.22	0.00	0.00	0.00	0.00	20.53	2.30	0.00	6.73	3.05	0.01
29-Apr-24	0.64	1.68	4.25	1.02	0.00	0.00	0.00	0.00	15.88	2.31	0.00	7.52	3.05	0.01
30-Apr-24	0.63	1.83	3.50	1.24	0.00	0.00	0.00	0.00	20.42	2.24	0.00	7.43	3.25	0.14
Total	**7.98**	**31.23**	**73.23**	**27.82**	**0.00**	**5.52**	**0.00**	**2.09**	**616.31**	**77.12**	**0.00**	**208.25**	**79.00**	**0.76**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – अप्रैल 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - APRIL 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

अप्रैल 2024 APRIL 2024			Apr'24- Mar'25	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	287	332	8925	34708
प.क्षे. WR	380	819	9826	19476
द.क्षे. SR	486	3439	9131	27995
पू.क्षे. ER	312	1318	6150	8302
पूर्वोत्तर क्षे. NER	100	13	1533	625
कुल TOTAL	1565	5921	35565	91106

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
कुल TOTAL	9860	7128	1565	5921

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
01.04.24 to 07.04.24	285.57	307.45	410.15	268.83	65.32
08.04.24 to 14.04.24	152.03	204.00	296.87	151.81	47.68
15.04.24 to 21.04.24	279.69	303.15	378.31	231.52	48.97
22.04.24 to 28.04.24	325.45	348.68	352.85	275.10	72.36

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अप्रैल 2024
EXCHANGES THROUGH POWER EXCHANGES - APRIL 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED	उत्तरी क्षेत्र NR	25.81	0.00
2	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		34.47	0.00
3	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		11.72	0.00
4	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		32.53	0.00
5	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED (infirm)		12.57	0.00
6	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED(Phalodi)		15.27	0.00
7	Adept Renewable Technologies Private Limited		29.96	0.00
8	Amp Energy Green Six Private Limited		25.12	0.00
9	Amplus Ages Private Limited		22.67	0.00
10	Ayana Renewable Power Three Private Limited		4.31	0.00
11	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		1.66	0.00
12	Chandigarh (UT)		35.70	1.21
13	Delhi		269.95	65.88
14	Grian Energy Private Limited		25.76	0.00
15	Haryana		646.25	33.67
16	Himachal Pradesh		180.28	264.56
17	IGSTPS JHAJJAR		13.03	0.00
18	Jammu Kashmir		22.20	269.98
19	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		25.04	0.00
20	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	18.70
21	NTPC ANTA GPS RLNG		0.02	0.00
22	NTPC AURAIYA GPS RLNG		0.03	0.00
23	NTPC Anta Solar		7.63	0.00
24	NTPC DADRI GPS RLNG		0.02	0.00
25	NTPC Dadri Stage I		7.57	0.00
26	NTPC Dadri Stage II		5.47	0.00
27	NTPC Rihand stage I		15.47	0.00
28	NTPC Rihand stage II		15.21	0.00
29	NTPC Rihand stage III		14.34	0.00
30	NTPC Singrauli		12.77	0.00
31	NTPC Tanda Stage II		12.22	0.00
32	NTPC Unchahar Stage I		1.98	0.00
33	NTPC Unchahar Stage II		4.93	0.00
34	NTPC Unchahar Stage III		1.58	0.00
35	NTPC Unchahar Stage IV		4.05	0.00
36	North Central Railway Prayagraj		0.00	41.53
37	Onevolt Energy Private Limited		25.21	0.00
38	Punjab		166.89	169.19
39	RENEW SURYA PRATAP PRIVATE LIMITED		41.74	0.00
40	RENEW SURYA PRATAP PRIVATE LIMITED_Infirm		0.16	0.00
41	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		28.89	0.00
42	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS_Infirm		10.94	0.00
43	Rajasthan		137.34	361.96
44	ReNew Surya Ravi Private Limited		48.79	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अप्रैल 2024
EXCHANGES THROUGH POWER EXCHANGES - APRIL 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	SHREE CEMENT LIMITED TPS		1.93	20.23
46	Sainj HEP		10.35	0.14
47	Serentica Renewables India 4 Private Limited		2.47	0.00
48	Singoli Bhatwari HEP		9.53	0.00
49	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		9.48	0.00
50	TPSL 200MW TPTCL Banderwala		40.64	0.00
51	Transition Energy Services Private Limited		8.28	0.00
52	Transition Green Energy Private Limited		2.50	0.00
53	Transition Sustainable Energy Services Private Limited		2.13	0.00
54	Uttar Pradesh		1140.39	414.76
55	Uttarakhand		15.13	391.68

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अप्रैल 2024
EXCHANGES THROUGH POWER EXCHANGES - APRIL 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
56	ACB (INDIA) LIMITED		44.42	0.28
57	ADANI GREEN ENERGY TWENTY SIX A LIMITED_infirm		0.43	0.00
58	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_Infirm		5.45	0.00
59	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		126.56	0.00
60	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		49.39	0.00
61	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		19.31	0.00
62	Adani Green Energy Twenty Five A Limited_Infirm		2.69	0.00
63	Adani Green Energy Twenty Five B Limited_infirm		50.69	0.00
64	Adani Green Energy Twenty Six B Limited_infirm		8.07	0.00
65	Adani Power Limited - Raigarh TPP		41.52	0.00
66	Adani Power Limited-Raipur TPP		75.17	5.56
67	ArcelorMittal Nippon Steel India Limited		0.00	73.79
68	BHARAT ALUMINIUM COMPANY LTD		14.53	0.00
69	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	9.98
70	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		4.91	0.00
71	Chhattisgarh		433.00	19.50
72	D B Power Limited		135.47	0.00
73	DGEN MEGA POWER PROJECT		32.33	0.00
74	DHARIWAL STU OTH		2.49	0.00
75	Daman and Diu - Dadra and Nagar Haveli		0.69	66.22
76	Dhariwal ISTS		9.03	0.00
77	GMR Warora Energy Limited		2.80	0.00
78	Goa WR		33.96	4.73
79	Gujarat		92.79	882.60
80	Jaypee Nigrie Super Thermal Power Plant		21.40	0.00
81	Jhabua Power Limited		8.55	0.58
82	Jindal Power Limited, Stage-1		45.97	0.00
83	Jindal Power Limited, Stage-2		115.10	0.00
84	Jindal Steel & Power Ltd , DCPP		72.17	0.00
85	KSK MAHANADI POWER COMPANY LIMITED		12.39	0.00
86	MAHAN ENERGEN LIMITED.		90.72	1.62
87	MB POWER (MADHYA PRADESH) LIMITED	पश्चिमी क्षेत्र WR	27.00	30.20
88	Madhya Pradesh		597.45	68.49
89	Maharashtra		158.68	607.06
90	Maruti Clean Coal and Power Limited		3.69	0.00
91	NREL-Dayapar Wind		8.47	0.00
92	NTPC Gadarwara		4.62	0.00
93	NTPC Jhanor Gandhar GPS		0.00	0.22
94	NTPC JhanorGandhar GPS RLNG		0.02	0.00
95	NTPC Kawas GPS		0.00	0.28
96	NTPC Kawas GPS RLNG		0.02	0.00
97	NTPC Korba Stage I &II		2.05	0.00
98	NTPC Korba Stage III		0.13	0.00
99	NTPC Lara Stage I		0.66	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अप्रैल 2024
EXCHANGES THROUGH POWER EXCHANGES - APRIL 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
100	NTPC Mouda Stage I		1.26	0.00
101	NTPC Mouda Stage II		1.74	0.00
102	NTPC SAIL POWER COMPANY LIMITED		0.26	0.00
103	NTPC Sipat Stage I		0.82	0.00
104	NTPC Sipat Stage II		0.85	0.00
105	NTPC Solapur		2.57	0.00
106	NTPC Vindhyachal Stage I		0.88	0.00
107	NTPC Vindhyachal Stage II		0.49	0.00
108	NTPC Vindhyachal Stage III		0.49	0.00
109	NTPC Vindhyachal Stage IV		0.16	0.00
110	NTPC Vindhyachal Stage V		0.09	0.00
111	NTPC khargone		8.13	0.00
112	Nani Virani Wind Energy Private Limited		2.16	0.00
113	R.K.M POWERGEN PRIVATE LIMITED		42.51	0.00
114	Ratnagiri Gas & Power Private Limited		0.00	0.78
115	SKS Power Generation Chhattisgarh Limited		16.13	11.25
116	Sasan Power Limited		12.91	0.00
117	TRN ENERGY PRIVATE LIMITED		41.15	0.00
118	The Tata Power Co Ltd (MTPS)		15.15	0.00
119	WIND FIVE RENERGY LIMITED		10.02	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अप्रैल 2024
EXCHANGES THROUGH POWER EXCHANGES - APRIL 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
120	Andhra Pradesh	दक्षिणी क्षेत्र SR	119.45	261.46
121	COASTAL ENERGEN PRIVATE LIMITED		0.00	0.00
122	Goa SR		0.26	15.76
123	IL&FS TAMIL NADU POWER COMPANY LIMITED		8.73	0.00
124	JINDAL POWER LIMITED SIMHAPURI		3.77	20.68
125	JSW RENEW ENERGY LIMITED		4.12	0.00
126	Karnataka		2.52	303.18
127	Kerala		8.74	170.22
128	Lanco Kondapalli Power Limited STG2		0.11	0.00
129	MEENAKSHI ENERGY LIMITED		2.21	0.00
130	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		3.15	0.00
131	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		1.22	0.00
132	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.63	0.00
133	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		0.40	0.00
134	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		0.61	0.00
135	NLC Tamilnadu Power Limited		0.73	0.00
136	NTECL VALLUR		1.68	0.00
137	NTPC KUDGI		4.74	0.00
138	NTPC Ramagundam Stage I &II		1.67	0.00
139	NTPC Ramagundam Stage III		0.32	0.00
140	NTPC Simhadri Stage I		3.37	0.00
141	NTPC Simhadri Stage II		1.95	0.00
142	NTPC Talcher Super Thermal Power Station Stage II		0.14	0.00
143	NTPC Telangana		1.55	0.00
144	OSTRO KANNADA POWER PRIVATE LIMITED		8.74	0.00
145	Pondicherry UT		43.03	0.00
146	RENEW SURYA OJAS PRIVATE LIMITED-Wind		3.08	0.00
147	RENEW SURYA OJAS PRIVATE LIMITED_INFIRM		13.09	0.00
148	Ramagundam Floating solar		9.26	0.00
149	SEIL ENERGY INDIA LIMITED		42.06	0.00
150	SEIL Energy India Limited Project II		8.96	0.00
151	Simhadri FSP 15 MW		2.68	0.00
152	Simhadri Floating solar (10 MW)		1.69	0.00
153	Tamil Nadu		24.03	376.29
154	Telangana		65.01	856.51

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अप्रैल 2024
EXCHANGES THROUGH POWER EXCHANGES - APRIL 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
155	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	6.15	0.00
156	Bihar		183.17	130.53
157	Chuzachen HEP		0.09	0.00
158	Damodar Valley Corporation		60.92	67.25
159	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	138.79
160	GMR KAMALANGA ENERGY LTD-CTU		2.04	0.00
161	IND BARATH ENERGY UTKAL LIMITED		15.07	0.00
162	Jharkhand		55.58	59.36
163	Jindal India Thermal Power Limited		79.93	0.00
164	KANTI BIJLEE UTPADAN NIGAM LIMITED		3.95	0.00
165	MAITHON POWER LIMITED		0.07	0.00
166	NABINAGAR POWER GENERATING COMPANY LIMITED		6.58	0.00
167	NEA - Bihar STU		0.00	14.04
168	NEA Nepal Solu Khola (Dudhkoshi) Hydropower Project		0.16	0.00
169	NEA Nepal Upper Dordi A Hydropower Project		0.02	0.00
170	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	173.01
171	NTPC BARH Stage I		11.83	0.00
172	NTPC BARH Stage II		82.12	0.00
173	NTPC Darlipali		2.30	0.00
174	NTPC Farakka stage I		4.37	0.00
175	NTPC Farakka stage III		2.29	0.00
176	NTPC Kahalgaon stage I		6.31	0.00
177	NTPC Kahalgaon stage II		12.27	0.00
178	NTPC North Karanpura STPS		1.80	0.00
179	NTPC Talcher Stage I		2.39	0.00
180	NTPP BRBCL		5.38	0.00
181	Odisha		99.64	241.50
182	Sikkim		12.11	13.70
183	West Bengal		128.65	325.72
184	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	0.13	0.00
185	ASSAM GAS BASED POWER STATION		1.68	0.00
186	Arunachal Pradesh		8.78	7.82
187	Assam		141.85	14.30
188	Bongaigaon Thermal Power Station NTPC		4.26	0.00
189	KAMENG HYDRO POWER STATION		11.99	0.00
190	Kopili Power Station NEEPCO		0.02	0.00
191	Manipur		16.13	26.56
192	Meghalaya		3.71	44.84
193	Mizoram		1.98	0.00
194	Nagaland		4.33	4.44
195	Palatana Plant		1.21	0.00
196	Tripura		0.99	26.31
Total			7129	7129

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : APRIL 2024

RE Source & Unit wise break up (01.04.2024-30.04.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	1	1	1	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	0	0	1	1
5	Small Hydro	24	1	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**25**	**2**	**2**	**2**

RECs Issued (01.04.2024-30.04.2024)

Sr.No.	Non Solar	Solar	Total
1	5185679	56852	5242531

Redemption of REC (01.04.2024-30.04.2024)

Sr.No.	Non Solar	Solar	Total
1	1070089	9994	1080083

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : APRIL 2024

RE Source & Unit wise break up (Apr'24-Apr'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	1	1	1	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	0	0	1	1
5	Small Hydro	24	1	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**25**	**2**	**2**	**2**

RECs Issued (Apr'24-Mar'25)

Sr.No.	Non Solar	Solar	Total
1	5185679	56852	5242531

Redemption of REC (Apr'24-Mar'25)

Sr.No.	Non Solar	Solar	Total
1	1070089	9994	1080083

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : APRIL 2024

RE Source & Unit wise break up Since Inception to Apr'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3134	531	2977	532
2	Urban or Municipal Waste	12	1	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1631	573	1469	480
5	Small Hydro	869	43	857	44
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**6875**	**1278**	**6067**	**1147**

RECs Issued since Inception to Apr'24

Sr.No.	Non Solar	Solar	Total
1	120290717	13597230	133887947

Redemption of REC since Inception to Apr'24

Sr.No.	Non Solar	Solar	Total
1	79574418	12459251	92033669

REC Closing balance as on 30.04.2024

Sr.No.	Non Solar	Solar	Total
1	4115590	46858	4162448

20.Details of Grid Events during the Month of April 2024 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	Himachal Pradesh	01-Apr-2024 18:37	01-Apr-2024 20:17	01:40	300	0	0.687	0.000	43667	49841	i)During antecedent condition, 100 MW Chamera II HPS- UNIT 1, 2 & 3 were generating approx. 100MW each. ii)As reported, at 18:37 hrs, the inverter supply to butterfly valve got disrupted due to malfunction of inverter system. This led to closing of butterfly valve. iii)As per scheme, due to sudden closure of butterfly valve while unit circuit breaker is in closed condition, lockout relay got activated and initiate emergency trip command to all units. This led to tripping of 100 MW Chamera-II HPS UNIT 1, 2 & 3. iv)As per PMU at Jalandhar(PG), no fault is observed in the system. v)As per SCADA, loss of generation of approx. 300MW is observed at Chamera-II(NHPC).	1) 100 MW Chamera II HPS- UNIT 1 2) 100 MW Chamera II HPS- UNIT 2 3) 100 MW Chamera II HPS- UNIT 3
2	GI-2	Rajasthan	06-Apr-2024 11:24	06-Apr-2024 13:42	02:18	4870	630	8.676	1.213	56133	51953	i)As reported, at 11:24hrs, 400kV Bhadla(RS)-Bikaner(RS) Ckt-1 tripped from Bhadla(RS) end only on R-Y phase to phase fault with fault distance of 49.19km and fault current of 8.002kA and 8.29kA in R and Y phase respectively from Bhadla(RS) and fault distance of 129.2km from Bikaner(RS) end. As per information received from SLDC Rajasthan, M/s Ramelex Pvt. Ltd. was asked to carry out patrolling of line and it was found that fault occurred due to conductor snapping between loc. no.171-172. ii)As per DR at Bikaner(RS) end of 400kV Bhadla(RS)-Bikaner(RS) Ckt-1, fault was sensed in zone-1; fault current was 4.18kA and 4.37kA in R and Y phase respectively from Bikaner(RS) end and fault clearing time was ~50ms. Time sync issue is observed. iii)As per PMU at Bhadla(PG), R-Y phase to phase fault is observed with fault clearance time of 80 ms. Voltage dipped upto 0.844 p.u. at Bhadla(PG). iv)As per SCADA, total NR RE generation drop/loss was approx.4870MW (~3884MW ISTS RE generation and ~986MW Rajasthan RE generation). Due to significant dip in RE generation frequency dropped by 0.49Hz (from 50.029Hz to 49.539Hz). v)As per details received from SLDCs, total load relief of approx. 630 MW observed in NR region (UP: ~125MW, Rajasthan: ~165MW, Punjab: ~340MW) on df/dt operation. vi)Due to significant dip in RE generation (as RE generation failed to recover 90% of pre-fault active power within 1 sec and further inverters tripping on OV, LVRT/HVRT Non-compliant), over voltage (1.114pu at 400kV Bhadla(PG)) scenario occured immediately after the fault. vii)As per SCADA SOE, 400kV Jodhpur(RS)-Rajwest(RS) Ckt also tripped during the same time. (Exact reason yet to be shared) it is suspected that line tripped due to over-voltage that occurred immediately after the fault. viii)At the same time, 135 MW Rajwest (IPP) LTPS - UNIT 5 also tripped due to GT tripped, as reported (further details yet to be received). ix)After rectification work (de-stringing,stringing,spacering,Jointing and repairing) at Loc No. 170-173 (Top Phase), 400kV Bhadla(RS)-Bikaner(RS) Ckt-1 was charged at 21:40hrs on 08th April, 2024.	1) 400kV Bhadla(RS)-Bikaner(RS) Ckt-1 2) 400kV Jodhpur(RS)-Rajwest(RS) Ckt 3) 135 MW Rajwest (IPP) LTPS - UNIT 5
3	GI-2	Haryana	07-Apr-2024 18:07	07-Apr-2024 18:54	00:47	0	0	0.000	0.000	39542	46314	i)During antecedent condition, 800kV HVDC Champa-Kurukshetra was carrying total 1940MW (approx. 485MW by each Pole). ii)As reported at 18:07hrs, 800 kV HVDC Kurukshetra (PG) Pole-01 blocked on T-zone protection operation at Kurukshetra end. iii)During the same time, 800 kV HVDC Kurukshetra (PG) Pole-03 also blocked on CAT-B sequence initiated by parallel Pole-01 due to latching of T-zone protection. iv)As further reported, sequence of event is as follows: a.17:52:34:291 –Pole-1 lane 2 to Bipole1 Lane 1 and Lane 2 Optic link was toggling (This link is used to transmit parallel pole data between Pole-1 and Pole-3) b.17:52:34:290 –Pole-1 lane 2 become unavailable c.17:57:48:481 – Pole-1 lane 2 Main 1 and Main 2, T-Zone protection got latched due to toggling of optic between Pole-1 Lane-2 and Bipole-1 d.18:07:13:502 – Pole-1 lane 2 become available automatically, due to already latched T-Zone protection, 2 out of 4 logic got satisfied after availability of Pole-1 Lane-2 and it initiated CAT B protection. e.18:07:13:502 – CAT-B got latched in Pole-1 lane 2 because of T-Zone protection f.18:07:13:639 – Pole-1 blocked g.18:07:13:594 – Pole-3 blocked v)Due to tripping of two poles (Pole-01 and Pole-03), power order reduced from 1940MW to 1855MW and shifted to the other two Poles. vi)As per PMU, fluctuation in voltage was observed. vii)As per SCADA, no change in demand is observed in Haryana control area. viii)As toggling of optics can be due to several reasons, so the 5003 card of Pole-1 Lane-2 where both the fiber were connected was replaced and Pole-1 Lane-2 was kept in maintenance mode for observation.	1) 800 kV HVDC Kurukshetra(PG) Pole-01 2) 800 kV HVDC Kurukshetra(PG) Pole-03
4	GI-2	Rajasthan	07-Apr-2024 10:24	07-Apr-2024 11:56	01:32	1680	0	3.250	0.000	51686	49513	i)As reported, at 10:24hrs, 400 KV Abdullapur-Kurukshetra (PG) Ckt-2 tripped on Y-N phase to earth fault due to insulator flashover with fault distance of 1.5km and fault current of ~19kA from Abdullapur(PG) end. ii)As per DR at Bikaner(RS) end of 400kV Bhadla(RS)-Bikaner(RS) Ckt-1, fault was sensed in zone-1; fault current was 4.18kA and 4.37kA in R and Y phase respectively from Bikaner(RS) end and fault clearing time was ~50ms. Time sync issue is observed. iii)As per PMU at Abdullapur(PG), Y-N phase to earth fault with unsuccessful A/R is observed. Voltage dipped upto 0.388 p.u. and 0.195p.u. respectively at Abdullapur(PG). iv)As per PMU at Bhadla(PG), voltage dipped upto 0.888 p.u. at Bhadla(PG). v)At the same time, 220/33 kV 100 MVA ICT 3 at RSDCL(PSS4)_SL_BHD2_PG also tripped due to over-flux protection operation (mal-operation suspected, exact details yet to be shared). vi)As per SCADA, during fault, total NR RE generation dip of approx. 1680MW is observed and almost all RE generation recovered within 04 minutes. vii)Due to significant dip in RE generation, frequency dropped by 0.132Hz (from 49.997Hz to 49.865Hz) viii)As per SCADA SOE, 33/4X.66kV 12.5MVA IDT-7 at MRPL(IP)_SL_BHDL_PG also tripped during the same time. (Exact reason yet to be shared)	1) 220/33 kV 100 MVA ICT 3 at RSDCL(PSS4)_SL_BHD2_PG 2) 400 kV Abdullapur-Kurukshetra (PG) Ckt-2
5	GD-1	Punjab	11-Apr-2024 03:01	11-Apr-2024 04:31	01:30	0	175	0.000	0.371	40503	47115	i)220/66kV Gobindgarh-2(PS) has single bus arrangement at 220kV and 66kV side. Gobindgarh-2(PS) is connected to 220/66kV Bhari(PS), 220/132 kV Ganguwal(BB) and 220/66kV Gobindgarh-1(PS)(D/C) form 220kV side. ii)During antecedent condition, 220kV Gobindgarh-1(PS)-Gobindgarh-2 (PS) D/C were not in service. iii)As reported, at 03:01 hrs, B-phase CT at Gobindgarh S/s end of 220kV Bhari(PS)-Gobindgarh-2(PS) ckt blasted and the line tripped. iv)During the same time, 220kV Ganguwal(BB)-Gobindgarh-2(PS) (BB) Ckt tripped only from Ganguwal(BB) end on B-N phase to earth fault with fault distanace of 94.63km (121.32%) and fault current of 2.64kA from Ganguwal(BB) end. v)As per SCADA SOE, no CB tripping is observed at Gobindgarh(PS). Hence it is suspected that line CB of 220 KV Bhari (PS)-Gobindgarh-2(PS) ckt at Gobindgarh-2 end didn't open which led to tripping of 220kV Ganguwal(BB)-Gobindgarh-2(PS) (BB) Ckt from Ganguwal(BB) end. (details of the same yet to be shared) vi)As per PMU at Jalandhar(PG), B-N phase to earth fault with unsuccessful A/R operation is observed in the system. Fault clearing time was 80ms. vii)As per SCADA, load loss of approx. 175MW is observed in Punjab control area.	1) 220 KV Ganguwal(BB)-Gobindgarh-2(PS) (BB) Ckt 2) 220 KV Bhari (PS)- Gobindgarh-2(PS) Ckt
6	GD-1	Uttar Pradesh	11-Apr-2024 00:31	11-Apr-2024 01:56	01:25	0	150	0.000	0.297	42607	50438	i)220kV side of 400/220/132kV Gr.Noida(UP) has double main & transfer bus scheme. ii)As reported, at 00:31 hrs, Y phase CT at 220kV side of 400/220kV 315MVA ICT-2 at Gr.Noida (UP) blasted which led to busbar protection operation at 220KV Bus-2 at Gr.Noida (UP). iii)Due to this, all the elements connected to 220KV Bus-2 at Gr.Noida (UP) tripped and Bus-2 became dead. iv)As per PMU at Meerut(PG), Y-N phase to phase fault with delayed fault clearance time of 280 ms is observed. v)As per SCADA, change in demand of approx. 150MW in UP control area.	1) 400/220 kV 315 MVA ICT 2 at Gr.Noida(UP) 2) 400/220 kV 500 MVA ICT 6 at Gr.Noida(UP) 3) 220/132 kV 200 MVA ICT 3 at Gr.Noida(UP) 4) 220/132 kV 200 MVA ICT 4 at Gr.Noida(UP) 5) 220kV Greater Noida - RC Green ckt-1 6) 220kV Greater Noida - RC Green ckt-2 7) 220kV Greater Noida - Jalpura ckt 8) 220KV Bus-2 at Gr.Noida(UP)
7	GI-2	Uttar Pradesh	13-Apr-2024 19:06	13-Apr-2024 19:27	00:21	0	225	0.000	0.428	47150	52597	i)During antecedent condition, 400/220kV 315 MVA ICT 1 at Obra_B(UP) was already under shutdown for replacement of broken conductor. Active power flow in 400/220kV 315 MVA ICT 2 and 240 MVA ICT-3 at Obra_B(UP) were 297MW and 230MW respectively. ii)As reported, after work completion and during closing of 220kV sequential isolator, its support structure of male portion of 220kV B-phase broke and dropped down. At the same, time extension of shutdown also requested. iii)At 19:06hrs, both ICT-2 and 3 tripped due to directional O/C protection operation. iv)During the incident "SPS for Transformers at Obra TPS(UPRVUNL) substation" didn't operate. As reported, optical fibre cable for SPS signal communication found damaged, which has been replaced with spare core. However, follow up is being done with OEM to implement an alarm system for identification of such failure of communication cable which is not available in current system. v)As per PMU at Singrauli(NT), no fault is observed in the system. vi)As per SCADA, change in demand of approx. 225MW is observed in UP control area.	1) 400/220kV 315 MVA ICT 2 at Obra_B(UP) 2) 400/220kV 240 MVA ICT 3 at Obra_B(UP)
8	GD-1	Himachal Pradesh	19-Apr-2024 04:30	19-Apr-2024 05:30	01:00	0	150	0.000	0.298	43577	50338	i)220/66kV Uperlanangal (HP) has double main bus scheme at both 220kV & 66kV level. During antecedent condition, power was flowing through 220/66kV 80/100MVA ICT-1 & 2 at Uperlanangal(HP) to the feeders connected at 66kV level of Uperlanangal (HP). ii)As reported, at 04:30 hrs, 220 kV Uperlanangal-Kinvan (HP) Ckt tripped on Y-N phase to earth fault due to Y-phase jumper broken. But as line CB at Uperlanangal(HP) end of 220 kV Uperlanangal-Kinvan (HP) Ckt didn't open, LBB operated. iii)Due to this, all other 220kV lines along with 220/66kV 80/100MVA ICT-1 & 2 at Uperlanangal(HP) tripped which led total blackout at Uperlanangal (HP). iv)As per SCADA SOE, 5.65MW Unit-1 at Ghanvi(HP) also tripped during the same time (exact reason yet to be shared). v)As per PMU at 400kV Nallagarh(PG), Y-N phase to earth fault is observed in the system with fault clearing time of 80ms. vi)As per SCADA, change in demand of approx. 150MW is observed in HP control area.	1) 220 kV Uperlanangal-Kinvan (HP) Ckt 2) 220 kV Nallagarh(PG)-Uperlanangal (HP) (HPSEB) Ckt-1 3) 220 kV Nallagarh(PG)-Uperlanangal (HP) (HPSEB) Ckt-2 4) 220 kV Uperlanangal-Wardthman (HP) Ckt 5) 220 kV Uperlanangal-Baddi (HP) Ckt 6) 220/66kV 80/100MVA ICT-1 at Uperlanangal(HP) 7) 220/66kV 80/100MVA ICT-2 at Uperlanangal(HP)
9	GD-1	Jammu & Kashmir	29-Apr-2024 06:06	29-Apr-2024 07:11	01:05	14	15	0.030	0.027	46486	56269	i)Power flows from Alusteng(PG) to Drass(PG) to Kargil to Khalsti to Leh (radial connection). Generation of Chutak is connected to Kargil and generation of Nimoo bazgo is connected to Leh. ii)As reported, at 06:06 hrs, 220 KV Alusteng-Drass (PG) Ckt tripped on R-B phase to phase fault with fault distance of 38.4km from Drass(PG). iii)With the tripping of 220 KV Alusteng-Drass (PG) Ckt, complete blackout occurred at 220/66kV Drass(PG) and supply to Kargil, Khalsti and Leh also failed. iv)Generation of Chutak and Nimoo Bazgo tripped due to loss of evacuation path resulting in generation loss of approx. 7MW each at Chutak and Nimoo Bazgo (as per SCADA). v)As per PMU at Amargarh(INDIGRID), R-B phase to phase fault is observed with fault clearing time of 120ms. vi)As per SCADA, change in demand of approx. 15MW is observed in J&K control area.	1) 220 KV Alusteng-Drass (PG) Ckt

20.Details of Grid Events during the Month of April 2024 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
10	GI-1	Jammu & Kashmir	29-Apr-2024 01:43	29-Apr-2024 02:51	01:08	80	35	0.173	0.063	46136	55963	i)132kV Sewa-II(NHPC) has double main bus scheme. During antecedent condition, 132 KV Sewa_2(NH)-Mahanpur(JK) (PG) Ckt, 132 KV Sewa_2(NH)- Hiranagar(PDD) (PG) Ckt-1 and 40 MW Sewa-II HPS- UNIT 3 were connected to 132kV Bus-1 at Sewa-II(NHPC) and 132 KV Sewa_2(NH)-Kathua(JK) (PG) Ckt, 132 KV Sewa_2(NH)- Hiranagar(PDD) (PG) Ckt-2 and 40 MW Sewa-II HPS- UNIT 1 & 2 were connected to 132kV Bus-2 at Sewa-II (NHPC). 40 MW Sewa-II HPS- UNIT 1, 2 & 3 were generating approx. 40MW each. At 132kV Mahanpur(JK), power was coming from Sewa-II(NHPC) and going to Kathua(JK). ii)As reported, at 01:43 hrs, bottom conductor of 220 kV Thein - Ghatti Ckt (JKPDD) snapped over Gantry tower location no. 158 - 159. iii)As per DR of 132 KV Sewa_2(NH) (end)-Kathua(JK) (PG) Ckt , 3-phase fault is observed; fault current: Ir=~2127A, Iy=~2306A, Ib=~2214A. Fault was sensed in zone-2 at Sewa-II(NHPC) end and carrier received signal was already persisting throughout the DR time. As carrier received signal was already triggered, on operation of zone-2 protection, relay issued 3-phase trip command. But line CB didn't open and after a delay of 300ms LBB operated. iv)Due to LBB operation, all the elements connected to bus-2 tripped and Bus-2 became dead. v)During the same time, 132 KV Kathua(JK)-Mahanpur(JK) (PG) Ckt also tripped as reported (exact reason yet to be shared). Hence, 132 KV Sewa_2(NH)-Mahanpur(JK) (PG) Ckt also tripped due to loss of evacuating line. vi)As per PMU at Kishenpur(PG), 3-phase fault with delayed fault clearance time of 400ms is observed. vii)As per SCADA, change in demand of approx. 35MW and loss of generation of approx. 80MW at Sewa-II are observed. viii)All 40 MW Sewa-II HPS- UNIT 1 & 2 were revived at 02:59 hrs and 02:51 hrs respectively.	1) 132 KV Sewa_2(NH)-Kathua(JK) (PG) Ckt 2) 132 KV Sewa_2(NH)- Hiranagar(PDD) (PG) Ckt-2 3) 40 MW Sewa-II HPS- UNIT 1 4) 40 MW Sewa-II HPS- UNIT 2 5) 132 KV Kathua(JK)-Mahanpur(JK) (PG) Ckt
11	GD-1	Jammu & Kashmir	29-Apr-2024 03:35	29-Apr-2024 04:44	01:09	120	25	0.269	0.047	44606	53173	i)132kV Sewa-II(NHPC) has double main bus scheme. During antecedent condition, only 132 KV Sewa_2(NH)- Hiranagar(PDD) (PG) Ckt-1 was in service through which all the generation of Sewa-II(NHPC) was evacuating. 40 MW Sewa-II HPS- UNIT 1, 2 & 3 were generating approx. 40MW each. ii)As reported, at 03:35 hrs, 132 KV Sewa_2(NH)- Hiranagar(PDD) (PG) Ckt-1 tripped only from Sewa-II(NHPC) end (line has no auto reclose facility) on Y-N phase to earth fault. iii)As per DR of 132 KV Sewa_2(NH) (end)- Hiranagar(PDD) (PG) Ckt-1, fault was sensed in zone-1 at Sewa-II(NHPC) end; Y-ph voltage (ph) reduced upto ~59.42kV and Y-ph current increased upto ~1035A. iv)As 132 KV Sewa_2(NH) (end)- Hiranagar(PDD) (PG) Ckt-1 was the only evacuating line available during antecedent condition, frequency swing was observed which led to the tripping of all the three running units on operation of over speed protection. v)As per PMU at Kishenpur(PG), two consecutive Y-N phase to earth faults with fault clearance time of 80ms are observed in the system. vi)As per SCADA, change in demand of approx. 25MW and loss of generation of approx. 120MW at Sewa-II are observed.	1) 132 KV Sewa_2(NH)- Hiranagar(PDD) (PG) Ckt-1 2) 40 MW Sewa-II HPS- UNIT 1 3) 40 MW Sewa-II HPS- UNIT 2 4) 40 MW Sewa-II HPS- UNIT 3
12	GD-1	Uttar Pradesh and Uttarakhand	30-Apr-2024 00:16	30-Apr-2024 00:47	00:31	146	60	0.289	0.104	50468	57536	i)Power of 82.5*4 MW Alaknanda HEP, 110*4MW Vishnuprayag HEP and 33*3MW Singoli Bhatwari HEP evacuates through 400 KV Alaknanda GVK (UPC)-Muzaffarnagar(UP) ckt and 400 KV Vishnuprayag(UP)-Muzaffarnagar (UP) (UP) Ckt. During antecedent condition, only 110MW unit-1 at Vishnuprayag HEP and 33MW unit-2 & 3 at Singoli Bhatwari HEP were in running condition and generating approx. 91MW, 28MW and 27MW respectively. No generation was there at Alaknanda HEP. ii)As reported, at 22:59 hrs on 29th Apr'24, 400 KV Vishnuprayag(UP)-Muzaffarnagar (UP) (UP) Ckt tripped on R-N phase to earth fault. As per PMU, fault current was ~2.7kA from Muzaffarnagar end. As per DR, fault was sensed in zone-1 at Muzaffarnagar end and fault current was 3.787kA from Muzaffarnagar end. A/R started in R-ph; R-ph CB closed from Vishnuprayag after ~750ms. Three phase tripping occurred from Muzaffarnagar end after ~1090ms due to A/R lockout. iii)Further, as reported, at 00:16 hrs, bus bar protection operated (zone-1 in bus bar differential relay) at 400KV Bus 1 at Muzaffarnagar(UP) due to damage of B-ph CB pole PIR (Pre Insertion Resistor) of 400 KV Vishnuprayag(UP)-Muzaffarnagar (UP) (UP) Ckt. Due to this all the elements connected to Bus 1, e.g., 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (UP) Ckt, 400/220 kV 315 MVA ICT 2 and 3 at Muzaffarnagar(UP) tripped and Bus 1 became dead. 400 KV Meerut(PG)-Muzaffarnagar(UP) (PG) Ckt was hand tripped due to isolator sparking at Muzaffarnagar end. iv)With the tripping of both 400 KV Vishnuprayag(UP)-Muzaffarnagar(UP) (UP) Ckt and 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (UP) Ckt, 110MW unit-1 at Vishnuprayag HEP tripped due to unavailability of power evacuating path. v)During the same time, 220 KV Singoli Bhatwari(Singoli(LTUHP)) (end)-Srinagar(UK) (PTCUL) Ckt-1 & 2 also tripped. As reported, DT received at Singoli Bhatwari end (exact reason yet to be shared). vi)Due to tripping of 220 KV Singoli Bhatwari(Singoli(LTUHP)) (end)-Srinagar(UK) (PTCUL) Ckt-1 & 2, 33 MW Singoli Bhatwari(Singoli (LTUHP)) HPS - UNIT 2 & 3 tripped due to unavailability of power evacuating path. vii)Due to this event, complete blackout occurred at 400kV Vishnuprayag HPS(UP) and 220kV Singoli Bhatwari HEP(Singoli(LTUHP)) S/s. viii)As per PMU at Muzaffarnagar(UP), Y-B phase to phase fault with fault clearance time of 120 ms is observed. ix)As per SCADA, no change in demand in UP control area and change in demand of approx. 60MW in Uttarakhand control area are observed. Generation loss of approx. 91MW and 55MW are observed at Vishnuprayag HEP and Singoli Bhatwari HEP respectively.	1)400 KV Vishnuprayag(UP)-Muzaffarnagar (UP) (UP) Ckt 2)400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (UP) Ckt 3)400KV Bus 1 at Muzaffarnagar(UP) 4)400/220 kV 315 MVA ICT 2 at Muzaffarnagar(UP) 5)400/220 kV 315 MVA ICT 3 at Muzaffarnagar(UP) 6)400 KV Meerut(PG)-Muzaffarnagar(UP) (PG) Ckt 7)110 MW Vishnuprayag HPS - UNIT 1 8)220 KV Singoli Bhatwari (Singoli(LTUHP)) (end)-Srinagar(UK) (PTCUL) Ckt-1 9)220 KV Singoli Bhatwari (Singoli(LTUHP)) (end)-Srinagar(UK) (PTCUL) Ckt-2 10)33 MW Singoli Bhatwari (Singoli(LTUHP)) HPS - UNIT 2 11)33 MW Singoli Bhatwari (Singoli(LTUHP)) HPS - UNIT 3

20.Details of Grid Events during the Month of April 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	08:14 / 01-04-2024	11:55 / 01-04-2024	03:41	41	-	0.06%	-	73481	62116	At 08:14 Hrs / 01-04-2024, 400 kV Khavda PS1-Khavda PSS2 tripped due to over voltage stage-1 protection operation (main-1 relay maloperated) at Khavda PSS2. Voltage at both the ends were within the normal operating limits, on inspection it was found that main 1 (GE make L90) maloperated and DT was sent to Khavda PS1 end. Generation loss of 41 MW occurred at Khavda PSS2 (AREH4L) due to loss of evacuation path.	Tripping of following Elements: 1. 400 kV Khavda PS1-Khavda PSS2
2	GD-1	WR	18:12 / 02-04-2024	22:56 / 02-04-2024	04:44	148	-	0.19%	-	78116	64061	At 18:12 Hrs / 02-04-2024, 220 kV Bhuj-Gadhsisa tripped due on Y-E fault. During patrolling no abnormality was found. Generation loss of 148 MW occurred at Gadhsisa (Renew Power) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa
3	GD-1	WR	05:15 / 03-04-2024	06:54 / 03-04-2024	01:39	129	-	0.17%	-	74270	61146	At 05:15 Hrs / 03-04-2024, 220 kV Indore(PG)-Pritamnagar(AWEMP1PL) tripped due on R-E fault. R phase tripped at Indore(PG) end and other phase tripped from Pritamnagar end on Zone-2 . As per DR at Pritamnagar end carrier not received at Pritamnagar. During patrolling no abnormality was found. Generation loss of 129 MW occurred at Pritamnagar(AWEMP1PL) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Indore(PG)-Pritamnagar(AWEMP1PL)
4	GD-1	WR	05:30 / 03-04-2024	07:02 / 03-04-2024	01:32	-	1235	-	1.99%	74394	61921	At 05:30 Hrs / 03-04-2024, 220 kV Suhela-Bhatapara-1 tripped on R-E fault from Suhela end only and no signal picked up at Bhatapara end. Subsequently, other lines at Suhela tripped on overcurrent protection operation resulting in blackout at Suhela, Paraswani,Bemetara and Saraipalli station. Prior to the event, 220 kV Bhilai-Bemetra was under forced outage. Load loss of around 1235 MW occurred at Suhela and adjacent station due to the event.	Tripping of following Elements: 1. 220 kV Bhatapara-Suhela-1,2&3 2. 220 kV DSPM-Suhela 3. 220 kV Suhela-Bemetra-1&2 4. 220 kV Suhela-Parswani-1&2 5. 220 kV Suhela-Banari 6. 220 kV Suhela-Bus-1&2
5	GD-1	WR	11:19 / 03-04-2024	21:08 / 03-04-2024	09:49	328	-	0.42%	-	78983	69244	At 11:19 Hrs / 03-04-2024, 220 kV Agar5(Umariya)-Pachora tripped from Agar5(Umariya) end on Y phase differential protection operation and auto recloser successful at Pachora substation. Generation loss of 328 MW occurred at Umariya (Beempow) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Agar5(Umariya)-Pachora
6	GD-1	WR	17:32 / 03-04-2024	19:52 / 03-04-2024	02:20	140	-	0.18%	-	79846	66826	At 17:32 Hrs / 03-04-2024, 220 kV Bhuj-Gadhsisa tripped due on B-E fault. During patrolling no abnormality was found. Generation loss of 140 MW occurred at Gadhsisa (Renew Power) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa
7	GI-2	WR	04:30 / 05-04-2024	09:51 / 05-04-2024	05:21	-	-	-	-	77738	62423	At 04:30 Hrs / 05-04-2024, 400 kV Navsari(PG)-Bus-2 tripped on Y-E Bus Bar differential protection operation resulting in tripping of all connected elements (400 kV Navsari(PG)-Kakrapar-1, 400 kV Navsari(PG)-Gandhar-1, 400 kV Navsari(PG)-DGEN-2, 400 kV Navsari(PG)-Magarwada-2, 400/220 kV Navsari(PG)-ICT-1&2). On inspection it was found that SF6 gas of B2 Compartment of 411898 Isolator of 400Kv Side of Navsari(PG)-ICT-3 was highly contaminated with SO2 gas. Prior to the event, 400 kV Kakrapar-Vapi-1&2 were under outage for LILO arrangement of Kakrapar-Vapi-1&2 at 400 kV Vapi-II. Manual generation backdown of 300 MW done at Kakrapar by NPCIL due to transmission constraints. No load loss / generation loss occurred due to the event.	Tripping of following Elements: 1. 400 kV Navsari(PG)-Bus-2 2. 400 kV Navsari(PG)-Bus Reactor 3. 400 kV Navsari(PG)-Kakrapar-1 4. 400 kV Navsari(PG)-Gandhar-1 5. 400 kV Navsari(PG)-DGEN-2 6. 400/220 kV Navsari(PG)-ICT-1&2 7. 400 kV Navsari(PG)-Magarwada-2
8	GD-1	WR	14:41 / 05-04-2024	15:09 / 05-04-2024	00:28	470	900	0.57%	1.29%	83076	69695	At 14:41 Hrs / 05-04-2024, 220 kV Korba(E)-Korba(W)-1 tripped from Korba(E) end on zone-2 operation and Earth fault operation at Korba(W) end. At same time 220 kV DSPM-Mopka tripped (reason not given by CSPTCL). Prior to the event, 220 kV Dardehi-Bhatapara and 220 kV Korba(W)-Mopka were under outage. With tripping of 220 kV DSPM-Mopka, load at Mopka end was being met through 220 kV Chhuri-Mopka-1&2 resulting in high loading on lines connected to 220 kV Chhuri. Further, R phase jumper of 220 kV Korba(E)-Chhuri-1 broke at Korba(E) end and line tripped on pole discrepancy operation. Subsequently,multiples lines tripped leading to blackout of Chhuri, Mopka, Dardehi, Bishrampur, Jamnipalli and Kharmora. Generation loss of 470 MW at DSPM (Chhattisgarh) and load loss of around 900 MW occurred due to the event.	Tripping of following Elements: 1. 220 kV Korba(E)-Chhuri-1&2 2. 220 kV Korba(E)-Budhipadhar-2&3 3. 220 kV Korba(E)-Bus-2 4. DSPM Unit-1&2 (250 MW) 5. 220 kV Korba(E)-Korba(W)-1&2 6. 220 kV DSPM-Mopka 7. 220 kV Chhuri-Mopka-1&2
9	GD-1	WR	12:41 / 06-04-2024	13:10 / 06-04-2024	00:29	-	700	-	1.03%	79999	67922	At 12:41 Hrs / 06-04-2024, 220 kV Korba(W)-Chhuri-2 tripped on R-E fault. Subsequently, 220 kV Korba(W)-Chhuri-1 tripped at Korba(W) on over current protection operation and DT sent to Chhuri end. Prior to the event 220 kV Mopka-Dardehi-D/C were under outage and load at Mopka end was being fed by Churri. Also many other lines at adjacents stations were under outage (details awaited from CSPTCL). Chhuri, Mopka, Dardehi, Bishrampur, Jamnipalli, Kharmora and Renki substation were blackout. Load loss of around 700 MW occurred due to the event.	Tripping of following Elements: 1. 220 kV Korba(W)-Chhuri-1&2 2. 220 kV Korba(W)-Mopka-1 3. 220 kV Churri-Bishrampur-1&2 4. 220 kV Mopka-Dardehi-1&2
10	GD-1	WR	12:43 / 07-04-2024	14:08 / 07-04-2024	01:25	328	-	0.45%	-	72783	65783	At 12:43 Hrs / 07-04-2024, 220 kV Agar5(Umariya)-Pachora tripped from Agar5(Umariya) end on B phase differential protection operation and auto recloser successful at Pachora substation. Generation loss of 328 MW occurred at Umariya (Beempow) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Agar5(Umariya)-Pachora
11	GI-2	WR	09:31 / 08-04-2024	10:03 / 08-04-2024	00:32	-	198.5	-	0.30%	75915	66206	At 09:31 Hrs / 08-04-2024,LBB operation of 400 kV Lonikhand-Bus-1 during closing of 220 kV side Circuit Breaker of 400/220 kV Lonikhand-ICT-1 resulting in tripping of all elements connected to 400 kV Lonikhand-Bus-1. Prior to these trippings 400/220 kV Lonikhand-ICT-1 was under shutdown for oil filteraion work. During closing of 220 kV side Circuit Breaker of 400/220 kV Lonikhand-ICT-1, LBB signal was sent by the relay. The defecive relay of 400/220 kV Lonikhand-ICT-1 has been replaced by MSETCL.Load loss of 198.5 MW occurred due to the event.	Tripping of following Elements: 1. 400 kV Lonikhand-Bus-1 2. 400/220 kV Lonikhand-ICT-2 3. 400 kV Lonikhand-Pune(PG)-1 4. 400 kV Lonikhand-Lonikhand-2
12	GD-1	WR	12:38 / 09-04-2024	17:35 / 09-04-2024	04:57	281	-	0.37%	-	76011	66773	At 12:38 Hrs / 09-04-2024, 220 kV Agar5(Umariya)-Pachora tripped from Agar5(Umariya) end on B phase differential protection operation and auto recloser successful at Pachora substation. Generation loss of 281 MW occurred at Umariya (Beempow) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Agar5(Umariya)-Pachora
13	GI-2	WR	08:08 / 20-04-2024	09:59 / 20-04-2024	01:51	-	22	-	0.03%	74778	63183	At 08:08 Hrs / 20-04-2024, R phase Current Transformer of 400 kV Nagda-Badnawar-2 at Nagda burst and Y phase CT also got damaged leading to oil leakage, both R and Y phase tripped. Due to non opening of B phase breaker of 400 kV Nagda-Badnawar-2 at Nagda, LBB (Local Breaker Backup) protection operated in 400 kV Nagda-Bus-1&2 as no other element is in dia of 400 kV Nagda-Badnawar-2. All the main bays connected to 400 kV Nagda-Bus-1&2 opened due to LBB operation. 400 kV Nagda-Mandsaur-1&2, 400 kV Nagda-Shujalpur-1&2, 400 kV Nagda-Dehgam-1&2, 400 kV Nagda-Ujjain-1&2 and 400/220 kV Nagda-ICT-3 were in service through respective tie bays. 400/220 kV Nagda-ICT-4 tripped on B phase differential protection operation due to flashover caused by burnig oil which spread from Y phase CT of 400 kV Nagda-Badnawar-2 in adjacent bay. 400 kV Nagda-Badnawar-1 tripped on B-E fault (Zone-1) due to flashover caused by burnig oil which spread from Y phase CT of 400 kV Nagda-Badnawar-2 in adjacent bay. 400 kV Nagda-Indirasagr tripped due to no other element connected in dia at Nagda end and DT sent to Indirasagar end. 400/220 kV Nagda-ICT-1 tripped because 400 kV Nagda-Bus Reactor was connected in dia at 400 kV Nagda end. At Badnawar end, R phase breaker of 400 kV Nagda-Badnawar-2 didn't open resulting in LBB operation of 400 kV Badnawar-Main Bus-2 and at the same time 400 kV Badnawar-Main Bus-1 tripped on End fault (Busbar) protection operation which was a maloperation. With this 400 kV side of Badnawar substation became dead. Load loss of 22 MW occurred due to the event as the 220 kV network at Nagda and Badnawar were intact.	Tripping of following Elements: 1. 400 kV Nagda-Bus-1&2 2. 400 kV Nagda-Badnawar-2 3. 400/220 kV Nagda-ICT-1&4 4. 400 kV Nagda-Badnawar-1 5. 400 kV Nagda-Indirasagr 6. 400 kV Nagda-Bus Reactor 7. 400 kV Badnawar-Main Bus-1&2 8. 400kV Badnawar-Rajgarh-1&2 9. 400 kV Badnawar-Pritampur-1&2 10. 400/220 kV Badnawar ICT-1&2 11. 400 kV Badnawar-Bus Reactor

20.Details of Grid Events during the Month of April 2024 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
14	GI-2	WR	20:15 / 23-04-2024	00:34 / 24-04-2024	04:19	1800	-	0.022756005	-	79100	62309	At 20:15 Hrs / 23-04-2024, 400 kV Tiroda-Warora-2 tripped on persistent R-E fault after successful auto recloser attempt.Due to failure of R phase breaker pole of main bay of 400 kV Tiroda-Warora-2 at Tiroda (R-phase pole found cracked), 400 kV Tiroda-Warora-1 tripped from Warora end on Z-2 protection operation and 765 / 400 kV Tiroda-ICT-1 tripped on earth fault protection operation. After 300 msec of tripping of 400 kV Tiroda-Warora-2, Tiroda (Adani) Unit-1,2 & 3 (660 MW*3) tripped due to differential protection operation of GTs on R-E fault which was undesirable.As informed by (Tiroda) Adani, maloperation of the relays of GTs is under inspection and it may be due to CT saturation of GTs due to high fault current as the fault was near to generating station (4 km from Tiroda end). With these trippings 400 kV Tiroda-Bus-1&2 became dead due to no voltage source. As informed by Adani-Tiroda, there were heavy storm and lightning near Tiroda during the event. Generation loss of about 1800 MW occured at APML Tiroda.	Tripping of following Elements: 1. 400 kV Tiroda-Warora-1&2 2. Tiroda (Adani) Unit-1,2 & 3 (660 MW*3), 3. 765 / 400 kV Tiroda-ICT-1 4. 400 kV Tiroda-Bus reactor-1&2
15	GI-2	WR	13:49 / 26-04-2024	14:33 / 26-04-2024	00:44	-	976	-	0.01423	75907	68586	At 13:49 Hrs / 26-04-2024, 400 kV Pune(PG)-Bus-2 Y-phase conductor snapped resulting in Busbar protection operation. Prior to the tripping 407 bay (Main bay of 400 kV Pune(PG)-Pune(GIS)-2) at Pune(PG) was under planned shutdown for AMP work, due to this 400 kV Pune(PG)-Pune(GIS)-2 and 400 kV Pune(PG)-Pune(GIS)-3 power flow became zero as they are in same dia at 400 kV Pune(PG). 400/220 kV Pune(PG)-ICT-1&2 tripped from LV side only during bus bar protection operation which is undesirable. As informed by Powergrid, the maloperation of relay is under investigation. Load loss of 976 MW occurred in Pune area due to LTS operation and DLS (Distress Load Shedding) by Maharashtra.	Tripping of following Elements: 1. 400 kV Pune(PG)-Bus-2 2. 400/220 kV Pune(PG)-ICT-1&2
16	GD-1	WR	18:54 / 30-04-2024	20:43 / 30-04-2024	01:49	244	-	0.002959656	-	82442	66681	At 18:54 Hrs / 30-04-2024, 220 kV Bhuj-Gadhsisa tripped due on B-E fault. During patrolling no abnormality was found. Generation loss of 244 MW occurred at Gadhsisa (Renew Power) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa

20.Details of Grid Events during the Month of April 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Karnataka	06-04-2024 18:19	06-04-2024 18:34	0:15	0	415	0.00%	0.80%	40775	52025	Tripping of 220kV Bus-1 220kV/110kV Kemar SS and Complete Outage of 220kV/110kV Kavoor SS and 220kV/110kV MSEZ SS of KPTCL: As per the reports submitted, while charging 220kV/110kV Transformer-3 of 220kV/110kV Kemar SS, 220kV Bus-1 LBB operated and all the elements connected to 220kV/110kV Kemar Bus-1 tripped. Since 220kV/110kV Kavoor SS and 220kV/110kV MSEZ SS are being radially fed from 220kV Bus-1 220kV/110kV Kemar SS tripping of the bus resulted in complete outage of Kavoor and MSEZ.	1. 220kV Kemar UPCL Line-1&2 2. 220kV Kemar Bajpe Line-1&2 3. 220kV Kemar Kavoor Line-3 4. 220kV/110kV Kemar Transformer-1&3
2	GD-1	Karnataka	13-04-2024 18:10	13-04-2024 19:47	1:37	62	31	0.16%	0.06%	38387	48567	Complete Outage of 220kV/33kV Gopalpura SS of SUZLON_KAR: As per the reports submitted, the triggering incident was 33kV level fault at 220/33kV Gopalpura station. However due to DC Supply failure at 220kV/33kV Gopalpura SS, the fault was cleared by the tripping of the lines connected to Gopalpura at remote ends causing a complete outage of the station. Wind Gen Loss: 62 MW	1. 220kV Gopalpura Hassan 2. 220kV Gopalpura Tubinekere
3	GD-1	Tamil Nadu	14-04-2024 18:19	14-04-2024 23:44	05:25	0	420	0.00%	0.94%	35345	44837	Complete Outage of 230kV/110kV Acharapakkam SS, 230kV/110kV Villupuram SS, 230kV/110kV Thiruvanammali SS of TANTRANSCO and Multiple trippings at 230kV/110kV NNTPP Generating station and tripping of 230kV Bus-1 of 230/110kV Cuddalore SS of TANTRANSCO: During antecedent conditions, 230kV/110kV Acharapakkam SS, 230kV/110kV Villupuram SS, 230kV/110kV Cuddalore SS, 230kV/110kV Thiruvanammali SS are being fed from 400kV/110kV NNTPP ICTs and 220kV Maps Acharapakkam line. As per the reports submitted, the triggering incident was tripping of 400kV/110kV NNTPP ICT-1 on PRD. Subsequently, 400kV/110kV NNTPP ICT-2, 230kV MAPS Acharapakkam line and 230kV Singarpet-Tiruvanamalai tripped on over loading. Tripping of all sources led to complete outage of 230kV/110kV Acharapakkam SS, 230kV/110kV Villupuram SS, 220kV/110kV Cuddalore SS, 230kV/110kV Thiruvanammali SS.	1. 400kV/110kV NNTPP ICT-1&2 2. 230kV MAPS Acharapakkam Line 3. 230kV Singarpet Tiruvanamalai
4	GD-1	Tamil Nadu	18-04-2024 04:31	21-04-2024 08:44	04:11	0	0	0.00%	0.00%	41829	52302	Complete Outage of 765kV/400kV NCPS of TANTRANSCO and 765kV/400kV NCTPS Stage-3 of TANGEDCO: During antecedent conditions, 765kV Ariyalur NCPS Line-2 was under outage. As per the reports submitted, the triggering incident was Y-N fault in 765KV-ARIYALUR-NCPS-1 and the line tripped. Tripping of only source resulted in complete outage of 765kV/400kV NCPS and which in turn led to complete outage of 765kV/400kV NCTPS Stage-3.	1. 765kV NCPS Ariyalur Line-1
5	GD-1	Karnataka	18-04-2024 15:49	18-04-2024 17:27	01:38	30	0	0.06%	0.00%	51512	64484	Complete Outage of 220kV Ayana_Six_Koppal: As per the reports submitted, 220KV-KOPPAL-Ayana_Six_Koppal-1 line tripped only at Ayana_Six_Koppal on over current protection due to R-Y fault in a downstream 33kV Line. Tripping of the only connected line led to complete outage of 220KV-KOPPAL-Ayana_Six_Koppal-1.Wind Gen Loss: 30 MW	1.220KV-KOPPAL-Ayana_Six_Koppal-1
6	GD-1	Tamil Nadu	21-04-2024 04:01	21-04-2024 09:36	05:35	0	0	0.00%	0.00%	41489	49432	Complete Outage of 765kV/400kV NCPS of TANTRANSCO and 765kV/400kV NCTPS Stage-3 of TANGEDCO: As per the reports submitted, the triggering incident was Y-N fault in 765KV-ARIYALUR-NCPS-1 and the line tripped. subsequently,765KV-ARIYALUR-NCPS-2 tripped on over voltage protection at NCPS end. Tripping of both lines resulted in complete outage of 765kV/400kV NCPS and which in turn led to complete outage of 765kV/400kV NCTPS Stage-3.	1. 765kV NCPS Ariyalur Line-1&2
7	GD-1	Karnataka	22-04-2024 15:53	22-04-2024 17:15	01:22	36	180	0.07%	0.29%	48909	62001	Complete Outage of 220kV Nadhihal Pooling Station, 220kV GM Navar SS, 220kV/110kV Bijapur SS, 220kV/110kV Indi SS, and 220kV/110kV Aheri SS: 220kV Nadhihal Pooling Station is operating with single bus. As per the reports submitted, the triggering incident was R-N fault in 220kV Kudgi Nandhihal Line-3. At Nandhihal end, the fault was not cleared and LBB operated. Immediately, all lines connected to 220kV Nandihal bus tripped resulting in complete outage of 220kV Nadhihal Pooling Station. This further led to complete outage of 220kV/110kV Bijapur SS, 220kV/110kV Indi SS, and 220kV/110kV Aheri SS. Solar Gen Loss: 36 MW	1.220kV Kudgi Nandihal 3,4,5&6 2. 220kV Nadihal GM Navar Line-1&2 3. 220kV Nandihal Bijapur Line-1&2
8	GD-1	Tamil Nadu	23-04-2024 04:40	23-04-2024 15:26	10:46	420	0	1.04%	0.00%	40364	49326	Complete Outage of 230kV NCTPS Generating station of TANGEDO: As per the reports submitted, all 230kV Feeders connected to the generating station tripped on different faults. Subsequently, NCTPS Units tripped on over frequency protection. This resulted in complete outage of 230kV NCTPS Generating station.	1. 230kV NCTPS Tondiarpet Line-1&2 2. 230kV NCTPS – Alamathy 3. 230kV NCTPS Kilpauk 4. 230kV NCTPS Sriperumbudur
9	GD-1	Tamil nadu	23-04-2024 05:46	23-04-2024 21:33	15:47	0	0	0.00%	0.00%	40904	49623	Complete Outage of 765kV/400kV NCPS of TANTRANSCO and 765kV/400kV NCTPS Stage-3 of TANGEDCO: During antecedent conditions, 765kV/400kV NCPS and 765kV/400kV NCTPS Stage-3 are being radially fed from 765kV Ariyalur-NCPS Line-2 as 765kV Ariyalur-NCPS Line-1 was under outage. The triggering incident is the Y-N fault in 765kV Ariyalur-NCPS Line-2 at a distance of 232km from Ariyalur end. At Ariyalur end, the fault was sensed in carrier aided zone-2 and all three poles tripped. At NCPS end, the fault was sensed in zone-1, A/R operated and line was holding.Tripping of only source led to complete outage of 765kV/400kV NCPS and 765kV/400kV NCTPS Stage-3	1. 765kV Ariyalur-NCPS Line-2
10	GD-1	Karnataka	30-04-2024 12:31	30-04-2024 13:48	01:17	0	260	0.00%	0.40%	53367	64578	Complete Outage of 220kV/66kV Chintamani SS and 220kV/66kV Srinivaspura SS of KPTCL: 220kV/66kV Chintamani SS and 220kV/66kV Srinivaspura SS are being radially fed through 220kV Kolar Chintamani Line-1&2. At 12:21hrs, 220kV Kolar Chintamani Line-2 tripped on R-N fault. Subsequently, 220kV Kolar Chintamani Line-1 tripped on R-N fault at 12:31hrs, tripping of both lines led to complete outage of 220kV/66kV Chintamani SS and 220kV/66kV Srinivaspura SS.	1. 220kV Kolar Chintamani Line-1&2

20.Details of Grid Events during the Month of April 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Chatra	06.04.2024 14:05	06.04.2024 15:01	00:56	0	40	0.00%	0.15%	27564	26265	At 14:05, 220kV Chatra-Latehar tripped only from Latehar end in Zone-2.At the same time, 220kV Chatra Daltongunj-1 tripped in Z-4 from Chatra end. This led to total power failure at 220kV Chatra S/S with approximate load loss of 40MW. At 15:01 Hrs, 220kV Chatra-Latehar was charged and power was restored at Chatra S/s.	220 kV Latehar-Chatra-1 220 kV Daltoanganj-Chatra-1
2	GD-1	Tenughat	18.04.2024 22:12	18.04.2024 23:42	01:30	300	0	1.01%	0.00%	29829	28679	At 22:12 hrs., an insulator flashover occurred in 220 kV Bus#1 Y-phase at 400/ 220kV Tenughat(Jharkhand), 2x210MW generating station. Bus bar protection didn't operate and subsequently 220kV Tenughat-Biharsarif and 220kV Tenughat-Govindpur D/C tripped from remote ends in Zone-2. This caused tripping of both the running units at Tenughat and resulted in a generation loss of about 300MW. At 23:42 hrs, 220 kV Bus#2 was charged through 220 kV Tenughat-Biharsarif.	220 kV Tenughat-Govindpur-1 220 kV Tenughat-Govindpur-2 220 kV Tenughat-Biharsharif-1 2*210 MW Units at Tenughat
3	GD-1	Pratapsasan	23.04.2024 14:22	23.04.2024 14:38	00:16	0	226	0.00%	0.88%	26628	25551	At 14:22 Hrs on 23.04.2024, 220 kV Pandiabili-Pratapsasan D/c tripped due to operation of bus bar protection at Pratapsasan during some testing work, leading to total power failure. Load loss of around 226 MW occurred at Pratapsasan.	220 kV Pandiabili-Pratapsasan D/c
4	GD-1	Kasba	25.04.2024 21:42	25.04.2024 22:05	00:23	0	601	0.00%	2.06%	32264	29135	At 21:42 Hrs on 25.04.2024, B_ph CT of 220 kV Kasba-Subahshgram-1 burst at Kasba. Bus bar prtoection operated at Kasba and it has single main and transfer bus scheme, leading to total power failure. CESC system which was syncrhonized at Kasba got islanded. Total load loss of around 601 MW occurred.	220 kV Kasba-Subahshgram D/c 220 kV Kasba-Barasat D/c 220 kV Kasba-EMSS Soutch (CESC) D/c 2*150 MVA 220/132 kV ATR-1&2 2*160 MVA 220/132 kV ATR-3&4
5	GD-1	Kasba	25.04.2024 23:17	25.04.2024 23:26	00:09	0	489	0.00%	1.64%	32958	29782	At 23:17 Hrs on 25.04.2024, 220 kV Kasba-subhahsgram-2 tripped on O/c with current reaching around 1180 A in each phase. Load restriction shceme is also implemented in this line which tripped 220 kV Kasba-Barast D/c and 132 kV feeders at Kasba. Thereby 220 kV Kasba S/s became dead. CESC system got islanded again. Load loss of around 489 MW occurred.	220 kV Kasba-Subahshgram-2 220 kV Kasba-Barasat D/c 220 kV Kasba-EMSS Soutch (CESC) D/c 2*150 MVA 220/132 kV ATR-1&2 2*160 MVA 220/132 kV ATR-3&4

20.Details of Grid Events during the Month of April 2024 in North-East Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD1	Chiephobozou area of Nagaland Power system	01-04-2024 15:36	01-04-2024 17:46	02:10:00	0	1	0.00%	0.05%	2178	2059	Chiephobozou area of Nagaland Power System was connected with rest of NER Grid through 132 kV Wokha – Chiephobozou and 132 kV Kohima- Chiephobozou lines. At 15:36 Hrs of 01-04-2024, 1132 kV Wokha – Chiephobozou and 132 kV Kohima- Chiephobozou lines tripped. Due to tripping of these elements,Chiephobozou area of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Chiephobozou area of Nagaland Power System by charging 132 kV Kohima- Chiephobozou line at 17:49 Hrs of 01-04-2024.	132 kV Wokha – Chiephobozou and 132 kV Kohima- Chiephobozou lines
2	GD1	Lumshnong area of Meghalaya Power system	01-04-2024 03:40	01-04-2024 04:07	00:27:00	0	27	0.00%	2.48%	1798	1089	Lumshnong area of Meghalaya Power System was connected with rest of NER Grid through 132 kV Lumshnong – Khliehriat and 132 kV Lumshnong - Panchgram Lines. At 03:40 Hrs of 01-04-2024, 132 kV Lumshnong – Khliehriat and 132 kV Lumshnong - Panchgram Lines tripped. Due to tripping of these elements, Lumshnong area of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Lumshnong area of Meghalaya Power System by charging 132 kV Lumshnong – Khliehriat line at 04:07 Hrs of 01-04-2024.	132 kV Lumshnong – Khliehriat and 132 kV Lumshnong - Panchgram Lines
3	GD1	Pasighat area of Arunachal Pradesh Power system	02-04-2024 21:55	03-04-2024 00:40	02:45:00	0	5	0.00%	0.22%	2680	2280	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Pasighat- Roing & 132 kV Along - Pasighat lines. At 21:55 Hrs of 02-04-2024, 132 kV Pasighat- Roing line & 132 kV Along - Pasighat line tripped. Due to tripping of these elements, Pasighat area of Arunachal Pradesh Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Pasighat area of Arunachal Pradesh Power System by charging 132 kV Pasighat- Roing line at 00:40 Hrs of 03-04-2024.	132 kV Pasighat- Roing & 132 kV Along - Pasighat lines
4	GD1	Zuangtui and radially connected Serchhip, Saitual, Khawawl and Vankal areas of Mizoram Power system	04-04-2024 16:21	04-04-2024 16:56	00:35:00	0	38	0.00%	1.58%	2064	2408	Zuangtui and radially connected Serchhip, Saitual, Khawawl and vankal areas of Mizoram power system were connected with rest of NER Grid through 132 kV Melriat(PG)-Zuangtui line. 132 kV Serchhip-Lunglei line is kept open due to system requirement. At 16:21 Hrs of 04-04-2024, 132 kV Melriat(PG)-Zuangtui line tripped. Due to tripping of this element, Zuangtui and radially connected Serchhip, Saitual, Khawawl and vankal areas of Mizoram Power system got isolated from NER grid due to no source available in this area. Power supply was extended to Zuangtui and radially connected Serchhip, Saitual, Khawawl and vankal areas Mizoram Power System by charging 132 kV Melriat(PG)-Zuangtui line at 16:56 Hrs of 04-04-2024.	32 kV Melriat(PG)-Zuangtui line
5	GD1	Dharmanagar area of Tripura and Dullavchhera area of Assam Power System	07-04-2024 11:52	07-04-2024 12:12	00:20:00	0	9	0.00%	0.46%	1853	1974	Dharmanagar area of Tripura Power System & Dullavchhera area of Assam Power System are connected with rest of NER Grid through 132 kV PK Bari-Dharmanagar and 132 kV Dullavchhera - Hailakandi lines. 132 kV P K Bari-Dharmanagar line was under outage since 09:15 Hrs of 07-04-2024 for facilitating shutdown of 132 kV PK Bari Substation. At 11:52 Hrs of 07-04-2024, 132 kV Dullavchhera-Hailakandi line tripped. Due to tripping of this element, Dharmanagar area of Tripura and Dullavchhera area of Assam power system got isolated from NER grid due to no source available in these areas. Power supply was extended to Dharmanagar and Dullavchhera areas by charging 132 kV Dullavchhera-Hailakandi line at 12:12 Hrs of 07-04-2024.	132 kV Dullavchhera-Hailakandi line
6	GD1	Depota, Rowta, Dhekiajuli and Tangla areas of Assam Power system	07-04-2024 13:41	07-04-2024 13:54	00:13:00	0	23	0.00%	1.25%	1774	1841	Depota, Rowta, Dhekiajuli, and Tangla areas of Assam Power System were connected with rest of NER Grid through 132 kV Depota Sonabil and 132 kV Depota Ghoramari. 132 kV Depota Dhekiajuli already under shutdown w.e.f. 10:48 for protection relay testing. At 13:29 Hrs of 07-04-2024, 132 kV Depota Sonabil and at 13:41 Hrs of 07-04-2024, 132 kV Depota Ghoramari lines tripped due to which Depota, Rowta, Dhekiajuli, and Tangla areas of Assam Power System were isolated from NER Grid and collapsed due to no source available in these areas. After tripping of the above lines, 132 kV Tangla GSS was shifted to 132 kV Rangia side to restore power to them at 15:40 hrs. 132 kV Depota Rowta was manually opened for safety purpose at 13:45 hrs. Later, 132 kV Sonabil Depota was charged at 13:54 hrs and 132 kV Depota Ghoramari was charged at 14:03 hrs. After that 132 kV Depota Rowta was manually closed at 14:04 hrs. After restoring all the mentioned lines 132 kV Tangla GSS was again shifted back to Rowta side.	132 kV Sonabil-Depota and 132 kV Depota-Ghoramari lines
7	GD1	Thoubal, Thoubal old, Kongba, Kakching, Chandel and Moreh area of Manipur Power system and Tamu load of Myanmar Power System	07-04-2024 13:59	07-04-2024 14:25	00:26:00	0	60	0.00%	3.38%	1865	1777	Thoubal, Thoubal old, Kongba, Kakching, Chandel and Moreh area of Manipur Power System and Tamu load of Myanmar Power System were connected with rest of NER Grid through 132 kV Yaingangpokpi – Kongba D/C Lines and 400/132 kV ICT at Thoubal (MSPCL). At 13:59 Hrs of 07-04-2024, 132 kV Yaingangpokpi – Kongba D/C Lines and 400/132 kV ICT at Thoubal tripped. Due to tripping of these elements, Thoubal, Thoubal old, Kongba, Kakching, Chandel and Moreh area of Manipur Power System and Tamu load of Myanmar Power System got isolated from NER grid due to no source available in these areas. Power supply was extended to Kongba S/S by charging 132 kV Yaingangpokpi – Kongba 2 Line at 14:25 Hrs of 07.04.2024. Power supply was extended to Kakching, Chandel, Moreh S/S of Manipur and Tamu load of Myanmar Power system by charging 132kV Kakching-Elangkangpokpi line at 14:47 Hrs of 07.04.2024.	132 kV Yaingangpokpi – Kongba D/C Lines and 400/132 kV ICT at Thoubal
8	GD1	Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh and Chapakhowa area of Assam Power System	07-04-2024 19:45	07-04-2024 22:18	02:33:00	0	16	0.00%	0.60%	3172	2663	Chapakhowa area of Assam power system and Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh power system were connected with rest of NER grid through 132 kV Rupai-Chapakhowa and 132 kV Along-Basar lines. Prior to the event, 132 kV Along-Basar line tripped at 17:31 Hrs of 07-04-2024 due to falling of tree on the line. At 19:45 Hrs of 07-04-2024, 132 kV Rupai-Chapakhowa line tripped. Due to tripping of this element, Chapakhowa area of Assam Power System and Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Chapakhowa area of Assam Power System by charging 132 kV Chapakowa-Rupai line at 22:12 Hrs of 07-04-2024 and Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh power system by charging 132 kV Roing-Chapakhowa – I & II at 22:18 hrs & 22:20 hrs of 07-04-2024 respectively.	132 kV Rupai-Chapakhowa line
9	GD1	Monarchak generation and Rabindranagar area of Tripura Power system	08-04-2024 13:04	08-04-2024 13:29	00:25:00	75	10	4.44%	0.42%	1691	2362	Monarchak Generation and Rabindranagar area of Tripura Power System were connected with rest of NER Grid through 132 kV Monarchak – Udaipur and 132 kV Monarchak – Rokhia lines. Prior to the event, 132 kV Monarchak-Rokhia line was under planned shutdown. At 13:04 Hrs of 08-04-2024, 132 kV Monarchak-Udaipur line tripped. Due to tripping of this element, Monarchak generation and Rabindranagar area of Tripura Power System was isolated from NER Grid and collapsed due to load generation mismatch in these areas. Power was extended to Rabindranagar area of Tripura Power System by charging 132 kV Monarchak – Udaipur line at 13:29 Hrs of 08-04-2024.	132 kV Monarchak-Udaipur line, Monarchak GT & ST
10	GD1	Pasighat area of Arunachal Pradesh Power system	14-04-2024 14:29	14-04-2024 14:59	00:30:00	0	4	0.00%	0.17%	1589	2304	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Pasighat- Roing & 132 kV Along - Pasighat lines. At 14:29 Hrs of 14-04-2024, 132 kV Pasighat- Roing & 132 kV Along - Pasighat lines. Due to tripping of these elements, Pasighat area of Arunachal Pradesh Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Pasighat area of Arunachal Pradesh Power System by charging 132 kV Roing-Pasighat line at 14:59 Hrs of 14-04-2024.	132 kV Roing-Pasighat & 132 kV Along-Pasighat lines

20.Details of Grid Events during the Month of April 2024 in North-East Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
11	GD1	Mawlai and Cherrapunji area of Meghalaya Power system	14-04-2024 17:15	14-04-2024 18:40	01:25:00	0	18	0.00%	0.75%	1848	2406	Mawlai & Cherapunji areas of Meghalaya Power System were connected with rest of NER Grid through 132 kV Mawlai - Mawngap, 132 kV Mawlai - NEHU & 132 kV Mawlai -Umiam 1 lines. At 17:15 Hrs of 14-04-2024, 132 kV Mawlai - Mawngap, 132 kV Mawlai - NEHU & 132 kV Mawlai -Umiam 1 lines tripped. Due to tripping of these elements, Mawlai and Cherrapunji areas Meghalaya Power System were isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Mawlai area of Meghalaya Power System by charging 132 kV Mawlai-Mawngap line at 18:40 Hrs of 14-04-2024.	132 kV Mawlai - Mawngap, 132 kV Mawlai - NEHU & 132 kV Mawlai -Umiam 1 lines
12	GD1	Leshka generating station of Meghalaya Power system	15-04-2024 13:02	15-04-2024 13:27	00:25:00	0	0	0.00%	0.00%	1773	2429	Leshka Generating Station of Meghalaya Power System was connected with rest of NER Grid through 132 kV Leshka-Khliehriat D/C lines. At 13:02 Hrs of 15-04-2024, 132 kV Leshka-Khliehriat D/C lines tripped. Due to tripping of these elements, blackout of Leshka Generating Station of Meghalaya Power system occurred. Power restored to Leshka Generating Station of Meghalaya Power System by charging 132 kV Leshka-Khliehriat 1 line at 13:27 Hrs of 15-04-2024.	132 kV Leshka-Khliehriat D/C
13	GD1	New Umtru generating station of Meghalaya Power system	15-04-2024 14:52	15-04-2024 15:03	00:11:00	0	0	0.00%	0.00%	1680	2464	New Umtru Generating Station of Meghalaya Power System was connected with rest of NER Grid through 132 kV Umtru – New Umtru line and 132kV New Umtru – EPIP II line. At 14:52 Hrs of 15-04-2024, 132 kV Umtru – New Umtru line and 132kV New Umtru – EPIP II line. Due to tripping of these elements blackout of New Umtru Generating Station of Meghalaya Power system occurred. Power restored to New Umtru Generating Station of Meghalaya Power System by charging 132kV New Umtru – EPIP II line at 15:03 Hrs of 15-04-2024.	132 kV Umtru – New Umtru line and 132kV New Umtru –EPIP II line
14	GD1	Dhaligaon, Gossaigaon, Barpeta and part load of Bornagar areas of Assam Power System	16-04-2024 04:04	16-04-2024 04:32	00:28:00	0	82	0.00%	4.24%	1899	1932	Dhaligaon, Gossaigaon, Barpeta and part load of Bornagar areas of Assam Power System were connected with rest of NER Grid through 132 kV BTPS - Dhaligaon 1 & 2 Lines. 132 kV Gauripur-Gossaigaon was open to avoid overloading of 132 kV Bilasipara Gauripur line and 132 kV Barpeta-Nalbari line was kept open to avoid overloading of 132 kV BTPS - Dhaligaon D/C Lines. At 04:04 Hrs of 16-04-2024, 132 kV BTPS - Dhaligaon 1 & 2 Lines tripped. Due to tripping of these elements blackout of Dhaligaon, Gossaigaon, Barpeta and part load of Bornagar areas of Assam Power System occurred due to no source available in these area.	132 kV BTPS - Dhaligaon 1 & 2
15	GD1	New Umtru Generating Station of Meghalaya Power System	16-04-2024 08:58	16-04-2024 09:26	00:28:00	0	0	0.00%	0.00%	1649	1956	New Umtru Generating Station of Meghalaya Power System was connected with rest of NER Grid through 132 kV Umtru – New Umtru line and 132kV New Umtru – EPIP II line. At 08:58 Hrs of 16-04-2024, 132 kV Umtru – New Umtru line and 132kV New Umtru – EPIP II line. Due to tripping of these elements blackout of New Umtru Generating Station of Meghalaya Power system occurred. Power restored to New Umtru Generating Station of Meghalaya Power System by charging 132kV New Umtru – EPIP II line at 09:26 Hrs of 16-04-2024.	132 kV Umtru – New Umtru line and 132kV New Umtru –EPIP II line
16	GD1	Rongkhon, Ampati area & Ganol HEP of Meghalaya Power System	16-04-2024 11:46	16-04-2024 13:00	01:14:00	0	30	0.00%	1.42%	1421	2108	Rongkhon, Ampati area & Ganol HEP of Meghalaya Power System is connected with rest of NER Grid through 132 kV Nangalbibra-Rongkhon line. At 11:46 Hrs of 16-04-2024, 132 kV Nangalbibra-Rongkhon line tripped. Due to tripping of this element, blackout of Rongkhon, Ampati area & Ganol HEP of Meghalaya Power System occurred. Power restored to Rongkhon, Ampati area & Ganol HEP of Meghalaya Power System by charging 132 kV Nangalbibra-Rongkhon line at 13:00 Hrs of 16-04-2024.	132 kV Nangalbibra-Rongkhon line
17	GD1	Wokha and Chiephobozou areas of Nagaland Power System	16-04-2024 23:42	17-04-2024 08:25	08:43:00	0	13	0.00%	0.60%	2053	2169	Wokha and Chiephobozou areas of Nagaland Power System were connected with rest of NER Grid through 132 kV Sanis-Wokha line and 132 kV Wokha-Chiephebozou – Kohima link. At 23:42 Hrs of 16-04-2024, 132 kV Sanis – Wokha line, 132 kV Wokha - Chiephobozou- Kohima link tripped. Due to tripping of these element, Wokha and Chiephobozou areas of Nagaland Power System were isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Wokha and Chiephebozou areas of Nagaland power system by charging 132 kV Sanis-Wokha line at 08:25 Hrs of 17.04.2024.	132 kV Sanis – Wokha line, 132 kV Wokha - Chiephobozou- Kohima link tripped
18	GD1	Dhekiajuli area of Assam Power system	17-04-2024 01:16	17-04-2024 01:30	00:14:00	0	11	0.00%	0.59%	1965	1860	Dhekiajuli area of Assam power system is connected with the rest of NER grid through 132 kV Depota-Dhekiajuli-Rowta link. At 01:16 Hrs of 17-04-2024, 132 kV Depota-Dhekiajuli-Rowta link tripped. Due to tripping of these elements, Dhekiajuli area of Assam power sytem got isolated due to no source available in this area. Power was extended to Dhekiajuli area of Assam power system by charging 132 kV Rowta-Dhekiajuli line at 01:30 Hrs of 17-04-2024.	132 kV Depota-Dhekiajuli-Rowta
19	GD1	Ningthoukhong area of Manipur Power System	17-04-2024 10:25	17-04-2024 11:45	01:20:00	0	9	0.00%	0.47%	1480	1920	Ningthoukhong area of Manipur Power System were connected with rest of NER Grid through 132 kV Loktak- Ningthoukhong and 132kV Imphal(PG)- Ningthoukhong lines. 132 kV Ningthoukhong - Churachandpur 1 Line was under tripped condition from 15:21 Hrs of 26.03.2024 and 132 kV Ningthoukhong - Churachandpur 2 Line was under tripped condition from 09:25 Hrs of 17.04.2024. At 10:25 Hrs of 17-04-2024, 132 kV Loktak- Ningthoukhong and 132kV Imphal(PG)-Ningthoukhong lines tripped (while charging attempt of Ningthokhong- Churachandpur 2 line). Due to tripping of these elements blackout of Ningthoukhong area of Manipur Power System occurred due to no source available in this area.	132 kV Loktak- Ningthoukhong and 132kV Imphal(PG)-Ningthoukhong lines
20	GD1	Wokha and Chiephobozou areas of Nagaland Power System	17-04-2024 18:19	17-04-2024 18:59	00:40:00	0	3	0.00%	0.11%	2933	2770	Wokha and Chiephebozou areas of Nagaland Power System was connected with rest of NER Grid through 132 kV Sanis-Wokha line and 132 kV Wokha-Chiephebozou line. Prior to the event, 132 kV Wokha-Chiephebozou line tripped at 11:42 Hrs of 17.04.2024. At 18:19 Hrs of 17-04-2024, 132 kV Sanis – Wokha line and 132 kV Wokha – Chiephobozou line tripped. Due to tripping of this element, Wokha and Chiephebozou areas of Nagaland Power System got isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Wokha and Chiephebozou areas of Nagaland power system by charging 132 kV Sanis-Wokha line at 18:59 Hrs of 17.04.2024.	132 kV Sanis – Wokha line

20.Details of Grid Events during the Month of April 2024 in North-East Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
21	GD1	Kolasib area, Turial HEP & Bairabi Generating Station of Mizoram Power System	17-04-2024 19:58	17-04-2024 20:32	00:34:00	20	1	0.62%	0.04%	3202	2597	Kolasib area, Turial HEP & Bairabi Generating Station of Mizoram Power System were connected with rest of NER Grid through 132 kV Aizawl – Kolasib line. 132 kV Badarpur-Kolasib line was under outage since 16:39 Hrs of 17.04.2024. At 19:58 Hrs of 17-04-2024, 132 kV Aizawl – Kolasib line tripped. Due to tripping of this element Kolasib area, Turial HEP & Bairabi Generating Station of Mizoram Power System were isolated from NER Grid due to no source available in these areas. Power supply was extended to Kolasib area, Turial HEP & Bairabi Generating Station of Mizoram Power System by charging 132 kV Aizawl – Kolasib line at 20:32 Hrs of 17-04-2024.	132 kV Aizawl – Kolasib line
22	GD1	Serchhip area of Mizoram Power System	17-04-2024 20:30	-	-	0	5	0.00%	0.20%	3186	2543	Serchhip area of Mizoram Power System was connected with rest of NER Grid through 132 kV Zuangtui - Serchhip line. 132kV Serchhip – Lunglei kept open for system requirement. At 20:30 Hrs of 17-04-2024, 132 kV Zuangtui - Serchhip line tripped. Due to tripping of this element Serchhip area of Mizoram Power System was isolated from NER Grid and collapsed due to no source available in this area.	132 kV Zuangtui - Serchhip line
23	GD1	Tuirial generating station of Mizoram Power System	18-04-2024 11:14	18-04-2024 11:55	00:41:00	0	0	0.00%	0.00%	1184	2108	Tuirial generating station of Mizoram Power System was connected with rest of NER Grid through 132kV-Tuirial-Kolasib line. At 11:14 Hrs of 18-04-2024, 132 kV-Tuirial-Kolasib line tripped. Due to tripping of this Tuirial generating station of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial generating station of Mizoram Power System by charging 132kV-Tuirial-Kolasib line at 11:55 Hrs of 18-04-2024.	132 kV-Tuirial-Kolasib line
24	GD1	Rabindranagar area & Monarchak Generatng Units & Rokhia Generating Units of Tripura Power System	18-04-2024 03:40	18-04-2024 04:50	01:10:00	35	15	1.72%	0.94%	2030	1588	Rabindranagar area & Monarchak Generatng Units & Rokhia Generating Units of Tripura Power System were connected with rest of NER Grid through 132 kV Monarchak – Udaipur line. 132 kV Agartala- Rokhia D/C lines were under outage since 03:07 Hrs. At 03:04 Hrs of 18-04-2024, 132 kV Monarchak – Udaipur line tripped. Due to tripping of this Rabindranagar area & Monarchak Generatng Units & Rokhia Generating Units of Tripura Power System were isolated from NER Grid and collapsed due to load generation mismatch in this area. Power was extended to Rabindranagar area & Monarchak Generatng Units & Rokhia Generating Units of Tripura Power System by charging 132 kV Monarchak – Udaipur line at 04:50 Hrs of 18-04-2024.	132 kV Monarchak – Udaipur line
25	GD1	Rengpang area of Manipur Power System	19-04-2024 19:52	20-04-2024 16:20	20:28:00	0	2	0.00%	0.08%	3201	2580	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam-Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 19:52 Hrs of 19-04-2024, 132 kV Loktak – Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available this area. Power was extended to Rengpang area of Manipur power system by charging 132 kV Loktak-Rengpang line at 16:20 Hrs of 20-04-2024.	132 kV Loktak – Rengpang line
26	GD1	Turial Generating station of Mizoram Power System	20-04-2024 17:33	20-04-2024 18:08	00:35:00	38	0	1.59%	0.00%	2388	2389	Turial Generating station of Mizoram Power System was connected with rest of NER Grid through 132 kV Turial-Kolasib line. At 17:33 Hrs of 20-04-2024, 132 kV Turial-Kolasib line tripped. Due to tripping of this element, Turial Generating station was isolated from NER Grid leading to generation loss due to no evacuation path. Power was extended to Turial substation by charging 132 kV Turial-Kolasib line at 18:08 Hrs of 20-04-2024.	132 kV Turial-Kolasib line
27	GD1	Wokha area of Nagaland Power System	20-04-2024 21:40	20-04-2024 22:37	00:57:00	0	6	0.00%	0.27%	2277	2248	Wokha area of Nagaland Power System was connected with rest of NER Grid through 132 kV Sanis - Wokha line and 132 kV Wokha- Chiephobozou line. At 21:27 Hrs of 20-04-2024, 132 kV Sanis - Wokha line tripped and prior to restoration, 132 kV Wokha- Chiephobozou line line tripped at 21:40 hrs. Due to tripping of these element, Wokha area of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Wokha area of NagalandPower System, by charging 132 kV Sanis - Wokha line at 22:37 Hrs of 20-04-2024.	132 kV Sanis - Wokha line
28	GD1	Kohima area of Nagaland Power System	21-04-2024 12:11	21-04-2024 12:56	00:45:00	0	4	0.00%	0.20%	1769	1964	Kohima area of Nagaland Power System was connected to rest of NER Grid through 132 kV Kohima – Dimapur line, 132 kV Kohima - Karong line, 132 kV Kohima – Meluri line and 132 kV Kohima - Chiephobozou line At 12:11 Hrs of 21-04-2024, 132 kV Kohima - Dimapur & 132 kV Kohima - Karong line tripped. Due to tripping of these element, as 132 kV Kohima - Meluri line and 132 kV Kohima - Chiephobozou line were already under outage prior to tripping of the above lines, Kohima area of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Kohima area of Nagaland Power System by charging 132 kV Kohima - Dimapur line at 12:56 Hrs of 21-04-2024.	132 kV Kohima - Dimapur & 132 kV Kohima - Karong line
29	GD1	Dharmanagar Area of Tripura Power System	22-04-2024 01:14	22-04-2024 01:37	00:23:00	0	5	0.00%	0.26%	1901	1932	Dharmanagar Substation of Tripura Power System was connected with rest of NER Grid via 132kV PK Bari – Dharmanagar and 132kV Dharmanagar –Dullavcherra lines. At 01:14 Hrs of 22.04.2024,132kV PK Bari – Dharmanagar and 132kV Dharmanagar – Dullavcherra lines tripped. Due to tripping of these lines, Dharmanagar area of Tripura Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Dharmanagar area of Tripura Power System by charging 132 kV PK Bari – Dharmanagar at 01:37 Hrs of 22.04.2024.	132 kV PK Bari-Dharmanagar and 132 kV Dharmanagar-Dullavchhera lines
30	GD1	Leshka generating station of Meghalaya Power system	23-04-2024 20:56	23-04-2024 22:27	01:31:00	0	0	0.00%	0.00%	3097	2916	Leshka Generating Station of Meghalaya Power System was connected with rest of NER Grid through 132 kV Leshka-Khleihriat D/C lines. At 20:56 Hrs of 23-04-2024, 132 kV Leshka-Khleihriat D/C lines tripped. Due to tripping of these elements blackout of Leshka Generating Station of Meghalaya Power system occurred. Power restored to Leshka Generating Station of Meghalaya Power System by charging 132 kV Leshka-Khleihriat I line at 22:27 Hrs of 23-04-2024.	132 kV Leshka-Khleihriat D/C lines
31	GD1	Lumshnong area of Meghalaya Power system	23-04-2024 21:45	23-04-2024 22:02	00:17:00	0	21	0.00%	0.77%	2636	2743	Lumshnong area of Meghalaya Power Systemwere connected with rest of NER Grid through 132 kV Khleihriat-Lumshnong and 132 kV Lumshnong-Panchgram lines. Prior to the event, 132 kV Khleihriat-Lumshnong line tripped at 21:23 Hrs of 23-04-2024. At 21:45 Hrs of 23-04-2024, 132 kV 132 kV Lumshnong-Panchgram line tripped. Due to tripping of this element, Lumshnong area of Meghalaya power system got isolated from the grid due to no source available in this area. Power supply was extended to Lumshnong of Meghalaya Power System by charging 132 kV Khleihriat-Lumshnong Line at 22:02 Hrs of 23-04-2024.	132 kV Khleihriat-Lumshnong and 132 kV Lumshnong-Panchgram lines
32	GD1	Tezu and Namsai areas of Arunachal Pradesh Power System	23-04-2024 18:50	23-04-2024 23:01	04:11:00	0	8	0.00%	0.26%	3086	3111	Tezu and Namsai areas of Arunachal Pradesh Power System were connected with rest of NER Grid via 132 kV Roing - Tezu Line. At 18:50 Hrs of 23.04.2024, 132 kV Roing - Tezu Line tripped. Due to tripping of this line, Tezu and Namsai areas of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Roing-Tezu Line at 23:01 Hrs of 23-04-2024.	132 kV Roing-Tezu line

20.Details of Grid Events during the Month of April 2024 in North-East Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
33	GD1	220 kV Tinsukia S/S in Assam Power System	24-04-2024 01:11	24-04-2024 04:28	03:17:00	0	0	0.00%	0.00%	1944	2124	220 kV Tinsukia S/S in Assam Power System was connected with rest of NER Grid via 220/132 kV ICT 1&2 at Tinsukia, 220kV NTPS - Tinsukia 1 Line, 220 kV Tinsukia-Behiating D/C lines, 220kV NRPP – Tinsukia & 220kV AGBPP - Tinsukia D/C Lines. At 01:11 Hrs of 24.04.2024, 220/132 kV ICT 1&2 at Tinsukia, 220/132 kV Bus-coupler, 220kV NTPS - Tinsukia 1 Line, 220 kV Tinsukia-Behiating D/C lines, 220kV NRPP – Tinsukia & 220kV AGBPP - Tinsukia D/C Lines tripped. Due to tripping of these elements, near Miss event occurred at 220 kV Tinsukia S/S in Assam power System, which could led to major Grid Disturbance. Power supply was extended to 220 kV Tinsukia S/S by charging 220/132kV, 100 MVA ICT 1 at TINSUKIA at 04:28 Hrs of 24.04.2024.	220/132 kV ICT 1&2 at Tinsukia, 220/132 kV Bus-coupler, 220 kV NTPS - Tinsukia 1 Line, 220 kV Tinsukia-Behiating D/C lines, 220kV NRPP – Tinsukia & 220kV AGBPP - Tinsukia D/C Lines
34	GD1	Kohima and Chiephobozou area of Nagaland Power System	24-04-2024 18:59	24-04-2024 19:26	00:27:00	0	18	0.00%	0.77%	1719	2330	Kohima and Chiephobozou area of Nagaland Power System was connected with rest of NER Grid via 132 kV Dimapur(PG) - Kohima Line. Prior to the event, 132 kV Wokha – Chiephobozou line and 132kV Kohima – Chiephobozou line tripped at 18:08 Hrs of 24.04.2024, 132kV-Kohima-Meluri line was under shutdown since 10:05 Hrs of 27.09.2024, 132 kV Karong - Kohima Line tripped at 18:15 of 24.04.2024. At 18:59 Hrs of 24.04.2024, 132 kV Dimapur(PG) - Kohima Line tripped. Due to tripping of this line, Kohima and Chiephobozou area of Nagaland Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Kohima and Chiephobozou areas of Nagaland Power System by charging 132 kV Dimapur(PG) - Kohima Line at 19:26 Hrs of 24.04.2024.	132 kV Dimapur(PG) - Kohima Line
35	GD1	Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar	24-04-2024 15:04	24-04-2024 15:29	00:25:00	0	65	0.00%	2.78%	1742	2337	Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar were connected with rest of NER Grid via 400 kV Imphal (PG) - Thoubal (MSPCL) 2 Line and 132 kV Yaingangpokpi - Kongba Line. 400 kV Imphal (PG) - Thoubal (MSPCL) 2 Line was under outage since 13:32 Hrs of 18.12.2021, 132kV-Ningthoukhong-Churachandpur-1 line was under outage since 15:21 Hrs of 26.03.2024, 132kV-Ningthoukhong-Churachandpur-2 line was under outage since 09:25 Hrs of 17.04.2024 and 132 kV Yaingangpokpi - Kongba 2 Line was idle charged from Yaingangpokpi end. At 15:05 Hrs of 24.04.2024, 400 kV Imphal (PG) - Thoubal (MSPCL) 2 Line and 132 kV Yaingangpokpi - Kongba Line tripped. Due to tripping of these lines, Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar by charging 132 kV Yaingangpokpi - Kongba 1 Line at 15:29 Hrs of 24.04.2024.	400 kV Imphal (PG) - Thoubal (MSPCL) 2 Line and 132 kV Yaingangpokpi - Kongba Line
36	GD1	Rengpang area of Manipur Power System	24-04-2024 14:45	24-04-2024 15:33	00:48:00	0	1	0.00%	0.04%	1720	2326	Rengpang area of Manipur Power System was connected with rest of NER Grid via 132 kV Loktak - Rengpang Line. 132kV-Jiribam-Rengpang Line was under outage since 18:18 Hrs of 17.11.2023. At 14:45 Hrs of 24.04.2024, 132 kV Loktak - Rengpang Line tripped. Due to tripping of this line,Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in theis areas. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak - Rengpang Line at 15:33 Hrs of 24.04.2024.	132 kV Loktak - Rengpang Line
37	GD1	Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar	24-04-2024 17:18	24-04-2024 19:59	02:41:00	0	40	0.00%	1.62%	2116	2465	Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar were connected with rest of NER Grid via 132 kV Yaingangpokpi – Kongba 2 Line. 400 kV Imphal (PG) - Thoubal (MSPCL) 1 Line tripped at 15:05 Hrs of 24.04.2024 due to multiple tower collapse because of high wind at Loc 38A, 39/0, 39/1, 39/2, 39/2, 400 kV Imphal (PG) - Thoubal (MSPCL) 2 Line was under outage since 13:32 Hrs of 18.12.2021, 132kV-Ningthoukhong Churachandpur-1 line was under outage since 15:21 Hrs of 26.03.2024, 132kV-Ningthoukhong Churachandpur-2 line was under outage since 09:25 Hrs of 17.04.2024 and 132 kV Yaingangpokpi – Kongba 1 Line tripped at 16:35 Hrs of 24.04.2024 due to jumper snapping, 132 kV Thoubal new – Kakching was hand tripped at 16:24 Hrs of 24.04.2024. At 17:18 Hrs of 24.04.2024, 132 kV Yaingangpokpi – Kongba 2 Line tripped. Due to tripping of this line, Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Thoubal new, Thoubal old, Kongba, Kakching, Elangkangpokpi, Chandel, Churachandpur, Thanlon and Moreh areas of Manipur Power System of NER and Tamu load of Myanmar by charging 132 kV Yaingangpokpi - Kongba 1 Line at 19:59 Hrs of 24.04.2024.	132 kV Yaingangpokpi – Kongba 2 Line
38	GD1	Karong area of Manipur Power System	25-04-2024 11:38	25-04-2024 12:53	01:15:00	0	10	0.00%	0.44%	1515	2279	Karong area of Manipur Power System was connected with rest of NER Grid via 132 kV Imphal (MSPCL) - Karong Line. 132 kV Karong - Kohima Line was under tripped condition since 18:15 Hrs of 24.04.2024. At 11:38 Hrs of 25-04-2024, 132 kV Imphal (MSPCL) - Karong Line tripped. Due to tripping of this line, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Karong area of Manipur Power System by charging 132 kV Imphal (MSPCL) - Karong Line at 12:53 Hrs of 25.04.2024.	132 kV Imphal (MSPCL) - Karong Line
39	GD1	Ziro and Daporijo area of Arunachal Pradesh Power System	25-04-2024 06:11	25-04-2024 07:01	00:50:00	0	7	0.00%	0.35%	1935	2011	Ziro and Daporijo area of Arunachal Pradesh Power System were connected with rest of NER Grid via 132 kV Panyor-Ziro-Daporijo-Basar-Along-Pasighat-Roing-rest of the grid. 132kV Ziro-Daporijo was under planned shutdown from 06:09hrs of 25.04.2024. At 06:11 hrs 132kV Panyor-Ziro and 132kV Daporijo-Basar tripped resulting in blackout at Ziro and Daporijo substation. Power was extended to Ziro and Daporijo area of Arunachal Pradesh by charging 132 kV-Panyor-Ziro line at 07:01 Hrs of 25-04-2024.	132kV Panyor-Ziro and 132kV Daporijo-Basar lines
40	GD1	Golaghat area of Assam Power System	28-04-2024 12:44	28-04-2024 12:55	00:11:00	0	0.5	0.00%	0.02%	1565	2010	Golaghat area of Assam Power System was connected with rest of NER Grid via 132 kV Golaghat – Sarupathar line and 132 kV Golaghat-Mariani(As) lines. At 12:44 Hrs of 28-04-2024, 132 kV Golaghat – Sarupathar line and 132 kV Golaghat Mariani(As) tripped. Due to tripping of this line, Golaghat area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Golaghat area of Assam Power System by charging 132 kV Golaghat-Mariani(As) Line at 12:55 Hrs of 28.04.2024.	132 kV Golaghat – Sarupathar and 132 kV Golaghat Mariani(As) lines
41	GD1	Gossaigaon area of Assam Power System	28-04-2024 14:59	28-04-2024 15:05	00:06:00	0	11	0.00%	0.52%	1600	2097	Gossaigaon area of Assam Power System was connected with rest of NER Grid via 132 kV Gossaigaon -Dhaligaon line. Gauripur-Gossaigaon line was kept open to avoid overloading of 132 kV Kokrajhar-Bilasipara line. At 14:59 Hrs of 28-04-2024, 132 kV Gossaigaon -Dhaligaon tripped. Due to tripping of this line, Gossaigaon area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Gossaigaon area of Assam Power System by charging 132 kV Gauripur Gossaigaon w.e.f. 15:05 hrs of 28.04.2024.	132 kV Gossaigaon -Dhaligaon line

20.Details of Grid Events during the Month of April 2024 in North-East Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
42	GD1	Leshka HEP of Meghalaya Power System	28-04-2024 22:23	28-04-2024 22:43	00:20:00	42	0	1.99%	0.00%	2108	2041	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C lines. At 22:23 Hrs of 28-04-2024, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these lines, Leshka HEP of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat 2 line at 22:43 hrs of 28.04.2024.	132 kV Myntdu Leshka - Khleihriat D/C lines
43	GD1	Serchhip area of Mizoram Power System	28-04-2024 18:30	28-04-2024 19:08	00:38:00	0	6	0.00%	0.25%	2839	2401	Serchhip area of Mizoram Power System was connected with rest of NER Grid via 132 kV Zuangtui-Serchhip line. 132 kV Serchhip - Lunglei line was kept open due to system requirement. At 18:30 Hrs of 28-04-2024, 132 kV Zuangtui-Serchhip tripped. Due to tripping of this line,Serchhip area of Mizoram Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Serchhip area of Mizoram Power System by charging 132 kV Zuangtui-Serchhip w.e.f. 19:08 hrs of 28.04.2024.	132 kV Zuangtui-Serchhip line
44	GD1	Leshka HEP of Meghalaya Power System	29-04-2024 20:28	29-04-2024 20:51	00:23:00	42	0	1.39%	0.00%	3017	2415	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C lines. At 20:28 Hrs of 29-04-2024, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these lines, Leshka HEP of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat I line at 20:51 hrs of 29.04.2024.	132 kV Myntdu Leshka - Khleihriat D/C lines

21. NEW ELEMENTS COMMISSIONED* IN APRIL 2024

COMMISSIONING OF NEW GENERATING UNITS

REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)	DATE@
NR	1	TRANSITION SUSTAINABLE ENERGY SERVICES PRIVATE LIMITED	Transition Sustainable Energy Services Private Limited(Solar)/Rajasthan	30	-	50	02-04-2024
	2	TRANSITION GREEN ENERGY PRIVATE LIMITED	Transition Green Energy Private Limited(Solar)/Rajasthan	44.44	-	100	02-04-2024
	3	AYANA_RP3PL	Ayana Renewable Power 3 Private Limited(Solar)/Rajasthan	97.16	-	272	19-04-2024
	4	SERENTICA_RI4PL_BIK2	Serentica Renewables India 4 Private Limited(Solar)/Rajasthan	180	-	180	25-04-2024
	5	BANDERWALA_TPSL	Banderwala TPSL(Solar)/Rajasthan	100	-	300	26-04-2024
	6	AMP ENERGY GREEN FIVE PRIVATE LIMITED	AMP Energy Green 5 Private Limited(Solar)/Rajasthan	100	-	100	26-04-2024
WR	7	SJVN GREEN ENERGY LIMITED	SJVN Green Energy Limited(Solar)/Gujarat	75	-	75	01-04-2024
	8	REWA ULTRA MEGA SOLAR LIMITED (RUMSL)	Avaada Reewa Ultra Mega Solar(Solar)/MP	200	-	200	11-04-2024
	9	REWA ULTRA MEGA SOLAR LIMITED (RUMSL)	Beempow Reewa Ultra Mega Solar(Solar)/MP	350	-	350	15-04-2024
	10	ALFANAR NETRA VAYU	Alfanar Netra Vayu(Wind)/Gujarat	45.4	-	206.5	25-04-2024
SR	11	JSW Green Energy	JSW(Wind)/Tamilnadu (Paramium)	51.3	LOT-1	51.3	05-04-2024
	12	JSW Green Energy	JSW(Wind)/Tamilnadu (Savalaperi)	24.3	LOT-4	91.8	10-04-2024
	13	Renew Surya Ojas Private Limited (RSOPL)	RSOPL(Wind)/Karnataka	17.325	LOT-6	311.85	16-04-2024

@RE (Solar & Wind) generation FTC for complete capacity is in phases. Date mentioned is the date by which complete (Added) capacity synch./COD

COMMISSIONING OF NEW ICTs

REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)	DATE
NR	1	AYANA RP3PL	Bikaner PG	400/33/11	I	315	11-04-2024
	2	UPPTCL	Unnao (UP)	400/220/33	II	500	23-04-2024
SR	3	JINDAL / KPTCL	Gowripura_W	400/33	I	316	29-04-2024
	4	JINDAL / KPTCL	Gowripura_W	400/33	II	317	02-04-2024
	5	TSTRANSCO	Kamalapuram	400/220	III	315	02-04-2024
NER	6	AEGCL	Nalbari	132/33	II	50	08-04-2024

COMMISSIONING OF NEW TRANSMISSION LINES

REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE
SR	1	JINDAL / KPTCL	400kV RAJAPURA_S-GOWRIPURA_W-2	2	400	02-04-2024

LILO OF TRANSMISSION LINES

REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE
NR-ER	1	PGCIL	Varanasi(PG)-Biharsharif-I	Sahupuri	400	20-04-2024

COMMISSIONING OF BUS/LINE REACTORS

REGION	S.NO.	ENTITY	SUB-STATION / LINE (@SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE
NR	1	THDC	Bus Reactor-I @Khurja STPP	400	125	24-04-2024
WR	2	KALLAM TL (INDIGRID)	Bus Reactor-I @Kallam PS	400	125	01-04-2024
SR	3	TSTRANSCO	Bus Reactor-I @Narsapur	400	125	25-04-2024
	4	TSTRANSCO	Bus Reactor-I @Suryapet	400	125	10-04-2024
	5	TSTRANSCO	Bus Reactor-I @Dindi	400	125	27-04-2024
NER	6	NEEPCO	Bus Reactor @PLHPS	400	80	15-04-2024

COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM

REGION	S.NO.	ELEMENT NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE

*Includes first time charging (FTC) as well

22.Voltage Profile

विद्युत विभव रूपरेखा माह - अप्रैल 2024 VOLTAGE PROFILE - APRIL 2024

Date of reporting: 05-Apr-24

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	799	754	774
2		दालिपली DARLIPALI	0%	100%	0%	0%	0	792	767	778
3		गया GAYA	0%	100%	0%	0%	0	784	752	766
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	800	740	769
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	803	775	788
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	800	749	774
7		राँची RANCHI	0%	100%	0%	0%	0	794	763	781
8		सासाराम SASARAM	0%	100%	0%	0%	1	805	743	763
1		आगरा AGRA	0%	100%	0%	0%	1	802	760	781
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	789	752	770
3		अजमेर AJMER	0%	99%	1%	1%	4	806	756	784
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	797	758	777
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	780	757	766
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	778	757	764
7		अंता ANTA	0%	100%	0%	0%	0	798	762	779
8		बलिया BALLIA	0%	100%	0%	0%	0	784	742	760
9		बारा BARA	0%	100%	0%	0%	0	784	757	768
10		भाड़ला BHADLA	0%	100%	0%	0%	0	799	735	778
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	0	801	743	779
12		भिवानी BHIWANI	0%	100%	0%	0%	0	804	765	783
13		बीकानेर BIKANER	0%	100%	0%	0%	0	798	747	779
14		बरेली BAREILLY	0%	100%	0%	0%	1	803	749	772
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	6	806	760	784
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	801	717	777
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	794	741	772
18	उत्तरी क्षेत्र NR	ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	0	800	759	780
19		हापुड़ HAPUR	0%	100%	0%	0%	0	793	750	772
20		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	802	748	773
21		झटिकरा JHATIKARA	0%	100%	0%	0%	0	797	753	777
22		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	796	737	773
23		खेतरी KHETRI	0%	100%	0%	0%	0	798	747	779
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	796	753	775
25		ललितपुर LALITPUR	0%	100%	0%	0%	0	774	747	759
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	795	744	767
27		मैनपुरी MAINPURI	0%	100%	0%	0%	0	793	742	767
28		मेरठ MEERUT	0%	100%	0%	0%	0	798	755	779
29		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	795	751	773
30		मोगा MOGA	0%	100%	0%	0%	1	806	751	779
31		ओबरा सी OBRA C	0%	100%	0%	0%	0	776	749	759
32		उरई ORAI	0%	100%	0%	0%	3	806	772	788
33		फागी PHAGI	0%	100%	0%	0%	1	804	759	782
34		रामपुर RAMPUR	0%	100%	0%	0%	1	805	746	773
35		उन्नाव UNNAO	0%	100%	0%	0%	0	792	738	758
36		वाराणसी VARANASI	0%	100%	0%	0%	0	793	760	774
1		अकोला AKOLA	0%	100%	0%	0%	0	792	751	771
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	2	805	756	781
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	789	751	770
4		भुज BHUJ	0%	100%	0%	0%	0	793	750	778
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	785	750	772
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	782	758	770
7		बीना BINA	0%	100%	0%	0%	0	798	772	784
8		बनसकेंठा BANASKANTHA	0%	100%	0%	0%	0	800	760	785
9		चांपा CHAMPA	0%	99%	1%	1%	9	804	774	790
10		धूले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	797	744	776
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	784	761	771
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	793	766	782
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	791	744	770
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	799	767	784
15		ग्वालियर GWALIOR	0%	100%	0%	0%	1	804	746	784
16		इंदौर INDORE	0%	100%	0%	0%	0	791	746	772
17		जबलपुर JABALPUR	0%	100%	0%	0%	0	802	776	788
18	पश्चिमी क्षेत्र WR	खंडवा KHANDWA	0%	100%	0%	0%	0	792	749	773
19		कोरडी KORADI	0%	100%	0%	0%	0	780	749	764
20		लकाडिया LAKADIYA	0%	100%	0%	0%	3	804	757	785
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	796	773	785
22		पड़घे PADGHE	0%	100%	0%	0%	1	806	743	774
23		परली PARLI	0%	99%	1%	1%	6	808	760	784
24		पुणे PUNE	0%	100%	0%	0%	1	805	744	774
25		राजनन्दगाँव RAJNANDGAON	0%	100%	0%	0%	1	803	770	787
26		सासन SASAN	0%	100%	0%	0%	0	787	769	778
27		सतना SATNA	0%	100%	0%	0%	0	799	774	785
28		सिवनी SEONI	0%	100%	0%	0%	0	793	761	777
29		सीपत SIPAT	0%	100%	0%	0%	0	783	760	771
30		सोलापुर SOLAPUR	0%	99%	1%	1%	8	807	738	785
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	775	753	763
32		तामनार TAMNAR	0%	100%	0%	0%	0	796	773	784
33		वड़ादरा VADODARA	0%	98%	2%	2%	12	804	746	782
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	791	772	780
35		वर्धा WARDHA	0%	100%	0%	0%	0	803	763	783
36		वरोरा WARORA	0%	100%	0%	0%	0	801	757	779
1		अरियलूर ARIYALUR	0%	100%	0%	0%	0	801	744	773
2		कड़पा CUDDAPAH	0%	98%	2%	2%	16	810	760	785
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	99%	1%	1%	7	812	763	785
4		कनूल KURNOOL	0%	100%	0%	0%	2	808	754	779
5		महेश्वरम MAHESWARAM	0%	98%	2%	2%	12	815	761	785
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	96%	4%	4%	29	817	761	788
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	805	755	774
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	1	806	730	769
9		रायचूर RAICHUR	0%	100%	0%	0%	0	805	755	778
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	2	810	756	782
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	796	745	773
12		वेमागिरी VEMAGIRI	0%	99%	1%	1%	10	813	757	785
13		वारंगल WARANGAL	0%	99%	1%	1%	7	811	759	784
1		बिस्वनाथ चरिआलि BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	419	392	405
2		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	414	396	407
3		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	415	398	408
4		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	420	359	405
5		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	420	401	410
6		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	416	391	403
7		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	412	399	407
8	पूर्वोत्तर क्षेत्र NER	मीसा MISA (400 kV)	0%	100%	0%	0%	0	414	392	404
9		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	417	394	405
10		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	420	393	407
11		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	418	399	407
12		पूर्वेकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	418	361	403
13		रंगानदी RANGANADI (400 kV)	0%	100%	0%	0%	1	424	388	409
14		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	419	398	408
15		सूर्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	418	361	402
16		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	415	384	401

All listed stations are 765 kV stations unless otherwise mentioned

***Percentage is calculated w.r.t. Time of one month.**

23.ALL TIME HIGHEST

30-04-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	81220 04-09-2023	76274 04-09-2023	1796 04-09-2023	443 01-08-2023	86 07-08-2023	184 30-04-2024
WR	74799 29-01-2024	66793 29-04-2024	1635 30-04-2024	167 18-12-2014	273 07-08-2023	102.85 30-04-2024
SR	68735 13-03-2024	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	298 21-07-2023	148.7 31-03-2024
ER	31895 30-04-2024	28982 19-04-2024	667 30-04-2024	157 14-09-2022	-	7 23-03-2023
NER	3712 04-09-2023	3510 12-08-2022	72 15-09-2023	41 29-08-2023	-	2 22-06-2022
All India	239978 01-09-2023	215592 28-08-2023	5224 02-09-2023	877 30-08-2022	611 02-08-2023	426 30-04-2024

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15237	23-06-2023	343.5	24-06-2023
	Haryana	12692	18-08-2023	273.1	18-08-2023
	Rajasthan	17949	20-01-2024	371.6	04-09-2023
	Delhi	7770	29-06-2022	153.5	28-06-2022
	UP	28553	25-07-2023	580.0	03-09-2023
	Uttarakhand	2594	14-06-2022	55.8	17-06-2023
	HP	2235	20-01-2024	40.7	22-08-2023
	J&K(UT) and Ladakh(UT)	3636	29-06-2023	66.8	26-01-2024
	Chandigarh	426	08-07-2021	8.4	08-07-2021
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	24544	01-09-2023	511.6	02-09-2023
	MP	17819	29-12-2023	335.9	10-11-2023
	Maharashtra	28969	07-02-2024	648.3	30-04-2024
	Goa	803	19-04-2024	17.3	30-04-2024
	DD & DNH	1327	17-08-2023	30.9	10-08-2023
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13418	30-04-2024	263.8	16-06-2023
	Telangana*	15623	08-03-2024	311.0	13-03-2024
	Karnataka	17220	12-03-2024	336.9	05-04-2024
	Kerala	5646	29-04-2024	113.3	30-04-2024
	Tamil Nadu	20701	30-04-2024	443.6	30-04-2024
	Pondy	517	29-04-2024	11.6	18-05-2023
ER	Bihar	7578	27-07-2023	161.3	28-07-2023
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	2187	30-04-2024	47.3	30-04-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	189	17-03-2024	3.4	25-03-2024
	Assam	2498	16-09-2023	50.0	15-09-2023
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	179	28-09-2023	3.29	05-09-2023
	Tripura	370	07-06-2023	7.0	06-06-2023
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24.System Reliability Indices Report for the month of APRIL 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	2	0.50	0.07

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पॉवर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
