ग्रिड-इंडिया
GRID-INDIA

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या : - **GRID-INDIA/NLDC/MR/** दिनांक : 25.09.2024

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **अगस्त 2024**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **अगस्त 2024** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
वरिष्ठ महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



अगस्त 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह अगस्त 2024 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF AUGUST -2024


पृष्ठसूची CONTENTS

1	माह अगस्त 2024 की सारांश रिपोर्ट Summary of report for the month of AUGUST 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	16 अगस्त के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 16-AUGUST (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अगस्त 2023 से तुलना Energy requirement and met comparison with AUGUST 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अगस्त 2023 से तुलना Peak demand requirement and met comparison with AUGUST 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-37
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	38-40
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	41
18	पावर मार्केट की सूचना Power market information	42-46
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	47-49
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	50-66
21	नए कमीशंड पारेषण तत्व New elements commissioned	67
22	विभव रूपरेखा Voltage profile	68
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह अगस्त 2024 तक All Time Highest (Demand & Energy) figures: Till AUGUST 2024	69
24	अगस्त 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for AUGUST 2024	70

1. SUMMARY OF REPORT FOR THE MONTH OF AUGUST-2024


EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

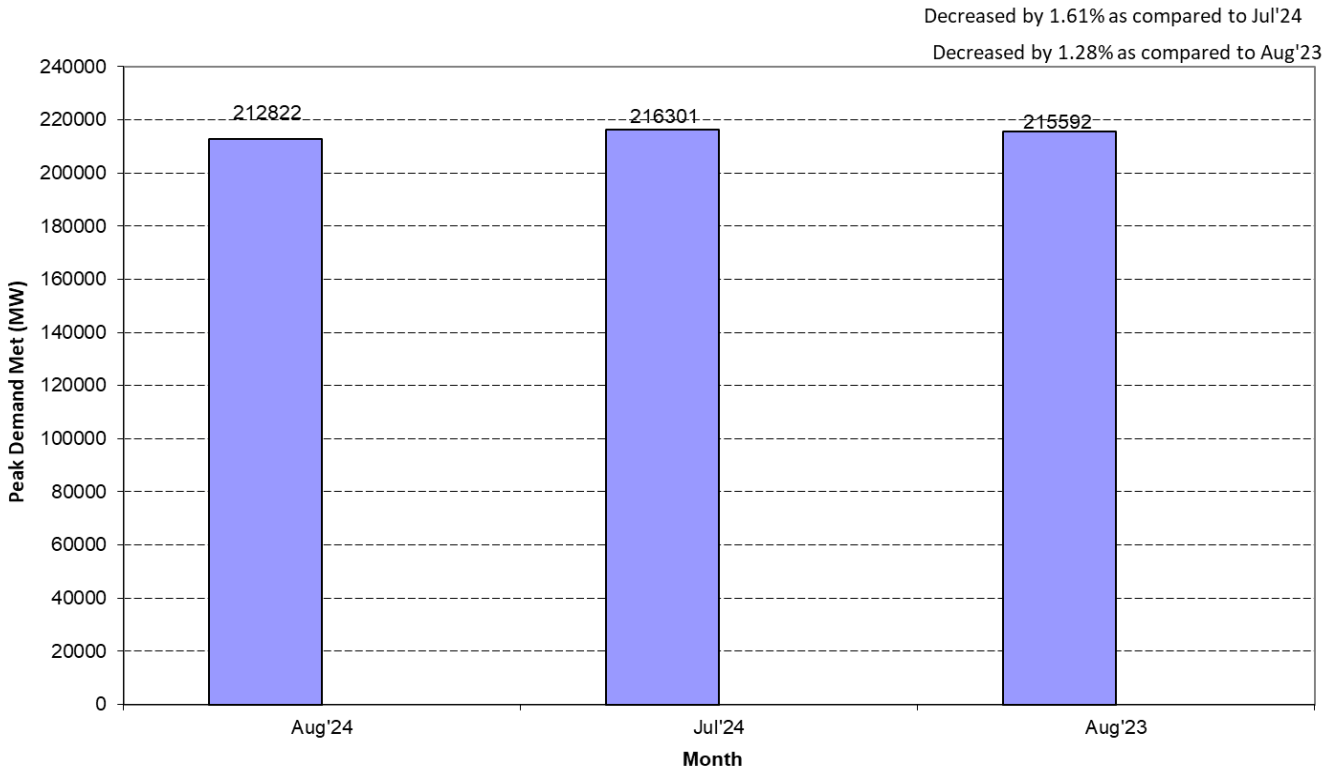


Frequency within IEGC Band

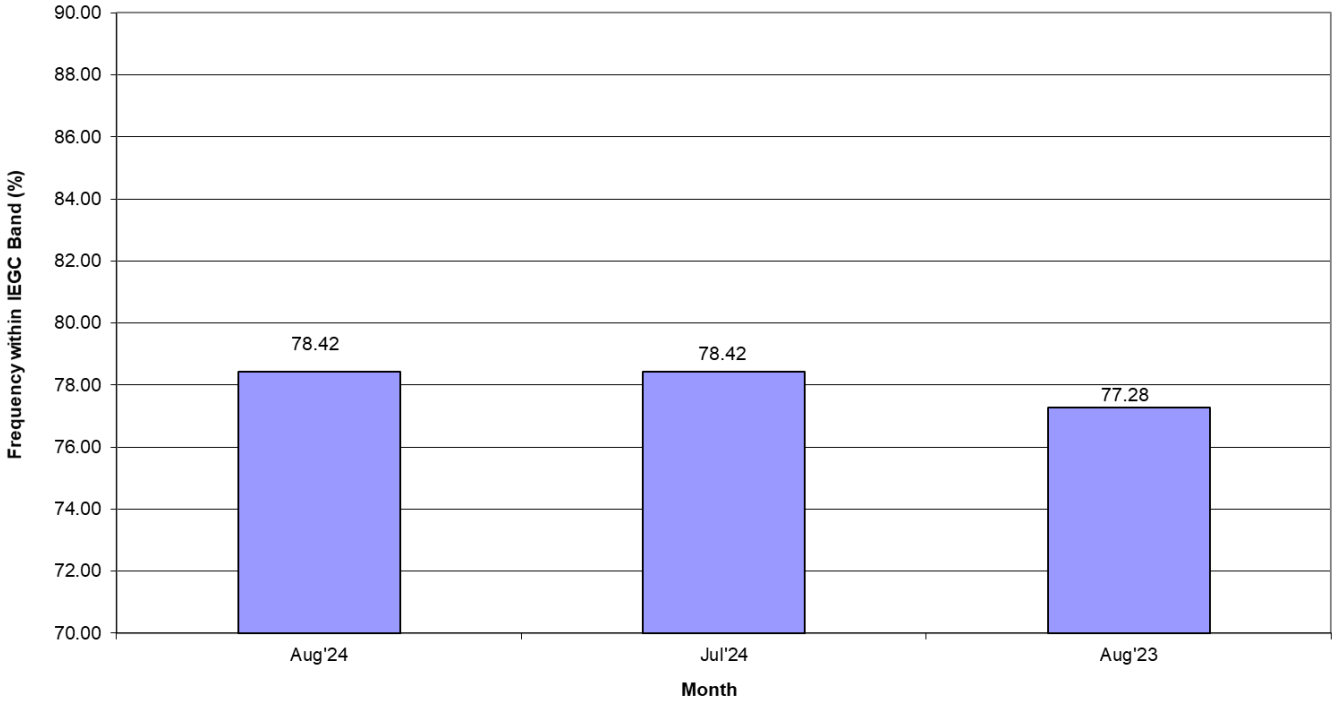

ENERGY MET AT NATIONAL LEVEL (MU)

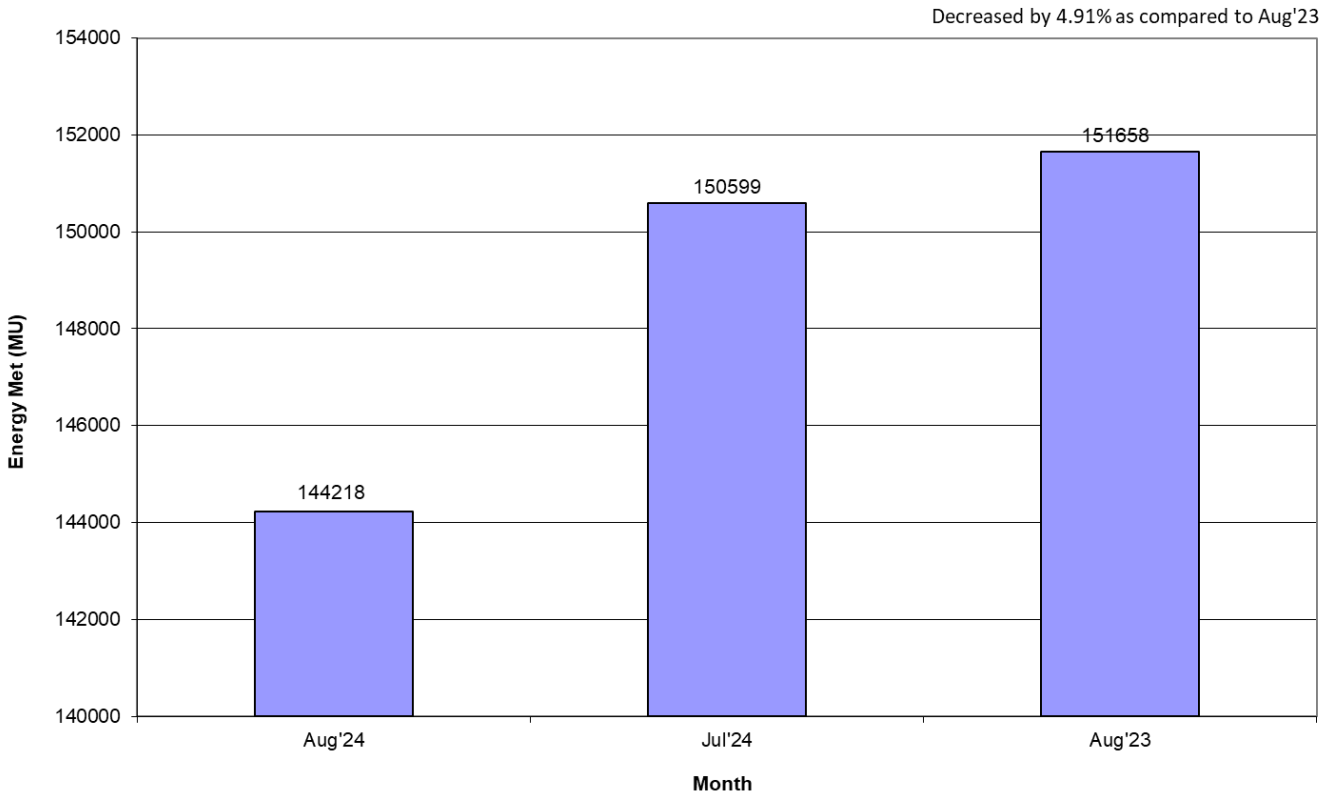


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

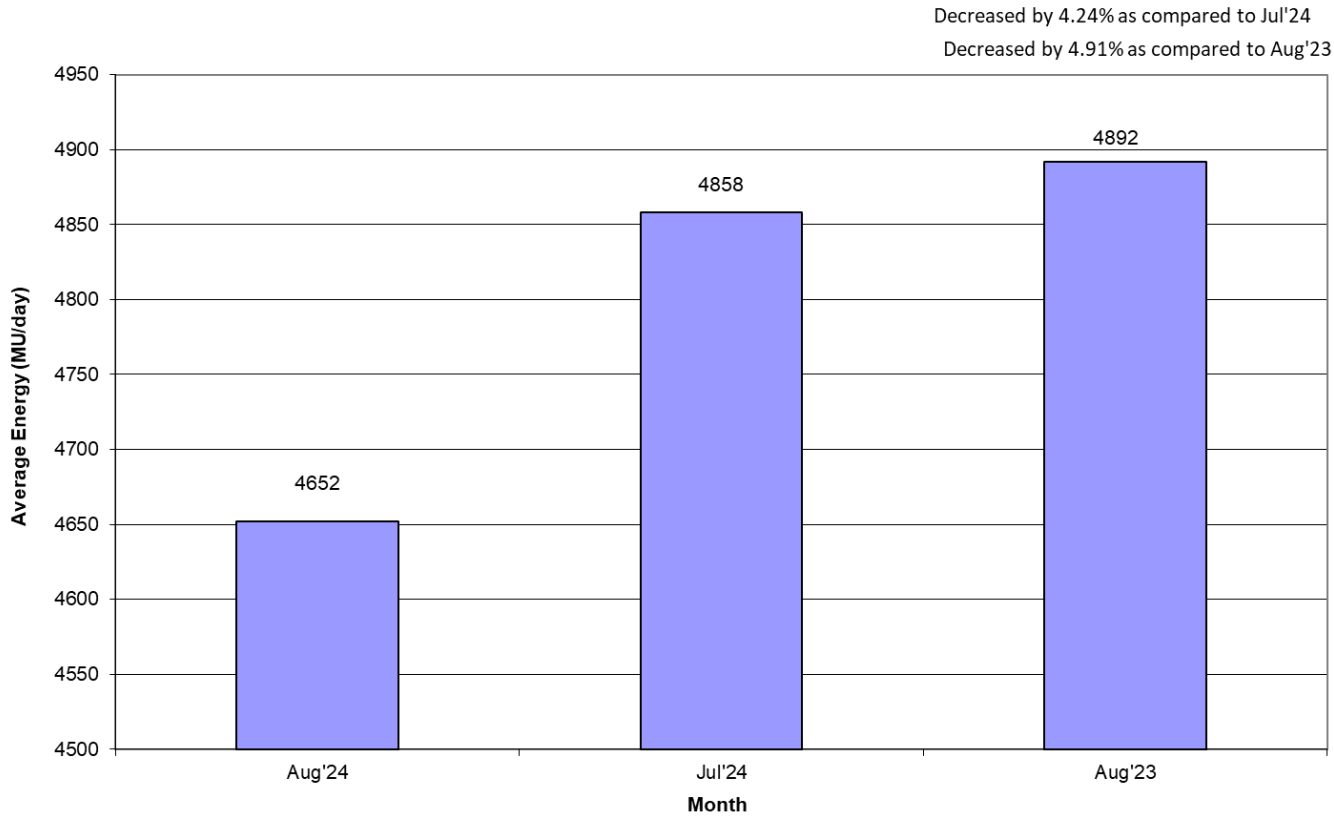

HYDRO GENERATION AT NATIONAL LEVEL (MU)


Decreased by 1.73% as compared to Aug'23

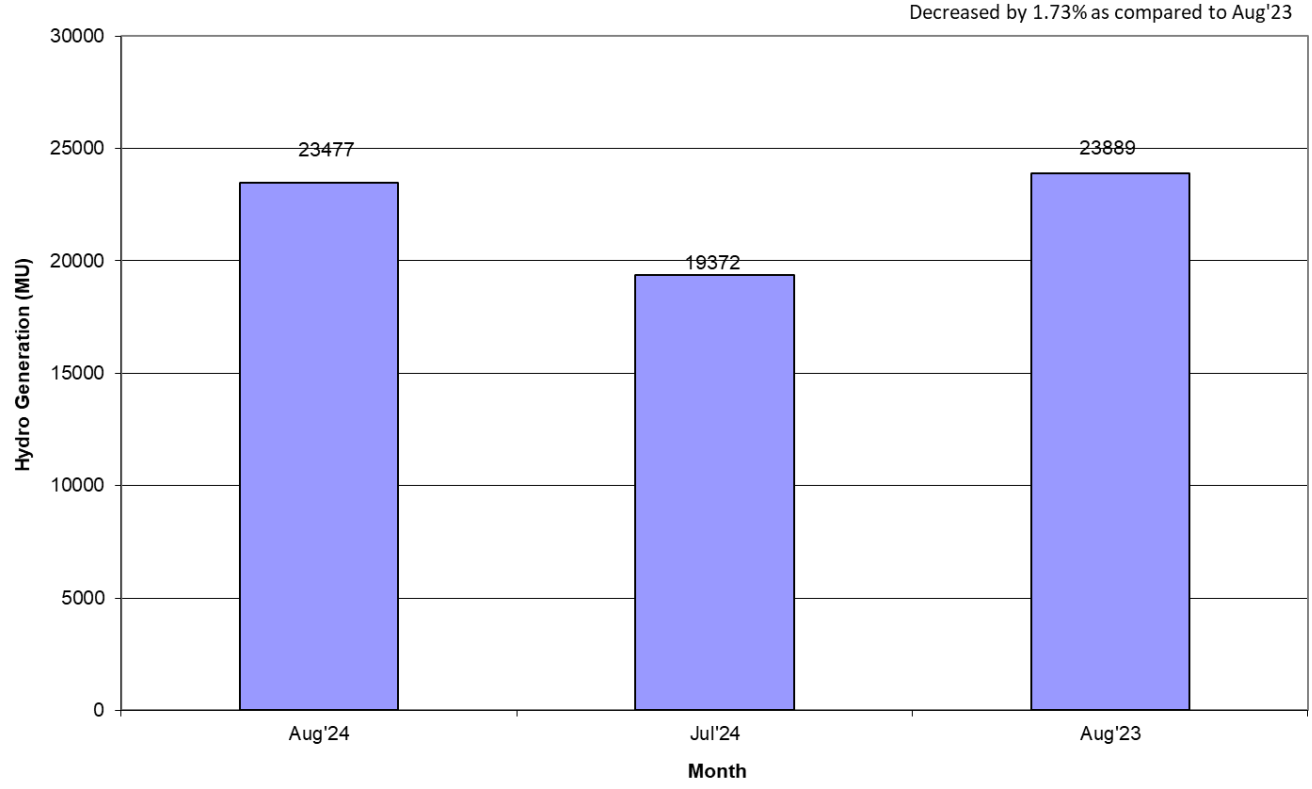

AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)


Increased by 21.19% as compared to Jul'24

Decreased by 1.73% as compared to Aug'23

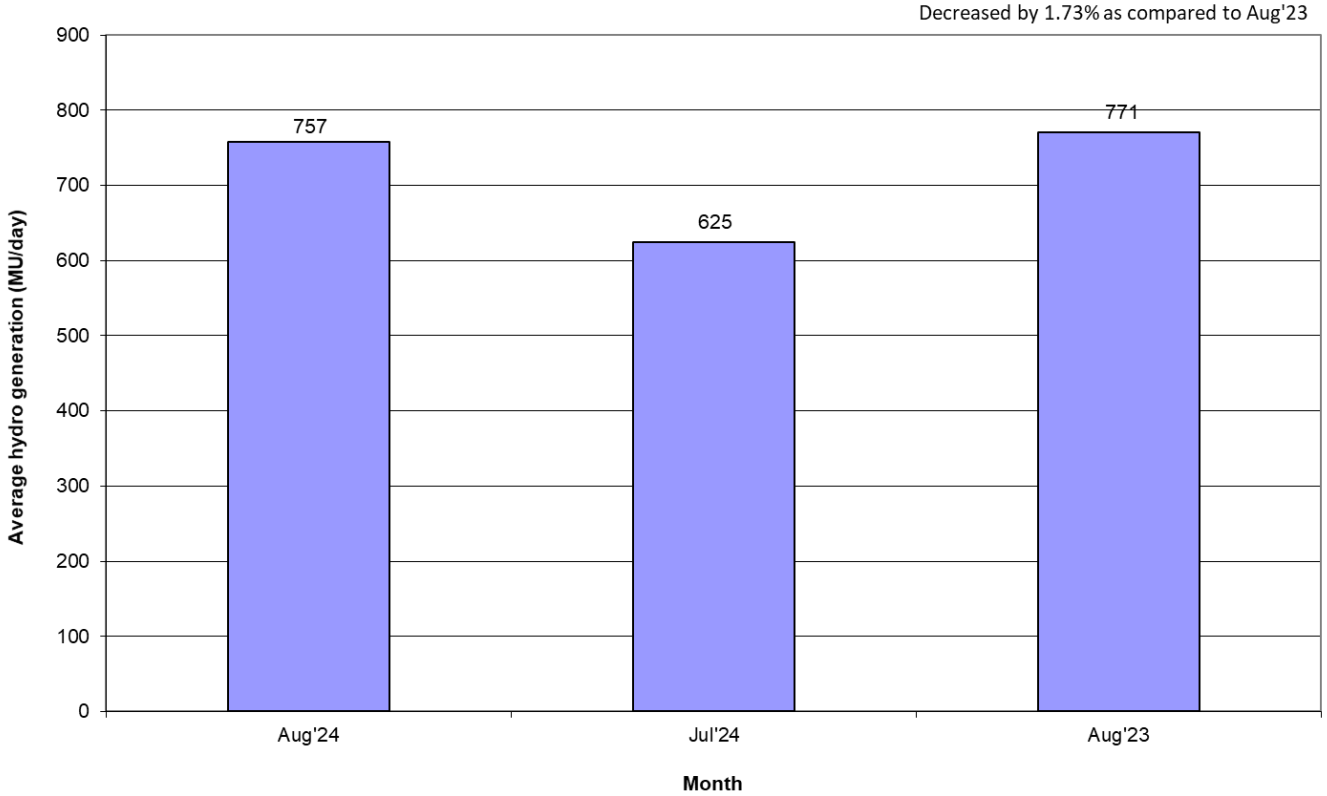

WIND GENERATION AT NATIONAL LEVEL (MU)


Decreased by 20.76% as compared to Aug'23

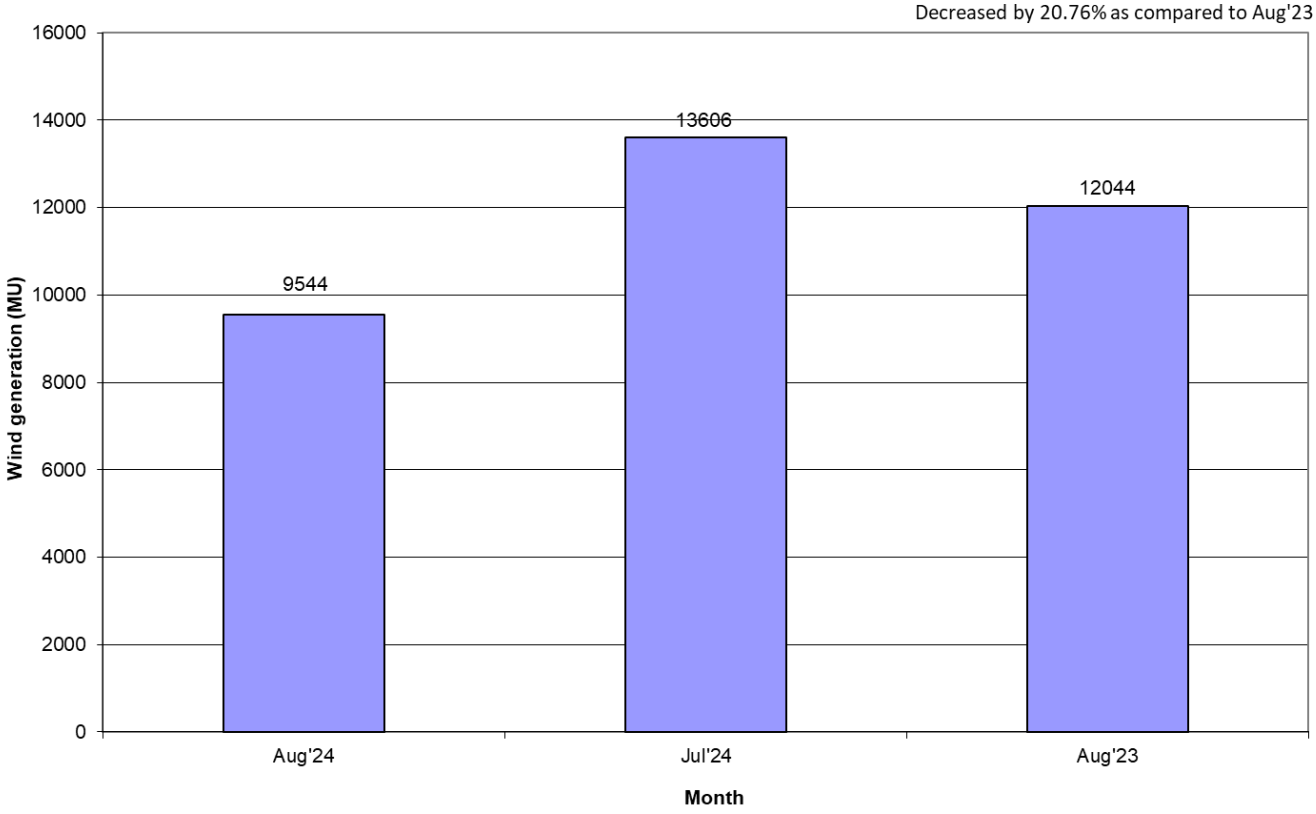


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

Decreased by 29.86% as compared to Jul'24


Decreased by 20.76% as compared to Aug'23

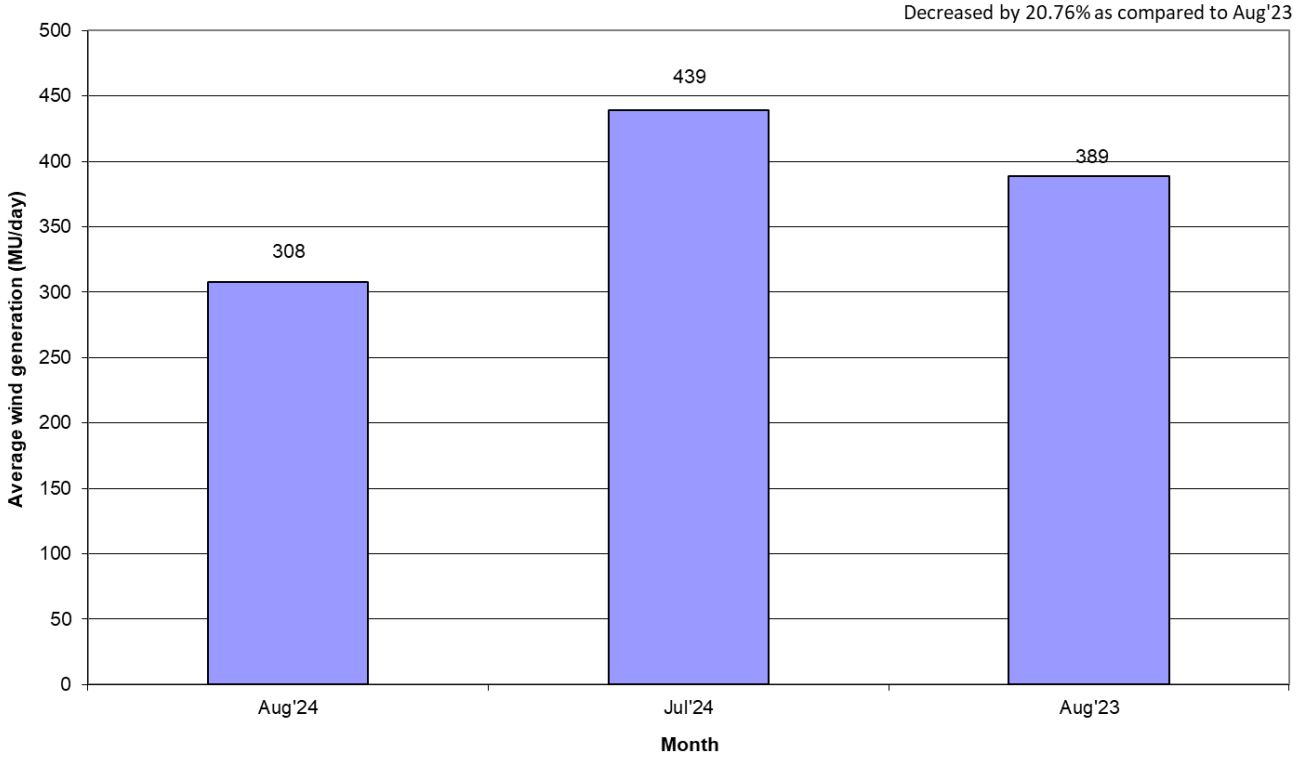

SOLAR GENERATION AT NATIONAL LEVEL (MU)

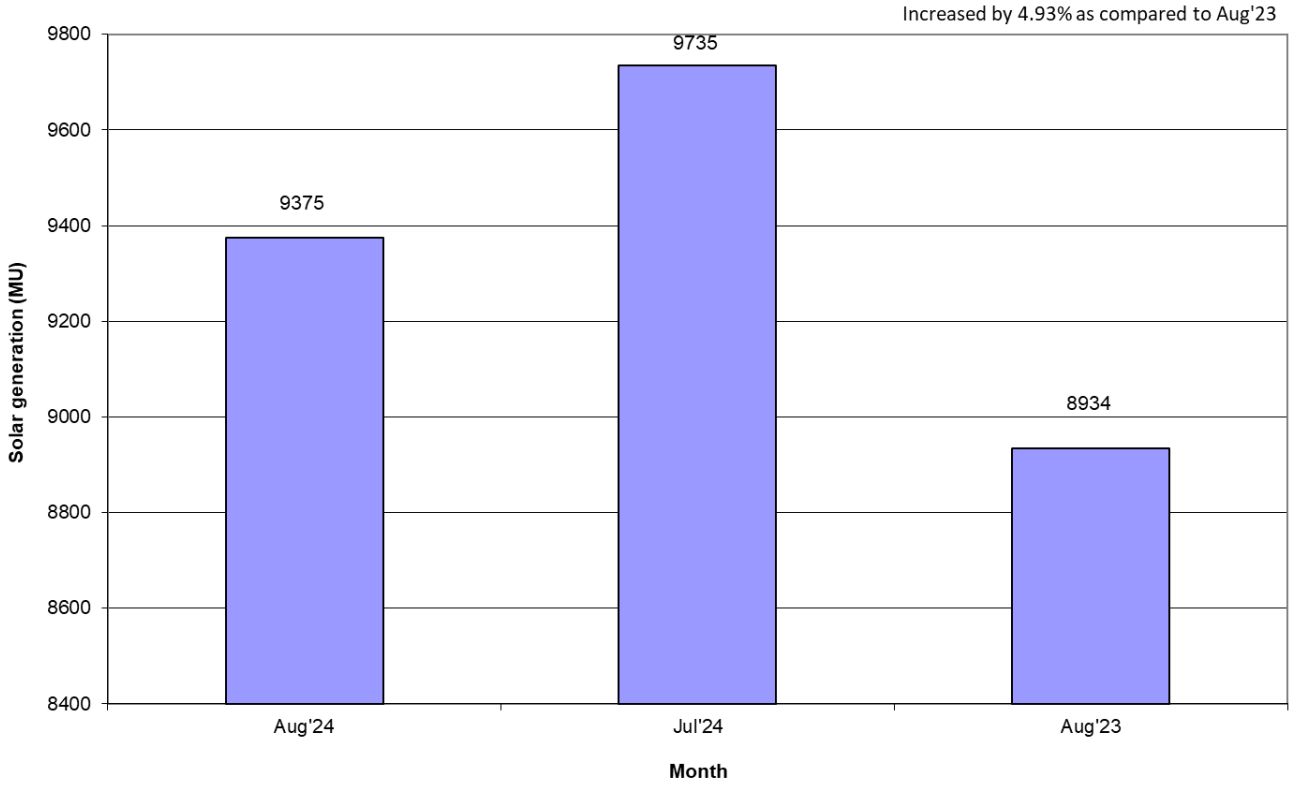

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

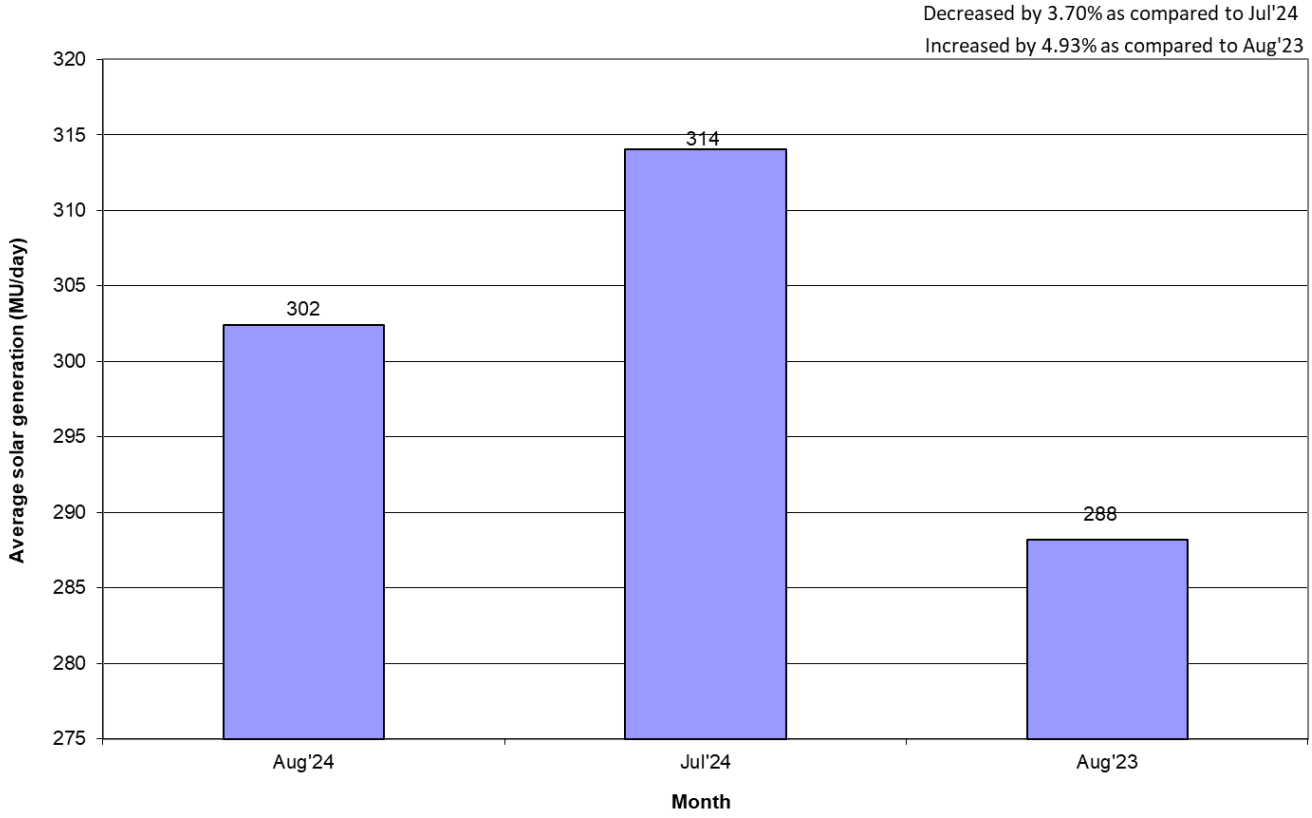

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.08.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56658	1580	5995	0	64233	1620	20830	42220	128903
2	WR	74663	1400	10806	0	86869	3240	7563	51680	149351
3	SR	49415	3640	6272	434	59760	3320	11827	56061	130969
4	ER	28992	0	80	0	29072	0	4764	2044	35880
5	NER	1242	0	1665	36	2943	0	1944	610	5497
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	210970	6620	24818	589	242997	8180	46928	152654	450760

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति

EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: अगस्त 2024 MONTH:- AUG 2024


सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Aug-24	74496	55044	47382	23905	3327	204154
2-Aug-24	74054	54430	47400	21798	3268	200950
3-Aug-24	72146	52949	46451	24005	3231	198782
4-Aug-24	69528	50178	43226	25934	3353	192219
5-Aug-24	73323	55106	48054	26817	3340	206640
6-Aug-24	73848	55504	45422	26146	3462	204382
7-Aug-24	70592	55678	45733	26861	3487	202351
8-Aug-24	71844	56363	45805	26773	3368	204153
9-Aug-24	70739	55430	47183	26150	3387	202889
10-Aug-24	70229	55725	48008	26157	3365	203484
11-Aug-24	60245	54849	43718	26419	3203	188434
12-Aug-24	65798	57610	48443	27637	3375	202863
13-Aug-24	70626	59256	48113	26427	3536	207958
14-Aug-24	68817	59337	48311	26925	3676	207066
15-Aug-24	68825	54376	43691	26828	2932	196652
16-Aug-24	72189	59105	47444	27411	3554	209703
17-Aug-24	72911	59492	47674	27343	3484	210904
18-Aug-24	71317	57511	44716	26391	3242	203177
19-Aug-24	66515	53431	46287	26806	3150	196189
20-Aug-24	70441	59322	48265	27403	2984	208415
21-Aug-24	73252	61252	47344	27714	3260	212822
22-Aug-24	73201	59565	47540	27055	3404	210765
23-Aug-24	72515	58001	47795	26022	3572	207905
24-Aug-24	74107	53857	45545	25797	3494	202800
25-Aug-24	72758	49972	42404	25641	3282	194057
26-Aug-24	68674	48603	47974	25820	3515	194586
27-Aug-24	67429	51611	48544	25985	3622	197191
28-Aug-24	70865	54142	48861	26878	3623	204369
29-Aug-24	66957	54811	47327	27757	3710	200562
30-Aug-24	72213	56675	45435	28278	3688	206289
31-Aug-24	73978	58317	43898	28116	3436	207745
उच्चतम MAXIMUM	74496	61252	48861	28278	3710	212822
निम्नतम MINIMUM	60245	48603	42404	21798	2932	188434
औसत AVERAGE	70788	55726	46580	26426	3398	202918
अब तक का उच्चतम All Time Max.	82312	67482	54798	29695	**3710**	227354
दिनांक Date	23.07.24	30.05.24	29.04.24	29.05.24	**29.08.24**	29.05.24

नोट : सभी आंकड़े 2000 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND(at 2000hrs)MET DURING THE MONTH OF AUGUST 2024

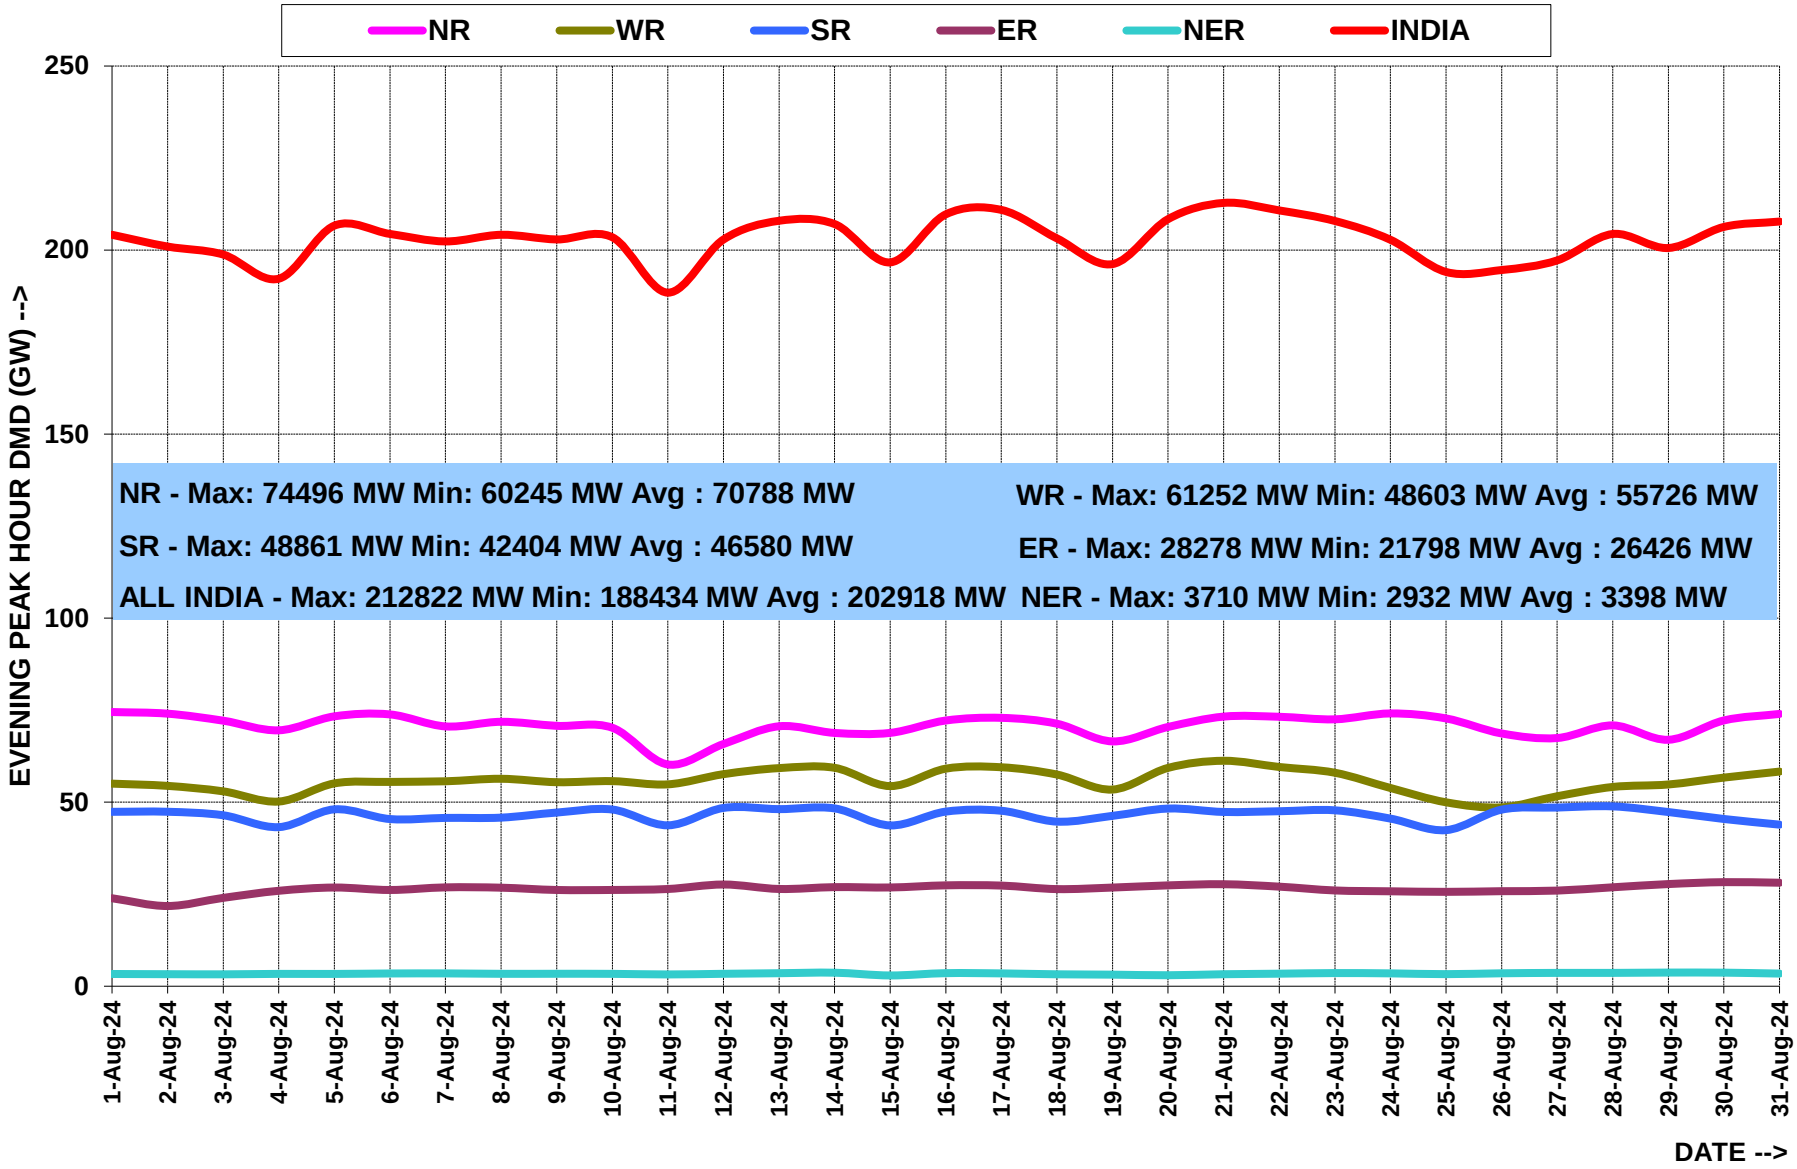


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: अगस्त 2024 MONTH:- AUG 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-24	1579	1278	1177	560	68	4662
02-Aug-24	1632	1262	1171	461	63	4589
03-Aug-24	1602	1228	1160	469	64	4523
04-Aug-24	1541	1167	1118	534	64	4424
05-Aug-24	1623	1231	1179	576	65	4673
06-Aug-24	1696	1276	1153	561	64	4751
07-Aug-24	1624	1279	1081	565	67	4616
08-Aug-24	1612	1011	1087	580	65	4354
09-Aug-24	1632	1312	1135	579	66	4723
10-Aug-24	1613	1304	1131	581	67	4694
11-Aug-24	1432	1280	1087	558	64	4421
12-Aug-24	1467	1329	1161	587	65	4609
13-Aug-24	1546	1368	1194	600	67	4776
14-Aug-24	1606	1393	1204	595	74	4874
15-Aug-24	1529	1295	1130	589	64	4607
16-Aug-24	1584	1363	1192	600	67	4806
17-Aug-24	1618	1403	1153	618	70	4862
18-Aug-24	1572	1375	1111	575	64	4697
19-Aug-24	1555	1318	1157	590	62	4682
20-Aug-24	1537	1376	1120	588	55	4677
21-Aug-24	1612	1423	1134	602	60	4831
22-Aug-24	1661	1427	1122	596	66	4871
23-Aug-24	1636	1405	1150	552	69	4812
24-Aug-24	1639	1307	1133	568	69	4716
25-Aug-24	1601	1198	1055	548	67	4470
26-Aug-24	1639	1160	1155	553	68	4575
27-Aug-24	1512	1157	1216	544	71	4499
28-Aug-24	1490	1221	1221	579	70	4581
29-Aug-24	1418	1249	1204	599	73	4543
30-Aug-24	1526	1280	1138	620	73	4637
31-Aug-24	1618	1316	1043	622	65	4664
कुल TOTAL	48951	39991	35472	17749	2054	144218
उच्चतम MAXIMUM	1696	1427	1221	622	74	4874
निम्नतम MINIMUM	1418	1011	1043	461	55	4354
औसत AVERAGE	1579	1290	1144	573	66	4652
संचयी 2024-25 Cumulative 2024-25	246077	221794	177908	92697	9313	747789
अब तक का उच्चतम All Time Max.	1990	1648	1416	692	76	5466
दिनांक Date	18.06.24	06.05.24	05.04.24	10.06.24	27.07.24	30.05.24

ENERGY MET DURING THE MONTH OF AUGUST' 2024

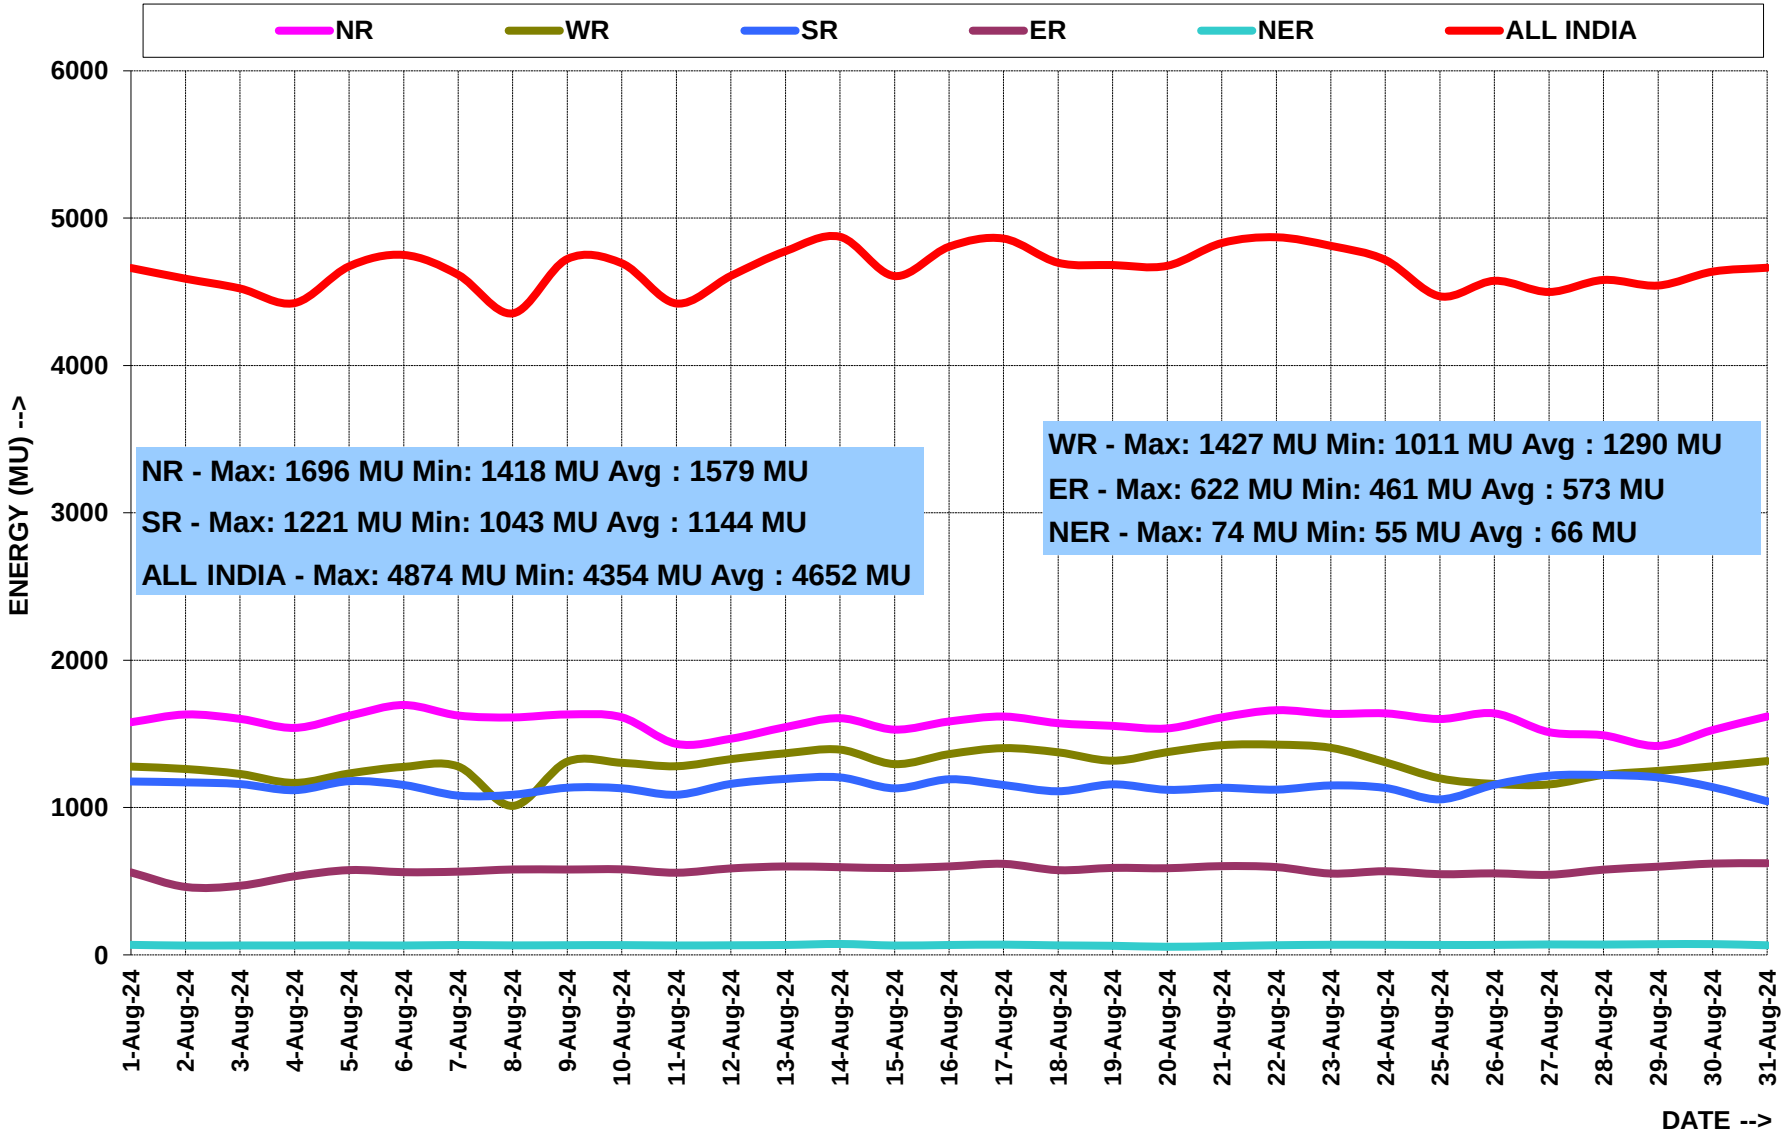

5. वर्ष 2024-25 के लिए आवृति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	2024-25 (upto Aug)	All India Grid	4.66	78.24	17.11		50.67	49.55	50.00

5.1 अगस्त 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR AUGUST 2024

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Aug-24	2.21	76.46	21.33		50.21	49.83	50.01	0.02
	02-Aug-24	1.89	79.33	18.78		50.20	49.84	50.01	0.03
	03-Aug-24	2.84	66.25	30.91		50.40	49.80	50.03	0.07
	04-Aug-24	4.43	69.29	26.27		50.39	49.71	50.03	0.14
	05-Aug-24	7.13	70.37	22.50		50.18	49.75	50.00	0.04
	06-Aug-24	5.93	75.30	18.77		50.16	49.68	50.00	0.03
	07-Aug-24	5.97	71.28	22.74		50.22	49.80	50.01	0.04
	08-Aug-24	4.00	81.24	14.76		50.27	49.74	50.00	0.03
	09-Aug-24	3.43	77.72	18.85		50.20	49.74	50.01	0.03
	10-Aug-24	4.07	74.75	21.18		50.16	49.74	50.00	0.03
	11-Aug-24	1.82	64.86	33.32		50.33	49.85	50.04	0.09
	12-Aug-24	8.60	79.79	11.61		50.14	49.65	49.99	0.04
	13-Aug-24	21.48	68.90	9.62		50.13	49.56	49.95	0.11
	14-Aug-24	6.91	83.67	9.42		50.13	49.57	49.98	0.05
	15-Aug-24	6.47	71.06	22.47		50.16	49.79	50.01	0.03
	16-Aug-24	3.33	76.26	20.41		50.13	49.83	50.01	0.02
	17-Aug-24	2.73	80.10	17.16		50.24	49.77	50.01	0.03
	18-Aug-24	3.14	78.95	17.92		50.28	49.82	50.01	0.04
	19-Aug-24	5.67	76.33	18.00		50.24	49.81	50.00	0.03
	20-Aug-24	2.72	74.25	23.03		50.20	49.77	50.01	0.03
	21-Aug-24	3.04	78.59	18.37		50.22	49.82	50.01	0.03
	22-Aug-24	5.06	78.60	16.34		50.20	49.79	50.00	0.03
	23-Aug-24	0.29	64.48	35.23		50.32	49.88	50.04	0.04
	24-Aug-24	1.83	82.78	15.39		50.23	49.85	50.00	0.03
	25-Aug-24	1.16	60.87	37.97		50.38	49.87	50.07	0.16
	26-Aug-24	6.53	69.55	23.92		50.27	49.60	50.00	0.05
	27-Aug-24	1.20	78.11	20.68		50.45	49.84	50.02	0.05
	28-Aug-24	3.18	79.22	17.59		50.27	49.79	50.01	0.04
	29-Aug-24	4.57	75.39	20.03		50.30	49.77	50.01	0.05
	30-Aug-24	6.50	78.91	14.58		50.25	49.81	50.00	0.04
	31-Aug-24	6.33	82.71	10.96		50.11	49.63	49.98	0.03


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: अगस्त 2024 MONTH:- AUG 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-24	329	50	167	74	31	651
02-Aug-24	359	64	176	69	28	696
03-Aug-24	372	75	179	78	31	735
04-Aug-24	367	72	172	86	32	729
05-Aug-24	385	86	180	84	33	768
06-Aug-24	381	91	176	81	39	768
07-Aug-24	375	98	181	71	38	763
08-Aug-24	381	89	178	86	36	769
09-Aug-24	387	90	174	86	34	772
10-Aug-24	380	104	174	88	34	781
11-Aug-24	296	101	174	84	35	689
12-Aug-24	365	113	180	84	38	781
13-Aug-24	393	122	179	89	34	818
14-Aug-24	383	128	167	90	34	802
15-Aug-24	376	108	166	86	32	768
16-Aug-24	382	115	172	88	33	789
17-Aug-24	374	120	169	90	32	785
18-Aug-24	376	109	163	90	31	770
19-Aug-24	384	106	150	85	31	757
20-Aug-24	372	109	145	91	33	750
21-Aug-24	373	114	143	93	34	756
22-Aug-24	375	114	154	85	34	764
23-Aug-24	361	102	157	92	35	747
24-Aug-24	367	104	151	88	35	746
25-Aug-24	367	99	154	86	33	739
26-Aug-24	367	110	165	90	32	764
27-Aug-24	376	112	172	80	32	772
28-Aug-24	373	114	169	79	31	767
29-Aug-24	368	118	165	79	32	762
30-Aug-24	374	119	162	80	31	766
31-Aug-24	371	116	159	82	29	757
कुल TOTAL	11491	3173	5173	2612	1029	23477
उच्चतम MAXIMUM	393	128	181	93	39	818
निम्नतम MINIMUM	296	50	143	69	28	651
औसत AVERAGE	371	102	167	84	33	757
संचयी 2024-25 Cumulative 2024-25	46944	8463	12653	7827	4074	79961
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

HYDRO ENERGY DURING THE MONTH OF AUGUST' 2024

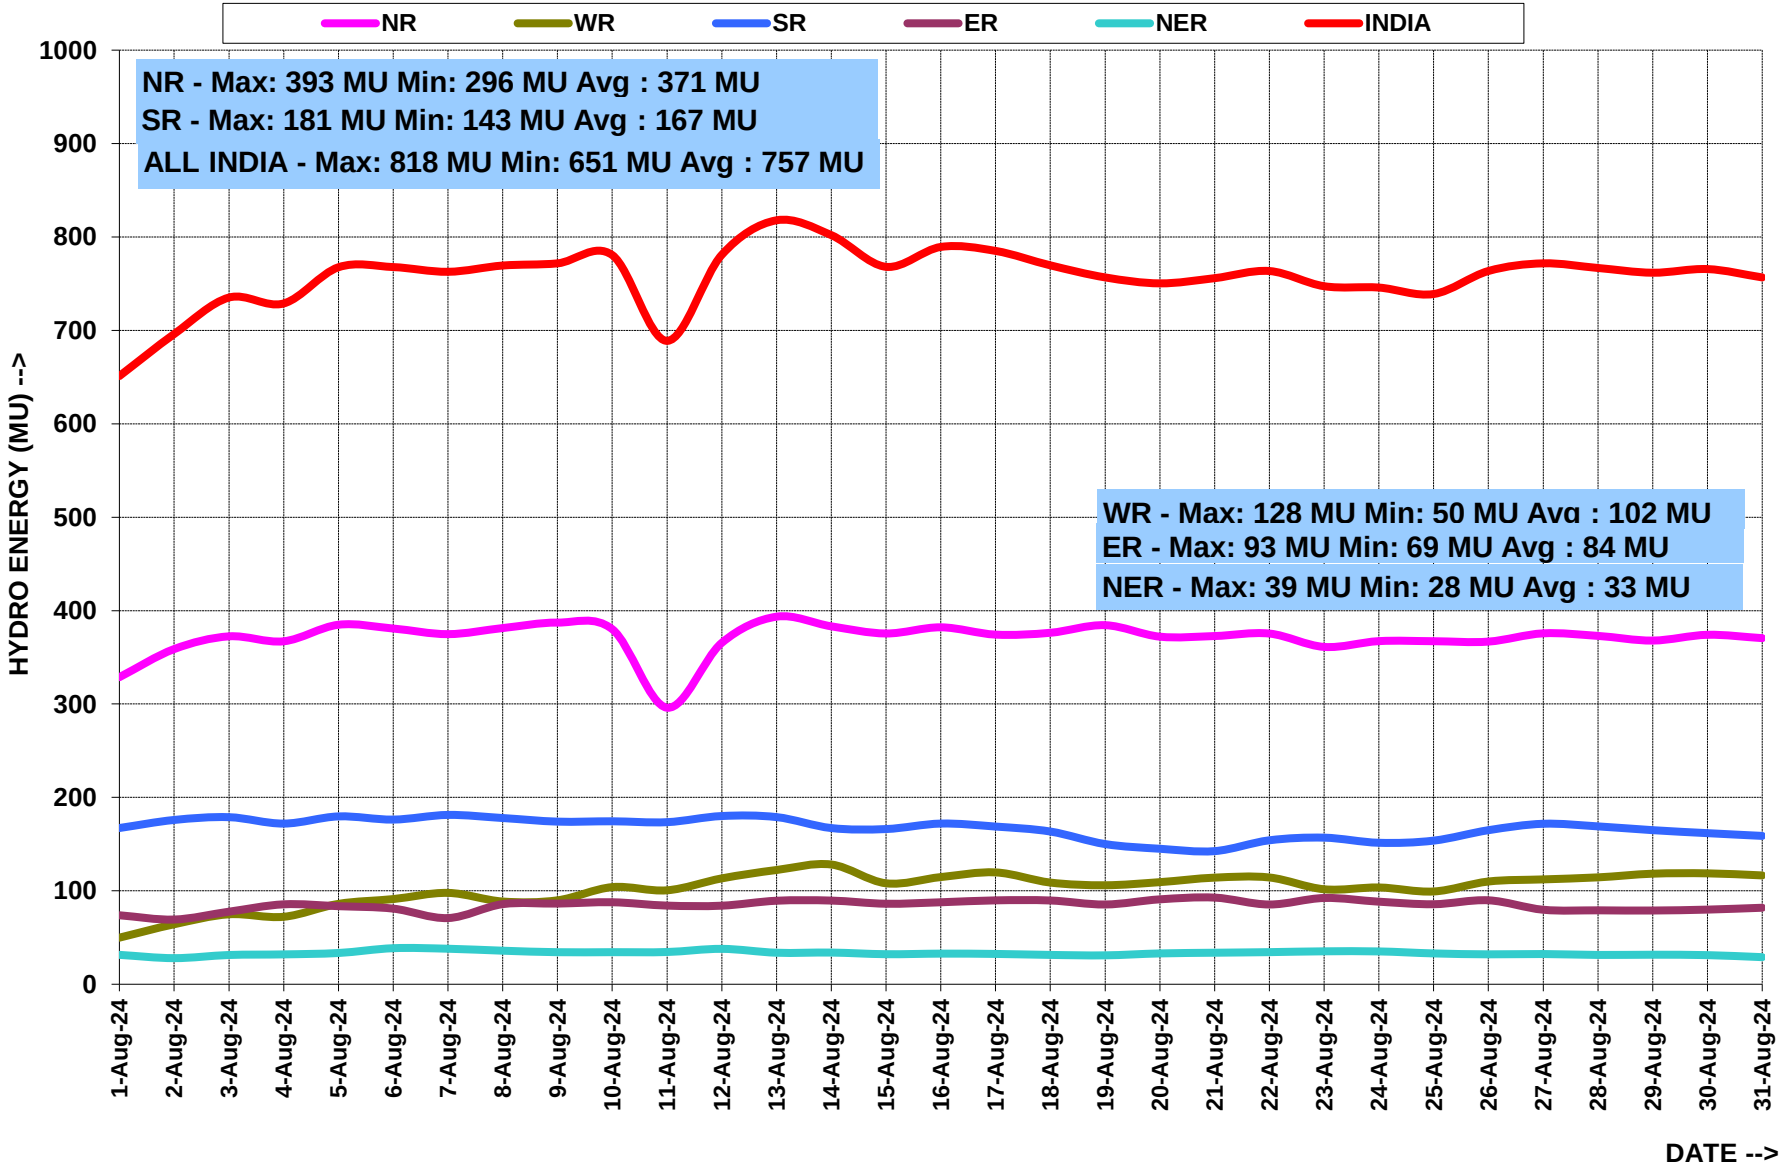

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन

WIND GENERATION AT NATIONAL LEVEL

माह: अगस्त 2024 MONTH:- AUG 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-24	50	222	249	----------	----------	521
02-Aug-24	28	262	262	----------	----------	552
03-Aug-24	14	250	215	----------	----------	479
04-Aug-24	17	230	180	----------	----------	427
05-Aug-24	29	184	107	----------	----------	320
06-Aug-24	52	196	124	----------	----------	372
07-Aug-24	60	210	101	----------	----------	371
08-Aug-24	32	175	124	----------	----------	330
09-Aug-24	25	151	112	----------	----------	288
10-Aug-24	39	190	99	----------	----------	328
11-Aug-24	44	201	81	----------	----------	326
12-Aug-24	15	152	41	----------	----------	207
13-Aug-24	12	74	31	----------	----------	117
14-Aug-24	14	70	38	----------	----------	122
15-Aug-24	23	89	29	----------	----------	141
16-Aug-24	23	90	38	----------	----------	151
17-Aug-24	28	72	83	----------	----------	182
18-Aug-24	23	54	47	----------	----------	124
19-Aug-24	17	45	50	----------	----------	112
20-Aug-24	25	53	38	----------	----------	116
21-Aug-24	16	38	73	----------	----------	127
22-Aug-24	8	43	113	----------	----------	164
23-Aug-24	9	86	122	----------	----------	217
24-Aug-24	9	145	222	----------	----------	376
25-Aug-24	16	256	248	----------	----------	521
26-Aug-24	41	268	244	----------	----------	553
27-Aug-24	65	221	216	----------	----------	501
28-Aug-24	45	205	208	----------	----------	459
29-Aug-24	41	161	211	----------	----------	413
30-Aug-24	21	107	204	----------	----------	332
31-Aug-24	4	70	218	----------	----------	292
कुल TOTAL	845	4571	4128	----------	----------	9544
उच्चतम MAXIMUM	65	268	262	----------	----------	553
निम्नतम MINIMUM	4	38	29	----------	----------	112
औसत AVERAGE	27	147	133	----------	----------	308
संचयी 2024-25 Cumulative 2024-25	3927	20603	21140	----------	----------	45670
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन

SOLAR GENERATION AT NATIONAL LEVEL

माह: अगस्त 2024 MONTH:- AUG 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-24	90	57	110	1.8	0.9	260
02-Aug-24	53	39	100	1.5	0.6	193
03-Aug-24	105	44	110	2.2	0.8	262
04-Aug-24	137	46	116	2.9	1.0	303
05-Aug-24	81	57	114	2.6	0.7	256
06-Aug-24	63	60	101	1.7	0.9	226
07-Aug-24	100	63	78	1.8	0.9	244
08-Aug-24	123	67	106	2.6	0.8	300
09-Aug-24	139	61	122	2.4	1.0	326
10-Aug-24	126	57	120	2.7	0.8	306
11-Aug-24	138	59	120	2.7	0.6	320
12-Aug-24	153	67	126	2.8	0.8	349
13-Aug-24	128	81	120	2.9	1.1	334
14-Aug-24	91	77	118	2.6	1.1	290
15-Aug-24	105	71	123	3.0	0.8	303
16-Aug-24	67	67	104	2.6	1.1	243
17-Aug-24	103	72	114	3.0	0.7	293
18-Aug-24	144	86	122	2.8	0.7	356
19-Aug-24	156	86	96	2.9	0.6	341
20-Aug-24	170	84	119	2.8	0.4	376
21-Aug-24	161	88	123	3.3	0.8	376
22-Aug-24	152	84	114	2.2	1.0	353
23-Aug-24	147	71	125	1.9	1.1	346
24-Aug-24	142	50	105	2.3	0.9	300
25-Aug-24	132	43	118	2.6	1.1	297
26-Aug-24	124	46	129	2.6	1.1	303
27-Aug-24	99	56	123	2.2	1.1	281
28-Aug-24	141	53	101	2.4	0.9	299
29-Aug-24	138	60	117	1.9	1.2	319
30-Aug-24	140	75	95	3.1	1.3	315
31-Aug-24	137	85	73	3.1	0.6	299
कुल TOTAL	3788	2013	3463	78	27	9369
उच्चतम MAXIMUM	170	88	129	3.3	1.3	376
निम्नतम MINIMUM	53	39	73	1.5	0.4	193
औसत AVERAGE	122	65	112	2.5	0.9	302
संचयी 2024-25 Cumulative 2024-25	23201	11925	17444	451	141.9	53163
अब तक का उच्चतम All Time Max.	186	103	149	7.0	2.4	426
दिनांक Date	01.05.24	30.04.24	31.03.24	14.07.24	22.06.22	30.04.24

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति

DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: अगस्त 2024 MONTH:- AUG 2024

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL		विभिन्नता फ़ैक्टर Diversity Factor*
01-Aug-24	75482	56519	54507	27745	3414	205428		1.060
02-Aug-24	75428	55216	54714	23672	3218	200005		1.061
03-Aug-24	72897	54673	54165	24744	3397	200225		1.048
04-Aug-24	73349	51630	52597	26683	3389	195676		1.061
05-Aug-24	76258	56518	56362	27585	3303	208736		1.054
06-Aug-24	77171	56750	54514	26956	3483	206522		1.060
07-Aug-24	74485	57319	50040	27438	3560	206147		1.032
08-Aug-24	74910	57990	49539	27408	3393	208742		1.022
09-Aug-24	73504	58411	51450	27161	3469	207395		1.032
10-Aug-24	73722	57655	51859	26738	3448	206434		1.034
11-Aug-24	69903	55520	49078	26181	3275	195244		1.045
12-Aug-24	68620	59134	53707	28308	3444	206248		1.034
13-Aug-24	70920	60470	54325	27687	3587	208297		1.042
14-Aug-24	72072	61029	55617	28038	3732	215360		1.024
15-Aug-24	69243	57552	50796	28121	3346	201364		1.038
16-Aug-24	72516	61248	56912	28152	3576	216685		1.026
17-Aug-24	73361	60843	51798	28297	3463	214688		1.014
18-Aug-24	72209	59201	50492	27716	3282	205478		1.036
19-Aug-24	70240	57038	55344	27212	3172	207670		1.026
20-Aug-24	71150	61116	50447	27753	3066	208948		1.022
21-Aug-24	73416	62508	51205	28111	3286	212020		1.031
22-Aug-24	74042	62291	50506	27342	3477	214451		1.015
23-Aug-24	73088	62710	53190	26290	3623	211407		1.035
24-Aug-24	74335	58069	51680	26265	3546	205462		1.041
25-Aug-24	74125	51347	48257	26111	3316	194416		1.045
26-Aug-24	73980	51116	54163	26282	3571	202182		1.034
27-Aug-24	67957	53072	57386	26779	3694	200088		1.044
28-Aug-24	71324	56160	57568	27237	3668	207078		1.043
29-Aug-24	67454	56703	57801	27767	3739	202730		1.053
30-Aug-24	72398	58410	54404	28777	3853	208965		1.042
31-Aug-24	74868	59109	48970	28528	3478	206996		1.038
उच्चतम MAXIMUM	77171	62710	57801	28777	3853	216685		1.061
निम्नतम MINIMUM	67454	51116	48257	23672	3066	194416		1.014
औसत AVERAGE	72723	57656	53013	27196	3460	206164		1.038
अब तक का उच्चतम All Time Max.	91215	74974	68735	32531	**3853**	250070		
दिनांक Date	19.06.24	01.06.24	13.03.24	10.06.24	**30.08.24**	30.05.24		


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 16 AUG (MAXIMUM DEMAND MET)

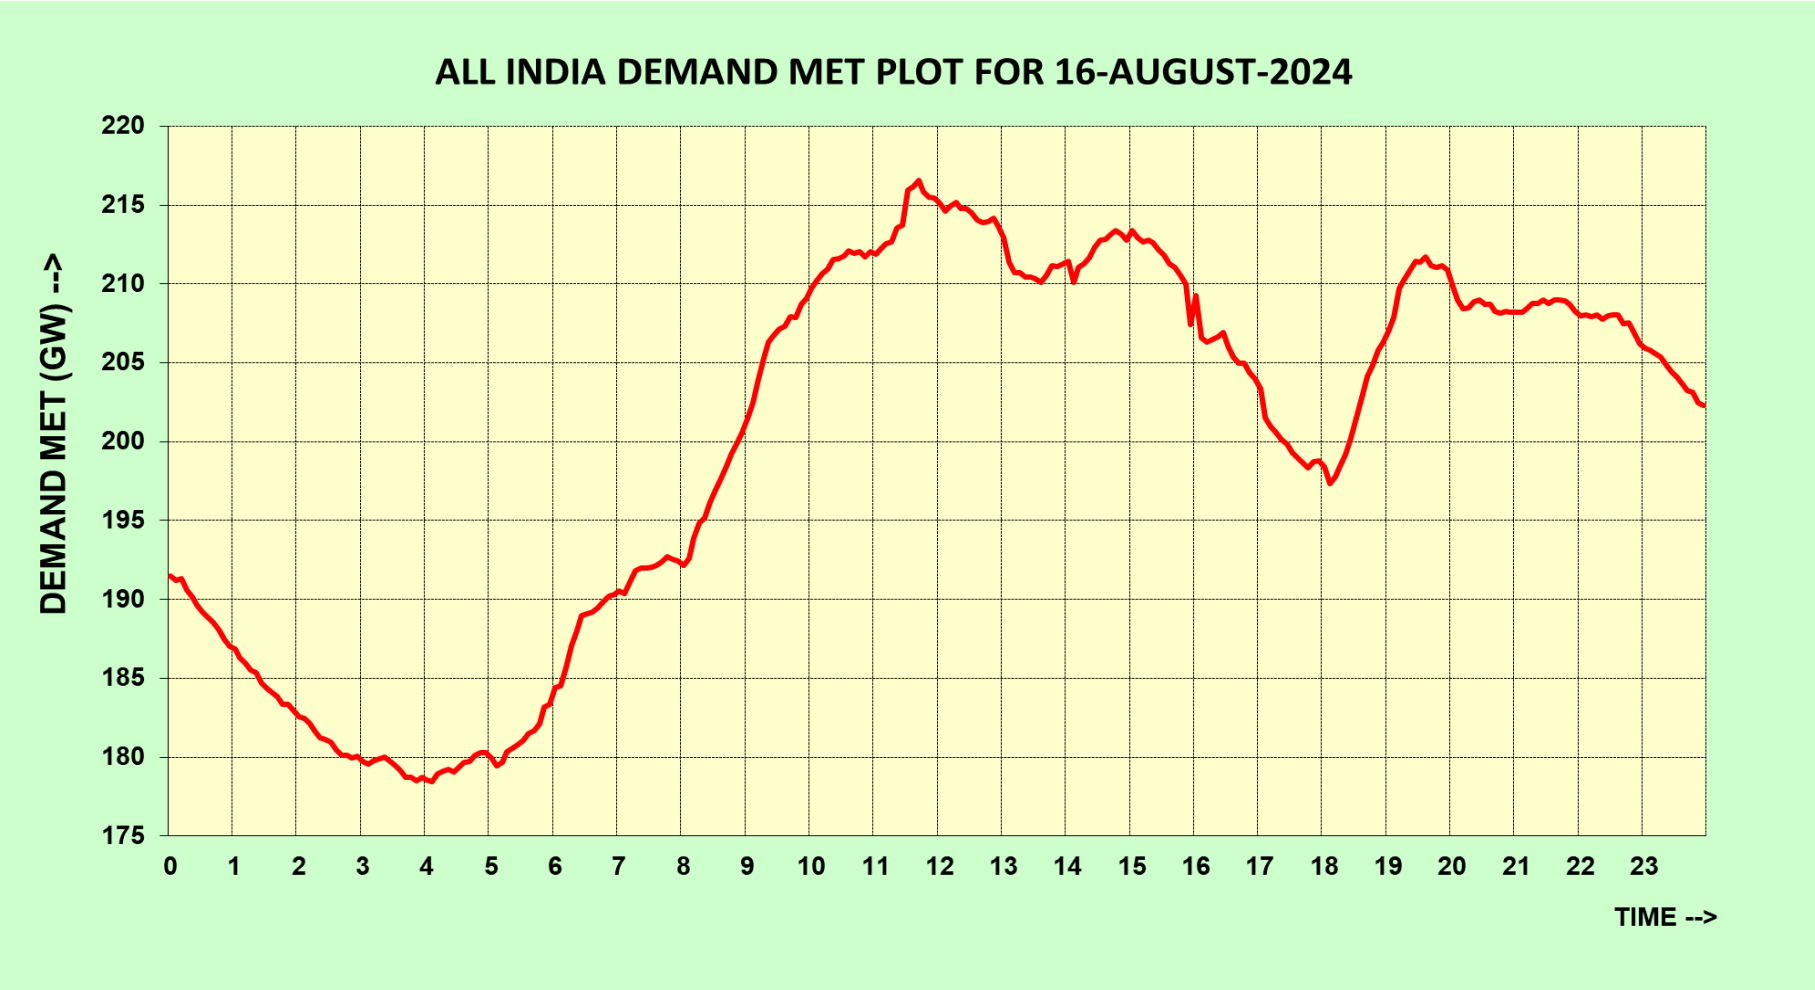

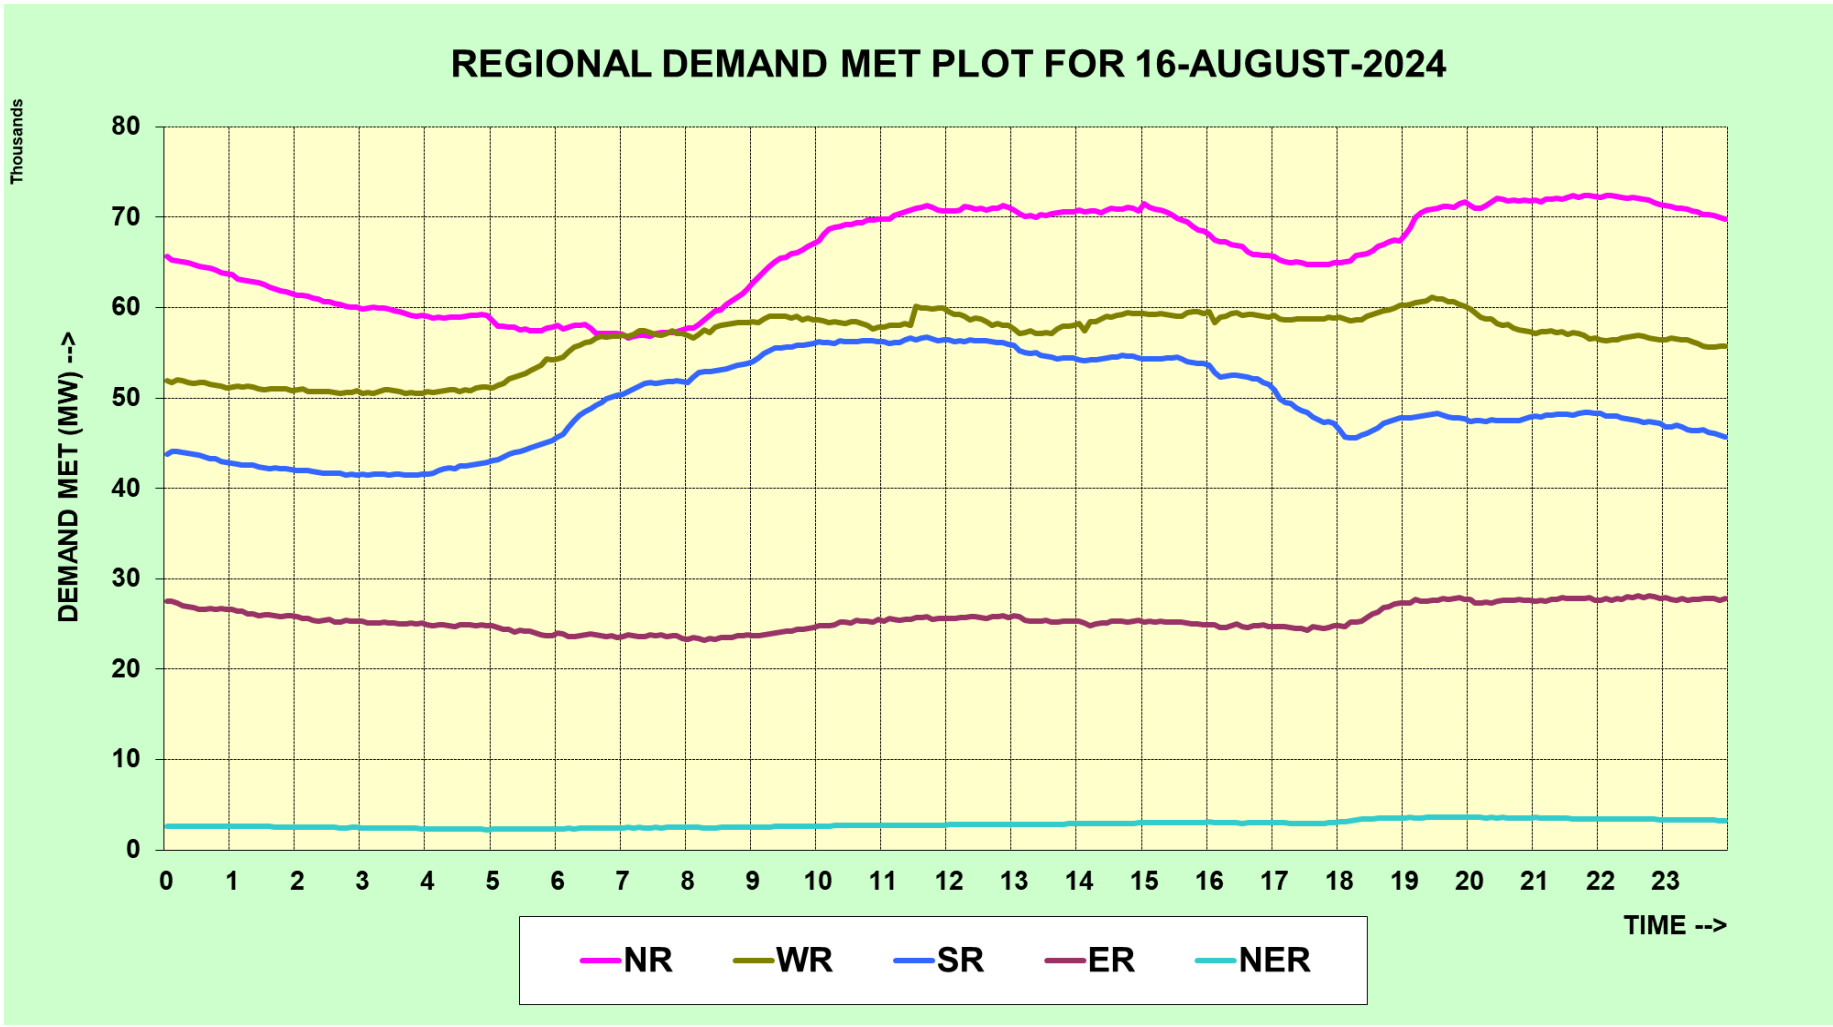
REGIONAL DEMAND MET PLOT FOR 16-AUGUST-2024
Thousands
DEMAND MET (MW) -->
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

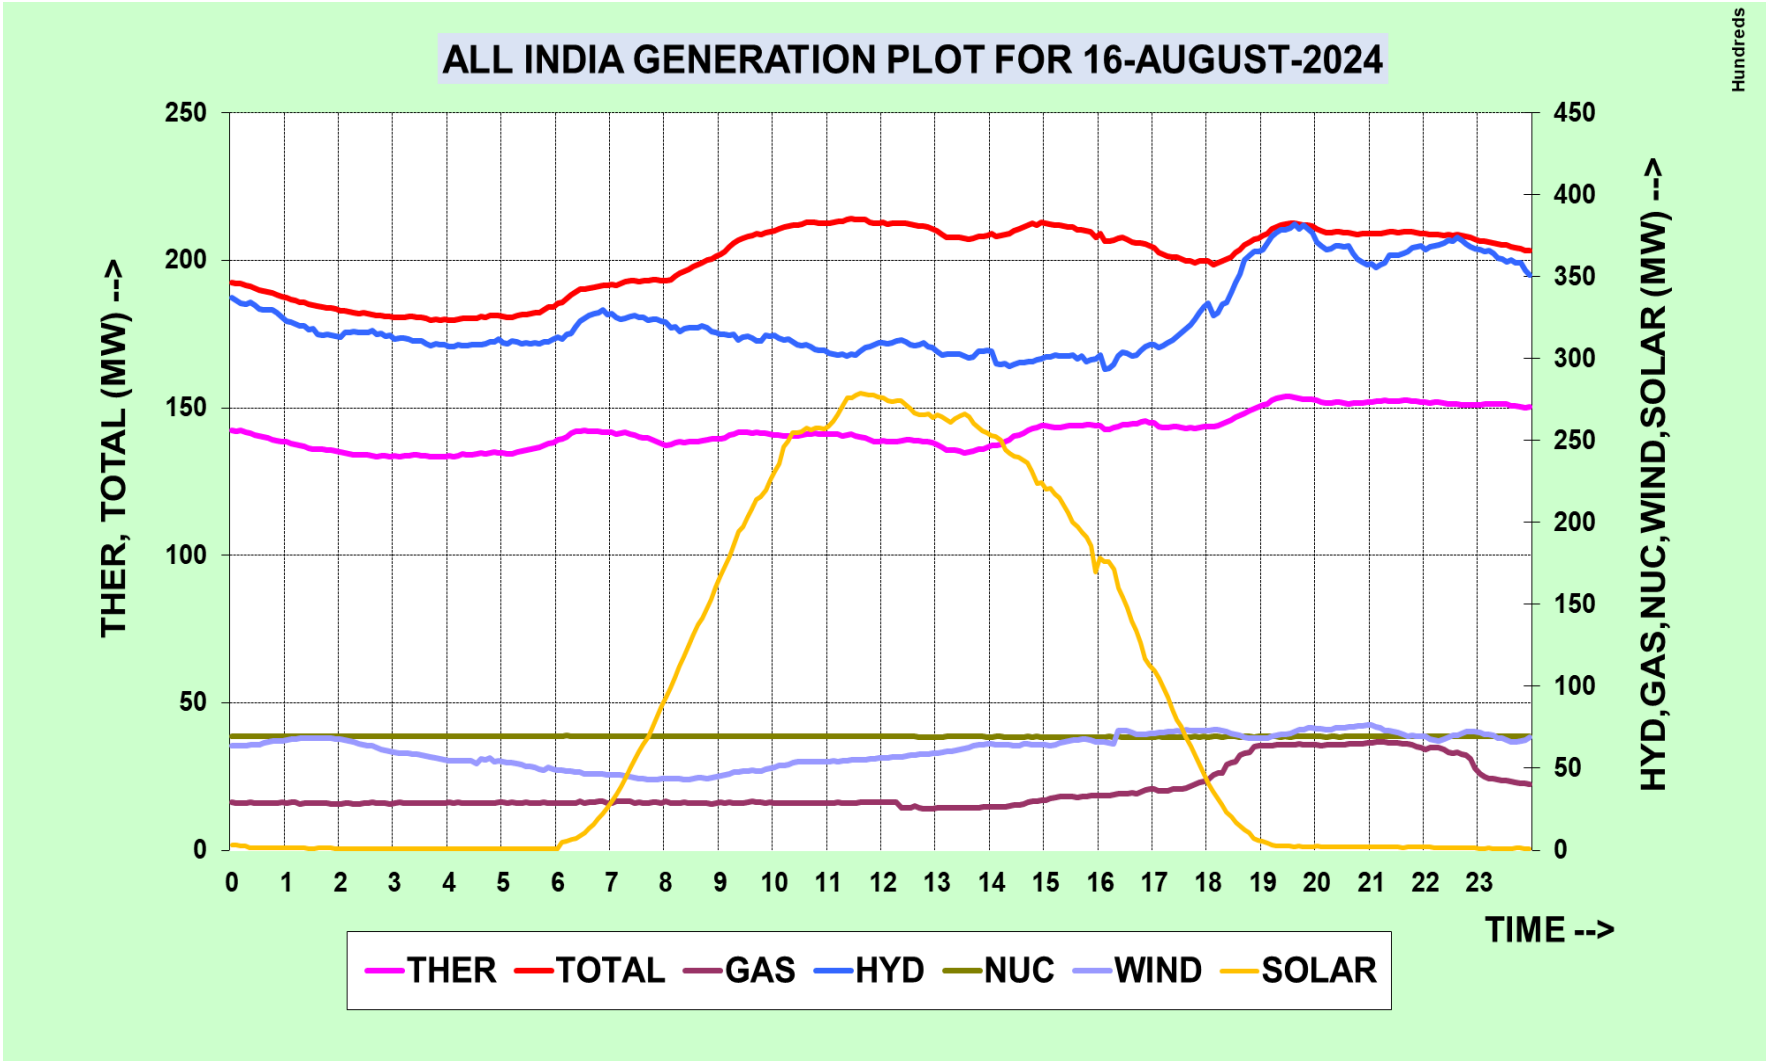
ALL INDIA GENERATION PLOT FOR 16-AUGUST-2024
Hundreds
THER, TOTAL (MW) -->
HYD,GAS,NUC,WIND,SOLAR (MW) -->
250
200
150
100
50
0
450
400
350
300
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
THER TOTAL GAS HYD NUC WIND SOLAR

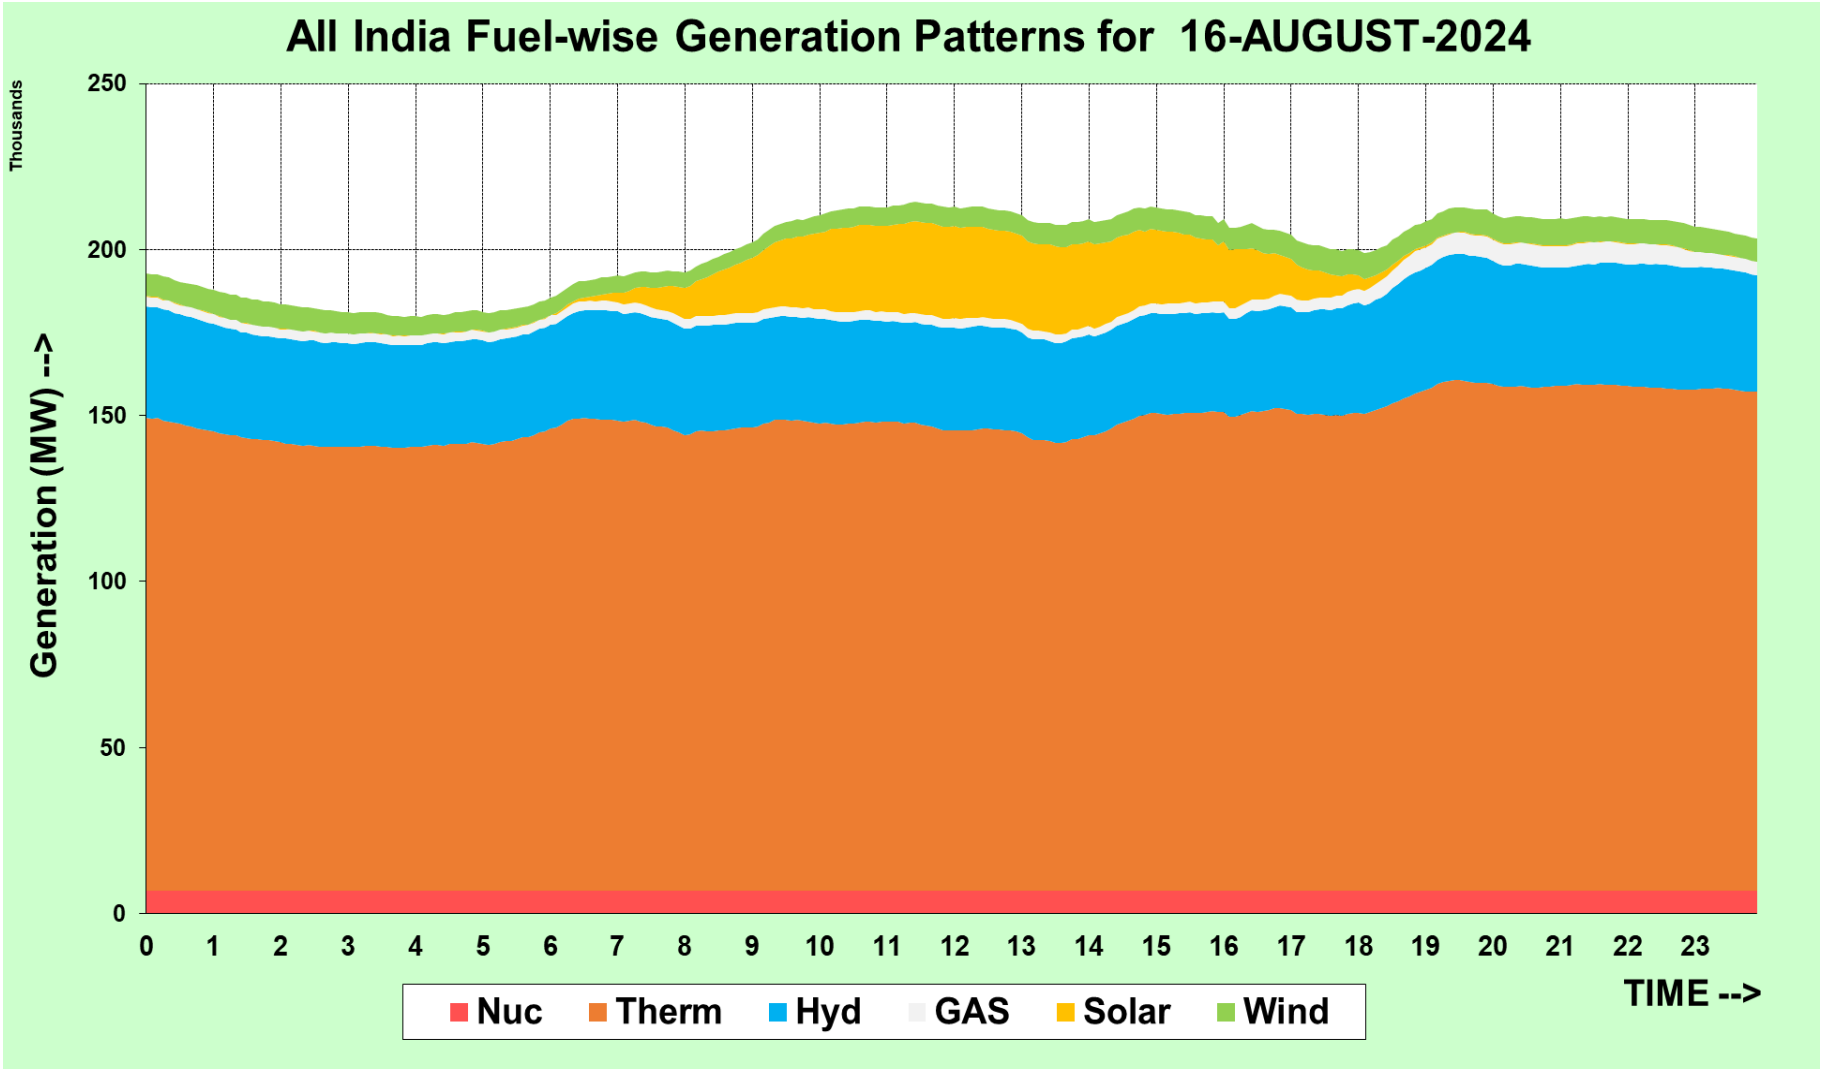
All India Fuel-wise Generation Patterns for 16-AUGUST-2024
Thousands
Generation (MW) -->
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Nuc
Therm
Hyd
GAS
Solar
Wind

16 अगस्त 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 16 AUGUST 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	191198		**12:05**	214592
00:20	190143		**12:20**	214781
00:35	188872		**12:35**	214045
00:50	187462		**12:50**	214148
01:05	186286		**13:05**	211378
01:20	185344		**13:20**	210417
01:35	184064		**13:35**	210090
01:50	183362		**13:50**	211115
02:05	182457		**14:05**	210077
02:20	181210		**14:20**	211678
02:35	180454		**14:35**	212834
02:50	179952		**14:50**	213176
03:05	179546		**15:05**	212921
03:20	179997		**15:20**	212592
03:35	179165		**15:35**	211275
03:50	178508		**15:50**	210012
04:05	178424		**16:05**	206582
04:20	179202		**16:20**	206634
04:35	179695		**16:35**	205343
04:50	180305		**16:50**	204351
05:05	179430		**17:05**	201544
05:20	180558		**17:20**	200147
05:35	181489		**17:35**	198964
05:50	183185		**17:50**	198758
06:05	184515		**18:05**	197363
06:20	188033		**18:20**	199195
06:35	189217		**18:35**	202793
06:50	190181		**18:50**	205826
07:05	190387		**19:05**	207848
07:20	191985		**19:20**	210888
07:35	192158		**19:35**	211724
07:50	192532		**19:50**	211159
08:05	192597		**20:05**	208974
08:20	195182		**20:20**	208888
08:35	197648		**20:35**	208718
08:50	199844		**20:50**	208237
09:05	202468		**21:05**	208228
09:20	206318		**21:20**	208754
09:35	207302		**21:35**	208972
09:50	208711		**21:50**	208711
10:05	210229		**22:05**	208017
10:20	211532		**22:20**	207782
10:35	212089		**22:35**	208050
10:50	211696		**22:50**	206859
11:05	212276		**23:05**	205832
11:20	213568		**23:20**	204888
11:35	216150		**23:35**	203645
11:50	215489		**23:50**	202446
Maximum Demand of 216685 MW met@11:38 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - AUGUST 2024

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	7	7	0.0	214	214	0	0.0	418	418	0	0.0
	Delhi	128	128	0.0	3954	3954	0	0.0	6890	6890	0	0.0
	Haryana	233	233	0.0	7212	7212	0	0.0	12703	12703	0	0.0
	Himachal Pradesh	35	35	0.0	1073	1073	0	0.0	1732	1732	0	0.0
	J&K(UT) and Ladakh(UT)	50	50	-0.1	1550	1546	-4	-0.2	2726	2624	-102	-3.7
	Punjab	300	300	0.0	9291	9291	0	0.0	15307	15307	0	0.0
	Rajasthan	251	251	0.0	7790	7790	0	0.0	13409	13409	0	0.0
	Uttar Pradesh	524	524	-0.2	16252	16245	-8	0.0	29126	29126	0	0.0
	Uttarakhand	54	54	0.0	1669	1668	-1	-0.1	2482	2452	-30	-1.2
	Railway	4	4	0.0	127	127	0	0.0	228	228	0	0.0
	NFL	0	0	0.0	3	3	0	0.0	5	5	0	0.0
	TOTAL	1585	1585	-0.4	49135	49123	-12	0.0	77380	77099	-281	-0.4
WR	Gujarat	381	381	0.0	11825	11825	0	0.0	21918	21918	0	0.0
	Madhya Pradesh	234	233	-1.0	7252	7221	-31	-0.4	11822	11822	0	0.0
	Chhattisgarh	107	106	-0.1	3303	3300	-2	-0.1	5478	5478	0	0.0
	Maharashtra	505	504	-0.3	15647	15636	-11	-0.1	28074	25855	-2218	-7.9
	Goa	14	14	0.0	428	427	0	-0.1	690	690	0	0.0
	DNHDDPDCL	29	29	0.0	896	896	0	0.0	1321	1321	0	0.0
	AMNSIL	18	18	0.0	564	564	0	0.0	899	899	0	0.0
	BALCO	13	13	0.0	389	389	0	0.0	559	559	0	0.0
	TOTAL	1300	1299	-1.4	40304	40260	-45	-0.1	67019	63713	-3306	-4.9
SR	Andhra Pradesh	205	205	0.0	6353	6353	0	0.0	11825	11825	0	0.0
	Telangana	224	224	0.0	6949	6949	0	0.0	15593	15573	-20	-0.1
	Karnataka	207	207	0.0	6411	6411	0	0.0	12594	12580	-14	-0.1
	Kerala	76	76	0.0	2363	2363	0	0.0	4262	4262	0	0.0
	Tamil Nadu	359	359	0.0	11135	11135	0	0.0	18052.50982	18047	-6	0.0
	Puducherry	10	10	0.0	318	318	0	0.0	517	517	0	0.0
	TOTAL	1082	1082	0.0	33529	33529	0	0.0	57854	57854	0	0.0
ER	Bihar	142	142	-0.2	4412	4405	-7	-0.2	7905	7815	-90	-1.1
	Jharkhand	41	41	-0.1	1278	1275	-2	-0.2	2182	2182	0	0.0
	DVC	70	70	0.0	2168	2168	0	0.0	3436	3436	0	0.0
	Odisha	118	118	0.0	3647	3647	0	0.0	6020	6020	0	0.0
	West Bengal	207	207	0.0	6428	6428	0	0.0	10707	10707	0	0.0
	Sikkim	1	1	0.0	37	37	0	0.0	104	104	0	0.0
	Railways_ER ISTS	0	0	0.0	4	4	0	0.0	29	29	0	0.0
	TOTAL	580	580	-0.3	17975	17966	-9	-0.1	28804	28804	0	0.0
NER	Arunachal Pradesh	3	3	0.0	99	99	0	0.0	195	195	0	0.0
	Assam	44	44	-0.1	1379	1376	-3	-0.2	2617	2617	0	0.0
	Manipur	2	2	0.0	74	74	0	0.0	214	214	0	0.0
	Meghalaya	6	6	0.0	173	173	0	0.0	346	346	0	0.0
	Mizoram	2	2	0.0	54	54	0	0.0	152	152	0	0.0
	Nagaland	3	3	0.0	80	80	0	0.0	183	183	0	0.0
	Tripura	7	7	0.0	210	210	0	0.0	341	341	0	0.0
	TOTAL	67	67	-0.1	2069	2065	-3	-0.2	3859	3859	0	0.0
ALL INDIA		4613	4611	-2.3	143013	142943	-70	0.0				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF AUGUST 2024 vs AUGUST 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Aug-23	Aug-24	Difference	% Change	Average MU/day for Jul-24	Aug-23	Aug-24	Difference	% Change	Average MU/day for Jul-24
NR	Chandigarh	213	214	1	1	7	213	214	1	1	7
	Delhi	4076	3954	-122	-3	128	4076	3954	-122	-3	128
	Haryana	7680	7212	-468	-6	233	7592	7212	-379	-5	233
	Himachal Pradesh	1059	1073	14	1	35	1056	1073	17	2	35
	J&K(UT) and Ladakh(UT)	1606	1550	-56	-3	50	1585	1546	-39	-2	50
	Punjab	9719	9291	-428	-4	300	9719	9291	-428	-4	300
	Rajasthan	10286	7790	-2497	-24	251	10173	7790	-2383	-23	251
	Uttar Pradesh	15784	16252	468	3	524	15672	16245	572	4	524
	Uttarakhand	1420	1669	249	18	54	1401	1668	267	19	54
	Railway/NFL	109	130	20	19	4	109	130	20	19	4
	TOTAL	51953	49135	-2818	-5	1585	51596	49123	-2473	-5	1585
WR	Gujarat	12895	11825	-1069	-8	381	12893	11825	-1068	-8	381
	Madhya Pradesh	7836	7252	-584	-7	234	7836	7221	-615	-8	233
	Chhattisgarh	3612	3303	-310	-9	107	3592	3300	-292	-8	106
	Maharashtra	16737	15647	-1090	-7	505	16632	15636	-995	-6	504
	Goa	409	428	18	5	14	409	427	18	4	14
	DNHDDPDCL	916	896	-19	-2	29	916	896	-19	-2	29
	AMNSIL	587	564	-23	-4	18	587	564	-23	-4	18
	BALCO	385	389	4	1	13	385	389	4	1	13
	TOTAL	43377	40304	-3073	-7	1300	43250	40260	-2990	-7	1299
SR	Andhra Pradesh	7212	6353	-859	-12	205	7175	6353	-821	-11	205
	Telangana	7933	6949	-984	-12	224	7890	6949	-940	-12	224
	Karnataka	7997	6411	-1586	-20	207	7954	6411	-1543	-19	207
	Kerala	2598	2363	-235	-9	76	2584	2363	-221	-9	76
	Tamil Nadu	11406	11135	-272	-2	359	11349	11135	-215	-2	359
	Puducherry	312	318	5	2	10	311	318	7	2	10
	TOTAL	37460	33529	-3931	-10	1082	37263	33529	-3733	-10	1082
ER	Bihar	4299	4412	113	3	142	4239	4405	167	4	142
	Jharkhand	1203	1278	75	6	41	1153	1275	122	11	41
	DVC	2299	2168	-132	-6	70	2299	2168	-132	-6	70
	Odisha	3627	3647	21	1	118	3625	3647	22	1	118
	West Bengal	6263	6428	165	3	207	6263	6428	165	3	207
	Sikkim	33	37	5	14	1	33	37	5	14	1
	Railways_ER ISTS	5	4	0	-7	0	5	4	0	-7	0
	TOTAL	17729	17975	247	1	580	17617	17966	349	2	580
NER	Arunachal Pradesh	83	99	16	19	3	83	99	16	19	3
	Assam	1352	1379	27	2	44	1320	1376	56	4	44
	Manipur	81	74	-7	-8	2	81	74	-7	-8	2
	Meghalaya	175	173	-2	-1	6	160	173	13	8	6
	Mizoram	53	54	1	2	2	53	54	1	2	2
	Nagaland	89	80	-9	-10	3	89	80	-9	-10	3
	Tripura	168	210	42	25	7	168	210	42	25	7
	TOTAL	2001	2069	67	3	67	1954	2065	111	6	67
ALL INDIA		152520	143013	-9507	-6	4613	151679	142943	-8736	-6	4611

13. DEMAND COMPARISON OF AUGUST 2024 vs AUGUST 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Aug-23	Aug-24	Difference	% Change	Aug-23	Aug-24	Difference	% Change
NR	Chandigarh	411	418	7	1.7	411	418	7	1.7
	Delhi	7437	6890	-547	-7.4	7437	6890	-547	-7.4
	Haryana	12844	12703	-141	-1.1	12844	12703	-141	-1.1
	Himachal Pradesh	1724	1732	8	0.5	1724	1732	8	0.5
	J&K(UT) and Ladakh(UT)	2735	2726	-9	-0.3	2735	2624	-111	-4.1
	Punjab	15220	15307	87	0.6	15220	15307	87	0.6
	Rajasthan	17420	13409	-4011	-23.0	17266	13409	-3857	-22.3
	Uttar Pradesh	27689	29126	1437	5.2	27689	29126	1437	5.2
	Uttarakhand	2303	2482	179	7.8	2228	2452	224	10.1
	Railway/NFL	206	233	27	13.1	206	233	27	13.1
WR	Gujarat	23012	21918	-1094	-5	22972	21918	-1054	-4.6
	Madhya Pradesh	13624	11822	-1802	-13	13605	11822	-1783	-13.1
	Chhattisgarh	5827	5478	-349	-6	5827	5478	-349	-6.0
	Maharashtra	31178	28074	-3104	-10	27996	25855	-2141	-7.6
	Goa	667	690	24	4	666	690	24	3.6
	DNHDDPDCL	1327	1321	-6	-0.5	1327	1321	-6	-0.5
	AMNSIL	942	899	-42	-4.5	942	899	-42	-4.5
	BALCO	522	559	37	7.0	522	559	37	7.0
SR	Andhra Pradesh	12508	11825	-683	-5.5	12508	11825	-683	-5.5
	Telangana	14835	15593	759	5.1	14816	15573	757	5.1
	Karnataka	16968	12594	-4375	-25.8	16950	12580	-4369	-25.8
	Kerala	4366	4262	-105	-2.4	4366	4262	-105	-2.4
	Tamil Nadu	18252	18053	-199	-1.1	18252	18047	-205	-1.1
	Puducherry	492	517	25	5.1	492	517	25	5.1
ER	Bihar	7258	7905	647	8.9	7185	7815	630	8.8
	Jharkhand	1827	2182	355	19.4	1827	2182	355	19.4
	DVC	3673	3436	-237	-6.5	3673	3436	-237	-6.5
	Odisha	6816	6020	-796	-11.7	6816	6020	-796	-11.7
	West Bengal	10642	10707	65	0.6	10642	10707	65	0.6
	Sikkim	92	104	12	13.0	92	104	12	13.0
	Railways_ER ISTS	31	29	-2	-6.5	31	29	-2	-6.5
NER	Arunachal Pradesh	155	195	40	25.6	155	195	40	25.6
	Assam	2353	2617	264	11.2	2353	2617	264	11.2
	Manipur	209	214	5	2.3	209	214	5	2.3
	Meghalaya	322	346	24	7.4	322	346	24	7.4
	Mizoram	126	152	26	20.4	126	152	26	20.4
	Nagaland	174	183	9	5.4	174	183	9	5.4
	Tripura	330	341	11	3.4	330	341	11	3.4

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - AUGUST 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	217.90	214.31	-3.59	-1.65	7.03	6.91	-0.12
	Delhi	3546.22	3542.55	-3.67	-0.10	114.39	114.28	-0.12
	Haryana	5266.91	5289.43	22.52	0.43	169.90	170.63	0.73
	Himachal Pradesh	93.27	65.75	-27.52	-29.51	3.01	2.12	-0.89
	J&K(UT) and Ladakh(UT)	784.13	773.79	-10.34	-1.32	25.29	24.96	-0.33
	Punjab	5994.60	5993.40	-1.20	-0.02	193.37	193.34	-0.04
	Rajasthan	2244.01	2071.01	-173.00	-7.71	72.39	66.81	-5.58
	Uttar Pradesh	7830.07	7879.64	49.57	0.63	252.58	254.18	1.60
	Uttarakhand	741.06	749.07	8.01	1.08	23.91	24.16	0.26
	Railway	118.55	127.25	8.70	7.34	3.82	4.10	0.28
	NFL	2.80	2.69	-0.11	-3.97	0.09	0.09	0.00
	Total	26839.52	26708.89	-130.63	-0.49	865.79	861.58	-4.21
WR	Gujarat	4494.77	4387.95	-106.82	-2.38	144.99	141.55	-3.45
	Madhya Pradesh	3597.82	3528.08	-69.74	-1.94	116.06	113.81	-2.25
	Chhattisgarh	2007.77	1970.87	-36.90	-1.84	64.77	63.58	-1.19
	Maharashtra	5519.42	5413.08	-106.34	-1.93	178.05	174.62	-3.43
	Goa	360.21	417.35	57.14	15.86	11.62	13.46	1.84
	DNHDDPDCL	898.95	896.40	-2.55	-0.28	29.00	28.92	-0.08
	AMNSIL	243.91	255.94	12.03	4.93	7.87	8.26	0.39
	BALCO*	390.28	388.81	-1.47	-0.38	12.59	12.54	-0.05
	Total	17513.13	17258.48	-254.65	-1.45	564.94	556.73	-8.21
SR	Andhra Pradesh	1973.10	1967.21	-5.89	-0.30	63.65	63.46	-0.19
	Telangana	4359.27	4357.74	-1.53	-0.04	140.62	140.57	-0.05
	Karnataka	1026.94	1011.60	-15.34	-1.49	33.13	32.63	-0.49
	Kerala	1401.73	1431.54	29.81	2.13	45.22	46.18	0.96
	Tamil Nadu	5248.14	5192.37	-55.77	-1.06	169.29	167.50	-1.80
	Puducherry	304.95	297.67	-7.28	-2.39	9.84	9.60	-0.23
	Goa (SR)	62.43	64.05	1.62	2.59	2.01	2.07	0.05
	Total	14376.56	14322.18	-54.38	-0.38	463.76	462.01	-1.75
ER	Bihar	4102.73	4081.99	-20.74	-0.51	132.35	131.68	-0.67
	Jharkhand	939.67	930.30	-9.36	-1.00	30.31	30.01	-0.30
	DVC	-1165.45	-1154.18	11.28	-0.97	-37.60	-37.23	0.36
	Odisha	1374.58	1337.90	-36.68	-2.67	44.34	43.16	-1.18
	West Bengal	2467.92	2412.64	-55.28	-2.24	79.61	77.83	-1.78
	Sikkim	41.61	37.29	-4.32	-10.39	1.34	1.20	-0.14
	Railways_ER ISTS	4.39	4.33	-0.06	-1.47	0.14	0.14	0.00
	Total	7765.46	7650.29	-115.18	-1.48	250.50	246.78	-3.72
NER	Arunachal Pradesh	86.90	82.95	-3.95	-4.55	2.80	2.68	-0.13
	Assam	1157.48	1154.50	-2.98	-0.26	37.34	37.24	-0.10
	Manipur	88.38	74.10	-14.28	-16.16	2.85	2.39	-0.46
	Meghalaya	7.58	3.73	-3.85	-50.75	0.24	0.12	-0.12
	Mizoram	20.27	9.20	-11.07	-54.61	0.65	0.30	-0.36
	Nagaland	82.02	64.90	-17.12	-20.87	2.65	2.09	-0.55
	Tripura	144.81	147.58	2.77	1.91	4.67	4.76	0.09
	Total	1587.44	1536.96	-50.48	-3.18	51.21	49.58	-1.63
All India Total		68082.11	67476.80	-605.31	-0.89	2196.20	2176.67	-19.53

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Fin. Year 2024-25
Name of Line						
Import of NR from WR (WR-NR)						
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	**5854.69**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	**2149.11**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	**5002.22**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	**3154.89**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	**11934.96**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	**487.04**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	**225.52**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	**14.35**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	**444.92**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	**309.01**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	**318.49**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	**15.03**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	**5567.59**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	**1490.56**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	**9476.69**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	**409.84**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**46854.91**
Export of NR to WR (NR-WR)						
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	**1389.00**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	**490.39**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	**365.56**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	**29.97**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	**214.68**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	**133.49**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	**2908.15**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	**642.29**

	Apr'24	May'24	June'24	July'24	Aug'24	Fin. Year 2024-25
Name of Line						
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	**193.92**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**6382.44**

	Apr'24	May'24	June'24	July'24	Aug'24	Fin. Year 2024-25
Name of Line						
Import of NR from ER (ER-NR)						
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	**580.84**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	**488.52**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	**1458.62**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	**810.38**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	**1271.61**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	**1078.42**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	**61.42**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	**809.09**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	**10.67**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	**182.17**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	**71.87**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	**106.07**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	**8.69**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	**323.28**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	**259.77**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**7523.03**
Import of NR from NER (NER-NR)						
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	**642.24**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**642.24**

	Apr'24	May'24	June'24	July'24	Aug'24	Fin. Year 2024-25
Name of Line						
Export of NR to ER (NR-ER)						
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	**7.17**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	**175.80**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	**355.97**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	**19.06**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	**7.13**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	**37.49**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	**3.66**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	**2.67**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	**2.95**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	**84.83**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	**6.23**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**825.37**
Export of NR to NER (NER-NR)						
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	**1365.53**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**1365.53**

	Apr'24	May'24	June'24	July'24	Aug'24	Fin. Year 2024-25
Name of Line						
Export of WR to ER (WR-ER)						
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	**4148.67**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	**1662.88**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	**26.90**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	**913.87**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	**639.78**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	**53.59**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	**14.75**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**7460.43**
Import of WR from ER (ER - WR)						
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	**70.92**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	**1243.25**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	**1188.36**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	**37.22**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	**1019.25**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	**123.03**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	**159.83**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**3841.86**
Export of ER to NER (ER - NER)						
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	**258.88**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	**385.33**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	**88.11**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**732.32**
Import of ER from NER (NER - ER)						
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	**452.52**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	**713.54**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	**116.69**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**1282.76**

	Apr'24	May'24	June'24	July'24	Aug'24	Fin. Year 2024-25
Name of Line						
Export of ER to SR (ER - SR)						
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	**974.16**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	**5311.61**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	**6174.34**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**12460.11**
Import of ER from SR (SR - ER)						
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	**455.80**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	**0.00**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**455.80**
Export of WR to SR (WR-SR)						
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	**1027.24**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	**1233.25**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	**4209.80**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	**0.02**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	**5759.40**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	**324.05**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	**147.17**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	**4473.89**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**17174.83**
Import of WR from SR (SR - WR)						
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	**1383.27**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	**2251.96**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	**79.32**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	**4241.26**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	**362.81**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	**0.01**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	**96.56**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**8415.20**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**115417**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during August 2024

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Aug-24	48.26	36.38	42.68	20.82	0.00	68.42	0.00	5.08		2.83	1.19	1.86	0.32	0.00	35.65	36.38	74.24	1.96	**376.07**
2-Aug-24	53.56	34.96	48.80	23.64	0.00	70.22	0.69	7.89		6.70	1.15	1.59	0.00	0.00	40.88	34.96	68.25	7.28	**400.57**
3-Aug-24	44.95	32.75	41.20	22.28	0.00	69.35	1.22	4.90		2.65	1.10	1.86	0.00	0.00	37.85	32.75	62.05	3.65	**358.56**
4-Aug-24	47.14	27.43	39.35	19.98	0.00	55.41	1.11	5.04		2.57	0.97	1.52	0.00	0.00	31.55	27.43	67.51	2.64	**329.65**
5-Aug-24	44.12	17.93	38.05	23.25	0.00	88.50	0.00	2.05		4.38	0.84	1.38	0.52	0.00	29.52	17.93	69.80	6.96	**345.23**
6-Aug-24	51.79	24.81	46.27	23.92	0.00	70.49	0.00	4.10		5.39	1.25	1.74	0.00	0.00	48.33	24.81	70.45	6.69	**380.04**
7-Aug-24	40.54	24.94	35.58	21.07	0.00	74.16	1.07	2.25		0.61	1.35	1.86	0.58	0.00	46.34	24.94	67.34	1.61	**344.24**
8-Aug-24	32.98	10.95	23.49	19.67	0.00	134.05	12.03	0.00		0.00	1.51	1.85	0.00	0.00	60.39	10.95	49.03	0.00	**356.90**
9-Aug-24	34.25	6.22	31.78	18.91	0.00	87.00	11.90	0.00		0.00	1.25	1.94	0.00	0.00	60.38	6.22	52.36	1.11	**313.32**
10-Aug-24	31.44	12.28	26.13	17.41	0.00	82.21	8.77	0.00		0.00	1.01	1.93	0.00	0.00	55.96	12.28	53.30	0.78	**303.50**
11-Aug-24	26.85	14.61	22.16	15.08	0.00	75.01	1.24	0.00		0.00	1.04	1.93	0.00	0.00	47.88	14.61	55.34	0.00	**275.75**
12-Aug-24	20.66	5.51	15.01	16.44	0.00	57.91	1.24	0.00		0.00	1.06	1.88	0.00	0.00	26.17	5.51	53.95	0.00	**205.34**
13-Aug-24	27.10	0.00	23.95	18.49	0.00	59.03	1.24	0.00		0.83	1.00	1.88	0.00	0.00	24.22	0.00	53.95	3.39	**215.08**
14-Aug-24	33.04	9.54	30.71	19.52	0.00	57.76	0.00	1.30		3.48	1.22	2.04	0.00	0.00	25.26	9.54	53.32	6.03	**252.76**
15-Aug-24	26.84	7.40	24.85	15.44	0.00	59.89	0.00	0.00		0.00	0.87	1.70	0.00	0.00	36.28	7.40	59.15	0.68	**240.50**
16-Aug-24	33.20	9.63	29.37	18.59	0.00	58.00	0.00	0.19		1.47	0.92	1.68	0.00		36.28	9.63	52.51	3.83	**255.30**
17-Aug-24	32.72	5.76	31.61	17.84	0.00	57.74	0.00	0.00		0.53	1.11	1.77	0.00		36.28	5.76	58.09	3.04	**252.25**
18-Aug-24	26.50	1.60	27.40	17.44	0.00	58.40	0.00		0.00	0.00	1.29	1.65	0.00		36.28	1.60	48.67	1.17	**222.00**
19-Aug-24	20.95	0.00	21.46	16.24	0.00	58.90	0.00	0.00		0.00	1.29	1.26	0.00	0.00	35.64	0.00	45.59	0.15	**201.48**
20-Aug-24	20.02	0.00	22.11	16.36	0.00	59.01	0.00	0.00		0.00	1.57	1.23	0.00	0.00	24.23	0.00	42.03	0.00	**186.56**
21-Aug-24	27.78	2.91	28.60	17.50	0.00	57.94	0.00	0.00		1.09	1.84	1.01	0.00		24.23	2.91	44.80	1.37	**211.98**
22-Aug-24	30.93	4.73	33.17	17.59	0.00	58.18	0.00	0.00		2.54	2.03	1.11	0.00		28.40	4.73	43.22	3.26	**229.89**
23-Aug-24	31.22	2.95	34.22	18.22	0.00	58.25	0.00	0.00		2.39	1.66	1.23	0.00		36.29	2.95	49.47	2.69	**241.54**
24-Aug-24	42.66	16.55	41.95	20.09	0.00	58.16	0.67	2.78		4.79	1.60	1.19	0.00		36.28	16.55	54.37	5.07	**302.71**
25-Aug-24	49.36	34.66	44.85	19.00	0.00	58.16	2.44	6.02		5.77	1.29	1.01	1.19		36.28	34.66	64.13	5.03	**363.85**
26-Aug-24	45.85	35.35	40.65	18.45	0.00	59.22	2.43		8.42	4.05	1.34	1.00	0.00		33.24	35.35	67.25	4.02	**356.62**
27-Aug-24	32.43	20.86	27.83	15.95	0.00	58.82	2.43		0.45	0.00	1.53	1.02	0.00	0.00	23.40	20.86	56.10	0.00	**261.68**
28-Aug-24	27.53	14.51	23.65	15.25	0.00	58.20	2.42	0.00	0.00	0.00	1.76	1.24	0.00	0.00	12.18	14.51	51.85	0.00	**223.10**
29-Aug-24	16.72	0.00	18.22	13.16	0.00	59.90	2.05	0.00	0.00	0.00	1.91	1.26	0.00		10.33	0.00	54.48	0.00	**178.03**
30-Aug-24	29.28	0.00	30.07	16.54	0.00	58.66	0.00	0.00	0.00	1.25	2.00	1.32	0.00			0.00	64.21	3.44	**206.77**
31-Aug-24	38.02	0.00	41.03	18.94	0.00	62.83	2.42		0.00	5.16	2.00	1.32	0.00			0.00	64.25	7.90	**243.87**
Total	**1068.69**	**415.22**	**986.20**	**573.08**	**0.00**	**2049.78**	**55.37**	**41.60**	**8.87**	**58.48**	**41.95**	**47.26**	**2.61**	**0.00**	**1016.00**	**415.22**	**1771.06**	**83.75**	**8635.14**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during August 2024

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Aug-24	0.00	0.00	0.00	0.00	9.62	0.00	0.80	0.00		0.00	0.00	0.00	0.00	20.34	0.00	0.00	0.00	0.00	**30.76**
2-Aug-24	0.00	0.00	0.00	0.00	9.66	0.00	2.63	0.00		0.00	0.00	0.00	-0.72	21.98	0.00	0.00	0.00	0.00	**33.55**
3-Aug-24	0.00	0.00	0.00	0.00	7.71	0.00	0.00	0.00		0.00	0.00	0.00	-0.07	21.97	0.00	0.00	0.00	0.00	**29.61**
4-Aug-24	0.00	0.00	0.00	0.00	4.52	0.00	0.20	0.00		0.00	0.00	0.00	1.01	18.31	0.00	0.00	0.00	0.00	**24.04**
5-Aug-24	0.00	0.00	0.00	0.00	7.85	0.00	2.44	0.00		0.00	0.00	0.00	0.00	21.50	0.00	0.00	0.00	0.00	**31.79**
6-Aug-24	0.00	0.00	0.00	0.00	8.08	0.00	2.42	0.00		0.00	0.00	0.00	-0.59	21.30	0.00	0.00	0.00	0.00	**31.21**
7-Aug-24	0.00	0.00	0.00	0.00	5.38	0.00	0.00	0.00		0.00	0.00	0.00	0.00	21.29	0.00	0.00	0.00	0.00	**26.67**
8-Aug-24	0.00	0.00	0.00	0.00	5.64	0.00	0.00	1.21		2.55	0.00	0.00	0.24	19.67	0.00	0.00	0.00	1.31	**30.62**
9-Aug-24	0.00	0.00	0.00	0.00	6.87	0.00	0.00	1.45		0.17	0.00	0.00	0.69	21.69	0.00	0.00	0.00	0.00	**30.87**
10-Aug-24	0.00	0.00	0.00	0.00	6.00	0.00	0.00	0.74		1.29	0.00	0.00	0.60	20.70	0.00	0.00	0.00	0.00	**29.33**
11-Aug-24	0.00	3.08	0.00	0.00	4.42	0.00	0.00	0.40		3.37	0.00	0.00	0.44	18.59	0.00	0.00	0.00	2.38	**32.68**
12-Aug-24	0.00	0.00	0.00	0.00	6.40	0.00	0.00	1.20		2.16	0.00	0.00	1.10	21.57	0.00	0.00	0.00	1.65	**34.08**
13-Aug-24	0.00	0.00	0.00	0.00	8.33	0.00	0.00	1.81		0.00	0.00	0.00	1.11	22.61	0.00	0.39	0.00	0.00	**34.25**
14-Aug-24	0.00	0.00	0.00	0.00	10.07	0.00	1.09	0.00		0.00	0.00	0.00	1.10	9.69	0.00	0.00	0.00	0.00	**21.95**
15-Aug-24	0.00	0.00	0.00	0.00	5.91	0.00	2.45	0.61		1.55	0.00	0.00	0.53	0.00	0.00	0.00	0.00	0.00	**11.05**
16-Aug-24	0.00	0.00	0.00	0.00	9.31	0.00	2.43	0.00		0.00	0.00	0.00	0.83		0.00	0.00	0.00	0.00	**12.57**
17-Aug-24	0.00	0.00	0.00	0.00	9.08	0.00	2.44	0.80		0.00	0.00	0.00	0.86		0.00	0.00	0.00	0.00	**13.18**
18-Aug-24	0.00	0.00	0.00	0.00	8.17	0.00	2.44		1.99	0.99	0.00	0.00	1.61		0.00	0.00	0.00	0.00	**15.20**
19-Aug-24	0.00	0.00	0.00	0.00	8.20	0.00	2.44	3.21		1.32	0.00	0.00	1.70	0.00	0.00	3.40	0.00	0.00	**20.27**
20-Aug-24	0.00	0.00	0.00	0.00	8.86	0.00	2.51	4.10		1.41	0.00	0.00	1.96	0.00	0.00	1.91	0.00	1.53	**22.28**
21-Aug-24	0.00	0.00	0.00	0.00	9.45	0.00	2.45	1.67		0.00	0.00	0.00	1.37		0.00	0.00	0.00	0.00	**14.94**
22-Aug-24	0.00	0.00	0.00	0.00	11.20	0.00	2.39	0.90		0.00	0.00	0.00	1.66		0.00	0.00	0.00	0.00	**16.15**
23-Aug-24	0.00	0.00	0.00	0.00	10.53	0.00	2.44	1.12		0.00	0.00	0.00	1.73		0.00	0.00	0.00	0.00	**15.82**
24-Aug-24	0.00	0.00	0.00	0.00	9.84	0.00	1.71	0.00		0.00	0.00	0.00	0.35		0.00	0.00	0.00	0.00	**11.90**
25-Aug-24	0.00	0.00	0.00	0.00	7.39	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	**7.39**
26-Aug-24	0.00	0.00	0.00	0.00	5.75	0.00	0.00		0.00	0.00	0.00	0.00	-0.64		0.00	0.00	0.00	0.00	**5.11**
27-Aug-24	0.00	0.00	0.00	0.00	4.78	0.00	0.00		0.00	0.52	0.00	0.00	0.71	0.00	0.00	0.00	0.00	0.26	**6.27**
28-Aug-24	0.00	0.00	0.00	0.00	5.56	0.00	0.00	0.96	3.05	1.76	0.00	0.00	1.00	0.00	0.00	0.00	0.00	0.65	**12.98**
29-Aug-24	0.00	0.00	0.00	0.00	6.87	0.00	0.46	1.25	6.44	3.17	0.00	0.00	1.99		0.00	1.36	0.00	1.47	**23.01**
30-Aug-24	0.00	0.00	0.00	0.00	9.24	0.00	0.56	0.85	4.81	0.00	0.00	0.00	1.37			5.73	0.00	0.00	**22.56**
31-Aug-24	0.00	0.00	0.00	0.00	11.56	0.00	0.00		4.13	0.00	0.00	0.00	0.98			7.49	0.00	0.00	**24.16**
Total	**0.00**	**3.08**	**0.00**	**0.00**	**242.25**	**0.00**	**34.30**	**22.28**	**20.42**	**20.26**	**0.00**	**0.00**	**22.92**	**281.21**	**0.00**	**20.28**	**0.00**	**9.25**	**676.25**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during August 2024

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Aug-24	0.92	0.00	9.98	8.42	3.38	10.68	0.00	4.12		1.22	0.96	0.00	0.00	0.00	0.00	0.98	2.40	**43.06**	7.20	**7.20**
2-Aug-24	6.21	9.35	11.95	13.01	9.06	16.65	2.98	8.97		0.15	2.01	0.69	0.00	0.00	0.00	4.85	6.15	**92.03**	7.08	**7.08**
3-Aug-24	6.52	8.22	10.45	16.90	10.35	13.64	2.06	7.92		0.02	2.12	0.80	0.00	0.00	0.00	2.47	5.38	**86.85**	7.00	**7.00**
4-Aug-24	1.96	1.23	8.40	18.39	6.38	9.83	0.00	4.89		0.54	1.66	1.00	0.00		0.00	1.07	3.20	**58.55**	7.47	**7.47**
5-Aug-24	2.34	3.20	10.67	18.39	8.75	10.04	0.00	5.84	0.00	1.08	1.18	0.35			0.00	1.85	3.69	**67.38**	6.97	**6.97**
6-Aug-24	5.47	9.44	12.66	16.72	12.39	14.31	1.71	9.28		0.66	1.68	0.67			0.00	3.30	5.35	**93.64**	7.09	**7.09**
7-Aug-24	1.28	2.20	10.35	18.31	6.09	8.25	0.00	5.77		1.21	1.02	1.25			0.00	0.98	2.53	**59.24**	7.87	**7.87**
8-Aug-24	0.00	0.11	7.11	10.55	3.98	6.80	0.00	3.79		1.01	1.01	0.98	0.00		0.00	0.82	1.01	**37.17**	7.92	**7.92**
9-Aug-24	0.82	3.99	8.85	8.81	8.78	10.20	0.00	6.56		5.34	2.85	0.48	0.00		0.00	1.92	2.28	**60.88**	8.45	**8.45**
10-Aug-24	0.15	0.82	7.65	13.32	7.49	8.10	0.00	4.64		5.91	2.70	0.00		0.00	0.00	1.49	0.98	**53.25**	8.12	**8.12**
11-Aug-24	0.00	0.00	6.66	17.22	5.21	5.89	0.00	3.73		3.52	0.60	0.44	0.48	0.00	0.00	0.81	0.62	**45.18**	7.98	**7.98**
12-Aug-24	0.33	0.00	6.37	18.23	5.94	6.34	0.00	3.48		2.70	0.00	0.90	0.00		0.00	1.10	0.30	**45.69**	8.59	**8.59**
13-Aug-24	3.89	2.37	8.71	14.40	7.93	7.74	0.00	4.54		2.36	0.14	0.30	0.00		0.00	1.88	2.07	**56.33**	8.53	**8.53**
14-Aug-24	5.88	8.44	12.05	10.73	9.67	10.66	1.11	5.72		2.14	0.22	0.65			0.00	2.43	4.12	**73.82**	8.47	**8.47**
15-Aug-24	0.44	0.00	9.89	15.95	4.82	8.98	0.00	3.93		2.80	0.00	0.05			0.00	0.69	1.22	**48.77**	8.47	**8.47**
16-Aug-24	4.32	6.90	7.62	16.50	7.56	9.50	0.05	4.22		2.28	0.11	0.14			0.00	1.50	3.19	**63.89**	8.44	**8.44**
17-Aug-24	2.07	2.81	8.30	16.98	5.71	7.77	0.00	3.74		2.78	0.00	0.00			0.00	0.88	0.83	**51.87**	8.44	**8.44**
18-Aug-24	3.09	2.56	8.75	16.60	4.97	8.24	0.00	3.64		2.25	0.29	0.00			0.00	0.79	1.59	**52.77**	8.23	**8.23**
19-Aug-24	1.71	1.88	9.35	16.09	5.33	8.07	0.00	3.68		2.89	0.00	0.76			0.00	0.90	1.20	**51.86**	8.26	**8.26**
20-Aug-24	3.71	4.77	8.19	17.08	8.16	8.87	0.00	4.86		2.47	0.00	0.80	0.00		0.00	1.86	0.83	**61.60**	8.46	**8.46**
21-Aug-24	4.15	6.32	9.28	18.11	8.39	8.49	0.00	4.85		2.33	0.00	0.00	0.00	0.00	0.00	1.85	0.35	**64.12**	8.47	**8.47**
22-Aug-24	5.54	10.43	11.00	16.50	10.42	10.55	0.11	5.51	0.00	2.01	0.51	0.00	0.00		0.00	2.61	3.67	**78.86**	8.34	**8.34**
23-Aug-24	6.25	10.99	12.60	17.18	11.75	12.17	2.07	6.54		1.99	0.68	0.59	0.00		0.00	3.65	3.90	**90.36**	8.47	**8.47**
24-Aug-24	5.04	8.06	12.71	12.01	11.83	12.18	2.25	5.89		1.87	0.61	0.31	0.00		0.00	3.28	3.10	**79.14**	6.04	**6.04**
25-Aug-24	2.10	2.64	12.60	11.98	9.69	11.12	1.34	5.61		2.15	0.52	0.48	0.00		0.00	2.45	2.28	**64.96**	8.51	**8.51**
26-Aug-24	1.11	1.03	12.88	11.56	7.83	11.44	1.44	4.93		2.60	0.04	0.09		0.00	0.00	1.78	2.12	**58.85**	11.44	**11.44**
27-Aug-24	0.00	0.00	8.45	11.50	6.84	6.66	0.00	3.46		2.78	0.00	0.71		0.00	0.00	1.55	1.32	**43.27**	11.50	**11.50**
28-Aug-24	1.50	0.00	8.23	13.35	6.21	3.11	0.00	2.07		2.60	0.00	0.25		0.00	0.00	1.17	0.00	**38.49**	12.28	**12.28**
29-Aug-24	0.00	0.00	6.86	17.74	4.83	1.18	0.00	0.89		3.26	0.00	0.75			0.00	0.58	0.00	**36.09**	11.78	**11.78**
30-Aug-24	0.00	0.00	10.59	16.86	6.52	3.29	0.00	1.95		3.03	0.00	0.75			0.00	1.16	3.30	**47.45**	12.34	**12.34**
31-Aug-24	1.62	2.29	13.36	16.27	11.32	8.23	0.00	4.87		2.77	0.00	0.10			0.00	2.86	2.00	**65.69**	12.05	**12.05**
Total	**78.42**	**110.05**	**302.52**	**465.66**	**237.58**	**278.98**	**15.12**	**149.89**	**0.00**	**70.72**	**20.91**	**14.29**	**0.48**	**0.00**	**0.00**	**55.51**	**70.98**	**1871.11**	**270.26**	**270.26**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.2 Import-Export of NR with ER & NER during August 2024

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri Karamnasa	NR - ER 132 kV Rihand -Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Aug-24	0.00	0.42	0.00	0.00	0.00	0.00	1.60	0.00		0.00	0.00	0.16	0.00	0.90	0.44	0.00	0.00	**3.52**	0.00	**0.00**
2-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.10	0.26	0.00	0.00	**0.36**	0.00	**0.00**
3-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.08	0.11	0.00	0.00	**0.19**	0.00	**0.00**
4-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.70	0.00		0.00	0.00	0.00	0.00		0.18	0.00	0.00	**0.88**	0.00	**0.00**
5-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.27	0.00	0.00	0.00	0.00	0.00			0.28	0.00	0.00	**1.55**	0.00	**0.00**
6-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.35	0.00	0.00	**0.35**	0.00	**0.00**
7-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	2.25	0.00		0.00	0.00	0.00			0.23	0.00	0.00	**2.48**	0.00	**0.00**
8-Aug-24	0.81	0.00	0.00	0.00	0.00	0.00	3.31	0.00		0.00	0.00	0.00	0.00		0.38	0.00	0.00	**4.50**	0.00	**0.00**
9-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.50	0.00		0.00	0.00	0.00	0.00		0.39	0.00	0.00	**1.89**	0.00	**0.00**
10-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.85	0.00		0.00	0.00	0.42		0.10	0.45	0.00	0.00	**2.82**	0.00	**0.00**
11-Aug-24	1.46	4.16	0.00	0.00	0.00	0.00	2.81	0.00		0.00	0.00	0.00	0.00	0.22	0.36	0.00	0.00	**9.01**	0.00	**0.00**
12-Aug-24	0.00	3.43	0.00	0.00	0.00	0.00	2.60	0.00		0.00	0.26	0.00	0.00		0.43	0.00	0.00	**6.72**	0.00	**0.00**
13-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.18	0.00		0.00	0.00	0.00	0.00		0.46	0.00	0.00	**1.64**	0.00	**0.00**
14-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.47	0.00	0.00	**0.47**	0.00	**0.00**
15-Aug-24	0.00	2.77	0.00	0.00	0.00	0.00	1.27	0.00		0.00	0.28	0.00			0.52	0.00	0.00	**4.84**	0.00	**0.00**
16-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.49	0.00	0.00	**0.49**	0.00	**0.00**
17-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	2.32	0.00		0.00	0.31	0.53			0.54	0.00	0.00	**3.70**	0.00	**0.00**
18-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.04	0.00		0.00	0.00	0.60			0.20	0.00	0.00	**1.84**	0.00	**0.00**
19-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.21	0.00		0.00	0.38	0.00			0.73	0.00	0.00	**2.32**	0.00	**0.00**
20-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.31	0.00		0.00	0.01	0.00	0.00		0.18	0.00	0.00	**0.50**	0.00	**0.00**
21-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	2.66	0.00		0.00	0.07	0.55	0.00	0.07	0.61	0.00	0.00	**3.96**	0.00	**0.00**
22-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.02	0.00		0.50	0.00	0.00	**0.52**	0.00	**0.00**
23-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.50	0.00	0.00	**0.50**	0.00	**0.00**
24-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.47	0.00	0.00	**0.47**	0.00	**0.00**
25-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.48	0.00	0.00	**0.48**	0.00	**0.00**
26-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.46	0.00	0.00	**0.56**	0.00	**0.00**
27-Aug-24	0.48	1.34	0.00	0.00	0.00	0.00	1.21	0.00		0.00	0.33	0.00		0.08	0.39	0.00	0.00	**3.83**	0.00	**0.00**
28-Aug-24	0.00	0.90	0.00	0.00	0.00	0.00	3.50	0.00		0.00	0.07	0.00		0.05	0.47	0.00	0.10	**5.09**	0.00	**0.00**
29-Aug-24	2.78	4.28	0.00	0.00	0.00	0.00	5.10	0.00		0.00	0.65	0.00			0.48	0.00	0.90	**14.19**	0.00	**0.00**
30-Aug-24	0.78	2.75	0.00	0.00	0.00	0.00	3.43	0.00		0.00	0.22	0.00			0.42	0.00	0.00	**7.60**	0.00	**0.00**
31-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	1.40	0.00		0.00	0.18	0.00			0.57	0.00	0.00	**2.15**	0.00	**0.00**
Total	**6.31**	**20.05**	**0.00**	**0.00**	**0.00**	**0.00**	**42.52**	**0.00**	**0.00**	**0.00**	**2.76**	**2.28**	**0.00**	**1.70**	**12.80**	**0.00**	**1.00**	**89.42**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.3 Import and Export of ER with WR & NER during August 2024

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda-2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda-2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Aug-24	34.6	7.7	0.7	8.4	2.4	0.5	0.1	**54.38**	0.0	5.8	2.6	0.0	2.3	0.2	0.3	**11.18**	4.23	8.43	1.67	**14.33**	0.00	0.00	0.00	**0.00**
2-Aug-24	25.6	3.6	0.2	6.2	1.9	0.3	0.0	**37.73**	0.0	5.8	4.2	0.0	2.6	0.1	0.6	**13.46**	3.69	5.88	1.34	**10.92**	0.00	0.01	0.00	**0.01**
3-Aug-24	23.1	4.6	0.8	4.8	2.6	0.5	0.2	**36.66**	0.3	2.7	5.1	0.1	2.3	0.3	0.3	**11.11**	2.99	3.69	1.04	**7.71**	0.00	0.06	0.00	**0.06**
4-Aug-24	30.5	6.3	1.3	6.7	3.5	0.7	0.3	**49.36**	0.0	3.4	3.8	0.0	1.9	0.1	0.2	**9.42**	2.97	3.29	1.06	**7.32**	0.00	0.01	0.00	**0.01**
5-Aug-24	27.2	9.8	0.0	5.4	3.0	0.4	0.0	**45.82**	0.0	2.6	5.5	0.1	1.9	0.6	0.4	**11.19**	2.76	3.09	1.02	**6.86**	0.02	0.20	0.00	**0.22**
6-Aug-24	22.9	5.1	0.0	4.2	1.2	0.0	0.0	**33.38**	0.2	3.3	5.5	0.2	2.7	1.4	0.6	**13.83**	1.60	1.80	0.68	**4.09**	0.24	0.66	0.02	**0.92**
7-Aug-24	26.5	6.3	0.2	5.3	1.9	0.1	0.0	**40.45**	0.1	3.0	4.4	0.2	1.8	0.9	0.5	**10.98**	3.94	2.03	1.02	**6.99**	0.00	0.67	0.00	**0.67**
8-Aug-24	22.9	2.5	0.0	4.9	2.0	0.1	0.1	**32.55**	0.1	6.9	4.4	0.1	1.6	0.7	0.2	**14.10**	2.24	3.91	1.10	**7.25**	0.00	0.06	0.00	**0.06**
9-Aug-24	18.9	1.9	0.0	3.7	0.7	0.0	0.0	**25.35**	0.5	5.2	5.9	0.3	3.9	1.3	0.5	**17.80**	1.48	3.76	0.91	**6.15**	0.20	0.07	0.00	**0.28**
10-Aug-24	19.8	2.9	0.1	3.7	0.4	0.0	0.0	**26.92**	0.4	3.7	4.9	0.4	5.9	2.3	1.3	**18.94**	2.41	4.08	1.17	**7.66**	0.03	0.00	0.00	**0.03**
11-Aug-24	19.9	4.9	0.4	3.9	0.3	0.0	0.0	**29.36**	0.4	3.5	2.5	0.3	5.7	1.9	0.6	**14.73**	2.75	2.94	1.07	**6.76**	0.00	0.05	0.00	**0.05**
12-Aug-24	16.8	6.6	0.0	2.7	0.2	0.0	0.0	**26.34**	0.8	1.4	3.5	0.6	6.9	1.3	0.8	**15.22**	2.39	1.47	0.78	**4.64**	0.08	0.71	0.01	**0.80**
13-Aug-24	14.6	4.1	0.0	1.8	0.0	0.0	0.0	**20.62**	0.4	3.4	5.1	0.6	9.7	2.6	0.5	**22.38**	3.30	5.19	1.16	**9.65**	0.02	0.18	0.00	**0.19**
14-Aug-24	15.1	1.2	0.0	1.9	0.0	0.0	0.0	**18.21**	0.6	5.7	4.8	0.8	8.3	2.0	0.6	**22.79**	4.44	7.39	1.55	**13.38**	0.00	0.00	0.00	**0.00**
15-Aug-24	25.3	3.3	0.4	4.8	0.6	0.0	0.4	**34.75**	0.0	4.2	2.7	0.1	5.6	1.0	0.3	**13.93**	2.98	3.77	0.97	**7.72**	0.00	0.03	0.01	**0.05**
16-Aug-24	21.5	2.7	0.0	3.2	0.0	0.0	0.0	**27.55**	0.0	4.3	4.3	0.2	5.7	1.1	0.4	**16.03**	2.51	3.02	0.85	**6.39**	0.12	0.33	0.01	**0.46**
17-Aug-24	27.8	1.4	0.0	4.3	0.1	0.0	0.0	**33.58**	0.0	5.7	3.9	0.1	6.6	1.6	0.4	**18.35**	3.91	4.99	1.28	**10.17**	0.00	0.00	0.00	**0.00**
18-Aug-24	19.4	2.6	0.0	3.0	0.2	0.0	0.1	**25.32**	0.2	4.8	4.5	0.5	7.2	1.6	0.3	**19.08**	3.01	3.74	1.03	**7.78**	0.07	0.17	0.00	**0.24**
19-Aug-24	16.2	4.5	0.0	1.8	0.2	0.0	0.0	**22.80**	0.2	5.2	5.3	0.6	6.9	1.3	0.5	**20.01**	2.12	2.50	0.73	**5.36**	0.17	0.53	0.00	**0.70**
20-Aug-24	14.2	3.1	0.0	1.2	0.0	0.0	0.0	**18.48**	0.7	7.2	5.6	1.3	9.0	1.4	0.7	**25.82**	0.39	0.36	0.11	**0.87**	0.70	1.59	0.23	**2.52**
21-Aug-24	17.5	1.4	0.0	1.4	0.0	0.0	0.0	**20.23**	0.1	8.1	5.2	0.8	10.2	1.8	0.8	**27.07**	1.24	1.00	0.36	**2.60**	1.00	2.06	0.29	**3.35**
22-Aug-24	17.6	0.6	0.0	1.6	0.0	0.0	0.0	**19.84**	0.1	11.4	4.3	0.8	9.2	2.3	0.8	**28.93**	2.05	2.12	0.71	**4.88**	0.17	0.59	0.02	**0.78**
23-Aug-24	17.0	1.7	0.0	2.1	0.1	0.0	0.0	**20.99**	0.4	6.1	3.4	0.7	6.7	1.3	0.6	**19.17**	3.10	3.16	1.09	**7.35**	0.11	0.37	0.00	**0.48**
24-Aug-24	22.0	1.5	0.5	4.1	1.0	0.3	0.1	**29.54**	0.3	5.9	1.9	0.3	4.0	0.7	0.4	**13.49**	2.26	3.59	1.05	**6.91**	0.12	0.18	0.01	**0.31**
25-Aug-24	32.9	1.0	1.3	6.4	1.3	0.1	0.1	**43.24**	0.0	7.7	1.4	0.0	3.3	0.7	0.2	**13.41**	3.26	5.46	1.29	**10.01**	0.00	0.00	0.00	**0.00**
26-Aug-24	33.7	1.1	0.9	6.4	1.5	0.2	0.2	**44.01**	0.0	9.5	3.1	0.0	3.6	1.1	0.4	**17.79**	4.75	7.71	1.81	**14.27**	0.00	0.00	0.00	**0.00**
27-Aug-24	29.0	4.8	0.7	5.3	1.0	0.3	0.2	**41.25**	0.0	2.6	3.1	0.0	5.3	1.0	0.4	**12.39**	6.45	9.56	2.09	**18.11**	0.00	0.00	0.00	**0.00**
28-Aug-24	28.2	3.3	0.2	4.7	0.6	0.1	0.0	**37.06**	0.0	5.6	4.6	0.1	7.0	1.3	0.5	**19.10**	7.29	10.16	2.20	**19.64**	0.00	0.00	0.00	**0.00**
29-Aug-24	32.4	6.7	0.4	5.4	0.5	0.1	0.2	**45.60**	0.0	3.9	4.2	0.2	6.7	1.2	0.3	**16.50**	8.27	10.38	2.34	**20.99**	0.00	0.00	0.00	**0.00**
30-Aug-24	37.6	2.2	0.0	6.5	0.6	0.1	0.1	**47.20**	0.0	10.2	4.9	0.1	6.1	1.2	0.2	**22.68**	8.67	10.90	2.51	**22.08**	0.00	0.00	0.00	**0.00**
31-Aug-24	37.3	0.2	0.1	6.5	0.5	0.0	0.0	**44.64**	0.0	16.5	4.7	0.0	6.3	1.8	0.7	**29.97**	6.28	7.28	1.79	**15.36**	0.00	0.00	0.00	**0.00**
Total	**747.98**	**110.03**	**8.20**	**132.26**	**28.29**	**4.06**	**2.41**	**1033.22**	**5.93**	**175.21**	**129.22**	**9.58**	**167.11**	**38.33**	**15.46**	**540.85**	**109.75**	**146.64**	**37.80**	**294.19**	**3.04**	**8.53**	**0.61**	**12.19**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 से मार्च 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
कुल Total	**137.84**	**3061.61**	**638.42**	**1139.69**	**3525.78**	**0.00**	**4.14**	**0.00**

* Based on daily operational data

16.1 Import from neighbouring countries during Aug 2024

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Aug-24	23.38	0.00	0.86	0.00	6.24	9.46	1.35	0.72	0.00	0.00	1.35	14.36	0.02	0.00
2-Aug-24	19.90	0.00	0.32	0.00	6.47	9.80	1.31	0.69	0.00	0.00	1.33	13.65	0.04	0.00
3-Aug-24	15.28	4.03	0.00	1.15	7.10	10.69	1.24	0.82	0.00	0.00	1.18	15.04	0.15	0.00
4-Aug-24	17.41	4.63	0.00	1.37	6.95	10.47	1.33	0.78	0.00	0.00	0.85	13.41	0.02	0.00
5-Aug-24	16.30	5.30	0.00	1.69	6.94	10.46	1.24	0.79	0.00	0.00	1.33	12.22	0.00	0.00
6-Aug-24	15.50	6.34	0.00	1.27	7.35	11.14	1.02	0.37	0.00	0.00	1.39	13.60	0.00	0.00
7-Aug-24	14.79	5.77	0.00	1.67	3.02	4.57	0.99	0.27	0.00	0.00	1.41	15.47	0.00	0.00
8-Aug-24	15.55	5.70	0.00	1.62	5.63	8.52	0.92	0.40	0.00	0.00	1.34	12.88	0.00	0.00
9-Aug-24	16.66	5.10	0.00	1.40	6.76	10.21	1.23	0.73	0.00	0.00	1.38	15.37	0.00	0.00
10-Aug-24	17.34	4.60	0.00	1.34	7.11	10.76	1.26	0.63	0.00	0.00	1.46	14.97	0.00	0.00
11-Aug-24	16.87	4.46	0.00	1.37	6.79	10.30	1.39	0.78	0.00	0.00	1.12	11.17	0.00	0.00
12-Aug-24	17.36	4.63	0.00	0.74	5.36	8.10	1.31	0.62	0.00	0.00	1.31	15.71	0.00	0.00
13-Aug-24	17.46	4.67	0.00	0.72	6.79	10.23	1.44	0.82	0.00	0.00	1.25	13.12	0.00	0.00
14-Aug-24	17.39	4.62	0.00	0.66	6.58	10.39	1.27	0.96	0.00	0.00	1.15	15.70	0.00	0.00
15-Aug-24	17.09	4.44	0.00	0.97	7.01	10.64	0.88	1.02	0.00	0.00	1.33	14.74	0.00	0.00
16-Aug-24	17.14	4.47	0.00	1.29	6.94	10.55	1.28	0.83	0.00	0.00	1.33	14.84	0.00	0.00
17-Aug-24	16.61	4.73	0.00	1.49	6.38	10.94	1.42	0.92	0.00	0.00	1.39	16.02	0.00	0.00
18-Aug-24	16.56	5.07	0.00	1.53	6.86	10.38	1.44	0.82	0.00	0.00	1.44	16.07	0.00	0.00
19-Aug-24	16.95	4.47	0.23	1.13	6.90	10.43	1.30	0.78	0.00	0.00	1.45	16.47	0.00	0.00
20-Aug-24	17.10	4.56	1.30	0.55	7.00	10.57	1.10	0.70	0.00	0.00	1.46	16.07	0.00	0.00
21-Aug-24	16.92	4.45	1.30	0.58	6.39	9.63	1.24	0.62	0.00	0.00	1.43	16.04	0.00	0.00
22-Aug-24	16.76	4.36	1.67	0.52	6.44	9.71	1.37	0.67	0.00	0.00	1.44	15.92	0.00	0.00
23-Aug-24	16.80	4.37	1.51	0.71	5.87	8.85	1.44	0.74	0.00	0.00	1.40	15.98	0.00	0.00
24-Aug-24	16.80	4.38	1.36	0.83	6.39	9.65	1.50	0.76	0.00	0.00	1.35	16.15	0.00	0.00
25-Aug-24	16.70	4.31	1.41	0.72	6.58	9.94	1.54	0.78	0.00	0.00	1.30	15.30	0.00	0.00
26-Aug-24	16.38	4.22	1.74	0.49	6.40	9.66	1.45	0.83	0.00	0.00	1.37	14.32	0.00	0.00
27-Aug-24	16.02	4.01	1.75	0.67	5.56	8.39	1.27	0.82	0.00	0.00	1.52	15.52	0.00	0.00
28-Aug-24	14.45	3.53	1.43	0.87	5.36	8.11	1.46	0.73	0.00	0.00	1.44	15.65	0.00	0.00
29-Aug-24	15.02	3.64	1.14	1.01	5.10	7.75	1.47	0.70	0.00	0.00	1.43	17.22	0.00	0.00
30-Aug-24	14.33	3.46	1.27	1.08	5.05	7.61	0.90	0.96	0.00	0.00	1.33	16.63	0.00	0.00
31-Aug-24	11.60	3.23	1.13	0.73	5.11	7.72	1.43	0.68	0.00	0.00	1.34	17.04	0.00	0.00
Total	**514.44**	**131.53**	**18.42**	**30.16**	**194.42**	**295.61**	**39.79**	**22.74**	**0.00**	**0.00**	**41.60**	**466.65**	**0.23**	**0.00**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

16.2 Export to neighbouring countries during Aug 2024

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Aug-24	0.00	3.15	0.00	1.15	0.00	0.00	0.00	0.00	22.40	1.81	0.00	0.00	0.00	0.03
2-Aug-24	0.00	1.60	0.00	0.63	0.00	0.00	0.00	0.00	22.45	1.59	0.00	0.00	0.00	0.03
3-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.02	1.70	0.00	0.00	0.00	0.03
4-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.16	1.80	0.00	0.00	0.00	0.03
5-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.28	1.81	0.00	0.00	0.00	0.03
6-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.34	1.78	0.00	0.00	0.00	0.03
7-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.92	2.00	0.00	0.00	0.00	0.03
8-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.54	2.01	0.00	0.00	0.00	0.03
9-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.25	1.84	0.00	0.00	0.00	0.03
10-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.26	1.85	0.00	0.00	0.00	0.03
11-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.98	1.85	0.00	0.00	0.00	0.04
12-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.18	1.65	0.00	0.00	0.00	0.02
13-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.05	1.97	0.00	0.00	0.00	0.03
14-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.76	2.26	0.00	0.00	0.00	0.03
15-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.13	2.27	0.00	0.00	0.00	0.03
16-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.37	1.88	0.00	0.00	0.00	0.03
17-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.42	1.23	0.00	0.00	0.00	0.00
18-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.53	1.39	0.00	0.00	0.00	0.02
19-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.74	1.33	0.00	0.00	0.00	0.02
20-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.15	1.30	0.00	0.00	0.00	0.03
21-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.10	1.08	0.00	0.00	0.00	0.03
22-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.86	0.81	0.00	0.00	0.00	0.03
23-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.10	1.28	0.00	0.00	0.00	0.03
24-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.43	1.37	0.00	0.00	0.00	0.03
25-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.76	1.23	0.00	0.00	0.00	0.03
26-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.73	1.16	0.00	0.00	0.00	0.03
27-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.88	1.23	0.00	0.00	0.00	0.03
28-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.88	1.37	0.00	0.00	0.00	0.03
29-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.14	1.60	0.00	0.00	0.00	0.03
30-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.09	1.49	0.00	0.00	0.00	0.03
31-Aug-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.58	1.58	0.00	0.00	0.00	0.03
Total	**0.00**	**4.75**	**0.00**	**1.78**	**0.00**	**0.00**	**0.00**	**0.00**	**664.48**	**49.52**	**0.00**	**0.00**	**0.00**	**0.87**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – अगस्त 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - AUGUST 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

अगस्त 2024 AUGUST 2024			Apr'24- Aug'24	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	807	5737	4025	19060
प.क्षे. WR	363	396	1836	3087
द.क्षे. SR	389	505	1829	7415
पू.क्षे. ER	317	2083	1836	8790
पूर्वोत्तर क्षे. NER	54	101	447	349
कुल TOTAL	1930	8822	9973	38701

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
कुल TOTAL	44314	42560	9973	38701

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
29.07.24 to 04.08.24	132.33	305.78	371.92	220.85	35.41
05.08.24 to 11.08.24	61.15	218.32	271.84	160.79	26.32
12.08.24 to 18.08.24	335.48	257.39	364.11	223.29	39.28
19.08.24 to 25.08.24	182.63	220.45	222.29	137.15	26.38

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अगस्त 2024
EXCHANGES THROUGH POWER EXCHANGES -AUGUST 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED		96.69	0.00
2	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		29.46	0.00
3	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		8.96	0.00
4	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		36.36	0.00
5	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED (infirm)		3.11	0.00
6	Adept Renewable Technologies Private Limited		25.93	0.00
7	Amp Energy Green Six Private Limited		20.70	0.00
8	Amplus Ages Private Limited		9.32	0.00
9	Ayana Renewable Power Three Private Limited Infirm		12.91	0.00
10	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		9.38	0.00
11	Chandigarh (UT)		24.95	6.37
12	Delhi		263.48	136.91
13	Government of Himachal Pradesh _ Chamera1HEP		29.51	2.70
14	Government of Himachal Pradesh _ Chamera3HEP		15.72	0.70
15	Government of Himachal Pradesh_ CHAMERA2HEP		18.82	0.76
16	Government of Himachal Pradesh_BairasuilHEP		7.73	2.06
17	Government of Himachal Pradesh_Koldam HEP		17.07	1.80
18	Government of Himachal Pradesh_NJHPS		30.70	0.23
19	Government of Himachal Pradesh_Parbati3HEP		12.23	1.51
20	Government of Himachal Pradesh_RampurHEP		30.56	0.08
21	Grian Energy Private Limited		21.16	0.00
22	Haryana		234.12	135.08
23	Himachal Pradesh		280.96	33.41
24	IGSTPS JHAJJAR		4.62	0.00
25	Jammu Kashmir		197.12	5.85
26	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		138.47	0.00
27	NEA Nepal Upper Chameliya Hydropower Project		26.83	0.00
28	NEA Nepal Upper Kalangagad Hydropower Project new		17.24	0.00
29	NTPC Dadri Stage I	उत्तरी क्षेत्र NR	0.83	0.00
30	NTPC Dadri Stage II		4.66	0.00
31	NTPC Rihand stage I		11.62	0.00
32	NTPC Rihand stage II		11.38	0.00
33	NTPC Rihand stage III		12.62	0.00
34	NTPC Singrauli		17.55	0.00
35	NTPC Tanda Stage II		8.74	0.00
36	NTPC Unchahar Stage I		2.05	0.00
37	NTPC Unchahar Stage II		4.88	0.00
38	NTPC Unchahar Stage III		1.67	0.00
39	NTPC Unchahar Stage IV		4.97	0.00
40	North Central Railway Prayagraj		0.00	38.93
41	Onevolt Energy Private Limited		9.80	0.00
42	Punjab		136.20	1050.64
43	RENEW SURYA PRATAP PRIVATE LIMITED		36.64	0.00
44	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.38	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अगस्त 2024
EXCHANGES THROUGH POWER EXCHANGES -AUGUST 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	Rajasthan		353.64	127.94
46	ReNew Surya Ravi Private Limited		38.52	0.00
47	SHREE CEMENT LIMITED TPS		45.56	0.00
48	Sainj HEP		44.78	1.43
49	Serentica Renewables India 4 Private Limited		2.70	0.00
50	Singoli Bhatwari HEP		51.75	2.43
51	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		15.62	0.00
52	TPSL 200MW TPTCL Banderwala		17.26	0.00
53	TPSL Banderwala SECI 100_INF		4.54	0.00
54	Transition Energy Services Private Limited		16.35	0.00
55	Transition Green Energy Private Limited		22.51	0.00
56	Uttar Pradesh		256.68	566.35
57	Uttarakhand		34.30	131.93
58	ACB (INDIA) LIMITED		47.24	1.09
59	ADANI GREEN ENERGY TWENTY SIX A LIMITED_infirm		0.49	0.00
60	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_Infirm		16.97	0.00
61	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_infirm		77.85	0.00
62	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		129.55	0.00
63	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		88.37	0.00
64	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		11.85	0.00
65	Adani Green Energy Twenty Five A Limited_Infirm		13.24	0.00
66	Adani Green Energy Twenty Five B Limited_infirm		87.26	0.00
67	Adani Green Energy Twenty Six B Limited_infirm		17.47	0.00
68	Adani Power Limited - Raigarh TPP		70.99	0.00
69	Adani Power Limited-Raipur TPP		161.66	1.93
70	ArcelorMittal Nippon Steel India Limited		0.00	151.20
71	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	55.58
72	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		3.88	0.00
73	Chhattisgarh		218.20	61.67
74	D B Power Limited		137.40	0.00
75	DGEN MEGA POWER PROJECT		5.77	0.00
76	DHARIWAL STU OTH		0.71	0.00
77	Daman and Diu - Dadra and Nagar Haveli		0.45	285.06
78	Dhariwal ISTS		0.57	0.00
79	GMR Warora Energy Limited		4.23	0.00
80	Goa WR		8.63	18.64
81	Gujarat		71.67	682.93
82	Jaypee Nigrie Super Thermal Power Plant		74.44	0.00
83	Jhabua Power Limited		39.31	5.20
84	Jindal Power Limited, Stage-1		102.19	4.89
85	Jindal Power Limited, Stage-2		188.26	19.88
86	Jindal Steel & Power Ltd , DCPP		45.72	7.29
87	MAHAN ENERGEN LIMITED U#1		151.52	1.71
88	MAHAN ENERGEN LIMITED U#2	पश्चिमी क्षेत्र WR	15.79	15.11

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अगस्त 2024
EXCHANGES THROUGH POWER EXCHANGES -AUGUST 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
89	MB POWER (MADHYA PRADESH) LIMITED	चौथी फील्ड WR	7.46	39.53
90	Madhya Pradesh		431.72	70.25
91	Maharashtra		100.64	565.67
92	Maruti Clean Coal and Power Limited		7.18	0.48
93	NREL-Dayapar Wind		11.13	0.00
94	NTPC Gadarwara		6.92	0.00
95	NTPC Jhanor Gandhar GPS		0.00	0.76
96	NTPC Kawas GPS		0.00	0.68
97	NTPC Korba Stage I &II		19.27	0.00
98	NTPC Korba Stage III		6.46	0.00
99	NTPC Lara Stage I		14.55	0.00
100	NTPC Mouda Stage I		3.15	0.00
101	NTPC Mouda Stage II		5.33	0.00
102	NTPC SAIL POWER COMPANY LIMITED		0.12	0.00
103	NTPC Sipat Stage I		25.33	0.00
104	NTPC Sipat Stage II		14.97	0.00
105	NTPC Solapur		2.88	0.00
106	NTPC Vindhyachal Stage I		10.90	0.00
107	NTPC Vindhyachal Stage II		12.47	0.00
108	NTPC Vindhyachal Stage III		10.35	0.00
109	NTPC Vindhyachal Stage IV		16.55	0.00
110	NTPC Vindhyachal Stage V		6.53	0.00
111	NTPC khargone		7.40	0.00
112	Nani Virani Wind Energy Private Limited		3.89	0.00
113	R.K.M POWERGEN PRIVATE LIMITED		7.78	0.00
114	Ratnagiri Gas & Power Private Limited		0.00	1.15
115	SKS Power Generation Chhattisgarh Limited		65.88	0.09
116	Sasan Power Limited		40.64	0.00
117	TRN ENERGY PRIVATE LIMITED		23.21	0.00
118	The Tata Power Co Ltd (MTPS)		21.36	0.36
119	WIND FIVE RENERGY LIMITED		10.53	0.00
120	Andhra Pradesh		118.95	582.39
121	COASTAL ENERGEN PRIVATE LIMITED		4.15	0.00
122	Goa SR		0.01	13.80
123	IL&FS TAMIL NADU POWER COMPANY LIMITED		40.49	0.00
124	JINDAL POWER LIMITED SIMHAPURI		16.04	0.45
125	JSW RENEW ENERGY TWO LIMITED INFIRM		0.06	0.00
126	Karnataka		621.17	78.67
127	Kerala		21.42	235.38
128	MEENAKSHI ENERGY LIMITED		24.18	1.59
129	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		3.56	0.00
130	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		3.76	0.00
131	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.76	0.00
132	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		1.31	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अगस्त 2024
EXCHANGES THROUGH POWER EXCHANGES -AUGUST 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
133	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II	दक्षिणी क्षेत्र SR	3.76	0.00
134	NLC Tamilnadu Power Limited		15.05	0.00
135	NTECL VALLUR		1.07	0.00
136	NTPC KUDGI		4.44	0.00
137	NTPC Ramagundam Stage I &II		2.33	0.00
138	NTPC Ramagundam Stage III		0.97	0.00
139	NTPC Simhadri Stage I		1.33	0.00
140	NTPC Simhadri Stage II		3.93	0.00
141	NTPC Talcher Super Thermal Power Station Stage II		13.73	0.00
142	NTPC Telangana		6.97	0.00
143	OSTRO KANNADA POWER PRIVATE LIMITED		31.42	0.00
144	Pondicherry UT		14.17	0.84
145	RENEW SURYA OJAS PRIVATE LIMITED-Wind		90.38	0.00
146	RENEW SURYA OJAS PRIVATE LIMITED_INFIRM		7.58	0.00
147	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		5.66	0.00
148	Ramagundam Floating solar		4.46	0.00
149	SEIL ENERGY INDIA LIMITED		76.96	0.00
150	SEIL Energy India Limited Project II		7.85	0.00
151	Serentica Renewables India 1 Private Limited		4.76	0.00
152	Serentica Renewables India 1 Private Limited- Koppal (Infirm)		4.25	0.00
153	Simhadri FSP 15 MW		2.33	0.00
154	Simhadri Floating solar (10 MW)		1.27	0.00
155	Tamil Nadu		265.59	363.39
156	Telangana		43.65	2638.12
157	Jharkhand	पूर्वी क्षेत्र ER	51.79	53.46
158	Jindal India Thermal Power Limited		211.32	0.00
159	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		88.59	0.00
160	KANTI BIJLEE UTPADAN NIGAM LIMITED		14.83	0.00
161	Kabeli B-1 Hydro Power Project NEPAL ELECTRICITY AUTHORITY		18.00	0.00
162	LIKHU-iV NEA		37.93	0.00
163	Lower Modi Hydro Power Project NEPAL ELECTRICITY AUTHORITY		14.42	0.00
164	MAITHON POWER LIMITED		4.99	0.00
165	MARSYANGDI NEPAL ELECTRICITY AUTHORITY		49.76	0.00
166	NABINAGAR POWER GENERATING COMPANY LIMITED		56.17	0.00
167	NEA Nepal Upper Balephi A Hydropower Project1		25.93	0.00
168	NEA Nepal Upper Dordi A Hydropower Project		17.99	0.00
169	NEPAL ELECTRICITY AUTHORITY-MIDDLE MARSYANGDI		49.38	0.00
170	NTPC BARH Stage I		3.18	0.00
171	NTPC BARH Stage II		21.35	0.00
172	NTPC Darlipali		4.52	0.00
173	NTPC Farakka stage I		42.43	0.00
174	NTPC Farakka stage III		13.09	0.00
175	NTPC Kahalgaon stage I		12.10	0.00
176	NTPC Kahalgaon stage II		18.08	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अगस्त 2024
EXCHANGES THROUGH POWER EXCHANGES -AUGUST 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
177	NTPC North Karanpura STPS		29.11	0.00
178	NTPC Talcher Stage I		20.79	0.00
179	NTPP BRBCL		9.83	0.00
180	Nikachhu Hydropower Project		20.55	0.00
181	Odisha		304.40	245.02
182	Sikkim		18.78	12.47
183	Solu Hydropower Project NEPAL ELECTRICITY AUTHORITY		16.96	0.00
184	TRISHULI NEPAL ELECTRICITY AUTHORITY		17.25	0.00
185	Tashiding HEP, Shiga Energy Private Limited		1.21	0.00
186	West Bengal		89.04	332.38
187	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	0.74	0.00
188	ASSAM GAS BASED POWER STATION		1.44	0.00
189	Arunachal Pradesh		41.53	0.00
190	Assam		112.64	118.40
191	Bongaigaon Thermal Power Station NTPC		9.86	0.00
192	KAMENG HYDRO POWER STATION		0.48	0.00
193	Manipur		9.45	7.40
194	Meghalaya		53.86	8.09
195	Mizoram		23.45	0.00
196	Nagaland		6.53	0.06
197	Palatana Plant		7.20	0.00
198	Tripura		16.41	8.40
Total			8516	8939

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : AUGUST 2024

RE Source & Unit wise break up (01.08.2024-31.08.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	0	0	6	2
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	3	3	72	8
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**3**	**3**	**78**	**10**

RECs Issued (01.08.2024-31.08.2024)

Sr.No.	Non Solar	Solar	Total
1	17862312	163770	18026082

Redemption of REC (01.08.2024-31.08.2024)

Sr.No.	Non Solar	Solar	Total
1	4039773	34590	4074363

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : AUGUST 2024

RE Source & Unit wise break up (Apr'24-Aug'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	19	4	20	5
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	95	16	89	14
5	Small Hydro	24	1	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**138**	**21**	**145**	**21**

RECs Issued (Apr'24-Aug'24)

Sr.No.	Non Solar	Solar	Total
1	26363627	424391	26788018

Redemption of REC (Apr'24-Aug'24)

Sr.No.	Non Solar	Solar	Total
1	12713644	165220	12878864

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : AUGUST 2024

RE Source & Unit wise break up Since Inception to Aug'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3152	534	2997	536
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	1730	590	1561	494
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**6992**	**1298**	**6215**	**1167**

RECs Issued since Inception to Aug'24

Sr.No.	Non Solar	Solar	Total
1	141468665	13964769	155433434

Redemption of REC since Inception to Aug'24

Sr.No.	Non Solar	Solar	Total
1	91217973	12614477	103832450

REC Closing balance as on 31.08.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of Aug 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	Rajasthan	01-08-2024 09:38	01-08-2024 14:46	05:08	143	0	0.272	0.000	52615	61649	i)220kV ABC Renewables(IP) has double main bus scheme at 220kV level. ii)During antecedent condition, loading of 220/33 kV 150 MVA ICT-1 & 2 were approx. 72 & 72 MW respectively (as per SCADA). iii)As reported, at 09:38 hrs, sparking occurred in LV cables of ICT-1 at ABC Renewables(IP) S/s which led to failure of LV cables and caused R-N phase to earth fault. On this fault ICT-1 tripped at ABC Renewables(IP) S/s (details of type of protection operated is yet to be received). iv)As per PMU at ABC Renewables(IP), R-N phase to earth fault with fault clearance time of 80msec is observed. v)As reported, due to nearby sparking in cables, for the safety of ICT-2 and remaining LV cables, ICT-2 hand tripped at ABC Renewables(IP) S/s. vi)During this event, dip in NR solar generation of approx. 120 MW is observed (As per SCADA). vii)As per SCADA, no change in demand is observed in Rajasthan control area. viii)As per SCADA, loss in solar generation of approx. 143MW is observed at 220kV ABC Renewables(IP) S/s.	1)220/33 kV 150 MVA ICT 1 at ABCRenew_RJ01_SL_BHD2_PG 2)220/33 kV 150 MVA ICT 2 at ABCRenew_RJ01_SL_BHD2_PG
2	GI-1	Jammu and Kashmir	02-08-2024 15:03	02-08-2024 15:35	00:32	0	345	0.000	0.498	51533	69320	i)As reported, at 15:03hrs, 220/132kV 160MVA ICT-1, 132kV Barn-Canal (JK) D/C tripped at Barn(JK) S/s on Y-B phase to phase fault which occurred on 132kV Barn-Canal (JK) D/C (exact reason, location of fault and type of protection operated is yet to be received). ii)As reported, due to tripping of ICT-1, the complete load shifted on 220/132kV 160MVA ICT-2 & 3 which led to tripping of 220/132kV 160MVA ICT-2 & 3 on overloading at Barn(JK) S/s. iii)As per PMU at Kishenpur(PG), Y-B phase to phase fault with fault clearing time of 120ms is observed. iv)As per SCADA, load loss of approx. 345MW occurred in J&K control area.	1)220/132kV 160MVA ICT-1 at Barn (JK) 2)220/132kV 160MVA ICT-2 at Barn (JK) 3)220/132kV 160MVA ICT-3 at Barn (JK) 4)132kV Barn-Canal (JK) Ckt-1 5)132kV Barn-Canal (JK) Ckt-2
3	GI-2	Punjab	07-08-2024 11:26	07-08-2024 12:48	01:22	0	30	0.000	0.044	57445	68389	i)400/220kV Patiala(PG) has double main and transfer bus arrangement at 220kV side. ii)During antecedent condition, loading of 400/220 315 MVA ICT-1 & 2 and 400/220 kV 500 MVA ICT-3 & 4 at Patiala(PG) were approx. 170 MW, 170 MW, 265 MW & 260 MW respectively. 220kV lines from Patiala(PG) to Nabha(PS) Ckt-2, Bahadurgarh(PS) Ckt-2 & Ablowal(PS) Ckt-2 and 400/220 kV 500 MVA ICT-4 & 400/220 kV 315 MVA ICT-2 were connected to 220kV Bus-2 at Patiala(PG) S/s. iii)As reported, at 11:26 hrs, during shifting of 400/220 kV 500 MVA ICT-4 from 220kV Bus-2 to 220kV transfer bus, protection switchover of ICT-4 bay was not successful and bus bar protection relay of 220kV Bus-2 maloperated due to wiring related issues. (Exact reason of bus bar protection maloperation is yet to be received). iv)Due to bus bar protection, all the elements connected to 220kV Bus-2 at Patiala(PG) tripped. v)As per PMU at Patiala(PG), fluctuation in voltage and no fault in system is observed. vi)As per SCADA, change in demand of approx. 30 MW in Punjab control area.	1)400/220 kV 500 MVA ICT 4 at Patiala(PG) 2)400/220 kV 315 MVA ICT 2 at Patiala(PG) 3)220 KV Patiala(PG)-Nabha(PS) (PSTCL) Ckt-2 4)220 KV Patiala(PG)-Ablowal(PS) (PSTCL) Ckt-2 5)220 KV Bahadurgarh(PS)-Patiala(PG) (PSTCL) Ckt-2 6)220KV Bus 2 at Patiala(PG)
4	GD-1	Uttar Pradesh & Uttarakhand	11-08-2024 18:25	11-08-2024 19:00	00:35	0	120	0.000	0.221	46027	54199	i)220kV Nara(UP) has main and transfer bus scheme at 220kV leel.(i) During antecedent condition, loading at Nara(UP) S/s was approx. 80 MW. Loading of 220/132kV 160 MVA ICT-1 & 220/132kV 200 MVA ICT-2 at Nara(UP) S/s were approx. 35 MW and 45 MW respectively. (iii) As reported, at 18:25 hrs, 220 KV Meerut(PG)-Nara(UP) (PG) Ckt tripped from Meerut(PG) end on B-N phase to earth fault with fault distance of 10.5 km (33.02%) from Meerut(PG) end with fault current of Ib=14.05k.iv) On this fault, B-phase pole of CB of 220 KV Meerut(PG)-Nara(UP) (PG) Ckt at Nara(UP) end got stuck and could not open properly. On this, LBB of Meerut bay at Nara(UP) S/s operated which led to tripping of 220kV line from Nara(UP) to Roorkee(UK), 200/132kV 160 MVA ICT-1 and 200 MVA ICT-2 at Nara(UP) S/s.v) As reported, during inspection (at Nara(UP) S/s) it was found that tripping command was issued to both 220kV Muzaffarnagar and 220kV Jansath bay also but their breakers were not tripped (cable found broken) hence both these lines were tripped from other end in zone -3. vi) As per PMU at Muzaffarnagar(UP), B-N phase to earth fault with delayed fault clearance time of 1240msec is observedvii) As per DR of Meerut end of 220 KV Meerut(PG)-Nara(UP) (PG) Ckt, B-N phase to earth fault with fault current of Ib=~12.3kA with unsuccessful A/R operation is observed. Zone-1 distance protection operated from Meerut(PG) end.viii)Due to LBB operation at Nara(UP) S/s and tripping of 220 KV Nara-Jansath (UP) Ckt & 220 KV Nara-Muzaffarnagar (UP) Ckt from remote ends, Nara(UP) S/s lost its connectivity from Grid which led to blackout at 220kV Nara(UP) S/s. ix)As reported, no fault record found at Nara(UP) S/s. During inspection, it was found that DC main fuse of relay panel was blown off. x)As per SCADA, change in demand of approx. 70 MW & 40 MW in UP and Uttarakhand control area respectively. However, SLDC-UP has reported load loss of approx. 80 MW at Nara(UP) S/s.	1)220 KV Meerut(PG)-Nara(UP) (PG) Ckt 2)220 KV Nara(UP)-Roorkee(UK) (UP) Ckt 3)220 KV Nara-Jansath (UP) Ckt 4)220 KV Nara-Muzaffarnagar (UP) Ckt 5)220/132kV 160MVA ICT-1 at Nara(UP) 6)220/132kV 200MVA ICT-2 at Nara(UP)
5	GD-1	Rajasthan	14-08-2024 16:12	14-08-2024 16:33	00:21	60	150	0.111	0.222	54124	67666	i)During antecedent condition, 220 kV Anta-Sakatpura (RS) Ckt was not in service. 110 MW Kota TPS - UNIT 1 was generating approx. 60 MW. ii)As reported, at 16:12 hrs, Y-ph CT of 220 kV RAPS_A(NP)-Sakatpura (RS) (RS) Ckt-1 at Sakatpura(RS) end damaged and created bus fault at 220kV buses of Sakatpura(RS). iii)Due to this, busbar protection of both the 220kV buses at Sakatpura(RS) operated and all the elements connected to the buses tripped and complete blackout occurred at Sakatpura(RS). iv)132kV feeder to Ranpur from Sakatpura also tripped. (Exact reason yet to be shared) All other 132kV feeders were hand-tripped after loss of supply. v)During the same time, 220 KV Kota(PG)-KTPS(RVUN) (RS) Ckt-1 also tripped on Y-N phase to earth fault sensing in zone-2 from Kota(PG) end. Also, 110 MW Kota TPS - UNIT 1 tripped (exact nature of protection operated yet to be shared). vi)As per PMU at Kota(PG), Y-N phase to ground fault converted to R-Y-N double phase to ground fault is observed with delayed fault clearing time of 200 ms. vii)As per SCADA, generation loss of approx. 60 MW is observed at KTPS. viii)As reported by SLDC Rajasthan, load loss of approx. 150 MW occurred in Rajasthan control area.	1) 220 kV RAPS_A(NP)-Sakatpura(RS) (RS) Ckt-1 2) 220 kV RAPS_A(NP)-Sakatpura(RS) (RS) Ckt-2 3) 220 kV RAPS_B(NP)-Sakatpura(RS) (RS) Ckt 4) 220 kV KTPS-Sakatpura (RS) Ckt-1 5) 220 kV KTPS-Sakatpura (RS) Ckt-2 6) 220 kV KTPS-Sakatpura (RS) Ckt-3 7) 220 kV KTPS-Sakatpura (RS) Ckt-4 8) 220 kV Sakatpura-Ranpur (RS) Ckt 9) 220 kV Sakatpura-Dahara (RS) Ckt 10) 220 kV Sakatpura-Mandalgarh (RS) Ckt 11) 220/132kV 160 MVA ICT-1 at Sakatpura(RS) 12) 220/132kV 100 MVA ICT-2 at Sakatpura(RS) 13) 220/132kV 100 MVA ICT-3 at Sakatpura(RS) 14) 220/132kV 100 MVA ICT-4 at Sakatpura(RS) 15) 220 kV Kota(PG)-KTPS(RVUN) (RS) Ckt-1 16) 110 MW Kota TPS - UNIT 1

Details of Grid Events during the Month of Aug 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
6	GD-1	Delhi	18-08-2024 04:53	18-08-2024 05:35	00:42	0	144	0.000	0.233	47934	61849	i)220kV Najafgarh(DTL) has double main bus arrangement at 220kV level. ii)During antecedent condition, 220/66kV 160 MVA ICT-3 & 5 at Pappankalan-I and 220KV Bamanauli-Pappankalan (DTL) D/C were connected to Bus-1 and 220/66kV 100 MVA ICT-1 & 2 at Pappankalan-I and 220KV Dwarka-Pappankalan-I (DTL) D/C were connected to Bus-2 at Pappankalan-I. 220KV Bamanauli-Pappankalan (DTL) D/C were not in service and 220kV Bus coupler at Pappankalan-I was in ON position. iii)As reported, at 04:53 hrs, R-ph conductor of 220kV bus coupler at Pappankalan-I broke with heavy sound and was hanging in yard which created bus fault at 220kV Bus-2 of Pappankalan-I. iv)Due to this, busbar protection operated at 220kV Bus-2 of Pappankalan-I and all the elements connected to Bus-2 tripped. v)After tripping of 220KV Dwarka-Pappankalan-I (DTL) D/C, 220/66kV 160 MVA ICT-3 & 5 at Pappankalan-I was also tripped due to loss of supply and complete blackout occurred at 220/66kV Pappankalan-I S/s. vi)As per PMU at Dwarka(PG), R-N phase to earth fault with fault clearing time of 80msec is observed. vii)As per SCADA, change in demand of approx. 230 MW in Delhi control area. However, SLDC-Delhi reported load loss of approx. 144 MW (28MW at Hiranagar, 40MW at G-2, 41MW at Bindapur, 15MW at D C Janakpuri, Chaukhandhi and 20MW at Bodella-1) in Delhi control area.	1) 220KV Dwarka-Pappankalan-I (DTL) Ckt-1 2) 220KV Dwarka-Pappankalan-I (DTL) Ckt-2 3) 220/66kV 100 MVA ICT-1 at Pappankalan-I 4) 220/66kV 100 MVA ICT-2 at Pappankalan-I 5) 220/66kV 160 MVA ICT-3 at Pappankalan-I 6) 220/66kV 160 MVA ICT-5 at Pappankalan-I
7	GI-2	Rajasthan	19-08-2024 23:48	20-08-2024 03:05	03:17	0	0	0.000	0.000	50301	66210	i)400/220kV Kankroli(PG) has one and half bus arrangement at 400kV side.ii)During antecedent condition, incoming power at Kankroli(PG) S/s from Zerda(GETCO) S/s through 400 KV Kankroli-Zerda (PG) Ckt-1 & 2 were approx. 50 MW & 30 MW respectively.iii)As reported, at 23:48 hrs, Y-phase CT of bus coupler of 400kV bus-1 & bus-2 at Zerda(GETCO) S/s damaged which led to bus bar protection operation on both 400kV buses at Zerda(GETCO) S/s.iv)Due to bus bar protection operation at Zerda(GETCO), 400 KV Kankroli-Zerda (PG) Ckt-1 & 2 tripped from Zerda(GETCO) end. At the same time, DT received at Kankroli(PG) end, on which 400 KV Kankroli-Zerda (PG) Ckt-1 & 2 tripped from kankroli(PG) end. v)As per DR of kankroli(PG) end of 400 KV Kankroli-Zerda (PG) Ckt-2, Y-N phase to earth fault is observed with fault current of Iy=~1.3kA. DT received at Kankroli(PG) end.vi)As per PMU at Kankroli(PG), Y-N phase to earth fault followed by R-Y phase to phase fault with fault clearing time of 80 msec and 80 msec is observed. Time difference between both fault signatures is approximately 2 seconds. vii)From SCADA SOE and PMU plot it can be confirmed that 400 KV Kankroli-Zerda (PG) Ckt-2 tripped on Y-N phase to earth fault and 400 KV Kankroli-Zerda (PG) Ckt-1 tripped on R-Y phase to phase fault. viii)As per SCADA, no change in demand of Rajasthan control area.	1)400 KV Kankroli-Zerda (PG) Ckt-1 2)400 KV Kankroli-Zerda (PG) Ckt-2
8	GI-2	Uttar Pradesh	21-08-2024 09:02	21-08-2024 10:00	00:58	0	127	0.000	0.198	56428	64073	i)During antecedent condition, 400/220kV 315 MVA ICT-1, 400/220kV 500 MVA ICT-4, 220kV Muzaffarnagar-Shamli (UP) Ckt, 220kV Muzaffarnagar-Khatauli (UP) Ckt, 220kV Muzaffarnagar-Badhni kalan (UP) Ckt & 220/132kV 160MVA ICT-4 were connected to 220kV bus-1 and 400/220 kV 315 MVA ICT-2, 400/220 kV 315 MVA ICT-3, 220kV Muzaffarnagar-Charla (UP) Ckt, 220kV Muzaffarnagar-Jansath (UP) Ckt & 220/132kV 160MVA ICT-5 were connected to 220kV bus-2 at Muzaffarnagar(UP) S/s. Bus coupler of 220kV bus-1 and 220kV bus-2 was in ON condition and 220kV Muzaffarnagar-Nara (UP) Ckt was not in service (under shutdown) during the tripping event. ii)As reported, at 09:02 hrs, R-N phase to earth fault occurred on 220kV Muzaffarnagar-Badhni kalan (UP) Ckt with fault distance of 3.8km from Muzaffarnagar(UP) end and 20.4km from Badhni kalan(UP) end. Fault was sensed in zone-1 from both ends.iii)On this fault 220kV Muzaffarnagar-Badhni kalan (UP) Ckt tripped from Badhni kalan end on zone-1 distance protection on R-N fault. During fault clearing process at Muzaffarnagar(UP) end, R-phase CB interrupting chamber got damaged which resulted into continuation of sparking between R phase male contact and R phase dropper wire of breaker. The circuit breaker operated mechanically (auxiliary contacts operated properly) and thus breaker status reflected as OPEN. iv)As breaker didn't open completely (sparking between R phase male contact and R phase dropper wire of breaker was still there), fault was not cleared yet. Due to continuous fault feeding 400/220kV 315MVA ICT-1 & 2 and 400/220kV 500 MVA ICT-4 tripped on directional earth fault protection and 400/220kV 315 MVA ICT-3 tripped on back up impedance protection. 220 kV Charla line, 220 kV Jansath line and 220 kV shamli line tripped from remote ends on zone-3 distance protection (it is confirmed from respective DRs also).v)Ideally, this fault would have been cleared by LBB protection of Badhni kalan bay, but as CB status changed from ON to OFF due to proper operation of breaker auxiliary contacts, LBB initiation got reset. vi)Further, as reported, bus bar protection of 220kV bus-1 at Muzaffarnagar(UP) also operated after 1 second of fault starting time due to persisting differential current.vii)As per DR of bus bar protection at Muzaffarnagar(UP), busbar protection operated on 220kV bus-1 after 1.05 second of fault starting time. On this, all remaining elements also tripped which were connected to 220kV bus-1 i.e. 220kV Muzaffarnagar-Khatauli (UP) Ckt	1)400/220 kV 315 MVA ICT 1 at Muzaffarnagar(UP) 2)400/220 kV 315 MVA ICT 2 at Muzaffarnagar(UP) 3)400/220 kV 315 MVA ICT 3 at Muzaffarnagar(UP) 4)400/220 kV 500 MVA ICT 4 at Muzaffarnagar(UP) 5)220kV Muzaffarnagar-Charla (UP) Ckt 6)220kV Muzaffarnagar-Jansath (UP) Ckt 7)220kV Muzaffarnagar-Shamli (UP) Ckt 8)220kV Muzaffarnagar-Khatauli (UP) Ckt
9	GD-1	Punjab	22-08-2024 20:33	22-08-2024 21:30	00:57	0	290	0.000	0.395	55995	73467	i)220kV Laltokalan(PS) has double main bus arrangement at 220kV side. ii)During antecedent condition, incoming power at Laltokalan(PS) S/s from Ludhiana(PG) S/s through 220 KV Ludhiana(PG)-Laltokalan(PS) (PSTCL) Ckt-1 & 2 were approx. 210 MW & 230 MW respectively. At 220kV level, all elements were connected to 220kV bus-1 at Laltokalan(PS) S/s. 220kV bus-2 was not in service due to ongoing augmentation work on 220kV bus-2 at Laltokalan(PS) S/s. iii)As reported, at 20:33 hrs, R-N phase to earth fault occurred on 220 KV Ludhiana(PG)-Laltokalan(PS) (PSTCL) Ckt-1 at a distance of 1.5km from Laltokalan(PS) end and 0.76km from Ludhiana(PG) end with fault current of Ir=30.1kA & Ir=12.97kA from Ludhiana(PG) and Laltokalan(PS) end respectively. iv)On this fault, 220 KV Ludhiana(PG)-Laltokalan(PS) (PSTCL) Ckt-1 tripped from Ludhiana(PG) on zone-1 distance protection (as per DR), but R-phase pole of CB couldn't open from Laltokalan(PS) end. v)Due to failure of CB opening, LBB of 220 KV Ludhiana(PG)-Laltokalan(PS) (PSTCL) Ckt-1 bay operated which led to tripping of all elements connected to 220kV bus-1 at Laltokalan(PS) S/s i.e. 220kV lines from Laltokalan(PS) to Ludhiana Ckt-2, Ferozpur Road (PS) Ckt, Hambran (PS) Ckt, Jagraon (PS) Ckt, 220/66 kV 160 MVA ICT-1, 220/66 kV 100 MVA ICT-4 & 5. vi)As per PMU at Ludhiana(PG), R-N phase to earth fault with delayed fault clearing time of 320msec is observed. vii)Due to tripping of all elements at 220kV level on LBB at Laltokalan(PS) S/s, blackout occurred at 220kV Laltokalan(PS) S/s. viii)As per SCADA, change in demand of approx. 290 MW in Punjab control area.	1)220 KV Ludhiana(PG)-Laltokalan(PS) (PSTCL) Ckt-1 2)220 KV Ludhiana(PG)-Laltokalan(PS) (PSTCL) Ckt-2 3)220 kV Lalton kalan – Ferozpur Road (PS) Ckt 4)220 kV Lalton kalan – Hambran (PS) Ckt 5)220 kV Lalton kalan – Jagraon (PS) Ckt 6)220/66 kV 160 MVA ICT-1 at Laltokalan(PS) 7)220/66 kV 100 MVA ICT-4 at Laltokalan(PS) 8)220/66 kV 100 MVA ICT-5 at Laltokalan(PS)
10	GI-2	Uttar Pradesh	25-08-2024 04:25	25-08-2024 05:51	01:26	220	0	0.488	0.000	45060	63093	i)During antecedent condition, 400 kV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt, 110 MW Unit-1 & 4 at Vishnuprayag(UP) were connected to 400kV Bus-1 at Vishnuprayag(UP) and 400 kV Alaknanda(UP)-Vishnuprayag(UP) (UP) Ckt, 110 MW Unit-2 & 3 at Vishnuprayag(UP) were connected to 400kV Bus-2 at Vishnuprayag(UP). 400 kV Vishnuprayag (UP)- Muzaffarnagar(UP) (UP) Ckt, 400kV Alaknanda-Muzaffarnagar ckt and 400kV Vishnuprayag-Alaknanda ckt were carrying ~343 MW, ~462 MW & 86 MW respectively.ii)As reported, at 04:25 hrs, 400 kV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt tripped on Y-B phase to phase fault. Fault occurred due to tree falling on the line between tower location no. 102 & 103, tower base at location no. 102 also got damaged due to land slide. Fault distance was ~225km (~79%) from Muzaffarnagar end.iii)Further after ~50msec, 400kV bus coupler at Vishnuprayag HEP tripped on over current stage-2 (DT) protection operation.iv)With the tripping of 400kV Bus coupler at Vishnuprayag HEP, 110 MW Unit-1 & 4 at Vishnuprayag HEP also tripped due to loss evacuation path.v)As per PMU at Muzaffarnagar(UP) and line DR files, Y-B phase to phase which cleared within 80msec is observed. Fault was in Z-1 from Vishnuprayag end. vi)As per SCADA, generation loss of ~220MW occurred at 110 MW Unit-1 & 4 at Vishnuprayag HEP due to tripping of 110 MW Unit-1 & 4.vii)As tower base at location no. 102 of 400 kV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt damaged during the event, line was taken under emergency shutdown after the event. Unit-1&4 were revived by 06:00 hrs and taken into service through 400kV Bus-2. Generation evacuated through 400kV Vishnuprayag-Alaknanda ckt & 400kV Alaknanda-Muzaffarnagar ckt path.viii)400 kV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt was revived at 17:33 hrs on 27.08.024. 400kV Bus-1 was also taken into service with the revival of 400 kV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt.	1)400 KV Muzaffarnagar(UP)-Vishnuprayag(JP) (UP) Ckt 2)110 MW Vishnuparyag HPS - UNIT 1 3)110 MW Vishnuparyag HPS - UNIT 4

Details of Grid Events during the Month of Aug 2024 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
11	GD-1	Haryana	26-08-2024 22:58	26-08-2024 23:15	00:17	0	350	0.000	0.543	48808	64478	i)220kV Rajokheri(HV) & 220kV Shahbad(HV) S/s have double main bus arrangement at 220kV side.ii)During antecedent condition, incoming power at Rajokheri(HV) S/s through 220 KV Abdullapur(PG)-Rajokheri (HV) (HVPNL) D/C was approx. 115 MW and outgoing power from Rajokheri(HV) through 220 KV Shahbad-Rajokheri(HV)(HVPNL) D/C was approx. 90 MW. Loading of 220 KV Shahbad-Joria(HV)(HVPNL) D/C and 220 KV Shahbad-Durla(HV)(HVPNL) D/C were approx. 100 MW and 75 MW feeding to Shahbad(HV) and Durla(HV) respectively.iii)As reported, at 22:58 hrs, due to inclement weather conditions, Y-B phase to phase occurred on 220 KV Shahbad-Rajokheri(HV)(HVPNL) Ckt-1 & 220 KV Abdullapur(PG)-Rajokheri (HV) (HVPNL) Ckt-1.iv)As reported, 220 KV Abdullapur(PG)-Rajokheri (HV) (HVPNL) D/C tripped only from Abdullapur(PG) end not from Rajokheri(HV) end. 220 KV Shahbad-Rajokheri(HV)(HVPNL) Ckt-1 tripped on zone-1 distance protection on Y-B-G double phase to ground fault with fault distance of 29km and fault current of Iy=~5.79kA & Ib=~5.39kA from Rajokheri(HV) end. 220 KV Shahbad-Rajokheri(HV)(HVPNL) Ckt-2 & 220 KV Tepla-Rajokheri(HV)(HVPNL) Ckt-2 tripped on direction earth fault from Rajokheri(HV) end. 220 KV Tepla-Rajokheri(HV)(HVPNL) Ckt-1 tripped on zone-3 distance protection on Y-B phase to phase fault from Rajokheri(HV) end (details regarding trippings at Shahbad(HV) S/s is yet to be received). v)As per PMU at Abdullapur(PG), Y-B phase to phase fault converted into R-Y-B three phase fault with delayed fault clearing time of 2040msec is observed.vi)Due to tripping of all 220kV lines at Rajokheri(HV) & Shahbad(HV), both sub-stations lost their connectivity from Grid which led to blackout of 220kV Rajokheri(HV) S/s & 220kV Shahbad(HV) S/s. vii)As per SCADA, change in demand of approx. 350 MW in Haryana control area.	1)220 KV Abdullapur(PG)-Rajokheri (HV) (HVPNL) Ckt-1 2)220 KV Abdullapur(PG)-Rajokheri (HV) (HVPNL) Ckt-2 3)220 KV Shahbad-Rajokheri(HV)(HVPNL) Ckt-1 4)220 KV Shahbad-Rajokheri(HV)(HVPNL) Ckt-2 5)220 KV Tepla-Rajokheri(HV)(HVPNL) Ckt-1 6)220 KV Tepla-Rajokheri(HV)(HVPNL) Ckt-2 7)220 KV Shahbad-Durla(HV)(HVPNL) Ckt-1 8)220 KV Shahbad-Durla(HV)(HVPNL) Ckt-2 9)220 KV Shahbad-Joria(HV)(HVPNL) Ckt-1 10)220 KV Shahbad-Joria(HV)(HVPNL) Ckt-2
12	GI-1	Jammu and Kashmir	26-08-2024 13:53	26-08-2024 17:18	03:25	0	180	0.000	0.247	57013	72984	i)220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. 220kV Amargarh-Ziankote ckt-1&2 are on the same tower (D/C tower) and line length is ~21.4km. ii)During antecedent condition, 220kV Amargarh(INDIGRID) –Ziankote(JK) D/C was carrying 104 MW each and feeding Ziankote load. iii)As reported, at 13:53 hrs, 220 KV Amargarh(INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2 tripped from both ends on R-Y phase to phase fault with fault distance of 6.6km and fault current of Ir=~2.15kA & Iy=~2.37kA from Ziankote(JK) end. 220 KV Amargarh(INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 tripped only from Amargarh(INDIGRID) end on the same R-Y phase to phase fault (Exact reason of fault is yet to be received). iv)As per DR of Amargarh(INDIGRID) end of 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1, R-Y phase to phase fault is observed in zone-2 with fault current of Ir=~2.5kA & Iy=~2.1kA. v)As per DR of Amargarh(INDIGRID) end of 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2, R-Y phase to phase fault is observed in zone-1 with fault current of Ir=~5.2kA & Iy=~4.9kA. vi)As confirmed by Amargarh(INDIGRID), in view of non-availability of carrier communication and A/R scheme at Ziankote end, A/R has been kept disabled at Amargarh end and time delay of Z-2 also kept as instantaneous at Amargarh end. vii)As per PMU at Amargarh(PG), R-Y phase to phase fault which cleared within 120 msec is observed. viii)As per SCADA, change in demand of approx. 180MW is observed in J&K control area.	1)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 2)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2
13	GI-2	Delhi	31-08-2024 16:40	31-08-2024 18:06	01:26	0	105	0.000	0.156	53755	67125	i)400kV Bawana(DTL) S/s has one and half breaker bus arrangement at 400kV level. ii)During antecedent condition, incoming power at Bawana(DTL) through 400 KV Bawana-Mundka (DV) Ckt-1 & 2 were approx. 514MW & 503MW respectively and outgoing power from Bawana(DTL) to Maharani Bagh(PG) through 400 KV Bawana(DV)-Maharanibagh(PG) (DTL) Ckt-1 & 2 were approx. 294 MW & 294 MW. iii)As reported, at 16:40 hrs, 400 KV Bawana(DV)-Maharanibagh(PG) (DTL) Ckt-1 tripped on R-Y phase to phase fault with fault distance of 4.71km and with fault current of Ir=~31.38kA & Iy=~29.27kA from Bawana end (Reason of fault is yet to be received). 400 KV Bawana(DV)-Maharanibagh(PG) (DTL) Ckt-1 tripped on zone-1 distance protection from Bawana(DTL) end. iv)As per DR of Bawana(DTL) end of 400 KV Bawana(DV)-Maharanibagh(PG) (DTL) Ckt-1, R-Y phase to phase fault is observed with fault current of Ir=~31.3kA, Iy=~29.3kA and line tripped on zone-1 distance protection. v)As reported, the same fault sensed in zone-1 from Mundka(DTL) end and 400 KV Bawana-Mundka (DV) Ckt-1 & 2 tripped on zone-1 distance protection from Mundka(DTL) end. vi)As per PMU at Maharani Bagh(PG), R-Y phase to phase fault with fault clearing time of 120msec is observed. vii)As per SCADA, change in demand of approx. 105MW is observed in Delhi control area. viii)As reported by SLDC Delhi, the case of over reach of GE D60 relays at Mundka(DTL) S/s is already forwarded to GE company for analysis and necessary corrective recommendations.	1)400 KV Bawana(DV)-Maharanibagh(PG) (DTL) Ckt-1 2)400 KV Bawana-Mundka (DV) Ckt-1 3)400 KV Bawana-Mundka (DV) Ckt-2

Details of Grid Events during the Month of Aug 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	01-08-2024 16:41	02-08-2024 01:50	09:09	230	-	0.34%	-	68094	52678	At 16:41 Hrs / 01-08-2024, 220 kV Bhuj-Nanavalka tripped on R-E fault after auto recloser attempt. It is seen that Auto recloser attempt taken from Bhuj End only and three phase trip issued at Nanavalka end for single phase fault. Generation loss of 230 MW occurred at Nanavalka (Alfanar) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Nanavalka
2	GD-1	WR	02-08-2024 03:47	02-08-2024 06:53	03:06	238	-	0.36%	-	66022	47652	At 03:47 Hrs / 02-08-2024, 220 kV Bhuj-Naranpar tripped on R-E fault at Bhuj end only. Generation loss of 238 MW occurred at Naranpar (GIWEL-3) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Naranpar
3	GD-1	WR	06-08-2024 09:36	06-08-2024 16:00	06:24	300	-	0.43%	-	69367	52967	At 09:36 Hrs / 06-08-2024, 220 kV Bhuj II-Nakhatrana tripped on R-E fault after unsuccessful Auto recloser attempt. At the time of patrolling, R Phase disc insulator failure observed at location 45. Generation loss of 300 MW occurred at Nakhatrana and Dedhiya (Adani) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj II-Nakhatrana
4	GD-1	WR	07-08-2024 13:59	07-08-2024 20:53	06:54	436	-	0.66%	-	66386	51173	At 13:59 Hrs / 07-08-2024, 220kV Bhuj-Ratadiya-1 tripped on Y-E fault. Simaltaneously, 220kV Bhuj-Ratadiya-2 tripped on under voltage protection operation. At the time of patrolling, Y phase jumper found open at location 165. Generation loss of 436 MW occurred at Ratadiya (Adani) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220kV Bhuj-Ratadiya-1&2
5	GI-2	WR	08-08-2024 09:14	08-08-2024 11:48	02:34	560	-	0.81%	-	68938	56200	At 09:14 Hrs / 08-08-2024, 400 / 33 kV KSTPS-Tie Transformer-4 tripped from LV side on Restricted Earth Fault, smoke observed in LV side terminal box. Due to non openeing of R phase breaker at 400 kV side, LBB operated resulting in tripping of 400 kV KSTPS-Bus-2 (Double Main and Transfer Bus) and all connected elements. Generation loss of 560 MW occurred at Korba-NTPC Thermal Power Plant due to the event.	Tripping of following Elements: 1. 400 / 33 kV KSTPS-Tie Transformer-4 2. 400 kV KSTPS-Bus-2 3. 400kV KSTPS-Bhilai-2 4. KSTPS-Unit-1,2&3 (210 MW occurred at)
6	GD-1	WR	11-08-2024 11:17	11-08-2024 13:40	02:23	131	-	0.21%	-	62076	53414	At 11:17 Hrs / 11-08-2024, 220 kV Bhuj II-Morjar (Srijan) tripped on Zone-2 distance protection operation on Y-E fault. During inspection it was found that, Y phase voltage was not seen by relay. The same was corrected and line was charged. PMU data stopped immediately after the line tripping indicating failure of back supply or absence of backup supply at station. Generation loss of 131 MW occurred at Morjar (Srijan) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj II-Morjar (Srijan)
7	GI-2	WR	12-08-2024 05:09	12-08-2024 09:00	03:51	-	70.06	-	0.14%	62436	50737	At 05:09 Hrs / 12-08-2024, 400/220 kV Dhule(MH)-ICT-3 tripped on differential protection operation due to blasting of Y phase bushing. 400/220 kV Dhule(MH)-ICT-1 tripped on Backup to Earth Fault protection operation. 400 kV Dhule(MH)-Khandwa-1 tripped on Over voltage stage-1 protection operation which was a maloperation. 400 kV Dhule(MH)-Dhule(BDTCL)-2 tripped on Z-4 protection operation at Dhule(MH) end and Z-2 protection operation at Dhule(BDTCL) end. 400 kV Dhule(MH)-SSP-2 tripped on Z-4 protection operation at Dhule(MH) end and Z-1 protection operation at SSP end (tripping on Z-1 at SSP) which was a maloperation. 400 kV Dhule(MH)-Bableshwar-2 tripped on Z-2 protection operation at Bableshwar end. Ideally the fault should have been cleared on LBB protection operation, but LBB protection not operated. Load loss of 70.06 MW occurred at occurred due to LTS stage-1 and LTS stage-2 operation due to 400/220 kV Dhule(MH)-ICT-1&3.	Tripping of following Elements: 1. 400/220 kV Dhule(MH)-ICT-3 2. 400/220 kV Dhule(MH)-ICT-1 3. 400 kV Dhule(MH)-Khandwa-1 4. 400 kV Dhule(MH)-Dhule(BDTCL)-2 5. 400 kV Dhule(MH)-SSP-2 6. 400 kV Dhule(MH)-Bableshwar-2
8	GD-1	WR	12-08-2024 21:49	13-08-2024 03:22	05:33	-	-	-	-	71388	55247	At 21:49 Hrs / 12-08-2024, 220 kV STT-Mahape and 220 kV STT-TIFIPL tripped on differential protection operation due to R phase lightening arrestor of 220 kV STT-Mahape burst at STT substation. Tripping of 220 kV STT-TIFIPL for a fault in 220 kV STT-Mahape is undesirable. No load loss occurred due to the event.	Tripping of following Elements: 1. 220 kV STT-Mahape 2. 220 kV STT-TIFIPL
9	GD-1	WR	17-08-2024 11:42	17-08-2024 19:54	08:12	187	-	0.26%	-	71293	60072	At 11:42 Hrs / 07-08-2024, 220 kV Jamkhambaliya-Khakharda tripped on R-E fault.During patrolling R phase insulator failure was observed. Generation loss of 187 MW occurred at Khakharda (Apraava) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Jamkhambaliya-Khakharda
10	GD-1	WR	19-08-2024 02:24	19-08-2024 09:02	06:38	47	-	0.07%	-	67243	53511	At 02:24 Hrs / 19-08-2024, 220 kV Bhuj II-Nakhatrana tripped on Y-E fault after unsuccessful autoreclose attempt. During patrolling Y phase insulator failure was observed at Tower location 51. Generation loss of 47 MW occurred at Nakhatrana and Dedhiya (Adani) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj II-Nakhatrana
11	GD-1	WR	19-08-2024 12:24	20-08-2024 07:42	19:18	9.6	-	0.01%	-	67063	55507	At 12:24 Hrs / 19-08-2024, 220 kV Jamkhambaliya-Sidhpur tripped on Y-E fault, 3 phase tripped for fault in 1 phase which is undesirable, also Auto Recloser block signal was active. During patrolling Y phase insulator failure was observed at Tower location 59. Generation loss of 9.6 MW occurred at Sidhpur (Torrent) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Jamkhambaliya-Sidhpur
12	GI-2	WR	19-08-2024 23:48	20-08-2024 01:16	01:28	-	-	-	-	66674	53297	At 23:48 Hrs / 19-08-2024, Y phase CT of 400 kV Kansari-Bus Coupler towards 400 kV Kansari-Bus-2 side failed, resulting in Bus Bar protection operation and tripping of 400 kV Kansari-Bus-2 and all connected elements. After 2 seconds the smoke from failed CT reached 400 kV Kansari-Bus-1 resulting in Bus Bar protection operation and tripping of 400 kV Kansari-Bus-1 and all connected elements. 400 kV Kansari-Bus-1: 400/220 kV Kansari-ICT-3&4, 400 kV Kansari-Soja-1,400 kV Kansari-Banaskantha, 400 kV Kansari-Charanka-1, 400 kV Kansari-Kankroli-1 and 400 kV Kansari-B/R-1 400 kV Kansari-Bus-2: 400 kV Kansari-Charanka-2, 400/220 kV Kansari-ICT-1&2, 400 kV Kansari-Kankroli-2 (Bypassed at Bhinamal), 400 kV Kansari-B/R-2. Prior to the trippings, 400 kV Kansari-Soja-1 was under outage for Voltage Regulation. 400 kV Kansari side became dead and 220 kV Kansari was intact. No generation / load loss occurred due to the event.	Tripping of following Elements: 1. 400 kV Kansari-Bus Coupler 2. 400 kV Kansari-Bus-1&2 3. 400 kV Kansari-Charanka-1&2 4. 400 kV Kansari-Banaskantha 5. 400 kV Kansari-Veloda 6. 400 kV Kansari-Soja-1 7. 400 kV Kansari-Kankroli-1 8. 400 kV Kansari-Kankroli-2 (Bypassed at Bhinamal) 9. 400/220 kV Kansari-ICT-1,2,3&4 (315 MVA) 10. 400 kV Kansari-B/R-1&2

Details of Grid Events during the Month of Aug 2024 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
13	GD-1	WR	24-08-2024 03:54	24-08-2024 08:02	04:08	-	25	-	0.05%	65914	51526	At 03:54 Hrs / 24-08-2024, 220 kV Chitegaon substation became dead due to Bus-Bar protection operation caused by abrupt closing of 220 KV Hybrid GIS Bus sectionalizer earth switch automatically at Chitegaon end. Load loss of 25 MW occurred due to the event.	Tripping of following Elements: 1. 220 kV Chitegaon Main Bus 2. 220 kV Chitegaon Auxillary Bus 3. 220/132 kV Chitegaon-ICT-1,2,3&4 4. 220/33 kV Chitegaon-ICT-1&2 5. 220 kV Chitegaon-Waluj
14	GD-1	WR	27-08-2024 01:51	27-08-2024 21:32	19:41	240	-	0.40%	-	60383	43432	At 01:51 Hrs / 27-08-2024, 220 kV Chugger-Bhuj-II-S/c tripped on R-E fault. During patrolling, R phase Jumper found open at Tower location 07 along with failure of insulator. Generation loss of 240 MW occurred at Chugger (Sitac) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Chugger-Bhuj-II-S/c
15	GD-1	WR	27-08-2024 16:58	27-08-2024 20:47	03:49	148	-	0.25%	-	60383	43432	At 16:58 Hrs / 27-08-2024, 220 kV Bhuj-Baranda-S/c tripped on B-E fault. Generation loss of 148 MW occurred at Baranda (ASIPL) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Baranda
16	GD-1	WR	29-08-2024 18:52	31-08-2024 13:39	42:47	69	-	0.11%	-	64777	55713	At 18:52 Hrs / 29-08-2024, 220 kV Bhuj-Naranpar tripped on Y-E fault after auto recloser attempt. At the time of patrolling, Y Phase disc insulator failure observed at location 45. Generation loss of 69 MW occurred at Naranpar (GIWEL-3) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Naranpar
17	GD-1	WR	30-08-2024 03:26	30-08-2024 05:31	02:05	19	-	0.03%	-	59121	48568	At 03:26 Hrs / 30-08-2024, 220 kV Bhuj-Kotda Madh-S/c tripped on B-E fault due to fault occurred during auto recloser reclaim time. Generation loss of 19 MW occurred at Kotda Madh (Alfanar) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Kotda Madh
18	GD-1	WR	30-08-2024 05:53	30-08-2024 14:00	08:07	98	-	0.16%	-	60172	51511	At 05:53 Hrs / 30-08-2024, 220 kV Bhuj-Dayapar-1&2 tripped due to blast in capacitor banks at Dayapar. Blast was due to grounding of PSS DC cable in Capacitor control panel, which resulting in burning of control panel of capacitor banks-1&2, meters, MCCBs. Simaltaneously, feeder-8 conductor also fell down within the plant. Generation loss of 98 MW occurred at Dayapar (INOX) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Dayapar-1&2
19	GD-1	WR	30-08-2024 06:34	30-08-2024 13:11	06:37	37.8	-	0.06%	-	61894	53483	At 06:34 Hrs / 30-08-2024, 220 kV Bhuj-Kotda Madh-S/c tripped on B-E fault after auto recloser attempt. During patrolling rope was found hanging on B-phase conductor. Generation loss of 37.8 MW occurred at Kotda Madh (Netra) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Kotda Madh
20	GD-1	WR	30-08-2024 11:40	01-09-2024 10:32	46:52	48	-	0.08%	-	61489	53100	At 11:40 Hrs / 30-08-2024, 220 kV Chugger-Bhuj-II tripped on B-E fault. At the time of patrolling, insulator failure observed at tower location 147 and 206. Generation loss of 48 MW occurred at Chugger (Sitac) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Chugger-Bhuj-II
21	GD-1	WR	31-08-2024 10:35	31-08-2024 11:08	00:33	-	219	-	0.35%	69146	62278	At 10:35 Hrs / 31-08-2024, 220 kV Nalasopara S/s became dead due to tripping of all elements on busbar protection operation. During the event, switchyard works were going on. 220 kV Palgar-Nalasopara and 220 kV Boisar-Nalasopara tripped from Nalasopara end only, DT was not sent to remote eneds which was undesirable. Load loss of 219 MW occurred at Nalasopara Substation due to the event.	Tripping of following Elements: 1. 220 kV Palgar-Nalasopara 2. 220 kV Boisar-Nalasopara 3. 220 kV Nalasopara-ICT-1,2&3

Details of Grid Events during the Month of Aug 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	TAMILNADU	04-08-2024 11:57	04-08-2024 14:20	02:23	0	0	0.00%	0.0	52515.27	52088.8	Complete Outage of 230kV/110kV Kayathar SS : The triggering incident was Y-N fault in 230kV Kayathar Sanganeri Line-1. At Kayathar end, at the time of lockout, Y-pole breaker failed to open at Kayathar end causing LBB to operate. Immedeately, LBB operated and all lines connected to the 230kV Kayathar Bus tripped. This led to complete outage of 230kV/110kV Kayathar SS of TANTRANSCO.	230KV-KAYATHAR(TN)-TIRUNELVELI-1, 230KV-KAYATHAR(TN)-SANGANERI-1, KAYATHAR(TN) - 230KV
2	GD - 1	KARNATAKA	05-08-2024 09:41	05-08-2024 13:06	03:25	120	62	0.24%	0.11%	49225.06	55827.5	Complete Outage of 220kV/66kV Hiriyur_KA SS and 220kV Enercon and 220kV Azure SS: 220kV Enercon and 220kV Azure SS are being radially connected to 220kV/66kV Hiriyur_KA SS. As per the reports submitted, the triggering incident was R-phase CT flashover in 66kV Bus sectionaliser in 220kV/66kV Hiriyur_KA SS which subseqeuntly became an RYB-N fault. At the same time, due to DC supply failure, CTDs of all lines and Transformers tripped causing complete outage of 220kV/66kV Hiriyur_KA SS which inturn led to complete outage of 220kV Enercon and 220kV Azure SS.	220KV-HIRIYUR-HIRIYUR_KAR-1, 220KV-HIRIYUR-HIRIYUR_KAR-2, HIRIYUR_KAR - 220KV - Bus 1, HIRIYUR_KAR - 220KV - Bus 2, AZURE_HIRIYUR - 220KV - Bus 1, ENERCON_HIRIYUR - 220KV - Bus 1, 220KV-HIRIYUR_KAR-TALLAK-1, 220KV-HIRIYUR_KAR-MADHUGIRI-1
3	GD - 1	KARNATAKA	07-08-2024 09:15	07-08-2024 10:15	01:00	62	120	0.14%	0.24%	42925.5	49250.44	Complete Outage of 220kV/66kV Hiriyur_KA SS and 220kV Enercon and 220kV Azure SS: As per the reports submitted, DC source failure occurred at the station due to 220V battery charger issue, causing the DCMCCB to trip. As a result, all 220kV line breakers and the 100MVA power transformer breakers tripped on CTD at 220kV/66kV Hiryur_KA SS. This led to complete outage of 220kV/66kV Hiryur_KA SS.	220KV-HIRIYUR-HIRIYUR_KAR-1, 220KV-HIRIYUR-HIRIYUR_KAR-2, ENERCON_HIRIYUR - 220KV, 220KV-HIRIYUR_KAR-MADHUGIRI-1, 220KV-HIRIYUR_KAR-AZURE_HIRIYUR-1, 220KV-HIRIYUR_KAR-TALLAK-1
4	GD - 1	TAMILNADU	10-08-2024 14:49	10-08-2024 15:30	00:41	85	0	0.17%	0.00%	49288.07	51419.11	Multiple trippings at 220kV/33kV Mytrah and Complete Outage of 230kV/33kV JSW_Vilathikulam, and 230kV/33kV JSW_Savalperi: The triggering incident was a Y-N fault caused by a bird strike on the 33kV bay BCU311 LA of a 33kV feeder at Mytrah. At Mytrah , 220kV/33kV PTR-1&2 tripped on Earth fault protection. At the same time, the 230kV TTGS JSW_Vilathikulam and 230kV TTGS JSW_Savalaperi lines tripped on maloperation of under voltage protection. Tripping of these lines led to complete outage of 230kV/33kV JSW_Vilathikulam, and 230kV/33kV JSW_Savalperi.	230KV-TTGS-JSW_Vilathikulam-1, 230KV/33KV MYTRAH-PT-1, 230KV/33KV MYTRAH-PT-2, JSW_Savalaperi - 230KV
5	GD - 1	TAMILNADU	13-08-2024 13:16	13-08-2024 14:32	01:16	0	0	0.00%	0.00%	48841.84	52739.68	Complete Outage of of 230kV/33kV GRT Solar Station: As per the reports submitted, the triggering incident was R-N fault in 230kV TTGS GRT line. Tripping of only connected line led to complete outage of 230kV/33kV GRT Solar Station.	230KV-TTGS-GRT-1
6	GD - 1	TAMILNADU	28-08-2024 06:23	28-08-2024 16:21	09:58	411	0	0.95%	0.00%	43169.45	48985.57	Complete Outage of 765kV NCTPS ST3 Generating Station of TANGEDCO: As per the reports submitted, the triggering incident was B-N fault near Unit-1 of 765kV NCTPS ST3. Immediately, overall differential protection operated and the Unit tripped. Simultaneously, 765kV NCPS NCTPS ST3 line-1&2 sensed the fault in zone-2 and tripped instantaneously at NCPS end. Subsequently, 765kV Ariyalur NCPS Line-2 tripped on over voltage protection at NCPS end. Tripping of both lines connected to 765kV NCTPS ST3 Generating Station resulted in Complete outage of the Generating Station.	NCTPS STG3 - UNIT 1, 765KV-NCPS-NCTPS STG3-1, 765KV-ARIYALUR-NCPS-2
7	GD - 1	KARNATAKA	28-08-2024 11:31	28-08-2024 11:52	00:21	250	300	0.45%	0.53%	55063.33	56690.25	Complete outage of 220kV/66kV Lingsugur SS, 220kV/110kV Bagewadii SS, 220kV Baluti SS, 220kV/66kV Kushtagi SS, 220kV/66kV Gangavathi SS, 220kV/66kV Kushtagi SS, 220kV/66kV Narayanpur SS, 220kV/66kV Mallat SS, 220kV/66kV Sindhanur SS of KPTCL , 220kV Almatti PH of KPCL, 220kV/33kV Fortune Five SS, 220kV,33kV Atria SS, 220kV/33kV Bagewadri_RBRK SS: During antecedent conditions, 220kV Lingapur Gangavathi Line-1&2, 220kV Nandhihal Bagewadi Line-1&2 were under outage. As per the reports submitted, the triggering incident was tripping of 220kV RTPS Lingsugur Line-2. Immediately, 220kV RTPS- Mallat line, 220kv Lingasugur- Bagewadi line 1, 220kV Bagewadi Narayanpur Line-1, 220kV ADPH-Bagalkot line 1&2 tripped on over load. Tripping of all these lines resulted in complete outage of 220kV/66kV Lingsugur SS, 220kV/110kV Bagewadii SS, 220kV Baluti SS, 220kV/66kV Kushtagi SS, 220kV/66kV Gangavathi SS, 220kV/66kV Kushtagi SS, 220kV/66kV Narayanpur SS, 220kV/66kV Mallat SS, 220kV/66kV Sindhanur SS of KPTCL , 220kV Almatti PH of KPCL, 220kV/33kV Fortune Five SS, 220kV,33kV Atria SS, 220kV/33kV Bagewadri_RBRK SS.	220KV-LINGSUGUR-RTPS-1, 220KV-LINGSUGUR-RTPS-2, 220KV-LINGSUGUR-SHAHAPUR-1, 220KV-RTPS-MALAT-1, 220KV-LINGSUGUR-BASAVANA_BAGEWADI-1, 220KV-ALMATTI-BAGALKOT-1, 220KV-ALMATTI-BAGALKOT-2, 220KV-BASAVANA_BAGEWADI-NARAYANPUR-2
8	GD - 1	KARNATAKA , KERALA	28-08-2024 11:38	28-08-2024 12:09	00:31	170	433	0.31%	0.76%	55334.14	57025.34	Complete outage of 220kV/66kV Kadakola SS, 220kV/66kV Adakanahalli SS, 220kV/66kV Chamrajnagar SS, 220kV/66kV Madhuvanahalli SS, 220kV/66kV Hebbani SS, 220kV/66kV TK Halli SS of KPTCL and 220kV/66kV Kaniyampetta SS of KSEB: During antecedent conditions, 220kV TK Halli Kanakpura, 220kV Vajamangala TK Halli, and 220kV Kadakola Hootagally are in open condition. As per the reports submitted, the triggering incident was R-phase jumper failure in 220kV Mysore Kadakola Line-2. Subsequently, 220kV Mysore Kadakola Line-1 and 220kV Kaniyampetta Kunnamangalam line tripped on over loading. Tripping of all these lines led to complete outage of 220kV/66kV Kadakola SS, 220kV/66kV Adakanahalli SS, 220kV/66kV Chamrajnagar SS, 220kV/66kV Madhuvanahalli SS, 220kV/66kV Hebbani SS, 220kV/66kV TK Halli SS of KPTCL and 220kV/66kV Kaniyampetta SS of KSEB.	220KV-KANIYAMPETTA-KUNAMANGALAM-1, 220KV-KANIYAMPETTA-KUNAMANGALAM-1
9	GD - 1	KARNATAKA	28-08-2024 12:15	28-08-2024 12:29	00:14	0	0	0.00%	0.00%	53764.64	55768.72	Complete Outage of 220kV Madhuvanahalli SS, 220kV Chamrajnagar SS and 220kV Hebbani SS: Supply failure occured at 220kV Madhuvanahalli SS, 220kV Chamrajnagar SS and 220kV Hebbani SS. Other details are awatied from KPTCL	

Details of Grid Events during the Month of Aug 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
10	GD - 1	KARNATAKA	28-08-2024 13:29	28-08-2024 13:38	00:09	265	300	0.50%	0.55%	52671.58	54354.39	Complete outage of 220kV/66kV Lingsugur SS, 220kV/110kV Bagewadii SS, 220kV Baluti SS, 220kV/66kV Kushtagi SS, 220kV/66kV Gangavathi SS, 220kV/66kV Kushtagi SS, 220kV/66kV Narayanpur SS, 220kV/66kV Mallat SS, 220kV/66kV Sindhanur SS of KPTCL , 220kV Almatti PH of KPCL, 220kV/33kV Fortune Five SS, 220kV,33kV Atria SS, 220kV/33kV Bagewadri_RBRK SS: During antecedent conditions, 220kV Lingapur Gangavathi Line-1&2, 220kV Nandhihal Bagewadi Line-1&2 were under outage. As per the reports submitted, the triggering incident was tripping of 220kV RTPS Lingsugur Line-2. Immediately, 220kV RTPS- Mallat line, 220kv Lingasugur- Bagewadi line 1, 220kV Bagewadi Narayanpur Line-1, 220kV ADPH-Bagalkot line 1&2 tripped on over load. Tripping of all these lines resulted in complete outage of 220kV/66kV Lingsugur SS, 220kV/110kV Bagewadii SS, 220kV Baluti SS, 220kV/66kV Kushtagi SS, 220kV/66kV Gangavathi SS, 220kV/66kV Kushtagi SS, 220kV/66kV Narayanpur SS, 220kV/66kV Mallat SS, 220kV/66kV Sindhanur SS of KPTCL , 220kV Almatti PH of KPCL, 220kV/33kV Fortune Five SS, 220kV,33kV Atria SS, 220kV/33kV Bagewadri_RBRK SS.	220KV-LINGSUGUR-RTPS-1, 220KV-LINGSUGUR-RTPS-2, 220KV-LINGSUGUR-SHAHAPUR-1, 220KV-RTPS-MALAT-1, 220KV-LINGSUGUR-BASAVANA_BAGEWADI-1, 220KV-ALMATTI-BAGALKOT-1, 220KV-ALMATTI-BAGALKOT-2, 220KV-BASAVANA_BAGEWADI-NARAYANPUR-2
11	GD - 1	TELANGANA , KARNATAKA	28-08-2024 15:20	28-08-2024 16:05	00:45	117	220	0.23%	0.40%	50665.77	54752.43	Complete Outage of 220kV Raichur_KA of KPTCL of and 220kV Upper Jurala_PH of TSGENCO: During antecedent conditions, 220kV Upper Jurala_PH Jurala Line-1&2 were under outage. The triggering incident was R-N fault in 220kV Raichur RTPS Line-2. At the same time, 220kV Raichur RTPS Line-1 also tripped at RTPS end . Tripping of both lines led to loss of power evacuation at 220kV Upper Jurala_PH leading to tripping of all units on over frequency. This led to complete outage of 220kV Raichur_KA SS and 220kV Upper Jurala_PH.	220KV-JURALA-RAICHUR_KA-1, JURALA - UNIT 1, JURALA - UNIT 2, JURALA - UNIT 4, JURALA - UNIT 5, JURALA - UNIT 6, 220KV-JURALA-RAICHUR_KA-2
12	GI-1	ANDHRA PRADESH	01-08-2024 02:21	01-08-2024 03:12	00:51	0	0	0.00%	0.00%	40913.86	42281.04	Tripping of 220kV Bus-1 of 220kV VSS SWS: During DEF operation of 220kV VSS Gajuwaka Line at VSS, B-pole didn't open and this resulted in the LBB operation of 220kV Bus-1 of 220kV VSS SWS.	VIZAG_SWS - 220KV - Bus 1, 400KV/220KV GAZUWAKA-ICT-3, 220KV-VIZAG_SWS-PARAVADA-1, 220KV-VIZAG_SWS-KALPAKKA-1, 220KV-GAZUWAKA_AP-VIZAG_SWS-1
13	GI-1	ANDHRA PRADESH	01-08-2024 16:36	01-08-2024 17:49	01:13	0	0	0.00%	0.00%	49771.8	51773.56	Tripping of 220kV Bus-2 of 400kV/220kV Jammalamadugu SS: The triggering incident was R-N fault in 220kV Bus-2 of 400kV/220kV Jammalamadugu SS. 220kV Bus-2 BBP operated and all lines connected to the 220kV Bus-2 got tripped at 400kV/220kV Jammalamadugu SS.	JAMMALAMADUGU - 220KV - Bus 2, 400KV/220KV JAMMALAMADUGU-ICT-3, 220KV-JAMMALAMADUGU-ANIMALA-1, 220KV-JAMMALAMADUGU-THIRUMALAYAPALLI-1, 220KV-JAMMALAMADUGU-BETAMCHERLA-1, 220KV-JAMMALAMADUGU-PORUMAMILA-2
14	GI-2	KARNATAKA	03-08-2024 15:54	03-08-2024 16:45	00:51	0	0	0.00%	0.00%	52178.2	51692.57	Tripping of 400kV Bus-1 of 400kV/220kV Talguppa SS: While hand tripping 400kV/220kV ICT#2 at Talguppa SS, 400kV/220kV ICT#1 tripped due to suspected maloperation and 400kV/220kV ICT#3 tripped due to operation of backup of OC protection. Tripping of all the 3 ICTs resulted in the de-energisation of 400kV Bus-1 of 400kV/220kV Talguppa SS.	400KV/220KV TALGUPPA-ICT-1, 400KV/220KV TALGUPPA-ICT-3, TALGUPPA - 400KV - Bus 1
15	GI-1	ANDHRA PRADESH	06-08-2024 18:25	06-08-2024 19:13	00:48	300	0	0.69%	0.00%	43481.35	44713.53	Tripping of 220kV Bus-1 of 400kV/220kV VTPS: As per the reports submitted, Unit-5 was synchronized to the grid after completing overhaul works. Immediately after closing the GT-5 breaker, TC1 and TC2 faulty alarms were triggered, and a turbine trip command was issued, leading to Unit-5 tripping on Low Forward Power (LFP).However, GT-5 breaker did not open despite and the LBB protection was activated, tripping all breakers connected to 220kV Bus-1 of 400kV/220kV VTPS.	VTPS - 220KV - Bus 1, 220KV-VTPS-PIDUGURALLA-1, 220KV-TADIKONDA-VTPS-1, 220KV-VTPS-RENTACHINTHALA-1, 220KV-VTPS-PODILI-1, 220KV-VTPS-CHILLAKALLU-1, 220KV-KONDAPALLI-VTPS-1, 220KV-GUNADALA-VTPS-1
16	GI-2	KARNATAKA	09-08-2024 23:48	10-08-2024 03:43	03:55	0	0	0.00%	0.00%	44042.59	43726.16	Tripping of 400kV Bus-2 of 400kV/220kV UPCL: While de-synchronising UPCL Unit-2, B phase pole of the main breaker didn't open and LBB operated resulting in the de-energisation of 400kV Bus-2 of 400kV/220kV UPCL.	400KV-HEBBANAHALLI-UPCL-2, UPCL - 400KV - Bus 2
17	GI-1	KARNATAKA	13-08-2024 09:51	13-08-2024 09:52	00:01	0	144	0.00%	0.27%	47244.65	53483.46	Tripping of 220kV Bus-2 of 220kV/66kV Somanahalli SS of KPTCL: During antecedent, 220kV Somanahalli Bidadi Line-1&2 were connected to 220kV Bus-2 and bus coupler was in open condition. The triggering incident was high resistance R-N fault in 220kV Bidadi Somanahalli Line-1. At Bidadi end, line tripped on zone-2 and was holding at Somanahalli end. At the same time, 220kV Bidadi Somanahalli Line-2 tripped only at Somanahalli end on zone-4 protection. Tripping of both lines led to loss of power supply to 220kV Bus-2 at 220kV/66kV Somanahalli SS.	220KV-BIDADI-SOMANAHALLI-2, 220KV-BIDADI-SOMANAHALLI-1
18	GI-1	ANDHRA PRADESH , TELANGANA	20-08-2024 05:04	20-08-2024 06:30	01:26	0	0	0.00%	0.00%	34752.79	39930.91	Tripping of 220kV Bus-1 of 220kV/132kV Srisailam RB of APGENCO: The triggering incident was R-N fault in 220kV Bus-2 due to jumper cut in 220kV Srisailam RB Nsagar Line-1 at 220kV Srisailam RB. Immediately, BBP operated and all elements connected to the 220kV Bus-2 got tripped at 220kV/132kV Srisailam RB.	220KV-SRISAILAM_RIGHT_BANK-BILAKALAGUDUR-1, 220KV-DOMALAPENTA-SRISAILAM_RIGHT_BANK-1, 220KV-SRISAILAM_RIGHT_BANK-MARKAPUR-1, SRISAILAM_RIGHT_BANK - 220KV - Bus 2

Details of Grid Events during the Month of Aug 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
19	GI-2	TELANGANA	22-08-2024 12:28	22-08-2024 14:16	01:48	0	0	0.00%	0.00%	52678.91	49995.32	Tripping of 400kV Bus-1 at 400kV Bhoopalpally Generating Station: As per the reports submitted, while tripping KTPP Unit-2 (1X600MW) due to boiler tube leakage, 52-15 CB R-pole didn't open due to mechanical problem resulting in the tripping of 400kV Bhoopalapally Bus-1 on operation of LBB protection.	BHOOPALAPALLY - 400KV - Bus 1, 400KV-BHOOPALAPALLY-WARANGAL-1
20	GI-2	KARNATAKA	22-08-2024 19:54	22-08-2024 22:20	02:26	0	0	0.00%	0.00%	48505.98	47871.3	Tripping of 400kV Bus-1 and 2 at 400kV/220kV Guttur SS of KPTCL: As per the reports submitted, the triggering incident was 400V Bus-2 BBP malopertion due to relay cable fault in 400kV/220kV Guttur ICT-2. At the same time, due to error in isolator selection, 400kV Bus-1 BBP also operated leading to tripping of all elements connected to 400kV Bus-1 and 400kV Bus-2 at 400kV/220kV Guttur SS.	GUTTUR - 400KV - Bus 1, GUTTUR - 400KV - Bus 2, 400KV-GUTTUR-HIRIYUR-2, 400KV-GUTTUR-HIRIYUR-1, 400KV-KAIGA-GUTTUR-1, 400KV-KAIGA-GUTTUR-2, 400KV-GUTTUR-BTPS-1, 400KV-DONI-GUTTUR-1, 400KV-NARENDRA-GUTTUR-2, 400KV-NARENDRA-GUTTUR-1
21	GI-2	TAMILNADU	25-08-2024 10:09	25-08-2024 13:24	03:15	0	0	0.00%	0.00%	53735.95	47779.7	Tripping of 400V Bus-2 of 400V/110kV Alamathy SS: As per the reports submitted, the triggering incident was B-phase CT failure in 400kV/110kV Alamathy ICT-1 causing Bus fault. Immdiately, 400kV Bus-2 BBP operated tripping all elements connected to Bus-2. At the same time, the 400kV/110kV Alamathy ICT-6, which is connected through main breakers to both 400kV Alamathy Bus-1 and Bus-2 without a Tie bay, also tripped.	ALAMATHY - 400KV - Bus 2, 400KV/110KV ALAMATHY-ICT-1, 400KV/110KV ALAMATHY-ICT-6

Details of Grid Events during the Month of Aug 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Purnea	01-08-2024 15:50	01-08-2024 16:13	00:23	0	110	0.00%	0.48%	26029	22769	At 15:50 Hrs on 01.08.2024, 220/132 kV Purnea (PG) S/s became dead due to tripping of 220 kV New Purnea-Purnea D/c and 220 kV Gazole-Dalkhola D/c (Gazole-Dalkhola-Purnea link) during a fault in downstream of 132 kV Purnea (PG). Load loss of around 110 MW occurred at Purnea.	220kV New Purnea - Purnea D/C 132kV Purnea (PG)- Purnea 2,3 220 kV Gazole- Dalkohla D/C (Gazole-Dalkhola-Purnea link)
2	GD-1	Darbhanga	01-08-2024 17:59	01-08-2024 18:34	00:35	00:00	80	0.00%	0.35%	28309	22666	At 17:59 hrs on 01.08.2024, a fault struck B phase of 220kV Darbhanga (DMTCL) – Darbhanga -1 closer to BSPTCL end. Due to failure of opening of Circuit Breaker at Darbhanga end all other circuit connected to Darbhanga (BSPTCL) opened from remote end in Zone-2 time which led to total power failure at 220kV Darbhanga (BSPTCL) S/s. Total load loss of around 80 MW was reported. Power was extended through 220 kV Darbhanga – Mushari–2.	220 kV Darbhanga - Darbhanga(DMTCL)-1 220 kV Darbhanga - Darbhanga(DMTCL)-2 220kV Darbhanga - Mushari -1 220kV Darbhanga - Mushari -2
3	GD-1	Arrah	09-08-2024 19:51	09-08-2024 20:11	00:20	0	294	0.00%	1.10%	31443	26690	At 19:51 Hrs on 09.08.2024, 220 kV Bus-2 at 220/132 kV Arrah(PG) S/s tripped during bus bar stability testing of 220 kV Bus-1. This led to total power failure at Arrah S/s. Load loss of 294 MW reported at Arrah and Dumraon which was radially fed through Arrah S/s. 220 kV Bus-2 at Arrah was charged via Nadokhar lines at 20:11Hrs and power extended to Arrah and Dumraon.	220kV Arrah - Naubatpur D/C 220kV Arrah - Dumraon D/C 220 kV Bus -2 At Arrah
4	GD-1	Katapalli	29-08-2024 06:52	29-08-2024 07:43	00:51	290	70	0.97%	0.29%	29822	23796	At 06:52 Hrs on 29.08.2024, a fault struck B phase of 220 kV Katapalli-Hindalco-2. Line tripped immediately from Hindalco. However, breaker at Katapalli didn't open immedaitely. As LBB protection is not available at Katapalli, all lines at Katapalli tripped and total power failed at 220/132 kV Katapalli, Burla, Chiplima S/s. Hindalco also got islanded from the system. Approximate load loss of around 70 MW and generation loss of 260 MW at Burla & Chiplima HEP reported. At 07:43 Hrs, power was extended through 220 kV Lapanga - Katapali - 2.	220kV - Katapali - Lapanga 1 & 2 220kV Katapali- Bargarh 220 kV Katapali - Bolangir 220 kV Katapali - Hindalco 1 &2 220 kV Main Bus 1 & 2 at Katapali 132 kV Burla - Katapali 1 & 2 132 kV chiplma - Katapali 1 & 2 132kV Bargarh - Katapali 1 & 2 Burla hydo generation unit 2, 3, 4, 5, 6,7 Chiplima Hydro generation unit 1 & 2

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Rengpang area of Manipur Power System	03-08-2024 08:15	03-08-2024 10:02	01:47	0	1	0.00%	0.04%	2423	2295	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam-Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 08:15 Hrs of 03-08-2024, 132 kV Loktak – Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available this area. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 10:02 Hrs on 03-08-2024.	132 kV Loktak – Rengpang line
2	GD I	Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System	03-08-2024 14:24	03-08-2024 15:03	00:39	0	14	0.00%	0.55%	2423	2541	Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System and Chapakhowa area of Assam Power system were connected with rest of NER Grid through 132 kV Along-Pasighat Line. 132 kV Rupai - Chapakhpwa line was under long outage since 07:41 Hrs of 03.08.2024. At 14:24 Hrs of 03-08-2024, 132 kV Along-Pasighat Line tripped. Due to tripping of this element, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh and Chapakhowa area of Assam were isolated from NER Grid and collapsed due to no source available in these areas. Power is restored at Pasighat area by charging 132 kV Along-Pasighat line at 15:03 Hrs of 03-08-2024.	132 kV Along-Pasighat Line
3	GD I	Rengpang area of Manipur Power System	04-08-2024 05:56	04-08-2024 12:29	06:33	0	1	0.00%	0.05%	2254	1958	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam-Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 05:56 Hrs of 04-08-2024, 132 kV Loktak – Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available this area. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 12:29 Hrs on 04-08-2024.	132 kV Loktak – Rengpang line
4	GD I	Udaipur area of Tripura Power System	04-08-2024 12:31	04-08-2024 12:44	00:13	0	32	0.00%	1.38%	2195	2311	Udaipur area of Tripura Power System was connected with rest of NER Grid through 132 kV Monarchak - Udaipur line. 132 kV Palatana - Udaipur line was under planned shutdown since 09:52 Hrs of 04.08.2024. At 12:31 Hrs of 04-08-2024, 132 kV Monarchak - Udaipur line tripped. Due to tripping of this element, Udaipur area of Tripura Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply is extended to Udaipur area of Tripura Power System by charging 132 kV Monarchak - Udaipur line at 12:44 Hrs on 04.08.2024.	132 kV Monarchak-Udaipur line
5	GD I	Leshka HEP of Meghalaya Power System	07-08-2024 16:30	07-08-2024 16:41	00:11	118	0	4.26%	0.00%	2768	2857	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C lines. At 16:30 Hrs of 07.08.2024, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these lines, Leshka HEP of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat 1 at 16:41 hrs of 07.08.2024.	132 kV Myntdu Leshka - Khleihriat D/C lines
6	GD I	Khandong HEP of NEEPCO Power System	13-08-2024 07:18	13-08-2024 09:56	02:38	25	0	0.84%	0.00%	2977	2476	Khandong HEP and 132 kV S/S of Kopili HEP of Assam Power System were connected with connected to NER Power system via 132kV Khandong – Umrangsho Line, 132kV Khandong –Khliehriat 2 Line and 132kV Khandong –Kopili 2 Line. At 07:18 Hrs of 13.08.2024, 220/132kV 160 MVA ICT 1 & 2 at Kopili, 132kV Khandong –Umrangsho Line, 132kV Khandong – Khliehriat 2 Line and 132kV Khandong – Kopili 2 Line tripped due to which Khandong HEP of Assam Power System were isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Khandong HEP by charging 132kV Khandong – Khliehriat 2 Line at 09:56 Hrs of 13.08.2024	220/132kV 160 MVA ICT 1 & 2 at Kopili, 132kV Khandong –Umrangsho Line, 132kV Khandong – Khliehriat 2 Line and 132 kV Khandong – Kopili 2 Line

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD I	Rengpang area of Manipur Power System	13-08-2024 12:11	13-08-2024 12:44	00:33	0	1	0.00%	0.04%	2493	2554	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam-Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 12:11 Hrs of 13-08-2024, 132 kV Loktak – Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available this area. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 12:44 Hrs on 13-08-2024.	132 kV Loktak-Rengpang Line
8	GD I	Kolasib area, Bairabi S/S and Turial Generation of Mizoram	13-08-2024 15:28	13-08-2024 17:35	02:07	54	5	2.06%	0.17%	2626	2915	Kolasib area, Bairabi S/S and Turial Generation of Mizoram Power System were connected with rest of NER Grid through 132 kV Badarpur - Kolasib Line, 132 kV Aizawl - Kolasib Line and 132 kV Turial-Kolasib Line. At 15:28 Hrs of 13-08-2024, 132 kV Badarpur - Kolasib Line, 132 kV Aizawl - Kolasib Line and 132 kV Turial-Kolasib Line tripped. Due to tripping of these elements, Kolasib area, Bairabi S/S and Turial Generation of Mizoram Power System were isolated from NER Grid and collapsed due to load generation mismatch. Power was extended to Kolasib area, Bairabi S/S of Mizoram Power System by charging 132 kV Badarpur-Kolasib Line at 17:35 Hrs of 13.08.2024.	132 kV Badarpur - Kolasib Line, 132 kV Aizawl - Kolasib Line and 132 kV Turial-Kolasib Line
9	GD I	Rengpang area of Manipur Power System	14-08-2024 09:30	14-08-2024 10:52	01:22	0	4	0.00%	0.15%	2804	2676	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam-Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 09:30 Hrs of 14-08-2024, 132 kV Loktak – Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 10:52 Hrs on 14-08-2024.	132 kV Loktak-Rengpang line
10	GD I	Baramura area of Tripura power system	14-08-2024 11:20	14-08-2024 11:40	00:20	0	12	0.00%	0.43%	2531	2791	Baramura area of Tripura Power System was connected with rest of NER Grid through 132 kV Baramura-Gamaitila line and 132 kV Baramura-Jirania line. At 11:20 Hrs of 14-08-2024, 132 kV Baramura-Gamaitila line and 132 kV Baramura-Jirania line tripped. Due to tripping of these elements, Baramura area of Tripura Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was restored by charging 132 kV Baramura-Jirania Line at 11:40 hrs.	132 kV Baramura-Gamaitila line and 132 kV Baramura-Jirania line
11	GD I	Rengpang area of Manipur Power System	14-08-2024 11:32	14-08-2024 19:07	07:35	0	4	0.00%	0.14%	2552	2791	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam-Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 11:32 Hrs of 14-08-2024, 132 kV Loktak – Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 19:07Hrs on 14-08-2024.	132 kV Loktak-Rengpang line
12	GD I	Karong area of Manipur Power System	14-08-2024 14:59	14-08-2024 16:33	01:34	0	13	0.00%	0.42%	2822	3112	Karong area of Manipur Power System was connected with rest of NER Grid via 132 kV Karong - Kohima Line. 132 kV Imphal (MSPCL) - Karong Line was under tripped condition since 11:13 Hrs of 14.08.2024. At 14:59 Hrs of 14.08.2024, 132 kV Karong - Kohima Line tripped. Due to tripping of this element, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Karong area of Manipur Power System by charging 132 kV Imphal (MSPCL) - Karong Line at 16:33 Hrs of 14.08.2024.	132 kV Karong - Kohima Line
13	GD I	Saitual, Vankal and Khawzawl areas of Mizoram power system	15-08-2024 17:56	15-08-2024 18:08	00:12	0	13	0.00%	0.52%	2853	2497	Saitual, Vankal and Khawzawl areas of Mizoram Power System were connected with rest of NER Grid via 132 kV Zuangtui - Saitual line. At 17:56 Hrs of 15-08-2024, 132 kV Zuangtui - Saitual line tripped. Due to tripping of this line, Saitual, Vankal and Khawzawl areas of Mizoram Power System were isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Saitual, Vankal and Khawzawl areas of Mizoram Power System by charging 132 kV Zuangtui – Saitual line at 18:08 hrs.	132 kV Zuangtui - Saitual line

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
14	GD II	Turial Generating Units of NEEPCO	15-08-2024 19:18	15-08-2024 19:32	00:14	54	0	1.78%	0.00%	3040	2926	Turial Generating Units of Mizoram Power System was connected with rest of NER Grid through 132 kV Turial-Kolasib Line. At 19:18 Hrs of 15-08-2024, 132 kV Turial-Kolasib Line tripped. Due to tripping of this element, Turial Generating Units of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Turial Generating Units by charging 132 kV Turial-Kolasib Line at 19:32 Hrs of 15.08.2024.	132 kV Turial-Kolasib Line
15	GD I	Melriat and Lunglei areas of Mizoram power system	15-08-2024 19:21	15-08-2024 19:38	00:17	0	48	0.00%	1.65%	3019	2911	Melriat and Lunglei areas of Mizoram Power System were connected with rest of NER Grid via 132 kV Luangmual – Melriat line. 132kV Serchip – Lunglei line was kept open. At 17:56 Hrs of 15-08-2024, 132 kV Luangmual – Melriat line tripped. Due to tripping of this line, Melriat and Lunglei areas of Mizoram Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Melriat and Lunglei areas of Mizoram Power System by charging 132 kV Luangmual - Melriat line at 19:38 hrs.	132 kV Luangmual – Melriat line
16	GD I	Rengpang area of Manipur Power System	16-08-2024 08:46	17-08-2024 08:33	23:47	0	1	0.00%	0.04%	2560	2421	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam -Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 08:46 Hrs of 16-08-2024, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 08:33 Hrs on 17-08-2024.	132 kV Loktak - Rengpang line
17	GD I	Leshka HEP of Meghalaya Power System	16-08-2024 13:30	16-08-2024 13:48	00:18	118	0	4.18%	0.00%	2821	2768	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C lines. At 13:30 Hrs of 16.08.2024, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these lines, Leshka HEP of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat 1 at 13:48 hrs of 16.08.2024.	132 kV Myntdu Leshka - Khleihriat D/C lines
18	GD I	Saitual, Vankal and Khawzawl areas of Mizoram power system	16-08-2024 14:48	16-08-2024 14:53	00:05	0	11	0.00%	0.38%	2884	2896	Saitual, Vankal and Khawzawl areas of Mizoram Power System were connected with rest of NER Grid via 132 kV Zuangtui - Saitual line. At 14:48 Hrs of 16-08-2024, 132 kV Zuangtui - Saitual line tripped. Due to tripping of this line, Saitual, Vankal and Khawzawl areas of Mizoram Power System were isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Saitual, Vankal and Khawzawl areas of Mizoram Power System by charging 132 kV Zuangtui – Saitual line at 14:53 hrs.	132 kV Zuangtui - Saitual line
19	GD I	Rengpang area of Manipur Power System	17-08-2024 10:42	18-08-2024 16:33	29:51	0	3	0.00%	0.11%	2536	2694	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam -Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 10:42 Hrs of 17-08-2024, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 16:33 Hrs on 18-08-2024.	132 kV Loktak - Rengpang line

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
20	GD I	Dhemaji & Silapathar area of Upper Assam power system	17-08-2024 11:58	17-08-2024 12:07	00:09	0	36	0.00%	1.33%	2573	2705	Dhemaji and Silapathar areas are radially connected through 132 kV North Lakhimpur- Dhemaji line. At 11:58 Hrs of 17-08-2024, 132 kV North Lakhimpur- Dhemaji line tripped. Due to tripping of this element, Dhemaji & Silapathar area of Upper Assam Power System was isolated from NER Grid. Power supply was extended to Dhemaji area by charging 132 kV North Lakhimpur- Dhemaji line at 12:07 Hrs on 17-08-2024.	132 kV North Lakhimpur- Dhemaji line
21	GD I	Gossaigaon area of Assam power system	17-08-2024 17:14	17-08-2024 18:02	00:48	0	4	0.00%	0.14%	2707	2842	Gossaigon area of Assam Power System was connected with NER Power system via 132 kV Dhaligaon-Gossaigaon-Gauripur link (132 kV Gauripur- Gossaigaon was kept open due to system requirement). At 17:14 Hrs of 17.08.2024, 132kV Dhaligaon-Gossaigaon line tripped due to which Gosaigaon area of Assam Power System was isolated from NER Grid and collapsed due to no source available in the area. Power supply was extended by charging 132kV Dhaligaon–Gossaigaon line at 18:02 Hrs of 17.08.2024.	132 kV Dhaligaon-Gossaigaon line
22	GD I	Rangia, Amingaon, Tangla, Sipajhar & Kamalpur Areas of Assam Power System	17-08-2024 17:18	17-08-2024 17:25	00:07	0	164	0.00%	5.78%	2720	2837	At 17:18 Hrs of 17.08.2024, 220 kV Rangia-BTPS D/C & 220kV Amingaon-Rangia D/C tripped due to which SPS in Rangia was operated and subsequently Rangia, Amingaon, Tangla, Sipajhar & Kamalpur Areas of Assam Power System were isolated from NER Grid and collapsed due to no source available in the areas. Power supply was extended by charging 220kV Salakati – Rangia I line at 17:25 Hrs of 17.08.2024.	220 kV Rangia-BTPS D/C & 220kV Amingaon-Rangia D/C lines
23	GD I	Ziro, Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh and Margerita, Rupai & Chapakhowa area of Assam power system	17-08-2024 20:17	17-08-2024 20:46	00:29	0	109	0.00%	3.20%	3520	3409	Ziro, Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System and Chapakhowa and Rupai area of Assam Power System were connected with rest of NER Grid through 132 kV Ranganadi - Ziro Line, 132 kV Tinsukia-Margherita and 132 kV Rupai - Tinsukia line.At 20:10 Hrs of 17-08-2024, 132 kV Tinsukia-Margherita Line tripped and at 20:17 Hrs of 17-08-2024, 132 kV Ranganadi - Ziro Line, and 132 kV Rupai - Tinsukia Line tripped. Due to tripping of these elements, Ziro, Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System and Margherita, Rupai & Chapakhowa areas of Assam Power System were isolated from NER Grid.Power supply was extended to Ziro, Daporizo, Basar, Along, Pasighat, areas of Arunachal Pradesh Power System by charging 132 kV Ranganadi - Ziro Line at 20:46 Hrs of 17.08.2024. Power supply was extended to and Chapakhowa and Rupai area of Assam Power System and Roing, Tezu and Namsai areas of Arunachal Pradesh Power System by first charging 132 kV Tinsukia-Margherita Line at 20:33 Hrs of 17.08.2024. 132 kV Roing - Pasighat Line was kept open to identify the fault.	132 kV Tinsukia-Margherita Line, 132 kV Ranganadi - Ziro Line, and 132 kV Rupai - Tinsukia Line
24	GD I	Roing, Tezu and Namsai areas of Arunachal Pradesh and Margerita, Rupai & Chapakhowa area of Assam power system	17-08-2024 22:05	17-08-2024 22:39	00:34	0	80	0.00%	2.35%	3520	3409	Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa, Rupai and Margherita areas of Assam Power System were connected with rest of NER Grid through 132 kV Tinsukia-Margherita, 132 kV Rupai - Margherita, 132 kV Rupai - Tinsukia line, 132 kV Rupai -Chapakhowa line, 132 kV Roing - Chapakhowa D/C lines, 132 kV Roing - Tezu Line and 132 kV Namsai - Tezu Line. At 22:05 Hrs of 17-08-2024, 132 kV Tinsukia-Margherita, 132 kV Rupai – Margherita Line, 132 kV Rupai - Tinsukia line and at 22:08 Hrs of 17-08-2024, 132 kV Rupai - Chapakhowa line and 132 kV Roing - Chapakhowa D/C lines tripped. Due to tripping of these elements, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa, Rupai and Margherita areas of Assam Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Roing, Tezu, Namsai areas of Arunachal Pradesh Power System by charging 132 kV Roing - Pasighat Line at 22:39 Hrs of 17.08.2024 and Chapakhowa, Rupai and Margherita areas of Assam Power System by first charging 132 kV Rupai – Tinsukia Line at 22:25 Hrs of 17-08-2024 and by subsequently charging the rest of the lines.	132 kV Tinsukia-Margherita, 132 kV Rupai – Margherita Line, 132 kV Rupai - Tinsukia line, 132 kV Rupai - Chapakhowa line and 132 kV Roing - Chapakhowa D/C lines
25	GD I	Khupi, Tenga & Dikshi areas of Arunachal Pradesh Power System	18-08-2024 13:33	18-08-2024 14:43	01:10	19	18	0.82%	0.73%	2313	2464	Khupi, Tenga & Dikshi areas of Arunachal Pradesh Power System were connected with rest of NER Power system via 132 kV Balipara- Tenga line and 400/132 kV, 3x40 MVA ICT at Kameng. At 13:33 Hrs of 18-08-2024, 132 kV Balipara-Tenga line & ICT at Kameng tripped which resulted in blackout of Khupi, Tenga & Dikshi areas of Arunachal Pradesh Power system. Power was restored to the Tenga, Tippi area by charging 132kV Balipara-Tenga line at 14:36 hrs and to Khupi area by charging 132kV Tenga-Khupi at 14:43 hrs of 18.08.2024.	132 kV Balipara-Tenga line & ICT at Kameng

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
26	GD I	Leshka HEP of Meghalaya Power System	18-08-2024 17:24	18-08-2024 17:47	00:23	119	0	4.50%	0.00%	2643	2563	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C lines. At 17:24 Hrs of 18-08-2024, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these lines, Leshka HEP of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat 1 at 17:47 hrs.	132 kV Myntdu Leshka - Khleihriat D/C lines
27	GD I	Rengpang area of Manipur Power System	19-08-2024 21:26	20-08-2024 17:14	19:48	0	1	0.00%	0.03%	3299	2989	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 21:26 Hrs of 19-08-2024, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 17:14 Hrs of 20.08.2024.	132 kV Loktak-Rengpang line
28	GD I	Rengpang area of Manipur Power System	23-08-2024 01:48	23-08-2024 06:59	05:11	0	1	0.00%	0.04%	2995	2720	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 01:48 Hrs of 23-08-2024, 132kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 06:59 Hrs of 23.08.2024.	132 kV Loktak-Rengpang Line
29	GD I	Serchhip area of Mizoram Power System	23-08-2024 09:30	23-08-2024 09:40	00:10	0	3	0.00%	0.11%	2768	2615	Serchhip area of Mizoram Power System was connected with rest of NER Grid via 132 kV Zuangtui - Serchhip line. At 09:30 Hrs of 23-08-2024, 132 kV Zuangtui – Serchhip line tripped. Due to tripping of this line, Serchhip areas of Mizoram Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Serchhip areas of Mizoram Power System by charging 132 kV Zuangtui – Serchhip line at 09:40 hrs of 23.08.2024.	132 kV Zuangtui – Serchhip line
30	GD I	Leshka Generating station of Meghalaya Power System	23-08-2024 11:08	23-08-2024 11:19	00:11	118	0	4.35%	0.00%	2710	2688	Leshka Generating station of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C Lines. At 11:08 Hrs of 23.08.2024, 132 kV Myntdu Leshka - Khleihriat D/C Lines tripped. Due to tripping of these elements, Leshka Generating station of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Leska Generating station by charging 132 kV Myntdu Leshka - Khleihriat 1 at 11:19 hrs of 23.08.2024.	132 kV Myntdu Leshka - Khleihriat D/C Lines
31	GD I	Rengpang area of Manipur Power System	23-08-2024 12:14	23-08-2024 23:15	11:01	0	3	0.00%	0.11%	2597	2674	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam -Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 12:14 Hrs of 23-08-2024, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 23:15 Hrs on 23-08-2024.	132 kV Loktak - Rengpang line

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
32	GD I	Kohima, Zhadima, Chiephobozou, Wokha and New Secretariat areas of Nagaland power system	23-08-2024 13:51	23-08-2024 14:21	00:30	0	20	0.00%	0.71%	2601	2810	Kohima, Zhadima, Chiephobozou, Wokha and New Secretariate areas of Nagaland Power System were connected with rest of NER Grid through 132kV Dimapur - Kohima line, 132kV Karong – Kohima and 132kV Kohima – Zhadima lines. 132kV Sanis – Wokha was under planned shutdown w.e.f. 08:35hrs of 23-08-2024. 132kV Koima-Meluri line was under long outage prior to event since 10:05 Hrs of 27.09.2023. At 13:51 Hrs of 23-08-2024, 132 kV Dimapur - Kohima line, 132 kV Karong – Kohima and 132 kV Kohima – Zhadima lines tripped. Due to tripping of these elements, Kohima, Zhadima, Chiephobozou, Wokha and New Secretariate areas of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Kohima, Zhadima, Chiephobozou, Wokha and New Secretariat areas by charging 132 kV	132 kV Dimapur - Kohima line, 132 kV Karong – Kohima and 132 kV Kohima – Zhadima lines
33	GD I	Leshka HEP of Meghalaya Power System	23-08-2024 16:38	23-08-2024 17:03	00:25	119	0	4.34%	0.00%	2741	3044	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C lines. At 16:38 Hrs of 23-08-2024, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these lines, Leshka HEP of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat 1 at 17:03 hrs.	132 kV Myntdu Leshka - Khleihriat D/C lines
34	GD I	Pasighat areas of Arunachal Pradesh Power System	24-08-2024 00:54	24-08-2024 01:53	00:59	0	8	0.00%	0.28%	3059	2836	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Pasighat & 132 kV Roing-Pasighat lines. At 00:54 Hrs of 24-08-2024, 132 kV Along-Pasighat Line and 132 kV Roing-Pasighat line tripped. Due to tripping of these elements, Pasighat area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Pasighat area by charging 132 kV Along-Pasighat Line at 01:53 Hrs of 24.08.2024.	132 kV Along-Pasighat Line and 132 kV Roing-Pasighat line
35	GD I	Pasighat areas of Arunachal Pradesh Power System	24-08-2024 02:01	24-08-2024 04:47	02:46	0	8	0.00%	0.30%	2568	2666	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Pasighat & 132 kV Roing-Pasighat lines. 132 kV Roing-Pasighat line was under faulty condition. At 02:01 Hrs of 24-08-2024, 132 kV Along-Pasighat Line tripped. Due to tripping of these elements, Pasighat area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Pasighat area by charging 132 kV Along-Pasighat Line at 04:47 Hrs of 24.08.2024.	132 kV Along-Pasighat Line
36	GD I	Khupi area of Arunachal Pradesh Power System	25-08-2024 22:13	25-08-2024 22:58	00:45	0	3	0.00%	0.10%	3153	3121	Khupi area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Tenga-Khupi and 132 kV Kameng-Khupi lines. At 22:13 Hrs of 25-08-2024, 132 kV Tenga-Khupi and 132 kV Kameng-Khupi lines tripped. Due to tripping of these elements, Khupi area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was restored to Khupi area of Arunachal Pradesh Power System by charging 132kV Tenga-Khupi line at 23:58 hrs of 25.08.024. 132kV Kameng-Khupi line was charged at 00:18 Hrs of 26.08.2024	132 kV Tenga-Khupi and 132 kV Kameng-Khupi lines
37	GD I	Gohpur Area of Assam Power System	26-08-2024 06:37	26-08-2024 07:36	00:59	0	9	0.00%	0.39%	2667	2285	Gohpur area of Assam Power System was connected with rest of NER Grid through 132kV Gohpur-BNC(PG), 132kV Gohpur – Nirjuli, 132 kV Gohpur- N. Lakhimpur D/C, 132kV Gohpur – Pavoi D/C and 132 kV Gohpur – Itanagar lines. At 06:37 Hrs of 26.08.2024, 132kV Gohpur-BNC(PG), 132kV Gohpur – Nirjuli, 132kV Gohpur - N. Lakhimpur D/C, 132kV Gohpur – Pavoi D/C and 132kV Gohpur – Itanagar lines tripped. Due to tripping of these elements, Gohpur area of Assam Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Gohpur area of Assam Power System by charging 132kV Gohpur – Nirjuli at 07:36 Hrs of of 26-08-2024.	132kV Gohpur-BNC(PG), 132kV Gohpur – Nirjuli, 132kV Gohpur - N. Lakhimpur D/C, 132kV Gohpur – Pavoi D/C and 132kV Gohpur – Itanagar lines
38	GD I	Pasighat areas of Arunachal Pradesh Power System	26-08-2024 09:42	26-08-2024 13:38	03:56	0	6	0.00%	0.24%	2384	2546	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Pasighat & 132 kV Roing-Pasighat lines. 132 kV Roing-Pasighat Line was under outage since 00:54 Hrs of 24.08.2024. At 09:42 Hrs of 26-08-2024, 132 kV Along-Pasighat Line tripped. Due to tripping of these elements, Pasighat area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Pasighat area by charging 132 kV Along-Pasighat Line at 13:38 Hrs of 26.08.2024.	132 kV Along-Pasighat Line

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
39	GD I	Serchhip area of Mizoram power system	26-08-2024 21:32	26-08-2024 22:30	00:58	0	3	0.00%	0.09%	3147	3286	Serchhip area of Mizoram Power System was connected with rest of NER Grid via 132 kV Zuangtui - Serchhip line. At 21:32 Hrs of 26-08-2024, 132 kV Zuangtui – Serchhip line tripped. Due to tripping of this line, Serchhip areas of Mizoram Power System was isolated from NER Grid and collapsed due to no source available in this area. To prevent load loss, power is fed to Serchhip via Zuangtui -Saitual- Vankal- Khawzawl E.Lungdar- Serchhip link.	132 kV Zuangtui – Serchhip line
40	GD I	Rengpang area of Manipur Power system	27-08-2024 11:16	27-08-2024 11:59	00:43	0	3	0.00%	0.11%	2508	2760	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam -Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 11:16 Hrs of 27-08-2024, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 11:59 Hrs on 27-08-2024.	132 kV Loktak - Rengpang line
41	GD I	Margherita area of Assam Power System	28-08-2024 01:13	28-08-2024 01:31	00:18	0	20	0.00%	0.69%	2548	2910	Margherita area of Assam Power System was connected with rest of NER Grid through 132 kV Tinsukia – Margherita & 132 kV Rupai- Margherita line. At 01:13 Hrs of 28-08-2024, 132 kV Tinsukia – Margherita & 132 kV Rupai- Margherita line tripped. Due to tripping of these elements, Margherita area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was restored to Margherita by charging 132 kV Rupai- Margherita line at 01:31 Hrs of 28.08.2024.	132 kV Tinsukia – Margherita & 132 kV Rupai-Margherita line
42	GD I	Umrangshu area of Assam Power System	28-08-2024 09:31	28-08-2024 12:38	03:07	0	1	0.00%	0.04%	2323	2638	Umrangshu area of Assam Power System was connected with rest of NER Grid through 132 kV Haflong-Umrangshu. (132 kV Khandong-Umrangshu line was under planned shutdown since 08:55 hrs of 28.08.2024) At 09:31 Hrs of 28-08-2024, 132 kV Haflong-Umrangshu line tripped. Due to tripping of theseelements, Umrangshu area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was restored by charging 132 kV Haflong-Umrangshu line at 12:38 Hrs of 28.08.2024.	132 kV Haflong-Umrangshu line
43	GD I	Sanis area of Nagaland Power System and Doyang HEP	28-08-2024 13:33	28-08-2024 13:55	00:22	73	1	2.92%	0.04%	2502	2835	Sanis area of Nagaland Power System and Doyang HEP were connected with rest of NER Grid through 132kV Doyang – Dimapur D/C lines. 132kV Doyang – Mokochung line and 132kV Wokha-Sanis line was under outage since 10:33 Hrs and 09:53 Hrs of 28.08.2024 respectively. At 13:33 Hrs of 28-08-2024, 132 kV Doyang – Dimapur D/C lines along with Doyang Unit 1,2 &3 tripped. Due to tripping of these elements, Sanis area of Nagaland Power System and Doyang HEP of Assam Power System were isolated from NER Grid and collapsed due to load generation mismatch in this area. Power was extended to Sanis area of Nagaland Power System and Doyang HEP by charging 132kV Doyang -	132 kV Doyang – Dimapur D/C lines along with Doyang Unit 1,2 &3
44	GD I	New Shillong Substation of Meghalaya Power System	28-08-2024 16:51	28-08-2024 17:39	00:48	0	0	0.00%	0.00%	2351	2962	New Shillong Substation of Meghalaya Power System was connected with rest of NER Grid through 220kV Mawngap-New Shillong line D/C lines. At 16:51 Hrs of 28-08-2024, 220 kV Mawngap-New Shillong line D/C lines tripped. Due to tripping of these elements, New Shillong Substation of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended New Shillong Substation of Meghalaya Power System by charging 220 kV Mawngap-New Shillong D/C lines at 17:39 hrs of 28.08.2024.	220 kV Mawngap-New Shillong D/C lines
45	GD I	Rengpang area of Manipur power system	29-08-2024 11:37	29-08-2024 17:15	05:38	0	3	0.00%	0.11%	2545	2801	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam -Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 11:37 Hrs of 29-08-2024, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 17:15 Hrs on 29-08-2024.	132 kV Loktak - Rengpang line

Details of Grid Events during the Month of Aug 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
46	GD I	Karbi Langpi HEP of Assam Power System	29-08-2024 11:45	29-08-2024 12:34	00:49	101	0	3.97%	0.00%	2543	2830	Karbi Langpi HEP of Assam Power System was connected with rest of NER Grid through 132 kV Sarusajai-Karbi Langpi 2 line. 132 kV Sarusajai-Karbi Langpi 1 line was under state approved planned shutdown. At 11:45 Hrs of 29-08-2024, 132 kV Sarusajai-Karbi Langpi 2 line tripped. Due to tripping of this element, Karbi Langpi HEP of Assam Power System was isolated from NER Grid. Power was extended to Karbi Langpi HEP of Assam Power System by charging 132 kV Sarusajai-Karbi Langpi 1 line at 12:34 hrs of 29.08.2024.	132 kV Sarusajai-Karbi Langpi 2 line
47	GD I	Karong area of Manipur Power System	29-08-2024 12:04	29-08-2024 12:23	00:19	0	10	0.00%	0.36%	2437	2813	Karong area of Manipur Power System was connected with rest of NER Grid through 132 kV Karong Kohima Line. 132 kV Yurembam-Karong line was under outage condition since 09:19 hrs of 29.08.2024. At 12:01 Hrs of 29-08-2024, 132 kV Karong-Kohima Line tripped. Due to tripping of this element, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Karong area of Manipur Power System by charging 132 kV Karong-Kohima Line at 12:23 Hrs of 29.08.2024	132 kV Karong-Kohima Line
48	GD I	Karong area of Manipur Power System	29-08-2024 12:35	29-08-2024 13:30	00:55	0	7	0.00%	0.25%	2462	2835	Karong area of Manipur Power System was connected with rest of NER Grid through 132 kV Karong Kohima Line. 132 kV Yurembam-Karong line was under outage condition since 09:19 hrs of 29.08.2024. At 12:35 Hrs of 29-08-2024, 132 kV Karong-Kohima Line tripped. Due to tripping of this element, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Karong area by charging 132 kV Imphal-Karong line at 13:30 Hrs of 29.08.2024.	132 kV Karong-Kohima Line
49	GD I	Rengpang area of Manipur Power System	30-08-2024 10:03	30-08-2024 22:11	12:08	0	3	0.00%	0.12%	2577	2420	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak – Rengpang line. 132 kV Jiribam -Rengpang line was under outage since 18:18 Hrs of 17.11.2023. At 10:03 Hrs of 30-08-2024, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak – Rengpang line at 22:11 Hrs on 30-08-2024.	132 kV Loktak - Rengpang line
50	GD I	Margherita area of Assam Power System	30-08-2024 23:40	31-08-2024 00:37	00:57	0	20	0.00%	0.62%	2993	3203	Margherita area of Assam power system is connected with the rest of the grid through 132 kV Tinsukia-Margherita and 132 kV Rupai-Margherita lines. At 23:40 Hrs of 30.08.2024, 132 kV Tinsukia-Margherita and 132 kV Rupai-Margherita lines tripped. Due to tripping of these elements, Margherita area of Assam power system got seperated from NER grid due to no source available in this area. Power was extended to Margherita area by charging 132 kV Rupai-Margherita line at 00:37 Hrs of 31.08.2024.Subsequently, 132 kV Tinsukia-Margherita line was charged at 00:58 Hrs of 31.08.2024.	132 kV Tinsukia-Margherita and 132 kV Rupai-Margherita lines

21. NEW ELEMENTS COMMISSIONED* IN AUGUST 2024

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
SR	1	TUTICORIN	JSW Renew Energy Ltd	LOT-7/Wind	18.9	207.9	13.08.2024
	2	TUTICORIN	JSW Renew Energy Two Limited	LOT-15/Wind	10.8	302.4	23.08.2024
	3	TUTICORIN	JSW_NEO	LOT-3/Wind	13.5	137.7	20.08.2024
NR	4	PANKI TPS(Stage CTPS)	UPRVUNL	Unit No -1/coal	660	660	06.08.2024
				Total Coal/Thermal addition	**660**		
				Total Wind Generation addition	**43**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
ER	1	PGCIL	ARA (PG)	ICT-4	220/132	200	15.08.2024
NR	2	UPRVUNL	Panki TPS (UP)	ICT-1	400/21	825	06.08.2024
	3	PSTCL	Ropar(PSTCL)	ICT-1	400/220/33	500	10.08.2024
	4	PSTCL	Ropar(PSTCL)	ICT-2	400/220/33	500	10.08.2024
	5	UPRVUNL	Jawaharpur_TPS(UP)	ICT-3	400/220/33	500	14.08.2024
	6	UPRVUNL	Jawaharpur_TPS(UP)	ICT-4	400/220/33	500	22.08.2024
	7	POWERGRID	Bikaner(PG)	ICT-3	400/220/33	500	30.08.2024
	8	Tehri PSP	Tehri(THDC)	ICT-5	420 /15.75	306	31.08.2024
WR	9	Mumbai Urja Marg Ltd. (MUML)	Vapi-II S/s	ICT-1	400/220	500	20.08.2024
	10	Mumbai Urja Marg Ltd. (MUML)	Vapi-II S/s	ICT-2	400/220	500	18.08.2024
SR	11	GADAG GTL	GADAG PSS	ICT-1	400/220/33	500	30.08.2024
	12	GADAG GTL	GADAG PSS	ICT-2	400/220/33	500	30.08.2024
					Total (MVA)	**5831**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
ER	1	BSPTCL	220KV-PUSAULI-NADHOKAR-2	6.504	HTLS Conductor	10.08.2024
	2	OPTCL	132KV-BARIPADA(PG)-BANGIRIPOSHI-2	31.23	ACSR Panther	01.08.2024
SR	3	GADAG GTL	400KV KUDGI_PG - GADAG PSS Line-1	93.5	ACSS/AW 478mm	30.08.2024
	4	GADAG GTL	400KV KUDGI_PG - GADAG PSS Line-2	93.5	ACSS/AW 478mm	30.08.2024
NR	5	HVPNL	220kV Abdullapur(PG)-Rajokheri (HV)-2	22.35	MOOSE	05.08.2024
	6	HVPNL	220kV Abdullapur(PG)-Rajokheri (HV)-1	22.35	MOOSE	06.08.2024
	7	PBTL	765kV Fatehgarh_II(PG)-Bhadla_2 (PG)-4	202.23	AL59 Zebra	14.08.2024
	8	POWERGRID	400kV Tehri(THDC)-Koteshwar(PG)-3	13.5	Quad Moose	28.08.2024
WR	9	MUML	220 kV Vapi-II-Sayali Ckt 1	22.97	ACSS HTLS	29.08.2024
	10	MUML	220 kV Vapi-II-Sayali Ckt 2	22.97	ACSS HTLS	23.08.2024
			Total ckt km	**531.1**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
SR	1	TNTRANSCO	400KV VIRUDHUNAGAR-KAYATHAR Line-1 (Bypass at Gantry of 400kV Virudhunagar)	88.637	QUAD MOOSE	14.08.2024
	2	TNTRANSCO	400KV VIRUDHUNAGAR-THENNAMPATTY Line-1 (Bypass at Gantry of 400kV Virudhunagar)	74.529	QUAD MOOSE	14.08.2024
WR	3	MUML	400 kV Vapi-II-Kakrapar3&4 Ckt 1	111.67	AAAC Moose	04.08.2024
	4	MUML	400 kV Vapi-II-Vapi(PG) Ckt 1	5.67	AAAC Moose	03.08.2024
	5	MUML	400 kV Vapi-II-Kakrapar3&4 Ckt 2	111.67	AAAC Moose	23.08.2024
	6	Vedanta Ltd.	400 kV Vedanta - Kotra (Temporary) Line 2	24.72	Quad ACSR Moose	23.08.2024

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
NR	1	UPPTCL	400kV, 125 MVAr Bus Reactor at Shamli(UP)	400	125	14.08.2024
WR	2	MUML	125 MVAR Bus Reactor at 400KV Vapi-II S/s	400	125	21.08.2024
SR	3	GADAG GTL	420KV Bus Reactor 1 at Gadag PSS	400	125	30.08.2024
				Total (MVAr)	**375**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

*Includes first time charging (FTC) as well

विद्युत विभव रूपरेखा माह - अगस्त 2024 VOLTAGE PROFILE - August 2024

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	792	745	772
2		दालिपली DARLIPALI	0%	100%	0%	0%	0	790	762	776
3		गया GAYA	0%	100%	0%	0%	0	792	736	769
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	794	739	764
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	798	768	784
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	794	749	771
7		राँची RANCHI	0%	100%	0%	0%	0	794	763	781
8		सासाराम SASARAM	0%	100%	0%	0%	1	802	738	767
1		आगरा AGRA	0%	100%	0%	0%	0	800	748	780
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	801	728	773
3		अजमेर AJMER	0%	99%	1%	1%	5	803	750	787
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	796	740	772
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	785	754	770
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	783	753	768
7		अंता ANTA	0%	100%	0%	0%	0	794	762	780
8		बलिया BALLIA	0%	100%	0%	0%	0	789	731	766
9		बारा BARA	0%	100%	0%	0%	0	793	753	770
10		भाडला BHADLA	0%	100%	0%	0%	0	795	748	780
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	0	800	750	782
12		भिवानी BHIWANI	0%	100%	0%	0%	0	798	750	781
13		बीकानेर BIKANER	0%	100%	0%	0%	0	799	742	782
14		बरेली BAREILLY	0%	100%	0%	0%	2	805	738	774
15		चित्ताड़गढ़ CHITTORGARH	0%	98%	2%	2%	13	805	766	787
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	794	749	777
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	797	742	773
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	794	762	780
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	1	804	746	776
20		हापुड़ HAPUR	0%	100%	0%	0%	0	801	736	770
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	799	737	767
22		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	794	742	773
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	796	742	773
24		खेतरी KHETRI	0%	100%	0%	0%	0	799	735	779
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	797	734	771
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	777	743	760
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	796	735	768
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	794	732	763
29		मेरठ MEERUT	0%	100%	0%	0%	0	799	749	777
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	1	801	737	771
31		मोगा MOGA	0%	100%	0%	0%	0	799	735	781
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	782	748	766
33		उरई ORAI	0%	99%	1%	1%	7	806	749	785
34		फागी PHAGI	0%	100%	0%	0%	0	801	756	783
35		रामपुर RAMPUR	0%	100%	0%	0%	0	802	734	769
36		उन्नाव UNNAO	0%	100%	0%	0%	0	789	734	763
37		वाराणसी VARANASI	0%	100%	0%	0%	0	793	747	775
1		अकोला AKOLA	0%	100%	0%	0%	0	796	755	775
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	799	745	775
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	789	753	775
4		भुज BHUJ	0%	100%	0%	0%	0	794	755	779
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	786	744	771
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	789	757	772
7		बीना BINA	0%	100%	0%	0%	0	799	753	782
8		बनसकंठा BANASKANTHA	0%	99%	1%	1%	6	803	761	785
9		चापा CHAMPA	0%	100%	0%	0%	3	804	757	785
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	793	752	777
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	784	754	770
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	791	761	778
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	795	751	776
14		गदरवाड़ा GADARWARA	0%	99%	1%	1%	5	803	765	788
15		ग्वालियर GWALIOR	0%	100%	0%	0%	1	802	752	783
16		इंदौर INDORE	0%	100%	0%	0%	0	789	752	773
17		जबलपुर JABALPUR	0%	99%	1%	1%	8	804	758	788
18	पश्चिमी क्षेत्र WR	खंडवा KHANDWA	0%	100%	0%	0%	0	790	754	775
19		कोरडी KORADI	0%	100%	0%	0%	0	781	750	765
20		लकाडिया LAKADIYA	0%	99%	1%	1%	4	802	756	783
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	794	764	781
22		पड़घे PADGHE	0%	100%	0%	0%	3	802	748	779
23		परली PARLI	0%	99%	1%	1%	4	803	751	785
24		पूणे PUNE	0%	100%	0%	0%	2	804	740	779
25		राजनन्दगांव RAJNANDGAON	0%	99%	1%	1%	8	808	762	787
26		सासन SASAN	0%	100%	0%	0%	0	793	760	779
27		सतना SATNA	0%	99%	1%	1%	9	805	763	787
28		सिवनी SEONI	0%	100%	0%	0%	1	802	761	782
29		सीपत SIPAT	0%	100%	0%	0%	0	787	761	773
30		सोलापुर SOLAPUR	0%	100%	0%	0%	0	800	753	783
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	774	749	760
32		तामनार TAMNAR	0%	100%	0%	0%	0	794	765	781
33		वड़ोदरा VADODARA	0%	100%	0%	0%	1	804	753	779
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	796	763	783
35		वर्धा WARDHA	0%	100%	0%	0%	3	807	748	782
36		वरोरा WARORA	0%	100%	0%	0%	1	801	742	785
1		अरियलूर ARIYALUR	0%	96%	4%	4%	30	806	740	787
2		कड़पा CUDDAPAH	0%	98%	2%	2%	12	805	755	785
3		चित्तूर CHILAKALURIPETA	0%	99%	1%	1%	6	802	738	777
4		कर्नूल KURNOOL	0%	100%	0%	0%	0	798	749	780
5		महेश्वरम MAHESWARAM	0%	99%	1%	1%	10	803	742	784
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	92%	8%	8%	56	808	741	789
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	793	754	776
8		नार्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	2	806	755	777
9		रायचूर RAICHUR	0%	100%	0%	0%	0	796	750	779
10		श्रीकाकुलम SRIKAKULAM	0%	97%	3%	3%	19	806	744	780
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	800	746	772
12		वेमागिरी VEMAGIRI	0%	93%	7%	7%	51	809	748	781
13		वारंगल WARANGAL	0%	100%	0%	0%	0	800	758	775
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	417	396	405
2		बिस्वनाथ चारिआली BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	414	399	406
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	416	402	409
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	414	395	404
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	412	396	402
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	412	396	402
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	416	391	403
8		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	411	400	406
9	पूर्वोत्तर क्षेत्र NER	मीसा MISA (400 kV)	0%	100%	0%	0%	0	415	394	404
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	416	392	406
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	417	396	406
12		पालाटाना PALATANA(400 kV)	0%	100%	0%	0%	0	415	398	408
13		पूर्वकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	414	393	403
14		रंगानदी RANGANADI(400 kV)	0%	100%	0%	0%	0	416	391	403
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	399	408
16		सुबानसिरी SUBANSIRI (400 kV)	0%	100%	0%	0%	0	415	384	401
17		सुंज्यामाणनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	413	392	402
18		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	415	384	401

All listed stations are 765 kV stations unless otherwise mentione

***Percentage is calculated w.r.t. Time of one month**

23.ALL TIME HIGHEST

31-08-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	186 01-05-2024
WR	74974 01-06-2024	67482 30-05-2024	1648 06-05-2024	167 18-12-2014	310 28-05-2024	102.85 30-04-2024
SR	68735 13-03-2024	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	323 26-07-2024	148.7 31-03-2024
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	7 14-07-2024
NER	3859 30-08-2024	3710 26-07-2024	76 27-07-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	426 30-04-2024

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	17949	20-01-2024	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	2235	20-01-2024	41.2	26-06-2024
	J&K(UT) and Ladakh(UT)	3636	29-06-2023	66.8	26-01-2024
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	17819	29-12-2023	335.9	10-11-2023
	Maharashtra	28969	07-02-2024	648.3	30-04-2024
	Goa	803	19-04-2024	17.6	18-05-2024
	DD & DNH	1353	25-06-2024	32.1	05-06-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	15623	08-03-2024	311.0	13-03-2024
	Karnataka	17220	12-03-2024	336.9	05-04-2024
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	7879	28-07-2024	172.8	30-07-2024
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26-05-2024	4.8	30-07-2024
	Assam	2617	30-08-2024	52.8	27-07-2024
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.42	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24.System Reliability Indices Report for the month of August 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	2	0.50	0.07
3	Import of NR	15	3.75	0.50
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	7	1.75	0.24
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
