ग्रिड-इंडिया
GRID-INDIA

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या:- GRID-INDIA/NLDC/MR/ दिनांक: **23.01.2025**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **दिसंबर 2024**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **दिसंबर 2024** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
मुख्य महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



दिसंबर 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह दिसंबर 2024 के लिए प्रचालन निष्पादन रिपोर्ट


OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF DECEMBER -2024

पृष्ठसूची CONTENTS


1	माह दिसंबर 2024 की सारांश रिपोर्ट Summary of report for the month of DECEMBER 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति Evening Peak Hour Demand Met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	20 दिसंबर के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 20-DECEMBER (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह दिसंबर 2023 से तुलना Energy requirement and met comparison with DECEMBER 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह दिसंबर 2023 से तुलना Peak demand requirement and met comparison with DECEMBER 2023	25

14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-37
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	38-40
17	एसटीओए (द्विपक्षीय एवं सामूहिक)एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	41
18	पावर मार्केट की सूचना Power market information	42-46
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	47-49
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	50-56
21	नए चार्ज किये गए तत्व New elements Charged	57
22	विभव रूपरेखा Voltage profile	58
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह दिसंबर 2024 तक All Time Highest (Demand & Energy) figures: Till DECEMBER 2024	59
24	दिसंबर 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for DECEMBER 2024	60


1. SUMMARY OF REPORT FOR THE MONTH OF DECEMBER-2024

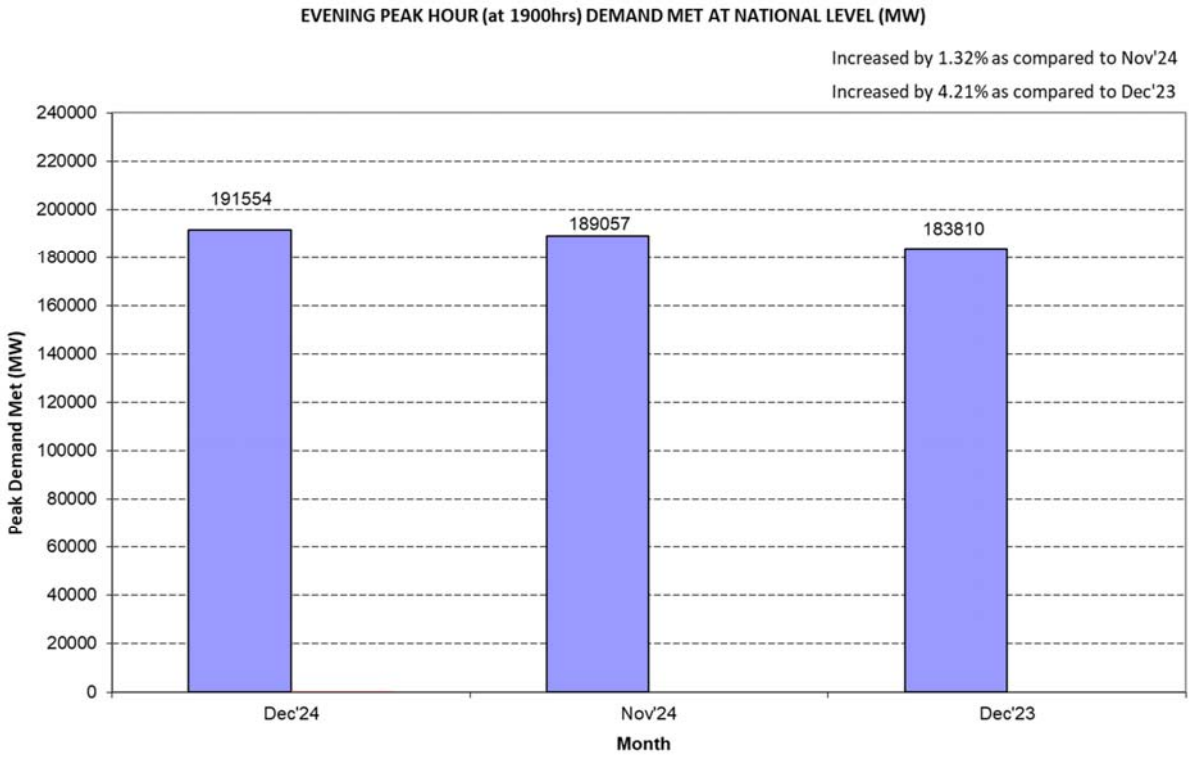


*Source: As per daily data furnished by states

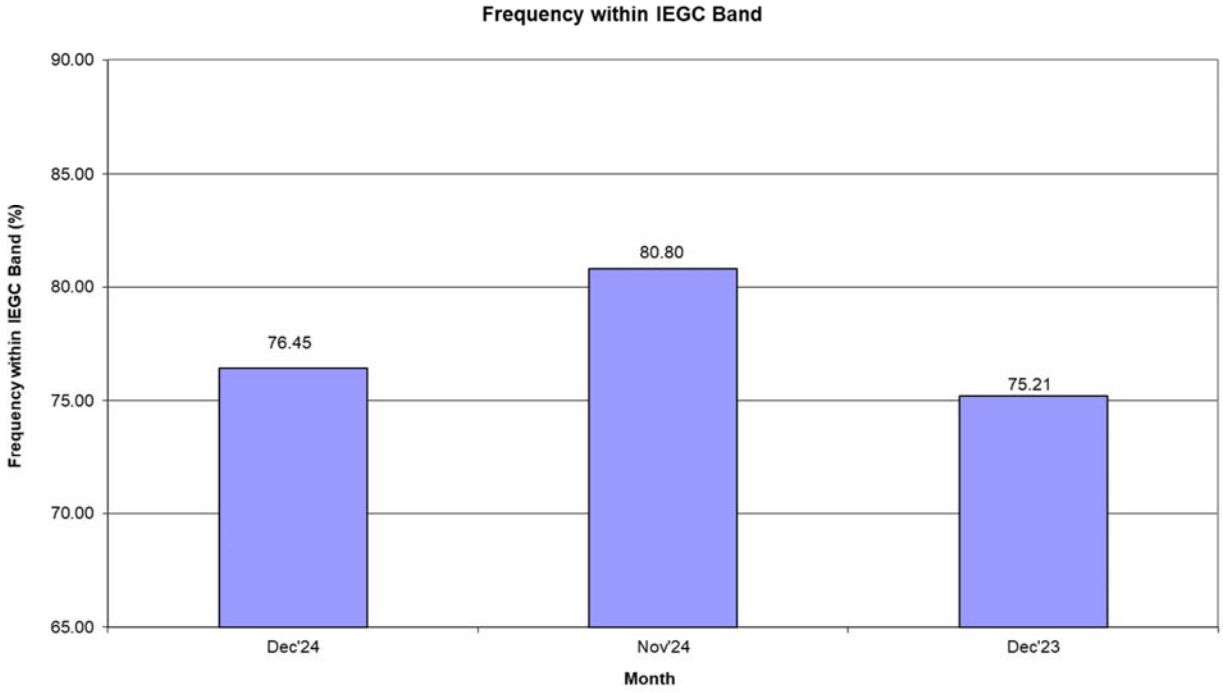


ENERGY MET AT NATIONAL LEVEL (MU)

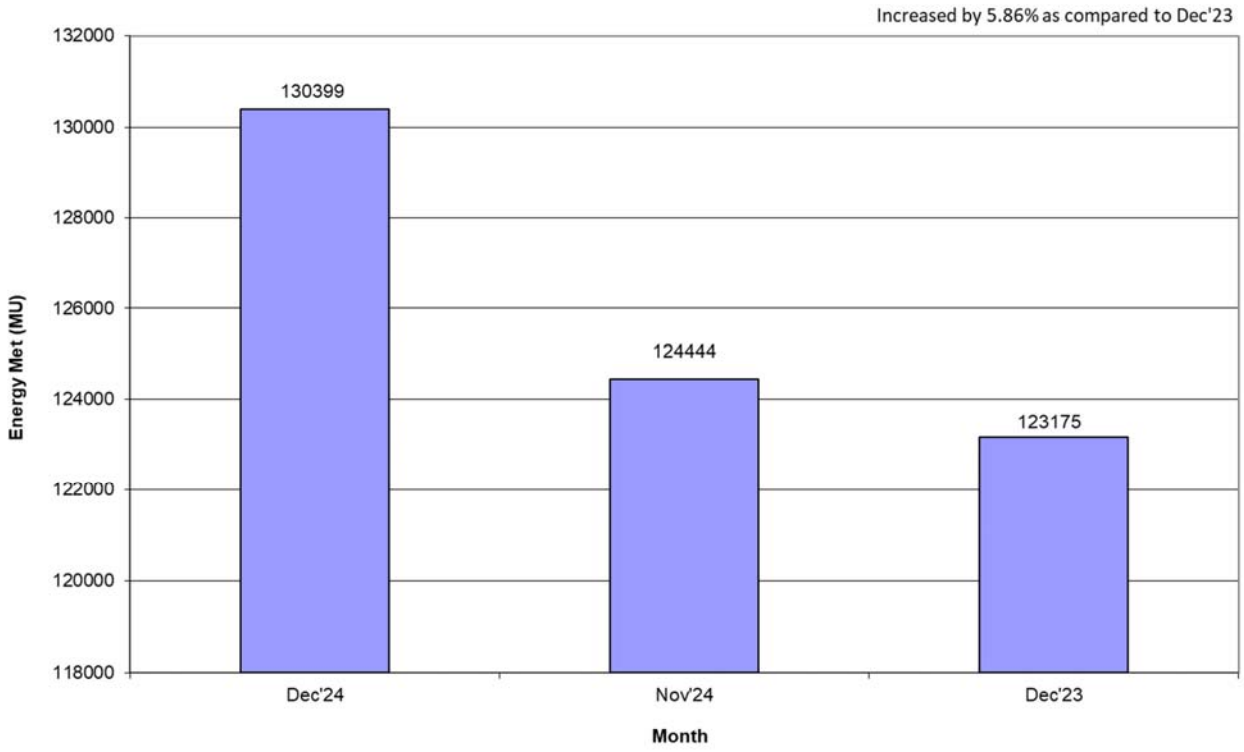


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

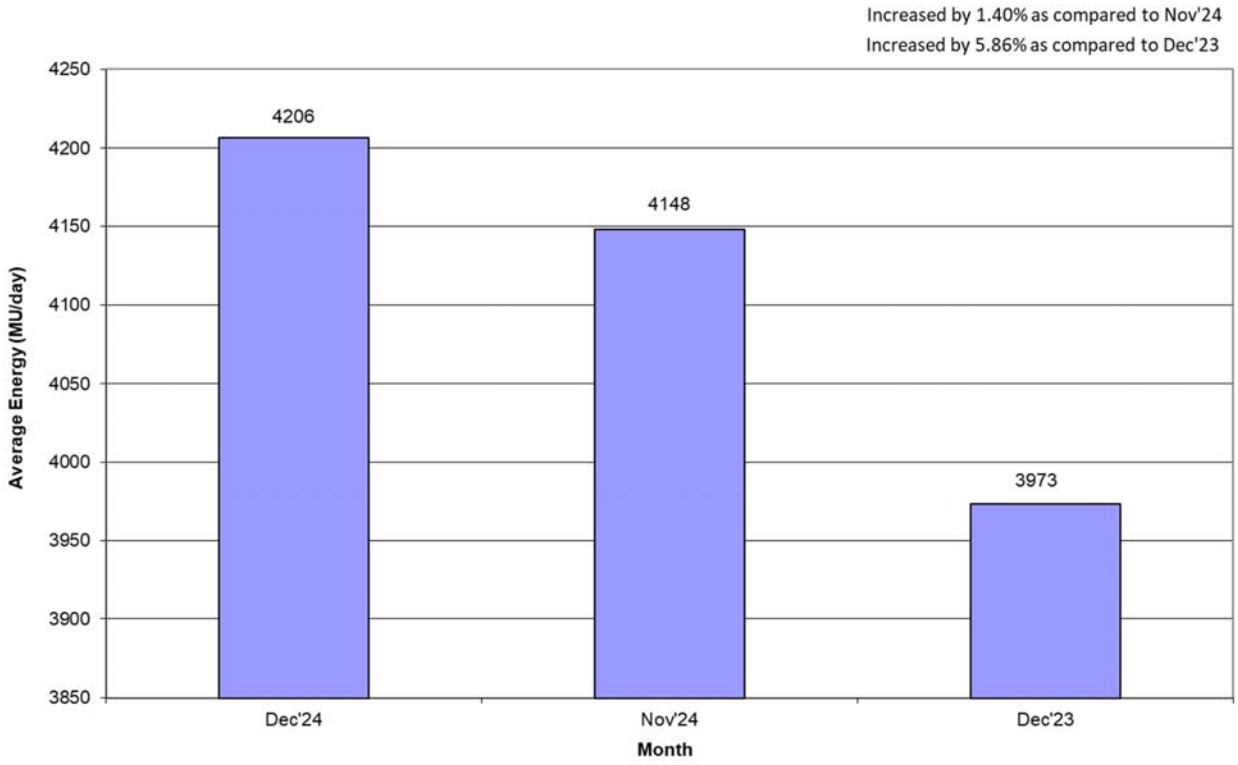


HYDRO GENERATION AT NATIONAL LEVEL (MU)

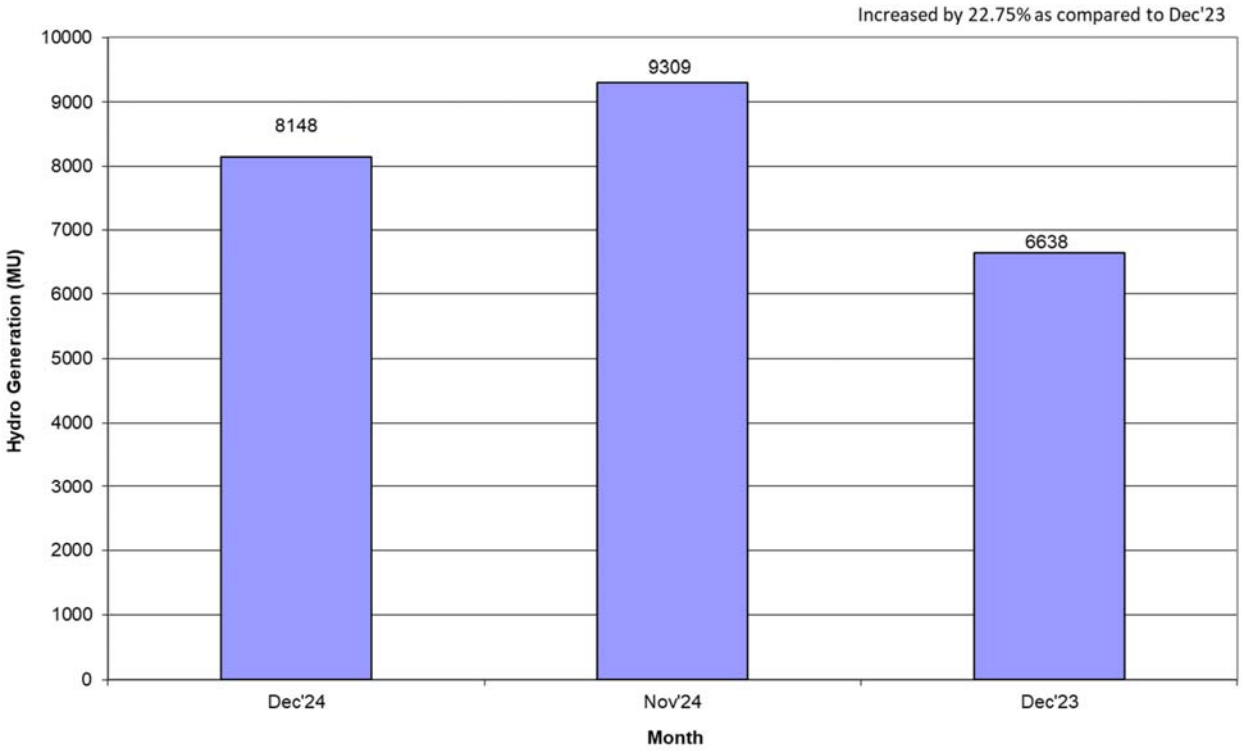


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

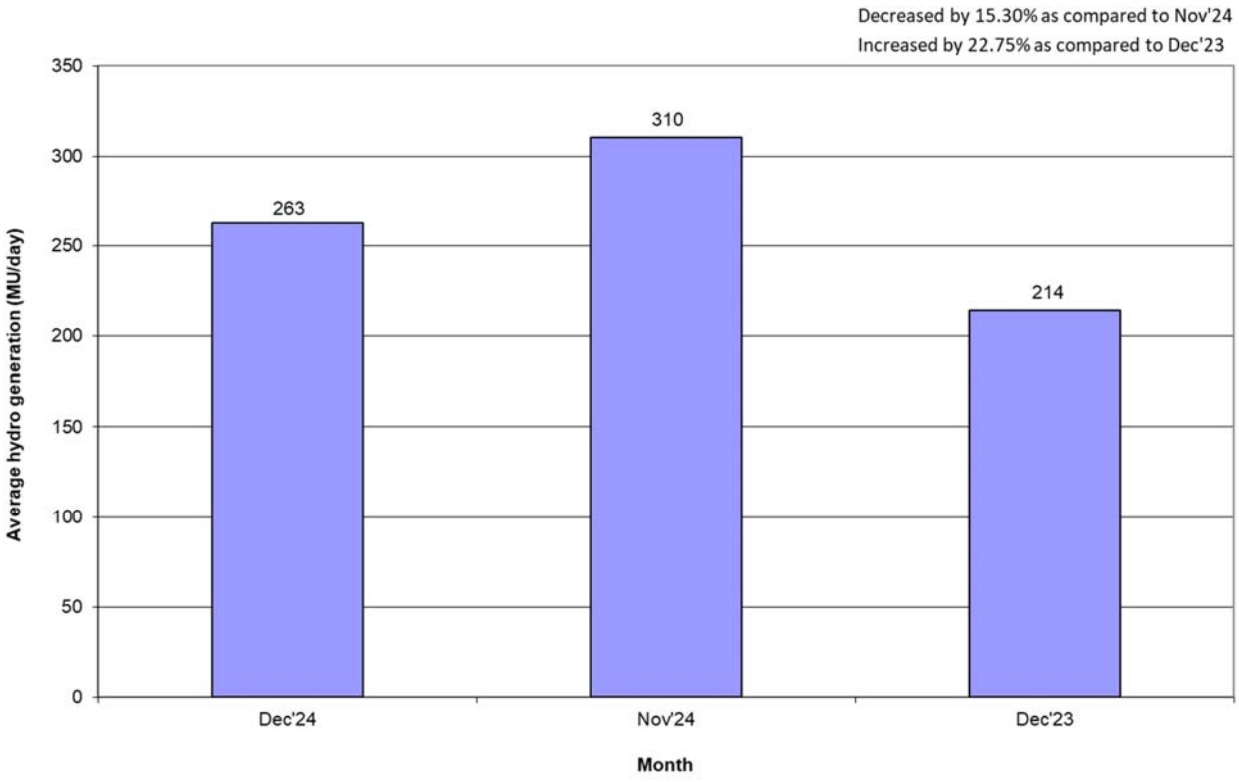


WIND GENERATION AT NATIONAL LEVEL (MU)

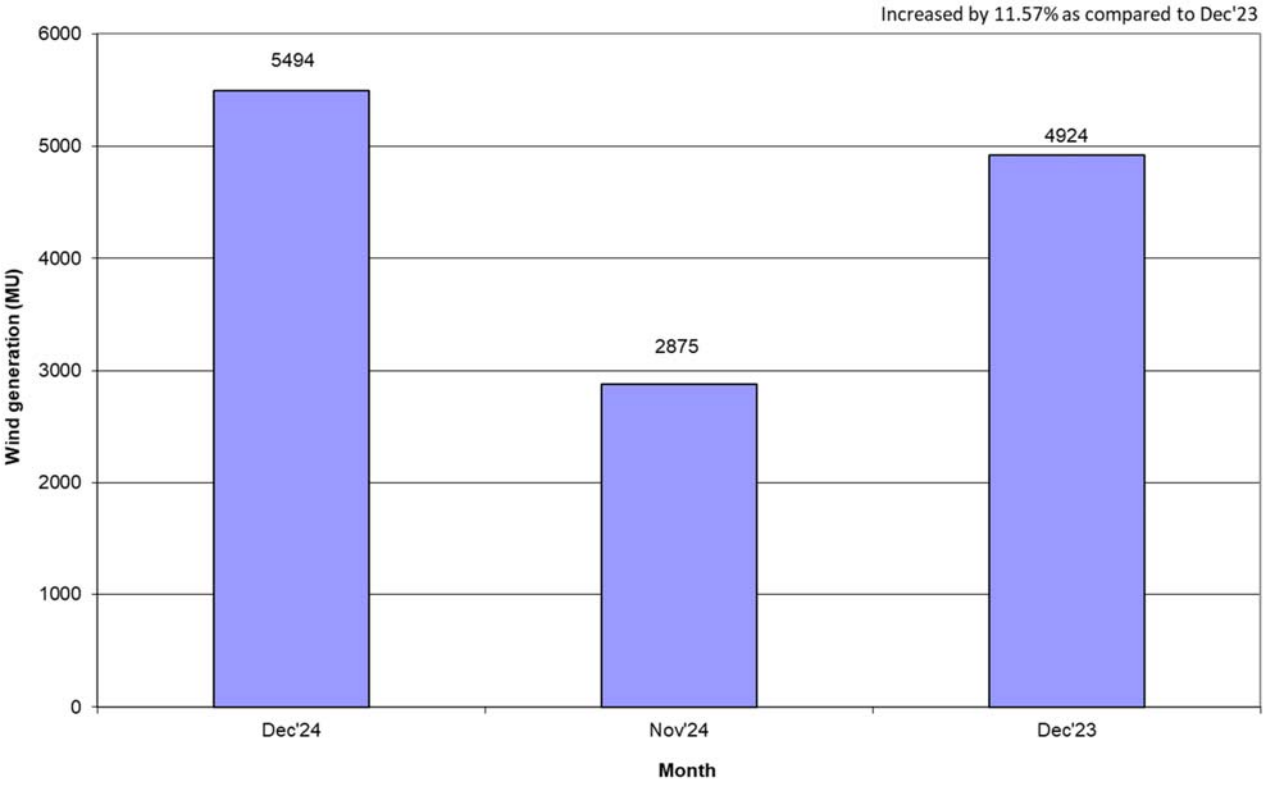


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

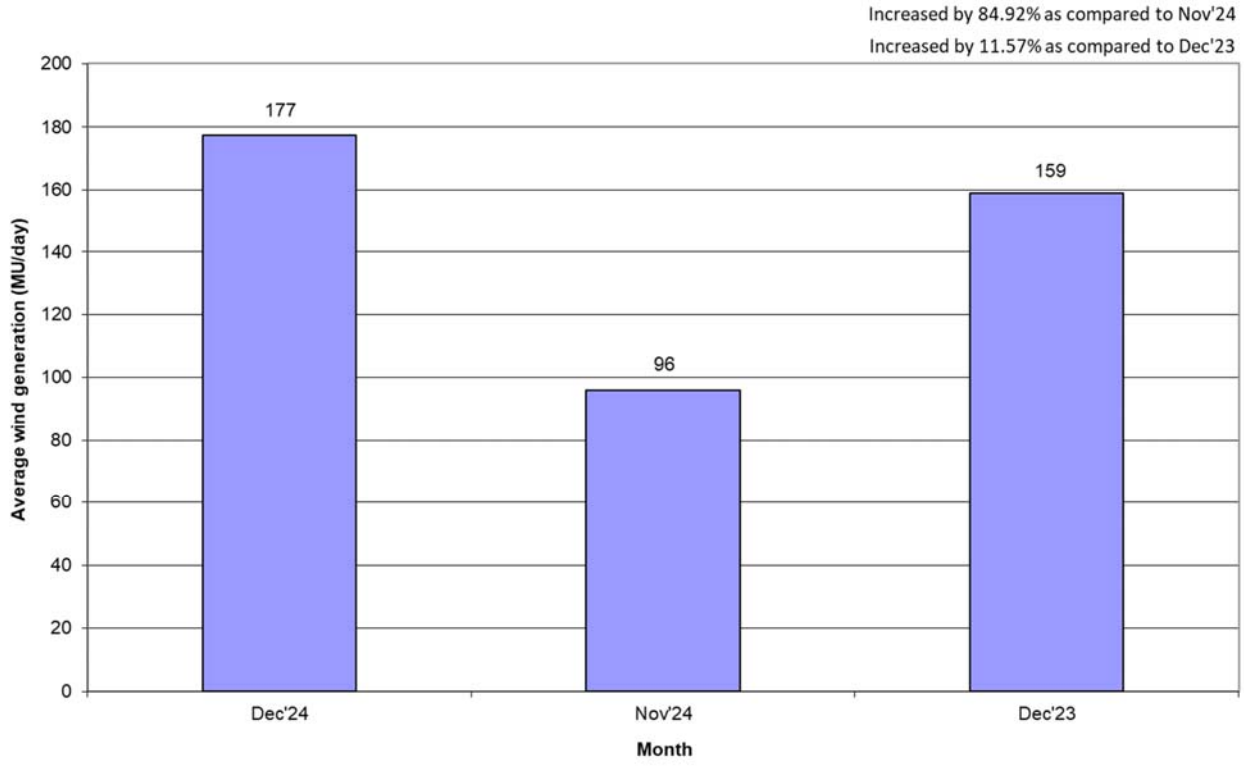

SOLAR GENERATION AT NATIONAL LEVEL (MU)

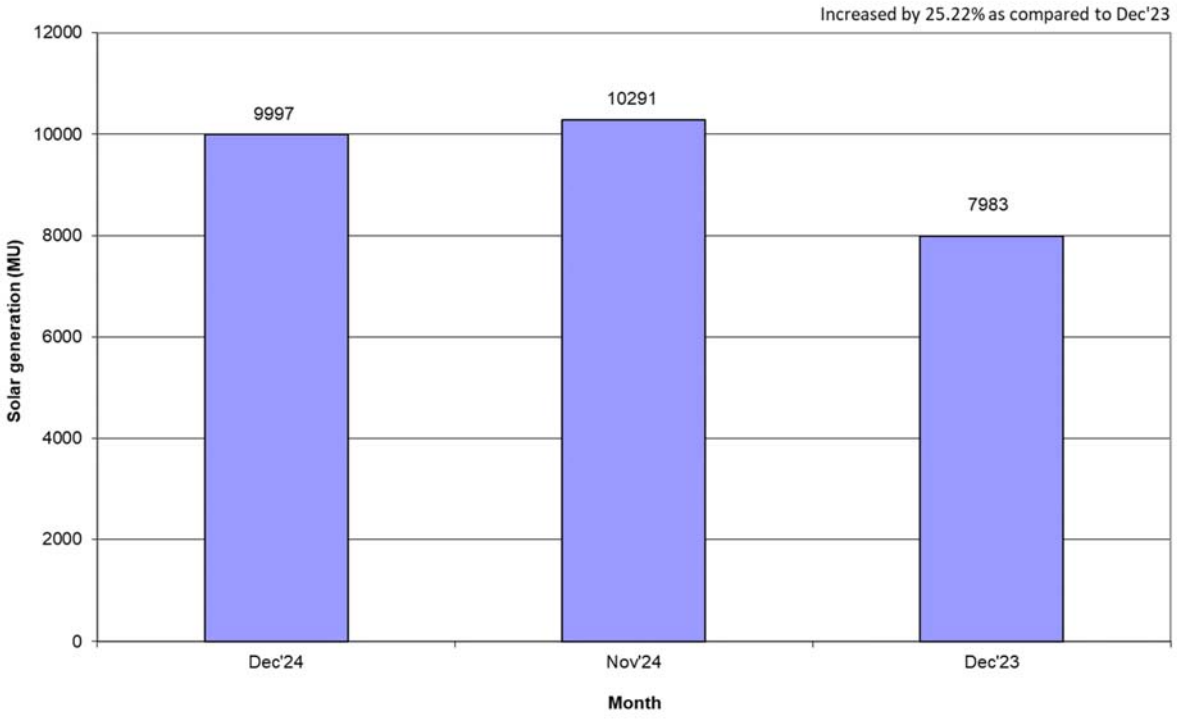

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

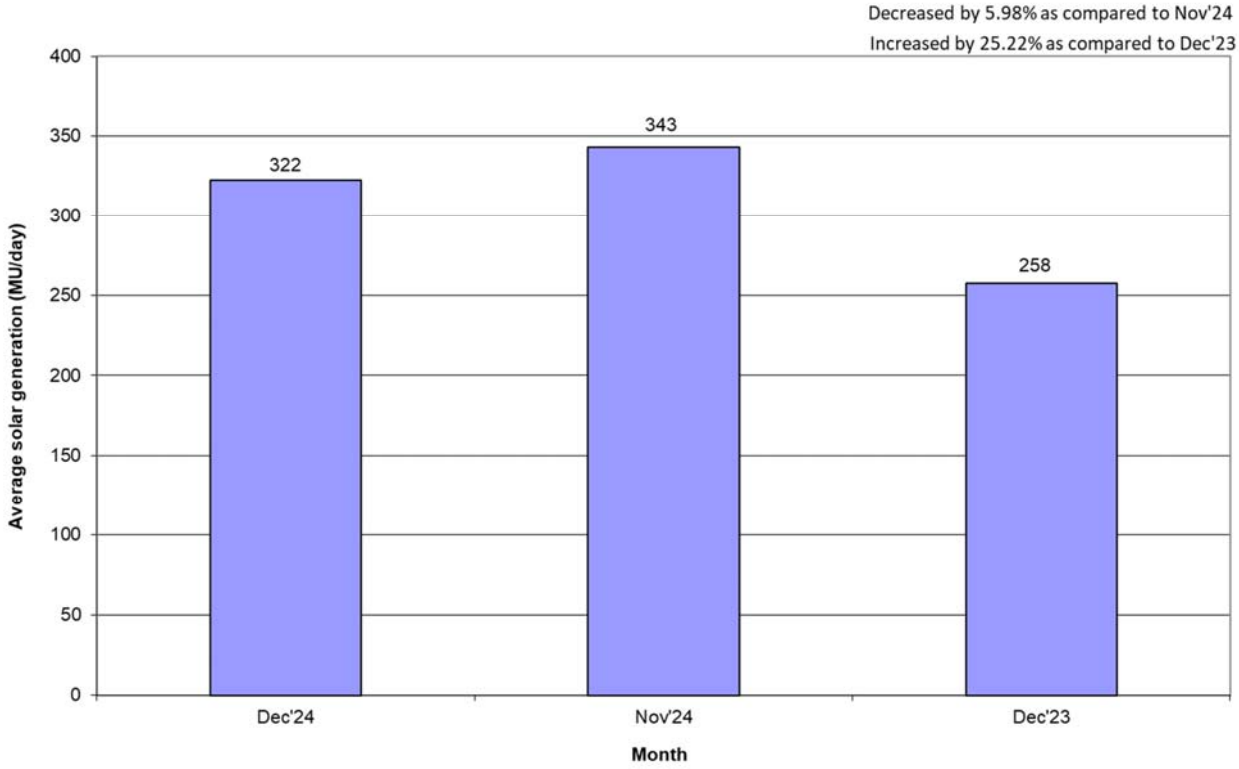

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.12.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	57859	1580	5995	0	65434	1620	20830	44903	132787
2	WR	74663	1400	10806	0	86869	3240	7563	56938	154609
3	SR	49592	3640	6272	434	59938	3320	11867	57615	132740
4	ER	28875	0	80	0	28955	0	4764	2363	36082
5	NER	1361	0	1665	36	3062	0	1944	618	5624
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	212350	6620	24818	589	244377	8180	46968	162477	462002

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति

EVENING PEAK HOUR (at 19:00hrs) DEMAND MET AT NATIONAL LEVEL


माह: दिसंबर 2024 MONTH:- DEC 2024

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Dec-24	48162	57255	36259	19574	2431	163681
2-Dec-24	51518	60771	40989	20102	2630	176010
3-Dec-24	52113	61691	43068	21113	2611	180596
4-Dec-24	52315	62452	43342	21172	2617	181898
5-Dec-24	52901	63523	44478	20655	2573	184130
6-Dec-24	53152	63059	44783	20591	2622	184207
7-Dec-24	53503	60780	44269	20535	2664	181751
8-Dec-24	50291	58724	40909	19623	2479	172026
9-Dec-24	53633	61279	45136	20590	2642	183280
10-Dec-24	55095	62116	45206	20614	2634	185665
11-Dec-24	55419	61759	43799	20823	2664	184464
12-Dec-24	56193	62485	42343	20701	2664	184386
13-Dec-24	57035	62420	42226	20913	2662	185256
14-Dec-24	56805	61762	39343	21377	2666	181953
15-Dec-24	53431	58662	37444	20756	2524	172817
16-Dec-24	58383	63063	41914	20952	2659	186971
17-Dec-24	58663	63359	43038	21187	2628	188875
18-Dec-24	59401	63825	43436	20989	2675	190326
19-Dec-24	58866	64263	44427	21281	2717	191554
20-Dec-24	58744	62778	45083	20817	2707	190129
21-Dec-24	58325	63166	44732	21241	2747	190211
22-Dec-24	55119	60599	40259	20457	2561	178995
23-Dec-24	57212	62887	46172	21845	2715	190831
24-Dec-24	57471	62989	43832	22108	2676	189076
25-Dec-24	57454	61765	41612	21348	2575	184754
26-Dec-24	57314	63844	43391	21839	2668	189056
27-Dec-24	50883	60702	43956	21730	2744	180015
28-Dec-24	55098	59982	43704	21498	2699	182981
29-Dec-24	53432	57823	40258	20959	2642	175114
30-Dec-24	57308	61061	43543	22192	2642	186746
31-Dec-24	58460	61083	44203	22021	2660	188427
उच्चतम MAXIMUM	59401	64263	46172	22192	2747	191554
निम्नतम MINIMUM	48162	57255	36259	19574	2431	163681
औसत AVERAGE	55281	61675	42811	21019	2639	183425
अब तक का उच्चतम All Time Max.	82312	67482	54798	29695	3787	227354
दिनांक Date	23.07.24	30.05.24	29.04.24	29.05.24	19.09.24	29.05.24

Source: As per daily data furnished by states

EVENING PEAK HOUR DEMAND(at 1900hrs) MET DURING THE MONTH OF DECEMBER' 2024

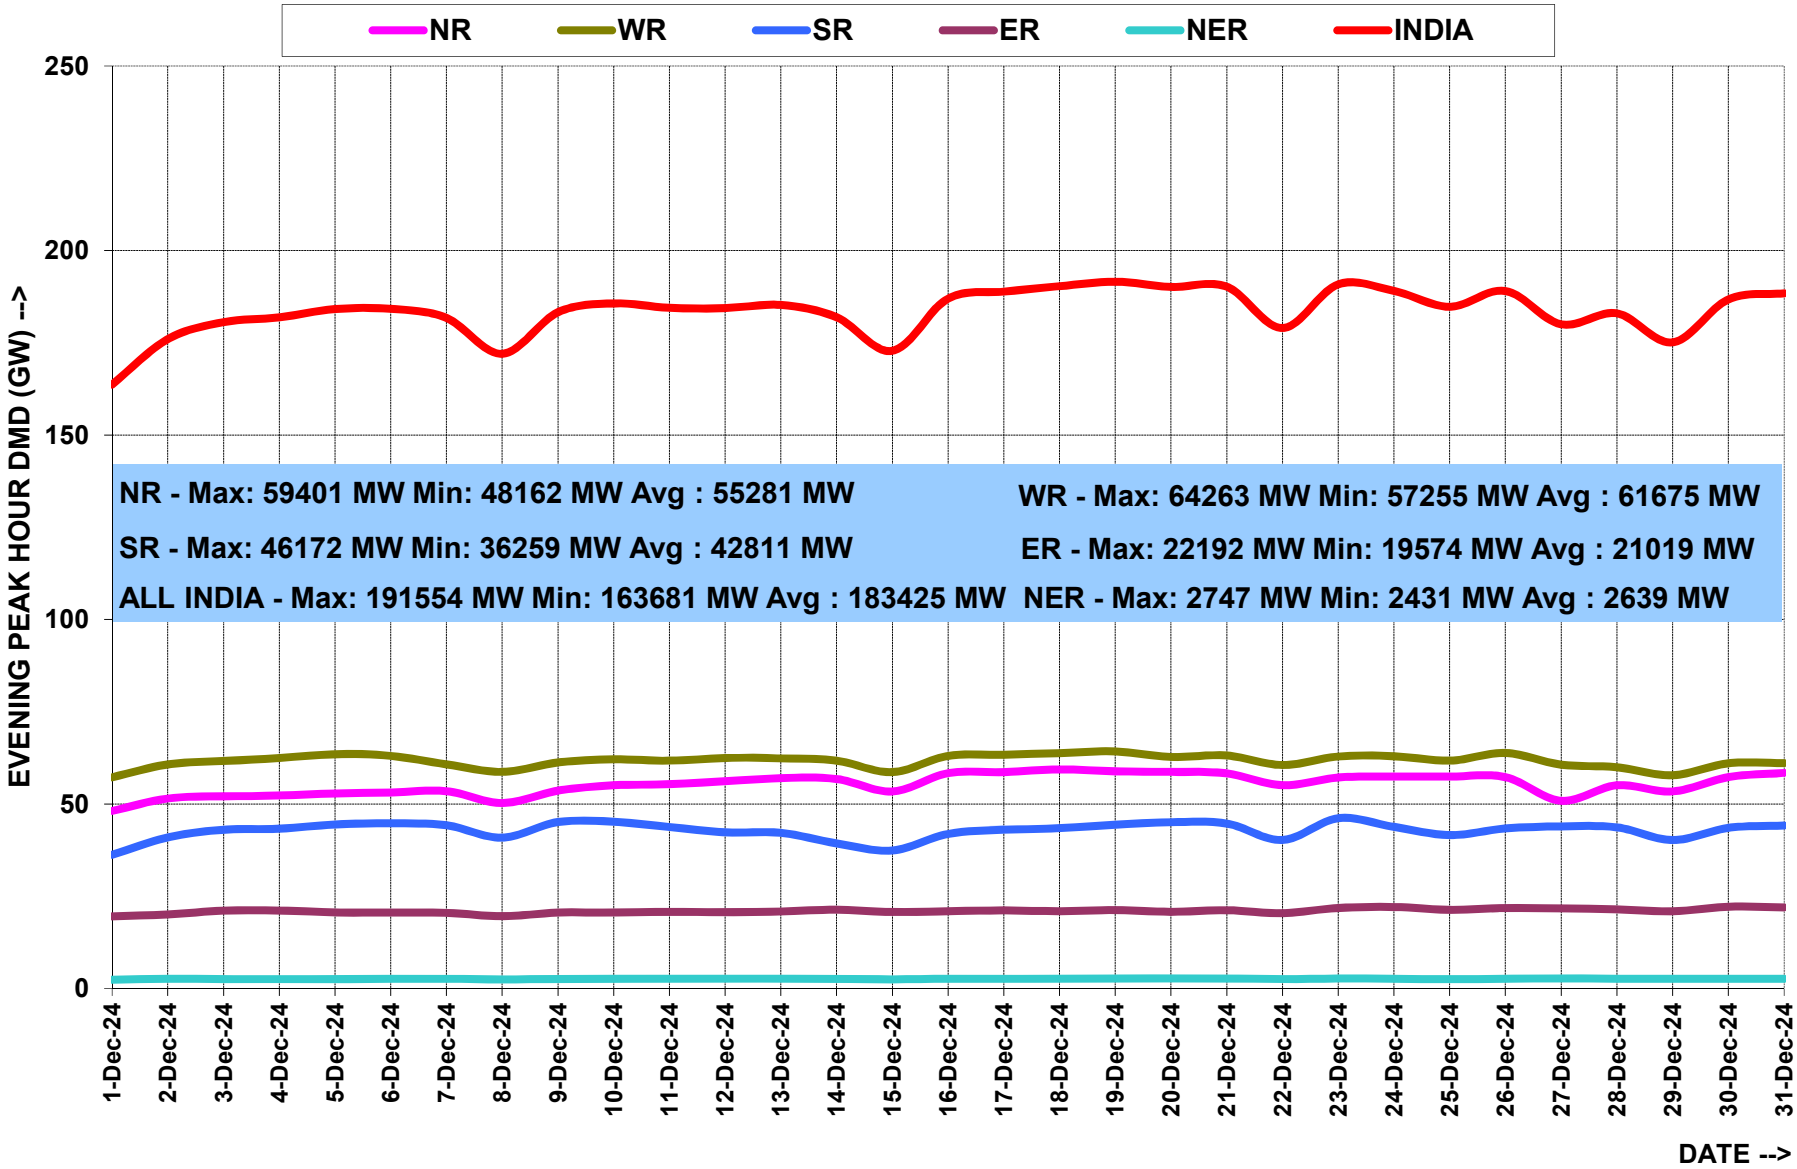


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: दिसंबर 2024 MONTH:- DEC 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Dec-24	1110	1416	903	408	46	3883
02-Dec-24	1144	1464	953	420	47	4028
03-Dec-24	1162	1496	973	431	48	4109
04-Dec-24	1171	1510	1009	431	47	4169
05-Dec-24	1173	1529	1028	426	48	4204
06-Dec-24	1184	1524	1067	423	49	4246
07-Dec-24	1177	1474	1063	421	49	4183
08-Dec-24	1126	1448	1005	408	46	4033
09-Dec-24	1170	1466	1075	412	48	4172
10-Dec-24	1204	1459	1112	418	48	4241
11-Dec-24	1214	1471	1093	418	49	4245
12-Dec-24	1210	1476	1059	423	49	4217
13-Dec-24	1232	1477	1045	425	50	4228
14-Dec-24	1222	1463	1021	418	48	4172
15-Dec-24	1178	1410	954	431	47	4019
16-Dec-24	1221	1466	1035	428	48	4198
17-Dec-24	1249	1492	1080	429	49	4298
18-Dec-24	1268	1507	1097	427	49	4348
19-Dec-24	1265	1518	1121	431	48	4383
20-Dec-24	1277	1525	1153	431	49	4435
21-Dec-24	1249	1521	1127	428	50	4374
22-Dec-24	1213	1480	1071	421	47	4232
23-Dec-24	1208	1500	1131	440	49	4328
24-Dec-24	1220	1503	1144	449	50	4366
25-Dec-24	1217	1499	1095	445	49	4305
26-Dec-24	1228	1512	1088	440	49	4318
27-Dec-24	1120	1486	1098	440	49	4193
28-Dec-24	1081	1363	1100	437	49	4030
29-Dec-24	1105	1355	1053	428	49	3990
30-Dec-24	1167	1404	1117	450	49	4188
31-Dec-24	1198	1422	1144	449	51	4265
कुल TOTAL	36961	45635	33017	13286	1500	130399
उच्चतम MAXIMUM	1277	1529	1153	450	51	4435
निम्नतम MINIMUM	1081	1355	903	408	46	3883
औसत AVERAGE	1192	1472	1065	429	48	4206
संचयी 2024-25 Cumulative 2024-25	408468	395445	310080	154426	16088	1284506
अब तक का उच्चतम All Time Max.	1990	1648	1416	692	80	5466
दिनांक Date	18.06.24	06.05.24	05.04.24	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF DECEMBER' 2024

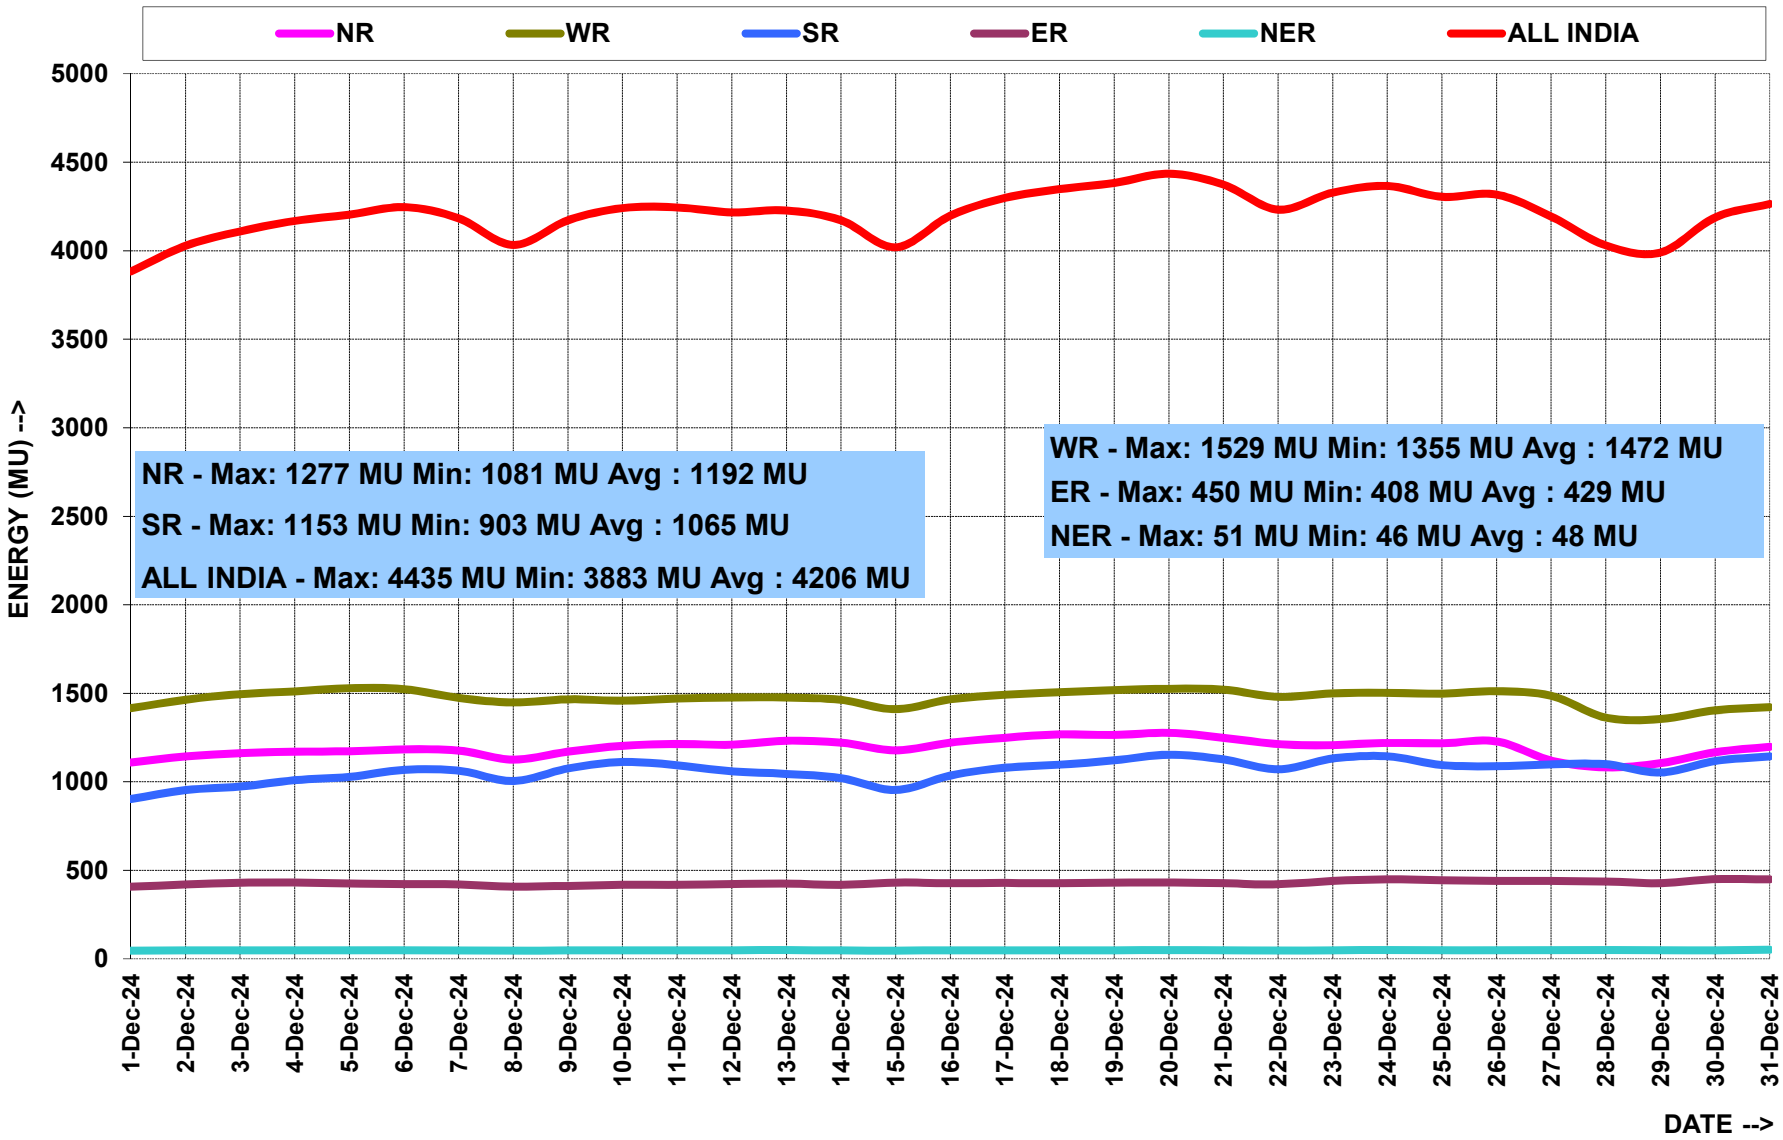

5. वर्ष 2024-25 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78		50.38	49.46	50.00
	Oct-24	All India Grid	4.86	80.27	14.87		50.39	49.58	50.00
	Nov-24	All India Grid	5.15	80.80	14.05		50.32	49.55	50.00
	Dec-24	All India Grid	5.58	76.45	17.97		50.42	49.49	50.00
	2024-25 (upto Dec)	**All India Grid**	**5.00**	**78.42**	**16.58**		**50.67**	**49.46**	**50.00**

5.1 दिसंबर 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR DECEMBER 2024


फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Dec-24	3.96	77.71	18.33		50.37	49.79	50.00	0.03
	02-Dec-24	2.71	72.11	25.19		50.18	49.79	50.01	0.03
	03-Dec-24	3.65	69.27	27.08		50.33	49.77	50.02	0.04
	04-Dec-24	3.16	81.49	15.35		50.18	49.78	50.00	0.03
	05-Dec-24	4.49	84.21	11.30		50.24	49.72	49.99	0.03
	06-Dec-24	6.78	80.29	12.93		50.16	49.65	49.99	0.04
	07-Dec-24	2.64	81.09	16.27		50.16	49.77	50.00	0.02
	08-Dec-24	3.85	77.28	18.87		50.34	49.75	50.00	0.04
	09-Dec-24	8.08	69.49	22.43		50.20	49.60	50.00	0.05
	10-Dec-24	4.88	78.16	16.96		50.26	49.75	50.00	0.03
	11-Dec-24	3.29	81.89	14.83		50.15	49.81	50.00	0.02
	12-Dec-24	2.44	77.19	20.37		50.20	49.76	50.01	0.03
	13-Dec-24	7.44	77.79	14.77		50.26	49.76	49.99	0.04
	14-Dec-24	7.66	77.27	15.07		50.36	49.73	49.99	0.05
	15-Dec-24	4.58	73.07	22.35		50.42	49.76	50.00	0.04
	16-Dec-24	18.88	65.03	16.09		50.18	49.51	49.97	0.09
	17-Dec-24	7.59	71.60	20.81		50.21	49.51	50.00	0.07
	18-Dec-24	6.47	79.97	13.56		50.25	49.65	49.99	0.04
	19-Dec-24	4.46	78.37	17.18		50.35	49.73	50.00	0.03
	20-Dec-24	8.52	75.90	15.58		50.28	49.67	49.99	0.05
	21-Dec-24	8.89	78.84	12.27		50.19	49.68	49.99	0.04
	22-Dec-24	10.65	76.56	12.79		50.24	49.49	49.98	0.08
	23-Dec-24	7.96	74.65	17.38		50.27	49.52	49.99	0.06
	24-Dec-24	2.51	81.20	16.28		50.22	49.81	50.00	0.03
	25-Dec-24	3.43	79.20	17.37		50.24	49.80	50.00	0.03
	26-Dec-24	9.00	76.45	14.55		50.27	49.65	49.99	0.05
	27-Dec-24	0.27	73.77	25.96		50.30	49.85	50.02	0.03
	28-Dec-24	5.50	76.16	18.34		50.26	49.76	50.00	0.04
	29-Dec-24	3.04	77.23	19.72		50.28	49.86	50.01	0.04
	30-Dec-24	1.48	76.55	21.97		50.25	49.79	50.01	0.03
	31-Dec-24	4.84	70.01	25.15		50.29	49.74	50.01	0.04

6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: दिसंबर 2024 MONTH:- DEC 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Dec-24	110	25	74	16	14	239
02-Dec-24	108	33	70	18	14	243
03-Dec-24	111	31	67	18	14	241
04-Dec-24	113	36	77	22	14	262
05-Dec-24	114	41	86	24	14	279
06-Dec-24	116	40	86	20	14	275
07-Dec-24	112	36	82	17	14	261
08-Dec-24	113	30	66	12	14	235
09-Dec-24	115	29	82	18	15	259
10-Dec-24	112	34	84	15	14	259
11-Dec-24	114	37	76	17	14	258
12-Dec-24	114	42	83	19	13	271
13-Dec-24	113	37	73	16	13	252
14-Dec-24	115	39	67	16	14	250
15-Dec-24	114	30	69	16	13	242
16-Dec-24	117	38	80	18	14	266
17-Dec-24	116	46	89	18	14	282
18-Dec-24	116	59	95	18	13	302
19-Dec-24	113	56	98	19	13	299
20-Dec-24	113	60	100	16	13	302
21-Dec-24	112	58	92	17	13	292
22-Dec-24	114	52	67	17	13	263
23-Dec-24	111	62	95	17	13	298
24-Dec-24	112	56	84	18	14	283
25-Dec-24	103	57	83	15	13	271
26-Dec-24	103	55	92	14	13	277
27-Dec-24	103	39	73	13	12	241
28-Dec-24	100	33	67	15	12	227
29-Dec-24	98	31	72	13	12	228
30-Dec-24	97	32	89	20	12	250
31-Dec-24	97	29	85	19	13	243
कुल TOTAL	3417	1285	2501	531	414	8148
उच्चतम MAXIMUM	117	62	100	24	15	302
निम्नतम MINIMUM	97	25	66	12	12	227
औसत AVERAGE	110	41	81	17	13	263
संचयी 2024-25 Cumulative 2024-25	70314	16484	27575	14676	6860	135908
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

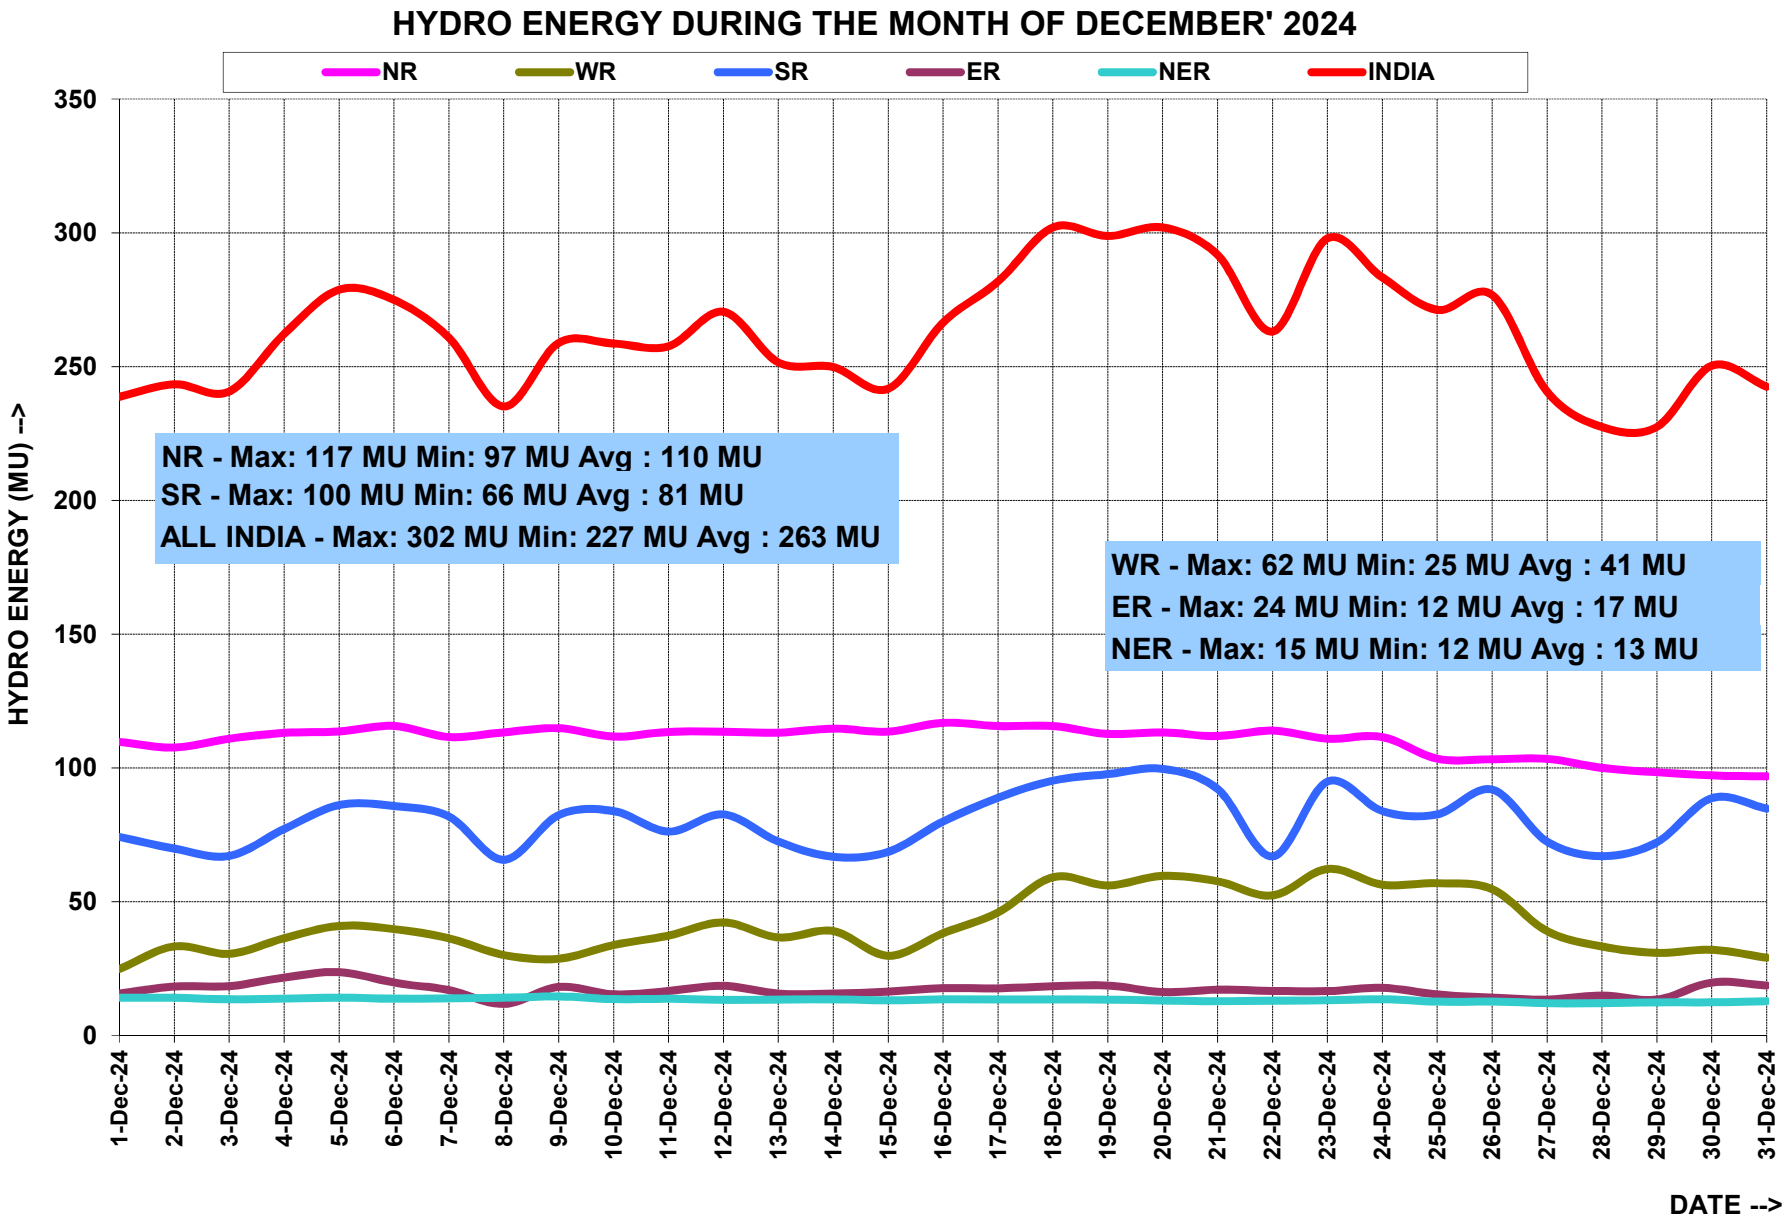
HYDRO ENERGY DURING THE MONTH OF DECEMBER' 2024
NR
WR
SR
ER
NER
INDIA
HYDRO ENERGY (MU) -->
350
300
250
200
150
100
50
0
NR - Max: 117 MU Min: 97 MU Avg : 110 MU
SR - Max: 100 MU Min: 66 MU Avg : 81 MU
ALL INDIA - Max: 302 MU Min: 227 MU Avg : 263 MU
WR - Max: 62 MU Min: 25 MU Avg : 41 MU
ER - Max: 24 MU Min: 12 MU Avg : 17 MU
NER - Max: 15 MU Min: 12 MU Avg : 13 MU
1-Dec-24
2-Dec-24
3-Dec-24
4-Dec-24
5-Dec-24
6-Dec-24
7-Dec-24
8-Dec-24
9-Dec-24
10-Dec-24
11-Dec-24
12-Dec-24
13-Dec-24
14-Dec-24
15-Dec-24
16-Dec-24
17-Dec-24
18-Dec-24
19-Dec-24
20-Dec-24
21-Dec-24
22-Dec-24
23-Dec-24
24-Dec-24
25-Dec-24
26-Dec-24
27-Dec-24
28-Dec-24
29-Dec-24
30-Dec-24
31-Dec-24
DATE -->

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: दिसंबर 2024 MONTH:- DEC 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Dec-24	8	86	119	----------	----------	213
02-Dec-24	10	89	124	----------	----------	224
03-Dec-24	26	125	93	----------	----------	244
04-Dec-24	23	150	51	----------	----------	223
05-Dec-24	2	101	31	----------	----------	134
06-Dec-24	2	54	26	----------	----------	82
07-Dec-24	3	23	22	----------	----------	48
08-Dec-24	27	50	28	----------	----------	105
09-Dec-24	12	147	21	----------	----------	180
10-Dec-24	18	155	29	----------	----------	202
11-Dec-24	9	125	68	----------	----------	202
12-Dec-24	12	154	57	----------	----------	223
13-Dec-24	26	206	56	----------	----------	287
14-Dec-24	13	153	73	----------	----------	239
15-Dec-24	11	92	79	----------	----------	181
16-Dec-24	10	89	49	----------	----------	149
17-Dec-24	21	111	19	----------	----------	151
18-Dec-24	26	154	14	----------	----------	194
19-Dec-24	25	79	17	----------	----------	120
20-Dec-24	47	150	30	----------	----------	227
21-Dec-24	26	98	17	----------	----------	141
22-Dec-24	18	67	24	----------	----------	109
23-Dec-24	21	57	25	----------	----------	103
24-Dec-24	37	106	25	----------	----------	168
25-Dec-24	38	125	20	----------	----------	183
26-Dec-24	35	113	32	----------	----------	180
27-Dec-24	34	128	75	----------	----------	237
28-Dec-24	8	113	76	----------	----------	197
29-Dec-24	19	107	71	----------	----------	197
30-Dec-24	13	77	84	----------	----------	174
31-Dec-24	13	59	105	----------	----------	177
कुल TOTAL	593	3343	1559	----------	----------	5494
उच्चतम MAXIMUM	47	206	124	----------	----------	287
निम्नतम MINIMUM	2	23	14	----------	----------	48
औसत AVERAGE	19	108	50	----------	----------	177
संचयी 2024-25 Cumulative 2024-25	5459	29298	30681	----------	----------	65437
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: दिसंबर 2024 MONTH:- DEC 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Dec-24	133	80	49	1.3	1.0	264
02-Dec-24	134	77	65	1.5	1.0	279
03-Dec-24	136	78	82	2.4	1.1	299
04-Dec-24	144	82	95	2.3	1.0	324
05-Dec-24	149	84	91	2.8	0.9	328
06-Dec-24	150	84	111	2.6	0.8	349
07-Dec-24	160	88	110	2.0	0.9	361
08-Dec-24	150	92	113	2.2	1.1	358
09-Dec-24	134	111	104	2.2	0.9	352
10-Dec-24	148	95	112	2.6	0.7	358
11-Dec-24	149	98	97	2.9	1.0	347
12-Dec-24	152	99	58	3.1	1.0	313
13-Dec-24	155	99	64	2.9	1.1	322
14-Dec-24	166	104	90	3.5	1.1	365
15-Dec-24	164	102	127	3.2	1.2	397
16-Dec-24	153	99	122	3.6	1.2	378
17-Dec-24	151	98	124	3.2	1.2	378
18-Dec-24	149	95	99	3.1	0.9	346
19-Dec-24	149	89	102	2.4	1.1	344
20-Dec-24	121	86	98	2.2	1.0	307
21-Dec-24	113	78	105	2.3	0.7	299
22-Dec-24	100	67	101	2.6	0.9	272
23-Dec-24	93	67	110	2.9	1.0	274
24-Dec-24	110	77	102	1.6	1.2	292
25-Dec-24	121	74	85	1.2	0.9	282
26-Dec-24	94	61	68	2.3	1.0	227
27-Dec-24	79	62	77	3.0	1.1	222
28-Dec-24	128	74	117	3.0	1.1	322
29-Dec-24	123	81	131	3.0	0.9	339
30-Dec-24	135	93	117	2.5	0.9	349
31-Dec-24	134	92	121	2.7	1.0	351
कुल TOTAL	4177	2665	3046	79	31	9997
उच्चतम MAXIMUM	166	111	131	3.6	1.2	397
निम्नतम MINIMUM	79	61	49	1.2	0.7	222
औसत AVERAGE	135	86	98	2.5	1.0	322
संचयी 2024-25 Cumulative 2024-25	41224	22363	30595	801	257.0	95240
अब तक का उच्चतम All Time Max.	186	**111**	149	4.1	3.5	426
दिनांक Date	01.05.24	**09.12.24**	31.03.24	09.06.24	08.09.24	30.04.24

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: दिसंबर 2024 MONTH:- DEC 2024

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फ़ैक्टर Diversity Factor*
01-Dec-24	59590	70715	45096	20591	2624	194277	1.022
02-Dec-24	61420	73555	46752	21691	2845	202959	1.016
03-Dec-24	61568	74611	46210	22217	2833	202180	1.026
04-Dec-24	62078	74488	47910	21373	2845	204287	1.022
05-Dec-24	62253	74851	48673	21510	2769	205860	1.020
06-Dec-24	62998	73982	50129	21581	2836	208017	1.017
07-Dec-24	62367	72989	49309	21167	2839	205207	1.017
08-Dec-24	60966	71700	47985	20388	2631	200033	1.018
09-Dec-24	63283	71751	51363	21259	2815	206182	1.021
10-Dec-24	64322	72519	53115	21505	2790	210581	1.017
11-Dec-24	65359	73040	52518	21234	2799	211191	1.018
12-Dec-24	65562	74592	51478	20878	2857	211751	1.017
13-Dec-24	66850	74029	52015	21481	2840	213941	1.015
14-Dec-24	66783	73474	50072	22003	2819	210497	1.022
15-Dec-24	65275	71564	47769	21638	2660	205080	1.019
16-Dec-24	66219	73581	51723	21953	2791	212807	1.016
17-Dec-24	67817	75025	53695	21992	2794	217258	1.019
18-Dec-24	68373	75288	54292	21346	2791	217753	1.020
19-Dec-24	67207	76488	54961	21860	2794	219721	1.016
20-Dec-24	68769	77436	57381	21420	2830	224169	1.016
21-Dec-24	66927	76378	54267	21888	2915	218790	1.016
22-Dec-24	65467	74761	52438	20978	2703	211807	1.021
23-Dec-24	64311	75474	55646	22066	2818	216168	1.019
24-Dec-24	65304	74645	57189	22941	2855	218812	1.019
25-Dec-24	65959	75915	55180	22539	2739	220225	1.010
26-Dec-24	65805	76583	54300	22699	2799	218593	1.016
27-Dec-24	59193	74722	54481	22867	2861	210819	1.016
28-Dec-24	58546	65814	54092	22580	2863	197742	1.031
29-Dec-24	58898	67000	52247	21863	2684	199497	1.016
30-Dec-24	61405	69945	56324	22935	2826	210780	1.013
31-Dec-24	64448	70255	57073	23063	2856	214787	1.014
उच्चतम MAXIMUM	68769	77436	57381	23063	2915	224169	1.031
निम्नतम MINIMUM	58546	65814	45096	20388	2624	194277	1.010
औसत AVERAGE	64043	73457	52119	21791	2797	210380	1.018
अब तक का उच्चतम All Time Max.	91215	**77436**	68735	32531	3905	250070	
दिनांक Date	19.06.24	**20.12.24**	13.03.24	10.06.24	19.09.24	30.05.24	


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 20th DEC (MAXIMUM DEMAND MET)

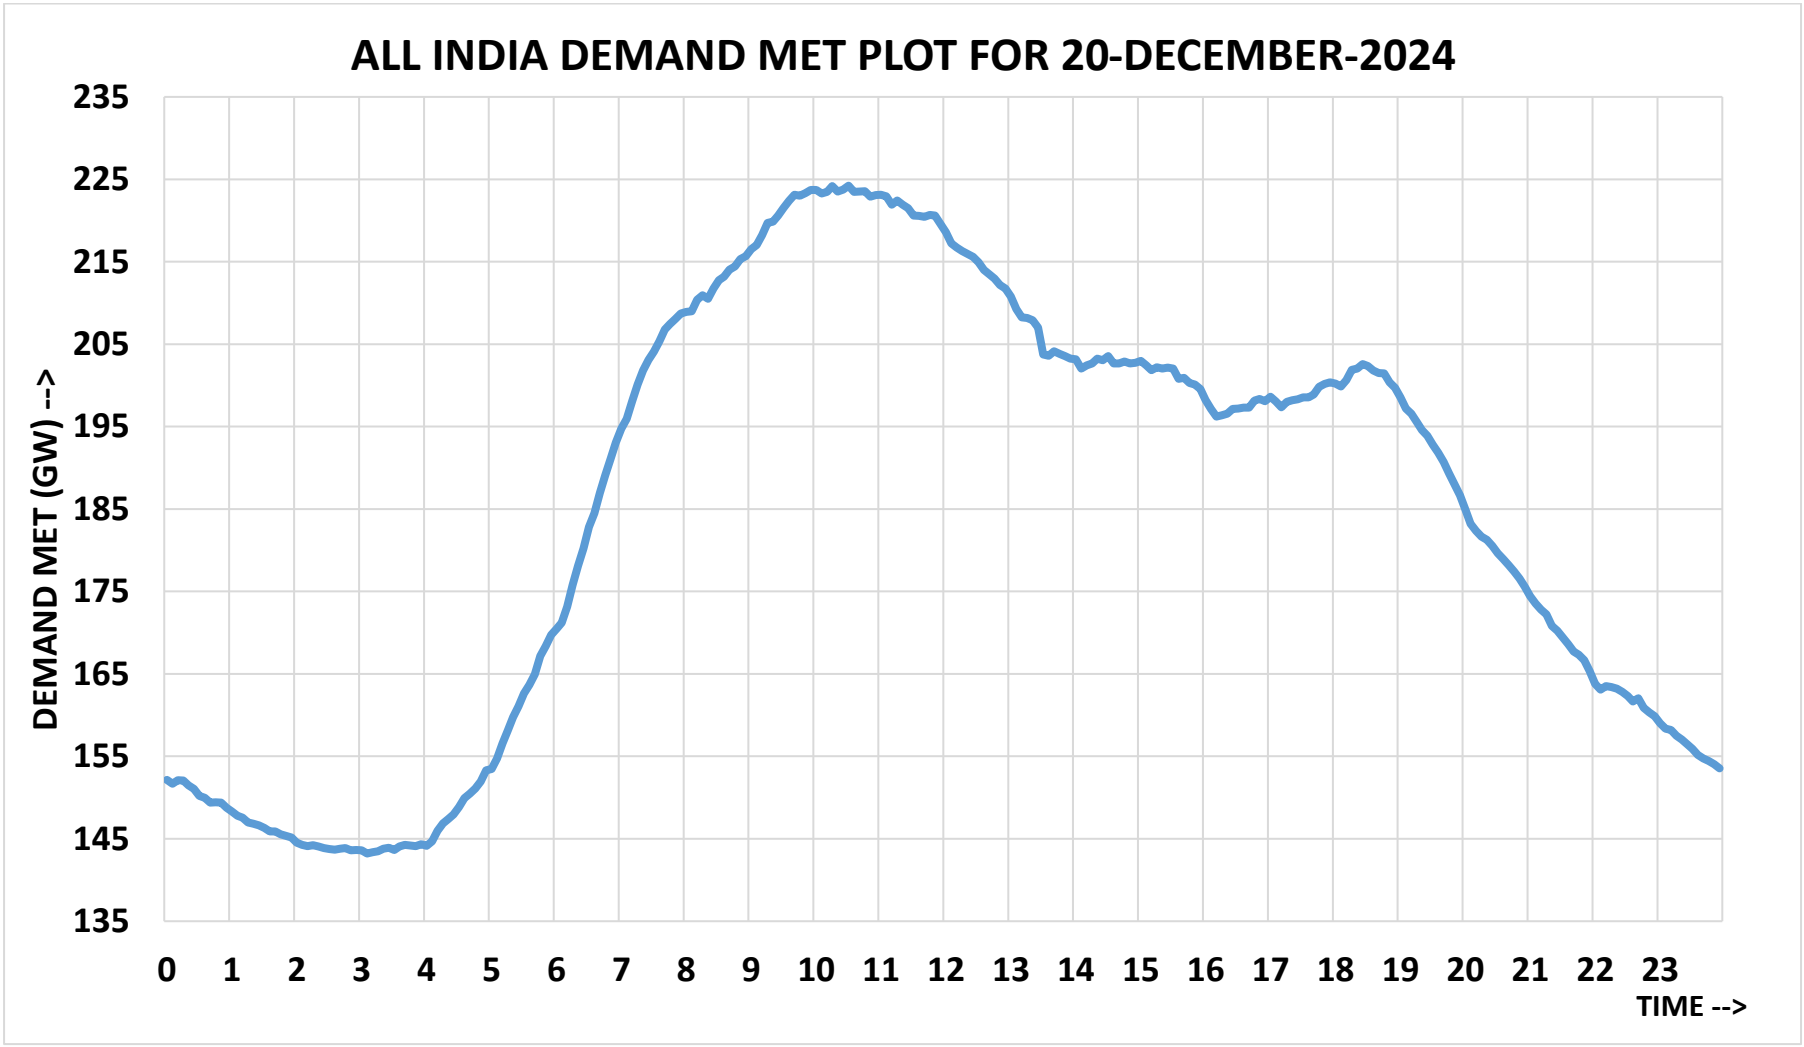

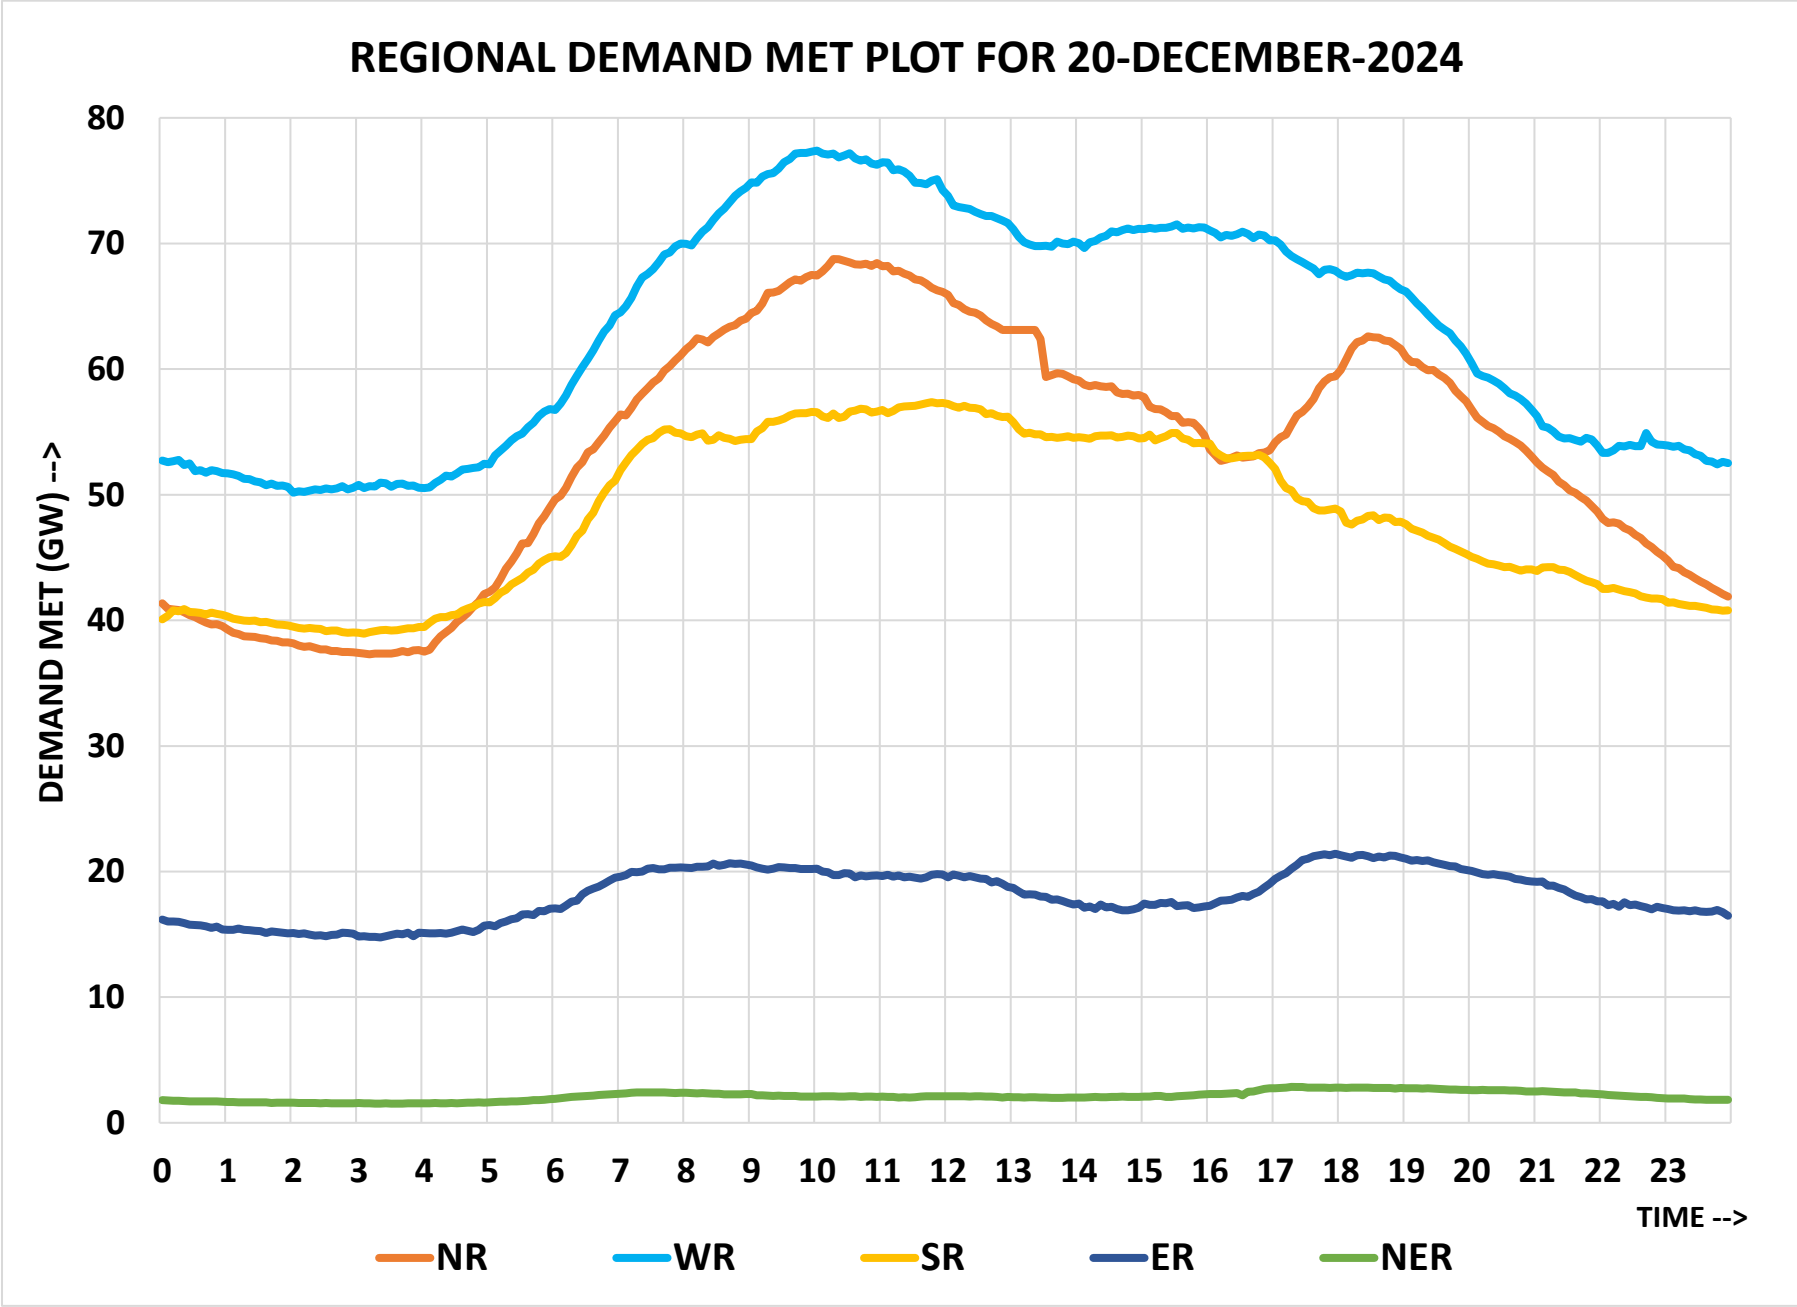
REGIONAL DEMAND MET PLOT FOR 20-DECEMBER-2024
DEMAND MET (GW) -->
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

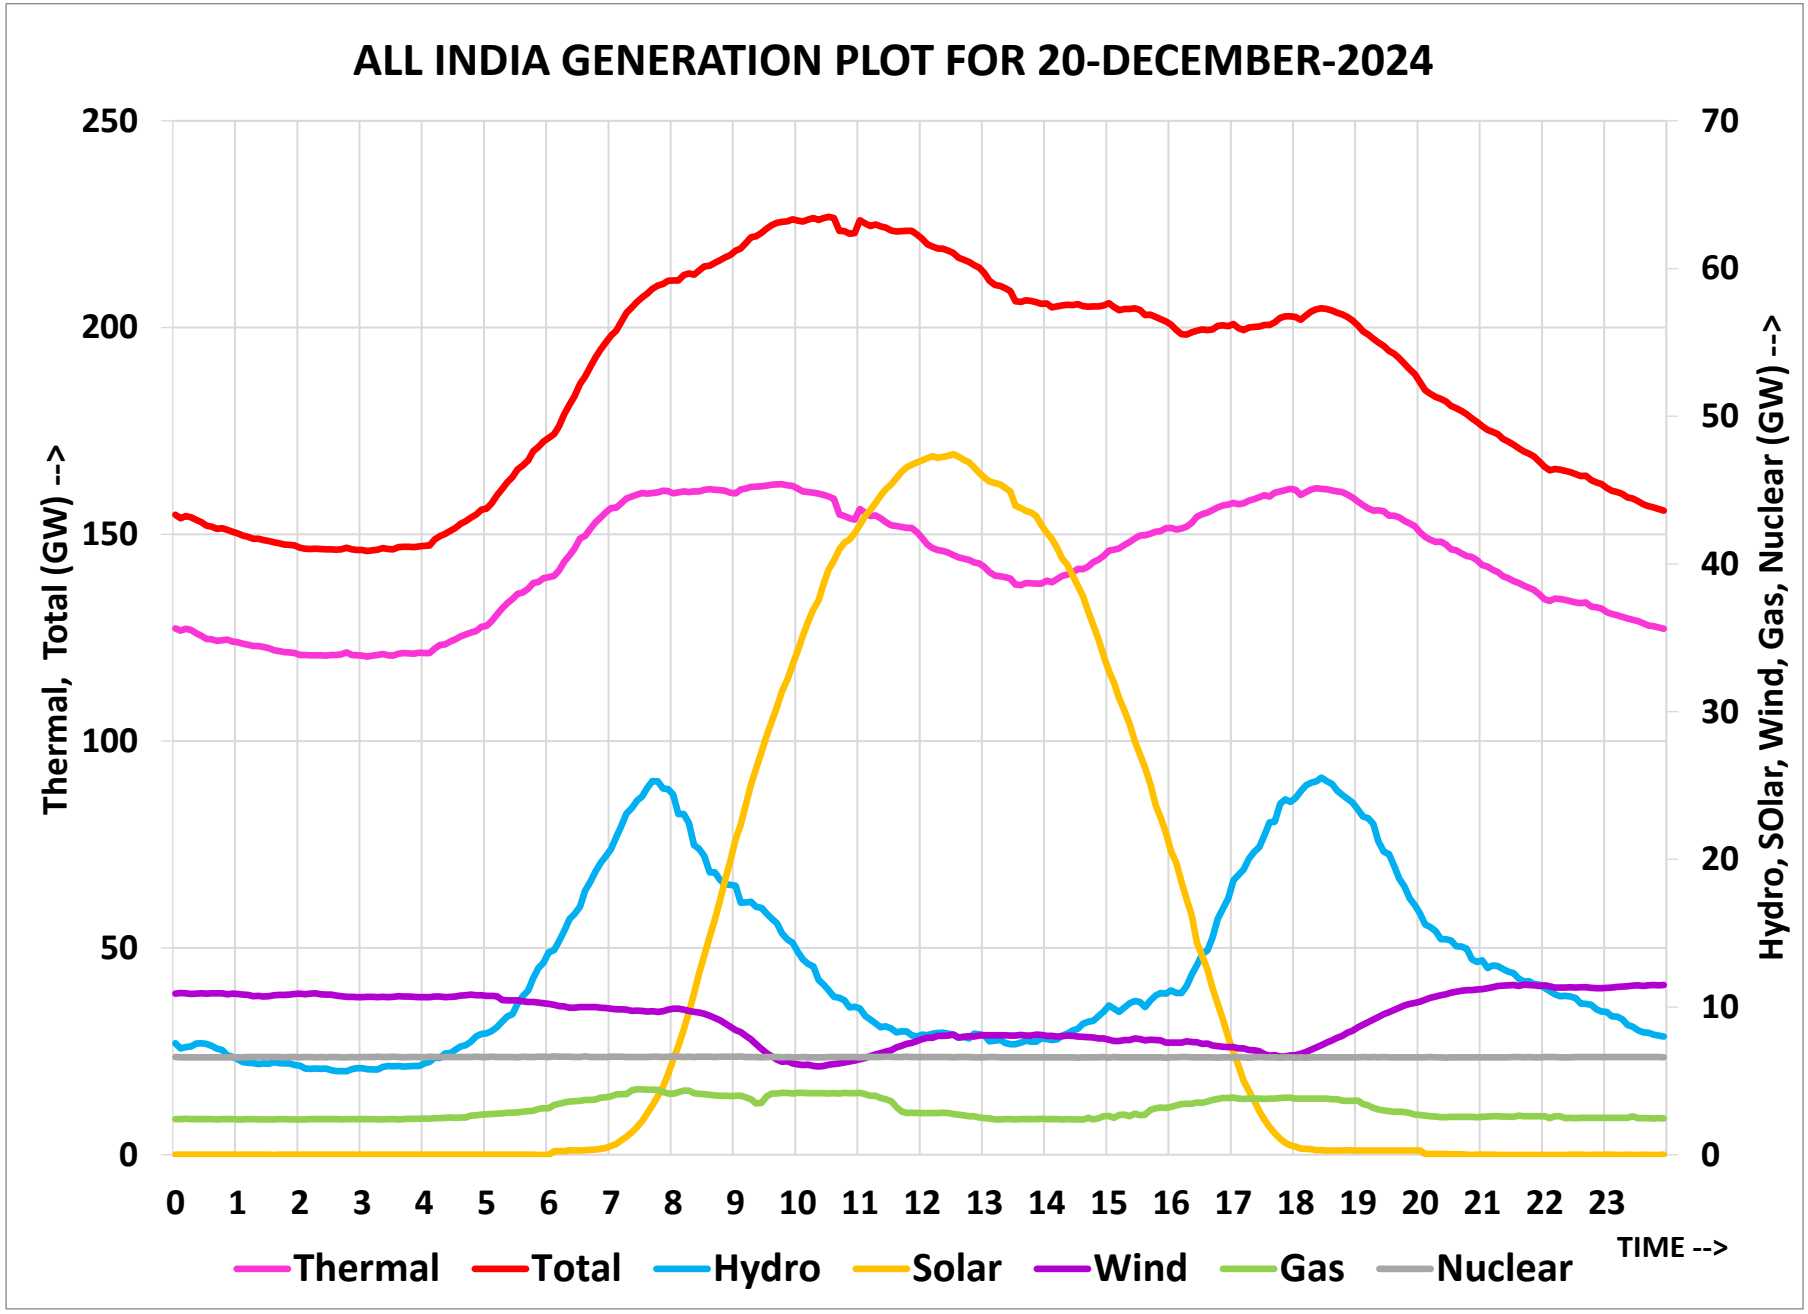
ALL INDIA GENERATION PLOT FOR 20-DECEMBER-2024
Thermal, Total (GW) -->
Hydro, SOlar, Wind, Gas, Nuclear (GW) -->
TIME -->
Thermal
Total
Hydro
Solar
Wind
Gas
Nuclear

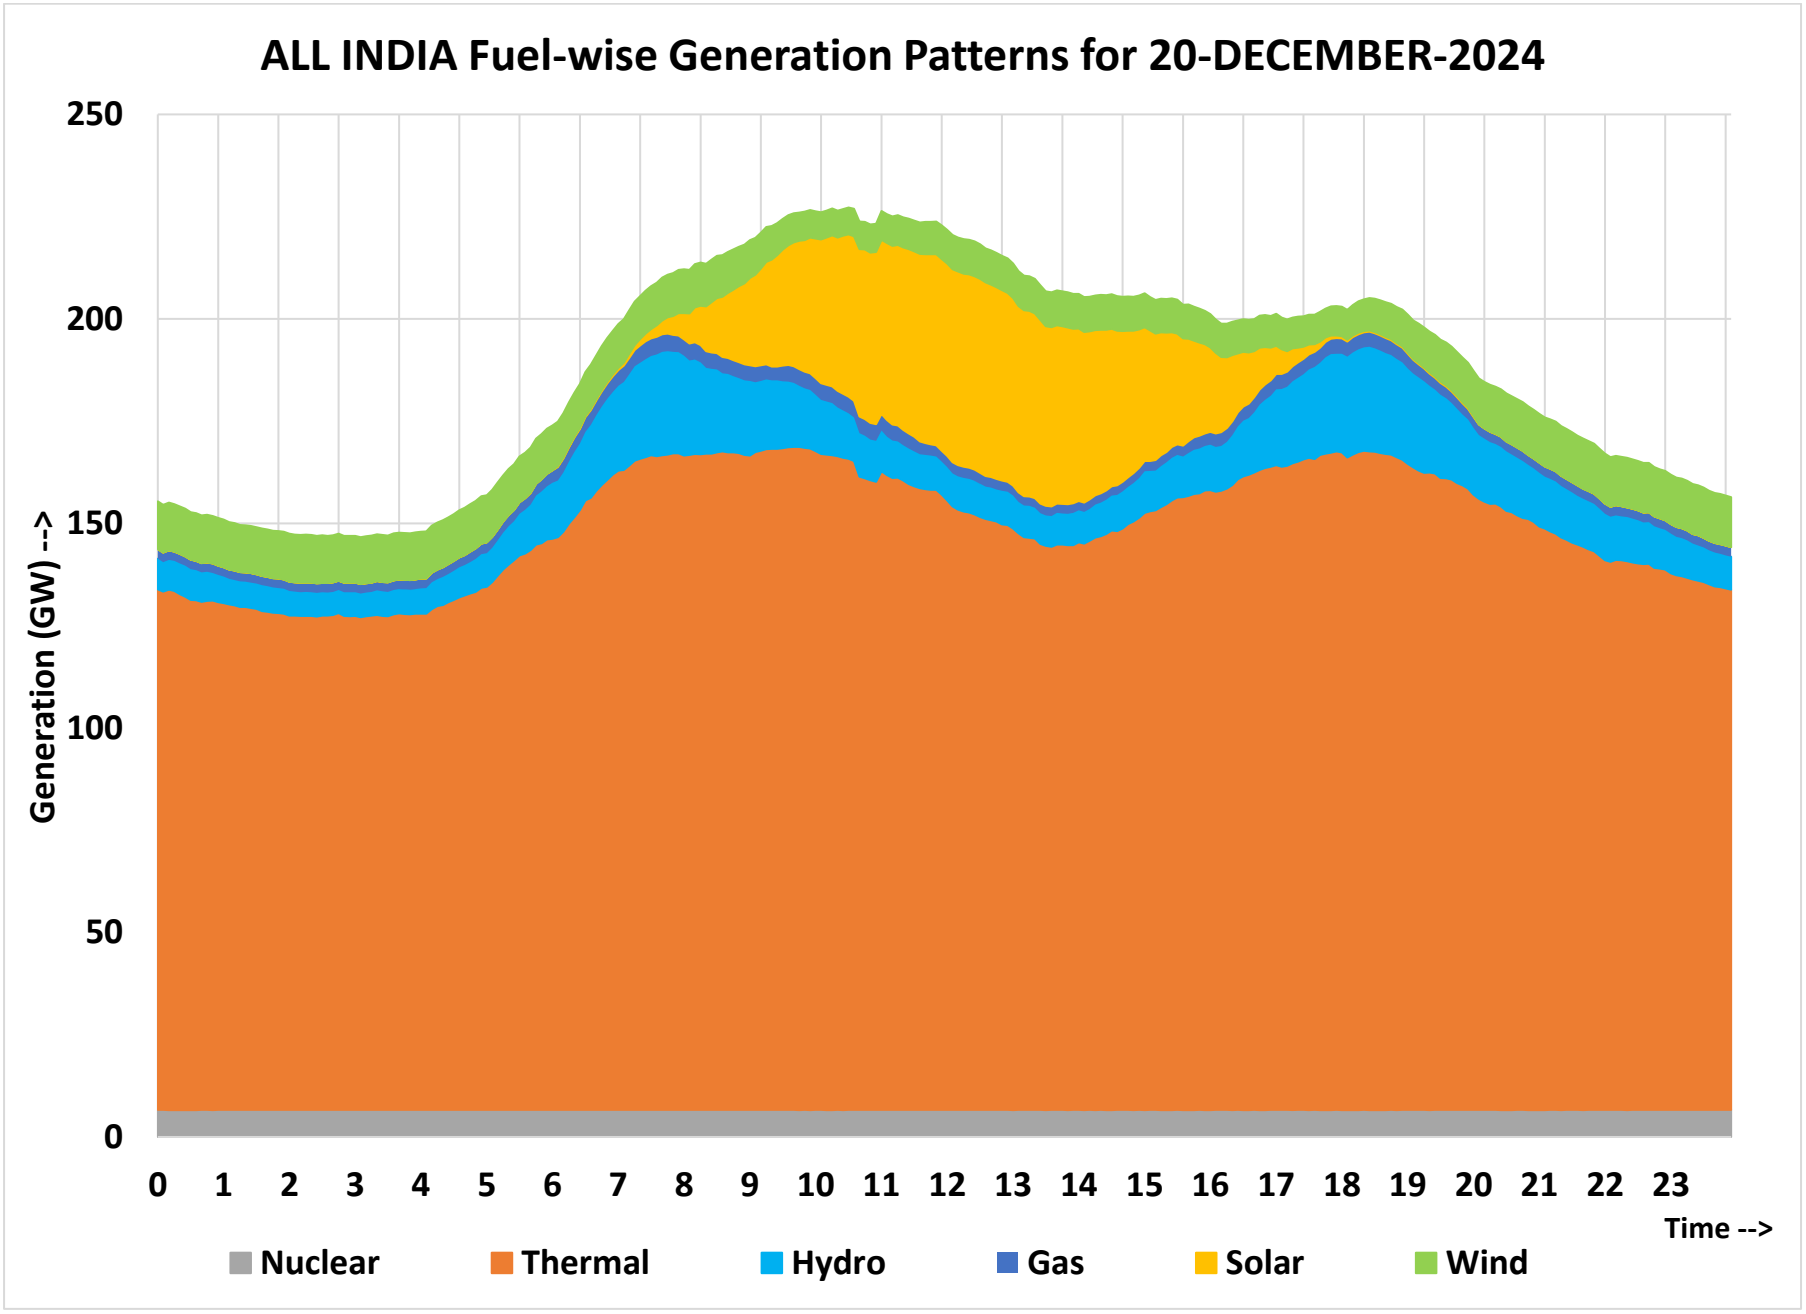
ALL INDIA Fuel-wise Generation Patterns for 20-DECEMBER-2024
Generation (GW) -->
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
Time -->
Nuclear
Thermal
Hydro
Gas
Solar
Wind

20 दिसंबर 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 20 DECEMBER 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	151670		**12:05**	217226
00:20	151494		**12:20**	215949
00:35	149985		**12:35**	213996
00:50	149402		**12:50**	212174
01:05	147782		**13:05**	209282
01:20	146830		**13:20**	207909
01:35	145878		**13:35**	203613
01:50	145351		**13:50**	203543
02:05	144272		**14:05**	202051
02:20	144051		**14:20**	203240
02:35	143688		**14:35**	202681
02:50	143587		**14:50**	202673
03:05	143212		**15:05**	202443
03:20	143808		**15:20**	202033
03:35	144071		**15:35**	200796
03:50	144099		**15:50**	200105
04:05	144702		**16:05**	197162
04:20	147422		**16:20**	196557
04:35	149923		**16:35**	197318
04:50	151968		**16:50**	198372
05:05	154765		**17:05**	198043
05:20	159768		**17:20**	198199
05:35	163666		**17:35**	198557
05:50	168386		**17:50**	200186
06:05	171222		**18:05**	199879
06:20	178121		**18:20**	202055
06:35	184507		**18:35**	201825
06:50	191140		**18:50**	200392
07:05	195963		**19:05**	197205
07:20	201827		**19:20**	194602
07:35	205336		**19:35**	191813
07:50	208068		**19:50**	187976
08:05	208998		**20:05**	183192
08:20	210492		**20:20**	181271
08:35	213207		**20:35**	178937
08:50	215307		**20:50**	176567
09:05	217039		**21:05**	173531
09:20	219860		**21:20**	170839
09:35	222392		**21:35**	168592
09:50	223308		**21:50**	166653
10:05	223273		**22:05**	163112
10:20	223534		**22:20**	163225
10:35	223476		**22:35**	161666
10:50	222889		**22:50**	160345
11:05	222951		**23:05**	158350
11:20	221939		**23:20**	157023
11:35	220577		**23:35**	155178
11:50	220599		**23:50**	154051
Maximum Demand of 224169 MW met@10:30 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - DECEMBER 2024

REGION	STATE	Energy Requirement & Met (MU/Day)			Energy Requirement & Met (MU)				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	128	128	0	0.0	283	283	0	0.0
	Delhi	76	76	0.0	2357	2357	0	0.0	5213	5213	0	0.0
	Haryana	152	152	0.0	4717	4717	0	0.0	9351	9351	0	0.0
	Himachal Pradesh	38	38	0.0	1186	1186	0	0.0	2254	2254	0	0.0
	J&K(UT) and Ladakh(UT)	64	63	-0.7	1978	1956	-22	-1.1	3157	3157	0	0.0
	Punjab	155	155	0.0	4811	4811	0	0.0	9355	9355	0	0.0
	Rajasthan	322	322	0.0	9976	9976	0	0.0	18643	18643	0	0.0
	Uttar Pradesh	334	334	-0.1	10355	10352	-3	0.0	20666	20666	0	0.0
	Uttarakhand	44	44	0.0	1354	1354	0	0.0	2504	2504	0	0.0
	Railway_NR ISTS	4	4	0.0	124	124	0	0.0	223	223	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	5	5	0	0.0
	TOTAL	1193	1192	-0.8	36988	36963	-25	-0.1	68491	68491	0	0.0
WR	Gujarat	410	410	0.0	12701	12701	0	0.0	22461	22453	-8	0.0
	Madhya Pradesh	323	323	-0.4	10026	10013	-13	-0.1	19341	19183	-159	-0.8
	Chhattisgarh	98	98	0.0	3045	3045	0	0.0	5169	5169	0	0.0
	Maharashtra	567	567	0.0	17572	17572	0	0.0	28632	28632	0	0.0
	Goa	14	14	0.0	444	444	0	0.0	749	749	0	0.0
	DNHDDPDCL	30	30	0.0	928	928	0	0.0	1362	1362	0	0.0
	AMNSIL	18	18	0.0	548	548	0	0.0	932	932	0	0.0
	BALCO	13	13	0.0	392	392	0	0.0	537	537	0	0.0
	RIL JAMNAGAR*	1	1	0.0	36	36	0	0.0	101	101	0	0.0
	TOTAL	1474	1474	0.0	45679	45679	0	0.0	77574	77438	-136	-0.2
SR	Andhra Pradesh	191	191	0.0	5923	5923	0	0.0	10527	10527	0	0.0
	Telangana	242	242	0.0	7494	7494	0	0.0	14375	14375	0	0.0
	Karnataka	238	238	0.0	7376	7376	0	0.0	15312	15312	0	0.0
	Kerala	82	82	0.0	2544	2544	0	0.0	4478	4478	0	0.0
	Tamil Nadu	304	304	0.0	9419	9419	0	0.0	16307	16307	0	0.0
	Puducherry	8	8	0.0	261	261	0	0.0	448	448	0	0.0
	TOTAL	1065	1065	0.0	33017	33017	0	0.0	57460	57460	0	0.0
ER	Bihar	90	90	-0.2	2782	2777	-5	-0.2	5424	5424	0	0.0
	Jharkhand	38	38	0.0	1170	1169	-1	-0.1	2090	2090	0	0.0
	DVC	68	68	0.0	2114	2114	0	0.0	3290	3290	0	0.0
	Odisha	96	96	0.0	2963	2963	0	0.0	5255	5255	0	0.0
	West Bengal	139	139	0.0	4310	4310	0	0.0	7256	7256	0	0.0
	Sikkim	2	2	0.0	57	57	0	0.0	127	127	0	0.0
	Railways_ER ISTS	0	0	0.0	5	5	0	0.0	29	29	0	0.0
	TOTAL	432	432	-0.2	13401	13395	-6	0.0	23057	23057	0	0.0
NER	Arunachal Pradesh	3	3	0.0	88	88	0	0.0	167	167	0	0.0
	Assam	27	27	0.0	824	824	0	0.0	1543	1523	-20	-1.3
	Manipur	4	4	0.0	112	112	0	0.0	269	269	0	0.0
	Meghalaya	6	6	0.0	201	201	0	0.0	378	378	0	0.0
	Mizoram	2	2	0.0	69	69	0	0.0	162	162	0	0.0
	Nagaland	3	3	0.0	79	79	0	0.0	176	176	0	0.0
	Tripura	5	5	0.0	160	160	0	0.0	239	239	0	0.0
	TOTAL	49	49	0.0	1533	1533	0	0.0	2912	2912	0	0.0
ALL INDIA		4213	4212	-1.0	130618	130587	-31	0.0				

* RIL Jamnagar has been added as new entity wef 01.12.2024

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF DECEMBER 2024 vs DECEMBER 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Dec-23	Dec-24	Difference	% Change	Average MU/day for Oct-24	Dec-23	Dec-24	Difference	% Change	Average MU/day for Oct-24
NR	Chandigarh	117	128	11	9	4	117	128	11	9	4
	Delhi	2211	2357	146	7	76	2211	2357	146	7	76
	Haryana	4447	4717	269	6	152	4446	4717	270	6	152
	Himachal Pradesh	1128	1186	59	5	38	1125	1186	61	5	38
	J&K(UT) and Ladakh(UT)	1822	1978	156	9	64	1809	1956	147	8	63
	Punjab	4402	4811	409	9	155	4402	4811	409	9	155
	Rajasthan	9343	9976	633	7	322	9339	9976	637	7	322
	Uttar Pradesh	9803	10355	552	6	334	9799	10352	553	6	334
	Uttarakhand	1280	1354	74	6	44	1277	1354	77	6	44
	Railway_NR ISTS/NFL	108	126	18	16	4	108	126	18	16	4
	TOTAL	34661	36988	2327	7	1193	34634	36963	2329	7	1192
WR	Gujarat	11959	12701	741	6	410	11958	12701	742	6	410
	Madhya Pradesh	8772	10026	1254	14	323	8772	10013	1241	14	323
	Chhattisgarh	2782	3045	263	9	98	2782	3045	263	9	98
	Maharashtra	16295	17572	1277	8	567	16295	17572	1277	8	567
	Goa	414	444	30	7	14	414	444	30	7	14
	DNHDDPDCL	881	928	47	5	30	881	928	47	5	30
	AMNSIL	587	548	-39	-7	18	587	548	-39	-7	18
	BALCO	386	392	6	1	13	386	392	6	1	13
	RIL JAMNAGAR*	-	-	-	-	-	-	-	-	-	-
	TOTAL	42077	45679	3602	9	1474	42076	45679	3603	9	1474
SR	Andhra Pradesh	5807	5923	115	2	191	5756	5923	167	3	191
	Telangana	6586	7494	908	14	242	6526	7494	968	15	242
	Karnataka	7952	7376	-576	-7	238	7892	7376	-516	-7	238
	Kerala	2566	2544	-22	-1	82	2547	2544	-2	0	82
	Tamil Nadu	9356	9419	63	1	304	9278	9419	141	2	304
	Puducherry	265	261	-4	-2	8	263	261	-2	-1	8
	TOTAL	32532	33017	485	1	1065	32261	33017	755	2	1065
ER	Bihar	2599	2782	183	7	90	2589	2777	188	7	90
	Jharkhand	984	1170	186	19	38	923	1169	246	27	38
	DVC	2181	2114	-67	-3	68	2181	2114	-67	-3	68
	Odisha	2961	2963	2	0	96	2961	2963	2	0	96
	West Bengal	4053	4310	257	6	139	4053	4310	257	6	139
	Sikkim	52	57	5	9	2	52	57	5	9	2
	Railways_ER ISTS	4	5	2	40	0	4	5	2	40	0
	TOTAL	12833	13401	568	4	432	12762	13395	633	5	432
NER	Arunachal Pradesh	83	88	5	6	3	83	88	5	6	3
	Assam	816	824	8	1	27	816	824	8	1	27
	Manipur	91	112	21	23	4	91	112	21	23	4
	Meghalaya	198	201	3	2	6	198	201	3	2	6
	Mizoram	52	69	17	32	2	52	69	17	32	2
	Nagaland	72	79	7	9	3	72	79	7	9	3
	Tripura	121	160	40	33	5	121	160	40	33	5
	TOTAL	1433	1533	100	7	49	1433	1533	100	7	49
ALL INDIA		123537	130618	7082	6	4213	123167	130587	7420	6	4212

* RIL Jamnagar has been added as new entity wef 01.12.2024

13. DEMAND COMPARISON OF DECEMBER 2024 vs DECEMBER 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Dec-23	Dec-24	Difference	% Change	Dec-23	Dec-24	Difference	% Change
NR	Chandigarh	201	283	82	40.8	201	283	82	40.8
	Delhi	4582	5213	631	13.8	4582	5213	631	13.8
	Haryana	8225	9351	1126	13.7	8225	9351	1126	13.7
	Himachal Pradesh	2162	2254	92	4.3	2162	2254	92	4.3
	J&K(UT) and Ladakh(UT)	2904	3157	253	8.7	2904	3157	253	8.7
	Punjab	8041	9355	1314	16.3	8041	9355	1314	16.3
	Rajasthan	17570	18643	1073	6.1	17570	18643	1073	6.1
	Uttar Pradesh	19874	20666	792	4.0	19874	20666	792	4.0
	Uttarakhand	2417	2504	87	3.6	2417	2504	87	3.6
	Railway_NR ISTS/NFL	222	228	6	2.8	222	228	6	2.8
WR	Gujarat	21430	22461	1030	5	21408	22453	1045	4.9
	Madhya Pradesh	17819	19341	1522	9	17819	19183	1364	7.7
	Chhattisgarh	4836	5169	333	7	4833	5169	336	7.0
	Maharashtra	27755	28632	877	3	27755	28632	877	3.2
	Goa	704	749	45	6	704	749	45	6.4
	DNHDDPDCL	1281	1362	81	6.3	1281	1362	81	6.3
	AMNSIL	901	932	30	3.4	901	932	30	3.4
	BALCO	532	537	5	0.9	532	537	5	0.9
	RIL JAMNAGAR*	-	-	-	-	-	-	-	-
SR	Andhra Pradesh	12085	10527	-1558	-12.9	12085	10527	-1558	-12.9
	Telangana	11857	14375	2518	21.2	11857	14375	2518	21.2
	Karnataka	15005	15312	308	2.1	15005	15312	308	2.1
	Kerala	4275	4478	203	4.7	4275	4478	203	4.7
	Tamil Nadu	16099	16307	208	1.3	16099	16307	208	1.3
	Puducherry	418	448	30	7.2	418	448	30	7.2
ER	Bihar	4963	5424	461	9.3	4963	5424	461	9.3
	Jharkhand	1827	2090	263	14.4	1827	2090	263	14.4
	DVC	3493	3290	-203	-5.8	3493	3290	-203	-5.8
	Odisha	5578	5255	-323	-5.8	5578	5255	-323	-5.8
	West Bengal	7096	7256	160	2.3	7096	7256	160	2.3
	Sikkim	115	127	12	10.4	115	127	12	10.4
	Railways_ER ISTS	27	29	2	7.4	27	29	2	7.4
NER	Arunachal Pradesh	163	167	4	2.5	163	167	4	2.5
	Assam	1553	1543	-10	-0.6	1553	1523	-30	-1.9
	Manipur	235	269	34	14.5	235	269	34	14.5
	Meghalaya	349	378	29	8.2	349	378	29	8.2
	Mizoram	140	162	22	15.7	140	162	22	15.7
	Nagaland	162	176	14	8.6	157	176	19	12.1
	Tripura	239	239	-1	-0.2	239	239	-1	-0.2

* RIL Jamnagar has been added as new entity wef 01.12.2024

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - DECEMBER 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	127.87	128.44	0.57	0.45	4.12	4.14	0.02
	Delhi	2311.06	2282.84	-28.22	-1.22	74.55	73.64	-0.91
	Haryana	3244.16	3192.63	-51.53	-1.59	104.65	102.99	-1.66
	Himachal Pradesh	971.52	932.92	-38.60	-3.97	31.34	30.09	-1.25
	J&K(UT) and Ladakh(UT)	1815.25	1803.53	-11.72	-0.65	58.56	58.18	-0.38
	Punjab	2090.77	2070.65	-20.12	-0.96	67.44	66.80	-0.65
	Rajasthan	3476.02	3409.62	-66.40	-1.91	112.13	109.99	-2.14
	Uttar Pradesh	3134.77	3093.32	-41.45	-1.32	101.12	99.78	-1.34
	Uttarakhand	1023.41	1029.29	5.88	0.57	33.01	33.20	0.19
	Railways_NR ISTS	117.54	124.07	6.53	5.56	3.79	4.00	0.21
	NFL	3.00	2.82	-0.18	-5.86	0.10	0.09	-0.01
	Total	18315.37	18070.14	-245.23	-1.34	590.82	582.91	-7.91
WR	Gujarat	5617.56	5525.72	-91.84	-1.63	181.21	178.25	-2.96
	Madhya Pradesh	6202.85	6092.45	-110.40	-1.78	200.09	196.53	-3.56
	Chhattisgarh	1336.31	1329.91	-6.40	-0.48	43.11	42.90	-0.21
	Maharashtra	6402.51	6323.76	-78.75	-1.23	206.53	203.99	-2.54
	Goa	416.26	428.47	12.21	2.93	13.43	13.82	0.39
	DNHDDPDCL	930.35	928.28	-2.07	-0.22	30.01	29.94	-0.07
	AMNSIL	258.55	266.99	8.44	3.26	8.34	8.61	0.27
	BALCO	393.59	391.51	-2.08	-0.53	12.70	12.63	-0.07
	RIL JAMNAGAR*	37.43	35.91	-1.52	-4.06	1.21	1.16	-0.05
	Total	21595.41	21323.00	-272.41	-1.26	696.63	687.84	-8.79
SR	Andhra Pradesh	1627.91	1615.57	-12.34	-0.76	52.51	52.12	-0.40
	Telangana	4548.94	4542.74	-6.20	-0.14	146.74	146.54	-0.20
	Karnataka	2084.63	2075.63	-9.00	-0.43	67.25	66.96	-0.29
	Kerala	2033.80	2070.36	36.56	1.80	65.61	66.79	1.18
	Tamil Nadu	5420.48	5363.84	-56.64	-1.04	174.85	173.03	-1.83
	Puducherry	252.84	245.91	-6.93	-2.74	8.16	7.93	-0.22
	Goa (SR)	69.14	71.14	2.00	2.89	2.23	2.29	0.06
	Total	16037.74	15985.19	-52.55	-0.33	517.35	515.65	-1.70
ER	Bihar	2450.46	2424.30	-26.16	-1.07	79.05	78.20	-0.84
	Jharkhand	836.20	824.40	-11.81	-1.41	26.97	26.59	-0.38
	DVC	-1253.97	-1244.23	9.74	-0.78	-40.45	-40.14	0.31
	Odisha	725.64	682.41	-43.24	-5.96	23.41	22.01	-1.39
	West Bengal	324.61	268.66	-55.95	-17.24	10.47	8.67	-1.80
	Sikkim	56.00	56.71	0.71	1.27	1.81	1.83	0.02
	Railways_ER ISTS	5.32	5.30	-0.02	-0.39	0.17	0.17	0.00
	Total	3144.27	3017.54	-126.73	-4.03	101.43	97.34	-4.09
NER	Arunachal Pradesh	85.92	82.82	-3.10	-3.61	2.77	2.67	-0.10
	Assam	607.08	615.15	8.07	1.33	19.58	19.84	0.26
	Manipur	115.01	112.30	-2.71	-2.36	3.71	3.62	-0.09
	Meghalaya	177.06	172.58	-4.48	-2.53	5.71	5.57	-0.14
	Mizoram	54.71	51.03	-3.68	-6.73	1.76	1.65	-0.12
	Nagaland	76.53	75.20	-1.33	-1.74	2.47	2.43	-0.04
	Tripura	117.40	118.21	0.81	0.69	3.79	3.81	0.03
	Total	1233.71	1227.29	-6.42	-0.52	39.80	39.59	-0.21
All India Total		60326.50	59623.16	-703.34	-1.17	1946.02	1923.33	-22.69

* RIL Jamnagar has been added as new entity wef 01.12.2024

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Fin. Year 2024-25
Name of Line										
Import of NR from WR (WR-NR)										
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	714.49	611.32	751.39	**8679.65**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	840.34	817.51	665.18	**5066.72**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	1009.96	819.22	774.41	**8557.89**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	583.07	599.61	586.45	**5423.12**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	1570.74	720.37	1288.63	**17068.33**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	0.00	39.19	106.05	**761.48**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	0.00	0.00	3.10	**231.57**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	17.54	0.00	1.08	**64.64**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	60.41	0.08	2.44	**596.82**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	60.83	64.26	52.46	**542.35**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	58.67	96.18	95.67	**611.38**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	0.00	0.00	0.00	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	1096.69	827.50	752.53	**9088.68**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	0.00	0.00	74.13	**1565.91**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	1113.89	1038.27	1036.90	**14213.89**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	89.57	0.00	0.00	**650.59**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**7216.20**	**5633.51**	**6190.42**	**73139.24**
Export of NR to WR (NR-WR)										
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	0.00	0.00	0.00	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	368.54	423.95	433.38	**2924.64**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	152.00	95.38	6.70	**744.93**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	126.24	173.03	73.94	**837.90**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	31.75	9.91	2.04	**103.36**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	1.94	45.97	66.66	**339.29**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	51.59	74.53	67.31	**357.43**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	0.00	561.44	663.38	**4132.97**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	391.69	523.07	148.17	**2224.42**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	0.00	51.46	94.50	**341.30**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**1123.75**	**1958.74**	**1556.08**	**12021.23**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Fin. Year 2024-25
Name of Line										
Import of NR from ER (ER-NR)										
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	139.89	211.26	229.72	**1243.02**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	405.62	482.45	443.73	**1985.65**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	366.56	351.78	368.50	**2879.46**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	250.72	211.75	12.40	**1669.22**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	527.53	418.43	523.23	**3092.97**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	319.38	212.80	260.15	**2124.23**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	95.04	41.13	143.70	**384.96**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	259.86	222.85	283.52	**1741.80**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	0.00	0.94	0.00	**11.61**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	136.66	108.64	109.12	**611.92**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	65.13	77.91	68.47	**295.29**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	7.45	17.59	22.02	**173.94**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	0.53	0.00	0.48	**14.58**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	0.00	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	159.57	132.81	163.60	**876.81**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	144.05	156.95	159.21	**807.01**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**2877.99**	**2647.29**	**2787.85**	**17914.08**
Import of NR from NER (NER-NR)										
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55	555.71	550.01	30.48	**2232.99**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**555.71**	**550.01**	**30.48**	**2232.99**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Fin. Year 2024-25
Name of Line										
Export of NR to ER (NR-ER)										
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	0.00	0.00	0.00	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	0.00	0.00	0.00	**225.17**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	7.00	8.26	0.00	**409.05**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	0.00	0.88	0.00	**19.94**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	0.00	0.20	0.00	**7.33**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	0.00	0.00	0.00	**44.74**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	4.74	0.65	0.00	**9.05**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	0.48	0.00	0.60	**3.86**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	0.58	0.91	1.34	**7.10**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	14.57	14.82	16.20	**144.95**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	0.00	0.00	0.00	**6.54**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**27.37**	**25.72**	**18.14**	**1021.46**
Export of NR to NER (NER-NR)										
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	0.00	0.00	445.16	**1810.69**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**0.00**	**0.00**	**445.16**	**1810.69**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Fin. Year 2024-25
Name of Line										
Export of WR to ER (WR-ER)										
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	308.09	84.78	53.41	**5388.20**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	65.67	50.80	64.41	**1907.05**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	0.04	0.00	0.00	**37.15**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	29.14	9.49	3.76	**1096.27**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	0.51	1.58	0.03	**651.78**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	4.23	14.85	12.46	**86.95**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	0.05	0.60	0.00	**15.60**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**407.73**	**162.10**	**134.08**	**9183.01**
Import of WR from ER (ER - WR)										
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	68.03	111.05	218.28	**508.01**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	334.28	233.51	328.11	**2629.80**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	325.55	520.92	389.23	**2648.96**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	59.96	84.87	42.89	**251.23**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	380.72	297.88	324.60	**2262.48**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	48.12	15.83	17.45	**260.95**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	60.23	34.62	45.32	**354.49**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**1276.89**	**1298.67**	**1365.88**	**8915.93**
Export of ER to NER (ER - NER)										
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	104.89	226.52	18.80	**817.07**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	173.82	295.36	19.99	**1209.96**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	32.38	44.04	2.57	**238.85**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**311.10**	**565.92**	**41.35**	**2265.88**
Import of ER from NER (NER - ER)										
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	18.09	0.00	87.66	**558.54**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	17.26	0.00	183.94	**914.74**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	2.72	0.00	38.42	**157.83**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**38.07**	**0.00**	**310.02**	**1631.11**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Fin. Year 2024-25
Name of Line										
Export of ER to SR (ER - SR)										
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	217.59	323.46	231.29	**2012.15**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	1105.23	1090.58	1197.54	**8908.81**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	1297.13	1542.96	1693.06	**11772.10**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**2619.95**	**2957.00**	**3121.89**	**22693.06**
Import of ER from SR (SR - ER)										
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	0.00	0.00	0.00	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	0.00	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**0.00**	**0.00**	**0.00**	**490.93**
Export of WR to SR (WR-SR)										
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	231.23	335.29	602.14	**2384.55**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	37.08	143.60	280.25	**1782.19**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	590.95	779.18	1057.49	**7225.70**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	0.00	0.00	0.01	**0.03**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	574.81	746.92	1396.79	**9035.31**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	72.89	67.59	70.47	**600.87**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	0.03	2.33	0.06	**149.63**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	686.47	951.98	1160.41	**7875.11**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**2193.47**	**3026.89**	**4567.60**	**29053.39**
Import of WR from SR (SR - WR)										
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	18.75	0.00	0.00	**1635.03**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	410.23	148.25	152.27	**3515.97**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	11.46	0.85	0.04	**158.59**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	948.20	690.35	704.16	**7581.62**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	0.00	0.00	0.00	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	0.02	0.01	0.01	**0.07**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	6.77	0.01	0.06	**165.44**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**1395.43**	**839.47**	**856.54**	**13475.38**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**20044**	**19665**	**21426**	**195848**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during December 2024

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Dec-24	23.71	27.57	29.56	19.02	0.00	23.85	7.21	0.00		0.00	1.73	3.11	0.00	0.00	18.90	0.00	37.30	0.00	**191.96**
2-Dec-24	23.92	30.33	31.59	20.47	0.00	24.10	7.21	0.00		0.17	1.65	2.97	0.00	0.00	11.64	0.00	39.64	0.00	**193.69**
3-Dec-24	27.29	28.42	32.76	20.54	0.00	23.37	7.21	0.00		0.00	1.64	3.17	0.00	0.00	14.80	0.00	37.54	0.00	**196.74**
4-Dec-24	24.55	21.46	23.22	19.09	0.00	44.23	7.16	0.00		0.00	1.62	3.29	0.00	0.00	17.01	3.75	33.50	0.00	**198.88**
5-Dec-24	17.55	24.56	22.27	20.58	0.00	63.56	7.15	0.00		0.00	1.63	3.39	0.00	0.00	17.24	0.00	30.97	0.00	**208.90**
6-Dec-24	20.22	26.46	24.54	18.40	0.00	46.87	7.25	0.00		0.00	1.66	3.32	0.00	0.00	23.67	0.00	24.31	0.00	**196.70**
7-Dec-24	20.24	24.27	23.34	17.14	0.00	51.51	7.22	0.00		0.00	1.67	3.38	0.00	0.00	29.46	0.00	19.49	0.00	**197.72**
8-Dec-24	19.41	17.52	21.06	15.08	0.00	55.20	7.24	0.00		0.00	1.71	3.38	0.00	0.00	17.94	0.00	25.24	0.00	**183.78**
9-Dec-24	29.34	17.68	25.22	18.24	0.00	39.74	7.21	1.61	1.08	0.00	1.72	3.17	0.00	0.00	15.65	12.21	37.64	0.00	**210.51**
10-Dec-24	28.50	17.30	25.99	19.90	0.00	49.90	7.14	0.00		0.00	1.73	3.25	0.00	0.00	20.08	7.63	39.81	0.00	**221.23**
11-Dec-24	22.92	16.40	22.58	19.28	0.00	62.30	7.24	0.00		0.00	1.66	3.31	0.00	0.00	30.69	0.90	36.28	0.00	**223.56**
12-Dec-24	21.90	15.50	20.36	18.53	0.00	56.09	6.58	0.11		0.00	1.43	2.91	0.00	0.00	29.16	6.46	34.18	0.00	**213.21**
13-Dec-24	27.05	14.51	24.57	19.47	0.00	43.80	1.21	1.13		0.00	1.69	3.32	0.00	0.00	24.22	11.65	38.48	0.00	**211.10**
14-Dec-24	27.30	17.33	28.21	17.37	0.00	36.01	1.23	0.00		0.00	1.82	3.20	0.00	0.00	30.82	1.19	24.54	0.00	**189.02**
15-Dec-24	22.85	20.10	28.02	18.46	0.00	46.56	1.21	0.00		0.00	1.84	3.26	0.00	0.00	31.27	0.00	35.40	0.00	**208.97**
16-Dec-24	25.32	21.95	27.32	19.57	0.00	53.32	1.21	0.00		0.00	1.86	3.23	0.00	0.00	26.09	0.00	33.21	0.00	**213.08**
17-Dec-24	27.59	22.74	28.68	19.46	0.00	47.61	1.22	0.00	0.00	0.00	1.86	3.29	0.00	0.00	28.87	0.00	34.36	0.00	**215.68**
18-Dec-24	22.96	20.03	22.95	18.55	0.00	61.50	1.21	0.00		0.00	1.92	3.31	0.00	0.00	28.66	0.00	33.27	0.00	**214.36**
19-Dec-24	21.42	20.42	22.33	19.22	0.00	47.91	1.21	0.00		0.00	2.00	3.33	0.00	0.00	39.57	0.00	32.50	0.00	**209.91**
20-Dec-24	23.23	17.68	23.38	18.81	0.00	33.41	1.20	0.00		0.00	1.81	3.29	0.00	0.00	30.30	8.71	36.74	0.00	**198.56**
21-Dec-24	24.98	24.19	26.36	20.27	0.00	28.16	0.00	0.00		0.00	2.02	3.38	0.00	0.00	24.12	0.00	35.62	0.00	**189.10**
22-Dec-24	22.67	29.53	26.60	20.30	0.00	23.25	0.00	0.00		0.00	1.92	3.31	0.00	0.00	24.22	0.00	30.54	0.00	**182.34**
23-Dec-24	21.66	26.31	23.78	19.12	0.00	23.25	0.64	0.00		0.00	1.91	3.26	0.00	0.00	24.21	0.00	23.28	0.00	**167.42**
24-Dec-24	16.83	18.75	17.91	17.26	0.00	33.33	1.24	0.00	0.00	0.00	1.94	3.24	0.00	0.00	28.06	0.00	23.54	0.00	**162.10**
25-Dec-24	23.30	17.65	21.52	18.35	0.00	32.77	1.24	0.25		0.00	1.94	3.18	0.00	0.00	18.20	9.12	30.02	0.00	**177.54**
26-Dec-24	25.56	24.49	26.01	17.85	0.00	28.95	1.23	0.00		0.00	1.96	3.17	0.00	0.00	18.12	5.74	33.29	0.00	**186.37**
27-Dec-24	18.66	18.76	21.58	18.47	0.00	32.74	1.24	0.00		0.00	1.72	2.73	0.00	0.00	27.13	0.39	32.48	0.00	**175.90**
28-Dec-24	26.95	18.40	21.92	18.47	0.00	32.08	1.24	0.00		1.16	1.29	1.74	0.00	0.00	18.92	0.68	41.48	0.00	**184.33**
29-Dec-24	37.42	22.50	29.02	20.94	0.00	22.28	1.24	0.00		1.11	1.32	2.42	0.00	0.00	18.18	5.70	44.72	0.00	**206.85**
30-Dec-24	30.59	20.81	27.46	19.30	0.00	54.42	1.24	0.00		0.00	1.15	2.22	0.00	0.00	29.09	0.00	40.16	0.00	**226.44**
31-Dec-24	25.50	21.56	24.30	18.94	0.00	66.56	1.22	0.00		0.00	0.64	2.14	0.00	0.00	36.24	0.00	37.37	0.00	**234.47**
Total	**751.39**	**665.18**	**774.41**	**586.45**	**0.00**	**1288.63**	**106.05**	**3.10**	**1.08**	**2.44**	**52.46**	**95.67**	**0.00**	**0.00**	**752.53**	**74.13**	**1036.90**	**0.00**	**6190.42**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during December 2024

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Dec-24	0.00	0.00	0.00	0.00	14.04	0.00	0.00	3.44		0.40	0.00	0.00	2.25	20.96	0.00	8.43	0.00	0.51	**50.03**
2-Dec-24	0.00	0.00	0.00	0.00	13.35	0.00	0.00	1.85		0.00	0.00	0.00	1.95	20.36	0.00	3.97	0.00	0.65	**42.13**
3-Dec-24	0.00	0.00	0.00	0.00	13.73	0.00	0.00	2.02		0.13	0.00	0.00	1.29	20.93	0.00	2.38	0.00	1.10	**41.58**
4-Dec-24	0.00	0.00	0.00	0.00	15.47	0.00	0.00	0.72		2.25	0.00	0.00	1.90	21.79	0.00	0.00	0.00	3.88	**46.01**
5-Dec-24	0.00	0.00	0.00	0.00	15.77	0.00	0.00	3.37		2.54	0.00	0.00	2.29	22.33	0.00	8.97	0.00	3.96	**59.23**
6-Dec-24	0.00	0.00	0.00	0.00	15.49	0.00	0.00	5.36		1.86	0.00	0.00	2.40	22.32	0.00	16.88	0.00	1.86	**66.17**
7-Dec-24	0.00	0.00	0.00	0.00	15.06	0.00	0.00	4.57		2.25	0.00	0.00	2.23	22.28	0.00	15.10	0.00	2.49	**63.98**
8-Dec-24	0.00	0.00	0.00	0.00	13.45	0.00	0.00	4.63		4.08	0.00	0.00	2.19	21.91	0.00	12.89	0.00	4.12	**63.27**
9-Dec-24	0.00	0.00	0.00	0.00	13.56	0.00	0.00	0.00	0.00	1.97	0.00	0.00	1.63	20.06	0.00	0.00	0.00	2.93	**40.15**
10-Dec-24	0.00	0.00	0.00	0.00	12.96	0.00	0.00	1.02		2.20	0.00	0.00	1.56	21.53	0.00	0.00	0.00	3.10	**42.37**
11-Dec-24	0.00	0.00	0.00	0.00	13.13	0.00	0.00	1.21		4.09	0.00	0.00	2.15	22.38	0.00	0.00	0.00	4.45	**47.41**
12-Dec-24	0.00	0.00	0.00	0.00	12.30	0.00	0.00	0.00		4.01	0.00	0.00	2.09	22.23	0.00	0.00	0.00	5.30	**45.93**
13-Dec-24	0.00	0.00	0.00	0.00	10.90	0.00	0.00	0.00		2.89	0.00	0.00	1.64	20.91	0.00	0.00	0.00	3.95	**40.29**
14-Dec-24	0.00	0.00	0.00	0.00	13.04	0.00	0.00	1.67		2.22	0.00	0.00	1.73	22.39	0.00	0.00	0.00	2.10	**43.15**
15-Dec-24	0.00	0.00	0.00	0.00	13.90	0.00	0.00	4.24		2.15	0.00	0.00	2.05	22.35	0.00	6.80	0.00	2.18	**53.67**
16-Dec-24	0.00	0.00	0.00	0.00	13.99	0.00	0.00	3.82		2.03	0.00	0.00	2.13	22.32	0.00	7.55	0.00	2.31	**54.15**
17-Dec-24	0.00	0.00	0.00	0.00	14.96	0.00	0.00	1.31	0.93	1.35	0.00	0.00	2.51	22.21	0.00	2.04	0.00	2.42	**47.73**
18-Dec-24	0.00	0.00	0.00	0.00	14.15	0.00	0.00	3.14		3.25	0.00	0.00	3.09	22.47	0.00	6.64	0.00	3.70	**56.44**
19-Dec-24	0.00	0.00	0.00	0.00	14.84	0.00	0.00	5.37		3.52	0.00	0.00	2.42	22.25	0.00	12.93	0.00	3.68	**65.01**
20-Dec-24	0.00	0.00	0.00	0.00	13.30	0.00	0.00	0.31		3.60	0.00	0.00	2.41	22.35	0.00	0.00	0.00	5.26	**47.23**
21-Dec-24	0.00	0.00	0.00	0.00	14.86	0.00	1.30	1.60		1.69	0.00	0.00	2.45	22.29	0.00	0.57	0.00	2.83	**47.59**
22-Dec-24	0.00	0.00	0.00	0.00	17.12	0.00	3.67	5.01		0.95	0.00	0.00	2.60	22.34	0.00	13.14	0.00	0.85	**65.68**
23-Dec-24	0.00	0.00	0.00	0.00	16.91	0.00	1.73	4.41		2.50	0.00	0.00	3.47	22.39	0.00	10.39	0.00	3.96	**65.76**
24-Dec-24	0.00	0.00	0.00	0.00	14.25	0.00	0.00	1.59	1.11	4.84	0.00	0.00	3.09	14.88	0.00	2.01	0.00	7.09	**48.86**
25-Dec-24	0.00	0.00	0.00	0.00	13.65	0.00	0.00	0.00		3.01	0.00	0.00	3.21	13.95	0.00	0.00	0.00	5.25	**39.07**
26-Dec-24	0.00	0.00	0.00	0.00	15.20	0.00	0.00	0.40		1.72	0.00	0.00	2.63	22.35	0.00	0.00	0.00	3.70	**46.00**
27-Dec-24	0.00	0.00	0.00	0.00	13.04	0.00	0.00	2.66		3.40	0.00	0.00	2.76	23.24	0.00	0.00	0.00	5.14	**50.24**
28-Dec-24	0.00	0.00	0.00	0.00	11.55	0.00	0.00	1.08		0.00	0.00	0.00	0.78	20.20	0.00	0.00	0.00	2.86	**36.47**
29-Dec-24	0.00	0.00	0.00	0.00	12.61	0.00	0.00	0.22		0.00	0.00	0.00	0.87	21.51	0.00	0.00	0.00	0.24	**35.45**
30-Dec-24	0.00	0.00	0.00	0.00	13.06	0.00	0.00	3.74		0.45	0.00	0.00	1.63	22.01	0.00	5.84	0.00	0.70	**47.43**
31-Dec-24	0.00	0.00	0.00	0.00	13.74	0.00	0.00	5.18		1.31	0.00	0.00	1.91	21.89	0.00	11.64	0.00	1.93	**57.60**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**433.38**	**0.00**	**6.70**	**73.94**	**2.04**	**66.66**	**0.00**	**0.00**	**67.31**	**663.38**	**0.00**	**148.17**	**0.00**	**94.50**	**1556.08**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during December 2024

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Dec-24	5.90	15.55	12.06	7.15	14.30	5.62	0.60	7.94		3.54	2.30	0.23		0.00	0.00	4.52	4.99	**84.70**	15.50	**15.50**
2-Dec-24	6.65	16.23	12.42	5.25	15.35	6.20	0.80	8.44		3.43	2.35	0.31		0.00	0.00	5.01	5.35	**87.79**	14.98	**14.98**
3-Dec-24	8.67	20.52	14.60		22.44	10.92	6.50	11.12		2.91	2.98	0.48		0.00	0.00	7.37	7.41	**115.92**	0.00	**0.00**
4-Dec-24	7.81	17.80	13.03		20.70	8.58	4.95	10.17		3.17	2.72	0.30			0.00	6.52	7.20	**102.95**	0.00	**0.00**
5-Dec-24	9.20	19.56	13.25		20.79	8.84	4.20	11.29		2.91	3.09	0.29			0.00	6.77	5.25	**105.44**	0.00	**0.00**
6-Dec-24	10.37	20.56	12.41	0.00	21.93	9.98	5.99	11.03		2.78	2.95	0.41			0.00	7.14	6.71	**112.26**	0.00	**0.00**
7-Dec-24	9.25	19.35	11.73	0.00	21.10	9.39	5.98	10.32		3.33	2.55	0.26	0.00		0.00	6.88	6.26	**106.40**	0.00	**0.00**
8-Dec-24	6.74	14.26	10.64		18.29	9.18	5.16	9.59		3.40	2.38	0.10		0.00	0.00	5.88	5.12	**90.74**	0.00	**0.00**
9-Dec-24	7.16	11.95	11.56		18.28	8.08	4.88	9.61		3.12	2.68	0.11	0.00		0.00	5.91	5.28	**88.62**	0.00	**0.00**
10-Dec-24	7.40	12.31	12.24		18.33	7.90	5.22	10.29		2.87	2.75	0.28	0.00	0.00	0.00	5.90	5.53	**91.02**	0.00	**0.00**
11-Dec-24	6.79	14.37	11.45		17.86	7.54	4.49	9.46		3.55	2.33			0.00	0.00	5.72	5.20	**88.76**	0.00	**0.00**
12-Dec-24	7.09	15.46	12.19		19.32	8.24	4.97	9.37		3.80	2.03	0.60		0.00	0.00	6.24	5.44	**94.75**	0.00	**0.00**
13-Dec-24	6.85	13.35	12.32		19.09	8.79	5.36	9.60		3.57	2.26	0.52		0.00	0.00	6.18	5.58	**93.47**	0.00	**0.00**
14-Dec-24	7.39	18.46	13.18	0.00	21.04	9.22	6.21	9.98		3.85	2.01	0.59			0.00	3.49	6.55	**101.97**	0.00	**0.00**
15-Dec-24	6.64	11.53	11.48		16.21	7.88	3.11	8.61		3.68	1.85	0.55	0.00		0.00	5.19	4.57	**81.30**	0.00	**0.00**
16-Dec-24	8.53	14.87	11.52		16.05	8.16	4.42	8.93		3.83	2.13	0.72		0.00	0.00	5.05	4.25	**88.46**	0.00	**0.00**
17-Dec-24	5.55	15.05	12.56		15.39	7.31	4.42	9.32		3.51	2.38	1.05			0.00	4.89	6.15	**87.58**	0.00	**0.00**
18-Dec-24	7.65	11.25	9.98		11.93	6.85	3.64	7.97		3.72	2.05	0.72	0.00		0.00	3.63	5.12	**74.51**	0.00	**0.00**
19-Dec-24	8.67	14.11	10.97		14.36	9.05	4.47	9.21		3.62	2.24	0.48	0.00		0.00	4.51	5.83	**87.52**	0.00	**0.00**
20-Dec-24	7.78	12.12	11.17		13.05	8.69	4.01	8.48		3.85	2.11	0.96		0.00	0.00	4.05	5.30	**81.57**	0.00	**0.00**
21-Dec-24	9.21	14.45	11.50		16.51	9.30	4.00	10.14		3.47	2.37	1.10	0.48		0.00	5.25	6.12	**93.90**	0.00	**0.00**
22-Dec-24	9.19	17.86	12.21		18.08	10.82	4.81	11.08		3.61	2.20	0.75	0.00		0.00	5.79	6.11	**102.51**	0.00	**0.00**
23-Dec-24	7.48	16.56	11.57		17.78	9.68	4.74	10.35		3.87	1.94	0.58	0.00		0.00	5.61	5.56	**95.72**	0.00	**0.00**
24-Dec-24	7.17	15.29	11.98		19.25	9.41	4.98	10.01		4.21	1.58	0.58	0.00	0.00	0.00	6.24	4.41	**95.11**	0.00	**0.00**
25-Dec-24	6.25	14.55	12.65		15.98	9.48	6.13	8.44		4.08	1.78	0.97			0.00	5.07	5.01	**90.39**	0.00	**0.00**
26-Dec-24	9.08	15.49	13.54		17.05	9.50	7.25	8.36		3.65	2.05	1.25			0.00	5.78	4.82	**97.82**	0.00	**0.00**
27-Dec-24	7.64	12.63	12.40		17.06	7.91	6.35	7.86		3.84	1.90	0.77		0.00	0.00	5.48	4.07	**87.91**	0.00	**0.00**
28-Dec-24	5.25	6.37	11.50		13.27	6.04	4.64	6.15		3.36	1.47	1.05			0.00	4.15	3.15	**66.40**	0.00	**0.00**
29-Dec-24	5.27	5.81	11.13		10.31	7.09	3.53	6.66		2.40	1.32	1.50		0.00	0.00	3.09	1.99	**60.10**	0.00	**0.00**
30-Dec-24	5.11	7.24	8.16		10.95	7.05	3.67	7.04		4.02	1.83	2.21			0.00	3.31	2.46	**63.05**	0.00	**0.00**
31-Dec-24	5.98	8.82	11.10		11.18	7.45	4.22	6.70		4.17	1.89	2.30	0.00		0.00	2.98	2.42	**69.21**	0.00	**0.00**
Total	**229.72**	**443.73**	**368.50**	**12.40**	**523.23**	**260.15**	**143.70**	**283.52**	**0.00**	**109.12**	**68.47**	**22.02**	**0.48**	**0.00**	**0.00**	**163.60**	**159.21**	**2787.85**	**30.48**	**30.48**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during December 2024

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Dec-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.53	0.00	0.00	**0.63**	0.00	**0.00**
2-Dec-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.53	0.00	0.00	**0.63**	0.00	**0.00**
3-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.08	0.53	0.00	0.00	**0.61**	15.66	**15.66**
4-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.72	0.00	0.00	**0.72**	12.42	**12.42**
5-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.52	0.00	0.00	**0.52**	9.73	**9.73**
6-Dec-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.53	0.00	0.00	**0.53**	12.62	**12.62**
7-Dec-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.55	0.00	0.00	**0.55**	16.30	**16.30**
8-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.08	0.58	0.00	0.00	**0.66**	16.85	**16.85**
9-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.46	0.00	0.00	**0.46**	16.15	**16.15**
10-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.18	0.50	0.00	0.00	**0.68**	17.15	**17.15**
11-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00			0.08	0.44	0.00	0.00	**0.52**	16.80	**16.80**
12-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.50	0.00	0.00	**0.60**	17.21	**17.21**
13-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.14	0.51	0.00	0.00	**0.65**	17.02	**17.02**
14-Dec-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.56	0.00	0.00	**0.56**	15.94	**15.94**
15-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.60		0.00	0.00	0.00	**0.60**	15.94	**15.94**
16-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.09	0.53	0.00	0.00	**0.62**	16.65	**16.65**
17-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.56	0.00	0.00	**0.56**	16.95	**16.95**
18-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.56	0.00	0.00	**0.56**	17.00	**17.00**
19-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.62	0.00	0.00	**0.62**	17.34	**17.34**
20-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.11	0.58	0.00	0.00	**0.69**	8.10	**8.10**
21-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.67	0.00	0.00	**0.67**	7.65	**7.65**
22-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.56	0.00	0.00	**0.56**	12.08	**12.08**
23-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.44	0.00	0.00	**0.44**	16.54	**16.54**
24-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.10	0.43	0.00	0.00	**0.53**	16.57	**16.57**
25-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.55	0.00	0.00	**0.55**	17.17	**17.17**
26-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.52	0.00	0.00	**0.52**	16.59	**16.59**
27-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.08	0.55	0.00	0.00	**0.63**	17.24	**17.24**
28-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.60	0.00	0.00	**0.60**	16.71	**16.71**
29-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.51	0.00	0.00	**0.61**	15.62	**15.62**
30-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.51	0.00	0.00	**0.51**	16.56	**16.56**
31-Dec-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.55	0.00	0.00	**0.55**	16.60	**16.60**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.60**	**1.34**	**16.20**	**0.00**	**0.00**	**18.14**	**445.16**	**445.16**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.3 Import and Export of ER with WR & NER during December 2024

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Dec-24	4.0	0.0	0.0	0.7	0.0	0.5	0.0	**5.18**	3.3	18.5	12.3	1.4	9.3	0.5	1.2	**46.49**	8.40	9.51	1.19	**19.10**	0.00	0.00	0.00	**0.00**
2-Dec-24	4.0	0.0	0.0	0.6	0.0	0.3	0.0	**4.91**	3.6	14.3	11.9	2.1	10.2	0.6	1.1	**43.80**	7.74	9.55	1.31	**18.59**	0.54	1.24	0.34	**2.13**
3-Dec-24	1.6	0.0	0.0	0.1	0.0	0.3	0.0	**1.95**	5.2	12.0	12.5	3.0	12.1	1.1	1.3	**47.16**	0.00	0.00	0.00	**0.00**	3.26	6.63	1.57	**11.46**
4-Dec-24	0.4	4.8	0.0	0.0	0.0	0.1	0.0	**5.30**	8.7	8.1	10.8	3.9	9.8	0.8	1.5	**43.66**	0.50	0.26	0.01	**0.77**	1.96	4.09	1.08	**7.12**
5-Dec-24	0.0	5.9	0.0	0.0	0.0	0.0	0.0	**6.00**	13.4	15.5	11.7	5.2	9.6	0.7	1.5	**57.68**	0.54	0.21	0.01	**0.76**	1.50	3.32	0.90	**5.72**
6-Dec-24	0.0	2.4	0.0	0.0	0.0	0.0	0.0	**2.39**	12.0	11.1	12.4	4.9	12.2	0.9	1.3	**54.83**	0.27	0.02	0.00	**0.29**	2.39	4.88	1.13	**8.41**
7-Dec-24	0.5	0.3	0.0	0.0	0.0	0.1	0.0	**0.87**	9.7	16.0	12.5	4.0	11.7	0.7	0.9	**55.50**	0.02	0.00	0.00	**0.02**	2.97	6.04	1.23	**10.24**
8-Dec-24	2.3	0.0	0.0	0.0	0.0	0.2	0.0	**2.58**	7.0	21.9	12.4	1.8	11.1	0.6	0.9	**55.73**	0.00	0.00	0.00	**0.00**	3.71	7.19	1.45	**12.35**
9-Dec-24	2.3	3.1	0.0	0.0	0.0	0.5	0.0	**5.91**	4.8	6.4	9.9	0.0	9.3	0.3	1.1	**31.86**	0.00	0.00	0.00	**0.00**	3.34	6.78	1.36	**11.48**
10-Dec-24	1.2	0.0	0.0	0.0	0.0	0.4	0.0	**1.67**	5.1	12.3	13.3	0.0	10.8	0.5	1.4	**43.41**	0.02	0.00	0.00	**0.02**	3.04	6.24	1.16	**10.44**
11-Dec-24	0.2	0.2	0.0	0.0	0.0	0.4	0.0	**0.71**	8.9	14.0	15.8	0.0	11.1	0.4	1.6	**51.89**	0.00	0.00	0.00	**0.00**	3.22	6.63	1.27	**11.12**
12-Dec-24	0.8	0.1	0.0	0.0	0.0	0.3	0.0	**1.19**	11.5	14.7	15.6	0.0	12.5	0.6	1.7	**56.71**	0.00	0.00	0.00	**0.00**	2.88	6.22	1.28	**10.38**
13-Dec-24	1.4	0.6	0.0	0.0	0.0	0.4	0.0	**2.39**	8.0	13.2	14.2	0.0	11.3	0.5	1.6	**48.85**	0.00	0.00	0.00	**0.00**	2.59	5.56	1.12	**9.26**
14-Dec-24	1.7	0.0	0.0	0.0	0.0	0.6	0.0	**2.33**	6.8	16.1	13.6	0.0	10.3	0.5	1.3	**48.54**	0.00	0.00	0.00	**0.00**	2.96	6.20	1.29	**10.44**
15-Dec-24	4.1	0.1	0.0	0.0	0.0	0.8	0.0	**5.01**	4.7	13.7	12.0	0.0	9.3	0.3	1.2	**41.22**	0.00	0.00	0.00	**0.00**	3.52	7.14	1.49	**12.15**
16-Dec-24	0.6	0.3	0.0	0.0	0.0	0.9	0.0	**1.69**	7.5	15.4	13.3	0.0	10.2	0.3	1.0	**47.67**	0.00	0.00	0.00	**0.00**	3.79	7.59	1.53	**12.91**
17-Dec-24	1.3	0.0	0.0	0.0	0.0	0.4	0.0	**1.66**	2.8	12.5	13.3	0.0	11.2	0.7	1.4	**42.01**	0.00	0.00	0.00	**0.00**	3.64	7.25	1.62	**12.52**
18-Dec-24	1.8	0.5	0.0	0.0	0.0	0.4	0.0	**2.73**	3.5	10.2	12.9	0.0	9.8	0.5	1.6	**38.46**	0.00	0.00	0.00	**0.00**	3.49	7.39	1.53	**12.41**
19-Dec-24	0.7	0.2	0.0	0.0	0.0	0.5	0.0	**1.44**	9.3	14.5	13.9	0.0	10.8	0.3	1.9	**50.69**	0.00	0.00	0.00	**0.00**	3.56	7.43	1.47	**12.47**
20-Dec-24	1.0	1.5	0.0	0.0	0.0	0.7	0.0	**3.21**	6.3	7.4	12.8	0.0	9.5	0.3	1.5	**37.72**	0.55	0.16	0.01	**0.73**	2.14	4.43	0.93	**7.50**
21-Dec-24	1.2	0.6	0.0	0.0	0.0	0.4	0.0	**2.23**	6.5	7.6	13.0	0.0	11.2	0.4	1.4	**40.03**	0.51	0.27	0.02	**0.80**	2.09	4.59	0.96	**7.64**
22-Dec-24	0.4	0.5	0.0	0.0	0.0	0.2	0.0	**1.15**	10.6	12.1	14.4	0.0	13.5	0.9	1.7	**53.29**	0.00	0.00	0.00	**0.00**	3.82	7.84	1.57	**13.22**
23-Dec-24	0.4	2.8	0.0	0.0	0.0	0.3	0.0	**3.54**	11.2	5.9	13.8	0.0	13.4	0.6	1.7	**46.67**	0.00	0.00	0.00	**0.00**	4.98	9.79	1.92	**16.69**
24-Dec-24	0.4	5.8	0.0	0.0	0.0	0.4	0.0	**6.64**	12.0	1.8	13.3	0.0	10.6	0.4	1.6	**39.70**	0.00	0.00	0.00	**0.00**	3.77	7.96	1.57	**13.30**
25-Dec-24	2.0	5.6	0.0	0.2	0.0	0.6	0.0	**8.33**	8.8	3.0	12.3	2.0	9.9	0.2	1.4	**37.57**	0.01	0.00	0.00	**0.01**	2.93	6.59	1.29	**10.81**
26-Dec-24	0.8	2.0	0.0	0.0	0.0	0.1	0.0	**2.88**	7.9	4.2	14.0	3.6	13.6	1.3	2.0	**46.55**	0.03	0.00	0.00	**0.03**	3.37	6.34	1.44	**11.15**
27-Dec-24	0.6	1.1	0.0	0.0	0.0	0.0	0.0	**1.73**	8.0	5.4	13.4	3.9	11.7	1.6	1.7	**45.76**	0.09	0.01	0.00	**0.10**	2.12	6.11	1.16	**9.39**
28-Dec-24	4.1	2.2	0.0	0.6	0.0	0.6	0.0	**7.52**	3.5	8.2	10.8	2.0	8.3	0.2	1.6	**34.68**	0.08	0.00	0.00	**0.08**	2.06	5.86	1.14	**9.07**
29-Dec-24	6.0	3.7	0.0	1.0	0.0	0.9	0.0	**11.72**	1.7	8.9	8.8	1.0	5.9	0.0	1.6	**27.91**	0.03	0.00	0.00	**0.03**	2.51	5.95	1.20	**9.66**
30-Dec-24	4.6	11.9	0.0	0.4	0.0	1.2	0.0	**18.08**	1.5	1.2	7.7	1.0	4.4	0.0	1.5	**17.36**	0.00	0.00	0.00	**0.00**	2.85	5.47	1.23	**9.55**
31-Dec-24	2.8	8.1	0.0	0.0	0.0	0.2	0.0	**11.15**	4.3	1.8	10.8	2.8	10.1	0.6	2.1	**32.48**	0.00	0.00	0.00	**0.00**	2.65	5.19	1.17	**9.01**
Total	**53.41**	**64.41**	**0.00**	**3.76**	**0.03**	**12.46**	**0.00**	**134.08**	**218.28**	**328.11**	**389.23**	**42.89**	**324.60**	**17.45**	**45.32**	**1365.88**	**18.80**	**19.99**	**2.57**	**41.35**	**87.66**	**183.94**	**38.42**	**310.02**

15.4 Import and Export of SR with ER & WR during December 2024

Date	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)								
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Dec-24	4.03	29.66	45.74	**79.43**	0.00	0.00	0.00	**0.00**	9.77	0.80	22.73	0.00	14.61	2.22	0.00	24.11	**74.23**	0.00	7.95	0.00	24.49	0.00	0.00	0.00	0.00	**32.44**
2-Dec-24	4.03	32.94	46.11	**83.07**	0.00	0.00	0.00	**0.00**	9.77	1.10	22.59	0.00	14.62	2.40	0.00	24.24	**74.71**	0.00	10.01	0.00	25.60	0.00	0.00	0.00	0.00	**35.61**
3-Dec-24	4.01	31.89	52.07	**87.97**	0.00	0.00	0.00	**0.00**	9.77	5.54	28.36	0.00	17.11	2.26	0.00	30.04	**93.08**	0.00	7.77	0.00	27.71	0.00	0.00	0.00	0.00	**35.48**
4-Dec-24	4.00	26.07	53.46	**83.53**	0.00	0.00	0.00	**0.00**	9.77	8.78	33.36	0.00	21.13	2.41	0.00	35.88	**111.35**	0.00	4.60	0.00	25.75	0.00	0.00	0.00	0.00	**30.35**
5-Dec-24	4.02	24.16	54.30	**82.48**	0.00	0.00	0.00	**0.00**	9.77	7.38	32.27	0.00	26.63	2.38	0.00	35.68	**114.12**	0.00	5.88	0.00	25.51	0.00	0.00	0.00	0.00	**31.39**
6-Dec-24	10.55	16.85	54.02	**81.42**	0.00	0.00	0.00	**0.00**	20.49	5.28	31.37	0.00	28.52	2.38	0.00	34.14	**122.19**	0.00	5.19	0.00	24.91	0.00	0.00	0.00	0.00	**30.10**
7-Dec-24	14.90	30.15	54.04	**99.09**	0.00	0.00	0.00	**0.00**	12.09	6.46	29.82	0.00	31.42	2.40	0.00	36.92	**119.11**	0.00	3.42	0.00	23.46	0.00	0.00	0.00	0.00	**26.88**
8-Dec-24	14.90	38.35	44.95	**98.21**	0.00	0.00	0.00	**0.00**	14.26	5.72	28.08	0.00	41.65	2.37	0.00	30.51	**122.59**	0.00	10.35	0.00	24.64	0.00	0.00	0.00	0.00	**34.99**
9-Dec-24	10.39	48.14	57.37	**115.90**	0.00	0.00	0.00	**0.00**	19.46	13.12	39.26	0.00	33.96	2.40	0.00	43.96	**152.16**	0.00	0.69	0.00	17.20	0.00	0.00	0.00	0.00	**17.89**
10-Dec-24	6.17	48.14	59.17	**113.48**	0.00	0.00	0.00	**0.00**	23.86	12.84	38.57	0.00	57.11	2.42	0.00	43.53	**178.34**	0.00	1.60	0.00	18.79	0.00	0.00	0.00	0.00	**20.39**
11-Dec-24	6.17	40.86	59.84	**106.87**	0.00	0.00	0.00	**0.00**	23.87	11.07	38.88	0.00	43.45	2.46	0.00	43.73	**163.47**	0.00	2.18	0.00	22.29	0.00	0.00	0.00	0.00	**24.46**
12-Dec-24	6.17	41.49	60.10	**107.76**	0.00	0.00	0.00	**0.00**	23.85	12.22	38.47	0.00	55.70	2.25	0.00	44.60	**177.11**	0.00	0.78	0.00	21.16	0.00	0.00	0.00	0.00	**21.95**
13-Dec-24	6.18	46.88	55.73	**108.78**	0.00	0.00	0.00	**0.00**	23.86	8.44	33.90	0.00	60.85	2.27	0.00	40.07	**169.39**	0.00	1.71	0.00	22.03	0.00	0.00	0.00	0.00	**23.74**
14-Dec-24	6.18	39.78	52.68	**98.64**	0.00	0.00	0.00	**0.00**	23.82	3.04	28.41	0.00	46.80	2.49	0.00	32.70	**137.27**	0.00	6.17	0.00	25.73	0.00	0.00	0.00	0.00	**31.89**
15-Dec-24	6.18	39.78	48.38	**94.34**	0.00	0.00	0.00	**0.00**	22.73	2.69	23.76	0.00	23.51	1.23	0.00	26.92	**100.83**	0.00	15.04	0.03	28.85	0.00	0.00	0.00	0.06	**43.96**
16-Dec-24	9.02	29.91	53.51	**92.43**	0.00	0.00	0.00	**0.00**	19.53	8.09	30.93	0.00	51.17	2.42	0.00	35.43	**147.57**	0.00	7.73	0.00	22.90	0.00	0.00	0.00	0.00	**30.64**
17-Dec-24	12.59	40.79	52.78	**106.16**	0.00	0.00	0.00	**0.00**	20.73	11.48	31.14	0.00	42.25	2.22	0.00	36.50	**144.32**	0.00	7.62	0.01	19.77	0.00	0.00	0.00	0.00	**27.40**
18-Dec-24	12.60	39.78	55.04	**107.41**	0.00	0.00	0.00	**0.00**	23.87	14.05	36.44	0.00	41.52	2.29	0.00	41.17	**159.34**	0.00	1.01	0.00	16.15	0.00	0.00	0.00	0.00	**17.15**
19-Dec-24	12.62	34.29	55.24	**102.16**	0.00	0.00	0.00	**0.00**	23.80	12.67	37.82	0.00	73.10	2.15	0.00	42.73	**192.27**	0.00	1.26	0.00	15.46	0.00	0.00	0.00	0.00	**16.72**
20-Dec-24	12.68	39.60	58.02	**110.30**	0.00	0.00	0.00	**0.00**	23.80	18.59	43.33	0.01	84.31	2.22	0.00	47.46	**219.72**	0.00	0.00	0.00	15.14	0.00	0.00	0.00	0.00	**15.14**
21-Dec-24	11.65	47.38	56.07	**115.09**	0.00	0.00	0.00	**0.00**	23.86	12.70	38.52	0.00	66.14	2.31	0.00	41.79	**185.32**	0.00	3.92	0.00	16.19	0.00	0.00	0.00	0.00	**20.12**
22-Dec-24	6.90	46.86	55.98	**109.75**	0.00	0.00	0.00	**0.00**	21.16	9.63	32.96	0.00	66.43	2.38	0.00	36.86	**169.42**	0.00	9.17	0.00	19.85	0.00	0.00	0.00	0.00	**29.03**
23-Dec-24	5.02	48.15	59.92	**113.09**	0.00	0.00	0.00	**0.00**	21.10	12.26	35.76	0.00	61.93	2.39	0.00	39.49	**172.93**	0.00	5.72	0.00	20.56	0.00	0.00	0.00	0.00	**26.28**
24-Dec-24	5.04	48.15	61.66	**114.86**	0.00	0.00	0.00	**0.00**	23.89	14.27	40.26	0.00	69.76	2.46	0.00	44.60	**195.24**	0.00	2.27	0.00	20.45	0.00	0.00	0.00	0.00	**22.72**
25-Dec-24	5.04	47.83	58.90	**111.78**	0.00	0.00	0.00	**0.00**	23.87	11.51	36.97	0.00	62.14	2.21	0.00	39.40	**176.10**	0.00	2.07	0.00	21.33	0.00	0.00	0.00	0.00	**23.40**
26-Dec-24	5.00	39.77	56.75	**101.52**	0.00	0.00	0.00	**0.00**	23.89	9.18	34.12	0.00	49.80	2.01	0.00	38.41	**157.41**	0.00	1.75	0.00	24.10	0.00	0.00	0.00	0.00	**25.85**
27-Dec-24	5.00	46.53	55.57	**107.10**	0.00	0.00	0.00	**0.00**	23.86	5.50	34.33	0.00	63.18	1.26	0.00	36.77	**164.90**	0.00	6.10	0.00	27.11	0.00	0.00	0.00	0.00	**33.21**
28-Dec-24	5.00	42.85	54.03	**101.89**	0.00	0.00	0.00	**0.00**	13.82	7.27	38.40	0.00	55.69	2.52	0.00	37.85	**155.56**	0.00	4.15	0.00	26.66	0.00	0.00	0.00	0.00	**30.80**
29-Dec-24	5.05	35.96	52.76	**93.76**	0.00	0.00	0.00	**0.00**	12.18	9.66	38.38	0.00	42.37	2.42	0.00	36.84	**141.86**	0.00	6.74	0.00	26.96	0.00	0.00	0.00	0.00	**33.71**
30-Dec-24	5.10	44.38	51.81	**101.29**	0.00	0.00	0.00	**0.00**	21.61	9.20	37.83	0.00	27.34	2.44	0.00	37.53	**135.95**	0.00	5.80	0.00	27.68	0.00	0.00	0.00	0.00	**33.48**
31-Dec-24	5.11	30.16	57.06	**92.32**	0.00	0.00	0.00	**0.00**	24.01	9.71	40.45	0.00	22.61	2.42	0.00	40.55	**139.75**	0.00	3.63	0.00	25.72	0.00	0.00	0.00	0.00	**29.34**
TOTAL	**231.29**	**1197.54**	**1693.06**	**3121.89**	**0.00**	**0.00**	**0.00**	**0.00**	**602.14**	**280.25**	**1057.49**	**0.01**	**1396.79**	**70.47**	**0.06**	**1160.41**	**4567.60**	**0.00**	**152.27**	**0.04**	**704.16**	**0.00**	**0.00**	**0.01**	**0.06**	**856.54**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 **से मार्च** 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
अक्तूबर 2024 OCT'24	0.00	918.96	0.00	283.29	695.63	0.00	0.80	0.00
नवंबर 2024 NOV'24	12.24	125.37	0.00	212.20	698.58	0.00	0.71	0.00
दिसम्बर 2024 DEC'24	187.39	0.00	70.80	11.26	521.28	0.00	0.72	0.00
कुल Total	337.47	5325.83	709.22	2141.11	6076.02	0.00	7.13	0.00

* Based on daily operational data

16.1 Import from neighbouring countries during Dec 2024

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Dec-24	5.68	0.00	0.00	0.00	1.65	4.95	0.74	0.29	0.00	0.00	1.52	8.94	0.11	0.00
2-Dec-24	5.23	0.00	0.00	0.00	1.55	4.67	0.64	0.29	0.00	0.00	1.53	9.22	0.00	0.00
3-Dec-24	5.08	0.27	0.00	0.00	1.41	4.24	0.63	0.27	0.00	0.00	1.56	9.62	0.00	0.00
4-Dec-24	8.14	0.00	0.00	0.00	1.25	3.78	0.62	0.32	0.00	0.00	1.55	9.58	0.00	0.00
5-Dec-24	11.40	0.00	0.00	0.00	1.10	3.33	0.68	0.31	0.00	0.00	1.50	10.11	0.00	0.00
6-Dec-24	10.73	0.00	0.00	0.00	1.12	3.37	0.66	0.31	0.00	0.00	1.49	10.10	0.00	0.00
7-Dec-24	10.51	0.00	0.00	0.00	0.97	2.94	0.63	0.29	0.00	0.00	1.50	10.51	0.00	0.00
8-Dec-24	10.55	0.00	0.00	0.00	0.88	2.65	0.64	0.25	0.00	0.00	1.45	10.64	0.00	0.00
9-Dec-24	9.60	0.00	0.00	0.00	0.68	2.57	0.61	0.28	0.00	0.00	1.52	10.54	0.00	0.00
10-Dec-24	10.23	0.00	0.00	0.00	1.03	3.13	0.57	0.26	0.00	0.00	1.47	9.27	0.00	0.00
11-Dec-24	9.74	0.00	0.00	0.00	0.37	2.41	0.55	0.17	0.00	0.00	1.36	8.42	0.00	0.00
12-Dec-24	9.81	0.00	0.00	0.00	0.00	3.53	0.48	0.12	0.00	0.00	1.41	7.67	0.00	0.00
13-Dec-24	9.61	0.00	0.00	0.00	0.00	2.54	0.49	0.10	0.00	0.00	1.32	6.61	0.00	0.00
14-Dec-24	9.21	0.00	0.00	0.00	0.00	2.73	0.53	0.61	0.00	0.00	1.44	6.34	0.00	0.00
15-Dec-24	8.87	0.00	0.00	0.00	0.00	2.60	0.56	0.15	0.00	0.00	1.35	5.60	0.00	0.00
16-Dec-24	9.42	0.00	0.00	0.00	0.00	2.63	0.47	0.16	0.00	0.00	1.37	5.96	0.00	0.00
17-Dec-24	9.11	0.00	0.00	0.00	0.00	2.31	0.41	0.10	0.00	0.00	1.33	5.20	0.00	0.00
18-Dec-24	8.25	0.00	0.00	0.00	0.64	2.19	0.46	0.19	0.00	0.00	1.13	4.72	0.00	0.00
19-Dec-24	8.48	0.00	0.00	0.00	1.10	1.68	0.31	0.20	0.00	0.00	0.90	3.31	0.00	0.00
20-Dec-24	8.46	0.00	0.00	0.00	0.85	1.30	0.34	0.14	0.00	0.00	0.78	3.17	0.00	0.00
21-Dec-24	8.77	0.00	0.00	0.00	0.76	1.19	0.34	0.11	0.00	0.00	0.66	2.74	0.00	0.00
22-Dec-24	8.36	0.00	0.00	0.00	0.58	0.93	0.30	0.10	0.00	0.00	0.70	2.83	0.00	0.00
23-Dec-24	8.03	0.00	0.00	0.00	0.61	0.96	0.21	0.08	0.00	0.00	0.69	4.80	0.00	0.00
24-Dec-24	7.98	0.00	0.00	0.00	0.53	0.85	0.34	0.04	0.00	0.00	0.61	2.89	0.00	0.00
25-Dec-24	8.01	0.00	0.00	0.00	0.40	0.64	0.14	0.01	0.00	0.00	0.59	2.63	0.00	0.00
26-Dec-24	7.21	0.00	0.00	0.00	0.59	0.93	0.24	0.04	0.00	0.00	0.24	2.13	0.00	0.00
27-Dec-24	7.74	0.00	0.00	0.00	0.47	0.77	0.14	0.03	0.00	0.00	0.18	1.86	0.00	0.00
28-Dec-24	7.80	0.00	0.00	0.00	0.37	0.92	0.00	0.08	0.00	0.00	0.00	1.56	0.00	0.00
29-Dec-24	7.75	0.00	0.00	0.00	0.36	0.57	0.05	0.00	0.00	0.00	0.00	1.91	0.00	0.00
30-Dec-24	6.90	0.00	0.00	0.00	0.31	0.55	0.06	0.02	0.00	0.00	0.00	2.32	0.00	0.00
31-Dec-24														
Total	**256.69**	**0.27**	**0.00**	**0.00**	**19.58**	**67.85**	**12.84**	**5.32**	**0.00**	**0.00**	**31.16**	**181.17**	**0.11**	**0.00**

16.2 Export to neighbouring countries during Dec 2024

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Dec-24	0.00	0.00	0.79	0.45	0.00	0.00	0.00	0.00	22.04	1.58	0.00	0.00	0.00	0.03
2-Dec-24	0.00	0.00	0.82	0.36	0.00	0.00	0.00	0.00	22.00	1.50	0.00	0.00	0.00	0.02
3-Dec-24	0.00	0.00	0.91	0.36	0.00	0.00	0.00	0.00	22.02	1.62	0.00	0.00	0.00	0.03
4-Dec-24	0.00	2.55	1.06	1.29	0.00	0.00	0.00	0.00	21.56	1.59	0.00	0.00	0.00	0.03
5-Dec-24	0.00	5.07	1.27	1.95	0.00	0.00	0.00	0.00	21.97	1.57	0.00	0.00	0.00	0.03
6-Dec-24	0.00	4.56	1.13	1.43	0.00	0.00	0.00	0.00	21.93	1.29	0.00	0.00	0.00	0.03
7-Dec-24	0.00	4.57	1.12	1.27	0.00	0.00	0.00	0.00	21.91	1.31	0.00	0.00	0.00	0.02
8-Dec-24	0.00	5.24	0.95	0.96	0.00	0.00	0.00	0.00	21.85	1.22	0.00	0.00	0.00	0.02
9-Dec-24	0.00	4.70	1.70	1.11	0.00	0.00	0.00	0.00	21.82	1.29	0.00	0.00	0.00	0.02
10-Dec-24	0.00	4.53	1.73	1.17	0.00	0.00	0.00	0.00	21.67	1.36	0.00	0.00	0.00	0.02
11-Dec-24	0.00	5.13	2.16	1.78	0.00	0.00	0.00	0.00	22.05	1.50	0.00	0.00	0.00	0.02
12-Dec-24	0.00	5.14	2.12	1.84	0.00	0.00	0.00	0.00	22.09	1.54	0.00	0.00	0.00	0.02
13-Dec-24	0.00	5.19	2.24	1.79	0.00	0.00	0.00	0.00	22.11	1.31	0.00	0.00	0.00	0.02
14-Dec-24	0.00	5.44	2.25	1.72	0.00	0.00	0.00	0.00	22.31	1.39	0.00	0.00	0.00	0.03
15-Dec-24	0.00	5.46	2.32	1.73	0.00	0.00	0.00	0.00	22.57	1.19	0.00	0.00	0.00	0.02
16-Dec-24	0.00	5.37	2.39	1.84	0.00	0.00	0.00	0.00	22.15	1.28	0.00	0.00	0.00	0.02
17-Dec-24	0.00	5.23	2.53	1.87	0.00	0.00	0.00	0.00	22.23	1.27	0.00	0.00	0.00	0.02
18-Dec-24	0.00	5.70	3.14	2.03	0.00	0.00	0.00	0.00	22.04	1.21	0.00	0.00	0.00	0.02
19-Dec-24	0.00	5.80	3.08	2.06	0.00	0.00	0.00	0.00	21.87	1.20	0.00	0.00	0.00	0.02
20-Dec-24	0.00	5.69	2.33	2.19	0.00	0.00	0.00	0.00	22.15	1.08	0.00	0.00	0.00	0.03
21-Dec-24	0.00	5.62	2.38	2.12	0.00	0.00	0.00	0.00	22.14	1.07	0.00	0.00	0.00	0.02
22-Dec-24	0.00	5.67	2.69	1.95	0.00	0.00	0.00	0.00	22.11	0.99	0.00	0.00	0.00	0.03
23-Dec-24	0.00	5.70	2.70	1.89	0.00	0.00	0.00	0.00	22.11	0.93	0.00	0.00	0.00	0.03
24-Dec-24	0.00	5.63	2.92	1.99	0.00	0.00	0.00	0.00	22.15	0.96	0.00	0.00	0.00	0.02
25-Dec-24	0.00	5.60	2.87	1.97	0.00	0.00	0.00	0.00	22.13	1.14	0.00	0.00	0.02	0.02
26-Dec-24	0.00	5.62	2.82	1.86	0.00	0.00	0.00	0.00	22.05	1.36	0.00	0.00	0.02	0.02
27-Dec-24	0.00	5.90	3.06	1.91	0.00	0.00	0.00	0.00	22.02	1.32	0.00	0.00	0.02	0.02
28-Dec-24	0.00	5.73	2.94	1.94	0.00	0.00	0.06	0.00	22.14	1.19	0.03	0.00	0.02	0.02
29-Dec-24	0.00	5.96	3.11	1.93	0.00	0.00	0.00	0.12	20.23	1.23	0.00	0.00	0.02	0.01
30-Dec-24	0.00	5.87	3.04	1.84	0.00	0.00	0.00	0.00	20.17	1.19	0.08	0.00	0.02	0.02
31-Dec-24														
Total	**0.00**	**142.68**	**64.55**	**48.59**	**0.00**	**0.00**	**0.06**	**0.12**	**657.62**	**38.67**	**0.11**	**0.00**	**0.13**	**0.71**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – दिसंबर 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - DECEMBER 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

दिसंबर 2024 DECEMBER 2024			Apr'24- Dec'24	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	488	546	5744	24961
प.क्षे. WR	459	359	3462	4689
द.क्षे. SR	458	375	3243	8927
पू.क्षे. ER	262	151	3057	11946
पूर्वोत्तर क्षे. NER	106	38	716	514
कुल TOTAL	1773	1468	16222	51037

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
अक्तूबर 2024 Oct'24	12567	8372	1511	2332
नवंबर 2024 Nov'24	11553	9432	1217	963
दिसम्बर 2024 Dec'24	12448	10602	1773	1468
कुल TOTAL	92863	80178	16222	51037

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
02.12.24 to 08.12.24	64.62	223.24	29.57	194.27	7.28
09.12.24 to 15.12.24	78.42	230.79	36.60	210.34	1.95
16.12.24 to 22.12.24	98.88	339.07	82.30	309.08	3.61
23.12.24 to 29.12.24	161.34	302.96	36.50	271.62	NA

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- दिसंबर 2024 EXCHANGES THROUGH POWER EXCHANGES-DECEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	ACME PHALODI SOLAR ENERGY PRIVATE LIMITED_INFIRM	उत्तरी क्षेत्र NR	19.89	0.00
2	ACME RAISAR SOLAR ENERGY PRIVATE LIMITED_INFIRM		13.03	0.00
3	AD HYDRO POWER LIMITED		15.21	0.00
4	ADANI GREEN ENERGY TWENTY FIVE LIMITED		24.74	0.00
5	ADANI GREEN ENERGY TWENTY FIVE LIMITED_infirm		19.25	0.00
6	ADANI GREEN ENERGY TWENTY FOUR LIMITED_infirm		11.12	0.00
7	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		23.48	0.00
8	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		8.61	0.00
9	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		34.77	0.00
10	AMP Energy Green Four Private Limited_Infirm		0.61	0.00
11	Adept Renewable Technologies Private Limited		15.99	0.00
12	Amp Energy Green Six Private Limited		15.05	0.00
13	Amplus Ages Private Limited		0.88	0.00
14	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		1.08	0.00
15	Chandigarh (UT)		26.10	4.80
16	Delhi		90.72	275.36
17	Government of Himachal Pradesh _ Chamera1HEP		5.15	0.07
18	Government of Himachal Pradesh _ Chamera3HEP		3.19	0.12
19	Government of Himachal Pradesh_ CHAMERA2HEP		4.16	0.42
20	Government of Himachal Pradesh_BairasuilHEP		1.30	0.05
21	Government of Himachal Pradesh_Koldam HEP		11.67	0.55
22	Government of Himachal Pradesh_NJHPS		27.33	0.70
23	Government of Himachal Pradesh_Parbati3HEP		2.17	0.40
24	Government of Himachal Pradesh_RampurHEP		8.13	0.21
25	Grian Energy Private Limited		1.68	0.00
26	Haryana		375.99	83.03
27	Himachal Pradesh		43.72	101.17
28	IGSTPS JHAJJAR		14.18	0.00
29	JUNIPER GREEN COSMIC PRIVATE LIMITED		15.99	0.00
30	Jammu Kashmir		35.15	341.33
31	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		19.29	0.00
32	KHURJA STPP		41.33	0.00
33	NEA Nepal Upper Chameliya Hydropower Project		0.09	0.00
34	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	13.14
35	NTPC Dadri Stage I		19.43	0.00
36	NTPC Dadri Stage II		12.51	0.00
37	NTPC Rihand stage I		12.43	0.00
38	NTPC Rihand stage II		12.37	0.00
39	NTPC Rihand stage III		16.59	0.00
40	NTPC Singrauli		21.56	0.00
41	NTPC Tanda Stage II		3.51	0.00
42	NTPC Unchahar Stage I		2.98	0.00
43	NTPC Unchahar Stage II		1.92	0.00
44	NTPC Unchahar Stage III		1.70	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- दिसंबर 2024
EXCHANGES THROUGH POWER EXCHANGES-DECEMBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	NTPC Unchahar Stage IV		4.58	0.00
46	North Central Railway Prayagraj		0.00	10.36
47	Onevolt Energy Private Limited		2.62	0.00
48	Punjab		8.95	631.40
49	RENEW SURYA PRATAP PRIVATE LIMITED		34.50	0.00
50	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.29	0.00
51	Rajasthan		100.54	408.09
52	ReNew Surya Ravi Private Limited		34.79	0.00
53	SHREE CEMENT LIMITED TPS		7.69	0.00
54	Sainj HEP		4.81	0.04
55	Serentica Renewables India 4 Private Limited		1.09	0.00
56	Serentica Renewables India 5 Private Limited		8.47	0.00
57	Serentica Renewables India 5 Private Limited- Infirm		0.41	0.00
58	Singoli Bhatwari HEP		12.76	0.00
59	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		9.01	0.00
60	TPSL 200MW TPTCL Banderwala		9.36	0.00
61	TPSL Banderwala SECI 100_INF		3.47	0.00
62	Transition Energy Services Private Limited		7.82	0.00
63	Transition Green Energy Private Limited		1.14	0.00
64	Transition Sustainable Energy Services One Private Limited		6.90	0.00
65	Uttar Pradesh		858.39	469.04
66	Uttarakhand		34.30	137.01
67	ACB (INDIA) LIMITED		44.23	0.00
68	ADANI GREEN ENERGY TWENTY SIX A LIMITED_PSS-3		0.28	0.00
69	ADANI GREEN ENERGY TWENTY SIX A LIMITED_infirm		0.75	0.00
70	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS-3 (162.5 MW Hybrid Solar of 187.5MW HPD)		20.12	0.00
71	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.27	0.00
72	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		0.38	0.00
73	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3_infirm (162.5 MW Hybrid Solar of 187.5MW HPD)		9.32	0.00
74	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3_infirm (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.15	0.00
75	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3_infirm (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		0.72	0.00
76	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS-3		47.20	0.00
77	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_infirm		19.74	0.00
78	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		67.64	0.00
79	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED_PSS-1		86.88	0.00
80	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		90.29	0.00
81	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		1.96	0.00
82	AMBUJA CEMENTS LIMITED(Khavda PSS-3)_infirm		5.00	0.00
83	AMBUJA CEMENTS LIMITED_PSS3		3.99	0.00
84	Adani Green Energy Twenty Five A Limited_Infirm		15.51	0.00
85	Adani Green Energy Twenty Five A Limited_PSS-2		24.21	0.00
86	Adani Green Energy Twenty Five B Limited_PSS-2		47.60	0.00
87	Adani Green Energy Twenty Five B Limited_infirm		32.18	0.00
88	Adani Green Energy Twenty Four A Limited_PSS-3		2.14	0.00
89	Adani Green Energy Twenty Four A Limited_infirm		8.70	0.00
90	Adani Green Energy Twenty Six B Limited_PSS-2		9.37	0.00
91	Adani Green Energy Twenty Six B Limited_infirm		6.22	0.00
92	Adani Power Limited - Raigarh TPP		229.48	15.60
93	Adani Power Limited-Raipur TPP		432.32	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- दिसंबर 2024
EXCHANGES THROUGH POWER EXCHANGES-DECEMBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
94	Adani Renewable Energy Forty Eight Limited (Wind)_PSS-9	पश्चिमी क्षेत्र WR	1.80	0.00
95	Adani Renewable Energy Forty Eight Limited(Wind)_infirm		7.79	0.00
96	ArcelorMittal Nippon Steel India Limited		0.00	228.75
97	BHARAT ALUMINIUM COMPANY LTD		68.42	0.00
98	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		5.95	0.00
99	Chhattisgarh		704.67	11.71
100	D B Power Limited		25.50	0.00
101	DHARIWAL STU OTH		0.35	0.00
102	Daman and Diu - Dadra and Nagar Haveli		0.36	74.23
103	Dhariwal ISTS		2.48	0.00
104	GMR Warora Energy Limited		7.13	0.00
105	Goa WR		25.77	5.01
106	Gujarat		39.30	1036.01
107	Jaypee Nigrie Super Thermal Power Plant		181.80	0.00
108	Jhabua Power Limited		59.23	0.00
109	Jindal Power Limited, Stage-1		246.10	1.35
110	Jindal Power Limited, Stage-2		578.26	8.66
111	Jindal Steel & Power Ltd , DCPP		99.26	0.00
112	KSK MAHANADI POWER COMPANY LIMITED		0.02	0.00
113	LANCO AMARKANTAK POWER LIMITED		1.13	0.00
114	MAHAN ENERGEN LIMITED U#1		142.51	5.58
115	MAHAN ENERGEN LIMITED U#2		55.01	0.00
116	MB POWER (MADHYA PRADESH) LIMITED		5.82	8.37
117	Madhya Pradesh		318.19	277.90
118	Maharashtra		88.19	1066.57
119	Maruti Clean Coal and Power Limited		3.98	0.13
120	NREL-Dayapar Wind		6.28	0.00
121	NTPC Gadarwara		9.43	0.00
122	NTPC Jhanor Gandhar GPS		0.00	0.54
123	NTPC Kawas GPS		0.00	0.66
124	NTPC Korba Stage I &II		17.70	0.00
125	NTPC Korba Stage III		6.12	0.00
126	NTPC Lara Stage I		10.23	0.00
127	NTPC Mouda Stage I		6.42	0.00
128	NTPC Mouda Stage II		10.61	0.00
129	NTPC SAIL POWER COMPANY LIMITED		0.91	0.00
130	NTPC SOLAPUR SOLAR PV Station		1.09	0.00
131	NTPC Sipat Stage I		11.35	0.00
132	NTPC Sipat Stage II		4.67	0.00
133	NTPC Solapur		7.65	0.00
134	NTPC Vindhyachal Stage I		14.08	0.00
135	NTPC Vindhyachal Stage II		7.00	0.00
136	NTPC Vindhyachal Stage III		12.08	0.00
137	NTPC Vindhyachal Stage IV		12.09	0.00
138	NTPC Vindhyachal Stage V		5.34	0.00
139	NTPC khargone		12.82	0.00
140	R.K.M POWERGEN PRIVATE LIMITED		18.29	0.00
141	Ratnagiri Gas & Power Private Limited		0.00	2.17
142	SKS Power Generation Chhattisgarh Limited		13.42	23.78

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- दिसंबर 2024 EXCHANGES THROUGH POWER EXCHANGES-DECEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
143	Sasan Power Limited		17.87	0.00
144	TRN ENERGY PRIVATE LIMITED		34.51	0.00
145	The Tata Power Co Ltd (MTPS)		18.29	0.00
146	WIND FIVE RENERGY LIMITED		5.65	0.00
147	Andhra Pradesh		47.49	524.09
148	COASTAL ENERGEN PRIVATE LIMITED		24.87	1.60
149	Goa SR		0.02	5.41
150	IL&FS TAMIL NADU POWER COMPANY LIMITED		1.76	0.00
151	JINDAL POWER LIMITED SIMHAPURI		13.07	4.46
152	Karnataka		433.54	200.43
153	Kerala		16.76	239.38
154	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		6.62	0.00
155	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		1.56	0.00
156	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.86	0.00
157	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		0.90	0.00
158	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		1.03	0.00
159	NLC Tamilnadu Power Limited		2.26	0.00
160	NTECL VALLUR		4.10	0.00
161	NTPC KUDGI		4.79	0.00
162	NTPC Ramagundam Stage I &II		4.14	0.00
163	NTPC Ramagundam Stage III		0.73	0.00
164	NTPC Simhadri Stage I	दक्षिणी क्षेत्र SR	0.05	0.00
165	NTPC Simhadri Stage II		2.01	0.00
166	NTPC Talcher Super Thermal Power Station Stage II		0.00	0.00
167	NTPC Telangana		5.40	0.00
168	OSTRO KANNADA POWER PRIVATE LIMITED		8.78	0.00
169	Pondicherry UT		18.21	0.69
170	RENEW SURYA OJAS PRIVATE LIMITED-Wind		14.30	0.00
171	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		1.01	0.00
172	Ramagundam Floating solar		2.66	0.00
173	SEIL ENERGY INDIA LIMITED		106.93	0.00
174	SEIL Energy India Limited Project II		25.79	0.00
175	SEMBCORP GREEN INFRA PRIVATE LIMITED (INFIRM)		3.33	0.00
176	Serentica Renewables India 1 Private Limited		0.32	0.00
177	Serentica Renewables India 1 Private Limited- Koppal (Infirm)		0.84	0.00
178	Simhadri FSP 15 MW		1.34	0.00
179	Simhadri Floating solar (10 MW)		0.82	0.00
180	Tamil Nadu		279.90	534.65
181	Telangana		22.45	2885.30
182	ADHUNIK POWER & NATURAL RESOURCES LIMITED		1.19	0.00
183	Bihar		943.46	1.40
184	Chuzachen HEP		0.04	0.00
185	Damodar Valley Corporation		57.53	206.28
186	Dikchu Hydro Electric Project (Sneha Kinetic Power Projects Pvt. Ltd.)		9.55	0.00
187	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	222.84
188	GMR KAMALANGA ENERGY LTD-CTU		1.75	0.00
189	IND BARATH ENERGY UTKAL LIMITED		92.88	2.42
190	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.05	0.00
191	Jharkhand		104.86	50.11

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- दिसंबर 2024 EXCHANGES THROUGH POWER EXCHANGES-DECEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
192	Jindal India Power Limited	पूर्वी क्षेत्र ER	111.97	0.00
193	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		8.53	0.00
194	KANTI BIJLEE UTPADAN NIGAM LIMITED		6.00	0.00
195	MAITHON POWER LIMITED		2.18	0.00
196	MARSYANGDI NEPAL ELECTRICITY AUTHORITY		0.04	0.00
197	NABINAGAR POWER GENERATING COMPANY LIMITED		70.07	0.00
198	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	59.57
199	NEPAL ELECTRICITY AUTHORITY-MIDDLE MARSYANGDI		0.60	0.00
200	NTPC BARH Stage I		24.21	0.00
201	NTPC BARH Stage II		36.56	0.00
202	NTPC Darlipali		11.69	0.00
203	NTPC Farakka stage I		38.62	0.00
204	NTPC Farakka stage III		10.56	0.00
205	NTPC Kahalgaon stage I		8.82	0.00
206	NTPC Kahalgaon stage II		13.91	0.00
207	NTPC North Karanpura STPS		17.01	0.00
208	NTPC Talcher Stage I		6.70	0.00
209	NTPP BRBCL		15.42	0.00
210	Odisha		723.12	196.72
211	Sikkim		9.26	1.76
212	Tashiding HEP, Shiga Energy Private Limited		0.04	0.00
213	West Bengal		570.70	71.63
214	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	11.59	0.00
215	ASSAM GAS BASED POWER STATION		1.83	0.00
216	AGARTALA GAS BASED POWER STATION		11.59	0.00
217	ASSAM GAS BASED POWER STATION		1.83	0.00
218	Arunachal Pradesh		3.89	8.94
219	Assam		229.21	45.01
220	Bongaigaon Thermal Power Station NTPC		2.82	0.00
221	KAMENG HYDRO POWER STATION		10.74	0.00
222	Manipur		3.25	14.56
223	Meghalaya		8.96	69.67
224	Mizoram		1.84	0.22
225	Nagaland		4.20	6.79
226	Palatana Plant		19.23	0.00
227	Tripura		20.29	3.03
	Total		10615	10601

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : DECEMBER 2024

RE Source & Unit wise break up (01.12.2024-31.12.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	68	5	22	2
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1001	2	181	2
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1069**	**7**	**203**	**4**

RECs Issued (01.12.2024-31.12.2024)

Sr.No.	Non Solar	Solar	Total
1	1391271	97848	1489119

Redemption of REC (01.12.2024-31.12.2024)

Sr.No.	Non Solar	Solar	Total
1	2352500	23903	2376403

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : DECEMBER 2024

RE Source & Unit wise break up (Apr'24-Dec'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	111	11	42	7
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	1281	23	264	18
5	Small Hydro	24	1	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1416**	**35**	**342**	**27**

RECs Issued (Apr'24-Dec'24)

Sr.No.	Non Solar	Solar	Total
1	34262911	862476	35125387

Redemption of REC (Apr'24-Dec'24)

Sr.No.	Non Solar	Solar	Total
1	18180432	255687	18436119

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : DECEMBER 2024

RE Source & Unit wise break up Since Inception to Dec'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3159	535	2996	538
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	2910	595	1744	500
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**8179**	**1304**	**6397**	**1175**

RECs Issued since Inception to Dec'24

Sr.No.	Non Solar	Solar	Total
1	149367949	14402854	163770803

Redemption of REC since Inception to Dec'24

Sr.No.	Non Solar	Solar	Total
1	96684761	12704944	109389705

REC Closing balance as on 31.12.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of Dec 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	Uttarakhand	02-12-2024 10:09	02-12-2024 10:49	00:40	0	72	0.000	0.118	49023	60826	i)As reported, at 10:09 hrs, B-N fault occurred in 132KV Haldwani – Bazpur Ckt-1 with fault distance of 7.8km from Haldwani end. As per DR, fault current was approx. 5.72 kA from Haldwani end and the fault clearing time was approx. 210msec (exact reason of fault yet to be shared). ii)Due to delay in fault clearance, directional overcurrent protection of 220/132 KV 100 MVA ICT-1 and 2 at Haldwani(UK) operated tripping both ICT-1 & 2. iii)As per PMU, B-N phase to earth fault with delayed fault clearing time of 240ms was observed in the system. iv)As per SCADA, change in demand of approx. 176 MW in Uttarakhand control area was observed. But, as reported, load loss of approx. 72MW occurred at Uttarakhand.	i)220KV/132KV 100 MVA ICT-1 at Haldwani(UK) ii)220KV/132KV 100 MVA ICT-2 at Haldwani(UK) iii)132KV Haldwani-Bazpur(UK) ckt-1
2	GI-1	Uttarakhand	05-12-2024 20:02	05-12-2024 21:04	01:02	223	83	0.614	0.165	36316	50444	i)During antecedent condition, three 30MW units of Khodri (Unit 1,2 & 4) and three 60 MW units of Chhibro (Unit 2,3 & 4) were running and total active power generation of Khodri and Chhibro was approx. 75 MW and 123 MW (as per SCADA). ii)As reported, at 20:02 hrs, while stopping of 30MW Khodri Unit-2, its 220kV CB malfunctioned and pole discrepancy operated. This led to LBB protection operation resulting in tripping of 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 and 220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt, 220 KV Khodri-Chhibro (UK) Ckt-1 and 30MW Khodri Unit-2. iii)As per SCADA, two 60 MW units of Chhibro Unit 2 & 3 also tripped at the same time which caused generation loss of 103 MW (exact reason yet to be shared). iv)As per PMU, no fault was observed in the system. v)As per SCADA, change in demand and generation of approx. 83 MW and 223 MW respectively in Uttarakhand control area were observed. vi)As remedial action taken, over hauling & testing of generator CB has been performed and found satisfactory.	i)220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 ii)220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt-1 iii)220 KV Khodri - Chhibro (UK) Ckt-1 iv)30 MW Khodri - UNIT 2 v)60MW Chhibro – UNIT 2 vi)60MW Chhibro – UNIT 3
3	GI-1	Uttarakhand	06-12-2024 21:01	06-12-2024 22:36	01:35	21	74	0.063	0.156	33496	47323	i)During antecedent condition, only one 30MW unit of Khodri (Unit 2) and one 60 MW unit of Chhibro (Unit 4) were running and total active power generation of Khodri and Chhibro was approx. 21 MW and 49 MW (as per SCADA). ii)As reported, at 21:01 hrs, while stopping of 30MW Khodri Unit-2, its 220kV CB malfunctioned and pole discrepancy operated. This led to LBB protection operation resulting in tripping of 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 and 220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt, 220 KV Khodri-Chhibro (UK) Ckt-1 and 30MW Khodri Unit-2 . iii)As per SCADA, change in demand and generation of approx. 74 MW and 21 MW respectively in Uttarakhand control area were observed. iv)As reported by SLDC-UK, testing of Generator CB of Unit -2 by expert service engineer is under progress.	i)220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 ii)220 KV Khodri-Chhibro (UK) Ckt-1 iii)220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt iv)30 MW Khodri - UNIT 2
4	GI-2	Rajasthan	11-12-2024 12:13	11-12-2024 13:20	01:07	835	0	1.540	0.000	54210	61487	i)400/220kV Jaisalmer(RS) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii)During antecedent condition, Renew Solar, Fortum Solar, ACME Aklera and Clean solar was injecting approx. 109 MW, 236 MW, 267 MW and 245 MW respectively to Jaisalmer(RS) at 220kV level. Active power was going out to Akal(RS) through 220kV Jaisalmer(RS)-Akal Ckt-1 & 2 carrying approx. 253 MW each. 400/220 kV 500 MVA ICT 1 & 3 at Jaisalmer(RS) were carrying approx. 261 MW and 248 MW respectively from 220kV level to 400kV level. iii)As reported, at 12:13 hrs, 400/220 kV 500 MVA ICT 1 & 3 tripped along with 220KV lines of Renew Solar, Fortum Solar, ACME Aklera and Clean solar connected from 220KV Jaisalmer(Exact reason for tripping needs to be shared). iv)As per PMU at Fatehgarh3(PG), no fault is observed. v)During this event, as per SCADA, solar generation loss of approx. 835 MW is observed in Rajasthan control area. vi)As per SCADA, no change in demand is observed in Rajasthan control area.	i)400/220 kV 500 MVA ICT 1 at Jaisalmer(RS) ii)400/220 kV 500 MVA ICT 3 at Jaisalmer(RS) iii)400 KV Jaisalmer-Barmer (RS) Ckt-2 iv)220kV Jaisalmer(RS)-Renew Solar Ckt v)220kV Jaisalmer(RS)-Fortum Solar Ckt vi)220kV Jaisalmer(RS)-Akal Ckt-1 vii)220kV Jaisalmer(RS)-Akal Ckt-2
5	GD-1	Rajasthan	12-12-2024 12:25	13-12-2024 03:35	15:10	1860	0	3.444	0.000	54001	60300	i)Generation of 220kV Azure 41(IP) station evacuates through 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt. During antecedent condition, Azure 41(IP) station was generating approx. 294 MW (as per PMU). ii)As reported, at 12:25hrs, 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt tripped on B-N phase to earth fault due to differential protection operation (exact reason and location of fault yet to be shared). iii)Due to tripping of 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt, Azure 41(IP) S/s lost its connectivity from grid and blackout occurred at 220kV Azure 41(IP) S/s. iv)As per PMU at Bhadla(PG), B-N phase to earth fault (voltage dipped upto 0.716 p.u.) followed by Y-N phase to earth fault (voltage dipped upto 0.678 p.u.) is observed with fault clearing time of 80ms. After the fault clearance voltage increased upto 1.076 p.u. v)As per PMU at Bassi(PG), a sharp drop in frequency is observed from 49.995 Hz to 49.750 Hz and frequency recovered to 49.988 Hz within 1 min. vi)As per PMU, solar generation loss of approx. 294 MW, 150 MW, 68 MW, 89 MW and 167 MW are observed respectively at Azure 41(IP), Avaada Pooling(IP), ABCRL(IP), ESURL(IP) and ASEPL(IP). vii)As per SCADA, dip in NR total solar generation of approx. 1860 MW is observed with change in Rajasthan solar generation of approx. 170 MW.	i)220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt
6	GI-2	Uttar Pradesh	12-12-2024 12:02	12-12-2024 14:15	02:13	0	140	0.000	0.228	54946	61451	i)During antecedent condition, 400/220 kV 500 MVA ICT 1 and ICT 2 at Basti was carrying approx. 97 MW each. 400KV Gorakhpur (PG)-Basti(UP) (PG) Ckt-2 and 400 KV LUCKNOW_1(PG)-BASTI(UP) (PG) CKT-2 was in open condition and site engineers were checking wiring of LBB and carrying out Circuit Breaker at Basti end . ii)As reported, at 12:02 hrs, during CB timing testing of 400 KV LUCKNOW_1(PG)-BASTI(UP) (PG) CKT-2 (Z1) Bus-Bar protection operated due to malfunction of 89A Gas density Monitor. iii)This led to the tripping of both 400KV Bus-I & II and the elements connected with them. iv)As per PMU at 400KV Lucknow(PG), no fault in system is observed. v)SCADA data of 400/220 kV 500 MVA ICT 3 was in suspected condition before and tripping the tripping incident. vi)As per SCADA, change in demand of approx. 140MW is observed in UP control area.	i)400 KV Gorakhpur (PG)-Basti(UP) (PG) Ckt-1 ii)400/220 kV 500 MVA ICT 1 at Basti(UP) iii)400 KV Tanda(NT)-Basti(UP) (UP) Ckt-2 iv)400 KV Lucknow_1(PG)-Basti(UP) (PG) Ckt-1 v)400/220 kV 500 MVA ICT 2 at Basti(UP) vi)400 KV Tanda(NT)-Basti(UP) (UP) Ckt-1 vii)125 MVAR BUS REACTOR NO 1 AT 400 KV BASTI(UP)
7	GI-1	Haryana	13-12-2024 10:41	13-12-2024 13:36	02:55	0	40	0.000	0.060	55849	66263	i)During antecedent condition, 220 KV Bhiwani-Charkhi Dadri (BB) Ckt-4, 220 KV Bhiwani-Charkhi Dadri (BB) Ckt-2 and 220 KV Bhiwani (HV)-Bhiwani (BB) (HVPNL) Ckt-2 were carrying appx. 18MW, 17MW and 186 MW respectively . ii)As reported, at 10:41 hrs, load shifting from 220KV Bus-2 to Bus-1 at 400/220KV Bhiwani was being done to avail shutdown of 220KV Bus-2 under annual maintenance. During load shifting Bus Bar protection operated causing tripping of 220KV Bus-2 and all the elements connected to it. iii)At the same time, 220 KV Bhiwani(HV)-Bhiwani(BB) (HVPNL) Ckt-1 also tripped which was connected to 220kV Bus-1 (exact nature of protection operated yet to be shared). Detailed report of the tripping is yet to be furnished from SLDC end. iv)As per PMU at Bhiwani (BBMB), Y-B phase to phase fault is observed with fault clearing time of ~120 ms. v)As per SCADA, 40MW loss occurred in Haryana control area.	i)220 KV Bhiwani-Charkhi Dadri (BB) Ckt-4 ii)220 KV Bhiwani-Charkhi Dadri (BB) Ckt-2 iii)220 KV Bhiwani (HV)-Bhiwani (BB) (HVPNL) Ckt-2 iv)220 KV Bhiwani(HV)-Bhiwani(BB) (HVPNL) Ckt-2 v)220 KV Bhiwani(HV)-Bhiwani(BB) (HVPNL) Ckt-1

Details of Grid Events during the Month of Dec 2024 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GI-2	Rajasthan	14-12-2024 18:05	14-12-2024 19:00	00:55	0	400	0.000	0.685	47300	58389	i)During antecedent condition, 400/220 kV 315 MVA ICT 1 and ICT 2 at Bikaner(RS) was carrying approx. 240MW each. 400KV Bikaner-Sikar(PG) Ckt-2 and 220kV Bikaner-Dungargarh (RS) line were in open condition. ii)As reported, at 18:35 hrs, Y phase isolator on 220KV side of 400/220 kV 315 MVA ICT 2 at Bikaner(RS) burnt and tripped. iii)As per PMU at Bhadla(PG), R-Y fault in system is observed with delayed fault clearance of 760ms . iv)Due to tripping of ICT-2, SPS implemented at Bikaner(RS) S/s related to overloading of remaining ICTs after tripping of any ICT operated. As per SPS scheme, 220kV Bikaner-Nokha (RS) line and 220kV Bikaner-Dungargarh (RS) line should open. However, 220kV Bikaner-Dungargarh (RS) line was already in open condition. v)During the event, both 400/220kV 315MVA ICT-1&2 tripped. At the same time, 125 MVAR BUS REACTOR NO 2 AT 400KV BIKANER(RS) also tripped due to Backup Impedance protection operation. vi)As per SCADA, change in demand of approx. 400MW is observed in Rajasthan control area. vii)As observed, the SCADA data remained frozen upto 18:10 hrs and subsequently became unavailable after 18:10hrs.	i)400/220 kV 315 MVA ICT 1 at Bikaner(RS) ii)400/220 kV 315 MVA ICT 2 at Bikaner(RS) iii)125 MVAR BUS REACTOR NO 2 AT 400KV BIKANER(RS)
9	GD-1	Rajasthan	15-12-2024 11:35	15-12-2024 12:30	00:55	1066	0	1.942	0.000	54898	62567	i)Generation of 220kV Azure 41(IP) station evacuates through 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt. which was generating approx. 294 MW (as per PMU). Similarly, 220kV Azure 34(IP) station evacuates through 220 KV BHADLA(PG)-AZURE POWER 34 SOLAR(APTFL) (APTFL) CKT-1 which was generating 121MW (as per PMU). ii)As reported, at 11:35hrs, 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt tripped on B-N phase to earth fault due to differential protection operation on account of broken jumper at tower location 50. At the same time 130 MVA 220/33KV ICT at 220kv Azure 34 also tripped on account of Differential relay protection (exact reason yet to be shared) iii)Due to tripping of 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt and 130 MVA 220/33KV ICT, Azure 41(IP) and Azure 34 S/s lost its connectivity from grid and blackout occurred at 220kV Azure 41(IP) and 220kV Azure 34(IP) S/s. iv)As per PMU at Bhadla(PG), B-N phase to earth fault (voltage dipped upto 0.63 p.u.) is observed with fault clearing time of 120ms. After the fault clearance voltage increased upto 1.08 p.u. v)As per PMU at Bassi(PG), a sharp drop in frequency is observed from 49.995 Hz to 49.803 Hz and frequency recovered to 49.97 Hz within 1 min.vi)As per PMU, solar generation loss of approx. 294 MW, 160 MW, 131 MW, 24 MW and 181 MW are observed respectively at Azure 41(IP), ESURL(IP), DVKOT_NT, ASHPL(IP) and ASEPL(IP).vii)As per SCADA, dip in NR total solar generation of approx. 1066 MW is observed with change in Rajasthan solar generation of approx. 126 MW. Demand change of 436 MW was observed in Punjab.viii)As reported by SLDC-Punjab, reduction in demand was due to operation of df/dt stage-1 operation. (Exact feeder wise details of df/dt operation is yet to be received from Punjab)ix)As per DR (Bhadla end) of 220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt, A/R closing attempt was not observed after dead time. POWERGRID has been communicated to resolve the issue related to A/R operation.	i)220 KV AzurePSS41 SL_BHD_PG (APFOL)-Bhadla(PG) (Azure) Ckt ii)130 MVA 220/33KV ICT at 220kV Azure 34
10	GD-1	Punjab	27-12-2024 13:48	27-12-2024 14:52	01:04	0	25	0.000	0.050	42449	49705	i)220/66kV Mehal_Kalan has double main bus scheme at 220kV level. ii)As reported at 13:48 hrs, Bus Bar protection operated due to the damage in B-phase Circuit Breaker limb of 220 KV PAKHOWAL(PSTCL)- MEHAL- KALAN(PS) (PSTCL) CKT-1 (details yet to be furnished). iii)Due to the operation of Bus Bar protection all the elements connected in the 220KV system tripped. Complete blackout occurred at 220kV Mehal_Kalan S/s. iv)As per PMU at Moga (PG), R-N phase to earth fault with fault clearing time of 120ms is observed. v)As per SCADA, change in demand of approx. 20 MW is observed in Punjab control area.	i)220 KV MOGA(PG)-MEHAL- KALAN(PS) (PSTCL) CKT-1 ii)220 KV MOGA(PG)-MEHAL- KALAN(PS) (PSTCL) CKT-2 iii)220 KV PAKHOWAL(PSTCL)- MEHAL- KALAN(PS) (PSTCL) CKT-1 iv)220 KV PAKHOWAL(PSTCL)- MEHAL- KALAN(PS) (PSTCL) CKT-2
11	GD-1	Uttar Pradesh	29-12-2024 15:56	29-12-2024 16:54	00:58	35	27	0.085	0.060	41015	45099	i)220/132kV CB Ganj(UP) has double main and transfer bus scheme at 220kV level. 220KV Rosa – CB Ganj line was not in service. ii)During the antecedent condition, 2 generators at Tanakpur were generating 19MW (Unit-2) and 16MW (Unit-3). iii)As reported at 15:56 hrs, 220kV CB Ganj-Dohna ckt tripped on Y-B phase to phase fault, fault distance was ~7.23km (Z-1) from CB Ganj end. At the same time, all the other lines connected to 220 CB Ganj (except 220kV CB Ganj-Sitarganj) and 220kV Tanakpur-Sitarganj ckt also tripped. 220 KV TANAKPUR(NH)-SITARGANJ(PG) (PG) CKT tripped due to Y-B phase to phase fault with fault current of 1.14KA. The fault was in Zone-3. iv)Further, 132kV Tanakpur-Mahindernagar ckt was hand tripped for safety purpose leading to tripping of 31.4 MW Unit-2&3 at Tanakpur HEP due to loss of evacuation path. v)As per PMU at Bareilly(PG), Y-B phase to phase fault with delayed fault clearing time of 920ms is observed. vi)As per SCADA, change in demand of approx. 27 MW is observed in Uttar Pradesh control area.	i)220 KV TANAKPUR(NH)-CBGANJ(UP) (PG) CKT-1 ii)31.4 MW TANAKPUR HPS - UNIT 3 iii)31.4 MW TANAKPUR HPS - UNIT 2 iv)220 KV TANAKPUR(NH)-SITARGANJ(PG) (PG) CKT-1 v)220 kv Bareilly-CB Ganj (UP) ckt-1 vi)220 kv Bareilly-CB Ganj (UP) ckt-2 vii)220 KV CB Ganj-Dohna viii)132kV Tanakpur- Mahindernagar ckt
12	GD-1	Rajasthan	29-12-2024 11:30	29-12-2024 12:10	00:40	0	305	0.000	0.536	48669	56913	i)220/132kV Dausa(RS) has double main and transfer bus scheme at 220kV level. ii)During antecedent condition, 220 kV Alwar(RS)-Dausa(RS) Ckt and 220 kV Lalsot(RS)-Dausa(RS) Ckt were not in service. iii)As reported, at 11:30 hrs, heavy sparking in the isolator of the 220 KV BASSI(PG)-DAUSA(RS) (PG) CKT-1 resulted into snapping of conductor and line tripped. iv)At the same time, all the elements connected to both the 220kV buses tripped and there was no source of supply at 132kV level, complete blackout occurred at 220/132kV Dausa(RS) S/s. v)As per PMU at Bassi(PG), R-B phase to phase fault with delayed fault clearing time of 480ms is observed. vi)As per SCADA, change in demand of approx. 308 MW is observed in Rajasthan control area.	i)220 KV BASSI(PG)-DAUSA(RS) (PG) CKT-1 ii)220 KV BASSI(PG)-DAUSA(RS) (PG) CKT-2 iii)220 KV SAWAIMADHOPUR(RS)- DAUSA(RS) (PG) CKT-1 iv)220 KV Sikarai - Dausa(RS) Ckt
13	GI-1	Jammu & Kashmir	31-12-2024 05:57	31-12-2024 09:16	03:19	0	225	0.000	0.501	33230	44900	i)400/220kV Amargarh S/s have two bus at 220kV side i.e., main bus & reserve bus. ii)During antecedent condition, 220 KV Amargarh (NRSS XXIX)-Delina(PDD) (PDD JK) Ckt-1 and Ckt-2 were carrying 105 and 107 MW respectively and feeding Delina load. iii)As reported, at 05:57 hrs, 220 KV Amargarh (NRSS XXIX)-Delina(PDD) (PDD JK) D/C tripped from both ends on B-N phase to earth fault. iv)As per PMU at Amargarh(PG), two successive B-N phase to earth fault which cleared within 120 msec is observed. v)As per SCADA, change in demand of approx. 225MW is observed in J&K control area.	i)220 KV Amargarh(NRSS XXIX)-Delina(PDD) (PDD JK) Ckt-1 ii)220 KV Amargarh(NRSS XXIX)-Delina(PDD) (PDD JK) Ckt-2
14	GI-1	Jammu & Kashmir	31-12-2024 13:33	31-12-2024 19:34	06:01	0	78	0.000	0.142	51255	54907	i)220/132/33kV Bisnah S/s have two bus at 220kV side i.e., main bus & reserve bus. ii)During antecedent condition, 220 KV SAMBA(PG)-BISHNAH(JK) (PDD JK) CKT-1 was carrying 76 MW load and feeding Bisnah load. iii)As reported, at 13:33 hrs, 132KV/33KV 50MVA ICT-1 BISHNAH tripped on account of fire incident. At the same time 220 KV SAMBA(PG)-BISHNAH(JK) (PDD JK) CKT-1 also tripped. The tripping details are still awaited. iv)As per PMU at Amargarh(INDIGRID), Y-N phase to earth fault with delayed fault clearing time of 880 msec is observed. v)As per SCADA, change in demand of approx. 78 MW is observed in J&K control area.	i)220 KV SAMBA(PG)-BISHNAH(JK) (PDD JK) CKT-1 ii)132KV/33KV 50MVA ICT-1 BISHNAH
15	GI-1	Jammu & Kashmir	31-12-2024 19:47	31-12-2024 21:07	01:20	0	235	0.000	0.402	42675	58436	i)220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. 220kV Amargarh-Ziankote ckt-1&2 are on the same tower (D/C tower) and line length is ~21.4km. ii)During antecedent condition, 220kV Amargarh (INDIGRID) –Ziankote(JK) D/C was carrying 157 MW each and feeding Ziankote load. iii)As reported, at 19:47 hrs, 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 tripped on R-N phase to earth fault with fault distance of 13.18 km and fault current of Ir~=1.199 kA from Ziankote end. Fault sensed in zone-1 at Ziankote end. iv)This led to overloading of 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2 and this line tripped from Ziankote end only on over-current protection operation. v)As per PMU at Amargarh(INDIGRID), R-N phase to earth fault with fault clearing time of 80 msec is observed. vi)As per SCADA, change in demand of approx. 235 MW is observed in J&K control area.	i)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 ii)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2

Details of Grid Events during the Month of Dec 2024 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	WR	01-12-2024 17:42	01-12-2024 19:05	01:23	761	-	1.11%	-	68467	62485	At 17:42 hrs / 01-12-2024, 400 kV RKM-Bus Reactor-1 (50 MVAR) tripped on Over current earth fault protection operation due to failure of R-phase Lightening arrester top stack. Non operation of differential protection operation of Bus reactor is undesirable. After 6 cycles of fault occurrence, RKM Unit-1,2&3 (360 MW) tripped simaltaneously on over current protection operation, which was undesirable since fault was outside the zone of protection. Generation loss of 761 MW at RKM thermal power plant due to the event.	Tripping of following Elements: 1. 400 kV RKM-Bus Reactor-1 (50 MVAR) 2. RKM Unit-1,2&3 (360 MW) 3. RKM GT-4 (Idle Charged)
2	GI-1	WR	03-12-2024 12:31	03-12-2024 17:25	04:54	-	48	-	0.07%	75782	70089	At 12:31 hrs / 03.12-2024, 220 kV Saki-Bus-2 and all connected elements (as mentioned in elements tripped column) tripped on bus bar protection operation due to fault in Y phase 220 kV Earth cum Disconnector Switch (EDS) Bus-2 side module of Bus coupler bay because of internal flashover. Load loss of 48 MW occurred at Saki and downstream network due to the event.	Tripping of following Elements: 1. 220 kV Saki-Bus-2 2. 220 kV Saki-Aarrey-2 3. 220 kV Saki-TPC-2 3. 220/33 kV Saki-ICT-2 (125 MVA)
3	GD-1	WR	09-12-2024 15:57	09-12-2024 16:32	00:35	927	-	1.19%	-	77952	67855	At 15:57 hrs / 09-12-2024, 400 kV KSK Mahanadi-Champa-4 tripped on phase to phase fault from KSK end only on Z-1, during inspection dead bird was found near the 400 kV KSK Mahanadi-Champa-4 bay at KSK switchyard. Prior to the incident 400 kV KSK Mahanadi-Champa-3 was under planned shutdown from 10:45 hrs / 09-12-2024 for AMP Work. Due to this KSK Mahanadi-Unit-2&3 (600 MW) tripped due to loss of evacuation path. Generation loss of 927 MW occurred at KSK Mahanadi Thermal Power Plant.	Tripping of following Elements: 1. 400 kV KSK Mahanadi-Champa-4 2. KSK Mahanadi-Unit-2&3 (600 MW)
4	GD-1	WR	10-12-2024 02:58	10-12-2024 06:29	03:31	-	-	-	-	62011	48055	At 02:58 hrs / 10-12-2024, 220 kV Barsaita Desh- Rewa 1 tripped only at Barsaita Desh end on Differential protection operation and Barsaita Desh- Rewa 2 tripped at Rewa end only (No indication as reported by Powergrid WR-2) During charging of 220/33 kV Barsaita Desh-ICT-2 which was under planned shutdown for AMP work since 19:37 hrs / 09-12-2024. With these trippings 220 kV Barsaitadesh Solar Plant became dead. No generation loss occurred due to the event.	Tripping of following Elements: 1. 220/33 kV Barsaita Desh ICT-1&3 2. 220 kV Barsaita Desh-Bus-1&2 3. 220 kV Barsaita Desh-Rewa-1&2
5	GI-2	WR	11-12-2024 15:04	11-12-2024 16:42	01:38	-	-	-	-	77282	63584	At 15:04 hrs / 11-12-2024, 400 kV Vapi II-Vapi(PG)-1&2 tripped on SOTF indication during CSD commisioning in main bay of 400 kV Vapi II-Bus Reactor at Vapi II, current in B phase of these lines reached upto 5.43 kA. After 1.1 seconds 400 kV Vapi II-Kakrapar 3&4-2 tripped on Zone-1 B-E fault. No generation or load loss occurred during the event	Tripping of following Elements: 1. 400 kV Vapi II-Vapi(PG)-1&2 2. 400 kV Vapi II-Bus Reactor
6	GD-1	WR	17-12-2024 07:12	17-12-2024 12:09	04:57	95	-	0.12%	-	76284	63494	At 07:12 hrs / 17-12-2024, 220kV Bhuj-Vadva tripped on B-E fault without auto recloser attempt at both ends. At the time of patrolling no abnormalities were found. Generation loss of 95 MW occurred at Vadva (GIWEL-II) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Vadva- Bhuj-1
7	GI-2	WR	26-12-2024 17:52	26-12-2024 19:42	01:50	719	-	0.93%	-	77498	67240	At 17:52 hrs / 26-12-2024, JPL Stage 1-Unit-1,2&3 (250 MW) tripped on over current to earth fault during charging of 400 kV JPL Stage 1-JPL Stage 2-I/C line, the line tripped on pole discrepancy operation. The tripping of units was undesirable. In earlier incidences of tripping of 400 kV JPL Stage 1-JPL Stage 2-I/C line at 06:12 hrs / 23-12-2024 and 05:22 hrs / 26-12-2024 on differential, 400 kV JPL Stage 2-Tamnar-3 tripped instantaneously for a fault in Z-3 at Tamnar end (Main 2 relay tripped for a fault seen in Z-3 by Main-1 relay). Generation loss of 719 MW occurred at JPL Stage 1 due to tripping of JPL Stage 1-Unit-1,2&3 (250 MW).	Tripping of following Elements: 1. JPL Stage 1-Unit-1,2&3 (250 MW)
8	GD-1	WR	28-12-2024 12:22	28-12-2024 15:31	03:09	28	-	0.04%	-	71360	62001	At 12:22 hrs / 28-12-2024, 220 kV Bhawsingpura-Khandwa-1 tripped on persistent R-E fault, auto recloser attempted from Khandwa end only. Due to this 220 kV Bhawsingpura-Kanwani-1 radial line also tripped due to disconnection with grid. Generation loss of 28 MW occurred at Bhawsingpura and Kanwani (Masaya) Solar Plant due to the above event.	Tripping of following Elements: 1. 220 kV Bhawsingpura-Khandwa-1 2. 220 kV Bhawsingpura-Kanwani-1
9	GI-2	WR	28-12-2024 19:52	28-12-2024 23:14	03:22	-	-	-	-	62011	49653	At 19:52 hrs / 28-12-2024, 765 kV Champa-Bus-3 tripped on busbar protection operation resulting in tripping of all connected Main Bays of element and 765 kV Champa-Kotra-1 due to flashover in R phase CT of 765 kV Champa Kotra-1 Earlier at 19:50 hrs / 28-12-2024, 765 kV Champa-ICT-3 tripped on Differential protection operation due to failure of its B phase CT. At 22:13 hrs / 28-12-2024, 765 kV Champa-Dharamjaigarh-1 tripped due to failure of its B phase CT. As informed by Powergrid, weather conditions at Champa deteriorated with very heavy wind, lightening and stormy rain. No generation or load loss occurred due to the event	Tripping of following Elements: 1. 765 kV Champa-Bus-3 2. 765 kV Champa-Kotra-1 3. 765 kV Champa-Dharamjaigarh-1 4. 765 kV Champa-ICT-3

Details of Grid Events during the Month of Dec 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KERALA	02-12-2024 08:43	02-12-2024 09:41	00:58	0	84	0.00%	0.19%	43163.61	44957.27	Complete Outage of 220kV/110kV/33kV Punnapura SS of KSEB: The triggering incident was failure of HV side Y-phase CT of 200MVA 220kV/110kV Transformer#2 at Punnapura SS resulting in 220kV Bus-2 fault. Due to non-operation of BBP protection, fault was cleared by tripping of both 220kV lines at remote end. This resulted in complete outage of 220kV/110kV/33kV Punnapura SS of KSEB.	220KV-KAYAMKULAM-PUNNAPRA-1, 220KV-PUNNAPRA-NEW PALLOM-1, PUNNAPRA - 220KV, PUNNAPRA - 220KV - Bus 1, PUNNAPRA - 220KV - Bus 2
2	GD - 1	TAMILNADU	03-12-2024 11:00	03-12-2024 11:15	00:15	24	0	0.05%	0.00%	44192.0	44403.98	Complete Outage of 400kV/110kV Thappagundu SS of TANTRANSCO: During antecedent conditions, 400kV Annaikadavu Thappagundu line-2 was under outage. The triggering incident was RN fault in 400kV Annaikadavu Thappagundu line-1. Due to loss of both 400kV connected lines there was complete outage of 400kV/110kV Thappagundu SS of TANTRANSCO.	400KV-ANAIKADAVU-THAPPUKUNDU-1
3	GD - 1	ANDHRA PRADE	04-12-2024 17:44	04-12-2024 20:35	02:51	5	0	0.01%	0.00%	41532.08	45168.3	Complete Outage of 400kV Greenko CPSS, 400kV AMGEPL Wind Plant, and 400kV Pinnapuram PSP: During antecedent conditions, 400kV Greenko CPSS, 400kV AMGEPL Wind Plant and 400kV Pinnapuram PSP were radially connected to 765kV/400kV Kurnool SS through 400kV Greenko CPSS Kurnool line-1. Triggering incident was inadvertent tripping of 400kV Greenko CPSS Kurnool line-1 at Greenko CPSS end during testing activity. This resulted in the complete outage of 400kV Greenko CPSS, 400kV AMGEPL Wind Plant, and 400kV Pinnapuram PSP.	400KV/11KV GREENKO_PSP-ST-1, 400KV/18KV GREENKO_PSP-GT-3, 400KV/33KV AMGEPL_WIND-ICT-2
4	GD - 1	TAMILNADU	13-12-2024 15:06	13-12-2024 16:06	01:00	0	169	0.00%	0.35%	40286.8	48649.96	Complete Outage of 400kV/230kV/110kV Tharamani SS of TANTRANSCO: 230kV Tharamani Bus-2 was not in service during antecedent conditions. As per the reports submitted, the triggering incident was tripping of 230kV Bus-1 BBP on maloperation. Tripping of 230kV Tharamani Bus-1 led to complete outage of 400kV/230kV Tharamani SS.	230KV-KALVENDAPATTU-THARAMANI, 230KV-SRIPERUMBADUR_TN-THARAMANI-1
5	GD - 1	ANDHRA PRADESH	29-12-2024 16:30	30-12-2024 06:44	14:14	0	0	0.00%	0.00%	37520.27	46882.62	Complete Outage of 400kV RYTPP Generating station of APGENCO: As per the reports submitted, the triggering incident was tripping of 400kV RYTPP Kalikiri Line-1&2 on over voltage at 19:41hrs and 16:30hrs respectively. Tripping of both lines led to complete outage of 400kV RYTPP Generating station.	400KV-RYTPP-KALIKIRI-1 400KV-RYTPP-KALIKIRI-2
6	GI-2	KARNATAKA	02-12-2024 20:52	02-12-2024 23:10	02:18	340	40	0.01	0.0	35595.59	39442.84	Tripping of 400kV Bus-1 at 400kV/220kV Jindal TPS: The triggering incident was breaker flashover (Unit side to Grid side external breaker flashover) in Unit-6 during synchronizing the unit. Due to the breaker flash-over Y-pole started conducting even when the breaker was open leading to LBB operation and tripping of 400kV Bus-1 at 400kV/220kV Jindal TPS.	JINDAL - 400KV - Bus 1, 400KV/220KV JINDAL-ICT-1, 400KV/220KV JINDAL-ICT-2, JINDAL - UNIT 3, JINDAL - UNIT 5, JINDAL - UNIT 6

Details of Grid Events during the Month of Dec 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GI-2	KARNATAKA	02-12-2024 21:35	02-12-2024 23:10	01:35	211	97	0.01	0.0	33965.06	37981.08	Tripping of 400kV Bus-2 of 400kV/220kV Jindal TPS: The triggering incident was Y-N fault after isolator and before the breaker at TR-18 of Jindal TPS (within the bus zone). During the previous event at 20:52 Hrs all the elements connected to 400kV Bus-1 tripped including TR-18 breaker. For the restoration of TR-18, the isolator to Bus-2 was closed on a suspected Y-N fault leading to Bus bar protection operation and tripping of all elements connected to 400kV Bus-2.	JINDAL - 400KV - Bus 2, 400KV-JINDAL-BPS-3, 400KV-JINDAL-BPS-4
8	GI-1	ANDHRA PRADESH	06-12-2024 23:09	06-12-2024 23:42	00:33	0	0	0.0	0.0	36147.52	40076.54	Tripping of 220kV Bus of 220/132 kV KV_KOTA_OLD SS: The triggering incident was Y-ph CT failure of 220kV KV_Kota-KV_Kota_Old-1 at KV_Kota Old station, Bus Bar protection operated leading to the tripping of all the elements connected to 220kV Bus. This led to the de-energization of 220kV Bus of 220/132 kV KV_KOTA_OLD SS. The 132kV network was intact during the event.	220KV-KV_KOTA_OLD-NUZVID-1, 220KV-KV_KOTA_OLD-KV_KOTA-2, KV_KOTA_OLD - 220KV - Bus 1, 220KV-KV_KOTA_OLD-KV_KOTA-1, 220KV-NIDADAVOLU-KV_KOTA_OLD-1
9	GI-2	KARNATAKA	14-12-2024 13:49	14-12-2024 15:49	02:00	0	0	0.0	0.0	42144.93	46943.85	Tripping of 400kV Bus-2 of RTPS of KPCL: As per the reports submitted, the triggering incident was tripping of 400kV RTPS Bus-2 on operation of BBP due to intiation of LBB trip from Main breaker of GT-7. This led to tripping of all elements connected to 400kV RTPS Bus-2.	RTPS - 400KV - Bus 2
10	GI-1	KARNATAKA, TAMILNADU	19-12-2024 13:58	19-12-2024 17:20	03:22	0	40	0.0	0.0	44453.45	51590.07	Tripping of 220kV Bus-2 at 220kV/66kV YERRAANDAHALLI: In the antecedent conditions, 220/66kV YERRAANDAHALLI is operating in bus split condition at 220kV level, where in 220kV Bus-2 was radially connected to 220kV Yerrahandalli Hosur line. The triggering incident is the R-N fault in the 220kV Yerrahandalli-Hosur line, the line tripped at both ends on Z1 protection. The tripping of the only line connected to Bus-2 led to the tripping of 220kV Bus-2 at 220kV/66kV YERRAANDAHALLI.	220KV-YERRAANDAHALLI-HOSUR-1
11	GI-1	KARNATAKA, TAMILNADU	21-12-2024 13:23	21-12-2024 13:50	00:27	0	36	0.0	0.0	45329.61	50797.74	Tripping of 220kV Bus-2 at 220kV/66kV YERRAANDAHALLI: In the antecedent conditions, 220/66kV YERRAANDAHALLI is operating in bus split condition at 220kV level, where in 220kV Bus-2 was radially connected to 220kV Yerrahandalli Hosur line. The triggering incident is the R-N fault in the 220kV Yerrahandalli-Hosur line, the fault was sensed in Z1 at both ends, at Hosur end AR operated and AR was successful and the line was holding, at Yerrahandalli end as AR is disabled and 3ph tripped. The tripping of the only line connected to Bus-2 led to the tripping of 220kV Bus-2 at 220kV/66kV YERRAANDAHALLI.	220KV-YERRAANDAHALLI-HOSUR-1
12	GI-1	KARNATAKA, TAMILNADU	21-12-2024 14:45	21-12-2024 15:28	00:43	0	27	0.0	0.0	45410.32	51561.68	Tripping of 220kV Bus-2 at 220kV/66kV YERRAANDAHALLI: In the antecedent conditions, 220kV/66kV YERRAANDAHALLI is operating in bus split condition at 220kV level, where in 220kV Bus-2 was radially connected to 220kV Yerrahandalli Hosur line. The triggering incident is the R-N fault in the 220kV Yerrahandalli-Hosur line, the line tripped at both ends on Z1 protection. The tripping of the only line connected to Bus-2 led to the tripping of 220kV Bus-2 at 220kV/66kV YERRAANDAHALLI.	220KV-YERRAANDAHALLI-HOSUR-1

Details of Grid Events during the Month of Dec 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-I	JSPL (CPP)	19.12.2024 13:27	19.12.2024 14:40	01:13	00:00	533	1.91%	2.97%	26591	17945	At 13:27 Hrs, 400 kV JSPL-Meramundali D/c tripped due to a fire incident at tower Loc. 62. Consequently, 400 kV Bus-1&2 at JSPL became dead. Captive power plant JSPL has 6 units of 135 MW capacity each. Unit-1 with emergency load of 107 MW was separately connected with 220 kV Bus-1 (220 kV bus-coupler remaining open). Unit-6 is under overhauling and other 4 units (unit-2,3,4,5) connected to 220 kV Bus-2 were generating around 508 MW and rest around 25 MW was imported from grid for its captive load. As both evacuating lines tripped, the captive island didn't survive.	400 kV Meramundali-JSPL D/c U#2,3,4,5 (135 MW) each at JSPL

Details of Grid Events during the Month of Dec 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Monarchak and Rokhia S/S of Tripura Power System	06-12-2024 13:06	06-12-2024 14:05	00:59	17	8	1.10%	0.40%	1550	1980	Monarchak and Rokhia S/S of Tripura Power System was connected with rest of NER Grid through 132 kV Monarchak – Udaipur Line, 132 kV Monarchak – Rokhia line and 132 kV Rokhia – Agartala D/C lines. At 13:06 Hrs of 06.12.2024, 132 kV Monarchak – Udaipur Line, 132 kV Monarchak – Rokhia line and 132 kV Rokhia – Agartala D/C lines tripped along with Rokhia unit-9 due to which Monarchak and Rokhia areas of Tripura Power System got isolated from NER Grid and collapsed due to no source available in these areas.Power supply was extended to Monarchak area of Tripura Power System by charging 132 kV Monarchak – Udaipur Line at 13:28 Hrs of 06.12.2024 and power extended to Rokhia S/S by charging 132 kV Monarchak-Rokhia line at 14:05 Hrs of 06.12.2024.	132 kV Monarchak – Udaipur Line, 132 kV Monarchak – Rokhia line and 132 kV Rokhia – Agartala D/C lines
2	GD I	Along and Pasighat areas of Arunachal Pradesh Power System	08-12-2024 03:46	08-12-2024 05:12	01:26	0	2	0.00%	0.14%	1632	1448	Along and Pasighat areas of Arunachal Pradesh Power System were connected with rest of NER Grid through 132 kV Along-Basar & 132 kV Roing-Pasighat lines. At 03:46 Hrs of 08-12-2024, 132 kV Along-Basar line, 132 kV Along-Pasighat Line and 132 kV Roing-Pasighat line tripped. Due to tripping of these elements, Along and Pasighat areas of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Along and Pasighat areas of Arunachal Pradesh Power System by charging 132 kV Roing-Pasighat Line at 05:12 Hrs of 08-12-2024.	132 kV Along-Basar line, 132 kV Along-Pasighat Line and 132 kV Roing-Pasighat line
3	GD I	Pavoi area of Assam Power System	16-12-2024 15:43	16-12-2024 16:23	00:40	0	11	0.00%	0.53%	1954	2070	Pavoi (BNC) area of Assam Power System was connected with rest of NER Grid through 132 kV BNC-Pavoi 1 &2 & 132 kV Gohpur-Pavoi 1 & 2 lines. At 15:43 Hrs of 16-12-2024, 132 kV BNC-Pavoi 1 &2 & 132 kV Gohpur-Pavoi 1 & 2 lines tripped. Due to tripping of these elements, Pavoi area of Assam Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Pavoi area of Assam Power System by charging 132 kV Gohpur-Pavoi 1 & 2 lines at 16:23 Hrs of 16-12-2024.	132 kV BNC-Pavoi 1 &2 & 132 kV Gohpur-Pavoi 1 & 2 lines
4	GD I	Sonabil, Ghoramari, Depota, Dhekiajuli and Rowta areas of Assam Power System	20-12-2024 15:04	20-12-2024 15:24	00:20	0	57	0.00%	2.79%	2051	2044	Sonabil, Ghoramari, Depota, Dhekiajuli and Rowta areas of Assam Power System was connected with rest of NER Grid through 220 kV Balipara-Sonabil II line. Prior to the event, 220 kV Balipara-Sonabil I line was under shutdown. 132 kV Rowta-Siphajhar and 132 kV Rowta-Tangla lines was open due to system requirement. At 15:04 Hrs of 20-12-2024, 220 kV Balipara-Sonabil II line tripped and SPS at Sonabil operated successfully which caused tripping of 220/132 kV, 100 MVA ICT-I & II at Sonabil. Due to tripping of these elements, Sonabil, Ghoramari, Depota, Dhekiajuli and Rowta areas of Assam Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to the affected areas by charging 220/132kV Sonabil ICT#1 & 2 at 15:24 Hrs of 20-12-2024.	220 kV Balipara-Sonabil II line

21. NEW ELEMENTS CHARGED IN DECEMBER 2024

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
WR	1	400/33 kV Khavda PSS-2	Adani Green Energy 25 A Limited (AGE25AL)	Solar	143.275	500	17.12.2024
	2	400/220 kV Pachora	NTPC Renewable Energy Limited (NTPC REL) Dehripal	Solar	50	220	28.12.2024
	3	400/33 kV Khavda PSS-9	Adani Renewable Energy Forty Eight Limited (ARE48L)	Wind	41.6	400	13.12.2024
	4	400/33 kV Khavda PSS-3	Adani Ports & Special Economic Zone (APSEZ)	Solar	192.5	200	13.12.2024
NR	5	Bhadla_2	AMP Energy Green Four Private Limited	Solar	46.15	100	02.12.2024
	6	Bikaner	AYANA RENEWABLE POWER THREE PRIVATE LIMITED (ARP3PL)	Solar	19.38	300	05.12.2024
	7	Bikaner	AYANA RENEWABLE POWER THREE PRIVATE LIMITED (ARP3PL)	Solar	28	272	26.12.2024
	8	Bikaner_2	Serentica Renewables India 5 Pvt Ltd (SRI5PL)	Solar	66	220	17.12.2024
	9	Fatehgarh	ACME Dhaulpur Powertech Private Limited	Solar	28	300	24.12.2024
	10	Fatehgarh	ACME Raisar Solar Energy Private Limited	Solar	28	300	24.12.2024
SR	11	220/33KV RSRPL PSS GADAG	Renew Surya Roshini Private Limited (RSRPL)	Wind	66	66	06.12.2024
	12	220/33KV RSRPL PSS GADAG	Renew Surya Roshini Private Limited (RSRPL)	Wind	26.4	92.4	20.12.2024
	13	400KV AMGEPL Solar Pooling Station	AMGEPL	Solar	290	290	29.12.2024
	14	220KV IRCON Solar PSS / PAVAGADA	IRCON Renewable Power Limited	Solar	100	200	16.12.2024
	15	400/33KV AMGEPL Wind Substation	AMGEPL	Wind	131.67	270.27	12.12.2024
	16	400KV GREENKO CPSS	GREENKO IREP	Hydro/PSP Generation(Unit-3)	240	720	19.12.2024
	17	400KV GREENKO CPSS	GREENKO IREP	Hydro/PSP Generation(Unit-4)	240	960	18.12.2024
				Total Hydro Generation Addition	480		
				Total Solar Generation addition	991		
				Total Wind Generation addition	266		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
NR	1	RRVPNL	400/220/33kV GSS Pachpadra(RS)	ICT-1	400/220/33	500	10.12.2024
	2	PATRAN	400/220/33kV Patran(PATR)	ICT-3	400/220/33	500	26.12.2024
	3	PBTSL	400/220/33kV Bikaner_2 (PBTSL)	ICT-6	400/220/33	500	28.12.2024
ER	4	MPL	MAITHON POWER LIMITED	ST-3	400/11	80	26.12.2024
	5	OCPL	DARLIPALI	ICT-1	132/33	31.5	27.12.2024
	6	OCPL	DARLIPALI	ICT-2	132/33	31.5	28.12.2024
SR	7	TNTRANSCO	765kV VIRUDDHANAGAR	ICT-1	765/40033	1500	17.12.2024
	8	TNTRANSCO	765kV VIRUDDHANAGAR	ICT-2	765/40033	1500	17.12.2024
	9	GREENKO	400KV GREENKO PSP	GT-3	400/18	300	19.12.2024
	10	GREENKO	400KV GREENKO PSP	GT-4	400/18	300	18.12.2024
	11	JSW RENEW Energy Ltd	230KV JSW DHARAPURAM (KARUR)	ICT-1	230/33	150	20.12.2024
	12	JSW RENEW Energy Ltd	230KV JSW DHARAPURAM (KARUR)	ICT-2	230/33	150	20.12.2024
	13	APTRANSCO	400KV JAMMALAMADUGU	ICT-4	400/220/33	500	23.12.2024
					Total (MVA)	6043	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name		Length (KM)	Conductor Type	DATE
NR	1	PSTL	765kV Bhadla_2 (PG)-Sikar_2(PSTL)-2		309.272	Hexa Zebra	16.12.2024
	2	PSTL	765kV Bhadla_2 (PG)-Sikar_2(PSTL)-1		309.272	Hexa Zebra	17.12.2024
ER	3	JUSNL	400KV-CHANDWA-LATEHAR(JUSNL)-2		41.216	ACSR Moose	14.12.2024
	4	JUSNL	400KV-CHANDWA-LATEHAR(JUSNL)-1		41.216	ACSR Moose	14.12.2024
	5	BSPTCL	220KV-GAYA(PG)-BODHGAYA-3		31.0	ACSR Zebra	16.12.2024
	6	OCPL	33KV-DARLIPALLI (NTPC)-MANOHARPUR-1		12.2	AAAC(11.7 km OH line +0.5 km U/G XLPE Cable)	31.12.2024
SR	7	JSW RENEW Energy Ltd.	230KV-KARUR-JSW_Dharapuram-2		4.5	Al-59 Zebra	20.12.2024
	8	GREENKO AP01 IREP	400KV-GREENKO_CPSS-KURNOOL_PG-2		12.2	ACSR Quad Moose	06.12.2024
NER				Total length (km)	760.9		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NIL						

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
NR	1	RRVPNL	400kV Kankani(RS)- GSS Pachpadra(RS)-1 (After LILO of 400 kV Rajwast - Kankani line at 400 kV GSS Pachpadra)	112.011	Twin Moose	07.12.2024
	2	RRVPNL	400kV Rajwest(RW)- GSS Pachpadra(RS)-1 (After LILO of 400 kV Rajwast - Kankani line at 400 kV GSS Pachpadra)	168.011	Twin Moose	07.12.2024
ER	3	Power Dept, Govt. of Sikkim	220KV-Legship-NEW MELLI-1	10.25	Twin Moose ACSR	31.12.2024

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
NR	1	RRVPNL	Bus Reactor-1 400 at kV Jodhpur(RS)	400	125	09.12.2024
SR	2	TNTRANSCO	3Bus Reactor -1 at 765KV VIRUDHANAGAR	765	330	18.12.2024
	3	TNTRANSCO	Bus Reactor -2 at 765KV VIRUDHANAGAR	765	330	17.12.2024
	4	TNTRANSCO	Line Reactor -1 at 765KV VIRUDHANAGAR	765	330	18.12.2024
	5	TNTRANSCO	Line Reactor -2 at 765KV VIRUDHANAGAR	765	330	18.12.2024
				Total (MVAr)	1445	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

Voltage Profile

विद्युत विभव रूपरेखा माह - दिसम्बर 2024 VOLTAGE PROFILE - December 2024

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	794	744	770
2		दार्लिपली DARLIPALI	0%	100%	0%	0%	0	790	759	774
3		गया GAYA	0%	100%	0%	0%	0	784	742	766
4	पूर्वी क्षेत्र	जीरत JEERAT	0%	100%	0%	0%	0	778	727	752
5	ER	झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	2	802	767	783
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	788	739	763
7		रांची RANCHI	0%	100%	0%	0%	0	797	761	778
8		सासाराम SASARAM	0%	100%	0%	0%	2	806	736	766
1		आगरा AGRA	0%	100%	0%	0%	0	801	744	779
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	2	802	743	777
3		अजमेर AJMER	0%	99%	0%	1%	4	804	710	784
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	799	741	777
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	789	760	775
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	789	756	773
7		अंता ANTA	0%	100%	0%	0%	0	796	753	778
8		बलिया BALLIA	0%	100%	0%	0%	0	792	739	767
9		बारा BARA	0%	100%	0%	0%	0	794	745	771
10		भाडला BHADLA	0%	100%	0%	0%	0	802	721	778
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	1	801	703	781
12		भिवानी BHIWANI	0%	100%	0%	0%	2	804	737	783
13		बीकानेर BIKANER	0%	100%	0%	0%	1	801	707	782
14		बरेली BAREILLY	0%	98%	2%	2%	12	813	740	780
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	5	804	748	784
16		फतहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	803	717	778
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	795	741	769
18	उत्तरी क्षेत्र	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	794	731	771
19	NR	ग्रेटर नोएडा GREATER NOIDA	0%	99%	1%	1%	8	804	744	783
20		हापुड़ HAPUR	0%	99%	1%	1%	5	805	739	779
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	796	732	770
22		झाटकरा JHATIKARA	0%	100%	0%	0%	0	802	744	778
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	794	739	771
24		खेतरी KHETRI	0%	100%	0%	0%	1	803	733	782
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	800	740	776
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	781	743	762
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	802	740	773
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	791	733	766
29		मेरठ MEERUT	0%	99%	1%	1%	9	808	744	782
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	1	804	738	778
31		मोगा MOGA	0%	100%	0%	0%	1	804	718	773
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	784	750	769
33		उरई ORAI	0%	93%	7%	7%	51	808	754	787
34		फागी PHAGI	0%	99%	1%	1%	4	803	746	782
35		रामपुर RAMPUR	0%	89%	8%	8%	61	814	748	786
36		उन्नाव UNNAO	0%	100%	0%	0%	0	792	743	767
37		वाराणसी VARANASI	0%	100%	0%	0%	0	791	749	774
1		अकोला AKOLA	0%	100%	0%	0%	0	797	748	775
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	799	741	774
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	796	740	772
4		भुज BHUJ	0%	100%	0%	0%	1	802	743	777
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	796	737	771
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	786	748	766
7		बीना BINA	0%	99%	1%	1%	8	806	752	781
8		बनसकंठा BANASKANTHA	0%	96%	4%	4%	27	804	745	784
9		चापा CHAMPA	0%	95%	5%	5%	37	808	767	788
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	799	746	776
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	791	754	769
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	792	753	775
13		एकटुनी EKTUNI	0%	100%	0%	0%	0	797	742	772
14		गदरवाड़ा GADARWARA	0%	98%	2%	2%	14	806	760	784
15		ग्वालियर GWALIOR	0%	99%	1%	1%	10	806	750	783
16		इंदौर INDORE	0%	100%	0%	0%	0	795	743	772
17		जबलपुर JABALPUR	0%	94%	6%	6%	46	810	761	786
18	पश्चिमी क्षेत्र	खंडवा KHANDWA	0%	100%	0%	0%	0	797	746	773
19	WR	कोरडा KORADI	0%	100%	0%	0%	0	787	748	770
20		लकाडिया LAKADIYA	0%	99%	1%	1%	8	808	748	783
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	800	768	782
22		पड़घे PADGHE	0%	99%	1%	1%	8	806	737	778
23		परली PARLI	0%	99%	1%	1%	4	802	749	781
24		पुणे PUNE	0%	97%	3%	3%	21	807	742	781
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	1	802	759	781
26		सासन SASAN	0%	100%	0%	0%	0	792	760	777
27		सतना SATNA	0%	98%	2%	2%	12	804	758	784
28		सिवनी SEONI	0%	100%	0%	0%	1	802	750	776
29		सीपत SIPAT	0%	100%	0%	0%	0	787	750	767
30		सोलापुर SOLAPUR	0%	100%	0%	0%	2	802	752	781
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	781	750	767
32		तामनार TAMNAR	0%	100%	0%	0%	0	797	763	781
33		वड़ोदरा VADODARA	0%	98%	2%	2%	12	807	740	780
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	795	762	780
35		वर्धा WARDHA	0%	100%	0%	0%	0	798	742	774
36		वरोरा WARORA	0%	100%	0%	0%	3	803	744	779
1		अरियलूर ARIYALUR	0%	100%	0%	0%	0	791	734	768
2		कड़पा CUDDAPAH	0%	95%	5%	5%	38	809	747	785
3		चिल्कलुरीपेट CHILAKALURIPETA	0%	100%	0%	0%	0	799	734	775
4		कनूल KURNOOL	0%	100%	0%	0%	0	798	745	776
5		महेश्वरम MAHESWARAM	0%	96%	4%	4%	31	809	746	784
6	दक्षिणी क्षेत्र	निज़ामाबाद NIZAMABAD	0%	96%	4%	4%	30	811	743	783
7	SR	नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	799	749	777
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	0	794	737	771
9		रायचूर RAICHUR	0%	100%	0%	0%	0	800	747	779
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	0	799	741	774
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	792	736	770
12		वेमागिरी VEMAGIRI	0%	100%	0%	0%	0	800	739	775
13		वारंगल WARANGAL	0%	99%	1%	1%	4	805	743	780
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	412	390	403
2		बिस्वनाथ चारिआलि BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	419	390	407
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	417	400	409
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	419	401	410
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	415	395	406
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	3	421	401	412
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	416	390	405
8	पूर्वोत्तर क्षेत्र	अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	412	404	408
9	NER	मीसा MISA (400 kV)	0%	100%	0%	0%	0	413	391	404
10		न्यू मारियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	417	393	407
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	417	395	407
12		पालाटाना PALATANA(400 kV)	0%	100%	0%	0%	0	412	400	407
13		पुवकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	411	392	402
14		रंगानदी RANGANADI(400 kV)	0%	100%	0%	0%	0	418	388	406
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	399	409
16		सूर्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	409	393	401
17		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	408	408	408

All listed stations are 765 kV stations unless otherwise mentione
***Percentage is calculated w.r.t. Time of one month**

23.ALL TIME HIGHEST

31-12-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	186 01-05-2024
WR	77436 20-12-2024	67482 30-05-2024	1648 06-05-2024	167 18-12-2014	310 28-05-2024	110.77 09-12-2024
SR	68735 13-03-2024	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	323 26-07-2024	148.7 31-03-2024
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	4 09-06-2024
NER	3905 19-09-2024	3787 19-09-2024	80 20-09-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	426 30-04-2024

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	18405	19-12-2024	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	2254	25-12-2024	41.3	20-12-2024
	J&K(UT) and Ladakh(UT)	3181	24-12-2024	68.4	26-12-2024
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	18888	20-12-2024	349.3	20-12-2024
	Maharashtra	28969	07-02-2024	648.3	30-04-2024
	Goa	803	19-04-2024	17.6	18-05-2024
	DD & DNH	1390	23-10-2024	32.6	16-10-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	15623	08-03-2024	311.0	13-03-2024
	Karnataka	17220	12-03-2024	336.9	05-04-2024
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	8001	23-09-2024	172.8	30-07-2024
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26-05-2024	3.9	18-06-2024
	Assam	2687	20-09-2024	55.8	20-09-2024
	Manipur	266	28-12-2024	4.1	31-12-2024
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.4	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24. System Reliability Indices Report for the month of December 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	31	7.75	1.04
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	5	1.25	0.17
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
