ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre
कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या:- GRID-INDIA/NLDC/MR/ दिनांक: **26.12.2024**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **नवंबर 2024**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **नवंबर 2024** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
वरिष्ठ महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



नवंबर 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह नवंबर 2024 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF NOVEMBER -2024

पृष्ठसूची CONTENTS

1	माह नवंबर 2024 की सारांश रिपोर्ट Summary of report for the month of NOVEMBER 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति Evening Peak Hour Demand Met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	29 नवंबर के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 29-NOVEMBER (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह नवंबर 2023 से तुलना Energy requirement and met comparison with NOVEMBER 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह नवंबर 2023 से तुलना Peak demand requirement and met comparison with NOVEMBER 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-37
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	38-40
17	एसटीओए (द्विपक्षीय एवं सामूहिक)एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	41
18	पावर मार्केट की सूचना Power market information	42-46
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	47-49
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	50-56
21	नए चार्ज किये गए तत्व New elements Charged	57
22	विभव रूपरेखा Voltage profile	58
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह नवंबर 2024 तक All Time Highest (Demand & Energy) figures: Till NOVEMBER 2024	59
24	नवंबर 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for NOVEMBER 2024	60

1. SUMMARY OF REPORT FOR THE MONTH OF NOVEMBER-2024


EVENING PEAK HOUR (at 1900hrs) DEMAND MET AT NATIONAL LEVEL (MW)

Decreased by 13.41% as compared to Oct'24


Increased by 0.51% as compared to Nov'23

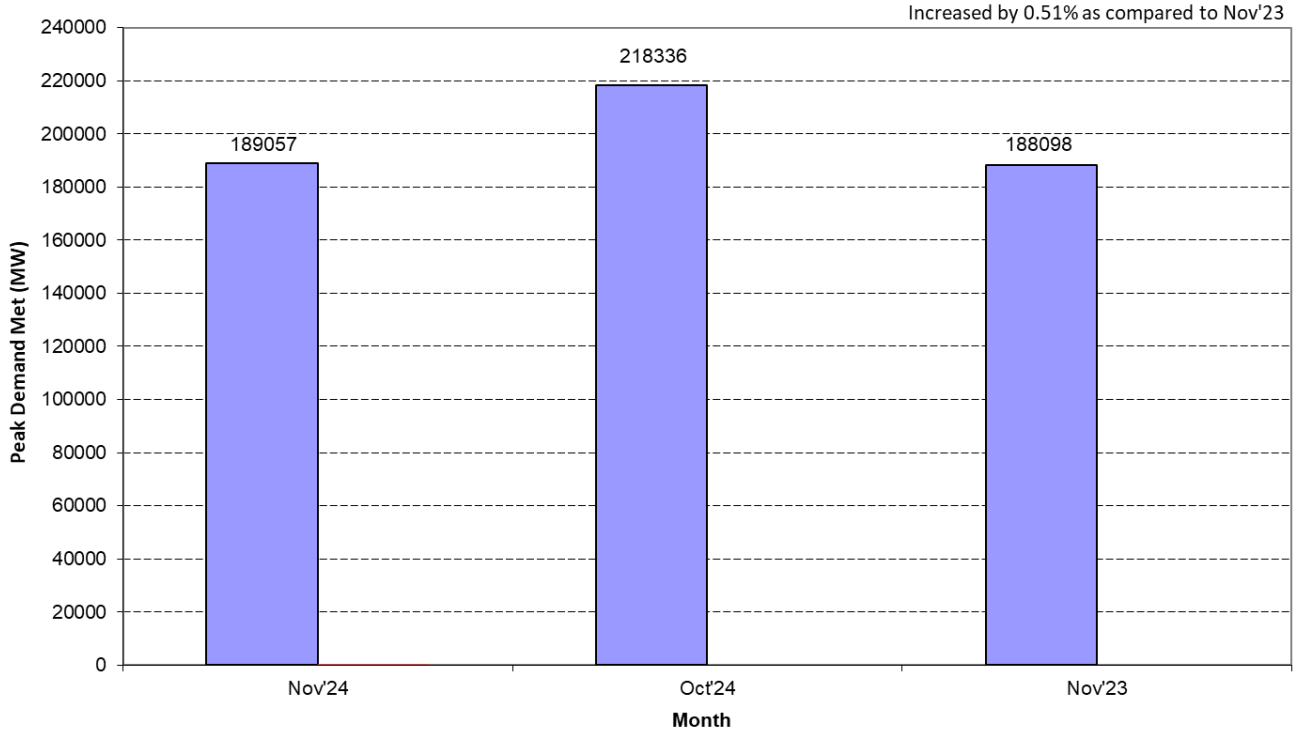


Frequency within IEGC Band

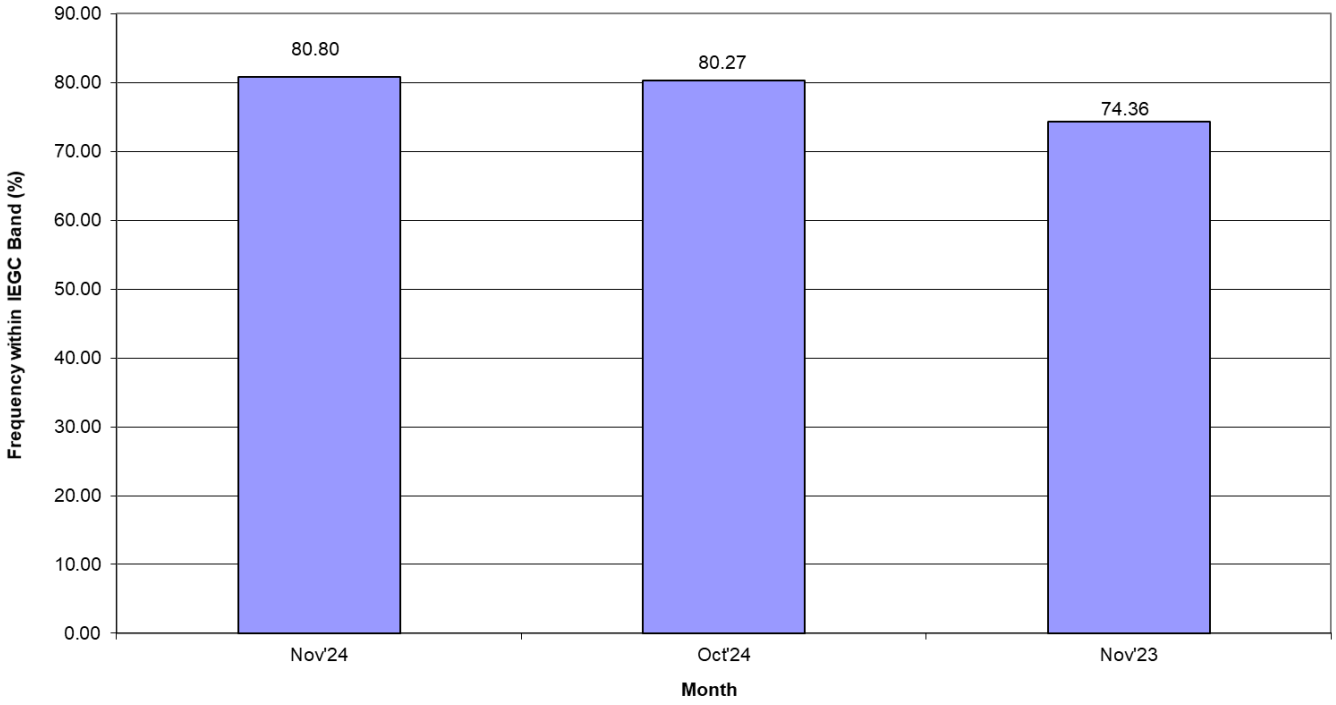


ENERGY MET AT NATIONAL LEVEL (MU)

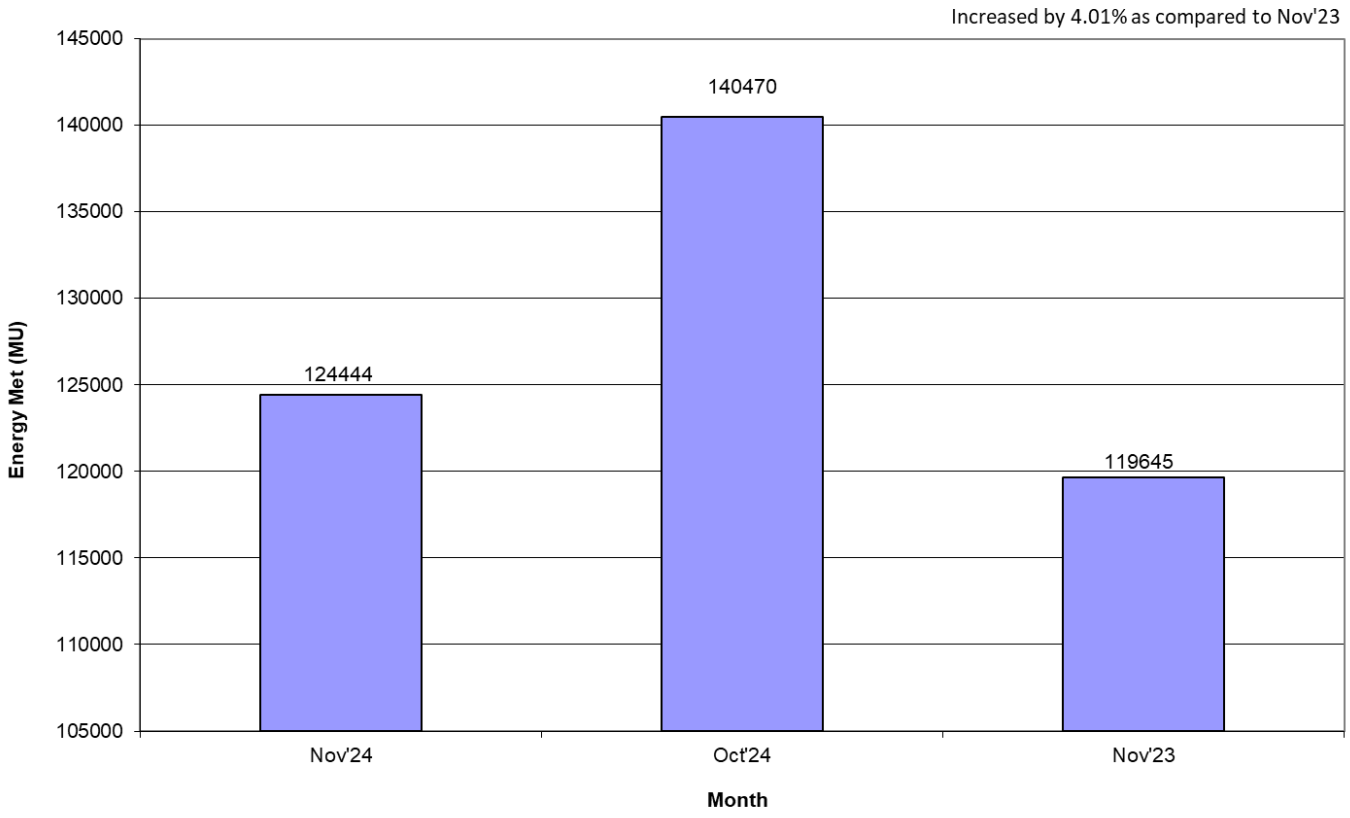


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

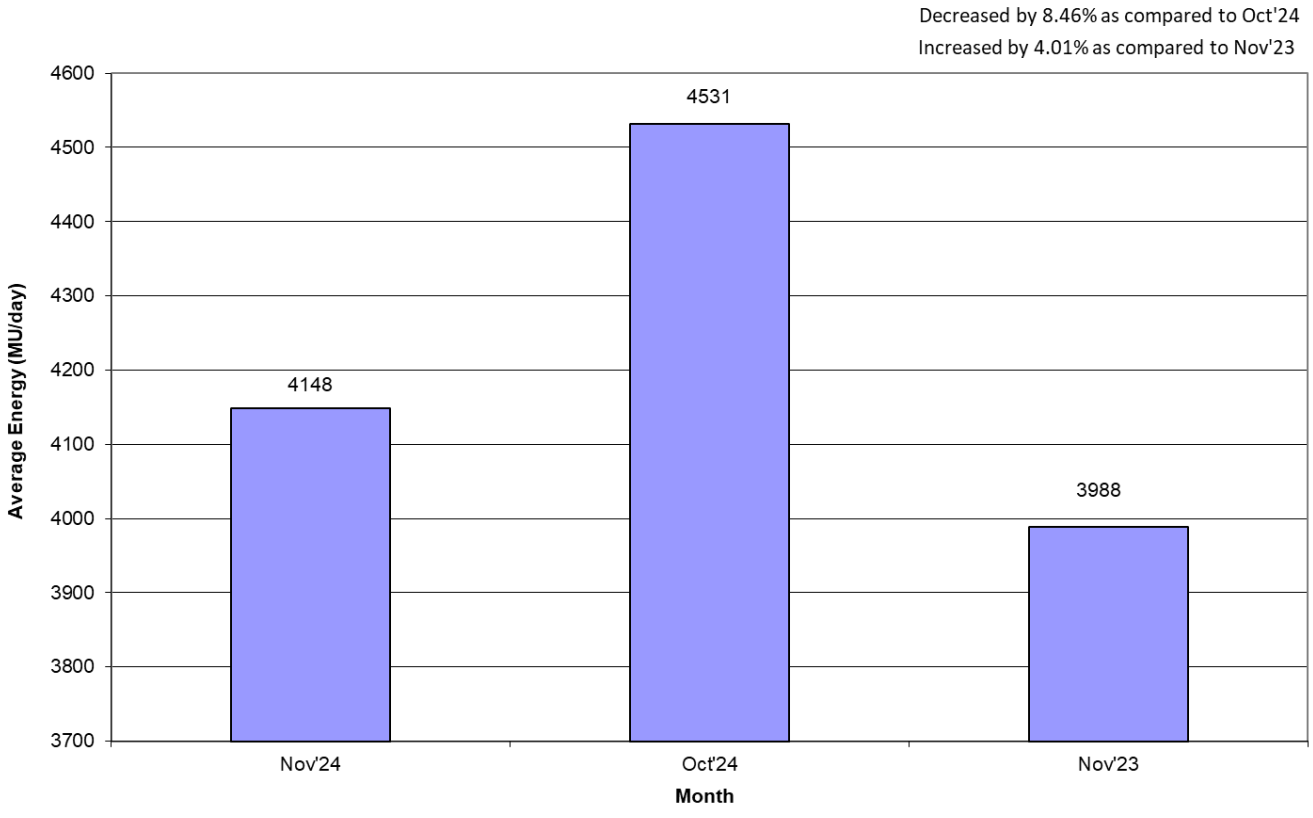

HYDRO GENERATION AT NATIONAL LEVEL (MU)

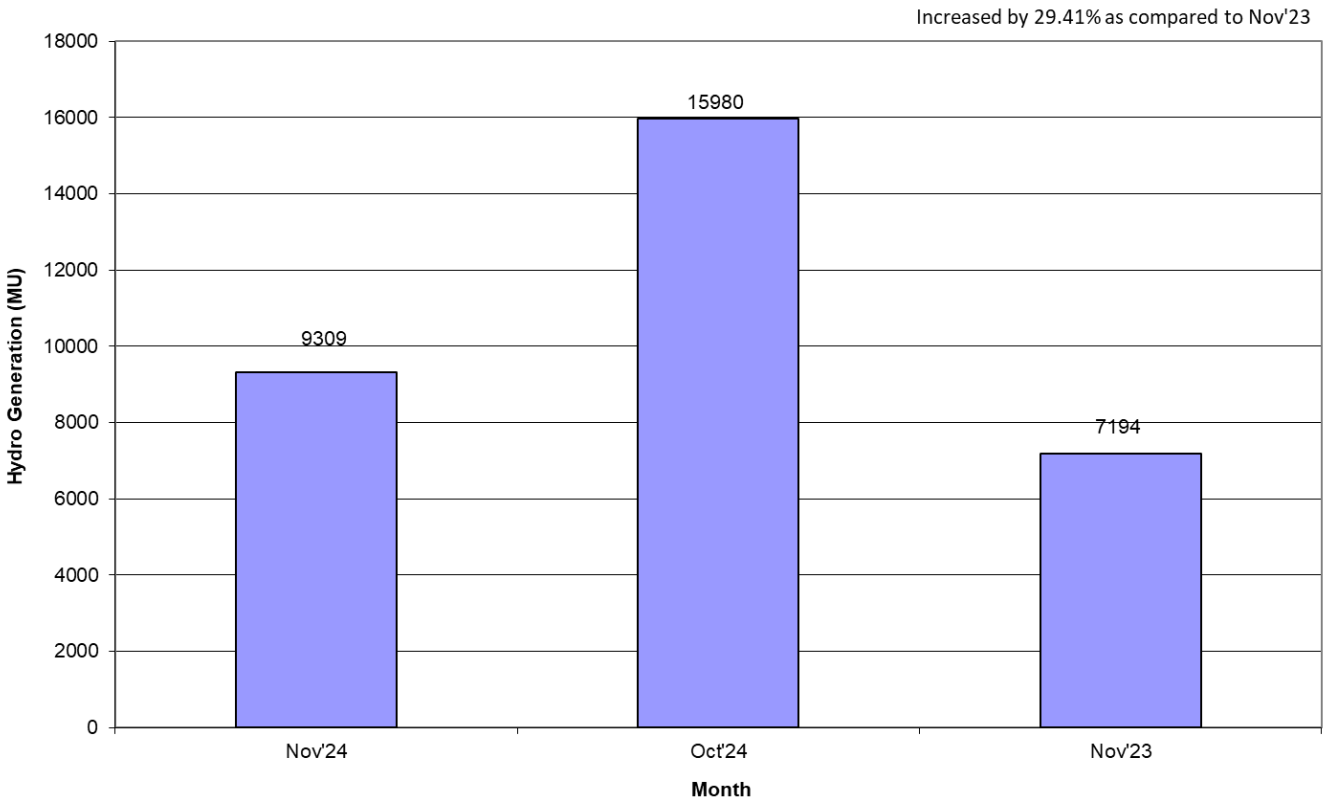


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

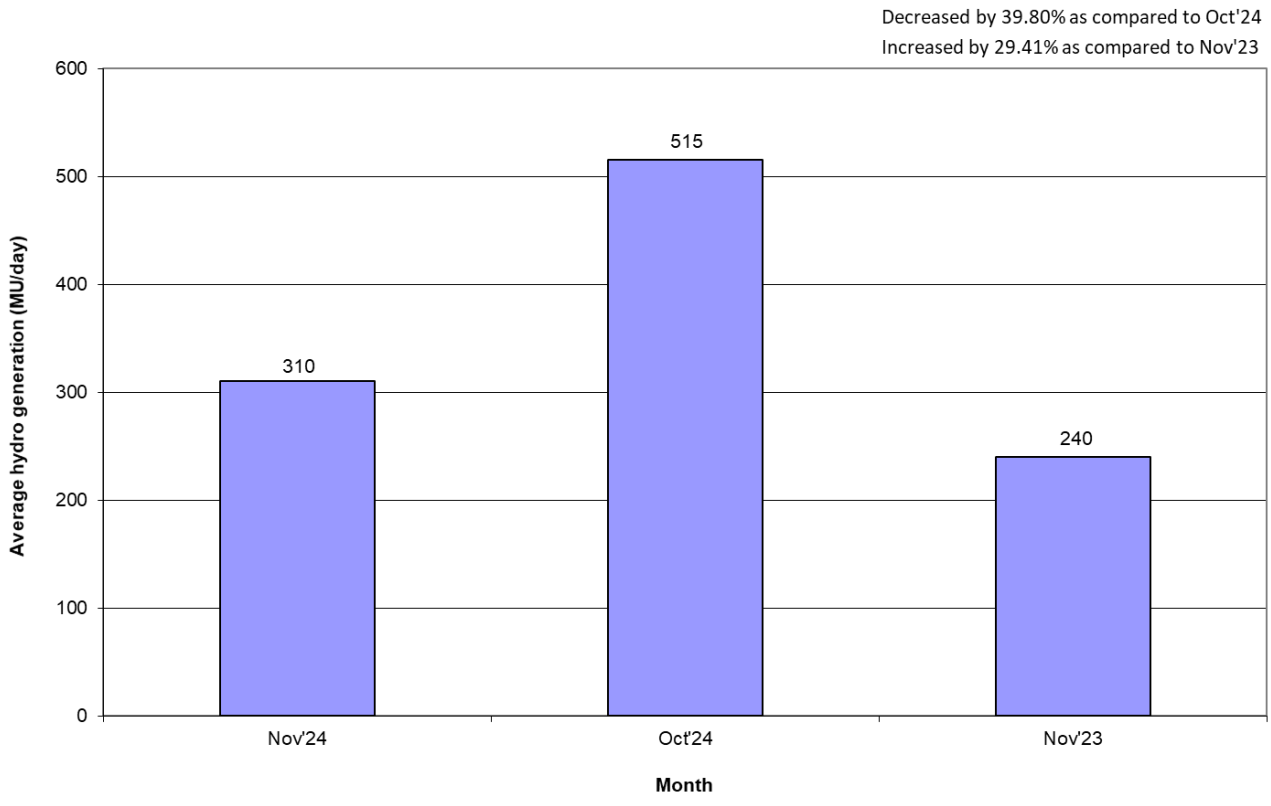

WIND GENERATION AT NATIONAL LEVEL (MU)


Decreased by 15.37% as compared to Nov'23

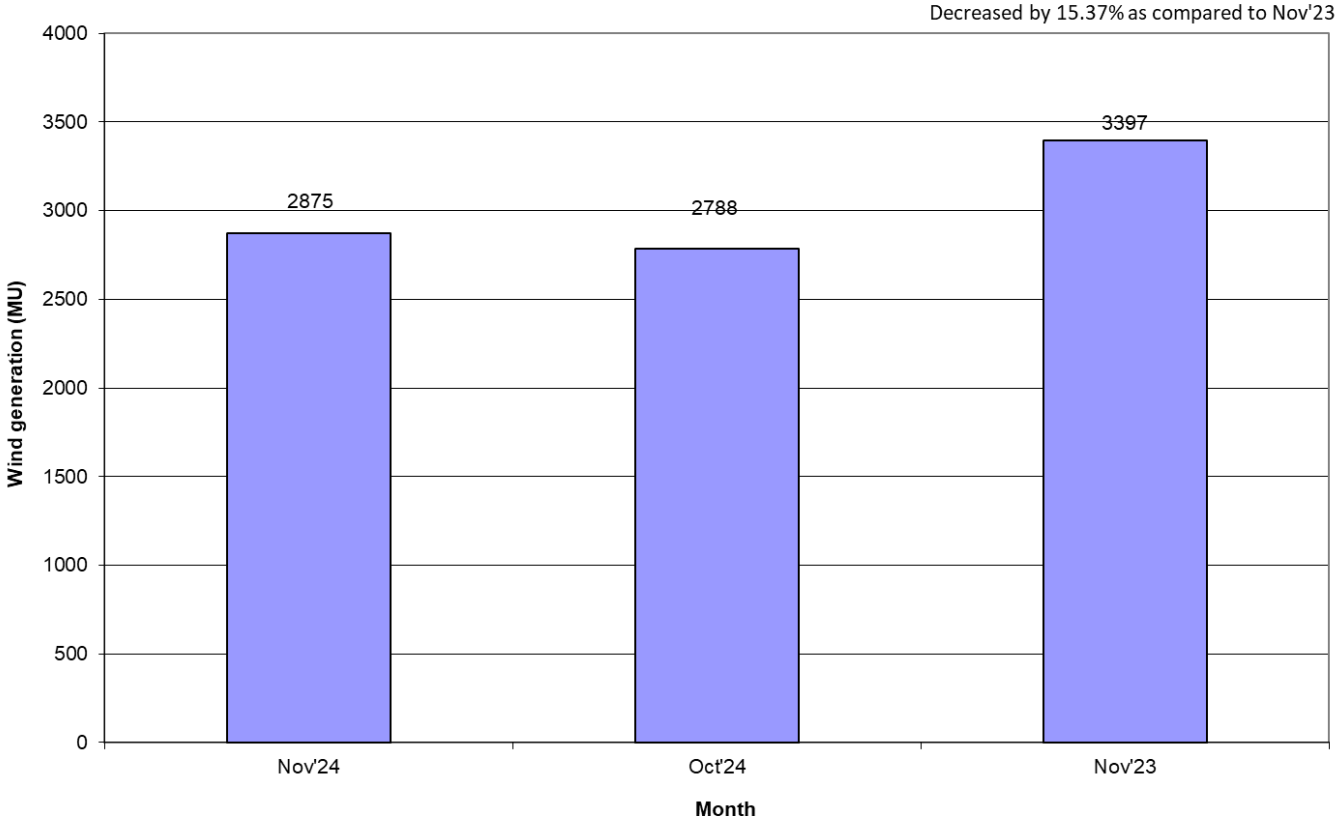


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

Increased by 6.56% as compared to Oct'24


Decreased by 15.37% as compared to Nov'23

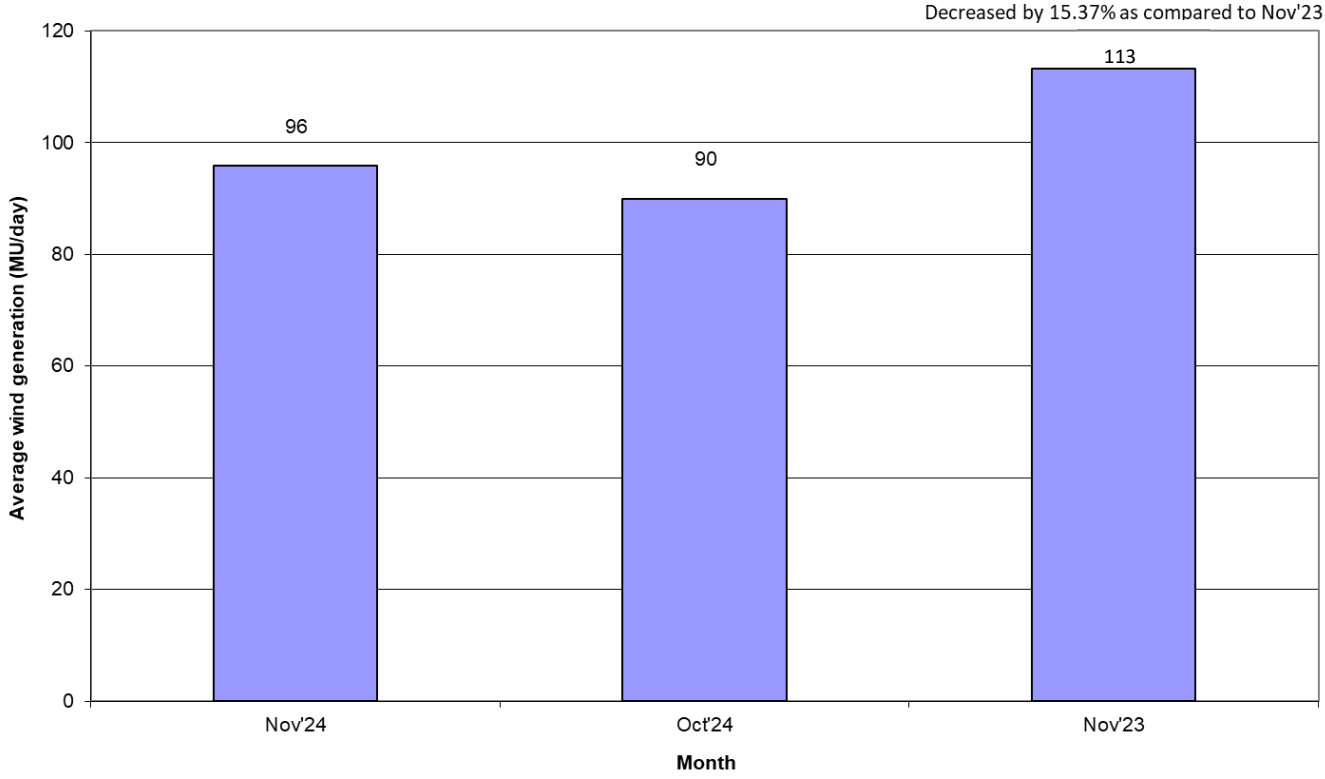

SOLAR GENERATION AT NATIONAL LEVEL (MU)

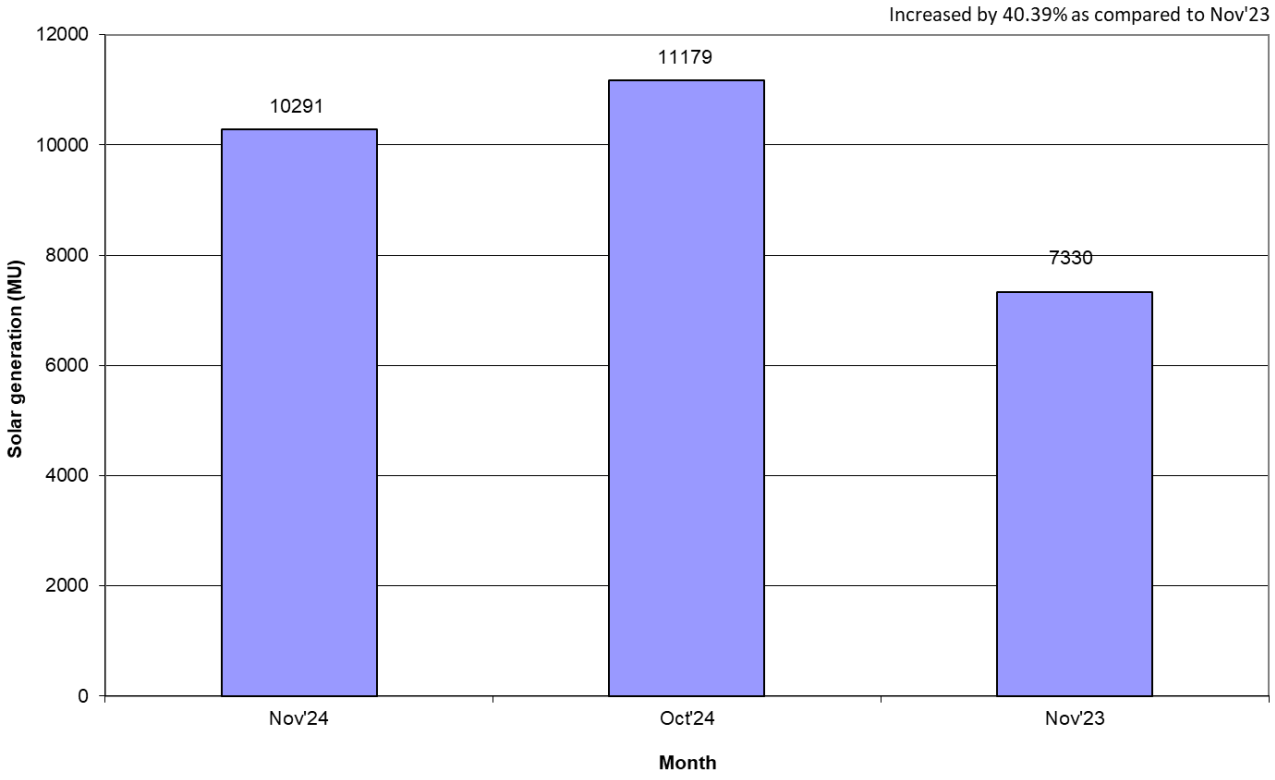

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

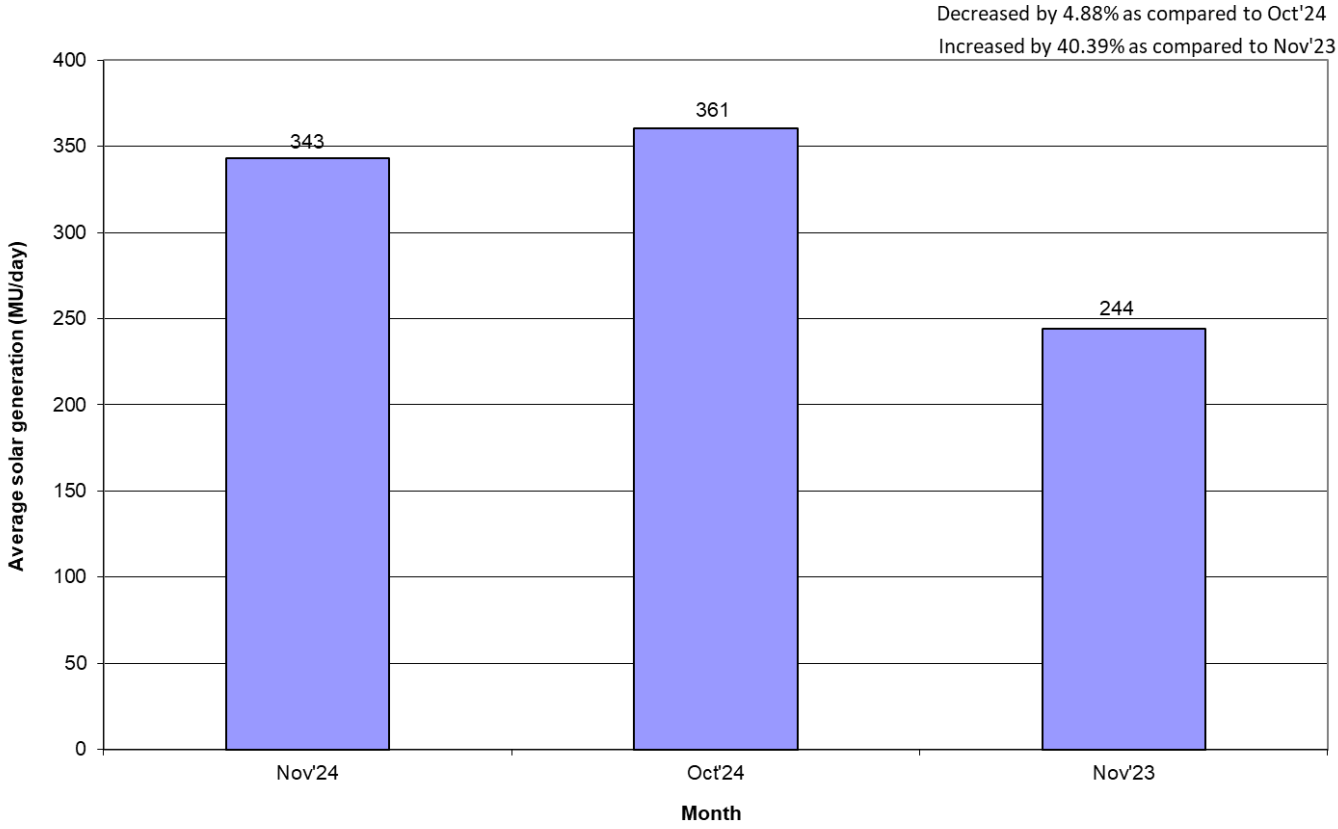

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 30.11.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56658	1580	5995	0	64233	1620	20830	43068	129751
2	WR	74663	1400	10806	0	86869	3240	7563	55200	152871
3	SR	49592	3640	6272	434	59938	3320	11867	57336	132461
4	ER	28875	0	80	0	28955	0	4764	2293	36012
5	NER	1242	0	1665	36	2943	0	1944	615	5502
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	211030	6620	24818	589	243057	8180	46968	158552	456757

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति

EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: नवंबर 2024 MONTH:- NOV 2024


सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Nov-24	47011	49380	39913	25031	2746	164081
2-Nov-24	47611	50182	40998	24507	2860	166158
3-Nov-24	48784	51095	40314	23379	2704	166276
4-Nov-24	53442	56034	44805	23967	2914	181162
5-Nov-24	54584	57774	46384	23869	2771	185382
6-Nov-24	55193	59447	46001	23545	2679	186865
7-Nov-24	54455	60170	45774	22884	2736	186019
8-Nov-24	55500	60869	45836	23248	2738	188191
9-Nov-24	55860	61779	44899	22688	2772	187998
10-Nov-24	52071	58354	41970	21812	2599	176806
11-Nov-24	55343	61730	46508	22736	2740	189057
12-Nov-24	54273	61103	46366	22759	2761	187262
13-Nov-24	53550	61685	45552	22699	2783	186269
14-Nov-24	52953	62096	44233	22084	2706	184072
15-Nov-24	51800	61428	44344	20984	2703	181259
16-Nov-24	52626	62000	43819	20664	2615	181724
17-Nov-24	48992	59260	39473	19584	2488	169797
18-Nov-24	51873	62127	45177	20560	2609	182346
19-Nov-24	52391	61372	44078	20560	2662	181063
20-Nov-24	51940	58928	43712	21256	2633	178469
21-Nov-24	52106	61735	44127	20567	2679	181214
22-Nov-24	51450	61324	44148	20177	2604	179703
23-Nov-24	51147	60239	43260	20230	2566	177442
24-Nov-24	48448	58138	39438	19693	2402	168119
25-Nov-24	52022	60702	43599	20686	2580	179589
26-Nov-24	51969	60902	42532	20372	2649	178424
27-Nov-24	51986	60824	42542	20384	2660	178396
28-Nov-24	52169	61434	43002	20663	2615	179883
29-Nov-24	53225	60962	42943	21213	2669	181012
30-Nov-24	52392	60627	39202	20627	2609	175457
उच्चतम MAXIMUM	55860	62127	46508	25031	2914	189057
निम्नतम MINIMUM	47011	49380	39202	19584	2402	164081
औसत AVERAGE	52239	59457	43498	21781	2675	179650
अब तक का उच्चतम All Time Max.	82312	67482	54798	29695	3787	227354
दिनांक Date	23.07.24	30.05.24	29.04.24	29.05.24	19.09.24	29.05.24

नोट : सभी आंकड़े 1900 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 1900 Hrs

EVENING PEAK HOUR DEMAND(at 1900hrs) MET DURING THE MONTH OF NOVEMBER' 2024

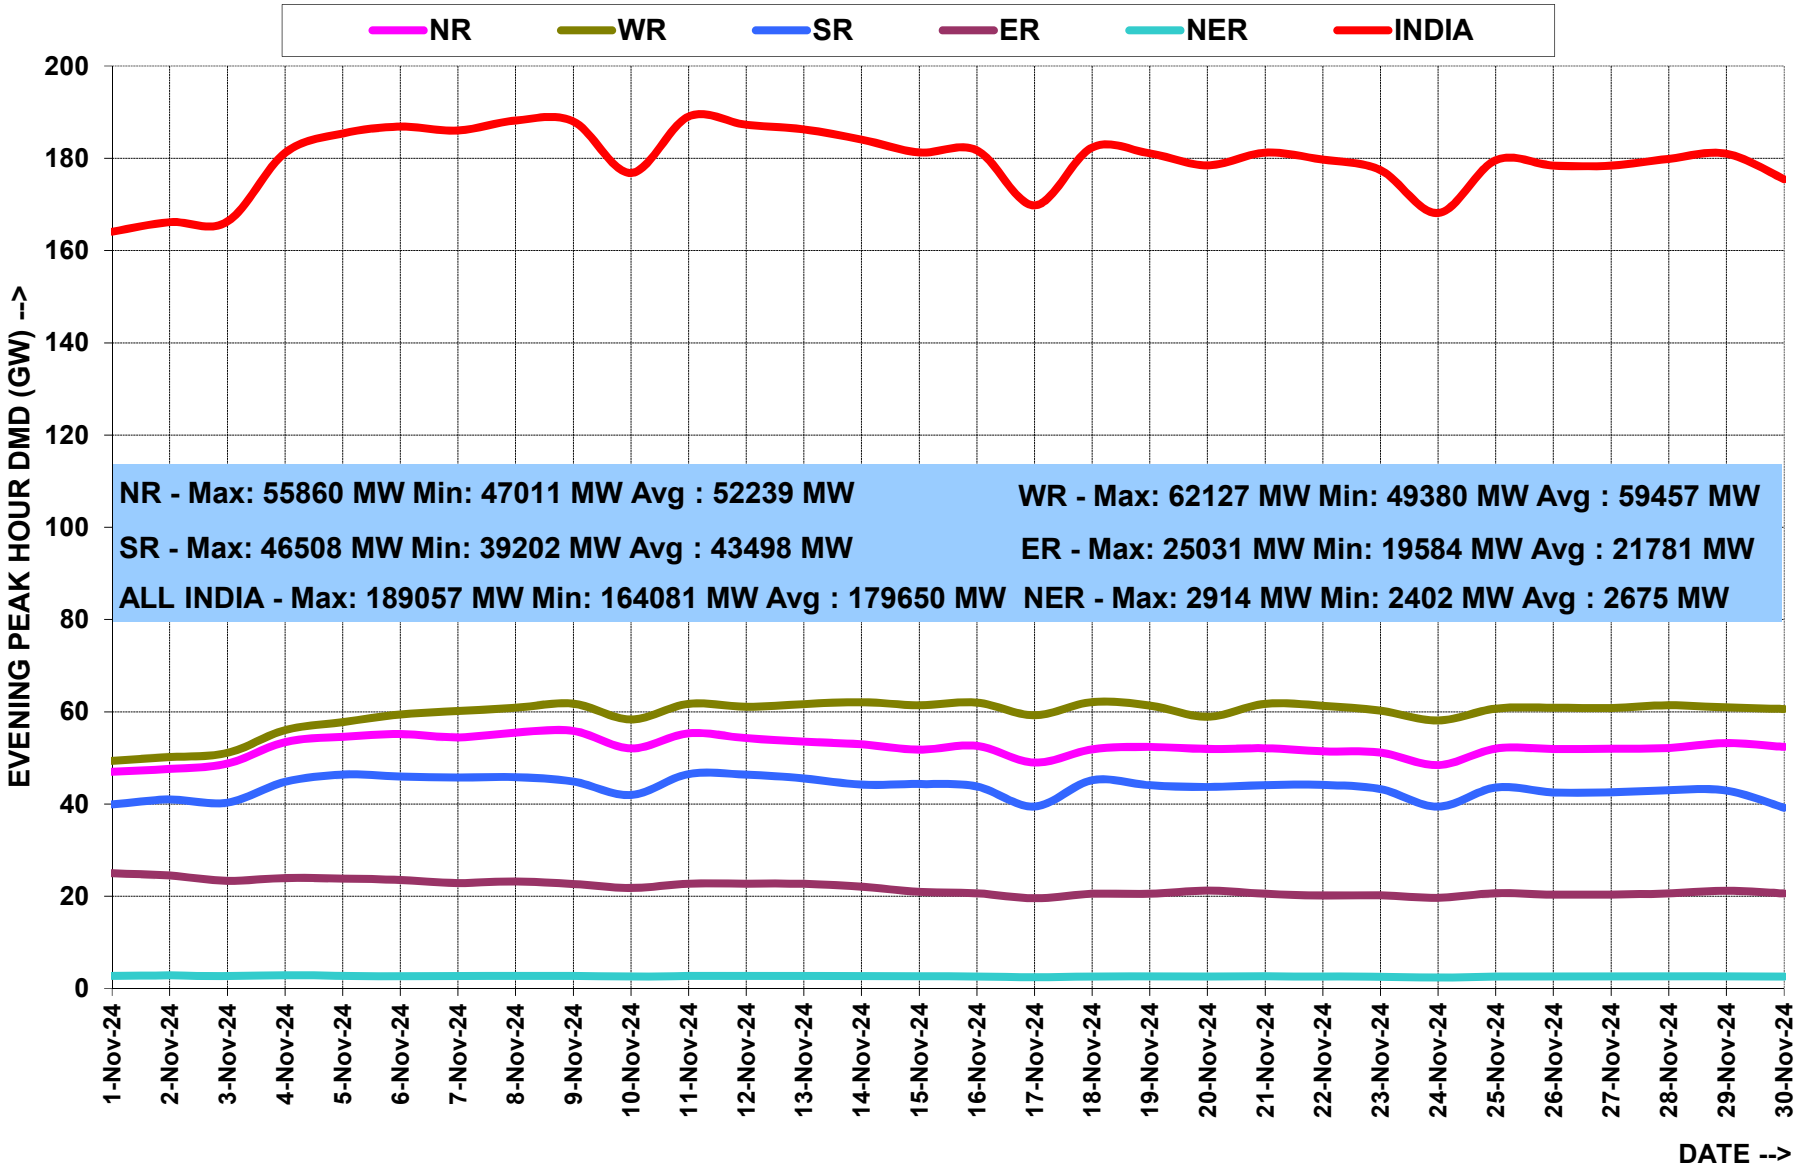


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: नवंबर 2024 MONTH:- NOV 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Nov-24	1098	1193	952	526	51	3819
02-Nov-24	1086	1185	979	516	52	3818
03-Nov-24	1107	1218	956	494	51	3826
04-Nov-24	1182	1317	1033	495	53	4079
05-Nov-24	1221	1372	1064	495	54	4207
06-Nov-24	1242	1409	1088	497	52	4287
07-Nov-24	1238	1435	1096	489	53	4311
08-Nov-24	1245	1453	1098	479	51	4326
09-Nov-24	1252	1460	1098	476	51	4337
10-Nov-24	1195	1425	1045	461	49	4175
11-Nov-24	1229	1472	1112	467	51	4330
12-Nov-24	1235	1481	1120	477	53	4365
13-Nov-24	1212	1478	1095	471	52	4308
14-Nov-24	1188	1494	1083	463	52	4280
15-Nov-24	1181	1497	1058	439	51	4226
16-Nov-24	1157	1499	1025	422	50	4154
17-Nov-24	1109	1454	953	408	47	3972
18-Nov-24	1135	1490	1021	411	47	4103
19-Nov-24	1145	1495	1046	420	50	4156
20-Nov-24	1146	1437	1044	435	49	4111
21-Nov-24	1139	1470	1048	431	49	4137
22-Nov-24	1147	1479	1067	419	49	4161
23-Nov-24	1142	1476	1074	421	47	4160
24-Nov-24	1096	1432	1009	416	46	4000
25-Nov-24	1132	1458	1065	422	47	4124
26-Nov-24	1149	1463	1061	420	48	4141
27-Nov-24	1165	1462	1033	414	49	4123
28-Nov-24	1160	1462	1044	418	49	4133
29-Nov-24	1167	1461	1062	430	45	4164
30-Nov-24	1169	1460	1004	430	49	4113
कुल TOTAL	35066	42885	31435	13562	1496	124444
उच्चतम MAXIMUM	1252	1499	1120	526	54	4365
निम्नतम MINIMUM	1086	1185	952	408	45	3818
औसत AVERAGE	1169	1429	1048	452	50	4148
संचयी 2024-25 Cumulative 2024-25	371506	349811	277063	141140	14588	1154107
अब तक का उच्चतम All Time Max.	1990	1648	1416	692	80	5466
दिनांक Date	18.06.24	06.05.24	05.04.24	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF NOVEMBER' 2024

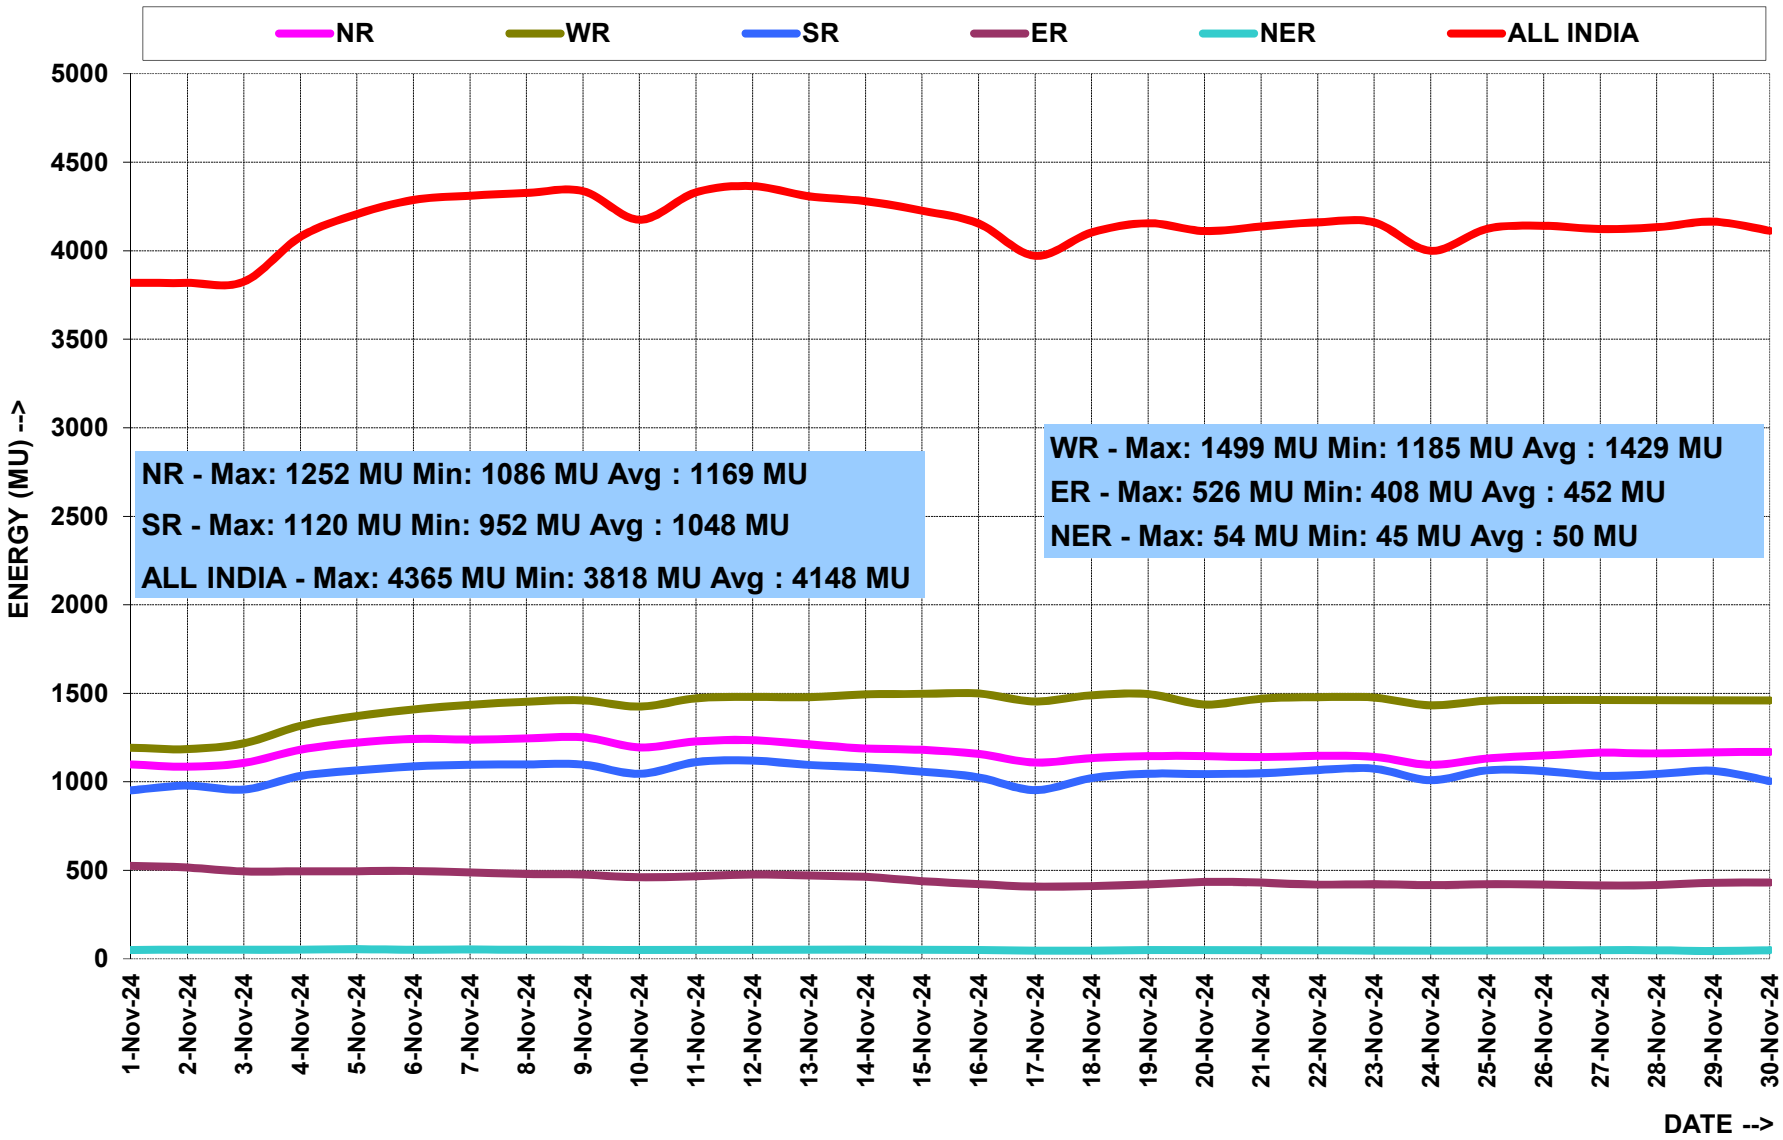

5. वर्ष 2024-25 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID								
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19	50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47	50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32	50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17	50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33	50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78	50.38	49.46	50.00
	Oct-24	All India Grid	4.86	80.27	14.87	50.39	49.58	50.00
	Nov-24	All India Grid	5.15	80.80	14.05	50.32	49.55	50.00
	2024-25 (upto Nov)	**All India Grid**	**4.92**	**78.67**	**16.41**	**50.67**	**49.46**	**50.00**

5.1 नवंबर 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR NOVEMBER 2024

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Nov-24	1.55	78.06	20.39		50.24	49.82	50.02	0.03
	02-Nov-24	0.98	74.79	24.22		50.32	49.83	50.02	0.04
	03-Nov-24	2.92	84.62	12.47		50.17	49.85	49.99	0.03
	04-Nov-24	3.39	81.90	14.71		50.23	49.80	50.00	0.03
	05-Nov-24	7.55	81.35	11.10		50.26	49.78	49.99	0.04
	06-Nov-24	3.16	84.64	12.20		50.20	49.80	50.00	0.02
	07-Nov-24	0.75	83.58	15.67		50.30	49.80	50.01	0.02
	08-Nov-24	7.43	84.22	8.34		50.18	49.76	49.98	0.03
	09-Nov-24	7.66	83.34	8.99		50.17	49.68	49.99	0.03
	10-Nov-24	6.93	78.45	14.62		50.24	49.79	49.99	0.03
	11-Nov-24	12.66	72.97	14.36		50.16	49.75	49.98	0.05
	12-Nov-24	12.05	77.65	10.30		50.13	49.63	49.98	0.05
	13-Nov-24	0.78	84.13	15.09		50.31	49.86	50.01	0.02
	14-Nov-24	5.27	89.16	5.58		50.17	49.79	49.98	0.03
	15-Nov-24	10.54	77.16	12.29		50.25	49.74	49.98	0.04
	16-Nov-24	7.04	79.76	13.21		50.20	49.68	49.99	0.04
	17-Nov-24	6.30	75.50	18.21		50.25	49.73	50.00	0.04
	18-Nov-24	1.92	76.34	21.74		50.16	49.86	50.01	0.03
	19-Nov-24	2.06	83.32	14.62		50.19	49.86	50.01	0.02
	20-Nov-24	1.23	84.09	14.69		50.22	49.84	50.01	0.02
	21-Nov-24	2.44	87.40	10.16		50.20	49.83	49.99	0.02
	22-Nov-24	3.99	80.41	15.60		50.23	49.72	50.00	0.03
	23-Nov-24	4.11	87.01	8.88		50.30	49.72	49.99	0.03
	24-Nov-24	4.13	82.89	12.97		50.27	49.75	50.00	0.03
	25-Nov-24	10.89	75.94	13.17		50.20	49.64	49.99	0.05
	26-Nov-24	9.95	79.07	10.97		50.25	49.64	49.98	0.05
	27-Nov-24	5.41	79.04	15.56		50.22	49.55	50.00	0.05
	28-Nov-24	3.95	79.75	16.31		50.20	49.77	50.00	0.03
	29-Nov-24	6.55	77.85	15.60		50.25	49.66	49.99	0.04
	30-Nov-24	0.96	79.65	19.39		50.30	49.84	50.01	0.03


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: नवंबर 2024 MONTH:- NOV 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Nov-24	139	24	121	51	25	361
02-Nov-24	139	27	123	51	25	364
03-Nov-24	136	24	125	48	23	356
04-Nov-24	139	30	125	47	23	364
05-Nov-24	137	29	126	49	24	364
06-Nov-24	138	38	112	47	21	356
07-Nov-24	138	32	110	45	22	346
08-Nov-24	140	36	119	44	20	360
09-Nov-24	133	39	112	47	20	351
10-Nov-24	132	34	88	45	19	318
11-Nov-24	132	45	99	35	19	329
12-Nov-24	127	43	99	40	18	327
13-Nov-24	123	36	79	33	18	289
14-Nov-24	121	40	81	30	18	290
15-Nov-24	120	48	83	28	17	296
16-Nov-24	117	39	81	27	17	282
17-Nov-24	116	32	72	24	17	261
18-Nov-24	116	41	76	28	16	277
19-Nov-24	112	37	83	25	17	275
20-Nov-24	112	32	91	27	17	279
21-Nov-24	111	36	103	26	16	292
22-Nov-24	112	37	96	28	16	289
23-Nov-24	110	37	99	27	16	289
24-Nov-24	110	34	86	23	15	268
25-Nov-24	110	38	97	24	16	285
26-Nov-24	109	40	102	26	16	293
27-Nov-24	109	44	97	23	16	289
28-Nov-24	110	40	86	25	16	276
29-Nov-24	109	38	109	24	15	296
30-Nov-24	111	39	104	21	15	289
कुल TOTAL	3668	1086	2983	1018	555	9309
उच्चतम MAXIMUM	140	48	126	51	25	364
निम्नतम MINIMUM	109	24	72	21	15	261
औसत AVERAGE	122	36	99	34	19	310
संचयी 2024-25 Cumulative 2024-25	66897	15199	25074	14146	6445	127761
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

HYDRO ENERGY DURING THE MONTH OF NOVEMBER' 2024

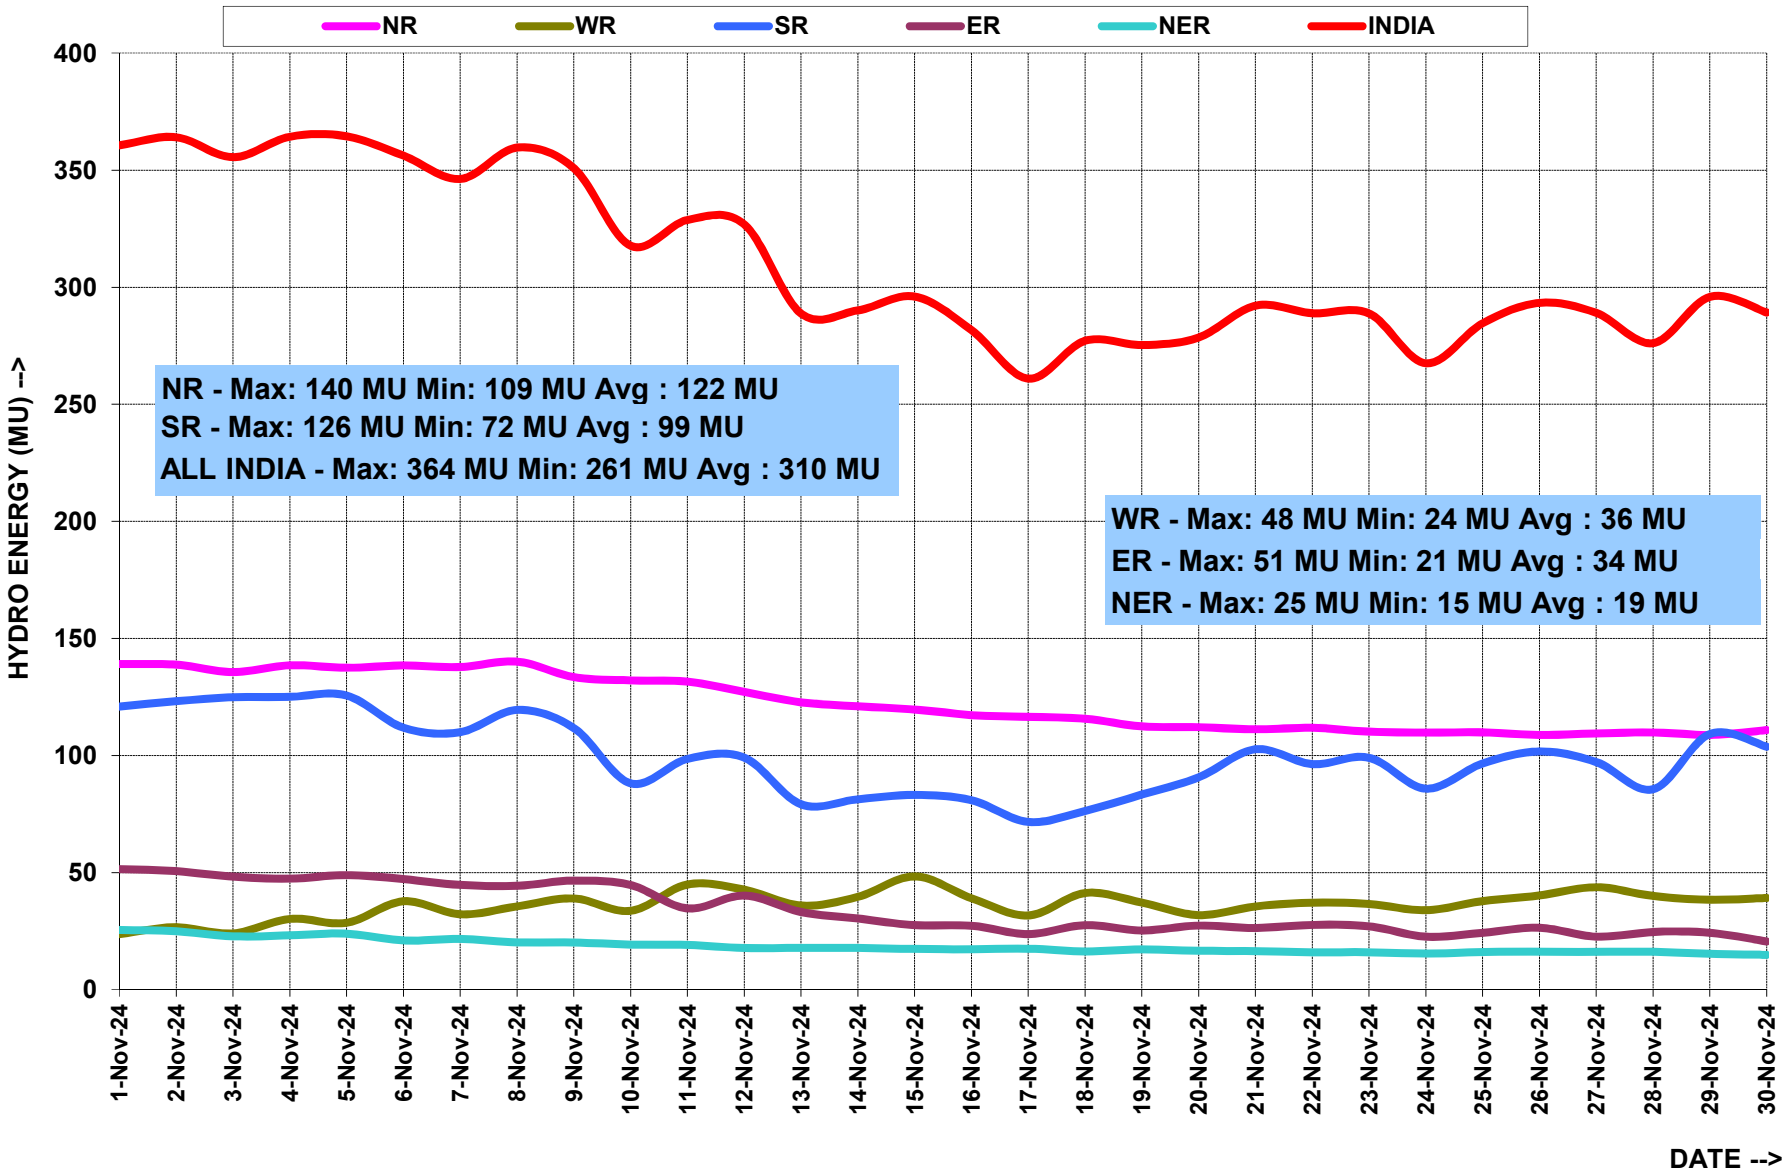

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन

WIND GENERATION AT NATIONAL LEVEL

माह: नवंबर 2024 MONTH:- NOV 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Nov-24	3	30	20	----------	----------	53
02-Nov-24	9	23	26	----------	----------	58
03-Nov-24	8	22	30	----------	----------	61
04-Nov-24	4	23	32	----------	----------	59
05-Nov-24	3	39	27	----------	----------	69
06-Nov-24	6	59	23	----------	----------	87
07-Nov-24	9	45	26	----------	----------	80
08-Nov-24	13	32	37	----------	----------	83
09-Nov-24	8	34	40	----------	----------	83
10-Nov-24	5	39	41	----------	----------	86
11-Nov-24	5	42	37	----------	----------	84
12-Nov-24	7	38	35	----------	----------	80
13-Nov-24	3	48	64	----------	----------	116
14-Nov-24	4	41	47	----------	----------	93
15-Nov-24	2	21	30	----------	----------	53
16-Nov-24	4	28	53	----------	----------	85
17-Nov-24	12	58	57	----------	----------	127
18-Nov-24	7	69	73	----------	----------	150
19-Nov-24	4	62	54	----------	----------	121
20-Nov-24	5	59	68	----------	----------	132
21-Nov-24	2	43	45	----------	----------	91
22-Nov-24	4	39	44	----------	----------	87
23-Nov-24	4	28	40	----------	----------	72
24-Nov-24	4	42	44	----------	----------	90
25-Nov-24	7	66	53	----------	----------	126
26-Nov-24	2	64	35	----------	----------	101
27-Nov-24	1	48	40	----------	----------	89
28-Nov-24	7	70	55	----------	----------	132
29-Nov-24	14	81	47	----------	----------	142
30-Nov-24	7	100	80	----------	----------	187
कुल TOTAL	174	1394	1307	----------	----------	2875
उच्चतम MAXIMUM	14	100	80	----------	----------	187
निम्नतम MINIMUM	1	21	20	----------	----------	53
औसत AVERAGE	6	46	44	----------	----------	96
संचयी 2024-25 Cumulative 2024-25	4866	25955	29122	----------	----------	59943
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: नवंबर 2024 MONTH:- NOV 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Nov-24	148	95	110	2.9	0.6	357
02-Nov-24	157	99	112	3.1	0.8	372
03-Nov-24	154	97	118	3.3	0.9	374
04-Nov-24	152	96	109	3.5	0.9	362
05-Nov-24	150	96	127	3.3	0.8	376
06-Nov-24	149	92	130	2.9	0.7	374
07-Nov-24	151	90	118	3.3	0.7	363
08-Nov-24	150	91	106	3.3	1.0	352
09-Nov-24	142	91	118	3.2	1.1	356
10-Nov-24	147	91	127	2.8	1.1	369
11-Nov-24	151	91	126	3.5	1.1	373
12-Nov-24	146	95	98	3.2	1.1	344
13-Nov-24	142	92	89	3.1	1.0	327
14-Nov-24	140	87	85	3.6	1.1	316
15-Nov-24	126	86	82	3.2	1.1	298
16-Nov-24	125	88	102	3.4	1.1	319
17-Nov-24	132	93	103	3.4	1.1	334
18-Nov-24	147	93	103	3.4	1.1	347
19-Nov-24	147	92	98	3.1	1.2	341
20-Nov-24	149	90	89	2.9	1.1	332
21-Nov-24	150	89	98	2.9	1.1	340
22-Nov-24	148	86	123	2.8	1.0	361
23-Nov-24	143	86	115	2.7	0.9	346
24-Nov-24	139	86	104	2.6	0.8	332
25-Nov-24	134	88	101	2.8	1.0	327
26-Nov-24	135	92	71	2.9	1.1	303
27-Nov-24	144	93	75	2.5	1.1	316
28-Nov-24	149	92	115	2.7	1.1	359
29-Nov-24	147	91	88	2.8	1.1	329
30-Nov-24	135	86	67	1.5	1.1	290
कुल TOTAL	4330	2733	3107	91	30	10291
उच्चतम MAXIMUM	157	99	130	3.6	1.2	376
निम्नतम MINIMUM	125	86	67	1.5	0.6	290
औसत AVERAGE	144	91	104	3.0	1.0	343
संचयी 2024-25 Cumulative 2024-25	37047	19698	27550	722	226.2	85243
अब तक का उच्चतम All Time Max.	186	106	149	4.1	3.5	426
दिनांक Date	01.05.24	07.10.24	31.03.24	09.06.24	08.09.24	30.04.24

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति

DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: नवंबर 2024 MONTH:- NOV 2024

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL		विभिन्नता फ़ैक्टर Diversity Factor*
01-Nov-24	50527	52554	45779	25733	2978	171519		1.035
02-Nov-24	51363	51900	46844	25889	3073	173372		1.033
03-Nov-24	51781	54215	44036	23915	2904	171952		1.028
04-Nov-24	57209	60304	48689	24710	3152	189942		1.022
05-Nov-24	58964	62382	49961	24732	3036	194137		1.025
06-Nov-24	59530	64778	50935	24940	2955	198374		1.024
07-Nov-24	58632	65934	51762	23536	2992	199121		1.019
08-Nov-24	59699	66706	51727	23930	2965	199924		1.026
09-Nov-24	59224	67149	52072	23439	3008	198426		1.033
10-Nov-24	55851	65332	48950	22789	2822	191376		1.023
11-Nov-24	58967	68222	53101	23700	2987	201924		1.025
12-Nov-24	59006	68595	52921	23995	3073	201977		1.028
13-Nov-24	58692	68155	51066	23582	3041	199261		1.026
14-Nov-24	57359	69305	52037	23148	2963	199347		1.027
15-Nov-24	58990	71020	50011	22272	2958	200165		1.025
16-Nov-24	57219	70189	47371	21902	2912	194384		1.027
17-Nov-24	55298	67511	44502	21010	2643	185797		1.028
18-Nov-24	56887	70424	48761	21648	2807	195580		1.025
19-Nov-24	57396	70922	49077	22005	2868	197349		1.025
20-Nov-24	57693	67675	50198	22695	2904	196812		1.022
21-Nov-24	57517	70585	50390	22057	2862	199420		1.020
22-Nov-24	59622	71222	52191	21783	2816	203813		1.019
23-Nov-24	58533	71498	52971	21315	2794	203771		1.016
24-Nov-24	56989	70133	49519	20741	2621	196507		1.018
25-Nov-24	59010	71643	52768	21539	2807	203846		1.019
26-Nov-24	59033	70863	53698	21399	2845	203890		1.019
27-Nov-24	60352	70991	50956	21181	2944	202356		1.020
28-Nov-24	59437	71250	51686	21509	2902	203102		1.018
29-Nov-24	61434	71647	53804	21652	2876	207429		1.019
30-Nov-24	61088	72385	50694	21721	2836	205301		1.017
उच्चतम MAXIMUM	61434	72385	53804	25889	3152	207429		1.035
निम्नतम MINIMUM	50527	51900	44036	20741	2621	171519		1.016
औसत AVERAGE	57777	67183	50283	22816	2911	196339		1.024
अब तक का उच्चतम All Time Max.	91215	74974	68735	32531	3905	250070		
दिनांक Date	19.06.24	01.06.24	13.03.24	10.06.24	19.09.24	30.05.24		


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 29th NOV (MAXIMUM DEMAND MET)

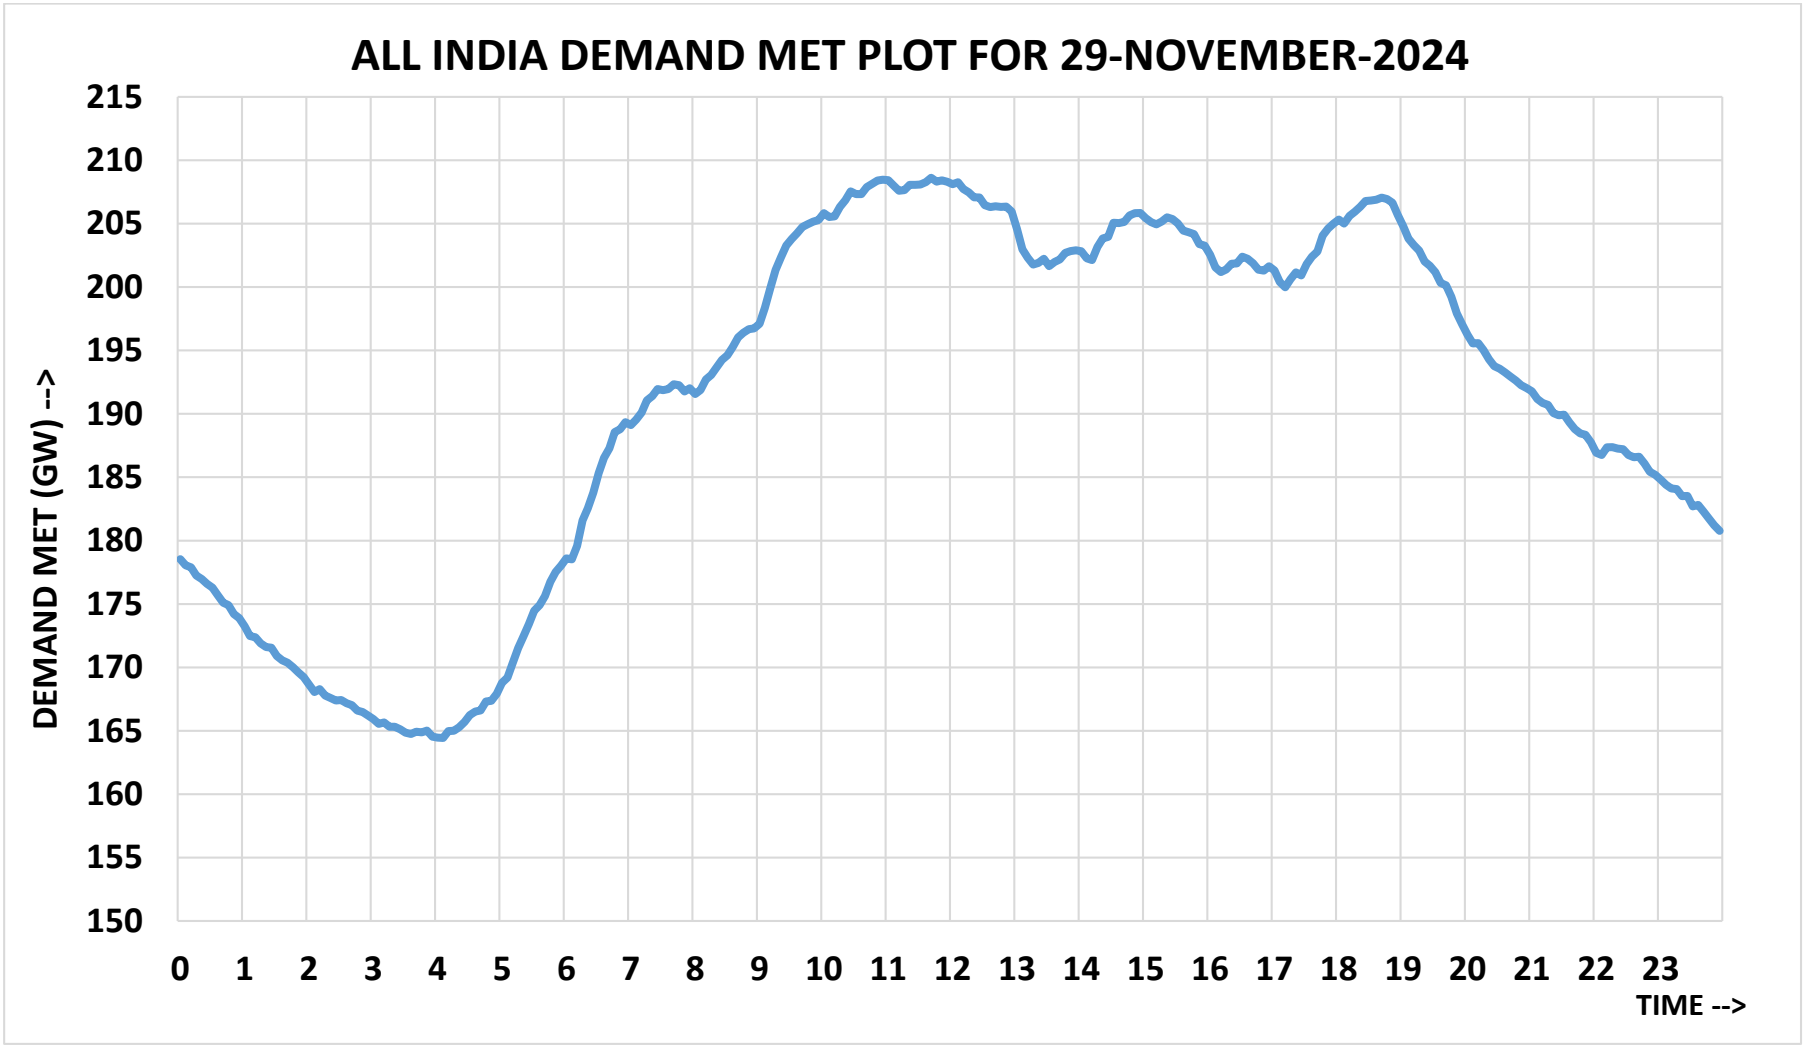

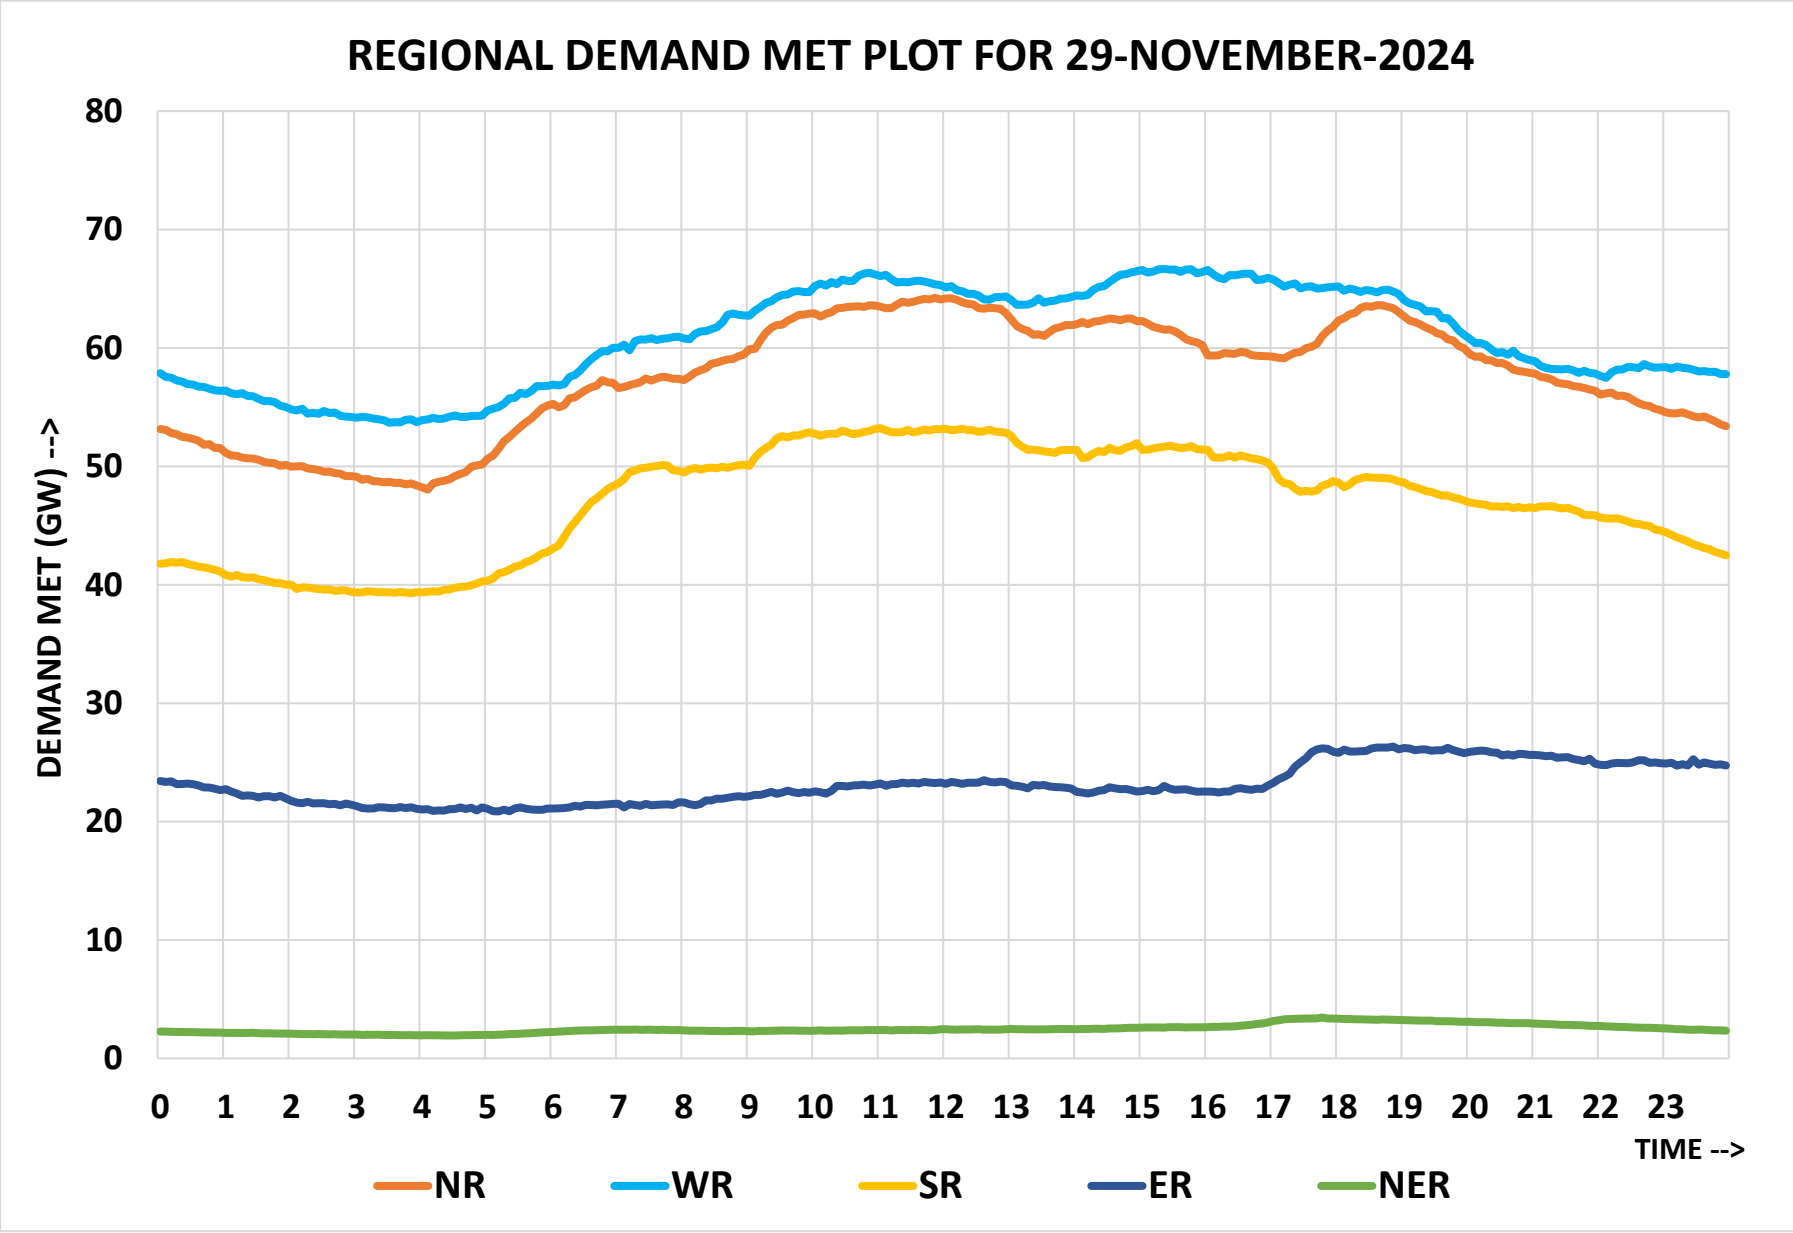
REGIONAL DEMAND MET PLOT FOR 29-NOVEMBER-2024
DEMAND MET (GW) -->
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

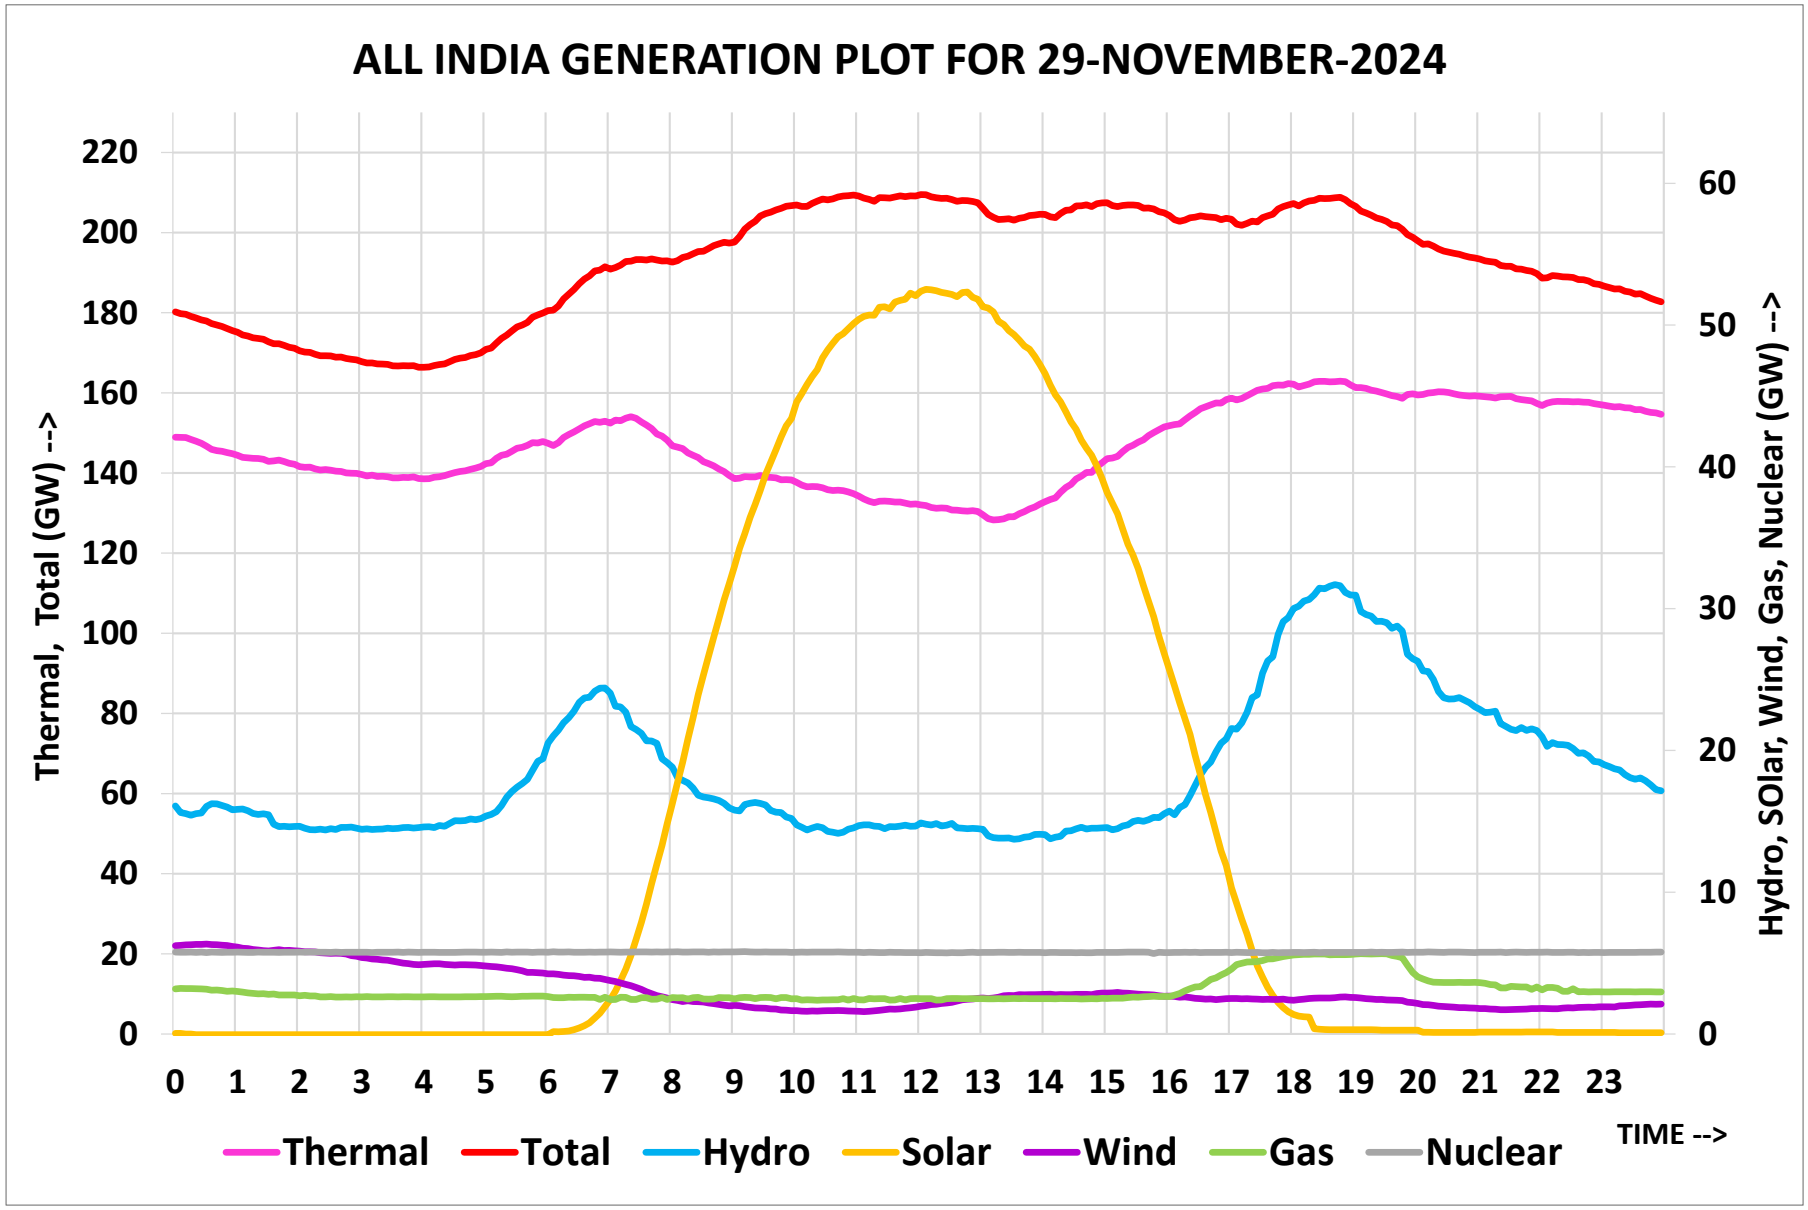
ALL INDIA GENERATION PLOT FOR 29-NOVEMBER-2024
Thermal, Total (GW) -->
Hydro, SOlar, Wind, Gas, Nuclear (GW) -->
TIME -->
Thermal
Total
Hydro
Solar
Wind
Gas
Nuclear

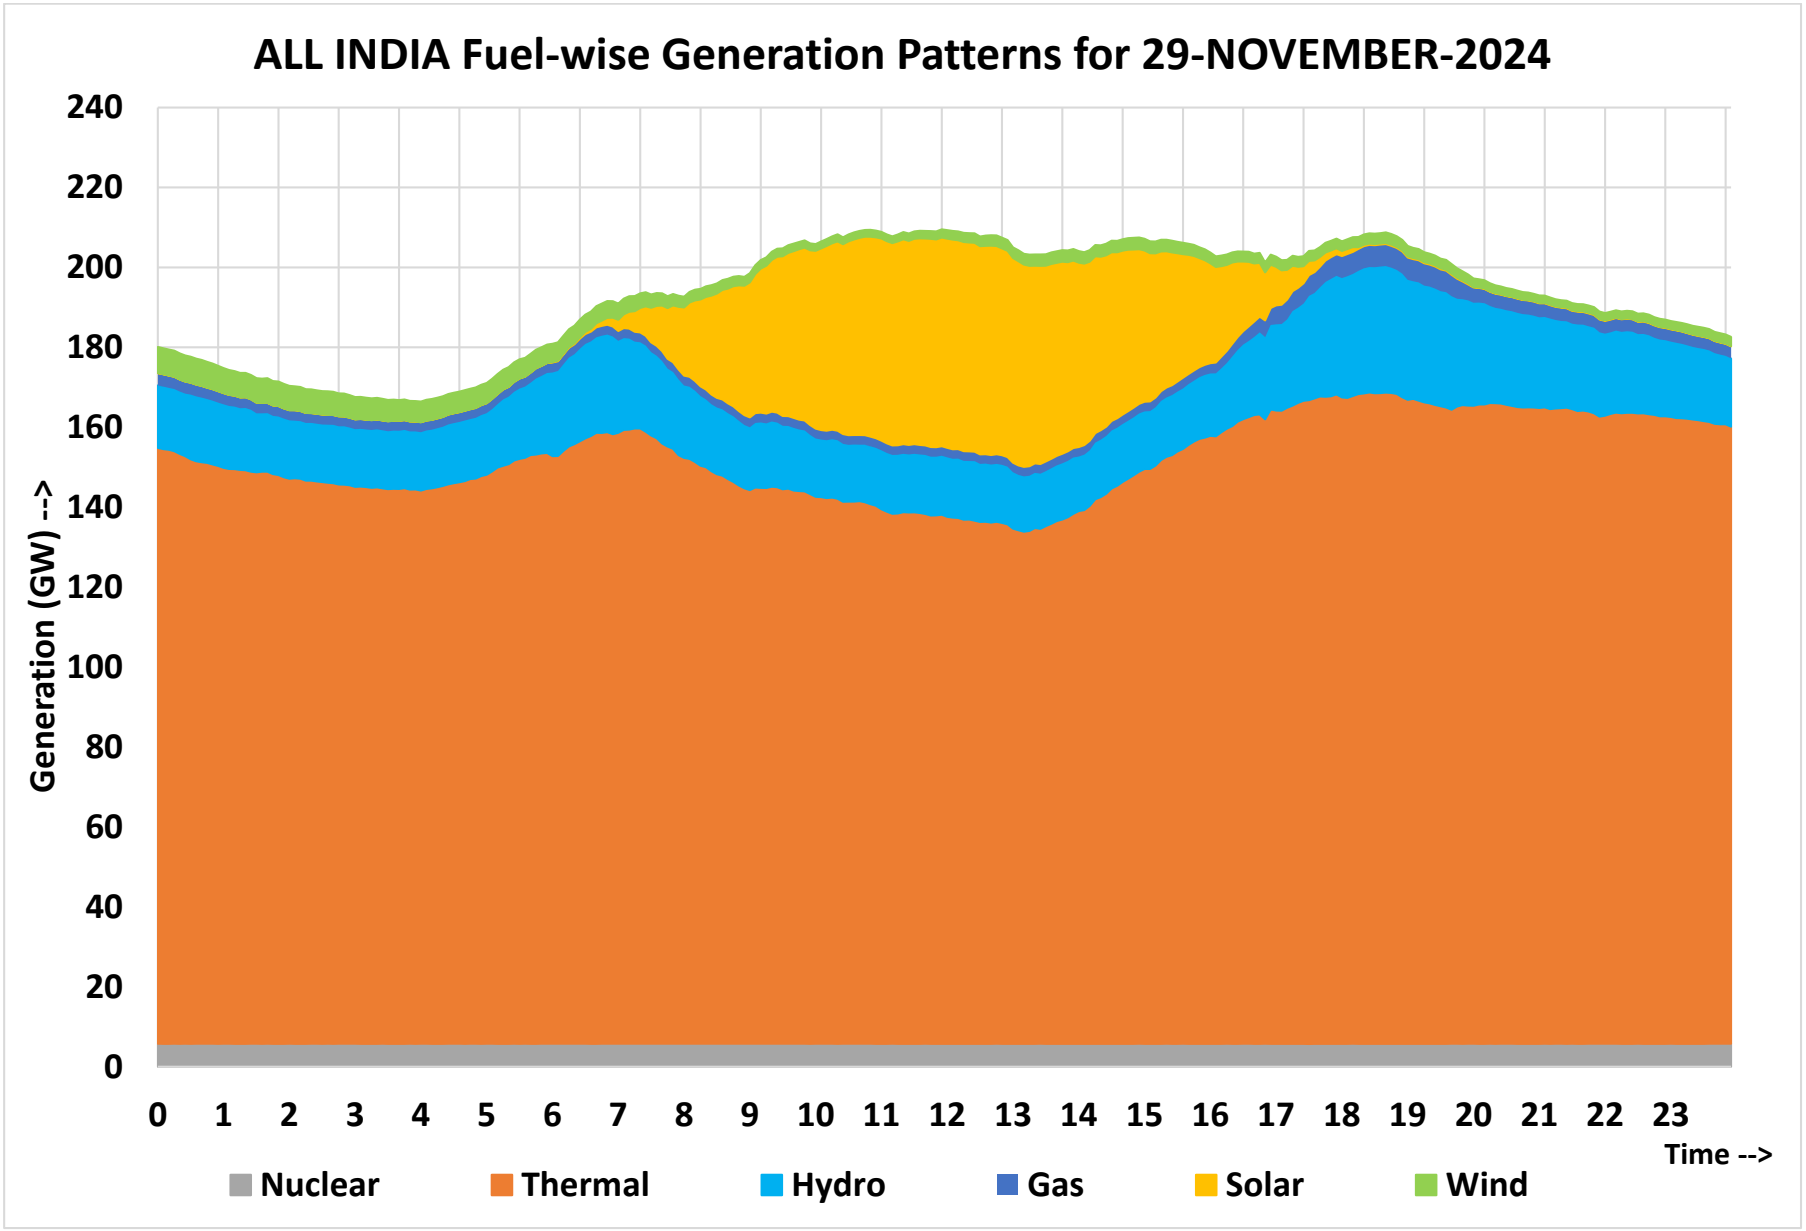
ALL INDIA Fuel-wise Generation Patterns for 29-NOVEMBER-2024
Generation (GW) -->
240
220
200
180
160
140
120
100
80
60
40
20
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
Time -->
Nuclear
Thermal
Hydro
Gas
Solar
Wind

29 नवंबर 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 29 NOVEMBER 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	142265		**12:05**	199841
00:20	141910		**12:20**	198974
00:35	141350		**12:35**	197477
00:50	140544		**12:50**	195607
01:05	139579		**13:05**	191390
01:20	139007		**13:20**	190149
01:35	138370		**13:35**	189929
01:50	137655		**13:50**	189660
02:05	136205		**14:05**	188476
02:20	136149		**14:20**	188958
02:35	135986		**14:35**	189319
02:50	135375		**14:50**	189438
03:05	135232		**15:05**	188730
03:20	135585		**15:20**	189105
03:35	135826		**15:35**	187710
03:50	136104		**15:50**	187043
04:05	137427		**16:05**	185073
04:20	139261		**16:20**	186147
04:35	141460		**16:35**	186966
04:50	143884		**16:50**	188237
05:05	147019		**17:05**	187742
05:20	151166		**17:20**	188748
05:35	154889		**17:35**	190565
05:50	159372		**17:50**	191866
06:05	162818		**18:05**	195262
06:20	170270		**18:20**	192504
06:35	176780		**18:35**	191568
06:50	182294		**18:50**	190401
07:05	185973		**19:05**	187045
07:20	189587		**19:20**	184569
07:35	192441		**19:35**	181138
07:50	193847		**19:50**	177248
08:05	195300		**20:05**	173282
08:20	196455		**20:20**	170473
08:35	200032		**20:35**	168089
08:50	200814		**20:50**	165567
09:05	202834		**21:05**	162963
09:20	205590		**21:20**	160658
09:35	207190		**21:35**	157944
09:50	207007		**21:50**	155691
10:05	205645		**22:05**	153815
10:20	206026		**22:20**	153911
10:35	206583		**22:35**	152151
10:50	205916		**22:50**	150827
11:05	204124		**23:05**	149212
11:20	203478		**23:20**	146004
11:35	202643		**23:35**	146596
11:50	201582		**23:50**	145088
Maximum Demand of 207429 MW met@09:46 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - NOVEMBER 2024

REGION	STATE	Energy Requirement & Met (MU/Day)			Energy Requirement & Met (MU)				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	109	109	0	0.0	221	221	0	0.0
	Delhi	75	75	0.0	2243	2243	0	0.0	4259	4259	0	0.0
	Haryana	145	145	0.0	4343	4343	0	0.0	7848	7848	0	0.0
	Himachal Pradesh	34	34	0.0	1018	1018	0	0.0	2107	2107	0	0.0
	J&K(UT) and Ladakh(UT)	55	55	-0.2	1643	1638	-5	-0.3	2836	2836	0	0.0
	Punjab	144	144	0.0	4308	4308	0	0.0	8962	8962	0	0.0
	Rajasthan	320	320	0.0	9606	9606	0	0.0	17434	17434	0	0.0
	Uttar Pradesh	350	349	0.0	10485	10485	-1	0.0	19929	19929	0	0.0
	Uttarakhand	40	40	0.0	1193	1193	0	0.0	2249	2249	0	0.0
	Railway_NR ISTS	4	4	0.0	128	128	0	0.0	235	235	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	4	4	0	0.0
	TOTAL	1169	1169	-0.2	35078	35072	-6	0.0	61028	60956	-72	-0.1
WR	Gujarat	394	394	0.0	11809	11809	0	0.0	21493	21493	0	0.0
	Madhya Pradesh	314	314	-0.1	9413	9411	-2	0.0	17939	17923	-16	-0.1
	Chhattisgarh	90	90	0.0	2712	2712	0	0.0	4580	4566	-14	-0.3
	Maharashtra	557	557	0.0	16708	16708	0	0.0	27845	27845	0	0.0
	Goa	14	14	0.0	433	433	0	0.0	743	743	0	0.0
	DNHDDPDCL	29	29	0.0	869	869	0	0.0	1343	1343	0	0.0
	AMNSIL	19	19	0.0	564	564	0	0.0	905	905	0	0.0
	BALCO	13	13	0.0	379	379	0	0.0	533	533	0	0.0
	TOTAL	1430	1429	-0.1	42886	42884	-2	0.0	72959	72959	0	0.0
SR	Andhra Pradesh	207	206	-1.7	6216	6166	-50	-0.8	11023	11023	0	0.0
	Telangana	203	201	-1.9	6083	6027	-56	-0.9	11180	11180	0	0.0
	Karnataka	237	235	-2.1	7115	7054	-62	-0.9	14853	14853	0	0.0
	Kerala	85	84	-0.7	2537	2517	-20	-0.8	4505	4505	0	0.0
	Tamil Nadu	316	313	-2.5	9474	9398	-75	-0.8	16872	16872	0	0.0
	Puducherry	9	9	-0.1	275	273	-2	-0.7	450	450	0	0.0
	TOTAL	1057	1048	-8.8	31700	31435	-265	-0.8	53897	53831	-66	-0.1
ER	Bihar	94	94	0.0	2820	2820	-1	0.0	6056	6056	0	0.0
	Jharkhand	37	37	0.0	1119	1118	0	0.0	2074	2074	0	0.0
	DVC	65	65	0.0	1952	1952	0	0.0	3146	3146	0	0.0
	Odisha	104	104	0.0	3116	3116	0	0.0	5643	5643	0	0.0
	West Bengal	154	154	0.0	4622	4622	0	0.0	8765	8765	0	0.0
	Sikkim	1	1	0.0	45	45	0	0.0	111	111	0	0.0
	Railways_ER ISTS	0	0	0.0	4	4	0	0.0	24	24	0	0.0
	TOTAL	456	456	0.0	13678	13677	-1	0.0	25883	25883	0	0.0
NER	Arunachal Pradesh	3	3	0.0	78	78	0	0.0	167	167	0	0.0
	Assam	30	30	0.0	886	886	0	0.0	1853	1823	-30	-1.6
	Manipur	3	3	0.0	79	79	0	0.0	233	233	0	0.0
	Meghalaya	6	6	0.0	185	185	0	0.0	368	368	0	0.0
	Mizoram	2	2	0.0	56	56	0	0.0	145	145	0	0.0
	Nagaland	2	2	0.0	72	72	0	0.0	178	178	0	0.0
	Tripura	4	4	0.0	132	132	0	0.0	310	310	0	0.0
	TOTAL	50	50	0.0	1489	1489	0	0.0	3151	3151	0	0.0
ALL INDIA		4161	4152	-9.1	124831	124558	-273	-0.2				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF NOVEMBER 2024 vs NOVEMBER 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Nov-23	Nov-24	Difference	% Change	Average MU/day for Oct-24	Nov-23	Nov-24	Difference	% Change	Average MU/day for Oct-24
NR	Chandigarh	102	109	7	7	4	102	109	7	7	4
	Delhi	2114	2243	128	6	75	2114	2243	128	6	75
	Haryana	3951	4343	392	10	145	3951	4343	392	10	145
	Himachal Pradesh	970	1018	48	5	34	968	1018	50	5	34
	J&K(UT) and Ladakh(UT)	1586	1643	56	4	55	1568	1638	70	4	55
	Punjab	3925	4308	383	10	144	3925	4308	383	10	144
	Rajasthan	8760	9606	846	10	320	8759	9606	847	10	320
	Uttar Pradesh	9445	10485	1040	11	350	9444	10485	1041	11	349
	Uttarakhand	1114	1193	79	7	40	1114	1193	79	7	40
	Railway_NR ISTS/NFL	113	130	17	15	4	113	130	17	15	4
	TOTAL	32080	35078	2997	9	1169	32057	35072	3015	9	1169
WR	Gujarat	11161	11809	648	6	394	11161	11809	648	6	394
	Madhya Pradesh	9323	9413	90	1	314	9323	9411	88	1	314
	Chhattisgarh	2694	2712	18	1	90	2694	2712	18	1	90
	Maharashtra	16726	16708	-18	0	557	16726	16708	-18	0	557
	Goa	422	433	11	3	14	422	433	11	3	14
	DNHDDPDCL	801	869	69	9	29	801	869	69	9	29
	AMNSIL	558	564	6	1	19	558	564	6	1	19
	BALCO	373	379	6	2	13	373	379	6	2	13
	TOTAL	42058	42886	828	2	1430	42058	42884	827	2	1429
SR	Andhra Pradesh	6296	6216	-80	-1	207	6296	6166	-130	-2	206
	Telangana	6217	6083	-134	-2	203	6220	6027	-192	-3	201
	Karnataka	7191	7115	-76	-1	237	7194	7054	-140	-2	235
	Kerala	2415	2537	122	5	85	2416	2517	102	4	84
	Tamil Nadu	8759	9474	715	8	316	8762	9398	636	7	313
	Puducherry	256	275	19	7	9	256	273	17	7	9
	TOTAL	31134	31700	567	2	1057	31143	31435	292	1	1048
ER	Bihar	2635	2820	185	7	94	2630	2820	190	7	94
	Jharkhand	929	1119	189	20	37	906	1118	213	23	37
	DVC	2105	1952	-152	-7	65	2105	1952	-152	-7	65
	Odisha	3010	3116	105	4	104	3010	3116	105	4	104
	West Bengal	4276	4622	345	8	154	4276	4622	345	8	154
	Sikkim	38	45	6	16	1	38	45	6	16	1
	Railways_ER ISTS	4	4	1	22	0	4	4	1	22	0
	TOTAL	12998	13678	680	5	456	12969	13677	708	5	456
NER	Arunachal Pradesh	74	78	4	5	3	74	78	4	5	3
	Assam	847	886	40	5	30	847	886	40	5	30
	Manipur	80	79	-1	-1	3	80	79	-1	-1	3
	Meghalaya	190	185	-4	-2	6	190	185	-4	-2	6
	Mizoram	51	56	6	11	2	51	56	6	11	2
	Nagaland	71	72	1	2	2	71	72	1	2	2
	Tripura	123	132	9	8	4	123	132	9	8	4
	TOTAL	1434	1489	55	4	50	1434	1489	55	4	50
ALL INDIA		119704	124831	5127	4	4161	119661	124558	4896	4	4152

13. DEMAND COMPARISON OF NOVEMBER 2024 vs NOVEMBER 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Nov-23	Nov-24	Difference	% Change	Nov-23	Nov-24	Difference	% Change
NR	Chandigarh	205	221	16	7.8	205	221	16	7.8
	Delhi	4320	4259	-61	-1.4	4320	4259	-61	-1.4
	Haryana	7685	7848	163	2.1	7685	7848	163	2.1
	Himachal Pradesh	1977	2107	130	6.6	1977	2107	130	6.6
	J&K(UT) and Ladakh(UT)	2710	2836	126	4.6	2710	2836	126	4.6
	Punjab	7572	8962	1390	18.4	7572	8962	1390	18.4
	Rajasthan	16409	17434	1025	6.2	16409	17434	1025	6.2
	Uttar Pradesh	19033	19929	896	4.7	19033	19929	896	4.7
	Uttarakhand	2141	2249	108	5.0	2141	2249	108	5.0
	Railway_NR ISTS/NFL	210	239	29	13.8	210	239	29	13.8
WR	Gujarat	21694	21493	-201	-1	21694	21493	-201	-0.9
	Madhya Pradesh	17117	17939	822	5	17097	17923	826	4.8
	Chhattisgarh	4648	4580	-67	-1	4644	4566	-79	-1.7
	Maharashtra	28386	27845	-541	-2	28356	27845	-511	-1.8
	Goa	733	743	10	1	733	743	10	1.3
	DNHDDPDCL	1267	1343	76	6.0	1267	1343	76	6.0
	AMNSIL	920	905	-15	-1.6	920	905	-15	-1.6
	BALCO	536	533	-3	-0.5	536	533	-3	-0.5
SR	Andhra Pradesh	12085	11023	-1062	-8.8	12085	11023	-1062	-8.8
	Telangana	11857	11180	-677	-5.7	11857	11180	-677	-5.7
	Karnataka	15203	14853	-350	-2.3	15203	14853	-350	-2.3
	Kerala	4300	4505	204	4.7	4300	4505	204	4.7
	Tamil Nadu	16099	16872	773	4.8	16099	16872	773	4.8
	Puducherry	454	450	-4	-0.9	454	450	-4	-0.9
ER	Bihar	5519	6056	537	9.7	5257	6056	799	15.2
	Jharkhand	1699	2074	375	22.1	1699	2074	375	22.1
	DVC	3427	3146	-281	-8.2	3427	3146	-281	-8.2
	Odisha	5264	5643	379	7.2	5264	5643	379	7.2
	West Bengal	8481	8765	284	3.3	8481	8765	284	3.3
	Sikkim	101	111	10	9.9	101	111	10	9.9
	Railways_ER ISTS	23	24	1	4.3	23	24	1	4.3
NER	Arunachal Pradesh	160	167	7	4.4	160	167	7	4.4
	Assam	1931	1853	-78	-4.0	1931	1823	-108	-5.6
	Manipur	207	233	26	12.4	207	233	26	12.4
	Meghalaya	363	368	5	1.4	363	368	5	1.4
	Mizoram	144	145	1	0.7	144	145	1	0.7
	Nagaland	147	178	31	21.0	147	178	31	21.0
	Tripura	299	310	11	3.8	299	310	11	3.8

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - NOVEMBER 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	108.39	108.81	0.42	0.39	3.61	3.63	0.01
	Delhi	2116.53	2089.74	-26.79	-1.27	70.55	69.66	-0.89
	Haryana	3130.93	3089.42	-41.51	-1.33	104.36	102.98	-1.38
	Himachal Pradesh	722.92	696.71	-26.21	-3.63	24.10	23.22	-0.87
	J&K(UT) and Ladakh(UT)	1441.02	1441.11	0.09	0.01	48.03	48.04	0.00
	Punjab	2043.68	2029.55	-14.13	-0.69	68.12	67.65	-0.47
	Rajasthan	3479.82	3456.54	-23.28	-0.67	115.99	115.22	-0.78
	Uttar Pradesh	3802.28	3779.07	-23.21	-0.61	126.74	125.97	-0.77
	Uttarakhand	901.05	908.49	7.44	0.83	30.04	30.28	0.25
	Railways_NR ISTS	117.04	127.65	10.61	9.06	3.90	4.25	0.35
	NFL	2.38	2.28	-0.10	-4.30	0.08	0.08	0.00
	Total	17866.04	17729.36	-136.68	-0.77	595.53	590.98	-4.56
WR	Gujarat	5985.44	5952.47	-32.97	-0.55	199.51	198.42	-1.10
	Madhya Pradesh	5810.17	5727.49	-82.68	-1.42	193.67	190.92	-2.76
	Chhattisgarh	1135.16	1131.93	-3.23	-0.28	37.84	37.73	-0.11
	Maharashtra	6421.87	6455.95	34.08	0.53	214.06	215.20	1.14
	Goa	407.76	416.72	8.96	2.20	13.59	13.89	0.30
	DNHDDPDCL	870.00	869.38	-0.62	-0.07	29.00	28.98	-0.02
	AMNSIL	262.17	273.23	11.06	4.22	8.74	9.11	0.37
	BALCO	379.99	378.92	-1.07	-0.28	12.67	12.63	-0.04
	Total	21272.56	21206.08	-66.48	-0.31	709.09	706.87	-2.22
SR	Andhra Pradesh	1835.47	1821.76	-13.71	-0.75	61.18	60.73	-0.46
	Telangana	2843.17	2846.12	2.95	0.10	94.77	94.87	0.10
	Karnataka	2441.88	2467.69	25.81	1.06	81.40	82.26	0.86
	Kerala	1935.01	1963.78	28.77	1.49	64.50	65.46	0.96
	Tamil Nadu	5520.88	5497.73	-23.15	-0.42	184.03	183.26	-0.77
	Puducherry	264.14	255.71	-8.43	-3.19	8.80	8.52	-0.28
	Goa (SR)	68.95	67.92	-1.03	-1.49	2.30	2.26	-0.03
	Total	14909.50	14920.71	11.21	0.08	496.98	497.36	0.37
ER	Bihar	2482.95	2498.69	15.74	0.63	82.77	83.29	0.52
	Jharkhand	778.57	742.68	-35.89	-4.61	25.95	24.76	-1.20
	DVC	-1242.01	-1238.66	3.35	-0.27	-41.40	-41.29	0.11
	Odisha	891.97	837.35	-54.63	-6.12	29.73	27.91	-1.82
	West Bengal	822.08	755.97	-66.11	-8.04	27.40	25.20	-2.20
	Sikkim	46.02	44.61	-1.41	-3.07	1.53	1.49	-0.05
	Railways_ER ISTS	4.26	4.29	0.03	0.64	0.14	0.14	0.00
	Total	3783.84	3644.93	-138.92	-3.67	126.13	121.50	-4.63
NER	Arunachal Pradesh	74.39	71.73	-2.66	-3.58	2.48	2.39	-0.09
	Assam	661.69	677.98	16.29	2.46	22.06	22.60	0.54
	Manipur	84.41	78.97	-5.44	-6.44	2.81	2.63	-0.18
	Meghalaya	151.92	147.75	-4.17	-2.74	5.06	4.93	-0.14
	Mizoram	47.50	37.93	-9.57	-20.15	1.58	1.26	-0.32
	Nagaland	67.80	65.58	-2.22	-3.27	2.26	2.19	-0.07
	Tripura	157.35	159.59	2.24	1.42	5.25	5.32	0.07
	Total	1245.06	1239.53	-5.53	-0.44	41.50	41.32	-0.18
All India Total		59077.01	58740.61	-336.40	-0.57	1969.23	1958.02	-11.21

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Fin. Year 2024-25
Name of Line									
Import of NR from WR (WR-NR)									
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	714.49	611.32	**7928.26**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	840.34	817.51	**4401.54**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	1009.96	819.22	**7783.48**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	583.07	599.61	**4836.67**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	1570.74	720.37	**15779.70**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	0.00	39.19	**655.43**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	0.00	0.00	**228.47**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	17.54	0.00	**63.56**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	60.41	0.08	**594.38**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	60.83	64.26	**489.89**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	58.67	96.18	**515.71**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	0.00	0.00	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	1096.69	827.50	**8336.15**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	0.00	0.00	**1491.78**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	1113.89	1038.27	**13176.99**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	89.57	0.00	**650.59**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**7216.20**	**5633.51**	**66948.82**
Export of NR to WR (NR-WR)									
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	0.00	0.00	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	368.54	423.95	**2491.26**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	152.00	95.38	**738.23**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	126.24	173.03	**763.96**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	31.75	9.91	**101.32**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	1.94	45.97	**272.63**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	51.59	74.53	**290.12**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	0.00	561.44	**3469.59**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	391.69	523.07	**2076.25**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	0.00	51.46	**246.80**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**1123.75**	**1958.74**	**10465.15**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Fin. Year 2024-25
Name of Line									
Import of NR from ER (ER-NR)									
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	139.89	211.26	**1013.30**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	405.62	482.45	**1541.92**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	366.56	351.78	**2510.96**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	250.72	211.75	**1656.82**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	527.53	418.43	**2569.74**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	319.38	212.80	**1864.08**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	95.04	41.13	**241.26**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	259.86	222.85	**1458.28**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	0.00	0.94	**11.61**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	136.66	108.64	**502.80**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	65.13	77.91	**226.82**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	7.45	17.59	**151.92**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	0.53	0.00	**14.10**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	159.57	132.81	**713.21**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	144.05	156.95	**647.80**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**2877.99**	**2647.29**	**15126.23**
Import of NR from NER (NER-NR)									
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55	555.71	550.01	**2202.51**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**555.71**	**550.01**	**2202.51**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Fin. Year 2024-25
Name of Line									
Export of NR to ER (NR-ER)									
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	0.00	0.00	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	0.00	0.00	**225.17**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	7.00	8.26	**409.05**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	0.00	0.88	**19.94**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	0.00	0.20	**7.33**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	0.00	0.00	**44.74**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	4.74	0.65	**9.05**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	0.48	0.00	**3.26**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	0.58	0.91	**5.76**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	14.57	14.82	**128.75**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	0.00	0.00	**6.54**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**27.37**	**25.72**	**1003.32**
Export of NR to NER (NER-NR)									
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	0.00	0.00	**1365.53**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**0.00**	**0.00**	**1365.53**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Fin. Year 2024-25
Name of Line									
Export of WR to ER (WR-ER)									
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	308.09	84.78	**5334.78**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	65.67	50.80	**1842.64**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	0.04	0.00	**37.15**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	29.14	9.49	**1092.51**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	0.51	1.58	**651.75**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	4.23	14.85	**74.50**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	0.05	0.60	**15.60**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**407.73**	**162.10**	**9048.92**
Import of WR from ER (ER - WR)									
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	68.03	111.05	**289.73**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	334.28	233.51	**2301.69**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	325.55	520.92	**2259.72**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	59.96	84.87	**208.34**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	380.72	297.88	**1937.89**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	48.12	15.83	**243.50**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	60.23	34.62	**309.17**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**1276.89**	**1298.67**	**7550.05**
Export of ER to NER (ER - NER)									
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	104.89	226.52	**798.27**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	173.82	295.36	**1189.97**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	32.38	44.04	**236.28**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**311.10**	**565.92**	**2224.52**
Import of ER from NER (NER - ER)									
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	18.09	0.00	**470.88**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	17.26	0.00	**730.80**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	2.72	0.00	**119.41**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**38.07**	**0.00**	**1321.09**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Fin. Year 2024-25
Name of Line									
Export of ER to SR (ER - SR)									
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	217.59	323.46	**1780.86**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	1105.23	1090.58	**7711.27**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	1297.13	1542.96	**10079.04**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**2619.95**	**2957.00**	**19571.17**
Import of ER from SR (SR - ER)									
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	0.00	0.00	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**0.00**	**0.00**	**490.92**
Export of WR to SR (WR-SR)									
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	231.23	335.29	**1782.41**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	37.08	143.60	**1501.94**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	590.95	779.18	**6168.21**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	0.00	0.00	**0.02**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	574.81	746.92	**7638.52**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	72.89	67.59	**530.40**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	0.03	2.33	**149.57**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	686.47	951.98	**6714.70**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**2193.47**	**3026.89**	**24485.78**
Import of WR from SR (SR - WR)									
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	18.75	0.00	**1635.03**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	410.23	148.25	**3363.69**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	11.46	0.85	**158.55**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	948.20	690.35	**6877.46**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	0.00	0.00	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	0.02	0.01	**0.05**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	6.77	0.01	**165.39**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**1395.43**	**839.47**	**12618.84**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**20044**	**19665**	**174423**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during November 2024

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Nov-24	14.69	18.65	21.24	16.86	0.00	14.42	0.00	0.00		0.00	2.07	1.89	0.00		12.18	0.00	27.27	0.00	**129.27**
2-Nov-24	13.99	14.82	19.62	15.59	0.00	8.07	0.00	0.00		0.00	2.04	1.98	0.00		12.08	0.00	30.81	0.00	**119.00**
3-Nov-24	18.18	22.19	25.15	17.25	0.00	8.00	0.00	0.00		0.00	1.99	1.98	0.00		12.10	0.00	33.04	0.00	**139.88**
4-Nov-24	21.82	28.04	29.01	20.11	0.00	15.56	0.00	0.00	0.00	0.08	2.10	2.54	0.00	0.00	17.67	0.00	38.48	0.00	**175.41**
5-Nov-24	21.35	29.73	30.55	21.57	0.00	23.00	0.00	0.00		0.00	2.24	3.28	0.00	0.00	24.22	0.00	41.81	0.00	**197.75**
6-Nov-24	20.29	31.15	29.83	22.11	0.00	26.14	1.30	0.00	0.00	0.00	2.32	3.58	0.00	0.00	35.57	0.00	37.40	0.00	**209.69**
7-Nov-24	20.03	28.98	30.37	21.67	0.00	23.04	2.42	0.00		0.00	2.16	3.52	0.00	0.00	36.28	0.00	36.11	0.00	**204.58**
8-Nov-24	18.90	28.30	27.61	21.50	0.00	23.06	2.36	0.00		0.00	2.15	3.38	0.00	0.00	36.28	0.00	34.19	0.00	**197.73**
9-Nov-24	21.22	31.06	31.42	22.12	0.00	24.15	0.00	0.00		0.00	2.14	3.42	0.00	0.00	33.24	0.00	35.80	0.00	**204.57**
10-Nov-24	18.57	28.54	30.65	19.30	0.00	23.50	1.11	0.00		0.00	2.20	3.39	0.00	0.00	35.83	0.00	35.69	0.00	**198.78**
11-Nov-24	22.44	30.54	33.58	19.45	0.00	22.94	0.98	0.00		0.00	2.18	3.26	0.00	0.00	36.28	0.00	29.85	0.00	**201.50**
12-Nov-24	25.50	31.05	32.11	22.33	0.00	22.29	0.00	0.00		0.00	2.15	3.25	0.00	0.00	36.28	0.00	39.85	0.00	**214.81**
13-Nov-24	21.86	27.91	27.73	21.01	0.00	36.82	0.00	0.00		0.00	2.25	3.44	0.00	0.00	36.28	0.00	39.34	0.00	**216.64**
14-Nov-24	17.73	26.83	24.11	19.51	0.00	46.90	0.90	0.00	0.00	0.00	2.25	3.20	0.00	0.00	36.29	0.00	33.59	0.00	**211.31**
15-Nov-24	18.27	29.95	26.96	19.93	0.00	46.41	0.00	0.00	0.00	0.00	2.25	3.47	0.00	0.00	36.29	0.00	30.30	0.00	**213.83**
16-Nov-24	18.56	31.14	28.31	20.47	0.00	31.56	0.00	0.00		0.00	2.28	3.53	0.00	0.00	36.29	0.00	34.44	0.00	**206.58**
17-Nov-24	15.34	26.98	24.21	18.79	0.00	36.25	0.00	0.00		0.00	2.25	3.35	0.00	0.00	33.56	0.00	33.05	0.00	**193.78**
18-Nov-24	19.60	24.28	25.71	19.80	0.00	33.74	0.00	0.00		0.00	2.31	3.45	0.00	0.00	24.22	0.00	37.53	0.00	**190.64**
19-Nov-24	21.56	25.56	27.33	19.97	0.00	23.66	0.00	0.00		0.00	2.27	3.37	0.00	0.00	30.58	0.00	40.02	0.00	**194.32**
20-Nov-24	23.76	26.41	29.92	20.21	0.00	11.50	0.00	0.00		0.00	2.20	3.41	0.00	0.00	30.16	0.00	36.89	0.00	**184.46**
21-Nov-24	23.07	25.27	27.89	19.23	0.00	19.32	0.00	0.00		0.00	2.14	3.49	0.00	0.00	24.16	0.00	34.89	0.00	**179.46**
22-Nov-24	23.52	27.77	24.51	22.35	0.00	23.53	0.00	0.00		0.00	2.15	3.41	0.00	0.00	26.45	0.00	42.43	0.00	**196.12**
23-Nov-24	23.22	31.35	18.57	24.61	0.00	23.42	1.48	0.00		0.00	2.56	3.25	0.00	0.00	26.21	0.00	38.98	0.00	**193.65**
24-Nov-24	17.02	27.30	22.12	19.32	0.00	23.44	2.41	0.00		0.00	2.25	3.29	0.00	0.00	31.85	0.00	31.00	0.00	**180.00**
25-Nov-24	17.89	25.32	24.35	17.07	0.00	28.01	2.42	0.00		0.00	2.03	3.17	0.00	0.00	24.77	0.00	18.16	0.00	**163.19**
26-Nov-24	12.72	23.65	21.58	16.60	0.00	36.46	2.42	0.00		0.00	2.06	3.36	0.00	0.00	24.52	0.00	23.83	0.00	**167.20**
27-Nov-24	23.16	28.35	29.49	19.84	0.00	12.12	2.41	0.00		0.00	1.97	3.42	0.00	0.00	19.19	0.00	32.93	0.00	**172.88**
28-Nov-24	26.40	30.39	33.15	20.09	0.00	11.57	4.57	0.00		0.00	1.86	3.43	0.00	0.00	19.49	0.00	36.78	0.00	**187.73**
29-Nov-24	25.56	27.67	31.01	21.10	0.00	18.01	7.20	0.00		0.00	1.97	3.31	0.00	0.00	19.86	0.00	34.85	0.00	**190.54**
30-Nov-24	25.10	28.33	31.13	19.85	0.00	23.48	7.21	0.00		0.00	1.47	3.36	0.00	0.00	19.32	0.00	38.96	0.00	**198.21**
Total	**611.32**	**817.51**	**819.22**	**599.61**	**0.00**	**720.37**	**39.19**	**0.00**	**0.00**	**0.08**	**64.26**	**96.18**	**0.00**	**0.00**	**827.50**	**0.00**	**1038.27**	**0.00**	**5633.51**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.1 Import-Export of NR with WR during November 2024

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Nov-24	0.00	0.00	0.00	0.00	12.42	0.00	7.32	5.10		3.15	0.00	0.00	2.24		0.00	13.61	0.00	3.25	**47.09**
2-Nov-24	0.00	0.00	0.00	0.00	11.70	0.00	7.35	6.11		4.23	0.00	0.00	2.25		0.00	13.13	0.00	3.65	**48.42**
3-Nov-24	0.00	0.00	0.00	0.00	13.53	0.00	7.34	5.89		2.17	0.00	0.00	2.01		0.00	14.89	0.00	2.02	**47.85**
4-Nov-24	0.00	0.00	0.00	0.00	14.28	0.00	7.30	6.98	0.00	0.33	0.00	0.00	2.01	10.15	0.00	18.50	0.00	1.08	**60.63**
5-Nov-24	0.00	0.00	0.00	0.00	14.01	0.00	7.29	7.62		0.31	0.00	0.00	1.68	22.40	0.00	20.40	0.00	0.55	**74.26**
6-Nov-24	0.00	0.00	0.00	0.00	15.74	0.00	3.27	4.58	3.15	0.63	0.00	0.00	2.20	22.37	0.00	18.31	0.00	1.15	**71.40**
7-Nov-24	0.00	0.00	0.00	0.00	14.88	0.00	0.00	7.98		1.66	0.00	0.00	2.24	22.10	0.00	18.76	0.00	2.23	**69.85**
8-Nov-24	0.00	0.00	0.00	0.00	15.59	0.00	0.00	9.19		2.13	0.00	0.00	2.48	22.52	0.00	24.51	0.00	2.26	**78.68**
9-Nov-24	0.00	0.00	0.00	0.00	15.50	0.00	0.59	7.51		0.63	0.00	0.00	2.45	21.46	0.00	19.30	0.00	0.90	**68.34**
10-Nov-24	0.00	0.00	0.00	0.00	15.17	0.00	0.00	8.03		0.97	0.00	0.00	2.41	22.19	0.00	17.42	0.00	2.23	**68.42**
11-Nov-24	0.00	0.00	0.00	0.00	14.39	0.00	2.53	3.98		0.64	0.00	0.00	2.24	0.52	0.00	16.05	0.00	1.07	**41.42**
12-Nov-24	0.00	0.00	0.00	0.00	14.33	0.00	7.30	6.65		0.83	0.00	0.00	2.37	20.76	0.00	16.92	0.00	1.63	**70.79**
13-Nov-24	0.00	0.00	0.00	0.00	14.29	0.00	4.45	6.76		1.96	0.00	0.00	2.43	21.42	0.00	18.60	0.00	2.25	**72.16**
14-Nov-24	0.00	0.00	0.00	0.00	14.92	0.00	0.00	4.71	3.31	2.75	0.00	0.00	2.94	22.05	0.00	22.83	0.00	3.01	**76.52**
15-Nov-24	0.00	0.00	0.00	0.00	15.52	0.00	2.44	4.99	3.45	1.65	0.00	0.00	2.73	20.06	0.00	24.56	0.00	1.72	**77.12**
16-Nov-24	0.00	0.00	0.00	0.00	16.58	0.00	4.89	8.89		1.27	0.00	0.00	2.74	21.69	0.00	26.01	0.00	1.68	**83.75**
17-Nov-24	0.00	0.00	0.00	0.00	15.18	0.00	7.29	7.81		2.90	0.00	0.00	2.96	22.99	0.00	23.10	0.00	3.06	**85.29**
18-Nov-24	0.00	0.00	0.00	0.00	14.41	0.00	7.21	6.51		2.24	0.00	0.00	3.10	22.07	0.00	21.02	0.00	2.50	**79.06**
19-Nov-24	0.00	0.00	0.00	0.00	14.64	0.00	7.29	7.15		1.86	0.00	0.00	2.64	22.15	0.00	23.03	0.00	2.04	**80.80**
20-Nov-24	0.00	0.00	0.00	0.00	14.30	0.00	5.71	5.21		1.70	0.00	0.00	2.61	22.23	0.00	16.38	0.00	1.86	**70.00**
21-Nov-24	0.00	0.00	0.00	0.00	14.82	0.00	2.44	4.46		1.63	0.00	0.00	2.78	22.46	0.00	14.29	0.00	1.56	**64.44**
22-Nov-24	0.00	0.00	0.00	0.00	13.10	0.00	2.44	5.27		0.70	0.00	0.00	2.61	22.34	0.00	16.72	0.00	0.58	**63.76**
23-Nov-24	0.00	0.00	0.00	0.00	11.22	0.00	0.93	5.98		0.30	0.00	0.00	2.64	21.87	0.00	20.05	0.00	0.17	**63.16**
24-Nov-24	0.00	0.00	0.00	0.00	12.99	0.00	0.00	5.52		2.01	0.00	0.00	2.81	22.36	0.00	18.70	0.00	1.80	**66.19**
25-Nov-24	0.00	0.00	0.00	0.00	14.64	0.00	0.00	4.46		2.20	0.00	0.00	3.08	21.96	0.00	14.20	0.00	2.06	**62.60**
26-Nov-24	0.00	0.00	0.00	0.00	9.01	0.00	0.00	4.32		2.97	0.00	0.00	3.01	22.50	0.00	13.99	0.00	2.85	**58.65**
27-Nov-24	0.00	0.00	0.00	0.00	14.24	0.00	0.00	3.54		1.58	0.00	0.00	2.34	22.05	0.00	11.56	0.00	1.52	**56.83**
28-Nov-24	0.00	0.00	0.00	0.00	14.33	0.00	0.00	2.04		0.15	0.00	0.00	2.16	22.22	0.00	11.04	0.00	0.08	**52.02**
29-Nov-24	0.00	0.00	0.00	0.00	14.19	0.00	0.00	3.54		0.22	0.00	0.00	2.30	22.29	0.00	9.41	0.00	0.48	**52.43**
30-Nov-24	0.00	0.00	0.00	0.00	14.03	0.00	0.00	2.25		0.20	0.00	0.00	2.07	22.26	0.00	5.78	0.00	0.22	**46.81**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**423.95**	**0.00**	**95.38**	**173.03**	**9.91**	**45.97**	**0.00**	**0.00**	**74.53**	**561.44**	**0.00**	**523.07**	**0.00**	**51.46**	**1958.74**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during November 2024

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Bihartariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Nov-24	2.82	10.17	7.82	6.38	9.40	3.47	0.00	5.34		4.96	2.33	0.00	0.00		0.00	2.53	2.57	**57.79**	22.62	**22.62**
2-Nov-24	1.75	5.60	7.68	6.95	9.77	2.62	0.00	4.44		4.84	2.30	0.00	0.00		0.00	2.92	1.72	**50.59**	24.18	**24.18**
3-Nov-24	3.16	8.51	8.56	7.04	11.37	4.55	0.00	5.40		4.52	2.51	0.10			0.00	3.22	2.92	**61.86**	24.27	**24.27**
4-Nov-24	4.68	13.05	10.10	7.01	14.37	5.41	0.00	6.05	0.00	3.74	3.32	0.00	0.00		0.00	4.32	4.91	**76.96**	23.98	**23.98**
5-Nov-24	6.52	12.52	10.95	7.21	14.89	6.04	0.00	6.96		3.40	3.56	0.18	0.00		0.00	4.51	4.58	**81.32**	24.01	**24.01**
6-Nov-24	8.99	15.56	11.70	7.39	17.12	7.65	0.88	8.30		3.51	3.45	1.65			0.00	5.32	5.45	**96.97**	24.24	**24.24**
7-Nov-24	9.04	15.75	11.53	7.07	16.59	8.12	0.85	8.65		3.49	3.50	1.62			0.00	5.42	5.52	**97.15**	23.27	**23.27**
8-Nov-24	8.45	18.32	11.86	7.45	19.45	8.59	1.92	9.17		3.49	3.41	0.95			0.00	6.08	6.01	**105.15**	24.20	**24.20**
9-Nov-24	8.64	18.03	12.49	7.22	19.54	8.62	2.13	9.03	0.00	3.78	3.00	0.83			0.00	6.13	6.09	**105.53**	24.39	**24.39**
10-Nov-24	7.40	15.94	11.80	7.01	14.87	7.37	1.58	6.95		4.52	2.31	0.47			0.00	4.61	5.10	**89.93**	23.01	**23.01**
11-Nov-24	8.10	16.33	12.51	6.96	14.34	9.12	2.59	6.97	0.94	5.12	1.91	0.66			0.00	4.83	5.92	**96.30**	17.15	**17.15**
12-Nov-24	8.75	15.95	12.55	6.85	15.50	10.56	3.13	9.05		4.74	2.05	0.55	0.00		0.00	4.87	6.09	**100.64**	15.55	**15.55**
13-Nov-24	8.26	17.35	12.52	7.01	16.11	10.07	2.33	9.25		4.00	2.90	0.80			0.00	5.00	6.25	**101.85**	15.60	**15.60**
14-Nov-24	7.19	17.06	12.25	7.15	14.86	8.33	2.26	7.65		4.45	2.56	0.92	0.00		0.00	4.59	5.79	**95.06**	15.67	**15.67**
15-Nov-24	8.97	19.35	12.92	6.70	13.95	8.02	2.43	7.41		4.16	2.81	0.88	0.00		0.00	4.44	6.95	**98.99**	15.66	**15.66**
16-Nov-24	8.53	18.50	12.88	7.15	12.68	8.63	2.40	7.62		4.07	2.81	0.64			0.00	3.97	5.65	**95.53**	15.70	**15.70**
17-Nov-24	7.35	17.90	12.05	6.80	12.01	7.36	1.53	7.15		3.57	3.35	0.65			0.00	4.06	5.92	**89.70**	14.50	**14.50**
18-Nov-24	6.93	16.86	12.45	6.95	13.60	7.41	1.49	7.67		3.51	3.58	0.49	0.00		0.00	4.09	5.55	**90.58**	15.05	**15.05**
19-Nov-24	8.57	18.55	13.70	7.22	14.90	8.01	2.88	8.50		1.78	2.60	0.80			0.00	4.72	5.60	**97.83**	17.61	**17.61**
20-Nov-24	6.00	17.18	12.30	7.32	11.73	7.37	1.65	7.50		3.36	3.14	0.21			0.00	3.74	6.02	**87.52**	15.58	**15.58**
21-Nov-24	6.78	17.46	13.04	7.04	11.88	7.17	1.61	6.78		3.91	3.08	0.31			0.00	3.70	5.71	**88.47**	15.58	**15.58**
22-Nov-24	6.81	15.87	13.17	7.10	10.95	6.24	0.99	6.85		3.86	3.09	0.33		0.00	0.00	3.93	3.93	**83.12**	14.65	**14.65**
23-Nov-24	8.15	18.61	11.09	7.22	12.15	8.05	1.31	7.89		3.62	3.35	0.45			0.00	3.82	5.92	**91.63**	15.82	**15.82**
24-Nov-24	6.53	17.41	10.70	7.13	13.29	6.76	0.63	6.48		3.93	3.00	0.33	0.00		0.00	4.00	5.52	**85.71**	15.66	**15.66**
25-Nov-24	7.15	16.72	13.85	7.61	13.94	7.12	1.13	7.24		3.61	2.52	0.50			0.00	5.37	5.31	**92.07**	15.79	**15.79**
26-Nov-24	2.63	19.65	12.37	7.04	13.80	6.61	1.71	8.13	0.00	3.47	2.60	1.18			0.00	5.24	5.70	**90.13**	15.64	**15.64**
27-Nov-24	9.11	18.94	12.90	6.79	14.96	6.40	1.07	8.18		1.33	1.21	0.73	0.00		0.00	4.74	5.39	**91.75**	14.71	**14.71**
28-Nov-24	9.21	17.64	12.86	7.13	13.64	6.40	1.20	7.87	0.00	0.00	0.13	0.75	0.00		0.00	4.27	5.47	**86.57**	15.83	**15.83**
29-Nov-24	8.78	19.28	8.33	6.90	14.68	6.01	1.43	7.55		1.58	0.17	0.51	0.00		0.00	4.66	5.24	**85.12**	15.33	**15.33**
30-Nov-24	6.01	12.39	12.85	6.95	12.09	4.72	0.00	6.82		4.32	1.36	0.10	0.00	0.00	0.00	3.71	4.15	**75.47**	14.76	**14.76**
Total	**211.26**	**482.45**	**351.78**	**211.75**	**418.43**	**212.80**	**41.13**	**222.85**	**0.94**	**108.64**	**77.91**	**17.59**	**0.00**	**0.00**	**0.00**	**132.81**	**156.95**	**2647.29**	**550.01**	**550.01**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during November 2024

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	3.68	0.00		0.00	0.00	0.30	0.00		0.53	0.00	0.00	**4.51**	0.00	**0.00**
2-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	2.57	0.00		0.00	0.00	0.25	0.00		0.56	0.00	0.00	**3.38**	0.00	**0.00**
3-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	1.15	0.00		0.00	0.00	0.00			0.51	0.00	0.00	**1.66**	0.00	**0.00**
4-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.51	0.00	0.88	0.00	0.00	0.10	0.00		0.50	0.00	0.00	**1.99**	0.00	**0.00**
5-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.09	0.00		0.00	0.00	0.00	0.00		0.46	0.00	0.00	**0.55**	0.00	**0.00**
6-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.51	0.00	0.00	**0.51**	0.00	**0.00**
7-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.53	0.00	0.00	**0.53**	0.00	**0.00**
8-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.45	0.00	0.00	**0.45**	0.00	**0.00**
9-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.46	0.00	0.00	**0.46**	0.00	**0.00**
10-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.44	0.00	0.00	**0.44**	0.00	**0.00**
11-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.46	0.00	0.00	**0.46**	0.00	**0.00**
12-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.49	0.00	0.00	**0.49**	0.00	**0.00**
13-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.48	0.00	0.00	**0.48**	0.00	**0.00**
14-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.48	0.00	0.00	**0.48**	0.00	**0.00**
15-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.46	0.00	0.00	**0.46**	0.00	**0.00**
16-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.48	0.00	0.00	**0.48**	0.00	**0.00**
17-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.47	0.00	0.00	**0.47**	0.00	**0.00**
18-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.48	0.00	0.00	**0.48**	0.00	**0.00**
19-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.47	0.00	0.00	**0.47**	0.00	**0.00**
20-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.49	0.00	0.00	**0.49**	0.00	**0.00**
21-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.48	0.00	0.00	**0.48**	0.00	**0.00**
22-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.80	0.50	0.00	0.00	**1.30**	0.00	**0.00**
23-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.50	0.00	0.00	**0.50**	0.00	**0.00**
24-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.49	0.00	0.00	**0.49**	0.00	**0.00**
25-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.50	0.00	0.00	**0.50**	0.00	**0.00**
26-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.50	0.00	0.00	**0.50**	0.00	**0.00**
27-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.50	0.00	0.00	**0.50**	0.00	**0.00**
28-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.20	0.00	0.00	0.00		0.52	0.00	0.00	**0.72**	0.00	**0.00**
29-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.60	0.00	0.00	**0.60**	0.00	**0.00**
30-Nov-24	0.00	0.00	0.00	0.00	0.00	0.00	0.26	0.00		0.00	0.00	0.00	0.00	0.11	0.52	0.00	0.00	**0.89**	0.00	**0.00**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**8.26**	**0.00**	**0.88**	**0.20**	**0.00**	**0.65**	**0.00**	**0.91**	**14.82**	**0.00**	**0.00**	**25.72**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.3 Import and Export of ER with WR & NER during November 2024

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Nov-24	8.8	6.3	0.0	1.3	0.4	1.3	0.0	**18.10**	1.5	2.8	11.8	1.5	6.1	0.0	0.9	**24.60**	6.46	9.11	1.57	**17.15**	0.00	0.00	0.00	**0.00**
2-Nov-24	10.1	8.8	0.0	1.6	0.8	2.0	0.0	**23.37**	1.0	0.9	10.7	1.2	4.7	0.0	0.6	**19.25**	7.28	10.22	1.87	**19.36**	0.00	0.00	0.00	**0.00**
3-Nov-24	9.2	5.1	0.0	1.6	0.3	1.7	0.1	**17.99**	1.4	3.7	11.2	1.4	6.3	0.0	0.6	**24.66**	7.40	10.19	1.88	**19.46**	0.00	0.00	0.00	**0.00**
4-Nov-24	5.6	1.8	0.0	0.9	0.0	1.2	0.0	**9.50**	1.3	4.4	13.6	2.3	7.5	0.1	1.1	**30.18**	9.16	12.56	2.33	**24.06**	0.00	0.00	0.00	**0.00**
5-Nov-24	6.1	0.6	0.0	0.5	0.0	1.0	0.0	**8.30**	1.7	6.6	12.2	2.1	7.9	0.1	0.9	**31.48**	9.31	12.40	2.32	**24.03**	0.00	0.00	0.00	**0.00**
6-Nov-24	2.9	0.8	0.0	0.3	0.0	0.6	0.0	**4.69**	2.8	5.8	13.7	3.1	9.2	0.2	1.1	**36.01**	8.96	11.92	2.21	**23.08**	0.00	0.00	0.00	**0.00**
7-Nov-24	3.1	3.3	0.0	0.4	0.0	1.2	0.0	**8.02**	2.5	1.2	18.7	2.5	8.7	0.1	1.0	**34.59**	9.29	12.25	2.27	**23.81**	0.00	0.00	0.00	**0.00**
8-Nov-24	1.5	2.4	0.0	0.1	0.0	0.8	0.0	**4.77**	3.9	1.2	19.0	3.2	10.0	0.2	1.1	**38.63**	9.10	11.73	2.04	**22.88**	0.00	0.00	0.00	**0.00**
9-Nov-24	1.3	0.5	0.0	0.1	0.0	0.5	0.0	**2.48**	3.9	7.5	19.2	3.0	9.7	0.2	1.2	**44.82**	7.38	11.93	2.12	**21.43**	0.00	0.00	0.00	**0.00**
10-Nov-24	4.2	2.1	0.0	0.4	0.0	0.7	0.0	**7.44**	2.9	4.3	17.0	2.2	9.2	0.1	1.0	**36.75**	8.59	11.21	1.98	**21.78**	0.00	0.00	0.00	**0.00**
11-Nov-24	5.0	1.0	0.0	0.4	0.0	0.7	0.0	**7.08**	1.0	3.1	17.8	1.7	11.9	0.2	1.5	**37.20**	7.75	9.39	1.06	**18.19**	0.00	0.00	0.00	**0.00**
12-Nov-24	0.9	0.8	0.0	0.0	0.0	0.3	0.0	**2.08**	3.1	3.1	20.9	2.9	12.2	0.3	2.4	**44.86**	5.96	6.63	0.86	**13.45**	0.00	0.00	0.00	**0.00**
13-Nov-24	1.7	1.5	0.0	0.2	0.0	0.2	0.0	**3.67**	3.6	5.1	17.9	2.6	10.6	0.4	2.1	**42.24**	6.52	7.20	1.01	**14.73**	0.00	0.00	0.00	**0.00**
14-Nov-24	0.1	2.7	0.0	0.0	0.0	0.3	0.0	**3.14**	7.3	8.9	19.2	3.8	10.2	0.4	0.8	**50.58**	7.87	9.36	1.24	**18.47**	0.00	0.00	0.00	**0.00**
15-Nov-24	0.4	2.6	0.0	0.0	0.0	0.2	0.0	**3.20**	4.3	9.1	19.3	3.1	8.8	0.2	1.5	**46.23**	7.95	7.51	1.32	**16.78**	0.00	0.00	0.00	**0.00**
16-Nov-24	1.6	1.2	0.0	0.1	0.0	0.2	0.0	**3.18**	4.9	7.4	21.4	3.5	11.2	0.4	1.2	**49.99**	8.28	8.12	1.40	**17.80**	0.00	0.00	0.00	**0.00**
17-Nov-24	2.1	2.0	0.0	0.3	0.0	0.2	0.0	**4.63**	8.0	9.0	20.0	4.1	10.8	0.7	1.0	**53.59**	7.29	8.46	1.07	**16.81**	0.00	0.00	0.00	**0.00**
18-Nov-24	0.7	0.6	0.0	0.0	0.0	0.0	0.0	**1.33**	6.1	9.8	24.2	3.8	11.0	1.4	1.8	**58.19**	7.56	8.92	1.03	**17.51**	0.00	0.00	0.00	**0.00**
19-Nov-24	1.0	0.7	0.0	0.0	0.0	0.0	0.0	**1.69**	5.4	7.7	26.0	3.7	12.0	1.5	1.7	**58.00**	7.88	9.39	1.08	**18.35**	0.00	0.00	0.00	**0.00**
20-Nov-24	1.9	2.0	0.0	0.0	0.0	0.1	0.0	**3.98**	3.1	2.0	23.4	3.0	10.2	0.8	1.2	**43.83**	7.98	9.42	1.16	**18.56**	0.00	0.00	0.00	**0.00**
21-Nov-24	0.9	0.4	0.0	0.0	0.0	0.1	0.0	**1.35**	4.5	6.2	22.3	3.2	10.1	0.8	1.2	**48.26**	7.77	9.01	1.14	**17.92**	0.00	0.00	0.00	**0.00**
22-Nov-24	2.5	0.3	0.0	0.3	0.0	0.5	0.4	**3.97**	2.7	10.9	21.8	2.3	11.0	0.7	0.8	**50.43**	6.60	10.30	1.33	**18.23**	0.00	0.00	0.00	**0.00**
23-Nov-24	1.3	0.0	0.0	0.1	0.0	0.1	0.0	**1.46**	3.2	13.8	15.1	2.6	10.5	0.7	0.9	**46.73**	6.50	9.94	1.06	**17.50**	0.00	0.00	0.00	**0.00**
24-Nov-24	0.9	0.5	0.0	0.0	0.0	0.2	0.0	**1.53**	4.3	7.9	14.0	2.8	9.6	0.4	0.6	**39.54**	6.20	9.75	1.24	**17.19**	0.00	0.00	0.00	**0.00**
25-Nov-24	0.4	1.6	0.0	0.0	0.0	0.0	0.0	**2.03**	7.8	11.4	15.1	4.6	11.4	1.6	0.9	**52.85**	5.94	8.67	1.08	**15.69**	0.00	0.00	0.00	**0.00**
26-Nov-24	0.0	1.2	0.0	0.0	0.0	0.0	0.0	**1.19**	9.3	18.0	16.6	5.2	11.8	1.3	0.7	**62.95**	5.95	9.90	1.28	**17.13**	0.00	0.00	0.00	**0.00**
27-Nov-24	0.7	0.0	0.0	0.0	0.0	0.0	0.0	**0.70**	3.4	17.3	16.6	3.4	12.4	0.9	1.2	**55.14**	7.11	9.66	1.23	**18.00**	0.00	0.00	0.00	**0.00**
28-Nov-24	3.4	0.0	0.0	0.2	0.0	0.0	0.0	**3.59**	2.2	18.3	15.8	2.2	12.5	1.0	1.2	**53.14**	6.59	10.04	1.27	**17.90**	0.00	0.00	0.00	**0.00**
29-Nov-24	1.9	0.1	0.0	0.0	0.0	0.2	0.0	**2.26**	2.7	13.2	14.1	2.4	11.0	0.4	1.2	**45.14**	8.50	8.81	1.12	**18.43**	0.00	0.00	0.00	**0.00**
30-Nov-24	4.5	0.0	0.0	0.5	0.0	0.3	0.0	**5.37**	1.3	13.1	12.2	1.3	9.4	0.5	1.0	**38.81**	7.40	11.36	1.47	**20.22**	0.00	0.00	0.00	**0.00**
Total	**84.78**	**50.80**	**0.00**	**9.49**	**1.58**	**14.85**	**0.60**	**162.10**	**111.05**	**233.51**	**520.92**	**84.87**	**297.88**	**15.83**	**34.62**	**1298.67**	**226.52**	**295.36**	**44.04**	**565.92**	**0.00**	**0.00**	**0.00**	**0.00**

15.4 Import and Export of SR with ER & WR during November 2024

Date	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)								
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Nov-24	12.58	29.80	45.82	**88.20**	0.00	0.00	0.00	**0.00**	7.30	7.04	27.09	0.00	14.62	2.09	0.00	33.29	**91.43**	0.00	3.75	0.00	14.31	0.00	0.00	0.00	0.00	**18.06**
2-Nov-24	12.59	36.13	43.67	**92.39**	0.00	0.00	0.00	**0.00**	7.32	4.55	25.07	0.00	21.56	1.73	0.00	31.60	**91.83**	0.00	3.44	0.00	15.01	0.00	0.00	0.00	0.00	**18.45**
3-Nov-24	12.59	29.97	37.23	**79.79**	0.00	0.00	0.00	**0.00**	7.39	0.88	16.47	0.00	24.19	2.39	0.00	22.81	**74.13**	0.00	9.71	0.77	18.87	0.00	0.00	0.00	0.01	**29.36**
4-Nov-24	12.59	30.79	45.46	**88.84**	0.00	0.00	0.00	**0.00**	11.61	1.86	22.32	0.00	29.26	1.10	0.00	29.94	**96.08**	0.00	4.85	0.00	22.32	0.00	0.00	0.00	0.00	**27.17**
5-Nov-24	12.59	39.74	41.32	**93.65**	0.00	0.00	0.00	**0.00**	14.29	0.35	16.38	0.00	36.23	2.38	0.00	23.43	**93.07**	0.00	11.52	0.00	28.40	0.00	0.00	0.00	0.00	**39.92**
6-Nov-24	12.59	39.74	53.71	**106.04**	0.00	0.00	0.00	**0.00**	7.35	6.74	29.06	0.00	36.23	2.46	0.00	36.85	**118.70**	0.00	4.98	0.00	24.93	0.00	0.00	0.00	0.00	**29.91**
7-Nov-24	12.59	45.89	54.28	**112.76**	0.00	0.00	0.00	**0.00**	13.27	4.87	29.16	0.00	44.45	2.18	0.00	36.81	**130.75**	0.00	4.07	0.00	25.07	0.00	0.00	0.00	0.00	**29.14**
8-Nov-24	12.59	48.12	56.82	**117.53**	0.00	0.00	0.00	**0.00**	20.90	7.34	29.78	0.00	43.47	1.56	0.00	37.93	**140.99**	0.00	3.75	0.00	24.04	0.00	0.00	0.00	0.00	**27.79**
9-Nov-24	12.59	48.12	47.26	**107.97**	0.00	0.00	0.00	**0.00**	20.84	2.84	20.50	0.00	70.47	2.30	0.95	27.86	**145.75**	0.00	10.39	0.01	27.48	0.00	0.00	0.00	0.00	**37.88**
10-Nov-24	12.60	41.39	43.11	**97.09**	0.00	0.00	0.00	**0.00**	17.39	0.02	14.61	0.00	44.93	2.13	0.68	20.99	**100.76**	0.00	15.63	0.03	28.93	0.00	0.00	0.00	0.00	**44.58**
11-Nov-24	12.62	36.15	49.22	**97.99**	0.00	0.00	0.00	**0.00**	9.75	2.84	22.55	0.00	30.75	2.33	0.00	28.76	**96.97**	0.00	6.93	0.00	26.04	0.00	0.00	0.00	0.00	**32.97**
12-Nov-24	12.67	36.14	50.90	**99.70**	0.00	0.00	0.00	**0.00**	18.47	3.24	24.27	0.00	36.22	2.38	0.00	31.18	**115.75**	0.00	2.64	0.00	25.45	0.00	0.00	0.00	0.00	**28.09**
13-Nov-24	12.67	37.39	50.80	**100.85**	0.00	0.00	0.00	**0.00**	23.85	1.54	25.99	0.00	36.22	2.36	0.00	30.63	**120.59**	0.00	5.07	0.00	27.36	0.00	0.00	0.00	0.00	**32.43**
14-Nov-24	12.67	43.21	51.73	**107.60**	0.00	0.00	0.00	**0.00**	23.19	0.97	29.12	0.00	34.57	2.30	0.00	32.08	**122.23**	0.00	4.94	0.00	28.61	0.00	0.00	0.00	0.00	**33.55**
15-Nov-24	12.67	48.10	54.44	**115.21**	0.00	0.00	0.00	**0.00**	7.33	1.92	32.08	0.00	14.57	2.57	0.00	35.34	**93.83**	0.00	3.74	0.00	26.65	0.00	0.00	0.00	0.00	**30.38**
16-Nov-24	12.67	41.62	53.78	**108.07**	0.00	0.00	0.00	**0.00**	7.36	1.77	25.68	0.00	14.57	2.33	0.00	32.48	**84.19**	0.00	10.88	0.00	27.86	0.00	0.00	0.00	0.00	**38.74**
17-Nov-24	12.67	33.73	51.88	**98.28**	0.00	0.00	0.00	**0.00**	7.43	2.86	25.24	0.00	14.61	2.27	0.65	31.81	**84.86**	0.00	10.78	0.04	26.80	0.00	0.00	0.00	0.00	**37.63**
18-Nov-24	11.95	35.92	55.18	**103.05**	0.00	0.00	0.00	**0.00**	5.91	3.99	27.82	0.00	14.62	2.34	0.00	36.30	**90.98**	0.00	4.61	0.00	24.14	0.00	0.00	0.00	0.00	**28.75**
19-Nov-24	4.90	29.78	58.46	**93.14**	0.00	0.00	0.00	**0.00**	5.76	5.77	28.89	0.00	16.09	2.24	0.00	37.96	**96.71**	0.00	4.07	0.00	22.09	0.00	0.00	0.00	0.00	**26.17**
20-Nov-24	4.90	28.94	57.18	**91.03**	0.00	0.00	0.00	**0.00**	7.36	7.93	28.19	0.00	15.61	2.27	0.00	36.93	**98.30**	0.00	0.07	0.00	19.65	0.00	0.00	0.00	0.00	**19.73**
21-Nov-24	7.16	28.94	54.73	**90.83**	0.00	0.00	0.00	**0.00**	7.35	7.67	26.21	0.00	14.62	2.28	0.00	35.22	**93.36**	0.00	1.17	0.00	21.29	0.00	0.00	0.00	0.00	**22.46**
22-Nov-24	8.71	36.58	52.25	**97.54**	0.00	0.00	0.00	**0.00**	7.37	3.55	24.28	0.00	14.61	2.48	0.00	31.01	**83.31**	0.00	4.43	0.00	24.37	0.00	0.00	0.00	0.00	**28.81**
23-Nov-24	8.78	40.95	52.25	**101.97**	0.00	0.00	0.00	**0.00**	7.37	2.92	24.12	0.00	14.60	2.52	0.00	27.48	**79.01**	0.00	4.84	0.00	23.63	0.00	0.00	0.00	0.00	**28.47**
24-Nov-24	8.82	40.93	52.35	**102.11**	0.00	0.00	0.00	**0.00**	7.36	2.66	26.32	0.00	14.62	2.32	0.00	29.50	**82.79**	0.00	3.96	0.00	21.71	0.00	0.00	0.00	0.00	**25.66**
25-Nov-24	8.79	33.97	55.35	**98.11**	0.00	0.00	0.00	**0.00**	7.33	10.24	29.14	0.00	14.61	2.38	0.00	32.50	**96.20**	0.00	1.52	0.00	19.46	0.00	0.00	0.00	0.00	**20.97**
26-Nov-24	8.98	32.78	57.57	**99.32**	0.00	0.00	0.00	**0.00**	10.63	14.43	32.89	0.00	22.20	2.42	0.00	36.31	**118.88**	0.00	0.09	0.00	16.32	0.00	0.00	0.00	0.00	**16.41**
27-Nov-24	8.98	28.92	55.77	**93.67**	0.00	0.00	0.00	**0.00**	14.04	7.60	29.01	0.00	14.60	2.44	0.00	31.42	**99.11**	0.00	0.49	0.00	15.44	0.00	0.00	0.00	0.00	**15.93**
28-Nov-24	8.98	28.94	52.87	**90.79**	0.00	0.00	0.00	**0.00**	9.87	6.49	26.24	0.00	14.61	2.37	0.00	28.04	**87.61**	0.00	2.50	0.00	22.37	0.00	0.00	0.00	0.00	**24.88**
29-Nov-24	8.99	28.95	56.07	**94.01**	0.00	0.00	0.00	**0.00**	10.00	11.97	31.29	0.00	14.61	2.31	0.00	34.99	**105.16**	0.00	0.03	0.00	19.88	0.00	0.00	0.00	0.00	**19.91**
30-Nov-24	9.00	28.95	51.51	**89.46**	0.00	0.00	0.00	**0.00**	9.88	6.77	29.41	0.00	14.61	2.37	0.00	30.51	**93.56**	0.00	3.40	0.00	21.88	0.00	0.00	0.00	0.00	**25.28**
TOTAL	**323.46**	**1090.58**	**1542.96**	**2957.00**	**0.00**	**0.00**	**0.00**	**0.00**	**335.29**	**143.60**	**779.18**	**0.00**	**746.92**	**67.59**	**2.33**	**951.98**	**3026.89**	**0.00**	**148.25**	**0.85**	**690.35**	**0.00**	**0.00**	**0.01**	**0.01**	**839.47**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 **से मार्च** 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
अक्तूबर 2024 OCT'24	0.00	918.96	0.00	283.29	695.63	0.00	0.80	0.00
नवंबर 2024 NOV'24	12.24	125.37	0.00	212.20	698.58	0.00	0.71	0.00
कुल Total	150.08	5325.83	638.42	2129.85	5554.74	0.00	6.40	0.00

* Based on daily operational data

16.1 Import from neighbouring countries during Nov 2024

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Nov-24	5.68	0.00	0.00	0.00	1.65	4.95	0.74	0.29	0.00	0.00	1.52	8.94	0.11	0.00
2-Nov-24	5.23	0.00	0.00	0.00	1.55	4.67	0.64	0.29	0.00	0.00	1.53	9.22	0.00	0.00
3-Nov-24	5.08	0.27	0.00	0.00	1.41	4.24	0.63	0.27	0.00	0.00	1.56	9.62	0.00	0.00
4-Nov-24	8.14	0.00	0.00	0.00	1.25	3.78	0.62	0.32	0.00	0.00	1.55	9.58	0.00	0.00
5-Nov-24	11.40	0.00	0.00	0.00	1.10	3.33	0.68	0.31	0.00	0.00	1.50	10.11	0.00	0.00
6-Nov-24	10.73	0.00	0.00	0.00	1.12	3.37	0.66	0.31	0.00	0.00	1.49	10.10	0.00	0.00
7-Nov-24	10.51	0.00	0.00	0.00	0.97	2.94	0.63	0.29	0.00	0.00	1.50	10.51	0.00	0.00
8-Nov-24	10.55	0.00	0.00	0.00	0.88	2.65	0.64	0.25	0.00	0.00	1.45	10.64	0.00	0.00
9-Nov-24	9.60	0.00	0.00	0.00	0.68	2.57	0.61	0.28	0.00	0.00	1.52	10.54	0.00	0.00
10-Nov-24	10.23	0.00	0.00	0.00	1.03	3.13	0.57	0.26	0.00	0.00	1.47	9.27	0.00	0.00
11-Nov-24	9.74	0.00	0.00	0.00	0.37	2.41	0.55	0.17	0.00	0.00	1.36	8.42	0.00	0.00
12-Nov-24	9.81	0.00	0.00	0.00	0.00	3.53	0.48	0.12	0.00	0.00	1.41	7.67	0.00	0.00
13-Nov-24	9.61	0.00	0.00	0.00	0.00	2.54	0.49	0.10	0.00	0.00	1.32	6.61	0.00	0.00
14-Nov-24	9.21	0.00	0.00	0.00	0.00	2.73	0.53	0.61	0.00	0.00	1.44	6.34	0.00	0.00
15-Nov-24	8.87	0.00	0.00	0.00	0.00	2.60	0.56	0.15	0.00	0.00	1.35	5.60	0.00	0.00
16-Nov-24	9.42	0.00	0.00	0.00	0.00	2.63	0.47	0.16	0.00	0.00	1.37	5.96	0.00	0.00
17-Nov-24	9.11	0.00	0.00	0.00	0.00	2.31	0.41	0.10	0.00	0.00	1.33	5.20	0.00	0.00
18-Nov-24	8.25	0.00	0.00	0.00	0.64	2.19	0.46	0.19	0.00	0.00	1.13	4.72	0.00	0.00
19-Nov-24	8.48	0.00	0.00	0.00	1.10	1.68	0.31	0.20	0.00	0.00	0.90	3.31	0.00	0.00
20-Nov-24	8.46	0.00	0.00	0.00	0.85	1.30	0.34	0.14	0.00	0.00	0.78	3.17	0.00	0.00
21-Nov-24	8.77	0.00	0.00	0.00	0.76	1.19	0.34	0.11	0.00	0.00	0.66	2.74	0.00	0.00
22-Nov-24	8.36	0.00	0.00	0.00	0.58	0.93	0.30	0.10	0.00	0.00	0.70	2.83	0.00	0.00
23-Nov-24	8.03	0.00	0.00	0.00	0.61	0.96	0.21	0.08	0.00	0.00	0.69	4.80	0.00	0.00
24-Nov-24	7.98	0.00	0.00	0.00	0.53	0.85	0.34	0.04	0.00	0.00	0.61	2.89	0.00	0.00
25-Nov-24	8.01	0.00	0.00	0.00	0.40	0.64	0.14	0.01	0.00	0.00	0.59	2.63	0.00	0.00
26-Nov-24	7.21	0.00	0.00	0.00	0.59	0.93	0.24	0.04	0.00	0.00	0.24	2.13	0.00	0.00
27-Nov-24	7.74	0.00	0.00	0.00	0.47	0.77	0.14	0.03	0.00	0.00	0.18	1.86	0.00	0.00
28-Nov-24	7.80	0.00	0.00	0.00	0.37	0.92	0.00	0.08	0.00	0.00	0.00	1.56	0.00	0.00
29-Nov-24	7.75	0.00	0.00	0.00	0.36	0.57	0.05	0.00	0.00	0.00	0.00	1.91	0.00	0.00
30-Nov-24	6.90	0.00	0.00	0.00	0.31	0.55	0.06	0.02	0.00	0.00	0.00	2.32	0.00	0.00
Total	**256.69**	**0.27**	**0.00**	**0.00**	**19.58**	**67.85**	**12.84**	**5.32**	**0.00**	**0.00**	**31.16**	**181.17**	**0.11**	**0.00**

16.2 Export to neighbouring countries during Nov 2024

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Nov-24	0.00	0.00	0.79	0.45	0.00	0.00	0.00	0.00	22.04	1.58	0.00	0.00	0.00	0.03
2-Nov-24	0.00	0.00	0.82	0.36	0.00	0.00	0.00	0.00	22.00	1.50	0.00	0.00	0.00	0.02
3-Nov-24	0.00	0.00	0.91	0.36	0.00	0.00	0.00	0.00	22.02	1.62	0.00	0.00	0.00	0.03
4-Nov-24	0.00	2.55	1.06	1.29	0.00	0.00	0.00	0.00	21.56	1.59	0.00	0.00	0.00	0.03
5-Nov-24	0.00	5.07	1.27	1.95	0.00	0.00	0.00	0.00	21.97	1.57	0.00	0.00	0.00	0.03
6-Nov-24	0.00	4.56	1.13	1.43	0.00	0.00	0.00	0.00	21.93	1.29	0.00	0.00	0.00	0.03
7-Nov-24	0.00	4.57	1.12	1.27	0.00	0.00	0.00	0.00	21.91	1.31	0.00	0.00	0.00	0.02
8-Nov-24	0.00	5.24	0.95	0.96	0.00	0.00	0.00	0.00	21.85	1.22	0.00	0.00	0.00	0.02
9-Nov-24	0.00	4.70	1.70	1.11	0.00	0.00	0.00	0.00	21.82	1.29	0.00	0.00	0.00	0.02
10-Nov-24	0.00	4.53	1.73	1.17	0.00	0.00	0.00	0.00	21.67	1.36	0.00	0.00	0.00	0.02
11-Nov-24	0.00	5.13	2.16	1.78	0.00	0.00	0.00	0.00	22.05	1.50	0.00	0.00	0.00	0.02
12-Nov-24	0.00	5.14	2.12	1.84	0.00	0.00	0.00	0.00	22.09	1.54	0.00	0.00	0.00	0.02
13-Nov-24	0.00	5.19	2.24	1.79	0.00	0.00	0.00	0.00	22.11	1.31	0.00	0.00	0.00	0.02
14-Nov-24	0.00	5.44	2.25	1.72	0.00	0.00	0.00	0.00	22.31	1.39	0.00	0.00	0.00	0.03
15-Nov-24	0.00	5.46	2.32	1.73	0.00	0.00	0.00	0.00	22.57	1.19	0.00	0.00	0.00	0.02
16-Nov-24	0.00	5.37	2.39	1.84	0.00	0.00	0.00	0.00	22.15	1.28	0.00	0.00	0.00	0.02
17-Nov-24	0.00	5.23	2.53	1.87	0.00	0.00	0.00	0.00	22.23	1.27	0.00	0.00	0.00	0.02
18-Nov-24	0.00	5.70	3.14	2.03	0.00	0.00	0.00	0.00	22.04	1.21	0.00	0.00	0.00	0.02
19-Nov-24	0.00	5.80	3.08	2.06	0.00	0.00	0.00	0.00	21.87	1.20	0.00	0.00	0.00	0.02
20-Nov-24	0.00	5.69	2.33	2.19	0.00	0.00	0.00	0.00	22.15	1.08	0.00	0.00	0.00	0.03
21-Nov-24	0.00	5.62	2.38	2.12	0.00	0.00	0.00	0.00	22.14	1.07	0.00	0.00	0.00	0.02
22-Nov-24	0.00	5.67	2.69	1.95	0.00	0.00	0.00	0.00	22.11	0.99	0.00	0.00	0.00	0.03
23-Nov-24	0.00	5.70	2.70	1.89	0.00	0.00	0.00	0.00	22.11	0.93	0.00	0.00	0.00	0.03
24-Nov-24	0.00	5.63	2.92	1.99	0.00	0.00	0.00	0.00	22.15	0.96	0.00	0.00	0.00	0.02
25-Nov-24	0.00	5.60	2.87	1.97	0.00	0.00	0.00	0.00	22.13	1.14	0.00	0.00	0.02	0.02
26-Nov-24	0.00	5.62	2.82	1.86	0.00	0.00	0.00	0.00	22.05	1.36	0.00	0.00	0.02	0.02
27-Nov-24	0.00	5.90	3.06	1.91	0.00	0.00	0.00	0.00	22.02	1.32	0.00	0.00	0.02	0.02
28-Nov-24	0.00	5.73	2.94	1.94	0.00	0.00	0.06	0.00	22.14	1.19	0.03	0.00	0.02	0.02
29-Nov-24	0.00	5.96	3.11	1.93	0.00	0.00	0.00	0.12	20.23	1.23	0.00	0.00	0.02	0.01
30-Nov-24	0.00	5.87	3.04	1.84	0.00	0.00	0.00	0.00	20.17	1.19	0.08	0.00	0.02	0.02
Total	**0.00**	**142.68**	**64.55**	**48.59**	**0.00**	**0.00**	**0.06**	**0.12**	**657.62**	**38.67**	**0.11**	**0.00**	**0.13**	**0.71**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – नवंबर 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - NOVEMBER 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

नवंबर 2024 NOVEMBER 2024			Apr'24- Nov'24	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	280	207	5256	24415
प.क्षे. WR	305	218	3003	4330
द.क्षे. SR	324	248	2785	8553
पू.क्षे. ER	217	278	2795	11795
पूर्वोत्तर क्षे. NER	91	11	610	476
कुल TOTAL	1217	963	14449	49568

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
अक्तूबर 2024 Oct'24	12567	8372	1511	2332
नवंबर 2024 Nov'24	11553	9432	1217	963
कुल TOTAL	80415	69576	14449	49568

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
04.11.24 to 10.11.24	107.75	274.55	36.91	257.34	68.23
11.11.24 to 17.11.24	61.28	282.26	36.87	266.46	49.64
18.11.24 to 24.11.24	83.26	275.35	38.42	244.78	47.91
25.11.24 to 01.12.24	48.60	264.01	44.35	236.81	49.41

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- नवंबर 2024
EXCHANGES THROUGH POWER EXCHANGES-NOVEMBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	ACME PHALODI SOLAR ENERGY PRIVATE LIMITED_INFIRM	उत्तरी क्षेत्र NR	45.90	0.00
2	ACME RAISAR SOLAR ENERGY PRIVATE LIMITED_INFIRM		29.65	0.00
3	AD HYDRO POWER LIMITED		20.96	0.00
4	ADANI GREEN ENERGY TWENTY FIVE LIMITED_infirm		46.13	0.00
5	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		24.97	0.00
6	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		5.98	0.00
7	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		36.81	0.00
8	Adept Renewable Technologies Private Limited		18.25	0.00
9	Amp Energy Green Six Private Limited		17.00	0.00
10	Amplus Ages Private Limited		2.39	0.00
11	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		1.66	0.00
12	Chandigarh (UT)		28.54	2.54
13	Delhi		106.40	156.18
14	Government of Himachal Pradesh _ Chamera1HEP		6.12	0.11
15	Government of Himachal Pradesh _ Chamera3HEP		4.18	0.23
16	Government of Himachal Pradesh_ CHAMERA2HEP		4.81	0.45
17	Government of Himachal Pradesh_BairasuilHEP		2.02	0.09
18	Government of Himachal Pradesh_Koldam HEP		16.05	1.06
19	Government of Himachal Pradesh_NJHPS		37.08	1.15
20	Government of Himachal Pradesh_Parbati3HEP		2.78	0.18
21	Government of Himachal Pradesh_RampurHEP		11.03	0.34
22	Grian Energy Private Limited		1.77	0.00
23	Haryana		480.34	61.59
24	Himachal Pradesh		102.08	67.54
25	IGSTPS JHAJJAR		10.86	0.00
26	JUNIPER GREEN COSMIC PRIVATE LIMITED		14.41	0.00
27	Jammu Kashmir		20.47	316.67
28	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		28.77	0.01
29	KHURJA STPP		32.90	0.00
30	NEA Nepal Upper Chameliya Hydropower Project		21.66	0.00
31	NEA Nepal Upper Kalangagad Hydropower Project new		9.48	0.00
32	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	0.65
33	NTPC Dadri Stage I		6.81	0.00
34	NTPC Dadri Stage II		6.97	0.00
35	NTPC Rihand stage I		12.24	0.00
36	NTPC Rihand stage II		9.20	0.00
37	NTPC Rihand stage III		13.24	0.00
38	NTPC Singrauli		19.99	0.00
39	NTPC Tanda Stage II		6.12	0.00
40	NTPC Unchahar Stage I		1.66	0.00
41	NTPC Unchahar Stage II		1.14	0.00
42	NTPC Unchahar Stage III		1.37	0.00
43	NTPC Unchahar Stage IV		3.31	0.00
44	North Central Railway Prayagraj		0.00	18.68

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- नवंबर 2024 EXCHANGES THROUGH POWER EXCHANGES-NOVEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	Onevolt Energy Private Limited		4.11	0.00
46	Punjab		12.14	415.41
47	RENEW SURYA PRATAP PRIVATE LIMITED		36.04	0.00
48	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.04	0.00
49	Rajasthan		87.32	637.81
50	ReNew Surya Ravi Private Limited		38.20	0.00
51	SHREE CEMENT LIMITED TPS		0.73	0.00
52	Sainj HEP		8.33	0.07
53	Serentica Renewables India 4 Private Limited		0.91	0.00
54	Serentica Renewables India 5 Private Limited		15.74	0.00
55	Singoli Bhatwari HEP		18.93	0.00
56	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		0.86	0.00
57	TPSL 200MW TPTCL Banderwala		11.17	0.00
58	TPSL Banderwala SECI 100_INF		1.40	0.00
59	TRANSITION SUSTAINABLE ENERGY SERVICES ONE PRIVATE LIMITED-Infirm		0.14	0.00
60	Transition Energy Services Private Limited		9.53	0.00
61	Transition Green Energy Private Limited		14.00	0.00
62	Transition Sustainable Energy Services One Private Limited		8.40	0.00
63	Uttar Pradesh		403.14	451.88
64	Uttarakhand		40.10	224.19
65	2X600 VEDANTA LIMITED Chhattisgarh Power Plant		0.00	0.01
66	ACB (INDIA) LIMITED		42.34	0.36
67	ADANI GREEN ENERGY TWENTY SIX A LIMITED_infirm		0.85	0.00
68	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3_infirm (162.5 MW Hybrid Solar of 187.5MW HPD)		27.43	0.00
69	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3_infirm (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.02	0.00
70	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3_infirm (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		0.03	0.00
71	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_infirm		18.08	0.00
72	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		172.68	0.00
73	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		25.57	0.00
74	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		2.99	0.00
75	AMBUJA CEMENTS LIMITED(Khavda PSS-3)_infirm		6.84	0.00
76	Adani Green Energy Twenty Five A Limited_Infirm		41.41	0.00
77	Adani Green Energy Twenty Five B Limited_infirm		85.07	0.00
78	Adani Green Energy Twenty Four A Limited_infirm		0.26	0.00
79	Adani Green Energy Twenty Six B Limited_infirm		16.63	0.00
80	Adani Power Limited - Raigarh TPP		131.51	23.67
81	Adani Power Limited-Raipur TPP		372.17	8.26
82	ArcelorMittal Nippon Steel India Limited		0.00	224.08
83	BHARAT ALUMINIUM COMPANY LTD		17.63	0.00
84	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	5.55
85	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		0.27	0.00
86	Chhattisgarh		739.80	0.80
87	D B Power Limited		58.19	0.00
88	DGEN MEGA POWER PROJECT		0.22	0.00
89	DHARIWAL STU OTH		1.84	0.00
90	Daman and Diu - Dadra and Nagar Haveli		0.06	147.54
91	Dhariwal ISTS		9.07	0.00
92	GMR Warora Energy Limited		4.43	0.00
93	Goa WR		8.50	18.14

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- नवंबर 2024
EXCHANGES THROUGH POWER EXCHANGES-NOVEMBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
94	Gujarat	पश्चिमी क्षेत्र WR	38.28	1337.55
95	Jaypee Nigrie Super Thermal Power Plant		236.92	0.00
96	Jhabua Power Limited		36.04	0.00
97	Jindal Power Limited, Stage-1		163.91	3.15
98	Jindal Power Limited, Stage-2		519.97	0.23
99	Jindal Steel & Power Ltd , DCPP		101.19	3.81
100	LANCO AMARKANTAK POWER LIMITED		0.57	0.00
101	MAHAN ENERGEN LIMITED U#1		171.44	0.00
102	MAHAN ENERGEN LIMITED U#2		249.49	0.00
103	MB POWER (MADHYA PRADESH) LIMITED		21.34	0.00
104	Madhya Pradesh		146.55	280.32
105	Maharashtra		41.28	1444.97
106	Maruti Clean Coal and Power Limited		2.82	0.00
107	NREL-Dayapar Wind		2.26	0.00
108	NTPC Gadarwara		4.05	0.00
109	NTPC Jhanor Gandhar GPS		0.00	0.75
110	NTPC Kawas GPS		0.00	0.74
111	NTPC Korba Stage I &II		3.25	0.00
112	NTPC Korba Stage III		1.11	0.00
113	NTPC Lara Stage I		3.49	0.00
114	NTPC Mouda Stage I		2.61	0.00
115	NTPC Mouda Stage II		3.00	0.00
116	NTPC SAIL POWER COMPANY LIMITED		0.10	0.00
117	NTPC SOLAPUR SOLAR PV Station		0.72	0.00
118	NTPC Sipat Stage I		2.95	0.00
119	NTPC Sipat Stage II		1.86	0.00
120	NTPC Solapur		5.48	0.00
121	NTPC Vindhyachal Stage I		2.50	0.00
122	NTPC Vindhyachal Stage II		0.60	0.00
123	NTPC Vindhyachal Stage III		2.60	0.00
124	NTPC Vindhyachal Stage IV		1.85	0.00
125	NTPC Vindhyachal Stage V		1.43	0.00
126	NTPC khargone		4.19	0.00
127	Nani Virani Wind Energy Private Limited		0.47	0.00
128	R.K.M POWERGEN PRIVATE LIMITED		9.86	0.00
129	Ratnagiri Gas & Power Private Limited		0.00	2.66
130	SKS Power Generation Chhattisgarh Limited		33.46	19.17
131	Sasan Power Limited		12.89	0.00
132	TRN ENERGY PRIVATE LIMITED		19.55	0.18
133	The Tata Power Co Ltd (MTPS)		9.90	0.00
134	WIND FIVE RENERGY LIMITED		2.80	0.00
135	Andhra Pradesh		48.60	636.93
136	COASTAL ENERGEN PRIVATE LIMITED		0.80	0.00
137	Goa SR		0.00	8.84
138	IL&FS TAMIL NADU POWER COMPANY LIMITED		0.86	0.00
139	JINDAL POWER LIMITED SIMHAPURI		20.17	0.40
140	JSW RENEW ENERGY LIMITED INFIRM		5.64	0.00
141	Karnataka		287.14	188.90
142	Kerala		7.94	216.73

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- नवंबर 2024
EXCHANGES THROUGH POWER EXCHANGES-NOVEMBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
143	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION	दक्षिणी क्षेत्र SR	7.11	0.00
144	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		1.62	0.00
145	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.57	0.00
146	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		1.37	0.00
147	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		1.18	0.00
148	NLC Tamilnadu Power Limited		6.15	0.00
149	NTECL VALLUR		0.30	0.00
150	NTPC KUDGI		2.13	0.00
151	NTPC Ramagundam Stage I &II		1.61	0.00
152	NTPC Ramagundam Stage III		0.00	0.00
153	NTPC Simhadri Stage I		0.01	0.00
154	NTPC Simhadri Stage II		0.40	0.00
155	NTPC Talcher Super Thermal Power Station Stage II		5.56	0.00
156	NTPC Telangana		7.94	0.00
157	OSTRO KANNADA POWER PRIVATE LIMITED		12.38	0.00
158	Pondicherry UT		7.97	0.40
159	RENEW SURYA OJAS PRIVATE LIMITED-Wind		45.91	0.00
160	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		1.33	0.00
161	Ramagundam Floating solar		3.56	0.00
162	SEIL ENERGY INDIA LIMITED		64.54	0.00
163	SEIL Energy India Limited Project II		25.79	0.00
164	SEMBCORP GREEN INFRA PRIVATE LIMITED (INFIRM)		7.46	0.00
165	Serentica Renewables India 1 Private Limited		0.05	0.00
166	Serentica Renewables India 1 Private Limited- Koppal (Infirm)		1.33	0.00
167	Simhadri FSP 15 MW		1.70	0.00
168	Simhadri Floating solar (10 MW)		1.12	0.00
169	Tamil Nadu		160.22	529.15
170	Telangana		44.63	1105.38
171	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	4.48	0.00
172	Bihar		869.90	0.00
173	Chuzachen HEP		0.02	0.00
174	DEVIGHAT NEPAL ELECTRICITY AUTHORITY		1.29	0.00
175	Damodar Valley Corporation		41.95	166.79
176	Dikchu Hydro Electric Project (Sneha Kinetic Power Projects Pvt. Ltd.)		3.67	0.00
177	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	24.16
178	GMR KAMALANGA ENERGY LTD-CTU		0.92	0.00
179	IND BARATH ENERGY UTKAL LIMITED		109.73	0.00
180	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.01	0.00
181	Jharkhand		146.68	25.09
182	Jindal India Power Limited		147.17	0.00
183	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		75.45	0.00
184	KANTI BIJLEE UTPADAN NIGAM LIMITED		11.75	0.00
185	LIKHU-iV NEA		16.83	0.00
186	Lower Modi Hydro Power Project NEPAL ELECTRICITY AUTHORITY		3.98	0.00
187	MAITHON POWER LIMITED		6.28	0.00
188	MARSYANGDI NEPAL ELECTRICITY AUTHORITY		26.90	0.00
189	NABINAGAR POWER GENERATING COMPANY LIMITED		33.05	0.00
190	NEA Nepal Upper Dordi A Hydropower Project		6.72	0.00
191	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	0.77

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- नवंबर 2024 EXCHANGES THROUGH POWER EXCHANGES-NOVEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
192	NEPAL ELECTRICITY AUTHORITY-MIDDLE MARSYANGDI		31.60	0.00
193	NTPC BARH Stage I		20.37	0.00
194	NTPC BARH Stage II		25.00	0.00
195	NTPC Darlipali		7.82	0.00
196	NTPC Farakka stage I		41.09	0.00
197	NTPC Farakka stage III		11.17	0.00
198	NTPC Kahalgaon stage I		7.36	0.00
199	NTPC Kahalgaon stage II		21.00	0.00
200	NTPC North Karanpura STPS		26.00	0.00
201	NTPC Talcher Stage I		22.01	0.00
202	NTPP BRBCL		6.23	0.00
203	Odisha		703.06	275.36
204	Sikkim		22.10	0.14
205	Solu Hydropower Project NEPAL ELECTRICITY AUTHORITY		5.58	0.00
206	West Bengal		233.26	238.56
207	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	9.84	0.00
208	ASSAM GAS BASED POWER STATION		1.38	0.00
209	Arunachal Pradesh		22.75	0.59
210	Assam		197.32	51.50
211	Bongaigaon Thermal Power Station NTPC		2.90	0.00
212	KAMENG HYDRO POWER STATION		15.91	0.00
213	Manipur		21.32	5.88
214	Meghalaya		19.91	54.38
215	Mizoram		3.15	0.00
216	Nagaland		8.67	1.27
217	Palatana Plant		18.22	0.00
218	Tripura		3.74	22.09
	Total		9432	9432

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : NOVEMBER 2024

RE Source & Unit wise break up (01.11.2024-30.11.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3	1	0	0
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	184	3	0	0
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**187**	**4**	**0**	**0**

RECs Issued (01.11.2024-30.11.2024)

Sr.No.	Non Solar	Solar	Total
1	3933185	160968	4094153

Redemption of REC (01.11.2024-30.11.2024)

Sr.No.	Non Solar	Solar	Total
1	593677	10227	603904

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : NOVEMBER 2024

RE Source & Unit wise break up (Apr'24-Nov'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	43	6	20	5
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	281	21	83	16
5	Small Hydro	24	1	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**348**	**28**	**139**	**23**

RECs Issued (Apr'24-Nov'24)

Sr.No.	Non Solar	Solar	Total
1	32879022	764628	33643650

Redemption of REC (Apr'24-Nov'24)

Sr.No.	Non Solar	Solar	Total
1	15827932	231784	16059716

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : NOVEMBER 2024

RE Source & Unit wise break up Since Inception to Nov'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3176	536	2997	536
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	1917	595	1563	498
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**7203**	**1305**	**6217**	**1171**

RECs Issued since Inception to Nov'24

Sr.No.	Non Solar	Solar	Total
1	147984060	14305006	162289066

Redemption of REC since Inception to Nov'24

Sr.No.	Non Solar	Solar	Total
1	94332261	12681041	107013302

REC Closing balance as on 30.11.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

20. Details of Grid Events during the Month of Nov 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	Rajasthan	01-11-2024 12:47	01-11-2024 15:04	02:17	300	0	0.604	0.000	49642	49437	i)Total generation of 220kV Saurya Urja(IP) S/s is evacuated to Bhadla(RS) at 220kV level through 220 kV Bhadla(RS)-Saurya Urja D/C. ii)During antecedent condition, 220 kV Bhadla(RS)-Saurya Urja Ckt-1 & 2 were carrying approx. 245 MW and 239 MW respectively. iii)As reported at 12:47 hrs, 220 kV Bhadla(RS)-Saurya Urja Ckt-1 tripped from Bhadla(RS) end only on R-N phase to earth fault with fault current of 5kA and fault distance of 1.85km from Bhadla(RS) end; fault sensed in zone-1 from Bhadla(RS) end. Exact reason of fault cannot be identified after patrolling. Hence it seems that fault was of transient nature and there was issue in A/R operation at Bhadla(RS) end. iv)As per PMU at Bhadla(PG), 3-phase to earth fault is observed with fault clearing time of 80msec. v)As per SCADA, change in solar generation of approx. 300 MW and no change in demand are observed in Rajasthan control area.	1) 220 kV Bhadla(RS)-Saurya Urja Ckt-1
2	GI-2	Uttar Pradesh	02-11-2024 01:51	02-11-2024 03:23	01:32	0	130	0.000	0.331	31301	39244	i)400/220kV Aligarh(UP) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii)As reported, at 01:51 hrs, 400 KV Aligarh-Muradnagar_1 (UP) Ckt tripped on B-N phase to earth fault with fault current of 2.912kA from Muradnagar_1 end and 18.916kA from Aligarh end; fault sensed in zone-1 at Aligarh end and zone-2 at Muradnagar_1 end. As per DR at Muradnagar_1 end, fault clearing time was ~377ms (delay in fault clearing at Muradnagar_1, carrier not received). As per DR at Aligarh end, unsuccessful A/R was observed with A/R dead time of 840 ms (less A/R dead time observed). iii)During the same time, 400 KV Aligarh-Shamli (UP) Ckt-1 & 2 also tripped on over-voltage at Aligarh end (as per EL of Main-1 at Aligarh). As per DR, R-ph voltage reached upto ~1.35 p.u. at Aligarh end of 400 KV Aligarh-Shamli (UP) Ckt-1 and B-N phase to earth fault with fault current of 642 A from Aligarh end is observed in 400 KV Aligarh-Shamli (UP) Ckt-2. Time sync issue is observed in Main-2 relay at Aligarh end of both 400 KV Aligarh-Shamli (UP) Ckt-1 & 2. As reported, DT received at Shamli end for both the lines. iv)As per PMU at Mainpuri(PG), B-N phase to earth fault with unsuccessful A/R is observed with fault clearing time of 80ms. v)As per SCADA, change in demand of approx. 130 MW is observed in UP control area.	1) 400 KV Aligarh-Muradnagar_1 (UP) Ckt 2) 400 KV Aligarh-Shamli (UP) Ckt-1 3) 400 KV Aligarh-Shamli (UP) Ckt-2
3	GI-1	Himachal Pradesh	06-11-2024 20:45	06-11-2024 22:54	02:09	125	0	0.319	0.000	39236	52045	i)During antecedent condition, 66MW Unit-2, 3, 5 & 6 at Pong HEP were running and generating approx. 66MW, 66MW, 64MW and 56MW respectively (as per SCADA). 66MW Unit-1 & 4 at Pong HEP were not in service. ii)As reported, at 20:45 hrs, while stopping 66 MW Unit-6 at Pong (BB), the Relay MICOM P643- CB Head Flashover operated. As informed by the site, the Earth Fault relay connected to Unit-06 GT neutral operated, and the CB of Unit-6 opened. However, the Earth Fault current did not reduce to 0 A immediately. As a result, due to the AND operation logic (where the CB is open and the Earth Fault remains active), the CB Head Flashover was initiated, causing simultaneous tripping of 220 kV Bus-2 at Pong(BB). iii)As 220 KV Jalandhar-Pong (BB) Ckt-2, 220 KV Jessore(HP)-Pong(BB) (PG) Ckt-1, 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-2 and 66 MW Pong HPS - UNIT 2 were connected to 220 kV Bus-2 at Pong(BB), all these elements tripped from Pong end along with Bus-2. iv)As discussed with BBMB personnel, a delay of 15 ms is kept for reduction of earth fault current to 0 A (in case of CB open condition) in CB Head Flashover protection logic to avoid overlapping conditions. v)As per PMU at Jalandhar(PG), no fault is observed in the system. However, fluctuation in voltage is observed. vi)As per SCADA, generation loss of approx. 125 MW at Pong HEP (BB) and no load loss is observed in HP control area.	1) 66 MW Pong HPS - UNIT 6 2) 66 MW Pong HPS - UNIT 2 3) 220KV Bus 2 at Pong(BB) 4) 220 KV Jalandhar-Pong (BB) Ckt-2 5) 220 KV Jessore(HP)-Pong(BB) (PG) Ckt-1 6) 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-2
4	GI-2	Uttar Pradesh	11-11-2024 15:56	11-11-2024 21:44	05:48	0	0	0.000	0.000	43687	53628	i)During antecedent condition, 400 kV Firozabad–Jawaharpur Ckt 2 (28 MW) and 400/220 kV 500 MVA ICT 4 (27 MW) were connected to 400 kV Bus 2. 400 kV Firozabad–Jawaharpur Ckt 1 (26 MW), 125 MVAR bus reactor, and 400/220 kV 500 MVA ICT 3 (27 MW) were connected to 400 kV Bus 1. The 765/400 KV ICT 1 and 2 were not in service at that point of time. ii)As reported at 15:56:14:463 hrs, R-N fault occurred at TEED portion of bay 401 & 402. On this fault, bus bar protection of 400KV Bus-2 at 400 KV JAWAHARPUR_TPS(UP) operated. This led to tripping of breakers 410, 407 & 401 bay connected to 400KV Bus 2. At the same time (with the gap of 20msec), TEED protection operated which tripped Bay 402 (Tie Bay of 400/220KV ICT 3 & 4). This led to tripping of 400/220KV ICT 4. Further after ~30msec, 400KV Bay No 403 breaker opened led to the tripping 400/220 KV ICT 3 at Jawaharpur(UP). Exact reason of operation of bus bar protection along with TEED protection is yet to be received from UP. DR/EL of the tripping events also yet to be received. iii)After further 60msec, 125 MVAR Bus Reactor No 1 at 400 KV Jawaharpur_TPS(UP) also tripped on back up impedance protection operation. DR of the tripping is yet to be received. iv)As per PMU at Mainpuri (PG), R-N fault which cleared within 100msec is observed. v)As per SCADA, no load loss is observed in UP control area.	1) 400 KV Jawaharpur_TPS(UP) - Bus 2 2) 400/220 kV 500 MVA ICT 3 at Jawaharpur_TPS(UP) 3) 400/220 kV 500 MVA ICT 4 at Jawaharpur_TPS(UP) 4) 410 MAIN BAY - 400 KV FIROZABAD(PJFTL)-JAWAHARPUR_TPS(UP) (UP) CKT-2 (UPRVUNL) AT 400 KV JAWAHARPUR_TPS(UP) 5) 125 MVAR Bus Reactor No 1 at 400 KV Jawaharpur_TPS(UP)
5	GI-2	Rajasthan	11-11-2024 12:22	11-11-2024 23:55	11:33	0	635	0.000	1.110	50765	57194	i)During antecedent condition, loading of 400/220 kV 315 MVA ICT 1 & 2 and 220/132kV 100MVA ICT-1, 2 & 3 at Merta(RS) were 171 MW, 177 MW, 62 MW, 62 MW and 56 MW respectively as per SCADA. 220kV Merta(RS)-Makrana(RS) Ckt was not in service. ii)As reported, at 12:22hrs, R-phase jumper of 220 kV Merta-Jethana snapped, and this broken jumper conductor fell on both 220 kV Bus-A and Bus-B at Merta. Because of this, Bus Bar protection operated at 400/220/132kV Merta S/s. iii)As a result, both 220KV Bus 1 & 2, along with all the elements connected to them i.e., 400/220 ICT-1 & 2, 220KV MERTA-JETHANA(RS), 220KV MERTA-BHOPALGARH (RS), 220KV MERTA-KUCHERA (RS), 220/132 KV 100 MVA ICT 1, ICT 2 & ICT 3 AT MERTA(RS) tripped. iv)As per PMU at Merta(RS), R-Y-B fault is observed with delayed fault clearance time of 720 msec. v)As per SCADA, change in demand of approx. 635 MW is observed in Rajasthan control area.	1) 220KV BUS1&2 AT MERTA(RS) 2) 400/220 KV 315 MVA ICT 1 AT MERTA(RS) 3) 400/220 KV 315 MVA ICT 2 AT MERTA(RS) 4) 220KV MERTA-BHOPALGARH (RS) CKT 5) 220KV MERTA-KUCHERA (RS) CKT 6) 220/132 KV 100 MVA ICT 1 AT MERTA(RS) 7) 220/132 KV 100 MVA ICT 2 AT MERTA(RS) 8) 220/132 KV 100 MVA ICT 3 AT MERTA(RS) 9) 220KV MERTA-JETHANA(RS) CKT

Details of Grid Events during the Month of Nov 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
6	GI-1	Rajasthan	16-11-2024 05:21	16-11-2024 07:23	02:02	0	325	0.000	0.762	31398	42640	i)As reported, at 05:21 hrs, interrupter of CB Pole (R-Ph.) blasted at the time of opening of CB of 125MVAR Bus Reactor at Hindaun (RS) on voltage regulation. ii)During the same time, 400 KV Hindaun(RS)-Chhabra(RVUN) (RS) Ckt, 400 KV Heerapura-Hindaun (RS) Ckt, and 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt at Hindaun(Raj) also tripped (exact reason of tripping yet to be shared). iii)As per DR of 400 KV Hindaun(RS)-Chhabra(RVUN) (end) (RS) Ckt, zone-2 distance protection operated at Chhabra end. R-N phase to earth fault was observed with fault current of 1.676kA and delayed fault clearance time of ~350ms. (DR nomenclature & time sync issue in DR need to be corrected.) iv)As per PMU at Heerapura (RS) and DR of Chhabra end, R-N fault is observed with delayed fault clearance time of 360 ms. v)As per SCADA, load loss of approx. 325 MW in Rajasthan control area was observed.	1) 125 MVAR BUS REACTOR NO 1 AT 400KV HINDAUN(RS) 2) 400 KV Heerapura-Hindaun (RS) CKT-1 3) 400 KV Hindaun(RS)-Chhabra(RVUN) (RS) Ckt 4) 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt
7	GI-1	Himachal	21-11-2024 08:42	21-11-2024 08:57	00:15	0	155	0.000	0.285	41923	54379	i)220/132 KV Hamitpur-II(HP) substation has double Bus scheme in both 220KV and 132KV system. It has 3 (three) 220/132 KV ICTs along with 2 circuits connecting to 220KV Hamirpur (PG) and in 132 KV Hamirpur I – Hamirpur-II Ckt1 & 2, 132 KV Hamirpur II – Kangoo Ckt.1 & 2 and 132KV Hamirpur-II – Dehra I & II. ii)As reported at 08:42hrs, 132 KV Hamirpur II – Kangoo Ckt-1 & 2 tripped (exact reason of tripping yet to be shared). iii)Also SCADA data for 132 KV Hamirpur II – Kangoo Ckt-1 & 2 wasn't available before or after the tripping incident. iv)As per PMU at Hamirpur (PG) end, no fault was observed. v)As per SCADA, a change in demand of approx. 155 MW is observed in Himachal Pradesh control area.	(i)132 KV HAMIRPUR-II (Mattansidh)(HPSEBL)-Kangoo(HPSEBL) 1 (ii)132 KV HAMIRPUR-II (Mattansidh)(HPSEBL)-KANGOO(HPSEBL) 2
8	GI-2	Rajasthan	23-11-2024 22:11	24-11-2024 00:02	01:51	0	0	0.000	0.000	29764	42355	i)During antecedent condition, 400 kV Firozabad–Jawaharpur Ckt 2 (28 MW) and 400/220 kV 500 MVA ICT 4 (27 MW) were connected to 400 kV Bus 2. 400 kV Firozabad–Jawaharpur Ckt 1 (26 MW), 125 MVAR bus reactor, and 400/220 kV 500 MVA ICT 3 (27 MW) were connected to 400 kV Bus 1. The 765/400 KV ICT 1 and 2 were not in service at that point of time. ii)As reported at 15:56:14:463 hrs, R-N fault occurred at TEED portion of bay 401 & 402. On this fault, bus bar protection of 400KV Bus-2 at 400 KV JAWAHARPUR_TPS(UP) operated. This led to tripping of breakers 410, 407 & 401 bay connected to 400KV Bus 2. At the same time (with the gap of 20msec), TEED protection operated which tripped Bay 402 (Tie Bay of 400/220KV ICT 3 & 4). This led to tripping of 400/220KV ICT 4. Further after ~30msec, 400KV Bay No 403 breaker opened led to the tripping 400/220 KV ICT 3 at Jawaharpur(UP). Exact reason of operation of bus bar protection along with TEED protection is yet to be received from UP. DR/EL of the tripping events also yet to be received. iii)After further 60msec, 125 MVAR Bus Reactor No 1 at 400 KV Jawaharpur_TPS(UP) also tripped on back up impedance protection operation. DR of the tripping is yet to be received. iv)As per PMU at Mainpuri (PG), R-N fault which cleared within 100msec is observed. v)As per SCADA, no load loss is observed in UP control area.	(i)400 KV Bhadla-Merta (RS) Ckt-1 (ii)400 KV Bikaner-Bhadla (RS) Ckt-1 (iii)400 KV Bikaner-Bhadla (RS) Ckt-2
9	GI-1	Jammu &Kashmir	26-11-2024 14:13	26-11-2024 15:20	01:07	0	260	0.000	0.506	47538	51370	i)220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. 220kV Amargarh-Ziankote ckt-1&2 are on the same tower (D/C tower) and line length is ~21.4km. ii)During antecedent condition, 220kV Amargarh (INDIGRID) –Ziankote(JK) D/C was carrying 138 MW each and feeding Ziankote load. iii)As reported, at 14:13 hrs, 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 tripped on B-N phase to earth fault with fault distance of 22.34 km (as per EL) and fault current of Ib=~2.81kA (as per DR) from Amargarh end. Fault sensed in zone-2 at Amargarh end. iv)During the same time, 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2 also tripped on B-N phase to earth fault with fault distance of 27.46km (as per EL) and fault current of Ib=~3.43kA (as per DR) from Amargarh end. Fault sensed in zone-2 at Amargarh end. v)As confirmed by Amargarh (INDIGRID), in view of non-availability of carrier communication and A/R scheme at Ziankote end, A/R has been kept disabled at Amargarh end and time delay of Z-2 was also kept as instantaneous at Amargarh end. vi)As per PMU at Amargarh (PG), B-N phase to earth fault which cleared within 80 msec is observed. vii)As per SCADA, change in demand of approx. 260 MW is observed in J&K control area.	(i)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 (ii)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2
10	GD-1	Jammu &Kashmir	27-11-2024 14:50	27-11-2024 15:33	00:43	110	0	0.234	0.000	46964	52087	i)During antecedent condition, 130MW Unit-2 at Dulhasti HEP were running generating approx. 110 MW and total generated power of 110MW was evacuating through 400 kV Dulhasti(NH)-Kishenpur(PG) (PG) Ckt-1 only. 130MW Unit-1 & 3 at Dulhasti HEP and 400 kV Dulhasti(NH)-Kishenpur(PG) (PG) Ckt-2 were not in service. ii)As reported, at 14:50hrs, 400 kV Dulhasti(NH)-Kishenpur(PG) (PG) Ckt-1 tripped on Y-N phase to earth fault (Exact reason, location and nature of fault along with DR/EL yet to be shared). As per PMU, unsuccessful A/R is observed with fault current of ~2.025kA followed by ~2.282kA from Kishenpur(PG) end. iii)Due to tripping of 400 kV Dulhasti(NH)-Kishenpur(PG) (PG) Ckt-1, 130MW Unit-2 at Dulhasti HEP tripped due to loss of evacuation path on over-speed protection operation. iv)As per PMU at Kishenpur (PG), Y-N phase to earth fault with unsuccessful A/R is observed with fault clearing time of 80ms. v)As per SCADA, generation loss of approx. 110MW is observed at Dulhasti HEP.	(i)400 KV Dulhasti(NH)-Kishenpur(PG) (PG) Ckt-1 (ii)130MW Unit-2 at Dulhasti HEP

Details of Grid Events during the Month of Nov 2024 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	03-11-2024 19:25	03-11-2024 20:04	00:39	-	44	-	0.08%	51438	58515	At 19:25 Hrs / 03-11-2024, 220 kV Kalwa-Knowldge Park tripped from Kalwa end only on Z-2 protection operation on Y-E fault, due to Y phase CT flashover and snapping of Y phase jumper at Knowledge Park during hand tripping of 220 kV Nasik-Knowledge Park. Line didn't tripped from Knowledge Park end which is undesirable. Load loss of 44 MW occurred at 220 kV Knowledge Park (Maharashtra) substation due to the event.	Tripping of following Elements: 1. 220 kV Kalwa-Knowledge Park
2	GI-2	WR	05-11-2024 02:50	05-11-2024 08:08	05:18	-	-	-	-	57621	49265	At 02:46 Hrs / 05-11-2024, 400 kV Ukai-Vav tripped on over voltage protection operation at Ukai end. After two minutes at 02:48 hrs, 400 kV Ukai-Kosamba-2 tripped on overvoltage protection operation at Ukai end. Further, after two minutes at 02:50 hrs, 400/220 kV Ukai-ICT-1 (315 MVA) tripped on over flux operation. Prior to the incident 400 kV Ukai-Kosamba-3 was manually opened due to high voltage and all units at Ukai were under Reserved Shut Down (RSD). No Load loss or generation loss occurred due to the event and 220 kV Ukai network was unaffected.	Tripping of following Elements: 1. 400 kV Ukai-Vav 2. 400 kV Ukai-Kosamba-2 3. 400/220 kV Ukai-ICT-1 (315 MVA)
3	GI-2	WR	06-11-2024 02:51	06-11-2024 08:57	06:06	-	-	-	-	60628	50993	At 02:51 Hrs / 06-11-2024, 400 kV Ukai-Vav tripped on over voltage protection operation at Ukai end. Simultaneously, 400/220 kV Ukai-ICT-1 (315 MVA) tripped on over flux operation. Prior to the incident 400 kV Ukai-Kosamba-2&3 were manually opened due to high voltage and all units at Ukai were under Reserved Shut Down (RSD). No Load loss or generation loss occurred due to the event and 220 kV Ukai network was unaffected.	Tripping of following Elements: 1. 400 kV Ukai-Vav 2. 400/220 kV Ukai-ICT-1 (315 MVA)
4	GD-1	WR	10-11-2024 11:19	10-11-2024 12:14	00:55	-	68	-	0.11%	68067	64427	At 11:19 Hrs / 10-11-2024, 220 kV Bhandup-Mulund tripped on B-E fault on Z-1 protection at both end due to fault in underground cable portion near Bhandup end. Auto recloser was disabled in 220 kV Bhandup-Mulund (being an transmission line with a mix of over head and underground cable portion). Simaltaneously 220 kV Bhandup-Borivali tripped from Borivali end only on Z-1 operation due to overreaching of relay at Borivali end (Fault in Z-2 seen as Z-1 fault). With this 220 kV Bhandup became dead. Prior to the incident 220 kV Borivali-Kalwa and 220 kV Borivali-CtrlS Datacenter circuit were under shutdown. Load loss of 68 MW occurred at Bhandup due to the event.	Tripping of following Elements: 1. 220 kV Bhandup-Mulund 2. 220 kV Bhandup-Borivali
5	GD-1	WR	25-11-2024 20:45	25-11-2024 21:28	00:43	-	200	-	0.36%	63730	55093	At 20:45 Hrs / 25-11-2024, all elements at 220 kV Apta (Details in elements tripped column) tripped on Busbar protection operation due to Y phase CT burst of 220 kV Apta-Bus Sectionaliser (Single Bus with Bus sectionalizer) . Load loss of 200 MW occurred at Apta substation during the event.	Tripping of following Elements: 1. 220 kV Uran-Apta-1,2,3&4 2. 220 kV Apta-ACCIL 3. 220 kV Apta-Bombay Dyeing 4. 220 kV Apta-Navi Mumbai-1&2 5. 220 kV Apta-Tambati 6. 220 kV Apta-HOC Apta 7. 220 kV Apta-ICT-1,2,3&4 (200 MVA)
6	GI-1	WR	27-11-2024 16:20	27-11-2024 17:16	00:56	-	-	-	-	72782	68152	At 16:20 Hrs / 27-11-2024, all elements connected to 220 kV Kansari-Bus-1 (Details in elements tripped column) tripped on bus bar protection operation of 220 kV Kansari-Bus-1 (Double main and transfer bus scheme) due to conductive wire coming in induction zone of Busbar Jumper. No Load loss or generation loss occurred due to the event and 220 kV Kansari-Bus-2 network was unaffected.	Tripping of following Elements: 1. 220 kV Kansari-Palanpur-1 2. 220 kV Kansari-Thaver-1 3. 220 kV Kansari-Deodar-1 4. 220 kV Kansari-Agthala 5. 400/220 kV Kansari-ICT-2&3 (315 MVA)
7	GI-1	WR	28-11-2024 17:17	28-11-2024 18:25	01:08	260	-	0.36%	-	72826	66865	At 17:17 Hrs / 28-11-2024, all elements connected to 220 kV Omkareshwar-Bus-2 (Details in elements tripped column) tripped on LBB operation during synchronizing of Omkareshwar-Unit-2 (65 MW) (Double main bus scheme). LBB operation was undesirable, Omkareshwar-Unit-2 (65 MW) should have been tripped on Pole Discrepancy operation due to non-closing of R phase circuit breaker. Generation loss of 260 MW occurred at Omkareshwar Hydro Plant due to tripping of Omkareshwar-Unit-3,4,6&8 (65 MW).	Tripping of following Elements: 1. 220 kV Omkareshwar-Bus-2 2. 220 kV Omkareshwar-Barwaha 3. 220 kV Omkareshwar-Julwaniya 4. 220 kV Omkareshwar-Bus Coupler 5. Omkareshwar-Unit-3,4,6&8 (65 MW)
8	GI-1	WR	29-11-2024 08:41	29-11-2024 10:41	02:00	195	-	0.26%	-	76111	68815	At 08:41 Hrs / 29-11-2024, all elements connected to 220 kV Omkareshwar-Bus-2 (Details in elements tripped column) tripped on LBB operation during de-synchronizing of Omkareshwar-Unit-2 (65 MW) (Double main bus scheme). Earlier, at 17:17 Hrs / 28-11-2024, all elements connected to 220 kV Omkareshwar-Bus-2 tripped on LBB operation during synchronizing of Omkareshwar-Unit-2 (65 MW). SLDC MP was advised to take corrective measures to avoid reoccurence of such incidences. Generation loss of 195 MW occurred at Omkareshwar Hydro Plant due to tripping of Omkareshwar-Unit-4,6&8 (65 MW).	Tripping of following Elements: 1. 220 kV Omkareshwar-Bus-2 2. 220 kV Omkareshwar-Nimrani 3. 220 kV Omkareshwar-Julwaniya 4. 220 kV Omkareshwar-Khandwa 5. 220 kV Omkareshwar-Bus Coupler 6. Omkareshwar-Unit-4,6&8 (65 MW)

Details of Grid Events during the Month of Nov 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA	01-11-2024 11:20	01-11-2024 12:04	00:44	5	144	0.01%	0.32%	43225.14	45209.78	Tripping of 220kV Bus-1 and Bus-2 of 400kV/220kV Guttur SS and Complete outage of 220kV/66kV Guttur SAS, 220kV/66kV Neelagunda, 220kV/66kV Davanagere, 220kV Bus-1 at Honnali, 220kV /66kV Benkikere, 220kV/66kV Hosadurga SS , 220kV Suzlon Wind and 220kV Wish Wind of KPTCL: During antecedent conditions, 220kV Neelagunda Ittagi was under outage. 220kV Honnali was operating with bus split condition. 220kV Guttur Davanagere Line-3 was charged through bus coupler breaker. As per the reports submitted, the triggering incident was Y-N fault in 220kV Guttur Davanagere Line-3. At 220kV Guttur end, due to non operation of protection, fault was cleared by tripping of 400kV/220kV Guttur ICT#1 and ICT#2 on opertion of backup Earth fault protection. This resulted in 220kV Bus outage at 400kV/220kV Guttur SS. Further, this led to complete outage of 220kV Guttur SAS, 220kV Neelagunda, 220kV Bus-1 of Honnali, 220kV Suzlon Wind, 220kV Wish Wind, 220kV Benkikere, 220kV Hosadurga.	220KV-GUTTUR-DAVANGERE-3, 400KV/220KV GUTTUR-ICT-1, 400KV/220KV GUTTUR-ICT-2
2	GD - 1	KARNATAKA	01-11-2024 12:10	01-11-2024 14:23	02:13	0	0	0.00%	0.00%	42320.27	45500.4	Complete Outage of 220kV Kalyani and Tripping of 220kV Bus-2 of 400kV/220kV Munirabad SS: As per the submitted reports, the triggering incident was R-N fault in 220kV Bus-2 of 400kV/220kV Munirabad SS causingBus-2 BBP to operate . Since 220kV Munirabad Kalyani steel was being radially fed from 220kV Bus-2 of 400kV/220kV Munirabad SS, tripping of the line led to complete outage of 220kV Kalyani Steel SS.	MUNIRABAD - 220KV - Bus 2, KALYANI - 220KV
3	GD - 1	KARNATAKA	01-11-2024 13:11	01-11-2024 18:26	05:15	0	117	0.00%	0.26%	42173.6	44420.54	Complete outage of 220kV/66kV Hebbal SS and 220kV/66kV CPRI SS of KPTCL During antecedent condition, 220kV Manyatha-Hebbal line was under idle charged condition from Manyatha end. As per the reports submitted, the triggering incident was RY fault in the 220kV Sahakarinagar-Hebbal line. The line tripped at Sahakarinagar end on operation of Zone-2(Time trip) distance protection. Tripping of 220kV Sahakarinagar-Hebbal line resulted in main supply failure to Hebbal 220kV Sub station and CPRI EHT resulting in the complete outage of Hebbal SS.	220KV-HEBBAL-SAHKARI_NAGAR-1
4	GD - 1	KARNATAKA	03-11-2024 23:30	04-11-2024 00:42	01:12	0	320	0.00%	0.85%	35170.38	37723.34	Tripping of 220kV Bus-1 and Bus-2 400kV/220kV Talguppa SS: During antecedent conditions at the 400/220kV Talaguppa substation, the 220kV Talaguppa-Sharavathy Line-1 was under a scheduled outage, and the 220kV bus coupler was kept open as per SLDC instructions. As per the reports submitted, due to fault in 110kV/66kV Talguppa ICT, fault current was induced in 220kV Talaguppa-Sharavathy Line-1 causing LBB to operate. Immediately elements connected to 220kV Bus-1 and Bus-2 tripped at 400kV/220kV Talaguppa SS.	220KV-SHARAVATHY-TALGUPPA-2, 220KV-SHARAVATHY-TALGUPPA-3, 220KV-GERUSOPPA-TALGUPPA-1, TALGUPPA - 220KV - Bus 1, TALGUPPA - 220KV - Bus 2, 400KV/220KV TALGUPPA-ICT-2, 400KV/220KV TALGUPPA-ICT-3
5	GD - 1	TAMILNADU	04-11-2024 06:54	04-11-2024 09:11	02:17	0	0	0.00%	0.00%	38248.05	44055.17	Complete Outage of 230kV/33kV Karur_JSW_Dharapuram Wind Station. The triggering incident was failure of the 230kV dropper Bus gantry insulator connected to Bus-2 at 230kV/33kV Karur_JSW_Dharapuram Wind Station. Immediately, the2 30kV Bus-2 BBP operated at 230kV/33kV Karur_JSW_Dharapuram Wind Station and DT was sent to remote end. Trippping of the only connected line resulted in complete outage of 230kV/33kV Karur_JSW_Dharapuram Wind Station.	230KV-KARUR-PERAMIUM-2, 230KV-KARUR-KARUR_JSW_Dharapuram-1, KARUR_JSW_Dharapuram - 230KV
6	GD - 1	KARNATAKA	05-11-2024 13:22	05-11-2024 15:20	01:58	126	0	0.27%	0.00%	45858.02	48469.2	Complete outage of 220kV Tirumani: As per the reports submitted, the triggering incident was RY fault in the line due to jumper damage in 220 kV line CT in the 220kV Pavagada_PG- Tirumani line-2. At both ends, line differential protection operated and the line tripped. Tripping of only connected line led to complete outage of 220kV Tirumani.	220KV-PAVAGADA_PG-TIRUMANI2, TIRUMANI2 - 220KV
7	GD - 1	TAMILNADU	17-11-2024 13:09	18-11-2024 16:01	26:52	0	0	0.00%	0.00%	41435.85	41738.27	Complete Outage of 230kV Sprng Pugalur As per the reports submitted, the triggering incident was LBB maloperation at 230kV Sprng Pugalur causing tripping of elements connected to 230kV Bus at 230kV Sprng Pugalur including 230kV Sprng Pugalur Pugalur line. Tripping of the only connected line led to complete outage of 230kV Sprng Pugalur	SPRING_PUGALUR - 230KV - Bus 1, 230KV-PUGALUR-SPRING_PUGALUR-1
8	GD - 1	ANDHRA PRADESH	23-11-2024 11:51	23-11-2024 13:29	01:38	0	0	0.00%	0.00%	49807.51	52487.33	Complete Outage of 400kV GREENKO_PSP: During relay testing works, 400kV Bus-1 BBP operated resulting in the complete outage of 400kV GREENKO_PSP due to the tripping of the only connected 400kV Kurnool Greenko_PSP line.	GREENKO_PSP - 400KV, GREENKO_PSP - 400KV - Bus 3, GREENKO_PSP - 400KV - Bus 4

Details of Grid Events during the Month of Nov 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD - 1	ANDHRA PRADESH	24-11-2024 17:37	24-11-2024 18:12	00:35	15	10	0.04%	0.02%	39153.8	42257.65	Complete Outage of 220KV SS Porumamilla, 132KV SS Brahmamgari matam,132KV SS Porumamillla,132KV SS Kalasapadu, 132KV Inox and 220KV Ecoren Stations: Triggering incident was tripping of 220KV Porumamilla-Jammalamadugu line 2 (only grid connected line that was in service by that time) due to transient fault. This resulted in the complete outage of 220KV SS Porumamilla, 132KV SS Brahmamgari matam,132KV SS Porumamillla,132KV SS Kalasapadu, 132KV Inox and 220KV Ecoren Stations.	220KV Porumamilla-Jammalamadugu line 2
10	GI-1	KARNATAKA	11-11-2024 14:27	11-11-2024 15:53	01:26	461	0	0.96%	0.00%	47796.48	52102.32	Tripping of 220kV South East bus of 220kV Sharavathy PH: As per the reports submitted, the triggering incident was tripping of Sharavathy Unit-3 on loss of excitation. However, LBB operated as the breaker of Unit-3 failed to open tripping all elements connected to the 220kV South East bus of 220kV Sharavathy PH.	220KV-MRS SHIMOGA-SHARAVATHY-1, 220KV-SHARAVATHY-TALGUPPA-1, 220KV-SHARAVATHY-TALGUPPA-3, 220KV-SHIRALKOPPA-SHARAVATHY-1
11	GI-1	KARNATAKA	13-11-2024 11:46	13-11-2024 12:23	00:37	0	246	0.00%	0.48%	46306.55	50937.04	Tripping of 220kV Bus-1 of 400kV/220kV Mylasandra SS of KPTCL: As per the reports submitted, the triggering incident was 220kV Bus-1 BBP. Immediately all elements connected to 220kV Mylasandra Bus-1 tripped.	220KV-JIGANI-MYLASANDRA-1, 220KV-MYLASANDRA-ELECTRONIC_CITY-1, 220KV-SOMANAHALLI-MYLASANDRA-1, 220KV-SOMANAHALLI-MYLASANDRA-2, 220KV-YERRAANDAHALLI-MYLASANDRA-2, 220KV-YERRAANDAHALLI-MYLASANDRA-3, MYLASANDRA - 220KV - Bus 1
12	GI-2	ANDHRA PRADESH	16-11-2024 03:49	16-11-2024 20:35	16:46	0	0	0.00%	0.00%	32103.12	36339.75	Tripping of 400kV Bus-2 of 400kV RYTPP Generating Station As per the reports submitted, the triggering incident was maloperation of 400kV Bus-2 BBP at RYTPP Generating Station. Immediately, all elements connected to Bus-2 tripped.	400KV/11.5KV RAYALSEEMA TPP-ST-6, 400KV/21KV RAYALSEEMA TPP-GT-6, 400KV-RAYALSEEMA TPP-KALIKIRI-2
13	GI-1	TELANGANA	16-11-2024 09:29	16-11-2024 09:56	00:27	0	0	0.00%	0.00%	45517.52	46946.86	Tripping of 220kV Bus-2 of 400kV/220kV Ghanapur SS of TGTRANSCO As per the reports submitted, the triggering incident was R-N fault in 220kV Ghanapur Hayathnagar Line-2. At Ghanapur end, the fault was sensed in zone-1 and the line tripped. However, after around 200ms, 220kV Bus-2 BBP maloperated at 400kV/220kV Ghanapur SS.	220KV-GHANAPUR-HAYATHNAGAR-2, 400KV/220KV GHANAPUR-ICT-4, 220KV-GHANAPUR-MOULALI-1, 220KV-GHANAPUR-NAGOLE-2, 220KV-GHANAPUR-CHNDRAYANGUTTA-2
14	GI-2	TAMILNADU	19-11-2024 12:44	19-11-2024 14:43	01:59	0	0	0.00%	0.00%	45343.83	48353.57	Tripping of 400kV Bus-2 of 400kV/220kV Alamathy SS As per the reports submitted, the triggering incident was an LBB trip that extended to the main breaker of Bus-B elements during LBB testing on the 400kV Thiruvalam Line-1 at the Alamathy. Although the LBB trip was disabled for the 400kV Alamathy Thiruvalam Line-1, a wiring issue during the commissioning of ICT-6 resulted in the trip signal being extended to the 96 relay of the 400kV/110kV Alamathy ICT-6. Consequently, the main breakers connected to Bus-2 tripped. Since the tie breaker of the 400kV/220kV Alamathy ICT-6 was not in service, the tripping of the main breaker resulted in the ICT to trip as well.	400KV/110KV ALAMATHY-ICT-6
15	GI-1	TELANGANA	25-11-2024 06:20	25-11-2024 11:48	05:28	0	0	0.00%	0.00%	36831.75	42469.39	Tripping 220kV/132kV Malyalalapalli Bus-2 Triggering incident was fault in 220kV RSS(Malyalapally)-Durshed feeder-1. At the same time, 220kV Bus-2 BBP maloperated resulting in the tripping of all the connected elements at 220kV Bus-2 of 220kV/132kV Malyalapalli SS	220KV-MALYALAPALLI-DURSHED-1, 220KV-MALYALAPALLI-JAGITIYAL-1, 220KV-MALYALAPALLI-JAGITIYAL-2, 220KV-MALYALAPALLI-MANTHANI-1, 220KV-MALYALAPALLI-MURMUR-1, 220KV-RAMAGUNDAM-MALYALAPALLI-2, 220KV-RAMAGUNDAM-MALYALAPALLI-4
16	GI-1	ANDHRA PRADESH , TELANGANA	27-11-2024 07:43	27-11-2024 09:24	01:41	300	0	0.68%	0.00%	44399.84	49350.31	Tripping of 220kV Bus-2 of 220kV/132kV NAGARJUNASAGAR_TS PH:220kV Bus-2 at 220kV/132kV NAGARJUNASAGAR_TS PH got deenergised due to maloperation of LBB in Bay-13 (100MVA PTR-2).	220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-NAGARJUNASAGAR_TS-CHALAKURTHY-1, NAGARJUNASAGAR_TS - 220KV - Bus 2, , 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-NAGARJUNASAGAR_TS-CHALAKURTHY-1, NAGARJUNASAGAR_TS - 220KV - Bus 2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-NAGARJUNASAGAR_TS-CHALAKURTHY-1, NAGARJUNASAGAR_TS - 220KV - Bus 2,

Details of Grid Events during the Month of Nov 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-I	MOTIPUR(BIHAR)	15-11-2024 18:23	15-11-2024 18:41	00:18	00:00	84	0.00%	0.38%	32279	21941	At 18:23 hrs, a bus fault occurred in 220 kV Bus of 220/132 kV Motipur S/s which led to tripping of all emanating lines from MotipurS/s. Total load loss of around 84 MW occurred at Motipur station. Power was restored through 132kV Motipur-Motihari ckt 1 at 19:08 Hrs..	220kV Motipur-Sitamarhi D/C 220kV Motipur-Darbhanga D/C 220 kV Motipur -MTPS-2 220kV Motipur-Mushari D/C 132kV Motipur-MTPS 132kV Motipur-Muzaffarpur D/C 132kV Motipur-Chakia S/C
2	GI-I	TENUGHAT TPS	21-11-2024 04:28	21-11-2024 08:23	03:55	00:00	0	1.36%	0.00%	25020	17031	At 04:28 Hrs, Y_ph CT of 220kv Tenughat Govindpur-1 burst at Tenughat . The line tripped, however, the two running units at Tenughat also tripped at the same time. Total generation loss of 341 MW occurred at Tenughat TPS. Tenughat unit 1 & 2 synchronised at 08:23 Hrs & 14:41 Hrs respectively.	220 kV TTPS-Govindpur ckt 1 T/L. 210 MW Tenughat Unit 1 210 MW Tenughat Unit 2
3	GI-I	LAPANGA	22-11-2024 11:03	22-11-2024 13:08	02:05	330	0	1.21%	0.00%	27353	19009	A bus fault occurred at 400 kV side of 400/220 kV Lapanga S/s while availing shutdown of 400 kV Lapanga-Sterlite-2. Bus bar protection didn't operate and thereafter, all 400 kV elements tripped at Lapanga. At the same time, auxiliary drives of thermal units at IB TPS (220 kV) also tripped which led to tripping of both running units. Around 330 MW generation loss occurred at IB TPS.Lapanga power restored at 13:52 hrs and IB.TPS - unit 1 & unit 2 synchronised at 19:08 hrs & 15:53 hrs respectively.	400KV-LAPANGA-OPGC (IB THERMAL)-1 & 2 400KV-MERAMUNDALI-LAPANGA-1 & 2 400KV-LAPANGA-STERLITE-1 400KV-MEERAMUNDALI-TSTPP-2 IB.TPS - UNIT 1 & 2 400KV/220KV 315 MVA ICT 1 AT LAPANGA 400KV/220KV 315 MVA ICT 2 AT LAPANGA 400KV MAIN BUS - 1 AT LAPANGA 400KV MAIN BUS - 2 AT LAPANGA

Details of Grid Events during the Month of Nov 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Lumshnong area of Meghalaya Power System	04-11-2024 12:50	04-11-2024 13:21	00:31	0	25	0.00%	1.15%	2060	2179	Lumshnong area of Meghalaya Power System were connected to NER Power system via 132 kV Lumshnong-Panchgram line. Prior to the event, 132 kV Lumshnong-Khleihriat line was under planned shutdown since 07:15 Hrs of 04.11.2024. At 12:50 Hrs of 04-11-2024, 132 kV Lumshnong-Panchgram Line tripped. Due to tripping of this line, Lumshnong area of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Lumshnong area of Meghalaya Power System by charging 132 kV Lumshnong-Panchgram line at 13:21 Hrs of 04-11-2024.	132 kV Lumshnong-Panchgram Line
2	GD I	Lumshnong area of Meghalaya Power System	15-11-2024 22:13	15-11-2024 23:14	01:01	0	43	0.00%	2.05%	2108	2093	Lumshnong area of Meghalaya Power System were connected to NER Power system via 132 kV Lumshnong-Panchgram line and 132 kV Lumshnong-Khleihriat line. At 22:13 Hrs of 15-11-2024, 132 kV Lumshnong-Panchgram Line and 132 kV Lumshnong-Khleihriat line tripped. Due to tripping of this line, Lumshnong area of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Lumshnong area of Meghalaya Power System by charging 132 kV Lumshnong-Khleihriat line at 23:14 Hrs of 15.11.2024.	132 kV Lumshnong-Panchgram Line and 132 kV Lumshnong-Khleihriat line
3	GD I	Pasighat area of Arunachal Pradesh Power System	16-11-2024 06:13	16-11-2024 07:03	00:50	0	8	0.00%	0.40%	1992	2004	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Pasighat & 132 kV Roing-Pasighat lines. At 06:13 Hrs of 16-11-2024, 132 kV Along-Pasighat Line and 132 kV Roing-Pasighat line tripped. Due to tripping of these elements, Pasighat area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Pasighat area of Arunachal Pradesh Power System by charging 132 kV Roing-Pasighat Line at 07:03 Hrs of 16.11.2024.	132 kV Along-Pasighat Line and 132 kV Roing-Pasighat line
4	GD I	Umrangsho area of Assam Power System	24-11-2024 04:55	24-11-2024 05:30	00:35	0	2	0.00%	0.13%	1861	1556	Umrangsho area of Assam Power System was connected with connected to NER Power system via 132 kV Haflong(PG) - Umrangsho Line & 132 kV Khandong - Umrangsho Line. At 04:55 Hrs of 24.11.2024, 132 kV Haflong(PG) - Umrangsho Line & 132 kV Khandong - Umrangsho tripped due to which Umrangsho area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Umrangsho area of Assam Power System by charging 132 kV Khandong - Umrangsho Line at 05:30 Hrs of 24.11.2024.	132 kV Haflong(PG) - Umrangsho Line & 132 kV Khandong - Umrangsho

21. NEW ELEMENTS CHARGED IN NOVEMBER 2024

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
WR	1	400/33 kV Khavda PSS-3	Adani Green Energy 24 A Limited (AGE24AL)	Solar	115.775	400	22.11.2024
	2	400/33 kV Khavda PSS-3	Adani Renewable Energy 55 Limited (ARE55L)	Solar	26.125	187.5	22.11.2024
	3	400/33 kV Khavda PSS-3	Adani Renewable Energy 55 Limited (ARE55L)	Wind	20.8	20.8	22.11.2024
	4	400/220 kV Pachora	NTPC Renewable Energy Limited (NTPC REL)	Solar	55	55	12.11.2024
ER	5	Dikchu	Kinetic power projects Pvt ltd/Dikchu Unit-1	Hydro	48	48	20.11.2024
NR	6	Tehri	THDC/Tehri PSP(Stage 1)	Hydro	250	1000	19.11.2024
	7	Fatehgarh Pooling	ACME Raisar Solar Energy Private Limited	Solar	79.33	272	19.11.2024
	8	Fatehgarh Pooling	ACME Dhaulpur Powertech Private Limited	Solar	79.33	272	24.11.2024
	9	Fatehgarh-II	Adani Green Energy Twenty Four Limited	Solar	238	500	30.11.2024
SR	10	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Lot-11/wind	21.6	413.2	25.11.2024
	11	230kV/33kV Vilathikulam S/S	JSW Renew Energy Ltd (JSW_540MW)	Lot-12/wind	5.4	418.6	25.11.2024
	12	230kV/33kV Vilathikulam S/S	JSW Renew Energy Ltd (JSW_540MW)	Lot-13/wind	8.1	426.7	25.11.2024
	13	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Lot-12/wind	10.8	437.5	25.11.2024
	14	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Lot-13/wind	16.2	453.7	25.11.2024
	15	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Lot-14/wind	13.5	467.2	25.11.2024
	16	400/33KV AMGEPL Wind Substation	AMGEPL	Lot-4/wind	16.5	138.6	22.11.2024
	17	400/33KV SIMHAPURI (SEPL) S/S	SEL_NELLLORE	Solar	52.6	52.6	27.11.2024
				Total Hydro Generation Addition	**298**		
				Total Solar Generation addition	**646**		
				Total Wind Generation addition	**113**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
WR	1	Goa Tamnar Transmission Projects Limited	400/220 kV Xeldem-GTTPL SS	ICT-1	400/220	500	04.11.2024
	2	Goa Tamnar Transmission Projects Limited	400/220 kV Xeldem-GTTPL SS	ICT-2	400/220	500	04.11.2024
	3	Madhya Pradesh Power Transmission Company Limited	400/220 kV Bhopal MPPTCL SS	ICT-2	400/220	500	04.11.2024
	4	Rewa Ultra Mega Solar Limited	220/33 kV Burlay RUMSL SS	ICT-1	220/33	110	09.11.2024
NR	5	PSTCL	Nakodar(PSG)	ICT-3	400/220/33	500	07.11.2024
	6	PBTSL	Bikaner_2 (PBTSL)	ICT-2	400/220/33	500	23.11.2024
	7	AGE24L	AGE24L(Bhimsar)SL_Ftg2_PG	Power Transformer-1	220/33	250	28.11.2024
	8	AGE24L	AGE24L(Bhimsar)SL_Ftg2_PG	Power Transformer-2	220/33	250	28.11.2024
	9	Tehri PSP	Tehri(THDC)	GT-6	420/15.75	306	30.11.2024
SR	10	GADAG_RSPPL	220kV RSRPL_GADAG	ICT-1	220/33	160	27.11.2024
	11	GADAG_RSPPL	220kV RSRPL_GADAG	ICT-2	220/33	160	27.11.2024
	12	TNTRANSCO	400KV VELLALAVIDUTHI	ICT-2	400/110/33	200	21.11.2024
	13	TNTRANSCO	400KV SRIPERUMBUDUR	ICT-1	400/230/33	500	27.11.2024
	14	GREENKO	GREENKO AP01 IREP	GT-2	400/18	300	04.11.2024
NER	15	NBTL	Nangalbibra	ICT-1	220/132	160	17.11.2024
	16	NBTL	Nangalbibra	ICT-2	220/132	160	16.11.2024
ER	17	Kinetic power projects Pvt ltd	DIKCHU HEP	ICT-1	400/132	270	20.11.2024
	18	NTPC	NTPC Kaniha	Tie Transformer-1	220/33	100	08.11.2024
	19	NTPC	NTPC Kaniha	Tie Transformer-2	220/33	100	22.11.2024
					Total (MVA)	**5326**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
WR	1	Rewa Ultra Mega Solar Limited	220 kV Burlay-Dehripal	7.6	702 A/Single ACSR Zebra	09.11.2024
	2	Goa Tamnar Transmission Projects Ltd	400 kV Xeldem (GTTPL)-Mapusa (PG) - 1	52.8	AAAC Moose/795 A	04.11.2024
	3	Goa Tamnar Transmission Projects Limited	400 kV Xeldem (GTTPL)-Mapusa (PG) - 2	52.8	AAAC Moose/795 A	11.11.2024
ER	4	BSPTCL	132 kV Chandauti (PMTL)-Barachatti ckt 1	29.3	ACSR Panther	13.11.2024
	5	BSPTCL	132 kV Chandauti (PMTL)-Barachatti ckt 2	29.3	ACSR Panther	13.11.2024
	6	WBSETCL	132KV-MALDA (PG)-MANIKCHAK-1	24.0	ACSR Panther	19.11.2024
	7	WBSETCL	132KV-MALDA (PG)-MANIKCHAK- 2	24.0	ACSR Panther	19.11.2024
	8	BSPTCL	220KV-BANKA (PG)-Havelikharagpur-1	92.8	ACSR Zebra (32.617	05.11.2024
NER	9	NBTL	220kV Bongaigaon- Nangalbibra- 1	122.9	AL 59 TWIN MOOSE	18.11.2024
	10	NBTL	220kV Bongaigaon- Nangalbibra- 2	123.9	AL 59 TWIN MOOSE	16.11.2024
NR	11	AGE24L	220kV AGE24L(Bhimsar)SL_Ftg2_PG- Fatehgarh_II(PG)-1	12.0	AL59 Zebra	27.11.2024
	12	AGE24L	220kV AGE24L(Bhimsar)SL_Ftg2_PG- Fatehgarh_II(PG)-2	12.0	AL59 Zebra	27.11.2024
SR	13	GADAG_RSRPL	220KV Gadag PSS-RSRPL PSS line-1	38.2	Al-59 MOOSE	26.11.2024
	14	AMGEPL	400KV-CPSS-AMGEPL Solar Pooling Station	24.6	ACSR Twin Moose	25.11.2024
			Total ckt km	**646.0**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
WR	1	Goa Tamnar Transmission Projects Ltd.	220 kV Xeldem (GED) exisitng - Xeldem (GTTPL) new - 1	22.2	ACSS HTLS/1600 A	05.11.2024
	2	Goa Tamnar Transmission Projects Ltd.	221 kV Xeldem (GED) exisitng - Xeldem (GTTPL) new - 2	22.2	ACSS HTLS/1600 A	05.11.2024

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
SR	1	KPTCL	220 KV RAGALPADU-SOMASAMUDRA Line 1	76.11	Drake, Zebra, Moose	19.11.2024
	2	KPTCL	220 KV ALIPURA-SOMASAMUDRA Line 1	39.4	Drake, Zebra	19.11.2024
WR	3	MSETCL	400 kV Karad - Solapur (PG)	299	0.5 ACSR Moose	23.11.2024

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
NER	1	NBTL	Bus Reactor-1 at 220/ 132 kV Nangalbibra SS	220	31.5	17.11.2024
	2	NBTL	Bus Reactor-2 at 220/ 132 kV Nangalbibra SS	220	31.5	17.11.2024
				Total (MVAr)	**63**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

22. Voltage Profile

विद्युत विभव रूपरेखा माह - नवंबर 2024 VOLTAGE PROFILE - November 2024

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	795	749	773
2		दार्लिपली DARLIPALI	0%	100%	0%	0%	0	790	764	777
3		गया GAYA	0%	100%	0%	0%	0	780	747	765
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	785	731	758
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	800	770	786
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	786	746	767
7		रांची RANCHI	0%	100%	0%	0%	0	795	763	781
8		सासाराम SASARAM	0%	100%	0%	0%	0	786	744	767
1		आगरा AGRA	0%	100%	0%	0%	0	803	743	781
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	798	744	778
3		अजमेर AJMER	0%	100%	0%	0%	3	802	748	781
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	798	738	777
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	788	762	775
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	787	760	773
7		अंता ANTA	0%	100%	0%	0%	0	797	757	778
8		बलिया BALLIA	0%	100%	0%	0%	0	783	742	767
9		बारा BARA	0%	100%	0%	0%	0	798	750	769
10		भाडला BHADLA	0%	100%	0%	0%	0	798	723	778
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	0	799	726	780
12		भिवानी BHIWANI	0%	99%	1%	1%	5	805	750	784
13		बीकानेर BIKANER	0%	100%	0%	0%	0	801	722	781
14		बरेली BAREILLY	0%	100%	0%	0%	0	802	744	779
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	1	802	751	779
16		फतहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	792	722	776
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	792	739	771
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	791	737	772
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	3	804	744	782
20		हापुड़ HAPUR	0%	100%	0%	0%	1	804	741	778
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	803	735	770
22		झाटीकरा JHATIKARA	0%	100%	0%	0%	0	799	741	779
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	791	740	772
24		खेतरी KHETRI	0%	100%	0%	0%	0	801	731	782
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	797	743	776
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	778	738	763
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	794	741	773
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	794	731	766
29		मेरठ MEERUT	0%	100%	0%	0%	3	803	744	780
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	802	741	778
31		मोगा MOGA	0%	100%	0%	0%	1	803	732	775
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	784	754	770
33		उरई ORAI	0%	98%	2%	2%	16	805	751	785
34		फागी PHAGI	0%	100%	0%	0%	0	804	726	780
35		रामपुर RAMPUR	0%	95%	3%	3%	22	806	752	786
36		उन्नाव UNNAO	0%	100%	0%	0%	0	789	737	770
37		वाराणसी VARANASI	0%	100%	0%	0%	0	791	751	774
1		अकोला AKOLA	0%	100%	0%	0%	0	794	745	770
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	800	746	775
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	793	742	770
4		भुज BHUJ	0%	100%	0%	0%	0	799	739	774
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	795	743	770
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	787	753	769
7		बीना BINA	0%	100%	0%	0%	0	798	750	779
8		बनसकंठा BANASKANTHA	0%	100%	0%	0%	1	806	746	779
9		चापा CHAMPA	0%	93%	7%	7%	49	811	773	790
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	801	749	775
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	788	757	772
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	1	802	763	779
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	793	739	769
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	1	801	762	783
15		ग्वालियर GWALIOR	0%	100%	0%	0%	3	803	746	781
16		इंदौर INDORE	0%	100%	0%	0%	0	797	744	771
17	पश्चिमी क्षेत्र WR	जबलपुर JABALPUR	0%	99%	1%	1%	7	803	760	785
18		खंडवा KHANDWA	0%	100%	0%	0%	0	797	748	774
19		कोरडा KORADI	0%	100%	0%	0%	0	784	745	765
20		लकाडिया LAKADIYA	0%	100%	0%	0%	1	807	749	778
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	799	771	785
22		पड़घे PADGHE	0%	100%	0%	0%	3	805	739	776
23		परली PARLI	0%	99%	1%	1%	5	804	755	782
24		पुणे PUNE	0%	97%	3%	3%	21	806	745	780
25		राजनन्दगांव RAJNANDGAON	0%	97%	3%	3%	19	808	765	786
26		सासन SASAN	0%	100%	0%	0%	0	793	759	776
27		सतना SATNA	0%	99%	1%	1%	8	804	756	783
28		सिवनी SEONI	0%	100%	0%	0%	0	801	754	778
29		सीपत SIPAT	0%	100%	0%	0%	0	787	756	770
30		सोलापुर SOLAPUR	0%	99%	1%	1%	4	803	758	782
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	778	748	764
32		तामनार TAMNAR	0%	100%	0%	0%	0	797	771	784
33		वड़ोदरा VADODARA	0%	99%	1%	1%	6	807	738	776
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	797	762	779
35		वर्धा WARDHA	0%	99%	1%	1%	10	806	752	774
36		वरोरा WARORA	0%	100%	0%	0%	1	802	757	781
1		अरियलूर ARIYALUR	0%	100%	0%	0%	0	795	744	772
2		कड़पा CUDDAPAH	0%	94%	6%	6%	41	809	748	784
3		चिल्कलुरीपेट CHILAKALURIPETA	0%	99%	1%	1%	6	805	752	781
4		कर्नूल KURNOOL	0%	100%	0%	0%	3	804	745	779
5		महेश्वरम MAHESWARAM	0%	91%	9%	9%	61	814	752	788
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	81%	19%	19%	139	813	764	791
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	798	748	778
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	3	809	742	777
9		रायचूर RAICHUR	0%	99%	1%	1%	4	803	750	781
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	0	799	748	779
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	791	736	765
12		वेमागिरी VEMAGIRI	0%	94%	6%	6%	40	806	758	784
13		वारंगल WARANGAL	0%	85%	15%	15%	104	809	754	789
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	412	389	403
2		बिस्वनाथ चारिआली BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	416	387	406
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	416	396	408
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	419	398	410
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	415	393	405
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	401	401	401
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	419	392	404
8	पूर्वोत्तर क्षेत्र NER	अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	412	401	408
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	416	391	404
10		न्यू मारियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	415	394	407
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	417	394	406
12		पालाटाना PALATANA(400 kV)	0%	100%	0%	0%	0	412	398	406
13		पुवकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	413	394	403
14		रंगानदी RANGANADI(400 kV)	0%	100%	0%	0%	0	415	405	409
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	396	408
16		सुबानसिरी SUBANSIRI (400 kV)	0%	100%	0%	0%	0	408	392	400
17		सुज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	415	394	402

All listed stations are 765 kV stations unless otherwise mentione
***Percentage is calculated w.r.t. Time of one month**

23.ALL TIME HIGHEST

30-11-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	186 01-05-2024
WR	74974 01-06-2024	67482 30-05-2024	1648 06-05-2024	167 18-12-2014	310 28-05-2024	105.61 07-10-2024
SR	68735 13-03-2024	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	323 26-07-2024	148.7 31-03-2024
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	4 09-06-2024
NER	3905 19-09-2024	3787 19-09-2024	80 20-09-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	426 30-04-2024

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	17949	20-01-2024	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	2235	20-01-2024	41.2	26-06-2024
	J&K(UT) and Ladakh(UT)	3107	12-01-2024	66.8	26-01-2024
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	17819	29-12-2023	335.9	10-11-2023
	Maharashtra	28969	07-02-2024	648.3	30-04-2024
	Goa	803	19-04-2024	17.6	18-05-2024
	DD & DNH	1390	23-10-2024	32.6	16-10-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	15623	08-03-2024	311.0	13-03-2024
	Karnataka	17220	12-03-2024	336.9	05-04-2024
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	8001	23-09-2024	172.8	30-07-2024
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26-05-2024	3.9	18-06-2024
	Assam	2687	20-09-2024	55.8	20-09-2024
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.4	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24. System Reliability Indices Report for the month of November 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	1	0.25	0.03
3	Import of NR	0	0.00	0.00
4	NEW-SR	1	0.25	0.03
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	1	0.25	0.03
3	Import of NR	0	0.00	0.00
4	NEW-SR	1	0.25	0.03
4	NER Import	1	0.25	0.03

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
