DRAFT

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report










अक्टूबर 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह अक्टूबर 2024 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF OCTOBER -2024


पृष्ठसूची CONTENTS

1	माह अक्टूबर 2024 की सारांश रिपोर्ट Summary of report for the month of OCTOBER 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	03 अक्टूबर के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 03-OCTOBER (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अक्टूबर 2023 से तुलना Energy requirement and met comparison with OCTOBER 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अक्टूबर 2023 से तुलना Peak demand requirement and met comparison with OCTOBER 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-37
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	38-40
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	41
18	पावर मार्केट की सूचना Power market information	42-46
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	47-49
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	50-58
21	नए चार्ज किये गए तत्व New elements Charged	59
22	विभव रूपरेखा Voltage profile	60
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह अक्टूबर 2024 तक All Time Highest (Demand & Energy) figures: Till OCTOBER 2024	61
24	अक्टूबर 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for OCTOBER 2024	62

1. SUMMARY OF REPORT FOR THE MONTH OF OCTOBER-2024


EVENING PEAK HOUR (at 1900hrs) DEMAND MET AT NATIONAL LEVEL (MW)

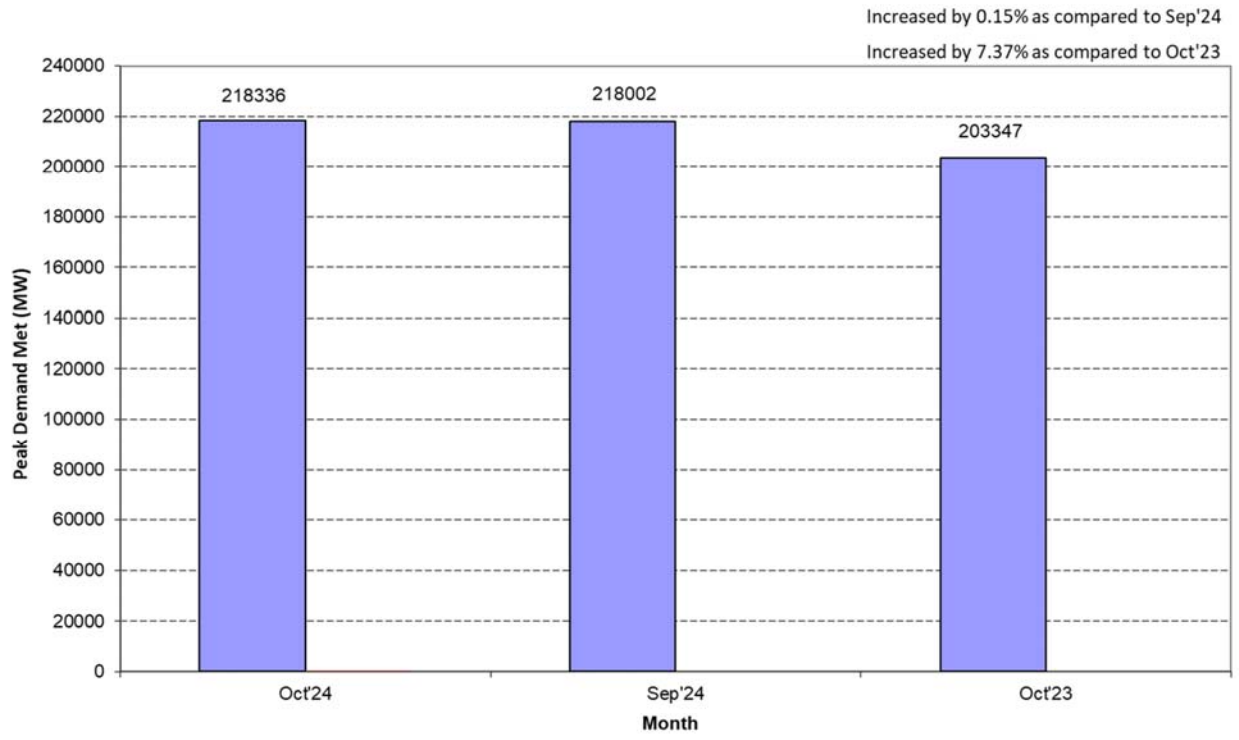


Frequency within IEGC Band

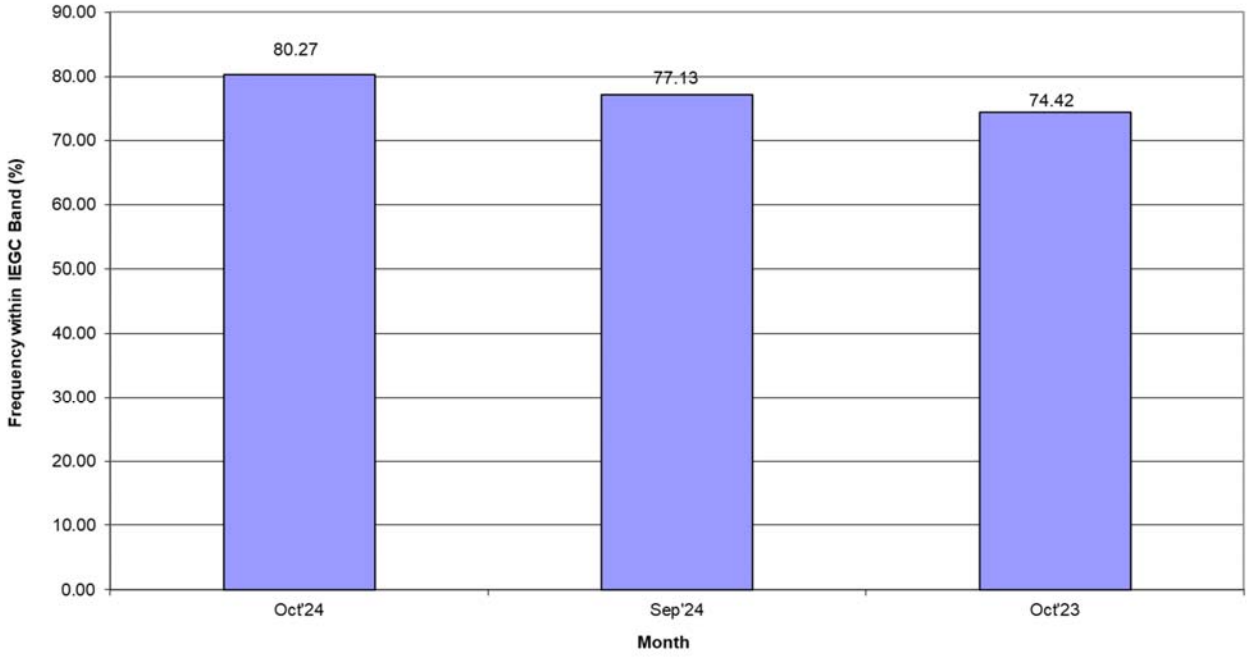


ENERGY MET AT NATIONAL LEVEL (MU)

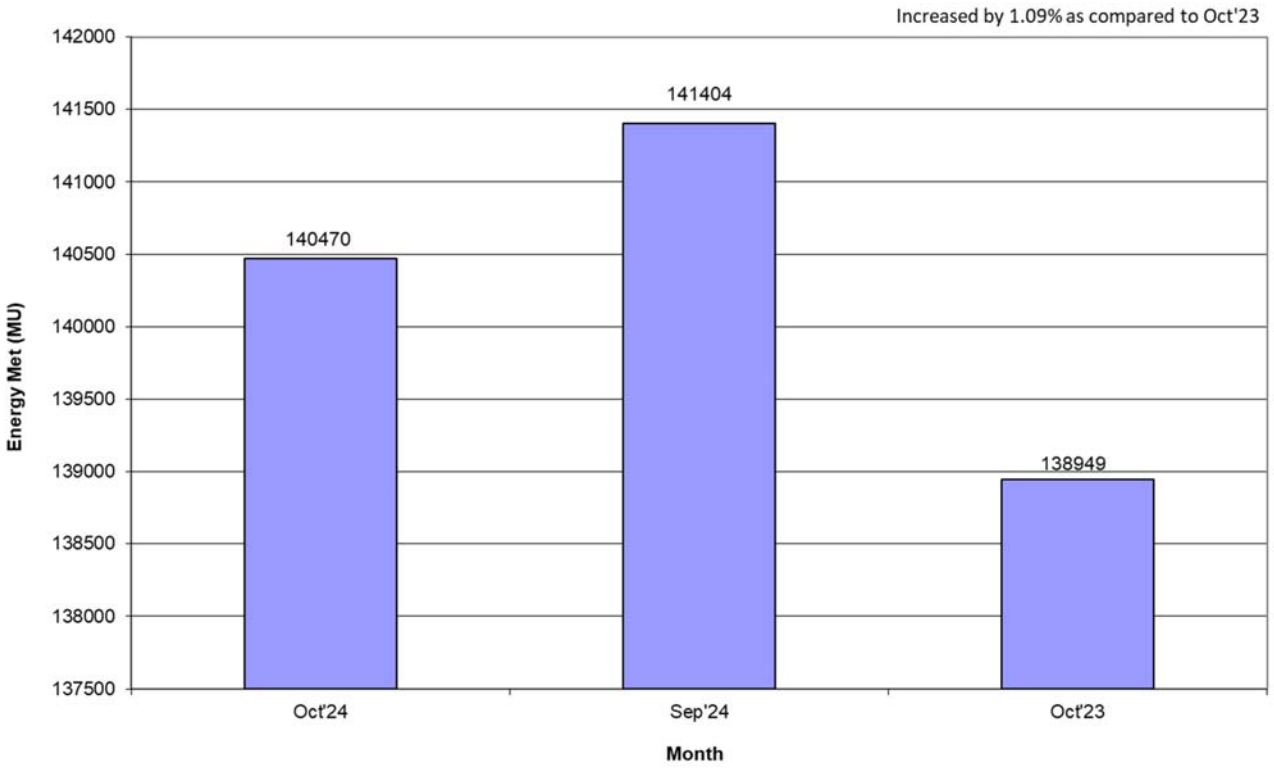


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

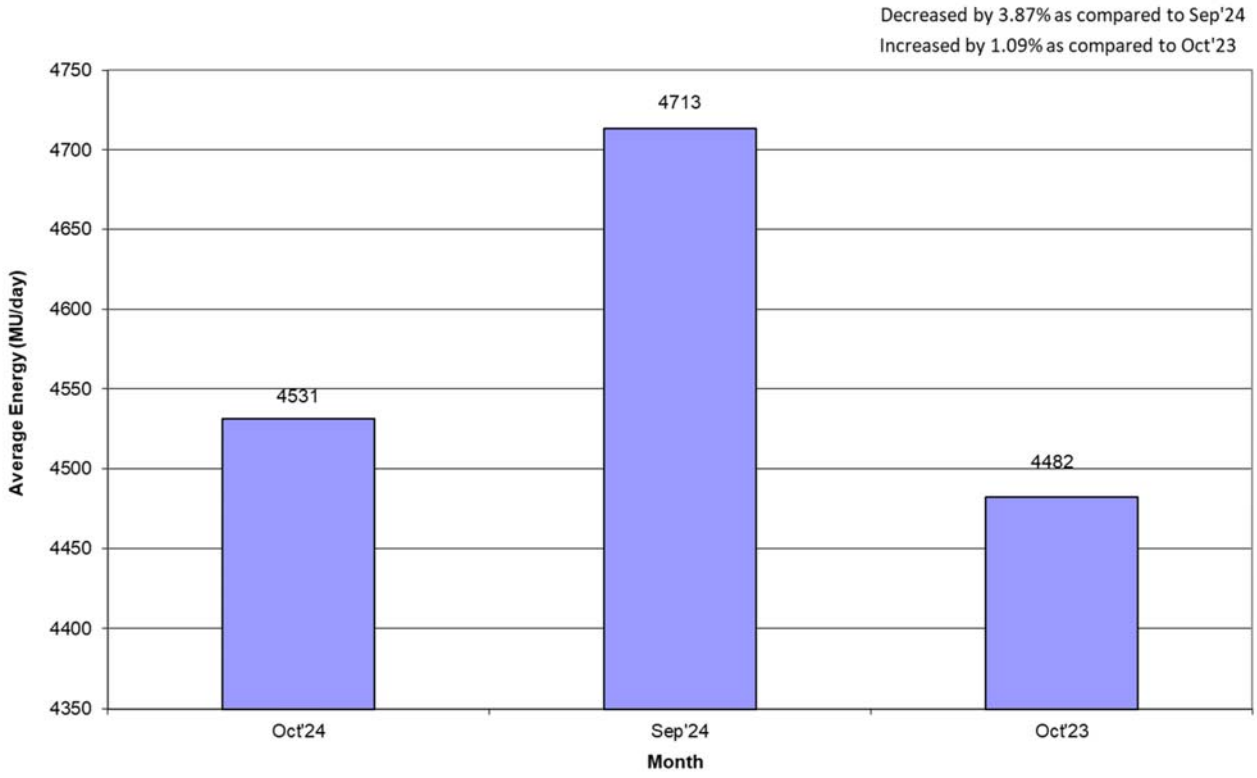


HYDRO GENERATION AT NATIONAL LEVEL (MU)

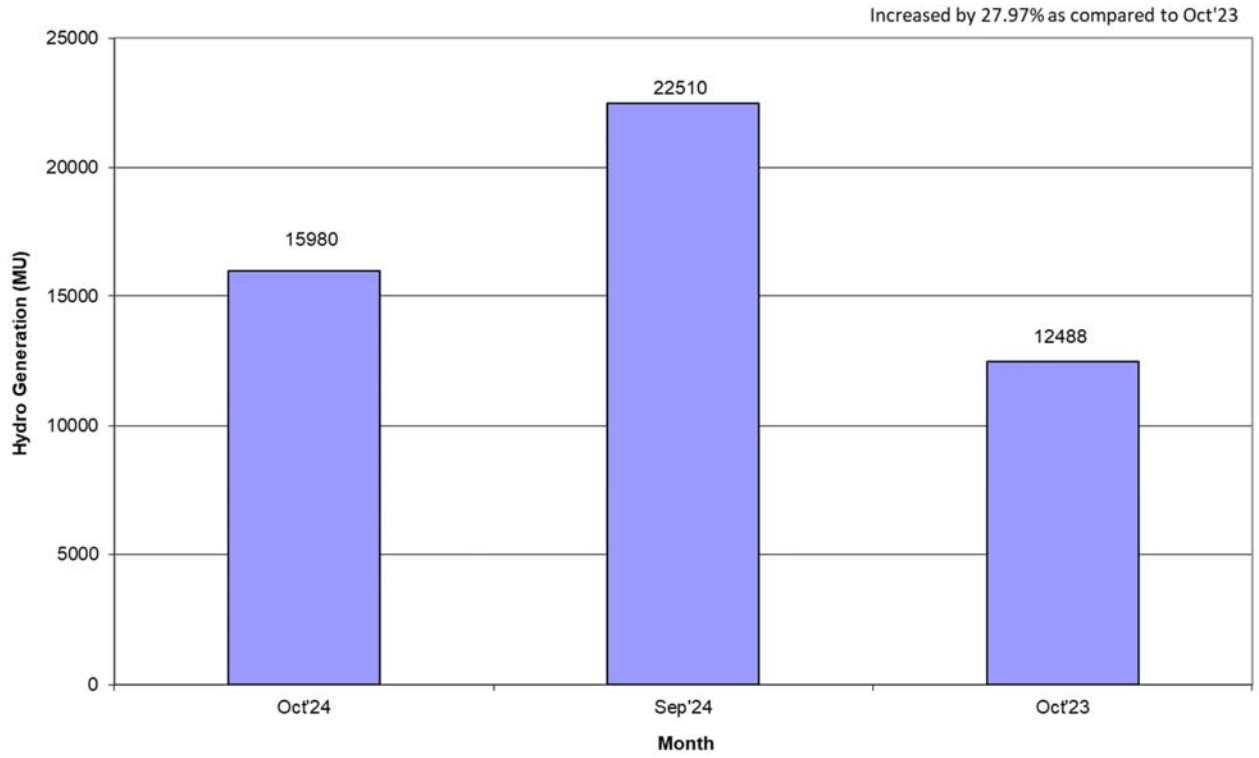


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

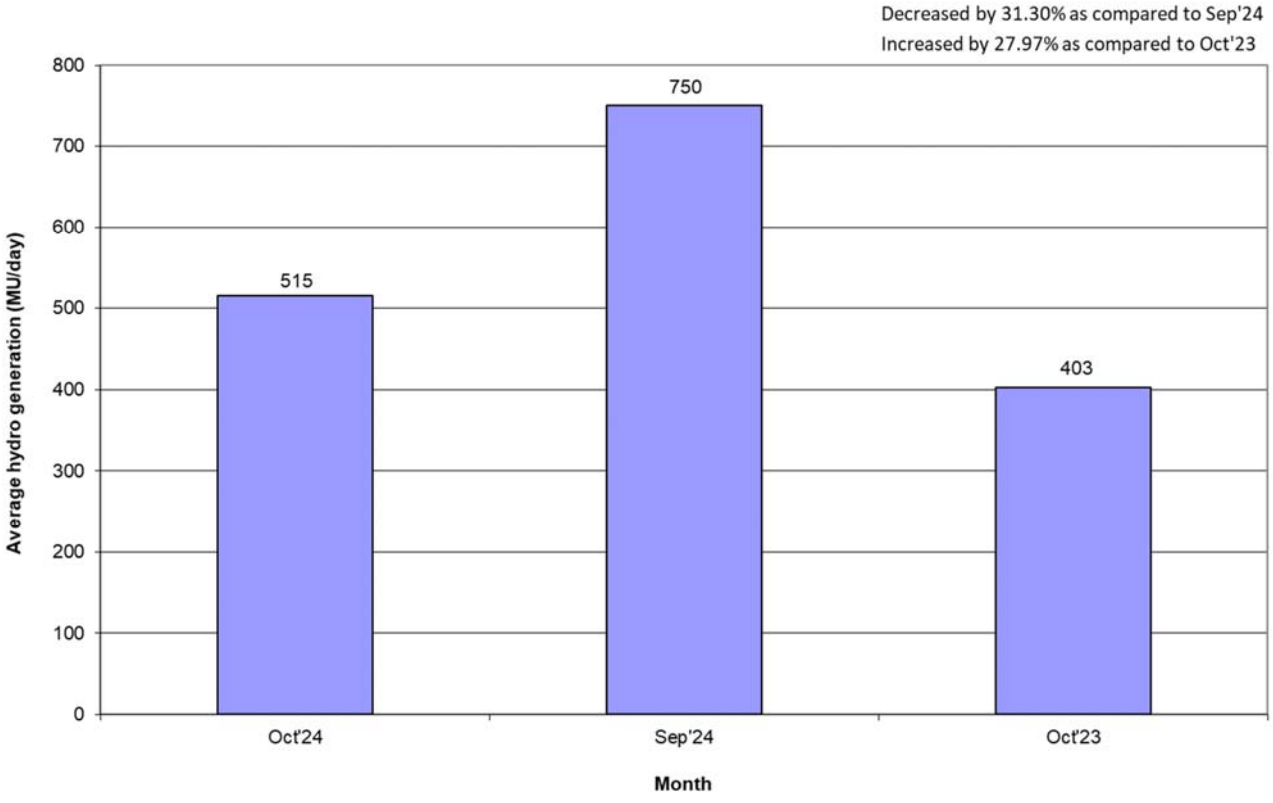


WIND GENERATION AT NATIONAL LEVEL (MU)

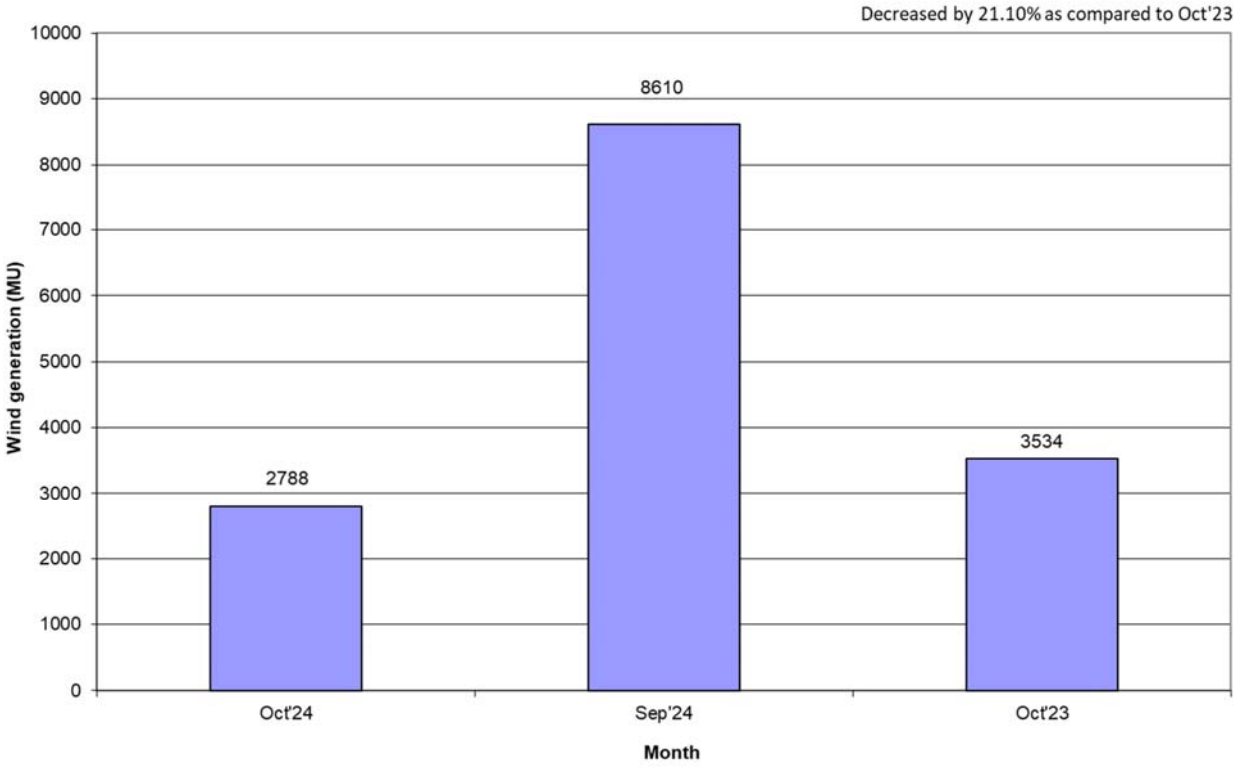


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

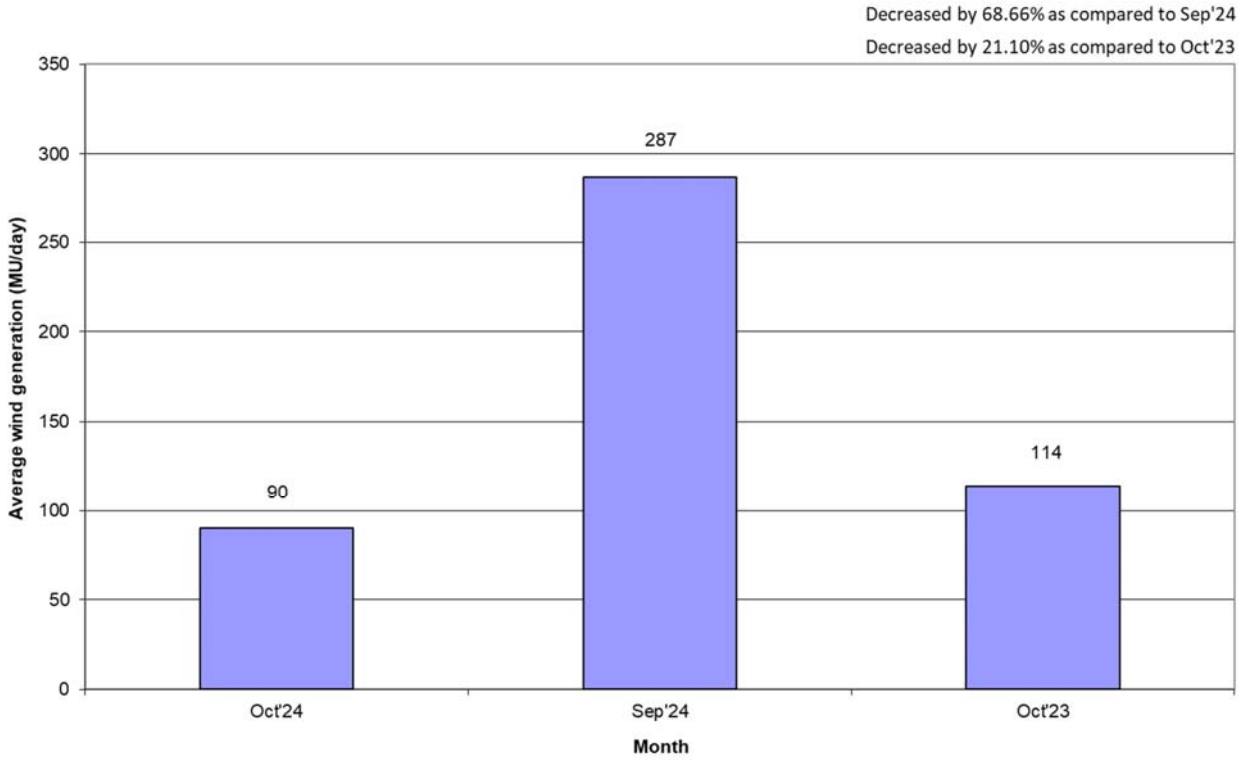

SOLAR GENERATION AT NATIONAL LEVEL (MU)

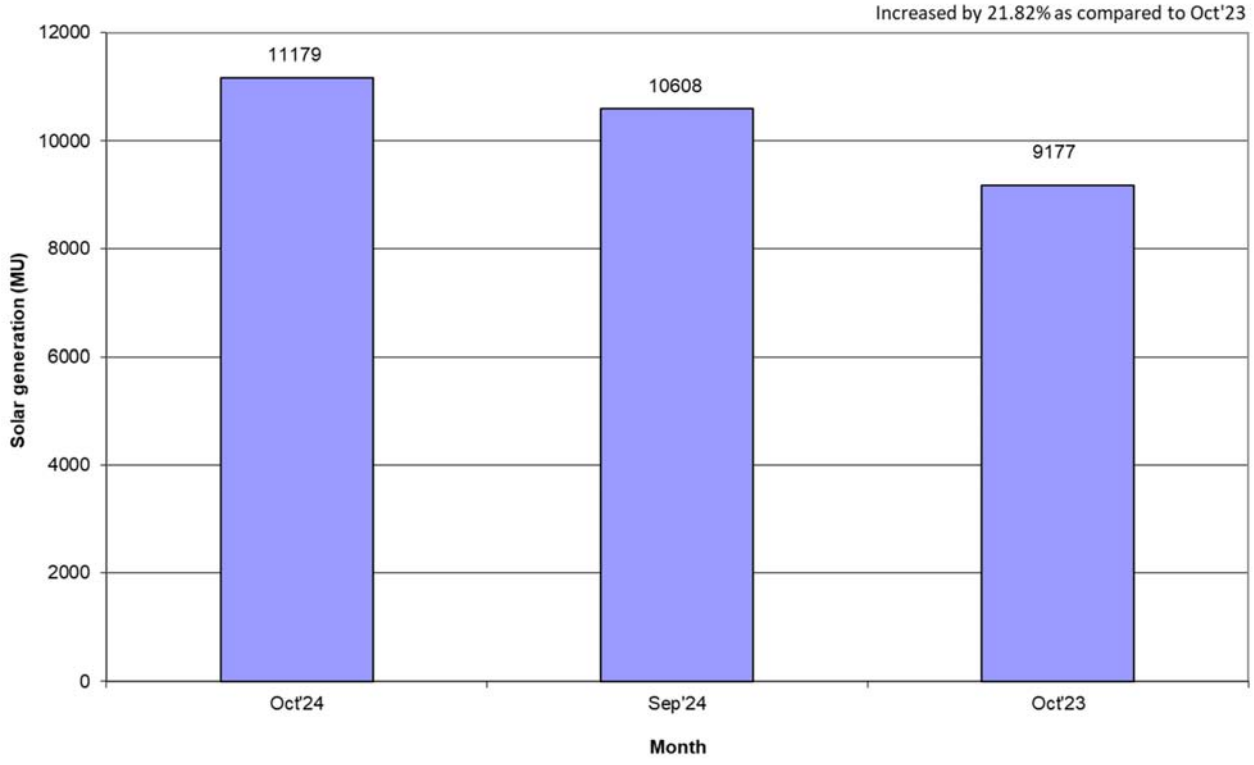

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

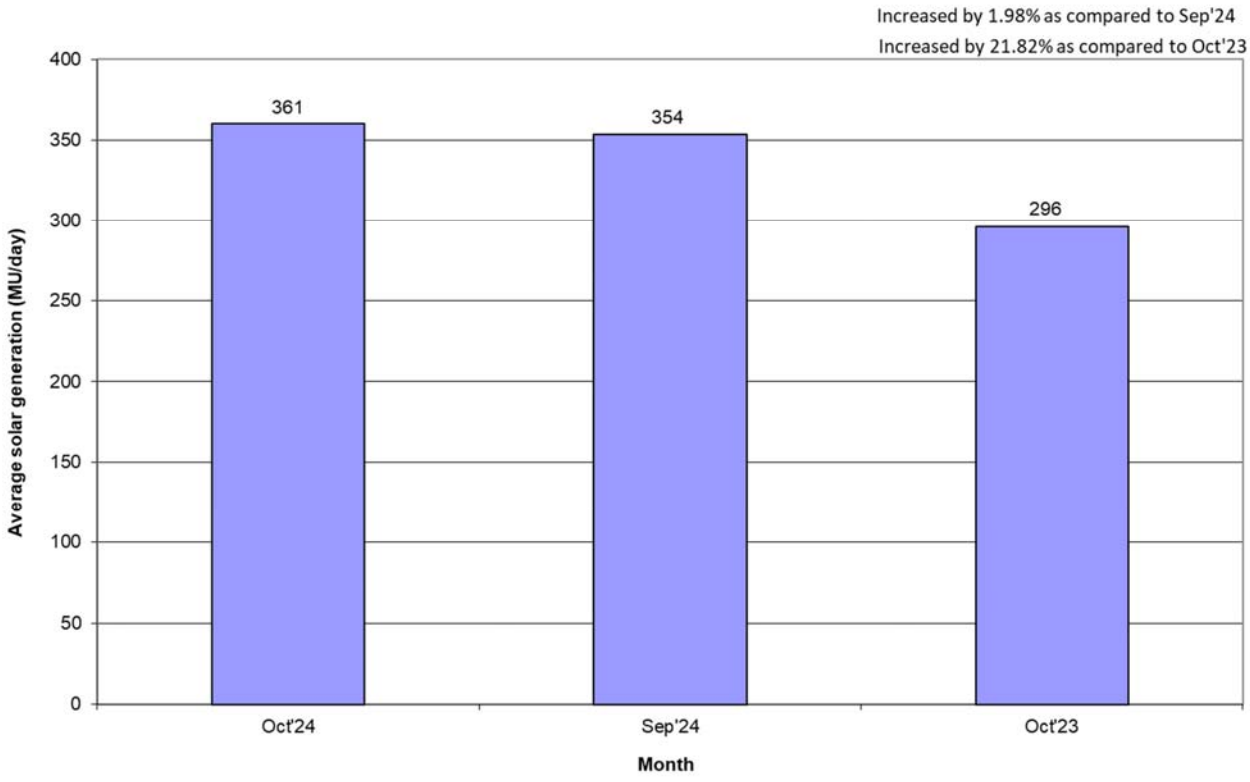

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.10.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56658	1580	5995	0	64233	1620	20830	42761	129444
2	WR	74663	1400	10806	0	86869	3240	7563	53613	151284
3	SR	49592	3640	6272	434	59938	3320	11867	56944	132069
4	ER	28875	0	80	0	28955	0	4764	2276	35995
5	NER	1242	0	1665	36	2943	0	1944	613	5500
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	211030	6620	24818	589	243057	8180	46968	156247	454452

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: अक्तूबर 2024 MONTH:- OCT 2024


सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Oct-24	71562	64203	48946	28941	3382	217034
2-Oct-24	68489	62897	43989	27881	3087	206343
3-Oct-24	73425	65240	48540	28000	2875	218080
4-Oct-24	73305	65680	48160	28369	2822	218336
5-Oct-24	70902	66129	47185	26610	2843	213669
6-Oct-24	67161	62249	43278	26520	2855	202063
7-Oct-24	69711	66419	46836	27614	3170	213750
8-Oct-24	69038	66599	47206	27589	3211	213643
9-Oct-24	68234	64878	46926	26846	3106	209990
10-Oct-24	67429	63486	44908	26434	2888	205145
11-Oct-24	64893	61634	41467	25882	2628	196504
12-Oct-24	56483	56045	39653	24213	2584	178978
13-Oct-24	59891	58582	40342	24131	2480	185426
14-Oct-24	63292	61949	43695	26300	2793	198029
15-Oct-24	62333	63999	43124	27038	2961	199455
16-Oct-24	62508	64474	43266	26235	2967	199450
17-Oct-24	63114	65216	44951	26620	2932	202833
18-Oct-24	63237	64679	45868	26617	2907	203308
19-Oct-24	63672	62715	44362	26167	2899	199815
20-Oct-24	59383	59441	41965	25772	2779	189340
21-Oct-24	62767	63457	47289	26777	2960	203250
22-Oct-24	63255	62771	45444	26800	3093	201363
23-Oct-24	62723	64271	46164	25437	2966	201561
24-Oct-24	61771	63406	46014	22781	2785	196757
25-Oct-24	61571	63270	45529	21648	2851	194869
26-Oct-24	60970	62988	45557	23211	2892	195618
27-Oct-24	58497	60707	43132	24094	2816	189246
28-Oct-24	61339	63466	48150	25863	3071	201889
29-Oct-24	60902	62959	47115	25581	3175	199732
30-Oct-24	58217	59898	44296	26146	3037	191594
31-Oct-24	48475	52312	37570	24601	2784	165742
उच्चतम MAXIMUM	73425	66599	48946	28941	3382	218336
निम्नतम MINIMUM	48475	52312	37570	21648	2480	165742
औसत AVERAGE	63824	62775	44869	26023	2923	200413
अब तक का उच्चतम All Time Max.	82312	67482	54798	29695	3787	227354
दिनांक Date	23.07.24	30.05.24	29.04.24	29.05.24	19.09.24	29.05.24

नोट : सभी आंकड़े 1900 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 1900 Hrs

EVENING PEAK HOUR DEMAND(at 1900hrs) MET DURING THE MONTH OF OCTOBER' 2024

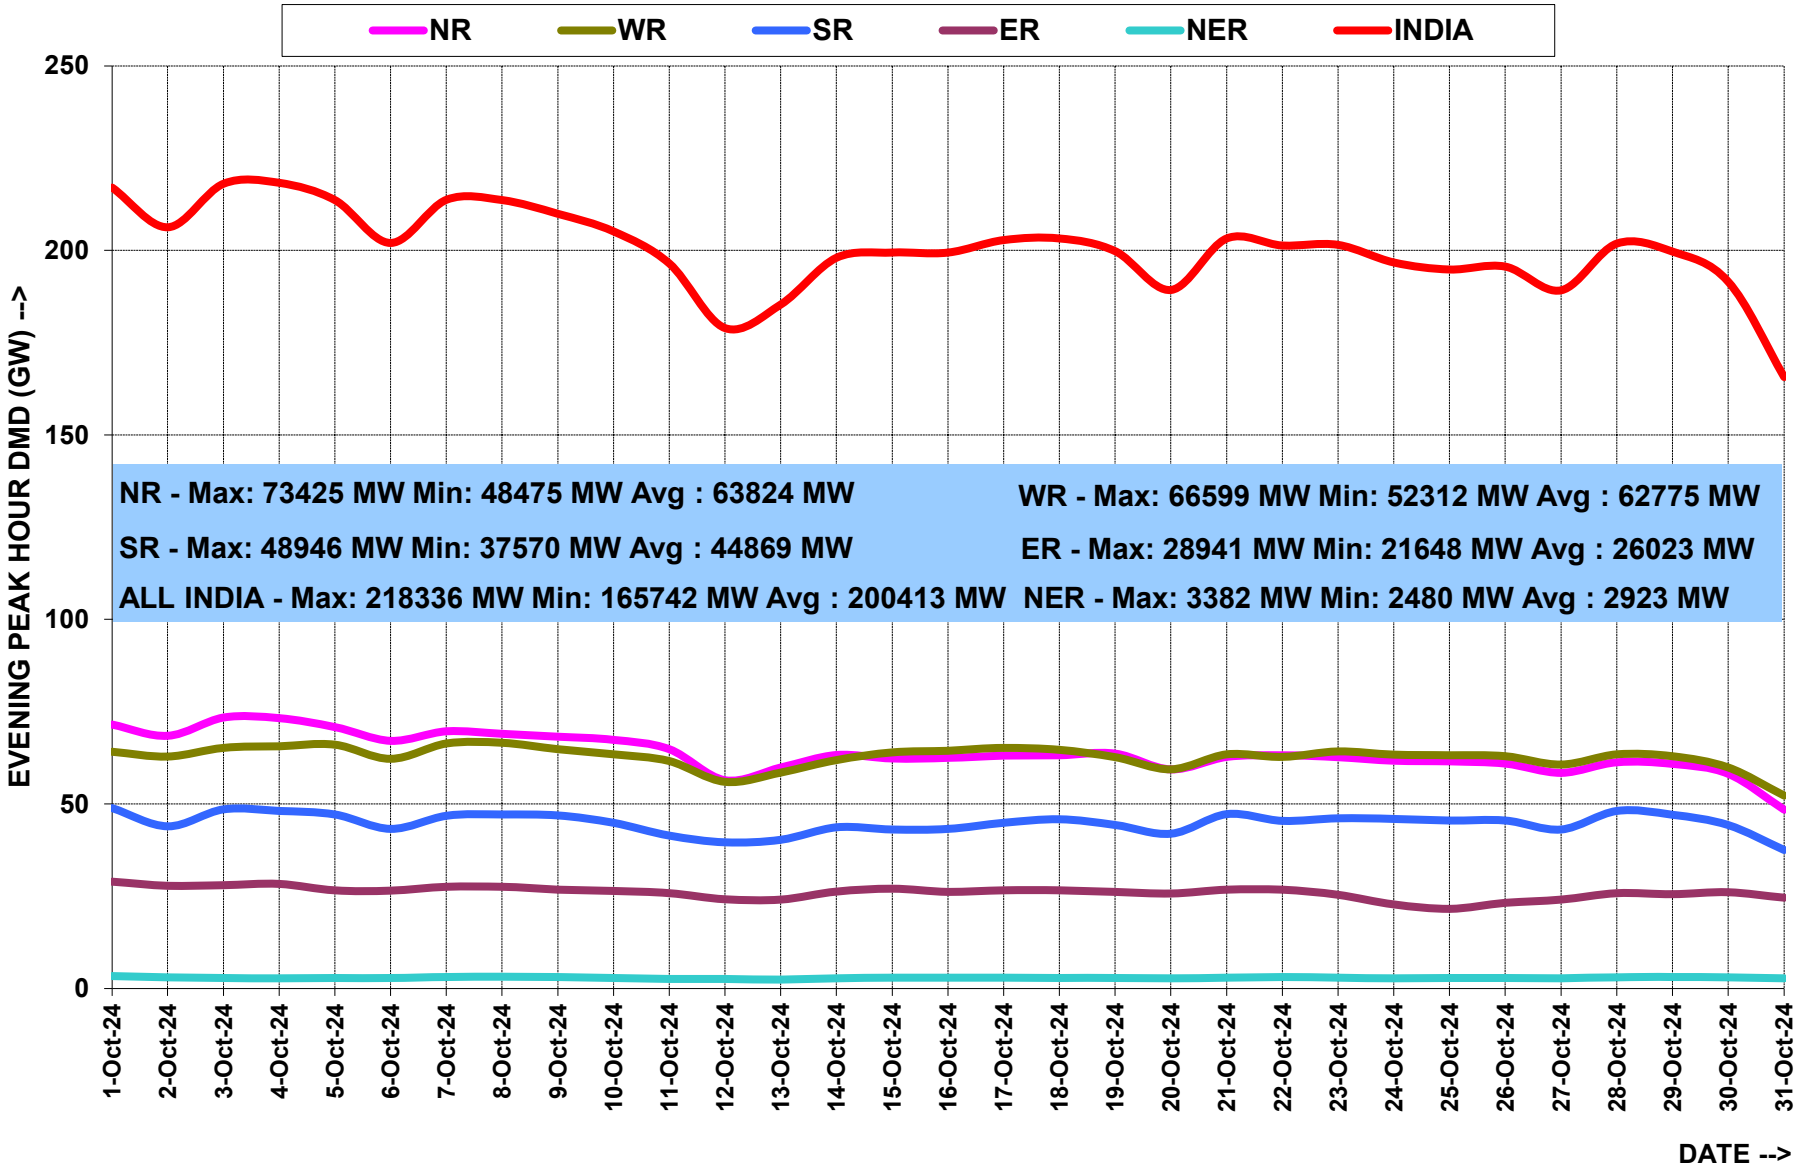


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: अक्तूबर 2024 MONTH:- OCT 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-24	1582	1400	1225	625	63	4895
02-Oct-24	1537	1405	1146	617	62	4768
03-Oct-24	1629	1449	1170	602	56	4906
04-Oct-24	1670	1466	1190	588	53	4967
05-Oct-24	1619	1482	1152	579	54	4885
06-Oct-24	1444	1446	1081	568	53	4593
07-Oct-24	1532	1500	1137	588	57	4814
08-Oct-24	1548	1539	1157	593	60	4897
09-Oct-24	1537	1519	1154	590	59	4858
10-Oct-24	1504	1487	1114	570	54	4729
11-Oct-24	1464	1444	1022	565	50	4545
12-Oct-24	1356	1331	963	552	49	4251
13-Oct-24	1300	1328	959	547	46	4179
14-Oct-24	1379	1395	1027	563	51	4415
15-Oct-24	1370	1429	1007	577	54	4438
16-Oct-24	1368	1434	993	570	55	4420
17-Oct-24	1383	1455	1005	567	54	4465
18-Oct-24	1399	1457	1034	571	62	4523
19-Oct-24	1396	1436	1018	564	55	4470
20-Oct-24	1347	1360	958	545	54	4263
21-Oct-24	1369	1393	1021	557	56	4396
22-Oct-24	1372	1409	1041	554	58	4434
23-Oct-24	1365	1420	1045	545	57	4433
24-Oct-24	1352	1428	1053	490	53	4377
25-Oct-24	1343	1417	1059	456	52	4327
26-Oct-24	1320	1414	1062	474	55	4324
27-Oct-24	1290	1396	1029	489	54	4257
28-Oct-24	1359	1453	1103	529	56	4499
29-Oct-24	1379	1475	1132	540	57	4582
30-Oct-24	1354	1434	1103	550	56	4496
31-Oct-24	1208	1293	972	537	52	4062
कुल TOTAL	44074	44291	33133	17265	1707	140470
उच्चतम MAXIMUM	1670	1539	1225	625	63	4967
निम्नतम MINIMUM	1208	1293	958	456	46	4062
औसत AVERAGE	1422	1429	1069	557	55	4531
संचयी 2024-25 Cumulative 2024-25	336440	306926	245628	127578	13092	1029663
अब तक का उच्चतम All Time Max.	1990	1648	1416	692	80	5466
दिनांक Date	18.06.24	06.05.24	05.04.24	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF OCTOBER' 2024

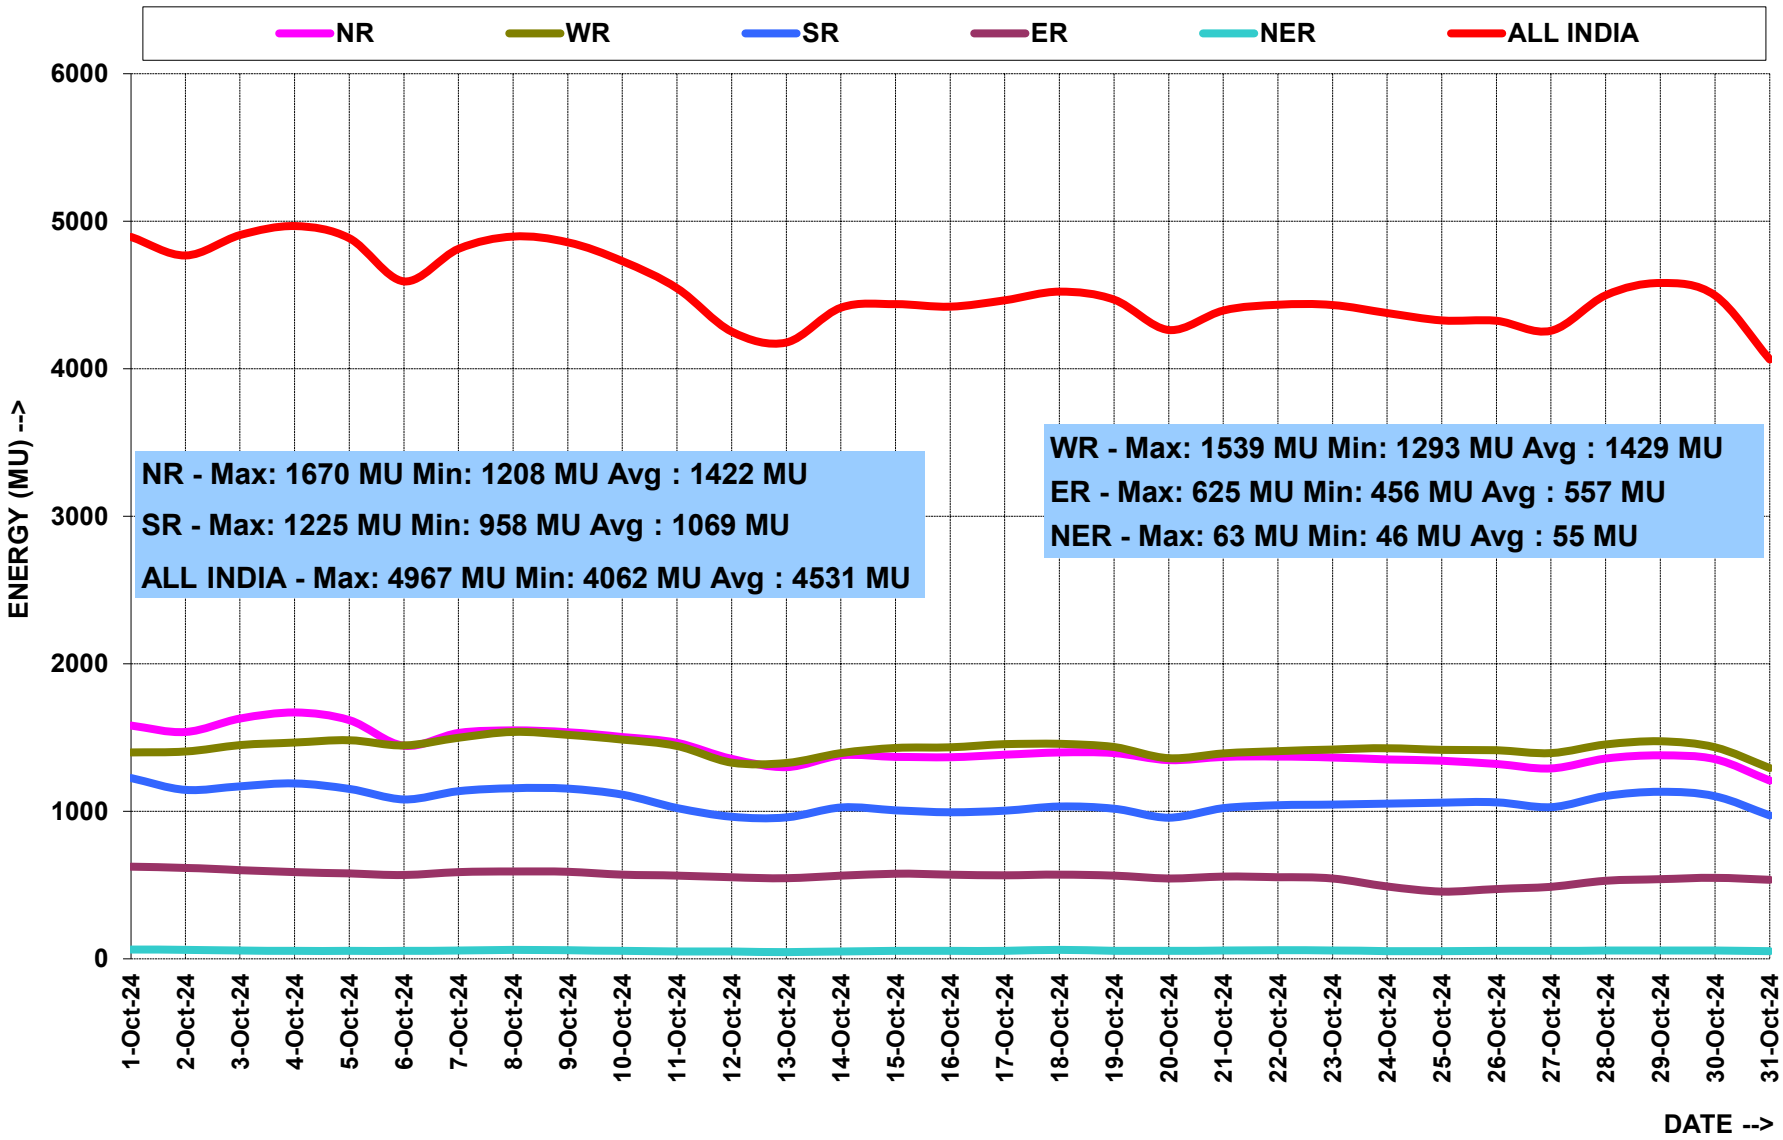

5. वर्ष 2024-25 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78		50.38	49.46	50.00
	Oct-24	All India Grid	4.86	80.27	14.87		50.39	49.58	50.00
	2024-25 (upto Oct)	All India Grid	**4.89**	**78.37**	**16.74**		**50.67**	**49.46**	**50.00**

5.1 अक्तूबर 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR OCTOBER 2024

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Oct-24	6.37	82.79	10.84		50.15	49.66	49.99	0.03
	02-Oct-24	2.26	75.31	22.43		50.18	49.75	50.01	0.03
	03-Oct-24	1.19	80.42	18.39		50.20	49.85	50.01	0.02
	04-Oct-24	0.64	77.89	21.47		50.20	49.88	50.01	0.02
	05-Oct-24	4.98	78.11	16.91		50.19	49.81	50.00	0.03
	06-Oct-24	9.69	78.23	12.08		50.19	49.72	49.99	0.04
	07-Oct-24	6.55	77.49	15.96		50.18	49.84	50.00	0.03
	08-Oct-24	9.04	83.11	7.85		50.15	49.70	49.98	0.04
	09-Oct-24	0.28	81.30	18.43		50.18	49.88	50.02	0.02
	10-Oct-24	0.58	81.26	18.16		50.18	49.88	50.01	0.02
	11-Oct-24	5.52	79.46	15.02		50.20	49.82	49.99	0.03
	12-Oct-24	7.62	71.27	21.11		50.22	49.78	50.00	0.04
	13-Oct-24	3.16	81.77	15.07		50.19	49.81	50.00	0.03
	14-Oct-24	1.70	81.34	16.96		50.24	49.84	50.01	0.02
	15-Oct-24	11.12	80.68	8.19		50.19	49.64	49.98	0.05
	16-Oct-24	6.47	81.60	11.93		50.16	49.58	49.99	0.04
	17-Oct-24	6.50	80.06	13.44		50.22	49.60	49.99	0.04
	18-Oct-24	0.69	80.68	18.62		50.18	49.84	50.01	0.02
	19-Oct-24	5.38	82.48	12.14		50.25	49.82	49.99	0.03
	20-Oct-24	2.42	75.98	21.60		50.27	49.75	50.01	0.03
	21-Oct-24	8.99	79.51	11.49		50.12	49.62	49.98	0.05
	22-Oct-24	5.06	80.75	14.19		50.22	49.79	50.00	0.03
	23-Oct-24	1.00	79.63	19.38		50.24	49.81	50.01	0.03
	24-Oct-24	7.88	72.72	19.40		50.37	49.72	50.01	0.06
	25-Oct-24	1.61	80.75	17.64		50.39	49.86	50.01	0.04
	26-Oct-24	3.26	85.19	11.55		50.16	49.82	49.99	0.02
	27-Oct-24	3.75	87.99	8.26		50.19	49.79	49.99	0.02
	28-Oct-24	13.11	81.25	5.64		50.12	49.60	49.97	0.06
	29-Oct-24	6.11	83.48	10.41		50.14	49.82	49.99	0.03
	30-Oct-24	3.43	88.04	8.53		50.15	49.76	49.99	0.02
	31-Oct-24	4.19	77.91	17.91		50.26	49.83	50.00	0.03


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: अक्तूबर 2024 MONTH:- OCT 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-24	275	105	153	102	26	661
02-Oct-24	267	99	138	97	29	628
03-Oct-24	267	102	145	100	32	646
04-Oct-24	258	95	144	98	40	636
05-Oct-24	246	98	164	100	41	649
06-Oct-24	240	84	146	102	40	612
07-Oct-24	224	86	138	102	38	589
08-Oct-24	221	86	151	96	36	590
09-Oct-24	211	72	146	98	35	562
10-Oct-24	203	61	146	96	38	543
11-Oct-24	196	51	139	96	37	519
12-Oct-24	186	68	107	90	37	488
13-Oct-24	182	65	124	87	34	491
14-Oct-24	181	56	145	85	31	497
15-Oct-24	175	63	142	84	29	493
16-Oct-24	165	82	152	85	30	513
17-Oct-24	163	78	146	79	29	494
18-Oct-24	160	84	144	85	29	503
19-Oct-24	160	69	144	79	28	480
20-Oct-24	156	67	141	76	28	468
21-Oct-24	160	68	154	75	25	481
22-Oct-24	155	86	160	73	26	500
23-Oct-24	151	58	154	66	26	456
24-Oct-24	150	59	158	61	27	456
25-Oct-24	146	51	158	65	27	446
26-Oct-24	144	43	152	65	27	431
27-Oct-24	143	43	147	62	25	419
28-Oct-24	145	57	156	60	25	443
29-Oct-24	145	66	161	56	25	453
30-Oct-24	144	56	152	61	26	439
31-Oct-24	140	54	126	46	27	393
कुल TOTAL	5760	2211	4530	2525	954	15980
उच्चतम MAXIMUM	275	105	164	102	41	661
निम्नतम MINIMUM	140	43	107	46	25	393
औसत AVERAGE	186	71	146	81	31	515
संचयी 2024-25 Cumulative 2024-25	63229	14113	22091	13128	5890	118451
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

HYDRO ENERGY DURING THE MONTH OF OCTOBER' 2024

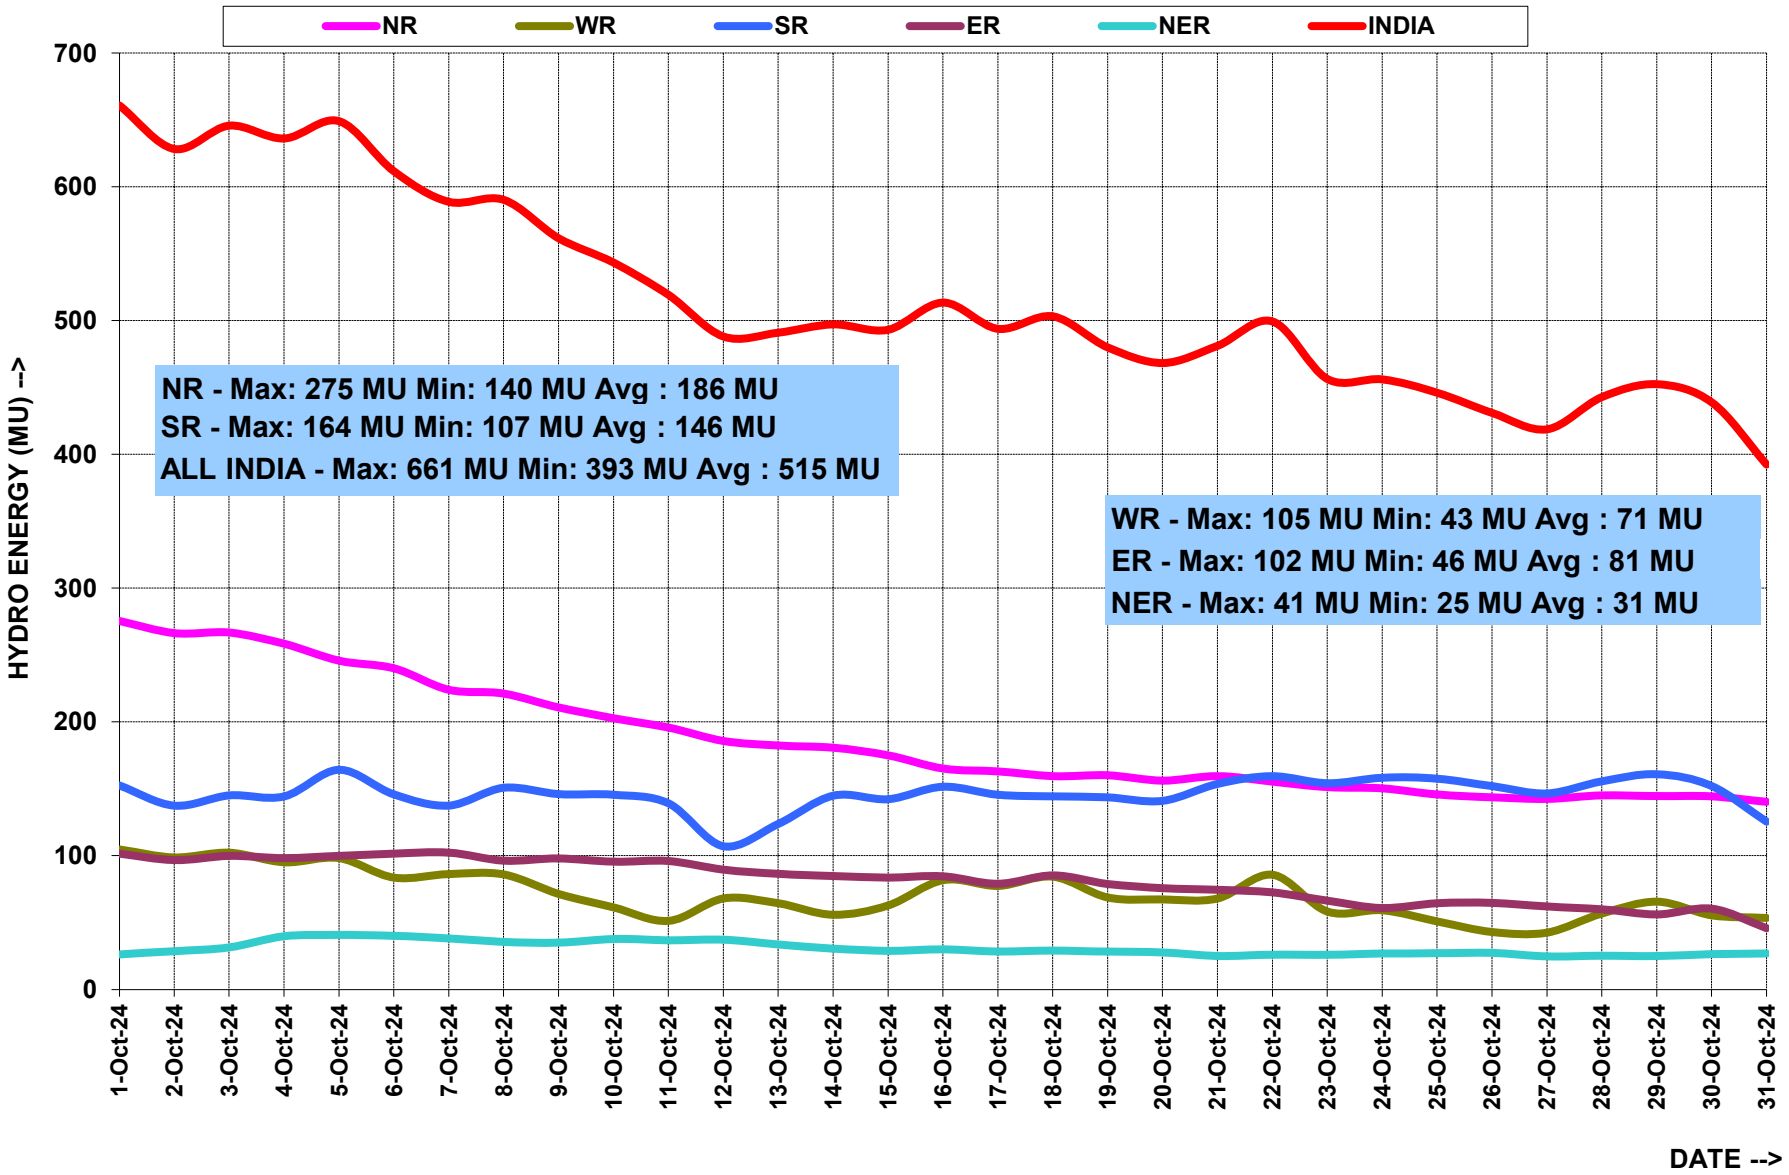

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: अक्तूबर 2024 MONTH:- OCT 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-24	23	50	17	----------	----------	90
02-Oct-24	31	63	44	----------	----------	138
03-Oct-24	42	108	74	----------	----------	224
04-Oct-24	50	103	75	----------	----------	228
05-Oct-24	21	57	40	----------	----------	118
06-Oct-24	6	26	17	----------	----------	49
07-Oct-24	2	45	44	----------	----------	91
08-Oct-24	12	33	40	----------	----------	85
09-Oct-24	5	29	44	----------	----------	79
10-Oct-24	12	45	63	----------	----------	120
11-Oct-24	6	67	37	----------	----------	110
12-Oct-24	3	49	56	----------	----------	107
13-Oct-24	8	46	36	----------	----------	90
14-Oct-24	5	24	22	----------	----------	51
15-Oct-24	3	18	26	----------	----------	47
16-Oct-24	4	26	60	----------	----------	90
17-Oct-24	10	37	94	----------	----------	141
18-Oct-24	7	45	61	----------	----------	113
19-Oct-24	3	26	25	----------	----------	54
20-Oct-24	8	25	23	----------	----------	55
21-Oct-24	18	17	25	----------	----------	60
22-Oct-24	6	18	15	----------	----------	39
23-Oct-24	3	27	19	----------	----------	49
24-Oct-24	3	35	23	----------	----------	61
25-Oct-24	3	42	25	----------	----------	70
26-Oct-24	3	24	36	----------	----------	63
27-Oct-24	12	39	36	----------	----------	87
28-Oct-24	7	38	43	----------	----------	89
29-Oct-24	9	33	40	----------	----------	81
30-Oct-24	9	24	15	----------	----------	47
31-Oct-24	4	37	20	----------	----------	61
कुल TOTAL	337	1255	1196	----------	----------	2788
उच्चतम MAXIMUM	50	108	94	----------	----------	228
निम्नतम MINIMUM	2	17	15	----------	----------	39
औसत AVERAGE	11	40	39	----------	----------	90
संचयी 2024-25 Cumulative 2024-25	4692	24561	27814	----------	----------	57068
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: अक्तूबर 2024 MONTH:- OCT 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-24	169	96	128	3.3	0.7	397
02-Oct-24	177	98	126	2.8	0.9	404
03-Oct-24	176	96	117	3.1	0.5	393
04-Oct-24	175	95	117	3.3	0.4	391
05-Oct-24	165	93	104	2.8	0.4	364
06-Oct-24	164	93	105	2.7	0.6	365
07-Oct-24	166	106	117	3.0	0.7	393
08-Oct-24	155	100	118	3.0	0.8	377
09-Oct-24	156	85	113	3.4	0.8	358
10-Oct-24	164	69	115	4.0	0.6	352
11-Oct-24	174	57	100	3.9	0.6	336
12-Oct-24	167	63	116	3.7	0.7	351
13-Oct-24	134	72	112	3.5	0.6	322
14-Oct-24	137	78	61	3.4	1.0	280
15-Oct-24	166	86	79	3.6	0.7	336
16-Oct-24	136	89	72	3.7	0.7	302
17-Oct-24	136	88	103	3.6	0.8	332
18-Oct-24	158	89	103	3.6	0.8	354
19-Oct-24	157	89	96	3.5	0.8	347
20-Oct-24	143	77	109	2.9	1.1	333
21-Oct-24	142	91	105	2.8	1.0	342
22-Oct-24	153	95	114	3.8	1.0	367
23-Oct-24	156	90	124	3.0	0.5	374
24-Oct-24	159	92	112	4.0	0.4	368
25-Oct-24	158	97	119	2.4	0.6	377
26-Oct-24	161	103	133	1.4	0.6	399
27-Oct-24	162	97	126	2.0	0.9	388
28-Oct-24	161	85	124	2.6	1.0	374
29-Oct-24	158	94	120	2.9	0.9	375
30-Oct-24	162	96	104	3.3	0.5	366
31-Oct-24	150	97	112	2.8	0.5	363
कुल TOTAL	4898	2756	3406	98	22	11179
उच्चतम MAXIMUM	177	106	133	4.0	1.1	404
निम्नतम MINIMUM	134	57	61	1.4	0.4	280
औसत AVERAGE	158	89	110	3.2	0.7	361
संचयी 2024-25 Cumulative 2024-25	32717	16965	24443	631	196.3	74953
अब तक का उच्चतम All Time Max.	186	**106**	149	4.1	3.5	426
दिनांक Date	01.05.24	**07.10.24**	31.03.24	09.06.24	08.09.24	30.04.24

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: अक्तूबर 2024 MONTH:- OCT 2024

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फ़ैक्टर Diversity Factor*
01-Oct-24	71899	65113	58658	29802	3479	217592	1.052
02-Oct-24	70386	63204	55464	29134	3166	207589	1.066
03-Oct-24	74273	65748	56859	28356	2971	219222	1.041
04-Oct-24	74226	66497	57060	27805	2927	218945	1.044
05-Oct-24	71538	67035	53581	27268	2980	215149	1.034
06-Oct-24	67596	63752	49623	27262	3008	204673	1.032
07-Oct-24	69839	67576	54063	28113	3250	215437	1.034
08-Oct-24	69607	68101	54472	27835	3320	216337	1.032
09-Oct-24	69041	67067	55328	27039	3270	217069	1.022
10-Oct-24	68327	66560	53089	26887	3083	212099	1.028
11-Oct-24	67373	64293	48179	26251	2820	203059	1.029
12-Oct-24	61124	57853	45087	25863	2746	186976	1.030
13-Oct-24	61806	59877	43995	25695	2536	190081	1.020
14-Oct-24	65998	64770	48204	26449	2955	205260	1.015
15-Oct-24	64502	65690	46656	27195	3026	205066	1.010
16-Oct-24	64155	65228	45661	26581	3128	203927	1.004
17-Oct-24	64783	66361	46858	27224	3115	207772	1.003
18-Oct-24	64351	66385	47850	27105	3113	208270	1.003
19-Oct-24	64351	66385	47850	27105	3113	208270	1.003
20-Oct-24	62346	60890	43241	25877	2991	194819	1.003
21-Oct-24	64603	65204	47551	27172	3157	207132	1.003
22-Oct-24	65581	65071	47682	27315	3337	208179	1.004
23-Oct-24	65435	65914	47840	25952	3162	207903	1.002
24-Oct-24	64716	66140	48031	23580	2959	204598	1.004
25-Oct-24	64336	65574	48129	22669	3078	202651	1.006
26-Oct-24	63680	65605	48667	24451	3082	203851	1.008
27-Oct-24	60565	62357	47172	25115	2885	194669	1.018
28-Oct-24	63284	66116	52338	26268	3164	206496	1.023
29-Oct-24	64270	66776	53240	26433	3384	208562	1.027
30-Oct-24	63577	64206	53051	26826	3260	205696	1.025
31-Oct-24	55621	57234	46313	25483	3038	182870	1.026
उच्चतम MAXIMUM	74273	68101	58658	29802	3479	219222	1.066
निम्नतम MINIMUM	55621	57234	43241	22669	2536	182870	1.002
औसत AVERAGE	65909	64793	50058	26649	3081	206136	1.021
अब तक का उच्चतम All Time Max.	91215	74974	68735	32531	3905	250070	
दिनांक Date	19.06.24	01.06.24	13.03.24	10.06.24	19.09.24	30.05.24	


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 03 OCT (MAXIMUM DEMAND MET)

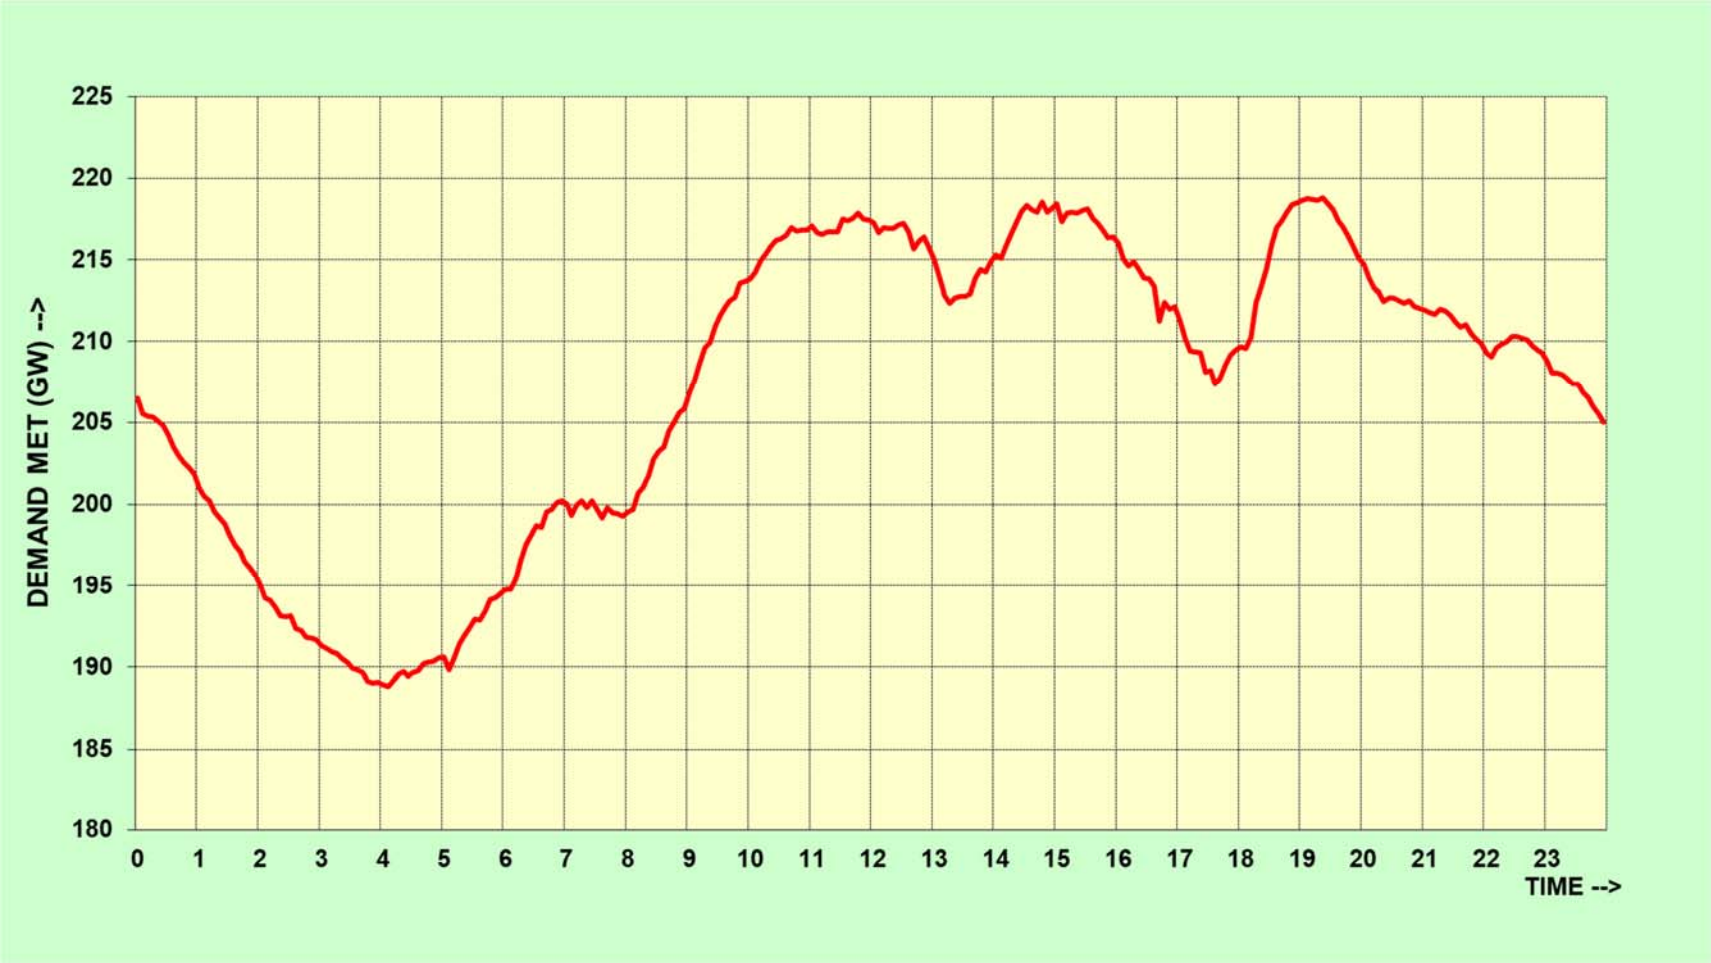

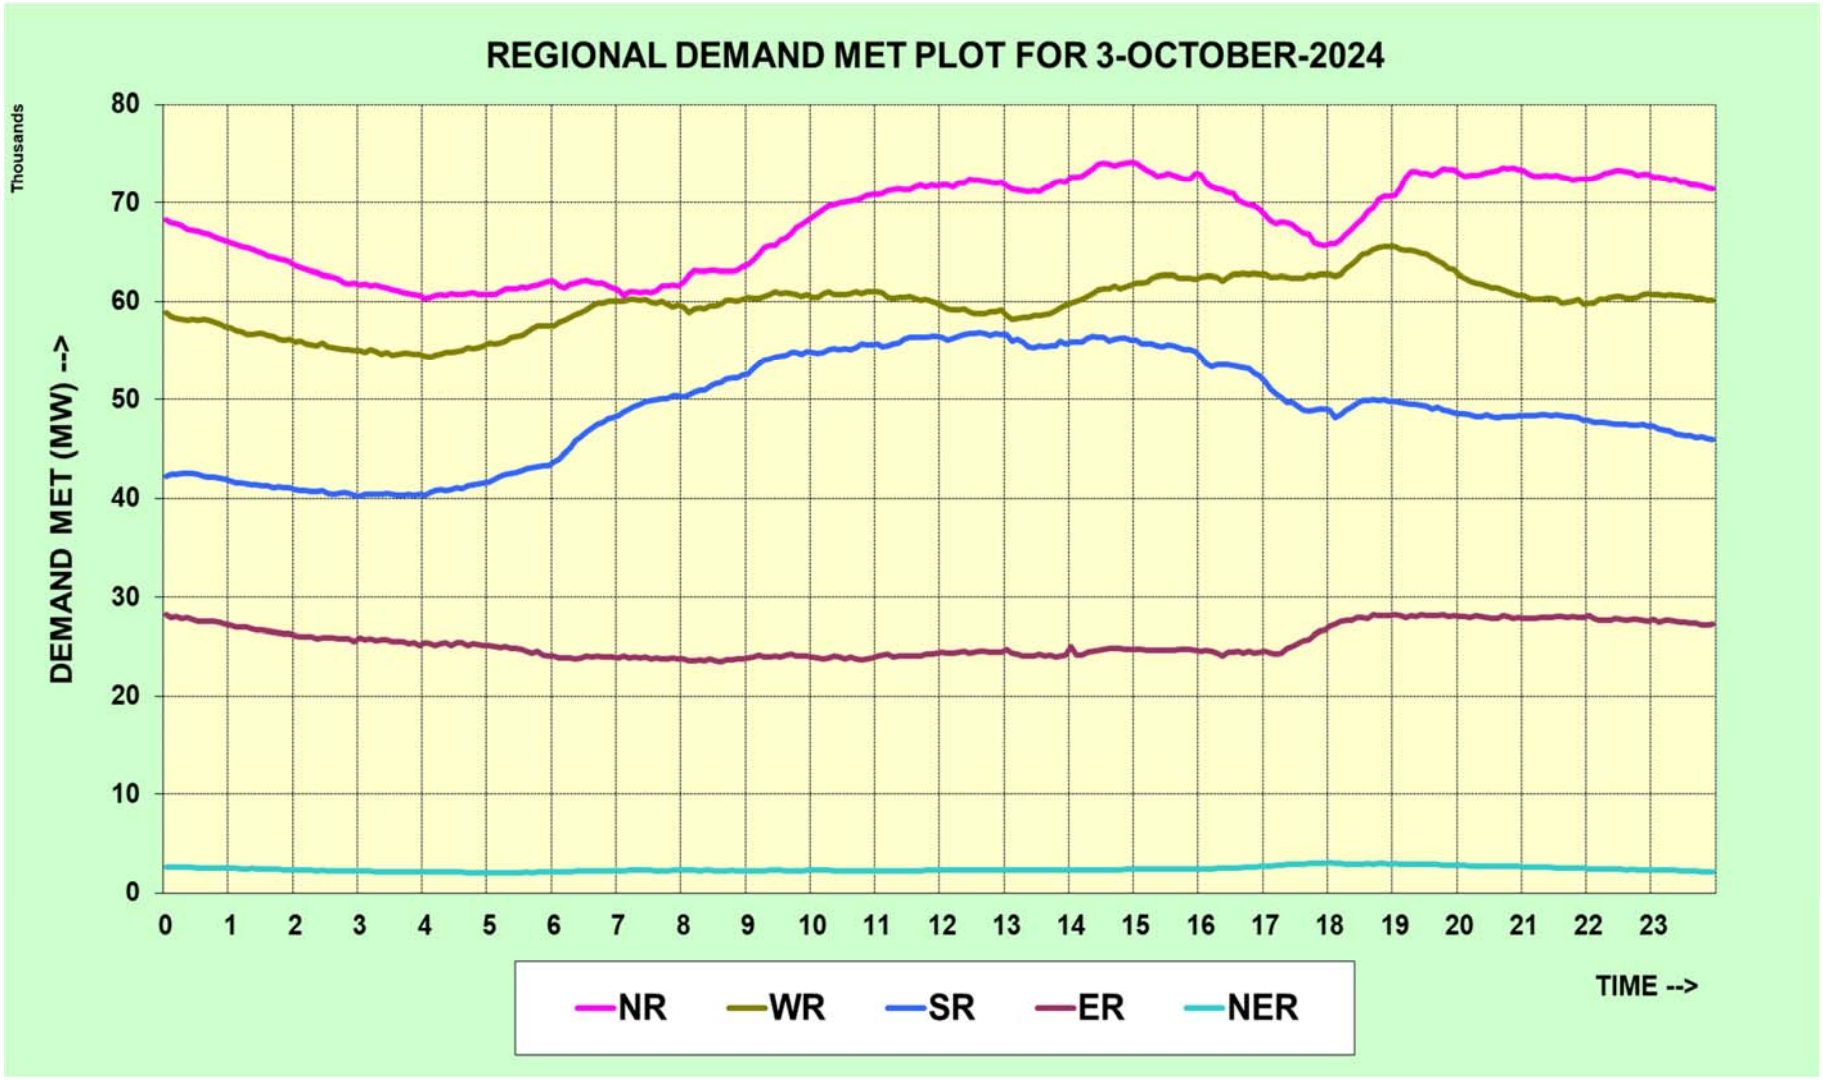
REGIONAL DEMAND MET PLOT FOR 3-OCTOBER-2024
Thousands
DEMAND MET (MW) -->
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

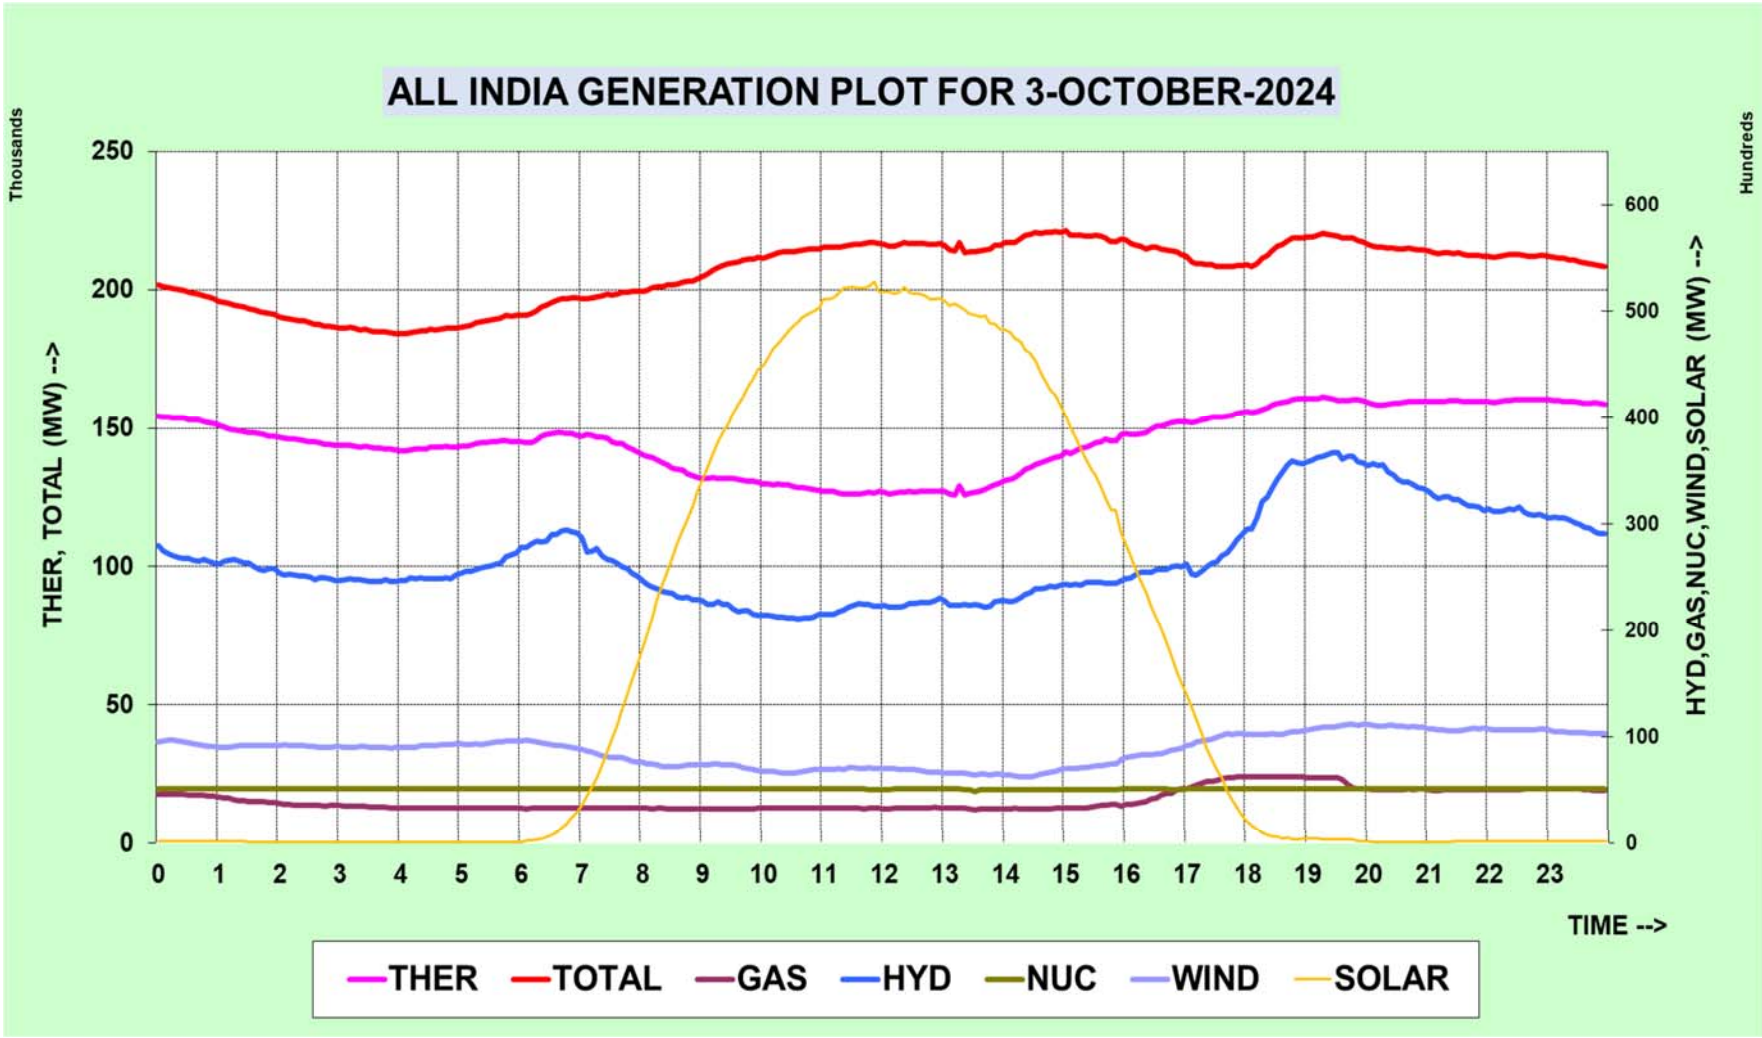
ALL INDIA GENERATION PLOT FOR 3-OCTOBER-2024
Thousands
THER, TOTAL (MW) -->
250
200
150
100
50
0
Hundreds
HYD,GAS,NUC,WIND,SOLAR (MW) -->
600
500
400
300
200
100
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
THER
TOTAL
GAS
HYD
NUC
WIND
SOLAR

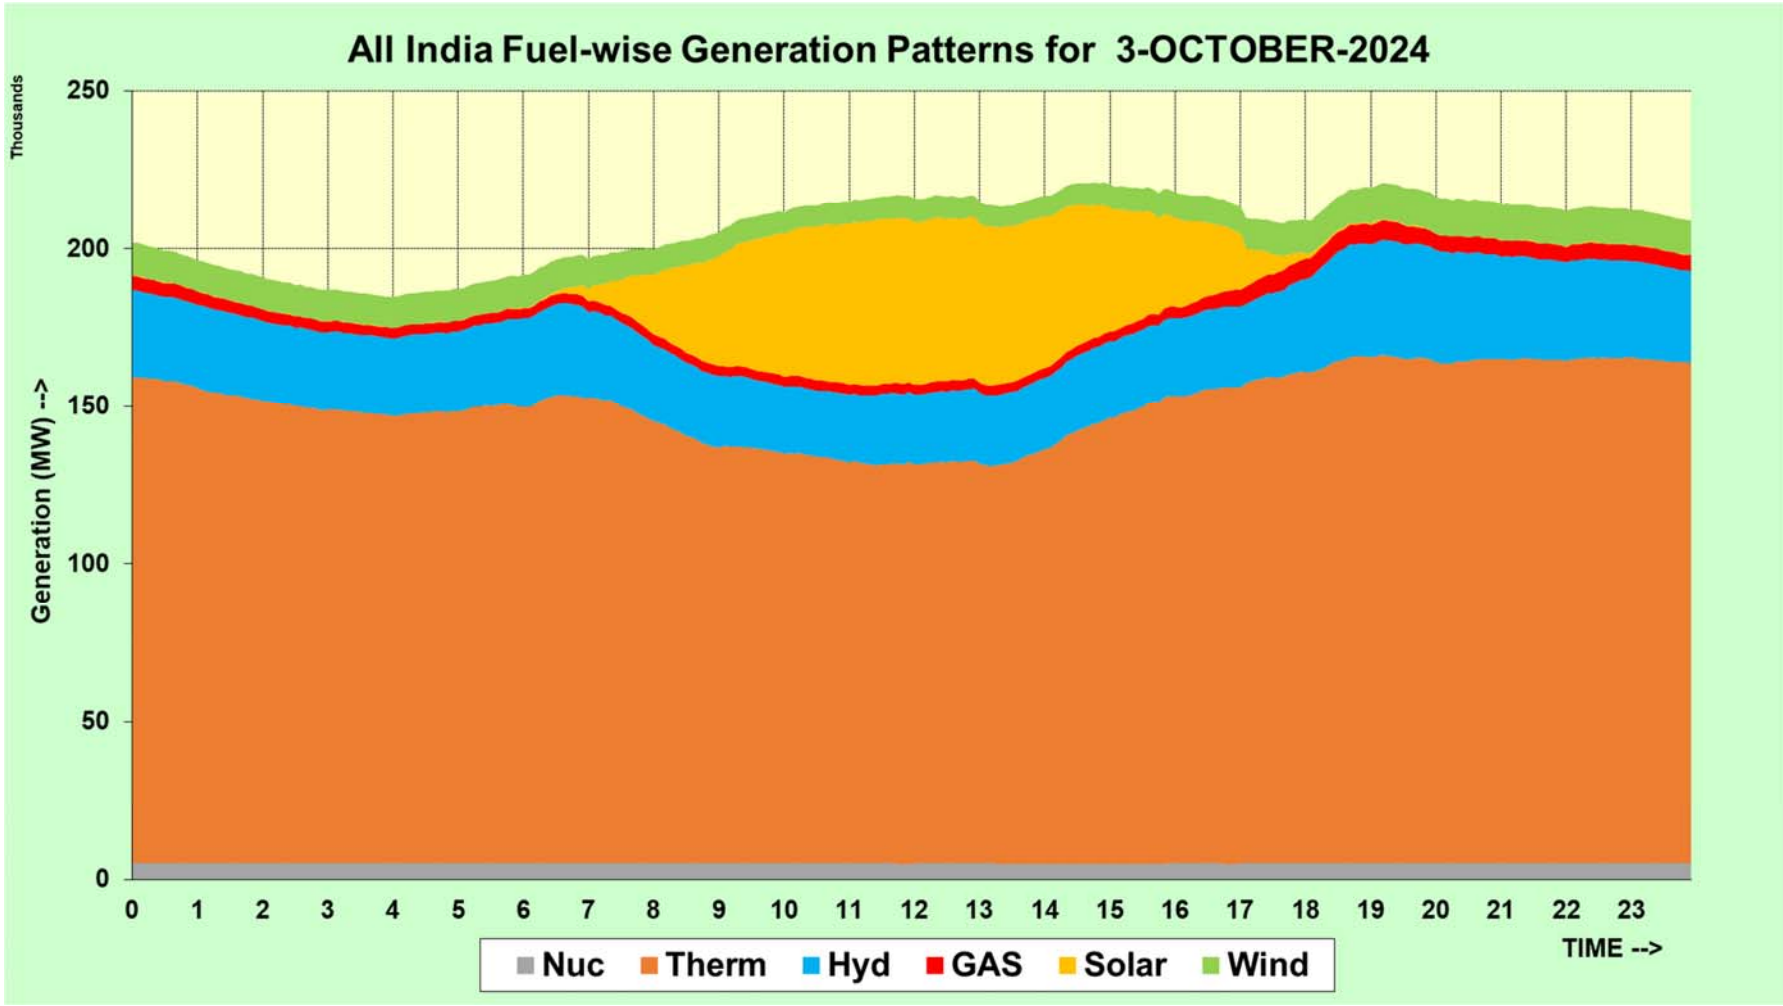
All India Fuel-wise Generation Patterns for 3-OCTOBER-2024
Thousands
Generation (MW) -->
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Nuc
Therm
Hyd
GAS
Solar
Wind

03 अक्तूबर 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 03 OCTOBER 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	199518		**12:05**	213698
00:20	198439		**12:20**	214770
00:35	197358		**12:35**	214710
00:50	196063		**12:50**	214462
01:05	193821		**13:05**	212286
01:20	192637		**13:20**	211297
01:35	191441		**13:35**	211992
01:50	189987		**13:50**	213906
02:05	188481		**14:05**	215006
02:20	187225		**14:20**	217610
02:35	186277		**14:35**	218369
02:50	185378		**14:50**	218886
03:05	184897		**15:05**	218344
03:20	184353		**15:20**	217688
03:35	183629		**15:35**	217870
03:50	183190		**15:50**	216931
04:05	182733		**16:05**	215173
04:20	183795		**16:20**	213467
04:35	184287		**16:35**	213487
04:50	184671		**16:50**	212262
05:05	185405		**17:05**	208633
05:20	187170		**17:20**	207741
05:35	187804		**17:35**	206778
05:50	188910		**17:50**	206998
06:05	189448		**18:05**	206811
06:20	192333		**18:20**	210762
06:35	194843		**18:35**	214671
06:50	195836		**18:50**	217207
07:05	195607		**19:05**	217526
07:20	196624		**19:20**	218646
07:35	196923		**19:35**	217180
07:50	197582		**19:50**	216292
08:05	197861		**20:05**	214438
08:20	199175		**20:20**	213633
08:35	200215		**20:35**	213384
08:50	201365		**20:50**	213128
09:05	203835		**21:05**	212053
09:20	206832		**21:20**	211968
09:35	208139		**21:35**	211303
09:50	209304		**21:50**	211201
10:05	210261		**22:05**	210300
10:20	211985		**22:20**	211131
10:35	212281		**22:35**	210897
10:50	213360		**22:50**	210990
11:05	213630		**23:05**	210062
11:20	214032		**23:20**	209292
11:35	214611		**23:35**	208181
11:50	214876		**23:50**	207011
Maximum Demand of 219222 MW met@14:59 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - OCTOBER 2024

REGION	STATE	Energy Requirement & Met (MU/Day)			Energy Requirement & Met (MU)				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	5	5	0.0	145	145	0	0.0	298	298	0	0.0
	Delhi	105	105	0.0	3250	3250	0	0.0	6161	6161	0	0.0
	Haryana	199	199	0.0	6162	6162	0	0.0	11087	11087	0	0.0
	Himachal Pradesh	34	34	0.0	1067	1067	0	0.0	1947	1947	0	0.0
	J&K(UT) and Ladakh(UT)	50	50	-0.4	1558	1546	-12	-0.8	3068	2742	-326	-10.6
	Punjab	204	204	0.0	6338	6338	0	0.0	14311	14311	0	0.0
	Rajasthan	318	318	0.0	9845	9845	0	0.0	16206	16206	0	0.0
	Uttar Pradesh	459	459	0.0	14230	14229	0	0.0	26756	26756	0	0.0
	Uttarakhand	44	44	0.0	1370	1369	0	0.0	2412	2412	0	0.0
	Railway_NR ISTS	4	4	0.0	132	132	0	0.0	238	238	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	5	5	0	0.0
	TOTAL	1423	1422	-0.4	44099	44086	-12	0.0	73686	73686	0	0.0
WR	Gujarat	425	425	0.0	13185	13185	0	0.0	22092	22092	0	0.0
	Madhya Pradesh	259	259	0.0	8024	8024	0	0.0	13603	13563	-40	-0.3
	Chhattisgarh	124	124	0.0	3853	3852	-1	0.0	5916	5916	0	0.0
	Maharashtra	544	544	0.0	16873	16871	-2	0.0	26632	26613	-19	-0.1
	Goa	15	15	0.0	455	455	0	0.0	741	741	0	0.0
	DNHDDPDCL	30	30	0.0	938	938	0	0.0	1390	1390	0	0.0
	AMNSIL	19	19	0.0	575	575	0	0.0	907	907	0	0.0
	BALCO	13	13	0.0	392	392	0	0.0	534	534	0	0.0
	TOTAL	1429	1429	-0.1	44294	44292	-3	0.0	68640	68568	-72	-0.1
SR	Andhra Pradesh	206	206	-0.6	6399	6382	-18	-0.3	11545	11545	0	0.0
	Telangana	235	234	-0.6	7270	7250	-20	-0.3	14003	14003	0	0.0
	Karnataka	207	206	-0.7	6408	6386	-22	-0.3	12850	12850	0	0.0
	Kerala	83	83	-0.2	2567	2560	-7	-0.3	4455	4455	0	0.0
	Tamil Nadu	331	330	-0.9	10267	10241	-26	-0.3	18113	18113	0	0.0
	Puducherry	10	10	0.0	301	300	-1	-0.2	517	517	0	-0.1
	TOTAL	1071	1068	-3.0	33212	33119	-93	-0.3	58678	58678	0	0.0
ER	Bihar	131	130	-0.1	4047	4044	-3	-0.1	7204	7204	0	0.0
	Jharkhand	42	42	0.0	1305	1304	-1	-0.1	2229	2229	0	0.0
	DVC	70	70	0.0	2181	2181	0	0.0	3453	3453	0	0.0
	Odisha	126	126	0.0	3916	3916	0	0.0	6388	6388	0	0.0
	West Bengal	192	192	0.0	5967	5967	0	0.0	11227	11227	0	0.0
	Sikkim	1	1	0.0	39	39	0	0.0	99	99	0	0.0
	Railways_ER ISTS	0	0	0.0	5	5	0	0.0	25	25	0	0.0
	TOTAL	563	563	-0.1	17459	17456	-3	0.0	29932	29827	-105	-0.4
NER	Arunachal Pradesh	3	3	0.0	86	86	0	0.0	170	170	0	0.0
	Assam	35	35	0.0	1072	1072	0	0.0	2262	2262	0	0.0
	Manipur	3	3	0.0	81	81	0	0.0	226	226	0	0.0
	Meghalaya	5	5	0.0	155	155	0	0.0	354	354	0	0.0
	Mizoram	2	2	0.0	57	57	0	0.0	136	136	0	0.0
	Nagaland	2	2	0.0	77	77	0	0.0	176	176	0	0.0
	Tripura	6	6	0.0	171	171	0	0.0	333	333	0	0.0
	TOTAL	55	55	0.0	1698	1698	0	0.0	3482	3482	0	0.0
ALL INDIA		4541	4537	-3.6	140761	140650	-111	-0.1				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF OCTOBER 2024 vs OCTOBER 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Oct-23	Oct-24	Difference	% Change	Average MU/day for Oct-24	Oct-23	Oct-24	Difference	% Change	Average MU/day for Oct-24
NR	Chandigarh	127	145	18	15	5	127	145	18	15	5
	Delhi	2805	3250	445	16	105	2805	3250	445	16	105
	Haryana	5377	6162	785	15	199	5346	6162	817	15	199
	Himachal Pradesh	1013	1067	54	5	34	1010	1067	57	6	34
	J&K(UT) and Ladakh(UT)	1540	1558	18	1	50	1504	1546	42	3	50
	Punjab	5391	6338	947	18	204	5391	6338	947	18	204
	Rajasthan	9137	9845	708	8	318	9129	9845	716	8	318
	Uttar Pradesh	12178	14230	2052	17	459	12124	14229	2105	17	459
	Uttarakhand	1246	1370	123	10	44	1240	1369	129	10	44
	Railway_NR ISTS/NFL	109	135	26	23	4	109	135	26	23	4
	TOTAL	38923	44099	5176	13	1423	38785	44086	5301	14	1422
WR	Gujarat	13162	13185	23	0	425	13162	13185	23	0	425
	Madhya Pradesh	8976	8024	-952	-11	259	8976	8024	-952	-11	259
	Chhattisgarh	3423	3853	430	13	124	3414	3852	439	13	124
	Maharashtra	18049	16873	-1176	-7	544	18044	16871	-1173	-6	544
	Goa	426	455	29	7	15	426	455	29	7	15
	DNHDDPDCL	898	938	40	4	30	898	938	40	4	30
	AMNSIL	555	575	20	4	19	555	575	20	4	19
	BALCO	385	392	6	2	13	385	392	6	2	13
	TOTAL	45874	44294	-1580	-3	1429	45859	44292	-1568	-3	1429
SR	Andhra Pradesh	7357	6399	-957	-13	206	7280	6382	-898	-12	206
	Telangana	8386	7270	-1116	-13	235	8296	7250	-1046	-13	234
	Karnataka	8138	6408	-1730	-21	207	8048	6386	-1662	-21	206
	Kerala	2496	2567	71	3	83	2467	2560	93	4	83
	Tamil Nadu	10734	10267	-467	-4	331	10617	10241	-376	-4	330
	Puducherry	310	301	-10	-3	10	307	300	-7	-2	10
	TOTAL	37420	33212	-4209	-11	1071	37014	33119	-3895	-11	1068
ER	Bihar	3576	4047	471	13	131	3510	4044	534	15	130
	Jharkhand	1016	1305	289	28	42	984	1304	321	33	42
	DVC	2191	2181	-10	0	70	2191	2181	-10	0	70
	Odisha	3536	3916	380	11	126	3536	3916	380	11	126
	West Bengal	5473	5967	493	9	192	5473	5967	493	9	192
	Sikkim	29	39	10	33	1	29	39	10	33	1
	Railways_ER ISTS	5	5	0	-7	0	5	5	0	-7	0
	TOTAL	15826	17459	1633	10	563	15728	17456	1728	11	563
NER	Arunachal Pradesh	82	86	4	5	3	82	86	4	5	3
	Assam	1090	1072	-19	-2	35	1085	1072	-14	-1	35
	Manipur	80	81	1	1	3	80	81	1	1	3
	Meghalaya	177	155	-22	-12	5	173	155	-18	-10	5
	Mizoram	53	57	4	7	2	53	57	4	7	2
	Nagaland	79	77	-2	-2	2	79	77	-2	-2	2
	Tripura	162	171	8	5	6	162	171	8	5	6
	TOTAL	1723	1698	-26	-1	55	1714	1698	-16	-1	55
ALL INDIA		139767	140761	994	1	4541	139101	140650	1549	1	4537

13. DEMAND COMPARISON OF OCTOBER 2024 vs OCTOBER 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Oct-23	Oct-24	Difference	% Change	Oct-23	Oct-24	Difference	% Change
NR	Chandigarh	265	298	33	12.5	265	298	33	12.5
	Delhi	5583	6161	578	10.4	5583	6161	578	10.4
	Haryana	9947	11087	1140	11.5	9947	11087	1140	11.5
	Himachal Pradesh	1871	1947	76	4.1	1871	1947	76	4.1
	J&K(UT) and Ladakh(UT)	2735	3068	333	12.2	2735	2742	7	0.3
	Punjab	12491	14311	1820	14.6	12491	14311	1820	14.6
	Rajasthan	15641	16206	565	3.6	15641	16206	565	3.6
	Uttar Pradesh	24096	26756	2660	11.0	24096	26756	2660	11.0
	Uttarakhand	2259	2412	153	6.8	2259	2412	153	6.8
	Railway_NR ISTS/NFL	218	243	25	11.7	218	243	25	11.7
WR	Gujarat	21689	22092	403	2	21689	22092	403	1.9
	Madhya Pradesh	15245	13603	-1642	-11	15209	13563	-1646	-10.8
	Chhattisgarh	5325	5916	591	11	5325	5916	591	11.1
	Maharashtra	28206	26632	-1574	-6	28206	26613	-1593	-5.6
	Goa	734	741	7	1	734	741	7	1.0
	DNHDDPDCL	1316	1390	74	5.6	1316	1390	74	5.6
	AMNSIL	924	907	-18	-1.9	924	907	-18	-1.9
	BALCO	525	534	9	1.8	525	534	9	1.8
SR	Andhra Pradesh	13039	11545	-1494	-11.5	13039	11545	-1494	-11.5
	Telangana	15285	14003	-1282	-8.4	15266	14003	-1263	-8.3
	Karnataka	15978	12850	-3128	-19.6	15978	12850	-3128	-19.6
	Kerala	4191	4455	264	6.3	4191	4455	264	6.3
	Tamil Nadu	17484	18113	629	3.6	17386	18113	727	4.2
	Puducherry	477	517	41	8.5	474	517	43	9.1
ER	Bihar	6597	7204	607	9.2	6475	7204	729	11.3
	Jharkhand	1891	2229	338	17.9	1672	2229	557	33.3
	DVC	3477	3453	-24	-0.7	3477	3453	-24	-0.7
	Odisha	6028	6388	360	6.0	6028	6388	360	6.0
	West Bengal	9684	11227	1543	15.9	9684	11227	1543	15.9
	Sikkim	86	99	13	15.1	86	99	13	15.1
	Railways_ER ISTS	32	25	-7	-21.9	32	25	-7	-21.9
NER	Arunachal Pradesh	167	170	3	1.6	167	170	3	1.6
	Assam	2226	2262	36	1.6	2226	2262	36	1.6
	Manipur	214	226	12	5.7	214	226	12	5.7
	Meghalaya	334	354	20	6.0	334	354	20	6.0
	Mizoram	141	136	-5	-3.6	141	136	-5	-3.6
	Nagaland	166	176	10	5.8	166	176	10	5.8
	Tripura	349	333	-16	-4.7	349	333	-16	-4.7

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - OCTOBER 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	146.55	147.42	0.87	0.59	4.73	4.76	0.03
	Delhi	2924.47	2902.66	-21.81	-0.75	94.34	93.63	-0.70
	Haryana	4392.32	4305.41	-86.91	-1.98	141.69	138.88	-2.80
	Himachal Pradesh	550.24	499.27	-50.97	-9.26	17.75	16.11	-1.64
	J&K(UT) and Ladakh(UT)	1187.11	1211.32	24.21	2.04	38.29	39.07	0.78
	Punjab	3197.27	3112.12	-85.15	-2.66	103.14	100.39	-2.75
	Rajasthan	3970.10	3954.87	-15.23	-0.38	128.07	127.58	-0.49
	Uttar Pradesh	5412.42	5455.24	42.82	0.79	174.59	175.98	1.38
	Uttarakhand	919.61	915.50	-4.11	-0.45	29.66	29.53	-0.13
	Railways_NR ISTS	119.97	132.36	12.39	10.33	3.87	4.27	0.40
	NFL	2.62	2.41	-0.21	-8.05	0.08	0.08	-0.01
	Total	22822.68	22638.57	-184.11	-0.81	736.22	730.28	-5.94
WR	Gujarat	5646.67	5547.47	-99.20	-1.76	182.15	178.95	-3.20
	Madhya Pradesh	4717.61	4625.38	-92.23	-1.96	152.18	149.21	-2.98
	Chhattisgarh	2226.16	2201.78	-24.38	-1.10	71.81	71.03	-0.79
	Maharashtra	6657.92	6702.26	44.34	0.67	214.77	216.20	1.43
	Goa	433.36	449.99	16.63	3.84	13.98	14.52	0.54
	DNHDDPDCL	933.46	937.93	4.47	0.48	30.11	30.26	0.14
	AMNSIL	268.54	274.07	5.53	2.06	8.66	8.84	0.18
	BALCO	392.99	391.68	-1.31	-0.33	12.68	12.63	-0.04
	Total	21276.71	21130.57	-146.14	-0.69	686.35	681.63	-4.71
SR	Andhra Pradesh	1726.53	1696.04	-30.49	-1.77	55.69	54.71	-0.98
	Telangana	2927.95	2987.15	59.20	2.02	94.45	96.36	1.91
	Karnataka	2007.71	1988.52	-19.19	-0.96	64.76	64.15	-0.62
	Kerala	1900.56	1917.83	17.27	0.91	61.31	61.87	0.56
	Tamil Nadu	5757.95	5752.38	-5.57	-0.10	185.74	185.56	-0.18
	Puducherry	288.94	281.13	-7.81	-2.70	9.32	9.07	-0.25
	Goa (SR)	72.06	73.30	1.24	1.72	2.32	2.36	0.04
	Total	14681.70	14696.35	14.65	0.10	473.60	474.08	0.47
ER	Bihar	3775.71	3725.74	-49.97	-1.32	121.80	120.19	-1.61
	Jharkhand	929.75	920.57	-9.18	-0.99	29.99	29.70	-0.30
	DVC	-1260.21	-1256.26	3.95	-0.31	-40.65	-40.52	0.13
	Odisha	1067.90	1021.67	-46.23	-4.33	34.45	32.96	-1.49
	West Bengal	1450.08	1389.82	-60.26	-4.16	46.78	44.83	-1.94
	Sikkim	43.37	39.16	-4.21	-9.71	1.40	1.26	-0.14
	Railways_ER ISTS	4.51	4.58	0.07	1.62	0.15	0.15	0.00
	Total	6011.10	5845.27	-165.84	-2.76	193.91	188.56	-5.35
NER	Arunachal Pradesh	72.76	72.70	-0.06	-0.08	2.35	2.35	0.00
	Assam	830.46	852.02	21.56	2.60	26.79	27.48	0.70
	Manipur	92.43	80.69	-11.74	-12.70	2.98	2.60	-0.38
	Meghalaya	72.22	65.24	-6.98	-9.66	2.33	2.10	-0.23
	Mizoram	22.05	8.92	-13.13	-59.55	0.71	0.29	-0.42
	Nagaland	71.52	63.78	-7.74	-10.82	2.31	2.06	-0.25
	Tripura	181.15	180.40	-0.75	-0.41	5.84	5.82	-0.02
	Total	1342.59	1323.75	-18.84	-1.40	43.31	42.70	-0.61
All India Total		66134.78	65634.50	-500.28	-0.76	2133.38	2117.24	-16.14

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Fin. Year 2024-25
Name of Line								
Import of NR from WR (WR-NR)								
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	714.49	**7316.94**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	840.34	**3584.03**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	1009.96	**6964.26**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	583.07	**4237.06**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	1570.74	**15059.33**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	0.00	**616.24**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	0.00	**228.47**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	17.54	**63.56**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	60.41	**594.30**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	60.83	**425.63**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	58.67	**419.53**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	0.00	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	1096.69	**7508.65**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	0.00	**1491.78**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	1113.89	**12138.72**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	89.57	**650.59**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**7216.20**	**61315.31**
Export of NR to WR (NR-WR)								
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	0.00	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	368.54	**2067.31**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	152.00	**642.85**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	126.24	**590.93**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	31.75	**91.41**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	1.94	**226.66**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	51.59	**215.59**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	0.00	**2908.15**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	391.69	**1553.18**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	0.00	**195.34**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**1123.75**	**8506.41**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Fin. Year 2024-25
Name of Line								
Import of NR from ER (ER-NR)								
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	139.89	**802.04**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	405.62	**1059.47**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	366.56	**2159.18**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	250.72	**1445.07**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	527.53	**2151.31**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	319.38	**1651.28**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	95.04	**200.13**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	259.86	**1235.43**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	0.00	**10.67**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	136.66	**394.16**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	65.13	**148.91**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	7.45	**134.33**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	0.53	**14.10**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	159.57	**580.40**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	144.05	**490.85**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**2877.99**	**12478.94**
Import of NR from NER (NER-NR)								
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55		**1096.79**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**0.00**	**1096.79**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Fin. Year 2024-25
Name of Line								
Export of NR to ER (NR-ER)								
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	0.00	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	0.00	**225.17**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	7.00	**400.79**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	0.00	**19.06**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	0.00	**7.13**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	0.00	**44.74**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	4.74	**8.40**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	0.48	**3.26**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	0.58	**4.85**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	14.57	**113.93**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	0.00	**6.54**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**27.37**	**977.60**
Export of NR to NER (NER-NR)								
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	0.00	**1365.53**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**0.00**	**1365.53**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Fin. Year 2024-25
Name of Line								
Export of WR to ER (WR-ER)								
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	308.09	**5250.00**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	65.67	**1791.84**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	0.04	**37.15**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	29.14	**1083.02**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	0.51	**650.17**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	4.23	**59.64**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	0.05	**15.00**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**407.73**	**8886.82**
Import of WR from ER (ER - WR)								
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	68.03	**178.68**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	334.28	**2068.18**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	325.55	**1738.81**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	59.96	**123.48**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	380.72	**1640.01**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	48.12	**227.67**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	60.23	**274.55**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**1276.89**	**6251.38**
Export of ER to NER (ER - NER)								
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	104.89	**571.75**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	173.82	**894.61**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	32.38	**192.24**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**311.10**	**1658.61**
Import of ER from NER (NER - ER)								
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	18.09	**470.88**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	17.26	**730.80**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	2.72	**119.41**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**38.07**	**1321.09**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Fin. Year 2024-25
Name of Line								
Export of ER to SR (ER - SR)								
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	217.59	**1457.40**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	1105.23	**6620.69**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	1297.13	**8536.07**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**2619.95**	**16614.17**
Import of ER from SR (SR - ER)								
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	0.00	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	0.00	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**0.00**	**490.92**
Export of WR to SR (WR-SR)								
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	231.23	**1447.12**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	37.08	**1358.35**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	590.95	**5389.04**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	0.00	**0.02**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	574.81	**6891.60**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	72.89	**462.81**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	0.03	**147.24**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	686.47	**5762.72**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**2193.47**	**21458.89**
Import of WR from SR (SR - WR)								
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	18.75	**1635.03**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	410.23	**3215.44**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	11.46	**157.70**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	948.20	**6187.11**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	0.00	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	0.02	**0.04**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	6.77	**165.38**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**1395.43**	**11779.37**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**19488**	**154202**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during October 2024

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Oct-24	17.44	21.30	26.62	18.54	0.00	47.41	0.00	0.00	2.84	1.77	1.87	1.94	0.00		45.63	0.00	45.25	3.82	**234.43**
2-Oct-24	17.66	18.18	25.11	17.42	0.00	48.38	0.00	0.00	2.95	1.58	1.72	1.92	0.00		48.34	0.00	43.00	3.39	**229.65**
3-Oct-24	22.45	21.79	33.56	20.44	0.00	46.60	0.00	0.00	4.01	3.90	1.79	2.03	0.00		48.33	0.00	45.08	5.41	**255.39**
4-Oct-24	22.87	22.80	33.60	21.30	0.00	64.88	0.00	0.00	3.99	2.84	2.12	2.12	0.00		47.80	0.00	43.32	4.25	**271.89**
5-Oct-24	16.94	25.54	30.66	8.41	0.00	63.80	0.00	0.00	2.64	2.44	2.06	1.98	0.00		48.63	0.00	36.45	4.08	**243.63**
6-Oct-24	7.28	18.83	17.86	16.44	0.00	78.04	0.00	0.00	1.11	0.00	2.50	2.03	0.00		43.73	0.00	30.09	1.23	**219.14**
7-Oct-24	10.54	22.78	20.70	17.58	0.00	87.27	0.00	0.00	0.00	0.00	2.58	1.67	0.00		47.72	0.00	27.39	1.29	**239.52**
8-Oct-24	17.17	25.18	27.92	18.31	0.00	71.96	0.00	0.00	0.00	1.40	2.32	2.13	0.00		39.27	0.00	29.68	2.43	**237.77**
9-Oct-24	17.47	27.38	30.72	19.21	0.00	70.22	0.00	0.00	0.00	1.75	2.33	2.28	0.00		30.22	0.00	34.40	2.81	**238.79**
10-Oct-24	26.62	34.62	36.27	21.19	0.00	33.96	0.00	0.00	0.00	3.16	2.49	2.01	0.00		35.68	0.00	39.04	2.55	**237.59**
11-Oct-24	22.75	33.48	36.77	21.54	0.00	44.91	0.00	0.00	0.00	3.16	2.20	1.85	0.00		19.51	0.00	43.61	2.45	**232.23**
12-Oct-24	17.23	21.34	27.53	16.81	0.00	86.50	0.00	0.00		0.71	1.92	1.70	0.00		19.41	0.00	42.78	1.97	**237.90**
13-Oct-24	20.55	23.31	28.26	16.19	0.00	70.95	0.00	0.00		1.03	1.46	1.40	0.00		24.22	0.00	37.50	2.25	**227.12**
14-Oct-24	26.54	31.09	34.23	19.31	0.00	52.95	0.00	0.00		2.54	1.69	1.60	0.00		24.22	0.00	31.18	3.12	**228.47**
15-Oct-24	23.25	22.85	32.11	17.64	0.00	57.85	0.00	0.00		0.53	1.65	1.58	0.00		26.72	0.00	36.50	2.19	**222.87**
16-Oct-24	26.99	26.27	34.32	18.58	0.00	53.50	0.00	0.00		2.87	0.85	2.74	0.00		35.89	0.00	36.12	4.78	**242.91**
17-Oct-24	30.24	28.54	38.72	19.21	0.00	47.78	0.00	0.00		3.10	1.73	1.84	0.00		36.27	0.00	39.65	5.00	**252.08**
18-Oct-24	29.86	25.55	36.53	19.01	0.00	46.73	0.00	0.00		3.11	1.80	1.98	0.00		36.28	0.00	37.10	5.00	**242.95**
19-Oct-24	28.11	28.14	37.92	17.63	0.00	47.89	0.00	0.00		2.44	1.97	2.28	0.00		36.28	0.00	31.21	4.30	**238.17**
20-Oct-24	28.61	27.83	37.77	18.01	0.00	46.85	0.00	0.00		3.76	1.97	1.95	0.00		34.80	0.00	36.85	5.17	**243.57**
21-Oct-24	30.42	31.95	36.78	20.47	0.00	41.15	0.00	0.00		2.12	1.91	1.92	0.00		36.28	0.00	43.05	3.52	**249.57**
22-Oct-24	32.95	30.26	43.15	21.25	0.00	35.01	0.00	0.00	0.00	3.02	1.67	1.87	0.00		36.25	0.00	42.98	2.98	**251.39**
23-Oct-24	31.85	31.48	36.24	21.10	0.00	35.06	0.00	0.00		2.91	2.54	1.15	0.00		36.28	0.00	43.05	2.38	**244.04**
24-Oct-24	29.23	32.07	36.72	20.87	0.00	29.42	0.00	0.00		2.48	1.87	1.80	0.00		36.28	0.00	34.75	3.17	**228.66**
25-Oct-24	20.84	31.08	31.96	19.46	0.00	63.97	0.00	0.00		1.02	2.22	1.81	0.00	0.00	41.34	0.00	22.54	1.61	**237.85**
26-Oct-24	14.59	29.45	28.64	15.48	0.00	59.42	0.00	0.00		0.46	1.92	2.14	0.00		58.96	0.00	15.40	0.92	**227.38**
27-Oct-24	19.62	29.19	30.51	18.65	0.00	40.10	0.00	0.00		1.64	1.88	2.09	0.00		26.50	0.00	28.58	1.60	**200.36**
28-Oct-24	26.05	30.18	35.36	21.57	0.00	28.56	0.00	0.00		1.26	2.20	1.80	0.00		24.21	0.00	33.46	1.43	**206.08**
29-Oct-24	29.09	33.59	38.18	21.91	0.00	22.04	0.00	0.00	0.00	2.03	2.21	1.91	0.00		24.12	0.00	36.19	1.39	**212.66**
30-Oct-24	28.43	30.94	36.17	21.77	0.00	21.88	0.00	0.00		1.38	1.67	1.57	0.00		24.02	0.00	36.19	1.70	**205.72**
31-Oct-24	20.85	23.35	29.07	17.77	0.00	25.70	0.00	0.00		0.00	1.72	1.58	0.00		23.50	0.00	31.50	1.38	**176.42**
Total	**714.49**	**840.34**	**1009.96**	**583.07**	**0.00**	**1570.74**	**0.00**	**0.00**	**17.54**	**60.41**	**60.83**	**58.67**	**0.00**	**0.00**	**1096.69**	**0.00**	**1113.89**	**89.57**	**7216.20**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during October 2024

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Oct-24	0.00	0.00	0.00	0.00	9.78	0.00	3.11	2.40	0.00	0.00	0.00	0.00	2.85		0.00	10.86	0.00	0.00	**29.00**
2-Oct-24	0.00	0.00	0.00	0.00	9.58	0.00	6.08	2.31	0.00	0.00	0.00	0.00	1.50		0.00	9.71	0.00	0.00	**29.18**
3-Oct-24	0.00	0.00	0.00	0.00	10.12	0.00	6.13	1.04	0.00	0.00	0.00	0.00	1.06		0.00	0.51	0.00	0.00	**18.86**
4-Oct-24	0.00	0.00	0.00	0.00	8.80	0.00	6.13	1.30	0.00	0.00	0.00	0.00	1.39		0.00	0.50	0.00	0.00	**18.12**
5-Oct-24	0.00	0.00	0.00	0.00	6.50	0.00	4.62	3.29	0.00	0.00	0.00	0.00	1.89		0.00	16.22	0.00	0.00	**32.52**
6-Oct-24	0.00	0.00	0.00	0.00	11.21	0.00	1.23	5.33	0.00	1.04	0.00	0.00	2.56		0.00	29.08	0.00	0.00	**50.45**
7-Oct-24	0.00	0.00	0.00	0.00	12.29	0.00	1.23	4.24	6.74	0.13	0.00	0.00	2.74		0.00	19.78	0.00	0.00	**47.15**
8-Oct-24	0.00	0.00	0.00	0.00	11.20	0.00	1.23	2.67	4.69	0.00	0.00	0.00	2.16		0.00	11.42	0.00	0.00	**33.37**
9-Oct-24	0.00	0.00	0.00	0.00	11.38	0.00	1.22	2.68	4.30	0.00	0.00	0.00	2.00		0.00	11.66	0.00	0.00	**33.24**
10-Oct-24	0.00	0.00	0.00	0.00	12.34	0.00	1.23	3.48	6.25	0.00	0.00	0.00	1.42		0.00	14.22	0.00	0.00	**38.94**
11-Oct-24	0.00	0.00	0.00	0.00	11.06	0.00	1.30	2.10	5.70	0.00	0.00	0.00	1.25		0.00	9.00	0.00	0.00	**30.41**
12-Oct-24	0.00	0.00	0.00	0.00	10.04	0.00	1.30	3.89		0.00	0.00	0.00	1.78		0.00	10.00	0.00	0.00	**27.01**
13-Oct-24	0.00	0.00	0.00	0.00	13.22	0.00	1.24	3.66		0.00	0.00	0.00	1.81		0.00	7.85	0.00	0.00	**27.78**
14-Oct-24	0.00	0.00	0.00	0.00	15.41	0.00	4.31	5.86		0.00	0.00	0.00	1.65		0.00	14.51	0.00	0.00	**41.74**
15-Oct-24	0.00	0.00	0.00	0.00	12.80	0.00	7.50	5.95		0.00	0.00	0.00	1.68		0.00	15.40	0.00	0.00	**43.33**
16-Oct-24	0.00	0.00	0.00	0.00	12.67	0.00	7.30	3.92		0.00	0.00	0.00	1.48		0.00	8.15	0.00	0.00	**33.52**
17-Oct-24	0.00	0.00	0.00	0.00	13.61	0.00	4.68	4.04		0.00	0.00	0.00	1.58		0.00	9.12	0.00	0.00	**33.03**
18-Oct-24	0.00	0.00	0.00	0.00	13.04	0.00	2.44	3.93		0.00	0.00	0.00	1.69		0.00	11.16	0.00	0.00	**32.26**
19-Oct-24	0.00	0.00	0.00	0.00	13.90	0.00	2.51	4.55		0.00	0.00	0.00	1.67		0.00	12.28	0.00	0.00	**34.91**
20-Oct-24	0.00	0.00	0.00	0.00	13.55	0.00	2.50	4.01		0.00	0.00	0.00	1.35		0.00	10.40	0.00	0.00	**31.81**
21-Oct-24	0.00	0.00	0.00	0.00	14.94	0.00	2.43	5.70		0.00	0.00	0.00	1.23		0.00	15.06	0.00	0.00	**39.36**
22-Oct-24	0.00	0.00	0.00	0.00	14.05	0.00	5.85	2.92	2.02	0.00	0.00	0.00	1.27		0.00	11.03	0.00	0.00	**37.14**
23-Oct-24	0.00	0.00	0.00	0.00	14.91	0.00	12.14	4.50		0.00	0.00	0.00	1.31		0.00	11.16	0.00	0.00	**44.02**
24-Oct-24	0.00	0.00	0.00	0.00	14.31	0.00	12.18	5.65		0.00	0.00	0.00	1.13		0.00	14.40	0.00	0.00	**47.67**
25-Oct-24	0.00	0.00	0.00	0.00	14.31	0.00	8.22	4.44		0.00	0.00	0.00	0.95	0.00	0.00	19.01	0.00	0.00	**46.93**
26-Oct-24	0.00	0.00	0.00	0.00	5.72	0.00	7.30	9.92		0.00	0.00	0.00	1.80		0.00	28.34	0.00	0.00	**53.08**
27-Oct-24	0.00	0.00	0.00	0.00	2.92	0.00	7.30	6.50		0.00	0.00	0.00	1.61		0.00	16.47	0.00	0.00	**34.80**
28-Oct-24	0.00	0.00	0.00	0.00	13.86	0.00	7.38	3.70		0.00	0.00	0.00	1.83		0.00	13.84	0.00	0.00	**40.61**
29-Oct-24	0.00	0.00	0.00	0.00	15.12	0.00	7.31	2.98	2.05	0.00	0.00	0.00	1.53		0.00	9.50	0.00	0.00	**38.49**
30-Oct-24	0.00	0.00	0.00	0.00	13.77	0.00	7.29	4.68		0.00	0.00	0.00	1.65		0.00	10.68	0.00	0.00	**38.07**
31-Oct-24	0.00	0.00	0.00	0.00	12.13	0.00	7.31	4.60		0.77	0.00	0.00	1.77		0.00	10.37	0.00	0.00	**36.95**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**368.54**	**0.00**	**152.00**	**126.24**	**31.75**	**1.94**	**0.00**	**0.00**	**51.59**	**0.00**	**0.00**	**391.69**	**0.00**	**0.00**	**1123.75**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during October 2024

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Oct-24	3.02	6.42	9.89	8.08	12.09	4.87	0.00	5.85		2.61	0.09		0.00	0.00	0.00	3.25	2.44	**58.61**	16.91	**16.91**
2-Oct-24	1.96	5.45	9.55	8.84	11.73	5.42	0.00	5.65		2.36	0.29	0.07	0.00		0.00	3.30	2.45	**57.07**	17.19	**17.19**
3-Oct-24	4.91	11.02	12.40	8.45	15.88	10.69	1.31	8.56		1.96	0.61	0.28	0.00		0.00	4.55	4.76	**85.38**	16.78	**16.78**
4-Oct-24	5.17	12.83	11.31	8.38	17.58	12.81	3.81	9.95		2.90	1.77	0.28			0.00	5.61	6.29	**98.69**	16.78	**16.78**
5-Oct-24	5.50	14.35	12.75	8.05	20.05	14.15	5.41	9.21		4.38	2.70	0.00		0.00	0.00	6.62	5.07	**108.24**	16.84	**16.84**
6-Oct-24	3.08	9.75	9.98	8.83	17.79	11.75	4.23	8.81		4.94	2.07	1.80			0.00	5.23	1.80	**90.06**	16.54	**16.54**
7-Oct-24	4.35	13.58	11.22	8.71	20.09	12.13	4.72	9.48		4.89	1.92	0.10	0.00		0.00	6.03	4.68	**101.90**	13.89	**13.89**
8-Oct-24	4.65	14.18	12.19	8.32	20.43	11.92	4.74	9.36		4.95	1.91	0.08	0.00		0.00	6.26	5.13	**104.12**	9.65	**9.65**
9-Oct-24	5.85	16.65	13.17	7.85	22.28	14.77	5.54	9.07		4.95	2.25	0.30			0.00	6.86	6.24	**115.78**	8.97	**8.97**
10-Oct-24	6.01	18.09	14.76	8.62	22.48	16.02	6.82	11.20		4.48	2.16	0.15	0.00		0.00	6.87	6.96	**124.62**	11.62	**11.62**
11-Oct-24	5.27	16.05	14.40	8.31	21.33	13.65	5.18	10.12		4.56	2.44	0.02	0.00		0.00	6.61	6.30	**114.24**	23.98	**23.98**
12-Oct-24	2.10	8.03	11.23	8.51	15.47	10.45	4.03	7.01		4.88	2.20	0.00	0.00		0.00	4.60	3.82	**82.33**	24.01	**24.01**
13-Oct-24	2.10	8.25	10.65	7.91	14.46	10.08	2.56	6.50		4.78	2.20	0.00		0.00	0.00	4.25	3.55	**77.29**	22.60	**22.60**
14-Oct-24	4.13	14.39	12.89	8.42	16.71	10.54	3.84	7.87		5.15	1.91	0.39		0.00	0.00	4.90	5.10	**96.24**	24.19	**24.19**
15-Oct-24	1.85	9.33	11.71	8.73	14.09	8.31	2.14	6.50		5.22	1.60	0.46	0.00		0.00	4.06	3.70	**77.70**	23.89	**23.89**
16-Oct-24	3.08	12.68	10.80	8.64	15.64	10.10	2.87	7.99		5.37	1.87	0.35			0.00	4.58	4.61	**88.58**	19.52	**19.52**
17-Oct-24	2.85	10.91	12.50	8.34	15.79	9.17	3.18	7.47		5.14	1.88				0.00	4.64	3.81	**85.68**	14.51	**14.51**
18-Oct-24	3.74	12.78	12.10	8.21	18.20	8.97	2.90	8.07	0.00	4.44	2.65	0.00			0.00	5.48	4.27	**91.81**	14.67	**14.67**
19-Oct-24	4.74	14.41	11.86	8.78	20.19	11.30	3.50	9.29		4.18	2.80	0.00			0.00	6.39	5.21	**102.65**	14.38	**14.38**
20-Oct-24	3.27	11.10	11.09	8.56	15.74	10.09	4.10	8.04		4.61	2.48	0.00	0.00		0.00	5.43	4.15	**88.66**	14.40	**14.40**
21-Oct-24	3.05	10.10	12.16	7.97	18.40	9.38	4.10	8.49		4.61	2.43	0.00	0.00	0.00	0.00	5.55	3.62	**89.86**	12.69	**12.69**
22-Oct-24	3.38	8.24	14.28	8.61	19.20	9.22	3.69	8.69		4.19	2.85	0.00	0.00		0.00	5.83	2.18	**90.36**	14.41	**14.41**
23-Oct-24	3.85	10.85	12.15	8.84	17.21	8.45	2.85	8.04		5.03	1.95	1.35	0.00		0.00	5.19	4.01	**89.77**	14.50	**14.50**
24-Oct-24	5.97	16.46	14.88	8.28	19.94	11.49	4.23	9.83		4.98	1.83	0.00			0.00	6.10	4.56	**108.55**	14.66	**14.66**
25-Oct-24	8.13	21.39	13.29	4.42	22.10	13.97	6.41	10.98		4.11	2.92	0.20	0.05		0.00	7.04	7.49	**122.50**	15.38	**15.38**
26-Oct-24	7.50	21.00	10.44	7.82	17.01	11.90	2.00	9.77		4.40	2.61	0.15	0.48		0.00	5.31	6.86	**107.25**	24.15	**24.15**
27-Oct-24	7.07	17.61	10.04	7.51	15.55	9.42	0.81	8.87		4.19	2.77	0.11			0.00	4.70	5.88	**94.53**	24.01	**24.01**
28-Oct-24	6.28	16.05	10.68	7.14	14.39	8.71	0.07	8.54		4.46	2.62	0.01			0.00	4.25	5.53	**88.73**	24.01	**24.01**
29-Oct-24	6.23	17.00	11.12	7.23	12.95	7.41	0.00	7.42		4.57	2.45				0.00	3.75	5.38	**85.51**	23.19	**23.19**
30-Oct-24	6.70	15.95	11.95	7.13	12.95	7.06	0.00	7.38		4.57	2.45				0.00	3.58	5.02	**84.74**	24.20	**24.20**
31-Oct-24	4.10	10.72	9.12	7.23	9.81	5.18	0.00	5.85		4.80	2.45	1.35			0.00	2.75	3.18	**66.54**	23.19	**23.19**
Total	**139.89**	**405.62**	**366.56**	**250.72**	**527.53**	**319.38**	**95.04**	**259.86**	**0.00**	**136.66**	**65.13**	**7.45**	**0.53**	**0.00**	**0.00**	**159.57**	**144.05**	**2877.99**	**555.71**	**555.71**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.2 Import-Export of NR with ER & NER during October 2024

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	1.84	0.00		0.00	0.00		0.00	0.15	0.61	0.00	0.00	**2.60**	0.00	**0.00**
2-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	1.51	0.00		0.00	0.00	0.00	0.48		0.48	0.00	0.00	**2.47**	0.00	**0.00**
3-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.61	0.00	0.00	**0.61**	0.00	**0.00**
4-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.66	0.00	0.00	**0.66**	0.00	**0.00**
5-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.13		0.06	0.32	0.00	0.00	**0.51**	0.00	**0.00**
6-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.41	0.00	0.00	**0.41**	0.00	**0.00**
7-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.05	0.00	0.00	**0.05**	0.00	**0.00**
8-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.53	0.00	0.00	**0.53**	0.00	**0.00**
9-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.47	0.00	0.00	**0.47**	0.00	**0.00**
10-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.55	0.00	0.00	**0.55**	0.00	**0.00**
11-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.56	0.00	0.00	**0.56**	0.00	**0.00**
12-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.10	0.00		0.46	0.00	0.00	**0.56**	0.00	**0.00**
13-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.15		0.08	0.44	0.00	0.00	**0.67**	0.00	**0.00**
14-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.18	0.46	0.00	0.00	**0.64**	0.00	**0.00**
15-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.41	0.00	0.00	**0.41**	0.00	**0.00**
16-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.55	0.00	0.00	**0.55**	0.00	**0.00**
17-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00				0.32	0.00	0.00	**0.32**	0.00	**0.00**
18-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.34			0.44	0.00	0.00	**0.78**	0.00	**0.00**
19-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	1.80			0.43	0.00	0.00	**2.23**	0.00	**0.00**
20-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.38	0.00		0.39	0.00	0.00	**0.77**	0.00	**0.00**
21-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.70	0.00	0.11	0.50	0.00	0.00	**1.31**	0.00	**0.00**
22-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.74	0.00		0.51	0.00	0.00	**1.25**	0.00	**0.00**
23-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.53	0.00	0.00	**0.53**	0.00	**0.00**
24-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.40			0.48	0.00	0.00	**0.88**	0.00	**0.00**
25-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.46	0.00	0.00	**0.46**	0.00	**0.00**
26-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.51	0.00	0.00	**0.51**	0.00	**0.00**
27-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.45	0.00	0.00	**0.45**	0.00	**0.00**
28-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.42	0.00	0.00	**0.42**	0.00	**0.00**
29-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.67	0.00		0.00	0.00				0.44	0.00	0.00	**1.11**	0.00	**0.00**
30-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.67	0.00		0.00	0.00				0.56	0.00	0.00	**1.23**	0.00	**0.00**
31-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	2.31	0.00		0.00	0.00	0.00			0.56	0.00	0.00	**2.87**	0.00	**0.00**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**7.00**	**0.00**	**0.00**	**0.00**	**0.00**	**4.74**	**0.48**	**0.58**	**14.57**	**0.00**	**0.00**	**27.37**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.3 Import and Export of ER with WR & NER during October 2024

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Oct-24	17.6	2.0	0.0	2.5	0.2	0.0	0.0	**22.35**	0.8	6.1	8.4	0.7	6.9	1.1	1.4	**25.48**	5.49	10.87	2.05	**18.40**	0.00	0.00	0.00	**0.00**
2-Oct-24	19.3	3.5	0.0	3.0	0.1	0.1	0.0	**25.96**	0.7	7.9	7.7	0.7	8.2	1.3	1.4	**27.92**	4.44	9.12	1.83	**15.39**	0.00	0.00	0.00	**0.00**
3-Oct-24	16.2	1.5	0.0	2.1	0.0	0.0	0.0	**19.84**	0.1	9.4	8.6	0.6	9.7	2.2	1.7	**32.49**	1.96	5.04	0.90	**7.90**	0.42	0.28	0.06	**0.76**
4-Oct-24	10.8	2.3	0.0	0.8	0.0	0.0	0.0	**14.00**	1.3	13.9	9.1	1.4	11.9	2.2	1.9	**41.70**	0.12	0.90	0.14	**1.17**	2.39	2.11	0.46	**4.97**
5-Oct-24	4.4	3.8	0.0	0.2	0.0	0.0	0.0	**8.41**	3.6	21.0	9.7	3.1	12.7	1.6	1.9	**53.57**	0.04	0.40	0.08	**0.51**	2.90	2.56	0.50	**5.95**
6-Oct-24	4.1	4.8	0.0	0.2	0.0	0.1	0.0	**9.23**	5.3	14.8	10.6	3.4	13.9	1.3	1.6	**50.92**	0.09	0.70	0.17	**0.97**	2.61	2.17	0.39	**5.17**
7-Oct-24	4.6	1.9	0.0	0.2	0.0	0.0	0.0	**6.71**	5.9	17.4	11.5	3.9	14.5	2.1	2.2	**57.52**	0.29	1.10	0.29	**1.69**	2.46	2.29	0.30	**5.05**
8-Oct-24	7.2	0.3	0.0	0.5	0.0	0.0	0.0	**8.06**	2.7	15.4	10.8	2.2	13.0	1.7	2.3	**48.15**	0.61	1.24	0.34	**2.19**	1.99	2.07	0.28	**4.34**
9-Oct-24	6.6	4.1	0.0	0.2	0.0	0.0	0.0	**10.97**	2.1	14.0	11.8	2.4	13.6	1.9	2.3	**48.17**	0.26	1.38	0.31	**1.95**	2.14	1.88	0.21	**4.24**
10-Oct-24	7.6	4.7	0.0	0.2	0.0	0.0	0.0	**12.44**	2.7	9.1	11.9	2.9	15.9	2.4	2.5	**47.42**	2.01	4.50	0.92	**7.44**	1.61	1.94	0.30	**3.85**
11-Oct-24	7.9	1.9	0.0	0.3	0.0	0.0	0.0	**10.18**	1.4	10.6	10.8	1.6	14.4	1.6	2.4	**42.79**	1.66	4.63	1.01	**7.29**	0.28	0.11	0.00	**0.39**
12-Oct-24	10.0	0.7	0.0	1.3	0.0	0.0	0.0	**11.98**	0.6	11.6	7.9	1.0	12.3	1.4	2.3	**37.08**	1.02	2.78	0.60	**4.40**	0.48	0.25	0.01	**0.73**
13-Oct-24	9.8	1.1	0.0	1.0	0.0	0.1	0.0	**12.13**	0.8	9.5	8.3	1.1	12.8	1.4	2.3	**36.14**	1.48	3.42	0.69	**5.60**	0.14	0.08	0.00	**0.22**
14-Oct-24	10.5	3.4	0.0	0.5	0.0	0.0	0.0	**14.38**	0.6	5.2	10.3	1.4	14.2	1.4	2.5	**35.59**	3.36	6.22	1.39	**10.98**	0.03	0.00	0.00	**0.03**
15-Oct-24	13.4	0.5	0.0	1.1	0.0	0.0	0.0	**15.08**	0.4	9.2	10.4	0.8	12.9	0.9	2.4	**37.05**	5.13	9.38	1.89	**16.40**	0.00	0.00	0.00	**0.00**
16-Oct-24	11.2	1.2	0.0	0.4	0.0	0.0	0.0	**12.82**	0.6	8.1	9.5	1.0	13.4	1.1	2.5	**36.06**	3.75	6.68	1.27	**11.71**	0.00	0.00	0.00	**0.00**
17-Oct-24	14.0	3.4	0.0	1.1	0.0	0.0	0.0	**18.43**	0.7	7.6	8.3	1.4	14.3	2.6	2.3	**37.31**	3.27	5.06	0.93	**9.26**	0.04	0.07	0.00	**0.11**
18-Oct-24	13.0	4.7	0.0	1.0	0.0	0.0	0.0	**18.79**	0.5	6.1	8.7	1.6	13.4	1.9	1.9	**34.13**	2.46	4.25	0.77	**7.48**	0.18	0.22	0.03	**0.43**
19-Oct-24	12.0	1.3	0.0	0.9	0.0	0.0	0.0	**14.18**	0.6	14.6	11.1	1.6	14.7	1.9	2.0	**46.55**	2.72	4.20	0.73	**7.66**	0.12	0.21	0.03	**0.36**
20-Oct-24	17.3	0.6	0.0	2.1	0.1	0.0	0.0	**20.11**	0.6	15.8	8.4	1.0	12.5	2.1	1.8	**42.25**	2.59	4.14	0.71	**7.44**	0.05	0.11	0.01	**0.17**
21-Oct-24	15.8	2.6	0.0	1.7	0.0	0.0	0.0	**20.12**	0.5	10.3	9.2	0.8	11.2	1.7	1.8	**35.52**	4.30	5.70	1.15	**11.15**	0.00	0.01	0.00	**0.01**
22-Oct-24	16.5	1.7	0.0	1.6	0.0	0.0	0.0	**19.86**	0.9	8.2	10.2	1.2	13.1	2.7	2.0	**38.32**	4.84	6.80	1.16	**12.79**	0.00	0.00	0.00	**0.00**
23-Oct-24	13.9	1.1	0.0	1.6	0.1	0.0	0.0	**16.71**	0.4	11.0	11.1	1.5	12.4	2.2	1.7	**40.26**	4.97	6.69	1.18	**12.84**	0.01	0.13	0.01	**0.15**
24-Oct-24	4.1	1.9	0.0	0.5	0.0	0.0	0.0	**6.50**	3.3	12.8	13.7	3.0	14.1	2.5	2.3	**51.68**	3.61	4.88	0.89	**9.38**	0.16	0.52	0.08	**0.76**
25-Oct-24	2.7	0.0	0.0	0.3	0.0	0.0	0.0	**3.01**	12.9	20.0	15.2	5.5	13.1	2.4	2.5	**71.63**	2.70	4.64	0.71	**8.05**	0.08	0.25	0.04	**0.36**
26-Oct-24	4.3	0.0	0.0	0.7	0.0	0.2	0.0	**5.26**	7.3	16.6	14.0	4.3	11.8	1.3	2.1	**57.44**	5.72	8.75	1.51	**15.97**	0.00	0.00	0.00	**0.00**
27-Oct-24	5.4	1.8	0.0	0.9	0.0	0.4	0.0	**8.55**	5.8	4.2	11.4	3.7	10.5	0.9	2.1	**38.53**	7.07	10.32	1.80	**19.18**	0.00	0.00	0.00	**0.00**
28-Oct-24	4.8	3.4	0.0	0.3	0.0	0.5	0.0	**9.05**	3.1	5.6	11.1	2.3	10.2	0.3	1.6	**34.05**	7.21	10.20	1.78	**19.18**	0.00	0.00	0.00	**0.00**
29-Oct-24	6.4	0.6	0.0	0.2	0.0	0.5	0.0	**7.77**	0.7	7.1	13.4	1.8	11.0	0.1	1.1	**35.22**	8.05	11.35	2.00	**21.40**	0.00	0.00	0.00	**0.00**
30-Oct-24	6.4	2.9	0.0	0.2	0.0	0.8	0.0	**10.25**	0.4	5.8	12.5	1.3	10.2	0.1	0.7	**30.97**	6.95	9.42	1.66	**18.03**	0.00	0.00	0.00	**0.00**
31-Oct-24	10.1	2.0	0.0	1.3	0.0	1.2	0.0	**14.60**	0.6	5.1	10.3	1.0	7.5	0.0	0.5	**25.00**	6.71	9.06	1.53	**17.30**	0.00	0.00	0.00	**0.00**
Total	**308.09**	**65.67**	**0.04**	**29.14**	**0.51**	**4.23**	**0.05**	**407.73**	**68.03**	**334.28**	**325.55**	**59.96**	**380.72**	**48.12**	**60.23**	**1276.89**	**104.89**	**173.82**	**32.38**	**311.10**	**18.09**	**17.26**	**2.72**	**38.07**

15.4 Import and Export of SR with ER & WR during October 2024

Date	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)								
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Oct-24	12.59	28.95	49.16	**90.70**	0.00	0.00	0.00	**0.00**	0.00	12.56	38.39	0.00	31.10	1.70	0.00	39.32	**123.08**	7.15	0.00	0.00	22.98	0.00	0.00	0.00	0.00	**30.13**
2-Oct-24	11.55	29.43	43.68	**84.67**	0.00	0.00	0.00	**0.00**	0.00	7.14	31.48	0.00	21.70	2.59	0.00	31.95	**94.86**	7.15	4.05	0.09	28.50	0.00	0.00	0.00	0.04	**39.83**
3-Oct-24	7.54	41.93	42.45	**91.93**	0.00	0.00	0.00	**0.00**	2.74	3.12	27.00	0.00	20.64	2.63	0.00	26.82	**82.96**	4.45	6.75	0.15	31.64	0.00	0.00	0.00	0.00	**43.00**
4-Oct-24	7.37	39.75	41.58	**88.70**	0.00	0.00	0.00	**0.00**	7.34	0.96	22.97	0.00	14.61	2.49	0.00	22.79	**71.16**	0.00	9.85	0.12	32.18	0.00	0.00	0.00	0.03	**42.18**
5-Oct-24	7.37	39.74	42.27	**89.38**	0.00	0.00	0.00	**0.00**	7.33	0.22	20.26	0.00	14.62	2.33	0.00	21.51	**66.27**	0.00	11.93	0.00	30.76	0.00	0.00	0.00	0.00	**42.69**
6-Oct-24	7.37	39.76	44.76	**91.89**	0.00	0.00	0.00	**0.00**	7.32	0.58	22.26	0.00	14.59	2.51	0.00	24.25	**71.52**	0.00	12.37	0.65	31.18	0.00	0.00	0.00	0.04	**44.24**
7-Oct-24	7.37	39.76	45.31	**92.44**	0.00	0.00	0.00	**0.00**	7.35	1.10	20.68	0.00	14.61	2.30	0.00	23.61	**69.65**	0.00	10.78	0.34	30.44	0.00	0.00	0.00	0.03	**41.60**
8-Oct-24	7.37	44.11	41.97	**93.45**	0.00	0.00	0.00	**0.00**	7.35	0.24	16.57	0.00	14.60	1.90	0.00	19.39	**60.06**	0.00	13.38	0.20	31.89	0.00	0.00	0.00	0.00	**45.47**
9-Oct-24	7.36	36.14	46.32	**89.82**	0.00	0.00	0.00	**0.00**	7.34	0.78	22.18	0.00	14.60	2.32	0.00	25.46	**72.67**	0.00	7.41	0.00	30.56	0.00	0.00	0.00	0.00	**37.97**
10-Oct-24	7.34	36.14	45.56	**89.04**	0.00	0.00	0.00	**0.00**	7.37	0.63	21.20	0.00	14.59	2.36	0.00	23.97	**70.11**	0.00	11.90	0.00	31.23	0.00	0.00	0.00	0.00	**43.13**
11-Oct-24	7.31	33.93	42.70	**83.94**	0.00	0.00	0.00	**0.00**	7.37	0.15	18.76	0.00	14.62	2.32	0.00	21.47	**64.69**	0.00	12.33	0.00	29.65	0.00	0.00	0.00	0.00	**41.98**
12-Oct-24	7.37	39.69	35.87	**82.93**	0.00	0.00	0.00	**0.00**	7.38	0.40	16.46	0.00	14.61	2.17	0.00	18.73	**59.75**	0.00	18.39	0.60	30.84	0.00	0.00	0.00	0.25	**50.09**
13-Oct-24	7.37	39.76	36.47	**83.61**	0.00	0.00	0.00	**0.00**	7.38	0.10	16.64	0.00	14.63	2.19	0.00	19.91	**60.85**	0.00	23.67	0.52	33.42	0.00	0.00	0.00	0.18	**57.79**
14-Oct-24	7.37	39.74	44.99	**92.10**	0.00	0.00	0.00	**0.00**	7.36	0.35	26.40	0.00	14.61	2.34	0.00	29.18	**80.23**	0.00	11.55	0.00	29.00	0.00	0.00	0.00	0.00	**40.55**
15-Oct-24	7.37	37.91	39.72	**85.00**	0.00	0.00	0.00	**0.00**	7.37	0.72	21.15	0.00	14.60	2.42	0.00	20.50	**66.76**	0.00	14.04	0.00	29.44	0.00	0.00	0.00	0.00	**43.48**
16-Oct-24	7.36	36.16	35.24	**78.76**	0.00	0.00	0.00	**0.00**	7.38	0.60	13.70	0.00	14.61	2.29	0.00	13.94	**52.51**	0.00	18.60	0.23	31.36	0.00	0.00	0.00	0.24	**50.42**
17-Oct-24	7.38	32.31	33.39	**73.07**	0.00	0.00	0.00	**0.00**	7.38	0.00	8.41	0.00	14.61	2.33	0.00	9.74	**42.48**	0.00	23.94	1.52	34.85	0.00	0.00	0.00	1.29	**61.60**
18-Oct-24	7.37	36.14	36.24	**79.75**	0.00	0.00	0.00	**0.00**	7.37	0.26	10.58	0.00	14.61	2.30	0.00	12.76	**47.88**	0.00	18.23	0.01	31.80	0.00	0.00	0.00	0.00	**50.05**
19-Oct-24	7.24	38.61	35.34	**81.20**	0.00	0.00	0.00	**0.00**	7.38	0.41	12.26	0.00	14.60	2.29	0.00	12.89	**49.84**	0.00	15.73	0.10	30.38	0.00	0.00	0.00	0.02	**46.23**
20-Oct-24	2.68	43.08	29.10	**74.86**	0.00	0.00	0.00	**0.00**	7.39	0.00	7.87	0.00	14.60	2.56	0.00	8.55	**40.97**	0.00	27.05	3.92	34.53	0.00	0.00	0.00	3.70	**69.21**
21-Oct-24	2.67	39.74	39.77	**82.18**	0.00	0.00	0.00	**0.00**	7.27	0.29	16.86	0.00	14.60	2.48	0.00	20.55	**62.07**	0.00	18.56	0.00	31.28	0.00	0.00	0.00	0.00	**49.85**
22-Oct-24	2.67	37.05	40.92	**80.65**	0.00	0.00	0.00	**0.00**	7.28	0.69	17.47	0.00	20.65	2.44	0.00	19.02	**67.55**	0.00	14.71	0.03	29.25	0.00	0.00	0.00	0.01	**44.00**
23-Oct-24	2.67	32.40	41.13	**76.20**	0.00	0.00	0.00	**0.00**	7.38	0.15	16.39	0.00	24.18	2.62	0.00	18.38	**69.11**	0.00	17.04	0.02	32.24	0.00	0.00	0.00	0.00	**49.30**
24-Oct-24	2.69	28.94	47.77	**79.41**	0.00	0.00	0.00	**0.00**	7.37	0.38	19.96	0.00	25.74	2.61	0.00	25.03	**81.09**	0.00	13.49	0.00	30.28	0.00	0.00	0.00	0.00	**43.77**
25-Oct-24	2.67	28.94	46.83	**78.44**	0.00	0.00	0.00	**0.00**	7.38	0.38	18.69	0.00	23.63	2.57	0.00	24.87	**77.53**	0.00	12.50	0.54	30.29	0.00	0.00	0.00	0.05	**43.39**
26-Oct-24	2.74	28.94	46.04	**77.72**	0.00	0.00	0.00	**0.00**	7.37	0.05	15.67	0.00	20.65	2.51	0.00	22.03	**68.28**	0.00	13.35	1.69	33.52	0.00	0.00	0.00	0.82	**49.38**
27-Oct-24	2.74	28.94	46.58	**78.25**	0.00	0.00	0.00	**0.00**	7.38	0.04	18.36	0.00	14.59	2.19	0.00	24.15	**66.72**	0.00	14.20	0.40	31.84	0.00	0.00	0.00	0.06	**46.50**
28-Oct-24	8.96	24.80	43.88	**77.63**	0.00	0.00	0.00	**0.00**	15.84	0.30	13.80	0.00	36.55	2.41	0.00	23.49	**92.38**	0.00	13.60	0.06	32.22	0.00	0.00	0.00	0.00	**45.88**
29-Oct-24	12.57	33.72	46.54	**92.83**	0.00	0.00	0.00	**0.00**	12.16	1.59	19.35	0.00	20.90	2.49	0.00	28.76	**85.24**	0.00	7.24	0.00	29.52	0.00	0.00	0.00	0.00	**36.77**
30-Oct-24	12.57	34.20	48.42	**95.19**	0.00	0.00	0.00	**0.00**	12.15	2.54	24.15	0.00	33.65	2.42	0.00	32.43	**107.34**	0.00	2.36	0.00	26.38	0.00	0.00	0.00	0.00	**28.74**
31-Oct-24	12.57	34.51	37.12	**84.20**	0.00	0.00	0.00	**0.00**	11.76	0.33	15.05	0.00	17.90	1.81	0.00	21.01	**67.86**	0.00	11.22	0.26	24.74	0.00	0.00	0.00	0.00	**36.23**
TOTAL	**217.59**	**1105.23**	**1297.13**	**2619.95**	**0.00**	**0.00**	**0.00**	**0.00**	**231.23**	**37.08**	**590.95**	**0.00**	**574.81**	**72.89**	**0.03**	**686.47**	**2193.47**	**18.75**	**410.23**	**11.46**	**948.20**	**0.00**	**0.00**	**0.02**	**6.77**	**1395.43**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 **से मार्च** 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
अक्तूबर 2024 OCT'24	0.00	918.96	0.00	283.29	695.63	0.00	0.80	0.00
कुल Total	137.84	5200.46	638.42	1917.65	4856.16	0.00	5.69	0.00

* Based on daily operational data

16.1 Import from neighbouring countries during Oct 2024

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Oct-24	16.12	4.16	1.93	0.53	4.49	13.50	1.25	0.73	0.00	0.00	1.34	4.37	0.00	0.00
2-Oct-24	16.05	4.16	1.76	0.47	4.43	13.35	1.20	0.65	0.00	0.00	1.34	5.57	0.00	0.00
3-Oct-24	16.56	4.35	1.69	0.27	4.57	13.74	1.04	0.61	0.00	0.00	1.39	6.65	0.00	0.00
4-Oct-24	16.77	4.48	1.56	0.10	4.63	13.87	0.93	0.41	0.00	0.00	1.44	6.72	0.00	0.00
5-Oct-24	16.90	4.56	1.68	0.16	4.56	13.73	1.05	0.12	0.00	0.00	1.43	7.67	0.00	0.00
6-Oct-24	17.07	4.66	1.68	0.19	4.62	13.92	0.97	0.30	0.00	0.00	1.40	6.71	0.00	0.00
7-Oct-24	17.03	4.64	1.87	0.35	4.56	13.73	0.97	0.30	0.00	0.00	1.43	6.15	0.00	0.00
8-Oct-24	16.74	4.47	1.71	0.40	3.94	11.88	1.05	0.41	0.00	0.00	1.47	5.90	0.00	0.00
9-Oct-24	16.86	4.54	1.52	0.38	4.70	14.15	0.97	0.22	0.00	0.00	1.48	5.32	0.00	0.00
10-Oct-24	16.97	4.61	1.72	0.48	4.17	12.56	1.12	0.50	0.00	0.00	1.51	8.55	0.00	0.00
11-Oct-24	16.01	4.32	1.59	0.31	4.45	13.40	0.89	0.52	0.00	0.00	1.44	8.64	0.00	0.00
12-Oct-24	14.42	3.82	1.37	0.02	3.95	11.90	0.92	0.48	0.00	0.00	1.51	9.03	1.30	0.00
13-Oct-24	13.64	3.55	1.17	0.00	3.56	10.73	0.81	0.30	0.00	0.00	1.49	8.03	2.54	0.00
14-Oct-24	12.15	3.04	1.15	0.00	3.40	10.25	0.83	0.14	0.00	0.00	1.48	7.54	2.48	0.00
15-Oct-24	11.96	2.94	1.26	0.00	3.64	10.99	0.99	0.35	0.00	0.00	1.52	7.11	2.33	0.00
16-Oct-24	11.95	3.07	1.04	0.00	3.34	10.06	0.77	0.45	0.00	0.00	1.53	6.62	2.36	0.00
17-Oct-24	11.54	3.00	0.80	0.00	2.78	8.38	0.92	0.37	0.00	0.00	1.49	5.94	2.40	0.00
18-Oct-24	10.65	2.73	0.55	0.00	3.24	9.77	0.97	0.38	0.00	0.00	1.49	5.85	2.55	0.00
19-Oct-24	9.91	2.44	0.21	0.00	2.88	8.68	0.94	0.34	0.00	0.00	1.47	6.16	2.63	0.00
20-Oct-24	9.81	2.44	0.02	0.00	2.90	8.77	0.89	0.34	0.00	0.00	1.44	5.84	2.47	0.00
21-Oct-24	9.31	2.17	0.00	0.00	2.64	7.98	0.70	0.35	0.00	0.00	1.47	5.80	2.51	0.00
22-Oct-24	8.49	1.79	0.00	0.00	2.34	7.07	1.01	0.41	0.00	0.00	1.40	5.23	2.29	0.00
23-Oct-24	6.62	1.23	0.00	0.00	2.19	6.63	0.82	0.32	0.00	0.00	1.32	4.97	1.78	0.00
24-Oct-24	6.63	2.08	0.00	0.00	2.04	6.15	0.65	0.23	0.00	0.00	1.25	5.04	1.84	0.00
25-Oct-24	7.49	0.89	0.00	0.00	2.04	6.14	0.74	0.23	0.00	0.00	1.37	6.52	1.77	0.00
26-Oct-24	8.66	0.00	0.04	0.00	2.30	6.94	0.92	0.40	0.00	0.00	1.42	7.78	1.88	0.00
27-Oct-24	7.16	0.00	0.00	0.00	1.93	5.81	0.82	0.38	0.00	0.00	1.32	6.00	2.16	0.00
28-Oct-24	6.40	0.00	0.00	0.00	1.74	5.22	0.79	0.34	0.00	0.00	1.29	5.48	1.70	0.00
29-Oct-24	5.85	0.00	0.00	0.00	1.65	4.94	0.75	0.35	0.00	0.00	1.24	5.21	1.89	0.00
30-Oct-24	5.71	0.00	0.00	0.00	1.53	4.59	0.71	0.30	0.00	0.00	1.23	4.60	1.94	0.00
31-Oct-24	5.40	0.00	0.00	0.00	1.49	4.48	0.62	0.26	0.00	0.00	1.38	6.97	1.91	0.00
Total	**366.81**	**84.13**	**26.31**	**3.68**	**100.71**	**303.32**	**28.01**	**11.49**	**0.00**	**0.00**	**43.78**	**197.96**	**42.72**	**0.00**

16.2 Export to neighbouring countries during Oct 2024

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.23	1.48	0.00	0.00	0.00	0.03
2-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.64	1.50	0.00	0.00	0.00	0.03
3-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.43	1.31	0.00	0.00	0.00	0.01
4-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.76	1.17	0.00	0.00	0.00	0.02
5-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.87	0.92	0.00	0.00	0.00	0.03
6-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.95	1.34	0.00	0.00	0.00	0.03
7-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.89	1.40	0.00	0.00	0.00	0.03
8-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.95	1.51	0.00	0.00	0.00	0.03
9-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.56	1.51	0.00	0.00	0.00	0.03
10-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.61	1.53	0.00	0.00	0.00	0.03
11-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.51	1.55	0.00	0.00	0.00	0.03
12-Oct-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.57	1.69	0.00	0.00	0.00	0.03
13-Oct-24	0.00	0.00	0.00	0.16	0.00	0.00	0.00	0.00	21.75	1.74	0.00	0.00	0.00	0.03
14-Oct-24	0.00	0.00	0.00	0.17	0.00	0.00	0.00	0.00	22.02	1.71	0.00	0.00	0.00	0.03
15-Oct-24	0.00	0.00	0.00	0.05	0.00	0.00	0.00	0.00	22.25	1.65	0.00	0.00	0.00	0.05
16-Oct-24	0.00	0.00	0.00	0.47	0.00	0.00	0.00	0.00	21.30	1.71	0.00	0.00	0.00	0.03
17-Oct-24	0.00	0.00	0.00	0.70	0.00	0.00	0.00	0.00	21.96	1.67	0.00	0.00	0.00	0.03
18-Oct-24	0.00	0.00	0.00	0.76	0.00	0.00	0.00	0.00	21.44	1.48	0.00	0.00	0.00	0.02
19-Oct-24	0.00	0.00	0.00	1.04	0.00	0.00	0.00	0.00	12.58	1.96	0.00	0.00	0.00	0.03
20-Oct-24	0.00	0.00	0.00	1.00	0.00	0.00	0.00	0.00	22.40	2.00	0.00	0.00	0.00	0.03
21-Oct-24	0.00	0.00	0.19	1.08	0.00	0.00	0.00	0.00	22.42	1.95	0.00	0.00	0.00	0.03
22-Oct-24	0.00	0.00	0.23	0.86	0.00	0.00	0.00	0.00	22.41	1.75	0.00	0.00	0.00	0.03
23-Oct-24	0.00	0.00	0.17	0.33	0.00	0.00	0.00	0.00	22.12	1.83	0.00	0.00	0.00	0.02
24-Oct-24	0.00	0.00	0.09	0.32	0.00	0.00	0.00	0.00	22.15	1.61	0.00	0.00	0.00	0.03
25-Oct-24	0.00	0.00	0.21	0.46	0.00	0.00	0.00	0.00	20.14	1.37	0.00	0.00	0.00	0.02
26-Oct-24	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	22.20	1.46	0.00	0.00	0.00	0.03
27-Oct-24	0.00	0.00	0.33	0.34	0.00	0.00	0.00	0.00	22.09	1.67	0.00	0.00	0.00	0.03
28-Oct-24	0.00	0.00	0.35	0.24	0.00	0.00	0.00	0.00	22.21	1.66	0.00	0.00	0.00	0.03
29-Oct-24	0.00	0.00	0.34	0.03	0.00	0.00	0.00	0.00	21.86	1.55	0.00	0.00	0.00	0.03
30-Oct-24	0.00	0.00	0.45	0.12	0.00	0.00	0.00	0.00	22.24	1.63	0.00	0.00	0.00	0.03
31-Oct-24	0.00	0.00	0.63	0.31	0.00	0.00	0.00	0.00	22.05	1.77	0.00	0.00	0.00	0.03
Total	**0.00**	**0.00**	**2.99**	**8.68**	**0.00**	**0.00**	**0.00**	**0.00**	**643.58**	**49.06**	**0.00**	**0.00**	**0.00**	**0.85**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – अक्तूबर 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - OCTOBER 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

अक्तूबर 2024 OCTOBER 2024			Apr'24- Oct'24	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	384	686	4976	24207
प.क्षे. WR	431	460	2698	4112
द.क्षे. SR	300	461	2461	8304
पू.क्षे. ER	347	719	2578	11517
पूर्वोत्तर क्षे. NER	49	6	519	465
कुल TOTAL	1511	2332	13232	48605

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
अक्तूबर 2024 Oct'24	12567	8372	1511	2332
कुल TOTAL	68862	60144	13232	48605

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
30.09.24 to 06.10.24	84.95	282.07	50.53	251.02	73.62
07.10.24 to 13.10.24	37.53	291.20	27.51	218.05	61.23
14.10.24 to 20.10.24	42.53	216.15	36.01	147.42	52.21
21.10.24 to 27.10.24	20.68	218.61	29.46	155.46	48.31
28.10.24 to 03.10.24	81.23	210.46	35.96	162.89	64.66

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2024
EXCHANGES THROUGH POWER EXCHANGES-OCTOBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	ACME PHALODI SOLAR ENERGY PRIVATE LIMITED_INFIRM		16.19	0.00
2	ACME RAISAR SOLAR ENERGY PRIVATE LIMITED_INFIRM		2.07	0.00
3	AD HYDRO POWER LIMITED		21.65	0.00
4	ADANI GREEN ENERGY TWENTY FIVE LIMITED_infirm		51.98	0.00
5	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		17.57	0.00
6	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		6.96	0.00
7	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		42.21	0.00
8	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED (infirm)		0.48	0.00
9	Adept Renewable Technologies Private Limited		24.71	0.00
10	Amp Energy Green Six Private Limited		22.89	0.00
11	Amplus Ages Private Limited		2.63	0.00
12	Ayana Renewable Power Three Private Limited Infirm		10.01	0.00
13	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		2.88	0.00
14	Chandigarh (UT)		21.86	7.72
15	Delhi		49.03	442.24
16	Government of Himachal Pradesh _ Chamera1HEP		8.73	0.23
17	Government of Himachal Pradesh _ Chamera3HEP		7.61	0.81
18	Government of Himachal Pradesh_ CHAMERA2HEP		10.24	2.32
19	Government of Himachal Pradesh_BairasuilHEP		3.54	0.27
20	Government of Himachal Pradesh_Koldam HEP		26.66	1.84
21	Government of Himachal Pradesh_NJHPS		63.15	3.79
22	Government of Himachal Pradesh_Parbati3HEP		4.87	0.45
23	Government of Himachal Pradesh_RampurHEP		18.76	1.10
24	Grian Energy Private Limited		6.52	0.00
25	Haryana		148.50	116.20
26	Himachal Pradesh		101.13	72.37
27	IGSTPS JHAJJAR		5.09	0.00
28	JUNIPER GREEN COSMIC PRIVATE LIMITED		13.14	0.00
29	JUNIPER GREEN COSMIC PRIVATE LIMITED_INFIRM		6.07	0.00
30	Jammu Kashmir		38.89	307.75
31	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		47.20	0.00
32	NEA Nepal Upper Chameliya Hydropower Project		27.67	0.00
33	NEA Nepal Upper Kalangagad Hydropower Project new	उत्तरी क्षेत्र NR	14.75	0.00
34	NTPC Dadri Stage I		2.75	0.00
35	NTPC Dadri Stage II		0.87	0.00
36	NTPC Rihand stage I		4.41	0.00
37	NTPC Rihand stage II		4.79	0.00
38	NTPC Rihand stage III		5.23	0.00
39	NTPC Singrauli		14.21	0.00
40	NTPC Tanda Stage II		19.59	0.00
41	NTPC Unchahar Stage I		1.23	0.00
42	NTPC Unchahar Stage II		2.06	0.00
43	NTPC Unchahar Stage III		0.42	0.00
44	NTPC Unchahar Stage IV		3.04	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2024
EXCHANGES THROUGH POWER EXCHANGES-OCTOBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	North Central Railway Prayagraj		0.00	33.51
46	Onevolt Energy Private Limited		6.49	0.00
47	Punjab		33.80	769.66
48	RENEW SURYA PRATAP PRIVATE LIMITED		40.68	0.00
49	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.04	0.00
50	Rajasthan		41.14	434.54
51	ReNew Surya Ravi Private Limited		40.14	0.00
52	SHREE CEMENT LIMITED TPS		29.37	0.00
53	Sainj HEP		14.08	0.18
54	Serentica Renewables India 4 Private Limited		0.39	0.00
55	Serentica Renewables India 5 Private Limited		8.36	0.00
56	Serentica Renewables India 5 Private Limited- Infirm		12.81	0.00
57	Singoli Bhatwari HEP		31.01	0.00
58	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		2.42	0.00
59	TPSL 200MW TPTCL Banderwala		20.24	0.00
60	TPSL Banderwala SECI 100_INF		3.58	0.00
61	TRANSITION SUSTAINABLE ENERGY SERVICES ONE PRIVATE LIMITED-Infirm		2.67	0.00
62	Transition Energy Services Private Limited		16.51	0.00
63	Transition Green Energy Private Limited		23.03	0.00
64	Uttar Pradesh		354.32	602.37
65	Uttarakhand		37.10	270.20
66	2X600 VEDANTA LIMITED Chhattisgarh Power Plant		0.00	0.01
67	ACB (INDIA) LIMITED		46.20	0.33
68	ADANI GREEN ENERGY TWENTY SIX A LIMITED_infirm		0.60	0.00
69	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_Infirm		28.66	0.00
70	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_infirm		31.14	0.00
71	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		163.24	0.00
72	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		26.84	0.00
73	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		3.57	0.00
74	AMBUJA CEMENTS LIMITED(Khavda PSS-3)_infirm		12.43	0.00
75	Adani Green Energy Twenty Five A Limited_Infirm		16.68	0.00
76	Adani Green Energy Twenty Five B Limited_infirm		105.83	0.00
77	Adani Green Energy Twenty Six B Limited_infirm		22.12	0.00
78	Adani Power Limited - Raigarh TPP		161.19	8.07
79	Adani Power Limited-Raipur TPP		265.17	0.00
80	ArcelorMittal Nippon Steel India Limited		0.00	193.32
81	BHARAT ALUMINIUM COMPANY LTD		55.99	0.00
82	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	26.29
83	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		2.01	0.00
84	Chhattisgarh		115.42	300.49
85	D B Power Limited		54.68	0.00
86	DGEN MEGA POWER PROJECT		13.00	0.00
87	DHARIWAL STU OTH		2.30	0.00
88	Daman and Diu - Dadra and Nagar Haveli		0.83	248.45
89	Dhariwal ISTS		3.46	0.00
90	GMR Warora Energy Limited		1.65	0.00
91	Goa WR		3.52	36.43
92	Gujarat		58.11	818.82
93	Jaypee Nigrie Super Thermal Power Plant		106.16	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2024
EXCHANGES THROUGH POWER EXCHANGES-OCTOBER 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
94	Jhabua Power Limited	पश्चिमी क्षेत्र WR	3.83	9.79
95	Jindal Power Limited, Stage-1		123.20	3.74
96	Jindal Power Limited, Stage-2		292.03	12.31
97	Jindal Steel & Power Ltd , DCPP		81.40	1.47
98	MAHAN ENERGEN LIMITED U#1		255.41	0.00
99	MAHAN ENERGEN LIMITED U#2		172.01	0.00
100	MB POWER (MADHYA PRADESH) LIMITED		15.08	3.54
101	Madhya Pradesh		565.16	84.27
102	Maharashtra		48.66	1153.06
103	Maruti Clean Coal and Power Limited		1.99	0.08
104	NREL-Dayapar Wind		4.38	0.00
105	NTPC Gadarwara		7.18	0.00
106	NTPC Jhanor Gandhar GPS		0.00	0.77
107	NTPC Kawas GPS		0.00	0.80
108	NTPC Korba Stage I &II		13.73	0.00
109	NTPC Korba Stage III		4.58	0.00
110	NTPC Lara Stage I		6.02	0.00
111	NTPC Mouda Stage I		1.68	0.00
112	NTPC Mouda Stage II		1.03	0.00
113	NTPC SAIL POWER COMPANY LIMITED		0.04	0.00
114	NTPC Sipat Stage I		23.81	0.00
115	NTPC Sipat Stage II		9.19	0.00
116	NTPC Solapur		2.43	0.00
117	NTPC Vindhyachal Stage I		12.26	0.00
118	NTPC Vindhyachal Stage II		8.80	0.00
119	NTPC Vindhyachal Stage III		11.65	0.00
120	NTPC Vindhyachal Stage IV		12.14	0.00
121	NTPC Vindhyachal Stage V		5.26	0.00
122	NTPC khargone		6.92	0.00
123	Nani Virani Wind Energy Private Limited		1.60	0.00
124	R.K.M POWERGEN PRIVATE LIMITED		6.40	0.00
125	Ratnagiri Gas & Power Private Limited		0.04	1.99
126	SKS Power Generation Chhattisgarh Limited		44.42	23.20
127	Sasan Power Limited		5.15	0.00
128	TRN ENERGY PRIVATE LIMITED		16.30	0.00
129	The Tata Power Co Ltd (MTPS)		7.43	0.00
130	WIND FIVE RENERGY LIMITED		4.62	0.00
131	Andhra Pradesh		108.11	250.67
132	COASTAL ENERGEN PRIVATE LIMITED		0.64	0.00
133	Goa SR		0.04	15.96
134	IL&FS TAMIL NADU POWER COMPANY LIMITED		6.85	0.00
135	JINDAL POWER LIMITED SIMHAPURI		29.75	0.49
136	JSW RENEW ENERGY LIMITED INFIRM		4.03	0.00
137	Karnataka		320.66	73.87
138	Kerala		8.38	72.03
139	MEENAKSHI ENERGY LIMITED		25.06	3.85
140	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		12.19	0.00
141	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		6.91	0.00
142	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		1.77	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2024 EXCHANGES THROUGH POWER EXCHANGES-OCTOBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
143	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I	दक्षिणी क्षेत्र SR	4.31	0.00
144	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		5.69	0.00
145	NLC Tamilnadu Power Limited		9.80	0.00
146	NTECL VALLUR		0.25	0.00
147	NTPC KUDGI		4.90	0.00
148	NTPC Ramagundam Stage I &II		2.73	0.00
149	NTPC Ramagundam Stage III		0.94	0.00
150	NTPC Simhadri Stage I		0.86	0.00
151	NTPC Simhadri Stage II		6.50	0.00
152	NTPC Talcher Super Thermal Power Station Stage II		38.96	0.00
153	NTPC Telangana		5.75	0.00
154	OSTRO KANNADA POWER PRIVATE LIMITED		5.42	0.00
155	Pondicherry UT		16.95	0.23
156	RENEW SURYA OJAS PRIVATE LIMITED-Wind		32.44	0.00
157	RENEW SURYA OJAS PRIVATE LIMITED_INFIRM		0.55	0.00
158	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		0.65	0.00
159	Ramagundam Floating solar		4.85	0.00
160	SEIL ENERGY INDIA LIMITED		107.36	0.00
161	SEIL Energy India Limited Project II		24.41	0.00
162	SEMBCORP GREEN INFRA PRIVATE LIMITED (INFIRM)		4.78	0.00
163	Serentica Renewables India 1 Private Limited		1.68	0.00
164	Simhadri FSP 15 MW		1.51	0.00
165	Simhadri Floating solar (10 MW)		0.93	0.00
166	Tamil Nadu		224.48	400.48
167	Telangana		156.23	734.20
168	VENA ENERGY VIDYUTH PRIVATE LIMITED_INFIRM		11.17	0.00
169	VENA ENERGY VIDYUTH PRIVATE LIMITED_SOLAR_INFIRM		5.10	0.00
170	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	3.48	0.00
171	Basochhu Hydropower Plant Bhutan		36.07	0.00
172	Bihar		356.76	9.21
173	Chuzachen HEP		0.65	0.00
174	DEVIGHAT NEPAL ELECTRICITY AUTHORITY		0.03	0.00
175	Damodar Valley Corporation		19.32	193.66
176	GMR KAMALANGA ENERGY LTD-CTU		1.61	0.00
177	IND BARATH ENERGY UTKAL LIMITED		49.27	0.00
178	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.42	0.00
179	Jharkhand		73.78	56.64
180	Jindal India Power Limited		198.05	0.00
181	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		60.11	0.00
182	KANTI BIJLEE UTPADAN NIGAM LIMITED		25.83	0.00
183	LIKHU-iV NEA		0.57	0.00
184	Lower Modi Hydro Power Project NEPAL ELECTRICITY AUTHORITY		0.04	0.00
185	MAITHON POWER LIMITED		6.53	0.00
186	MARSYANGDI NEPAL ELECTRICITY AUTHORITY		4.38	0.00
187	NABINAGAR POWER GENERATING COMPANY LIMITED		56.51	0.00
188	NEA Nepal Upper Balephi A Hydropower Project1		0.11	0.00
189	NEA Nepal Upper Dordi A Hydropower Project		0.02	0.00
190	NEPAL ELECTRICITY AUTHORITY-MIDDLE MARSYANGDI		9.59	0.00
191	NTPC BARH Stage I		6.98	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2024 EXCHANGES THROUGH POWER EXCHANGES-OCTOBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
192	NTPC BARH Stage II		22.17	0.00
193	NTPC Darlipali		4.73	0.00
194	NTPC Farakka stage I		68.47	0.00
195	NTPC Farakka stage III		13.82	0.00
196	NTPC Kahalgaon stage I		11.66	0.00
197	NTPC Kahalgaon stage II		23.82	0.00
198	NTPC North Karanpura STPS		19.88	0.00
199	NTPC Talcher Stage I		31.25	0.00
200	NTPP BRBCL		9.78	0.00
201	Nikachhu Hydropower Project		14.73	0.00
202	Odisha		489.30	141.32
203	Sikkim		31.30	0.12
204	Solu Hydropower Project NEPAL ELECTRICITY AUTHORITY		0.07	0.00
205	Tashiding HEP, Shiga Energy Private Limited		0.44	0.00
206	West Bengal		131.78	330.35
207	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	0.31	0.00
208	ASSAM GAS BASED POWER STATION		1.09	0.00
209	Arunachal Pradesh		64.74	0.00
210	Assam		331.23	60.29
211	Bongaigaon Thermal Power Station NTPC		9.30	0.00
212	KAMENG HYDRO POWER STATION		121.28	0.00
213	Manipur		32.30	1.51
214	Meghalaya		61.24	12.83
215	Mizoram		19.98	0.00
216	Nagaland		14.51	0.00
217	Palatana Plant		23.19	0.00
218	Tripura		7.71	20.38
	Total		8373	8373

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : OCTOBER 2024

RE Source & Unit wise break up (01.10.2024-31.10.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	0	0	0	0
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1	1	2	3
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1**	**1**	**2**	**3**

RECs Issued (01.10.2024-31.10.2024)

Sr.No.	Non Solar	Solar	Total
1	1306374	93964	1400338

Redemption of REC (01.10.2024-31.10.2024)

Sr.No.	Non Solar	Solar	Total
1	767183	52618	819801

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : OCTOBER 2024

RE Source & Unit wise break up (Apr'24-Oct'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	21	1	0	0
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1	1	2	3
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**22**	**2**	**2**	**3**

RECs Issued (Apr'24-Oct'24)

Sr.No.	Non Solar	Solar	Total
1	1306374	93964	1400338

Redemption of REC (Apr'24-Oct'24)

Sr.No.	Non Solar	Solar	Total
1	767183	52618	819801

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : OCTOBER 2024

RE Source & Unit wise break up Since Inception to Oct'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3173	535	2997	536
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	1733	592	1563	498
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**7016**	**1301**	**6217**	**1171**

RECs Issued since Inception to Oct'24

Sr.No.	Non Solar	Solar	Total
1	144050875	14144038	158194913

Redemption of REC since Inception to Oct'24

Sr.No.	Non Solar	Solar	Total
1	93738584	12670814	106409398

REC Closing balance as on 31.10.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of Oct 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Rajasthan	05-10-2024 11:50	05-10-2024 22:25	10:35	310	0	0.488	0.000	63574	70955	i) Generation of 220/33KV RSRPL FTG3 station evacuates through 220 KV Fatehgarh III(PG)- RSRPL_Hyb_FTHG3_PG (RENEW SURYA ROSHNI PRIVATE LIMITED) Ckt. During antecedent condition, RSRPL FTG3 station station was generating approx. 310MW (as per PMU). ii) As reported, at 11:51hrs, 220 KV Fatehgarh III(PG)- RSRPL_Hyb_FTHG3_PG (RENEW SURYA ROSHNI PRIVATE LIMITED) Ckt. was hand tripped due to spark observed in B-Phase line isolator. iii) Due to tripping of 220 KV Fatehgarh III(PG)- RSRPL_Hyb_FTHG3_PG (RENEW SURYA ROSHNI PRIVATE LIMITED) Ckt, both ICT-I & II of 220/33KV also tripped along with 220KV Bus – I and Bus-II. iv) As per PMU, solar generation loss of approx. 312 MW is observed at 220KV RSRPL S/S. v) As per SCADA, during this event, dip in solar generation of approx. 326 MW is observed in NR control area. vi) Due to dip in RE generation, frequency dropped by 0.039 Hz (from 50.036 Hz to 49.997 Hz). vii) As per SCADA, no change in demand is observed in Rajasthan control area.	1) 220 KV Fatehgarh III(PG)- RSRPL_Hyb_FTHG3_PG (RENEW SURYA ROSHNI PRIVATE LIMITED) Ckt
2	GD-1	Uttarakhand	05-10-2024 18:23	05-10-2024 19:06	00:43	70	0	0.106	0.000	53633	65902	i) During antecedent condition, only 70 MW Unit-4 at Dhauliganga(NH) was running and generating approx. 69MW (as reported, SCADA data not available). Unit-1, 2 & 3 were under shutdown. ii) As reported, at 18:24hrs, 220 KV Jauljivi (PG)-Dhauliganga(NH) (PG) Ckt-1 & 2 tripped due to malfunction of GIS controller software. iii) Along with the same, 70 MW Unit-4 at Dhauliganga(NH) also tripped due to loss of evacuation path. Hence 220kV Dhauliganga(NH) S/s became dead. iv) As per PMU at 400kV Bareilly(PG), no fault signature was observed. v) As per SCADA, no change in NR hydro generation is observed. vi) As reported by Dhauliganga, Generation loss of 69MW was reported at Dhauliganga(NH).	1) 220 KV Jauljivi (PG)-Dhauliganga(NH) (PG) Ckt-1 2) 220 KV Jauljivi (PG)-Dhauliganga(NH) (PG) Ckt-2 3) 70 MW Unit-4 at Dhauliganga(NH)
3	GI-2	Uttar Pradesh	09-10-2024 11:39	09-10-2024 12:22	00:43	0	0	0.000	0.000	9381	68876	i) 400/220 KV Obra -B substation has 2*315 MVA (ICT-1&2) and one 240MVA ICT (ICT-3). During antecedent condition, 2*315 MVA & 240 MVA ICTs were carrying 104MW (ICT1), 101MW (ICT2) and 78MW (ICT3) respectively. ii) 400/220kV 315 MVA ICT-1, 240 MVA ICT-3 at Obra_B, 220kV Obra_A-Allahabad Rewa Road ckt-2 & 220kV Obra_A-Sahupuri ckt were all connected to 220KV Bus-1 during the antecedent condition. iii) As reported at 11:39 hrs, R-Y fault occurred on 220kV Obra-Sahupuri ckt. Fault location was 5km from Sahupuri end. Fault was in Z-1 from Obra end and Z-2 from Sahupuri end. iv) On this fault, distance protection at both ends operated. CB opened from Sahupuri end however, CB at Obra end failed to open. v) As reported, LBB protection didn't operate (relay is of static type) and fault cleared with the tripping of 220kV Obra_A-Allahabad Rewa Road ckt-2 on Z-4 distance protection operation and 400/220kV 315 MVA ICT-1, 240 MVA ICT-3 on directional O/C E/F protection operation. 220kV bus coupler CB also opened on over current protection and 220kV Bus-2 got isolated. vi) After tripping ICT-1 & 3 all the load shifted to ICT-2 and the loading of ICT-2 increased to 240 MW. vii) As per PMU at Anpara(UP), R-Y fault with delayed clearance of ~960msec is observed. viii) Both the transformers were restored back into service at 12:22 hrs (ICT-1) and 14:41 hrs (ICT-3) respectively. ix) As per SCADA, no generation or load loss was observed in UP control area. x) As per SCADA, no change in demand is observed in the Northern Region.	1) 220kV Obra_A-Sahupuri ckt 2) 220kV Obra_A-Rewa Road ckt-2 3) 400/220kV 315 MVA ICT 1 at Obra_B(UP) 4) 400/220kV 240 MVA ICT 3 at Obra_B(UP)
4	GI-2	Uttar Pradesh	09-10-2024 17:04	09-10-2024 17:43	00:39	215	100	0.352	0.164	13090	61049	i) Obra-A has 3, 220/132 KV, 100MVA transformers which were carrying approx. 46MW, 51MW and 45MW during antecedent condition. ii) As reported, during inclement weather conditions, 220/132kV 100 MVA ICT-1 & ICT-2 tripped on B-N earth fault protection at Obra-A(UP) which led to complete shifting of load on 220/132kV 100 MVA ICT-3 at Obra-A (UP). iii) As a result of overloading of the 3rd transformer, ICT-3 also tripped on O/C protection at 17:04hrs. iv) At the same time 17:04hrs, 03 Units at Obra Hydro and 03 Units at Rihand HEP (connected at Bus-2) also tripped leading to a total generation loss of approx. 215 MW. v) Considering the above incident, Rihand manually tripped Obra-A, Obra H1, Obra H2 and Gharwad lines from perspective of safety. vi) As per SCADA, change in demand of approx. 100MW is observed in UP control area.	1) 33 MW Unit-1 at Obra HEP (UP) 2) 33 MW Unit-2 at Obra HEP (UP) 3) 33 MW Unit-3 at Obra HEP (UP) 4) 50 MW Unit-1 at Rihand HEP (UP) 5) 50 MW Unit-2 at Rihand HEP (UP) 6) 50 MW Unit-4 at Rihand HEP (UP) 7) 220/132kV 100 MVA ICT-1 at Obra-A (UP) 8) 220/132kV 100 MVA ICT-2 at Obra-A (UP) 9) 220/132kV 100 MVA ICT-3 at Obra-A (UP)
5	GI-2	Uttarakhand	10-10-2024 10:56	10-10-2024 11:17	00:21	0	247	0.000	0.366	9411	67486	i) 400/220/132kV Kashipur has 2*315 400/220kV and 2*160MVA 220/132kV ICTs. ii) As reported, at 10:56:13.086, LV side CB of 315MVA ICT-2 tripped. Uttarakhand-SLDC in its tripping report mentioned the reason for the fault was operation of Restricted Earth Fault (REF) as well as some external fault, which is of contradictory nature. REF is an internal fault of the transformer. Further clarification may be given by Uttarakhand -SLDC on this matter. iii) With the tripping of 315MVA ICT-1 at Kashipur, case-2 of SPS for transformers at 400KV Kashipur (PTCUL) substation operated. As a result of the SPS present in Kashipur sub-station, the following lines also tripped. i. 220kV Jafarpur-Kashipur (UK) Ckt ii. 220kV Pantnagar – Kashipur (UK) Ckt iii. 132kV Kahipur – Jaspur (UK) Ckt iv) Even after tripping of the aforementioned lines, loading of 315MVA ICT-1 didn't reduce and increase to ~339MVA. As reported, load of 220kV Kamalwaganja was being fed from 220kV Pantnagar and 132kV Bajpur. After tripping of 220kV Kashipur-Pantnagar ckt, load of Kamalwaganja which was feeding through Kashipur-Pantnagar shifted to Bajpur source. Due to this, loading of 315MVA ICT-3 didn't reduce after SPS operation. v) Further, at 10:56:24.522,315MVA ICT-1 HV and LV Side tripped on Over Current Protection. However, from the DR of ICT-1, loading of ICT-1 before tripping was ~107%. vi) Further, 220/132kV 160 MVA ICT-3 also tripped at Kashipur. As reported, no flag was observed for the said tripping. vii) As per PMU at Roorkee(PG), no fault in system is observed. viii) As per SCADA, a change in demand of approx. 247MW is observed in Uttarakhand control area.	1) 400/220kV 315 MVA ICT-1 at Kashipur(UK) 2) 400/220kV 315 MVA ICT-2 at Kashipur(UK) 3) 220/132kV 160 MVA ICT-3 at Kashipur(UK) 4) 220kV Jafarpur-Kashipur (UK) Ckt 5) 220kV Pantnagar – Kashipur (UK) Ckt 6) 132kV Kahipur – Jaspur (UK) Ckt
6	GI-1	Jammu & Kashmir	11-10-2024 10:03	11-10-2024 11:09	01:06	0	175	0.000	0.269	9322	65076	i) 220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. 220kV Amargarh-Ziankote ckt-1&2 are on the same tower (D/C tower) and line length is ~21.4km. ii) During antecedent condition, 220kV Amargarh(INDIGRID) –Ziankote(JK) D/C was carrying 114 MW each and feeding Ziankote load. iii) As reported, at 10:03 hrs, 220 KV Amargarh(INDIGRID)-Ziankote(JK) (PDD JK) D/C tripped from both ends on Y-B phase to phase fault. During patrolling it was found that the fault had occurred between Tower no. 76 and 77, as some locals were cutting trees in the vicinity of line and branches of tree had fallen on the line. iv) As per PMU at Amargarh(PG), B-N phase to earth fault which cleared within 80 msec is observed. v) As per SCADA, change in demand of approx. 175MW is observed in J&K control area.	1) 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 2) 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2

Details of Grid Events during the Month of Oct 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GI-1	Jammu & Kashmir	16-10-2024 13:45	16-10-2024 13:49	00:04	0	350	0.000	0.605	46640	57853	i)220/132kV Pampore(PDD) has single main and transfer Bus arrangement at 220kV side. ii)During antecedent condition, power flow from Wagoora(PG) S/s to Pampore(PDD) S/s was approx. 140 MW (70 MW each) through 220 KV Wagoora(PG)-Pampore(PDD) (PG) D/C. iii)As reported, at 13:45 hrs, Y-phase disc ruptured in 220kV main Bus at Pampore. iv)Due to this, 220kV Wagoora(PG)-Pampore(PDD) (PG) Ckt-1 tripped from Pampore end on Y-N phase to earth fault (exact location of fault and nature of protection operated yet to be shared). v)During the same time, 220kV Wagoora(PG)-Pampore(PDD) (PG) Ckt-2 also tripped from Wagoora end sensing the fault in zone-2 with fault distance of 11.91km from Wagoora end. vi)As per PMU at Amargarh(INDIGRID), Y-N phase to earth fault converted to Y-B-N double phase to earth fault with delayed fault clearing time of 1000ms is observed. vii)As per SCADA, change in demand of approx. 350 MW is observed in J&K control area.	1) 220 KV Wagoora(PG)-Pampore(PDD) (PG) Ckt-1 2) 220 KV Wagoora(PG)-Pampore(PDD) (PG) Ckt-2
8	GI-2	Uttar Pradesh	17-10-2024 00:43	17-10-2024 02:48	02:05	0	0	0.000	0.000	39096	53675	i)400/220/132kV Muradnagar-New(UP) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii)As reported, at 00:43 hrs, 400kV Muradnagar_2-Mathura (UP) Ckt tripped on Y-N phase to earth fault with fault current of 4.065kA from Muradnagar_2 end and fault clearing time of 291 ms; zone-1 distance protection operated (as per DR at Muradnagar_2 end) and DT received at Mathura end (as reported). iii)Due to delayed opening of CB at Muradnagar_2 end of 400kV Muradnagar_2-Mathura (UP) Ckt, LBB protection operated and both main and tie CBs at Muradnagar_2 end of 400 KV Dadri(NT)-Muradnagar_2(UP) (PG) Ckt and 400kV Muradnagar_2-Simbholi_PMSTL (UP) Ckt-1 & 2 opened and all the 400kV lines connected at Muradnagar_2 tripped. DT received at remote ends (as reported). iv)As informed by SLDC-UP, the logic of LBB operation was wrong in 400kV Muradnagar_2-Simbholi_PMSTL (UP) Ckt-1 & 2: on LBB operation opening command was sent to both main and tie CBs. Reason of opening of tie CB of 400 KV Dadri(NT)-Muradnagar_2(UP) (PG) Ckt is under investigation and yet to be shared. v)As per PMU at Muradnagar1(UP), Y-N phase to earth fault with delayed fault clearing time of 280ms is observed. vi)As per SCADA, no change in demand is observed in UP control area.	1) 400kV Muradnagar_2-Mathura (UP) Ckt 2) 400kV Muradnagar_2-Simbholi_PMSTL (UP) Ckt-1 3) 400kV Muradnagar_2-Simbholi_PMSTL (UP) Ckt-2 4) 400 KV Dadri(NT)-Muradnagar_2(UP) (PG) Ckt
9	GD-1	Rajasthan	21-10-2024 15:32	21-10-2024 16:08	00:36	0	170	0.000	0.285	47795	59608	i)220/132kV Dausa(RS) has double main and transfer bus scheme at 220kV level. ii) During antecedent condition, 220 kV Alwar(RS)-Dausa(RS) Ckt was not in service. iii)As reported, at 15:32 hrs, R-phase CVT of Main-Bus-I flashover occurred due to reptile climbing on structure at Dausa end and bus fault created. Bus bar protection at Dusa(RS) was not operational during the event and due to delay in opening of bus coupler (bus coupler opening delay setting was 110ms), fault was also sensed by Main Bus-II. iv)Due to this bus fault, all the 220kV lines connected to Bus-I & II at Dausa(RS) sensed the fault in zone-4 and fault cleared from Dausa(RS) end in zone-4 (zone-4 delay setting was 160ms). But in 220 KV Lalsote(RS)-Dausa(RS) (PG) Ckt and 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-2, CB didn't open from Dausa(RS) end and finally fault cleared in zone-2 from remote end. v) During the same time, 220/132kV 160MVA ICT-1 and 100MVA ICT-2 at Dausa(RS) also tripped on over-current protection operation (exact reason yet to be shared). vi) As all the elements connected to both the 220kV buses tripped and there was no source of supply at 132kV level, complete blackout occurred at 220/132kV Dausa(RS) S/s. vii)As per DR at Lalsote end of 220 KV Lalsote(RS)-Dausa(RS) (PG) Ckt, R-N phase to earth fault occurred with fault current of 1.729kA from Lalsote end and fault sensed in zone-2 at Lalsote end. viii)As per PMU at Bassi(PG), R-N phase to earth fault converted to R-B-N double phase to earth fault with delayed fault clearing time of 560ms is observed. ix)As per SCADA, change in demand of approx. 170 MW is observed in Rajasthan control area.	1) 220 KV Lalsote(RS)-Dausa(RS) (PG) Ckt 2) 220 KV Sawaimadhopur(RS)-Dausa(RS) (PG) Ckt 3) 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-1 4) 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-2 5) 220 KV Mandawar(RS)-Dausa(RS) Ckt 6) 220 KV Sikrai(RS)-Dausa(RS) Ckt 7) 220/132kV 160MVA ICT-1 at Dausa(RS) 8) 220/132kV 100MVA ICT-2 at Dausa(RS)
10	GI-1	Himachal Pradesh	21-10-2024 09:42	21-10-2024 09:52	00:10	0	215	0.000	0.354	48257	60747	i)During antecedent condition, 220/132kV 100MVA ICT-1 & 2 at Giri(HP) were carrying approx. 108 MVA each. ii)As reported, at 09:42 hrs, 220/132kV 100MVA ICT-1 & 2 at Giri(HP) tripped on over-loading (exact reason of over-loading of ICTs yet to be shared). iii)As per SCADA, MVA loading of both the ICTs were approx. 86 MVA each at 09:33hrs. Suddenly within one minute loading increased to approx. 106 MVA each and it gradually increased further to approx. 108 MVA each within another 8 minutes and finally at 09:42 hrs, both the ICTs tripped on over-loading. iv)Since these ICTs were the only source of power at 132kV level, their tripping resulted in tripping of all the feeders connected at 132kV level. v)As per PMU at Shahranpur(PG), no fault is observed in the system. vi)As per SCADA, change in demand of approx. 215 MW is observed in HP control area.	1) 220/132kV 100MVA ICT-1 at Giri(HP) 2) 220/132kV 100MVA ICT-2 at Giri(HP)
11	GI-2	Uttar Pradesh	23-10-2024 12:08	23-10-2024 12:52	00:44	0	0	0.000	0.000	52196	60961	i)400/220kV Aligarh(UP) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii)As reported, at 12:08 hrs, differential protection of line reactor of 400 KV Panki-Aligarh (UP) Ckt operated (exact reason of differential protection operation of line reactor of 400 KV Panki-Aligarh (UP) Ckt yet to be shared). iii)During the same time, Bus bar protection operated at 400kV Bus-1 at Aligarh(UP) also operated (exact reason of bus bar operation of 400kV Bus-1 at Aligarh(UP) yet to be shared). iv)Due to this, all the elements connected to 400kV Bus-1 at Aligarh(UP) tripped and Bus-1 became dead (exact reason of opening of tie CBs of 400 KV lines connected to Bus-1 at Aligarh(UP) yet to be shared). v)As per PMU at Aligarh(PG), no fault is observed in the system. vi)As per SCADA, no change in demand is observed in UP control area.	1) 400KV Bus 1 at Aligarh(UP) 2) 400 KV Panki-Aligarh (UP) Ckt 3) 400 KV Aligarh-Sikandrabad (UP) Ckt 4) 400 KV Aligarh-Mainpuri (UP) Ckt-1 5) 400 KV Aligarh-Shamli (UP) Ckt-2
12	GI-2	Uttar Pradesh	25-10-2024 12:52	25-10-2024 14:06	01:14	150	0	0.254	0.000	49979	59077	i)400/220kV Obra-B(UP) has double main and transfer bus scheme at both 400kV and 220kV level. ii)During antecedent condition, 200 MW Obra TPS - UNIT 11 and 13 were generating approx. 48 MW and 102 MW respectively. 200 MW Obra TPS - UNIT 09 was under tripped condition since 09:57 hrs on 25th Oct'24. 400/220 kV 315 MVA ICT 1 at Obra_B(UP), 400 KV Obra_B-Rewa Road (UP) Ckt-1 and 200 MW Obra TPS - UNIT 09, 11 & 13 were connected to 400KV Bus 1 at Obra-B(UP) and rest of the elements were connected to 400KV Bus 2 at Obra-B(UP). iii)As reported, at 12:52 hrs, while synchronizing 200 MW Obra TPS - UNIT 09, busbar differential protection operated at 400KV Bus 1 at Obra-B(UP) (exact reason of busbar protection operation yet to be shared). iv)Due to busbar protection operation, all the elements connected to 400kV Bus-1 at Obra-B(UP) tripped and Bus-1 became dead. v)As per PMU at Anpara-TH(UP), B-N phase to earth fault is observed with fault clearing time of 120 ms. vi)As per SCADA, no change in demand is observed in UP control area. However, generation loss of approx. 150 MW occurred at Obra-B(UP). vii)As reported by Obra-B, after investigation it was found that interrupter unit of CB at 400kV side of 200 MW Obra TPS - UNIT 09 was damaged. This CGL make SF6 type CB which was commissioned on 30th Nov'23 and was continuously in service since 16th Feb'24, is under warranty period. CGL service engineer was called for detailed analysis regarding the same as primarily it seems that there is some manufacturing defect of CB.	1) 400KV Bus 1 at Obra-B(UP) 2) 400/220 kV 315 MVA ICT 1 at Obra_B(UP) 3) 400 KV Obra_B-Rewa Road (UP) Ckt-1 4) 200 MW Obra TPS - UNIT 09 5) 200 MW Obra TPS - UNIT 11 6) 200 MW Obra TPS - UNIT 13
13	GD-1	Rajasthan	30-10-2024 14:15	30-10-2024 16:33	02:18	0	500	0.000	0.818	53878	61088	i)400/220kV Alwar400(RS) has one and half-breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt is the only 400kV line connected to Alwar400(RS). The active power coming from Hindaun(RS) goes to Alwar(RS), Alwar MIA(RS), Mandawar(RS) and Dausa(RS) through two 400/220kV ICTs at Alwar400(RS). ii)During antecedent condition, 220kV Alwar400-Dausa(RS) Ckt was on no-load. 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt was carrying 356 MW. iii)As reported, at 14:15 hrs, 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt tripped on R-Y-N double phase to earth fault with fault current of 5.759kA and 5.272kA in R and Y phase respectively from Hindaun(RS) end; fault sensed in zone-1 at Hindaun(RS) end (exact reason and location of fault yet to be shared). iv)As 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt is the only source of power at Alwar400(RS), with the tripping of this line there was no source of power left to any of the 220kV feeders. Hence complete blackout occurred at 400/220kV Alwar400(RS). v)As per SCADA SOE, 220kV Alwar-Kukas(RS) Ckt also tripped during the same time (exact reason of the same yet to be shared). vi)As per PMU at Bassi(PG), R-N phase to earth fault is observed with fault clearing time of 80 ms. vii)As per SCADA, change in demand of approx. 500 MW is observed in Rajasthan control area.	1) 400 KV Alwar(ATIL)-Hindaun(RS) (ATIL) Ckt

Details of Grid Events during the Month of Oct 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	01-10-2024 02:45	01-10-2024 06:41	03:56	63	-	0.09%	-	67761	53125	At 02:45 Hrs / 01-10-2024, 220 kV Bhuj-Baranda tripped on B-E fault, Autorecloser not attempted at Baranda end, line tripped at Bhuj end after autorecloser attempt. During patrolling Lunger thrown by villagers found at tower location 233. Generation loss of 63 MW occured at Baranda (Avikiran) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Baranda
2	GI-1	WR	01-10-2024 16:40	01-10-2024 17:05	00:25	77	14	0.11%	0.02%	73249	60985	At 16:40 Hrs / 01-10-2024, LBB protection maloperated of 220 kV Uran-Bus-1 resulting in tripping of all connected elements (as mentioned in elements tripped column). Generation loss of 77 MW and load loss of 14 MW occurred at Uran substation due to the event.	Tripping of following Elements: 1. 220 kV Uran Bus-1 2. Uran U-7 (108 MW) 3. 220 kV Uran-Apta-2 4. 220 kV Uran-Apta-4 5. 220 kV Uran-Ulwe-2 6. 220 kV Uran-ONGC 7. 220/33 kV Uran-ICT-1 (50 MVA)
3	GI-1	WR	07-10-2024 09:29	07-10-2024 13:40	04:11	-	-	-	-	68810	62753	At 09:29 Hrs / 07-10-2024, Bus bar protection operated in 220 kV Haldarwa-Bus-2 (Double Main Bus scheme) due to broken jumper over Y phase Bus side isolator of 220 kV GPEC-Haldarwa-1, resulting in of tripping of all the connected elements (as mentioned in elements tripped column). No Generation loss or load loss of occurred to the event.	Tripping of following Elements: 1. 220 kV Gandhar-Haldarwa 2 2. 220 kV Haldarwa-Kawas-2 3. 220 kV Haldarwa-Kakrapar(1&2)-2 4. 220 kV Dahej-Haldarwa-1 5. 220 kV GPEC-Haldarwa-1 6. 220 kV Jambuva-Haldarwa-1 7. 220 kV Suva-Haldarwa 8. 220 kV Haldarwa-Bus-2 9. 220/66 kV Haldarwa ICT-2&3
4	GI-1	WR	08-10-2024 23:37	09-10-2024 04:42	05:05	-	444	-	0.72%	74260	61651	At 23:37 Hrs / 08-10-2024, 220/66 kV Khadoli-ICT-2 tripped due to bursting of 66 kV side Y phase CT causing damage to R and Y phase circuit brakers. After 80 msec, 220/66 kV Khadoli-ICT-1&3 tripped on Earth Fault protection operation. Due to the above trippings of ICTs flow on 220 kV lines connected to Khadoli became zero due to load loss of 444 MW in DNHDD network.	Tripping of following Elements: 1. 220/66 kV Khadoli-ICT-2 2. 220/66 kV Khadoli ICT-1 3. 220/66 kV Khadoli ICT-3
5	GD-1	WR	10-10-2024 15:24	11-10-2024 17:30	26:06	96	-	0.14%	-	71006	64759	At 15:24 Hrs / 10-10-2024, 220kV Nakhtrana-Dedhiya tripped on R-E fault from Nakhatrana end only, Auto recloser successful at Dedhiya end. It is seen from DR at Nakhatrana end that all three phases tripped for a fault in single phase which is a maloperation. During patrolling it was found that R phase conductor fell from suspension insulator clamp at tower location 55. Generation loss of 96 MW occurred at Nakatrana & Dedhiya wind power plant (Adani) due to the event.	Tripping of following Elements: 1. 220kV Nakhtrana-Dedhiya
6	GD-1	WR	11-10-2024 13:04	11-10-2024 15:32	02:28	98	-	0.15%	-	65386	60886	At 13:05 Hrs / 11-10-2024, 220 kV Bhawsingpura- Khandwa tripped on Y-E fault on Z-3 protection operation. The tripping was not in order because instantaneous trip issued at Bhawsingpura end for a fault in Zone-3 in 400 kV Khandwa-Dhule-1 at the same time. 220 kV Bhawsingpura- Kanwani line also tripped after 200 msec without any relay indication. Generation loss of 98 MW occurred at Bhawsingpura and Kanwani solar power plant (Masaya Solar) due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhawsingpura-Kanwani-1 2. 220 kV Bhawsingpura-Khandwa-1 3. 220/33 kV Kanwani-ICT-1

Details of Grid Events during the Month of Oct 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD-1	WR	14-10-2024 16:43	14-10-2024 19:39	02:56	38	-	0.06%	-	68840	61457	At 16:43 Hrs / 14-10-2024, 220 kV Nakhatrana-Dedhiya ckt tripped on B Ph-E fault. As seen from DR at Nakhatrana end all 3-phases tripped due to tripping command from main-2 relay, fault was seen in zone-2. As seen from DR at Dhediya end even though fault was seen in zone-3, carrier was sent to Nakhatrana end which is not in order. During patrolling no abnormilites were found. Generation loss of 38 MW occurred at Nakatrana & Dedhiya wind power plant (Adani) due to the event.	Tripping of following Elements: 1 220 kV Nakhatrana-Dedhiya line 2 220kV Dedhiya SS Bus-1 3 220kV Dedhiya SS Bus-2 4 220/33kV Dedhiya ICT-1 5 220/33kV Dedhiya ICT-2
8	GD-1	WR	14-10-2024 22:20	14-10-2024 23:58	01:38	140	-	0.21%	-	65928	54858	At 22:20 Hrs / 14-10-2024, 220 kV Bachau-Ostro-1&2 tripped on R-E fault. It is seen from Disturbance recorders at Ostro end that all three phases tripped for a fault in single phase which is a maloperation. During patrolling no abnormalites were found. Generation loss of 140 MW occurred at Ostro (Renew Power) Wind power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bachau-Ostro-1 2. 220 kV Bachau-Ostro-2
9	GD-1	WR	15-10-2024 00:29	18-10-2024 21:51	93:22	-	-	-	-	66357	56369	At 00:29 Hrs /15-10-2024, 220 kV Naranpar(Roha)-Bhuj S/C tripped on B-E fault. During patrolling it was found that tower no.67 and 68 collapsed due to conductor theft by miscreants. No generation loss ocurred due to the event.	Tripping of following Elements: 1. 220 kV Naranpar(Roha)- Bhuj
10	GD-1	WR	15-10-2024 16:24	15-10-2024 17:49	01:25	84	-	0.12%	-	68383	61104	At 16:24 Hrs /15-10-2024, 220 kV Vadva-Bhuj S/C tripped on R-E fault from Vadva end only. A/R successful at Bhuj end. During inpection LA counter of transformer increased by 1 indicating presence of surges. Generation loss of 84 MW occurred at Vadva (GIWEL-2) wind power plant due to the event.	Tripping of following Elements: 1. 220 kV Vadva- Bhuj
11	GD-1	WR	18-10-2024 07:23	18-10-2024 09:06	01:43	726	-	1.05%	-	68938	60776	At 07:23 Hrs / 18-10-2024, Bus bar protection operated in 220 kV Raigarh-Bus-1&2 (Double Main and Transfer Bus scheme) due to breaking of jumper of Y phase CT of 220 kV Raigarh-Jindal and felling of conductor of same on 220 kV Raigarh-Auxilary Bus, resulting in tripping of all connected elements (as mentioned in elements tripped column). Load loss of 726 MW occurred at Raigarh(CG), Saraipalli and asscoiated down stream network due to the event.	Tripping of following Elements: 1. 220 kV Raigarh(PG)-Raigarh(CG)-1,2&3 2. 220 kV Raigarh(CG) Bus-1&2 3. 220 kV Raigarh-Saraipali-1&2 4. 220 KV Raigarh-Gerwani 5. 220 KV Raigarh-JSPL-1&2 6. 220 KV Raigarh-Korba East
12	GD-1	WR	18-10-2024 13:02	18-10-2024 14:45	01:43	247	-	0.37%	-	66568	59582	At 13:02 Hrs /18-10-2024 220kV Umariya (Agar Unit-5) Pachora ckt tripped on Differential protection operation on Y-phase to Earth fault. A/R not operated for single phase fault. During patrolling no abnormilities found. Generation loss of 247 MW occurred at Umariya (Agar) Wind Power Plant due to loss of evacuation.	Tripping of following Elements: 1. 220kV Umariya (Agar)-Pachora
13	GD-1	WR	23-10-2024 22:36	01-11-2024 23:59	217:23	-	-	-	-	70192	58961	At 22:36 Hrs / 23-10-2024 220 kV Bhuj-Gadhsisa tripped on B-E fault. During pattrolling it was found that Tower got damaged from Top section due to conductor theft of spare line at tower location 13/2. No Generation loss occurred due to the event.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa
14	GI-2	WR	25-10-2024 02:16	25-10-2024 04:13	01:57	-	-	-	-	66568	59582	At 02:16 hrs / 25-10-2024, Busbar protection operated in 400 kV New Koyna-Bus-2 due to B phase CT blast of 400 kV New Koyna-Karad-1 at Koyna, resulting in resulting in tripping of all connected elements (as mentioned in elements tripped column). Two machines at Koyna(4) running in condesor mode also got triped. No generation or load loss occurred due to the event.	Tripping of following Elements: 1. 400 kV New Koyna Bus-2 2. 400 kV New Koyna-Karad2 3. 400 kV New Koyna-Jaigad-1 4. 400/200kV New Koyna ICT-1,3 5. 400 kV New Koyna-Dhabol-2 6. 400 kV New Koyna Bus Coupler. 7. 400 kV New Koyna-Koyna(4)-2
15	GD-1	WR	27-10-2024 06:25	27-10-2024 07:53	01:28	28		0.05%		61455	56859	At 06:25 Hrs / 27-10-2024 220 kV Bhuj-Nanavalka tripped on B-E fault. It is seen from Disturbance recorders at Nanavalka end that all three phases tripped for a fault in single phase which is a maloperation. During patrolling no abnormalites were found. Generation loss of 28 MW occurred at Nanavalka (Alfanar) Wind power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Nanavalka

Details of Grid Events during the Month of Oct 2024 in Southern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA	02-10-2024 22:21	02-10-2024 22:46	00:25	0	137	0.00%	0.31%	45987.18	44260.4	Complete outage of 220kV/66kV Kanakpura , 220kV/66kV KIADB Harohalli, 220kV Harohalli and 220kV Tataguni SS of KPTCL: During antecedent conditions 220kV Kanakpura TK Halli were under outage. 220kV/66kV Kanakpura , 220kV/66kV KIADB Harohalli, 220kV Harohalli were being radially fed through 220kV Somanahalli Harohalli line and the line tripped. Also, It is also reported that, Earth fault protection operated at Tataguni end in 220kV Somanahalli Tataguni and 220kV Vrishabhavathy Tataguni. Tripping of both lines led to complete outage of 220kV/66kV Kanakpura , 220kV/66kV KIADB Harohalli, 220kV Harohalli and 220kV Tataguni SS of KPTCL.	220KV-TATAGUNI-SOMANAHALLI-1, 220KV-HAROHALLI-SOMANAHALLI-1
2	GD - 1	KARNATAKA	03-10-2024 00:58	03-10-2024 01:06	00:08	0	80	0.00%	0.19%	40617.48	41997.15	Complete outage of 220kV/66kV Kanakpura , 220kV/66kV KIADB Harohalli, 220kV Harohalli and 220kV Tataguni SS of KPTCL: 220kV During antecedent conditions 220kV Kanakpura TK Halli were under outage. 220kV/66kV Kanakpura , 220kV/66kV KIADB Harohalli, 220kV Harohalli were being radially fed through 220kV Somanahalli Harohalli line. As per the reports submitted, the triggering incident was Y-N fault which Subsequently became a YB-N fault. It is reported that and the line sensed in Z1 but the breaker did not open. At the same time, 400kV/220kV Somanahalli ICT-1&2 tripped on HV side E/F protection. It is also reported that, Earth fault protection operated at Tataguni end in 220kV Somanahalli Tataguni and 220kV Vrishabhavathy Tataguni. This led to complete outage of 220kV/66kV Kanakpura , 220kV/66kV KIADB Harohalli, 220kV Harohalli and 220kV Tataguni SS of KPTCL.	400KV/220KV SOMANAHALLI-ICT-2, 400KV/220KV SOMANAHALLI-ICT-1, 220KV-HAROHALLI-SOMANAHALLI-1, 220KV-TATAGUNI-SOMANAHALLI-1
3	GD - 1	KARNATAKA	03-10-2024 05:51	03-10-2024 06:29	00:38	0	40	0.00%	0.09%	39942.35	43298.53	Complete Outage of 220/66kV Khodays: 220/66kV Khodays is equipped with single bus and 2 lines 220kV Somanahalli-Khodays and 220kV Subramanyapura-Khodays. The triggering incident is suspected charging of 220kV Somanahalli-Harohalli on fault, during which 220kV Khodays-Somanhalli tripped at Khodays end on Z2 extension. However 3ph tripped and closed again within 40 ms which led to the operation of LBB and led to tripping of one and only Bus at Khodays. This led to the Complete Outage of 220/66kV Khodays.	220KV-SOMANAHALLI-KHODAYS-1, 220KV-SUBRAMANYAPURA-KHODAYS-1
4	GD - 1	PONDICHERRY	06-10-2024 03:50	06-10-2024 06:24	02:34	0	64	0.00%	0.15%	38271.11	41539.62	Complete outage of 230kV/110kV Bahoor SS of Pondicherry: During antecedent conditions, 230kV Pondicherry Bahoor was under outage. As per the reports submitted, the triggering incident was R-N fault in 230kV Bahour Karaikal line. Tripping of the only source resulted in complete outage of 230kV/110kV Bahoor SS.	230KV-BAHOOR-KARAIKAL-1, BAHOOR - 230KV
5	GD - 1	KARNATAKA	09-10-2024 12:48	09-10-2024 13:08	00:20	0	159	0.00%	0.30%	48333.23	53107.05	Complete Outage of 220kV/66kV Khodays SS and 220kV/66kV Subramanyapura SS of KPTCL: 220/66kV Khodays is equipped with single bus and 2 lines 220kV Somanahalli-Khodays and 220kV Subramanyapura-Khodays. As per the reports submitted, the triggering incident was B-N fault in 220kV Subramanya Pura Peenya line and the line tripped. At the same time, 220kV Somanahalli Khodays line tripped at Somanahalli end, on DPR. Tripping of both lines led to complete outage of 220kV/66kV Subramanyapura SS and 220kV/66kV Khodays SS.	220KV-SUBRAMANYAPURA-KHODAYS-1, 220KV-SUBRAMANYAPURA-PEENYA-1

Details of Grid Events during the Month of Oct 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
6	GD - 1	KARNATAKA	09-10-2024 13:38	09-10-2024 13:57	00:19	0	123	0.00%	0.24%	47345.6	51655.96	Complete Outage of 220kV Exora SS, 220kV Vikas Tech and Bus-1 outage at 220kV Malur SS : 220kV Malur SS was operating with split bus condition with 220kV Hoody Malur line feeding 220kV Malur Bus-1. 220kV Exora and 220kV Vikas Tech Park were being radially fed from 220kV Malur Bus-1. As per the reports submitted, the triggering incident was R-N fault in 220kV Hoody Malur line. Tripping of this line led to loss of power supply to 220kV Malur Bus-1 which intrun led to complete outage of 220kV Exora SS and 220kV Vikas Tech Park.	220KV-HOODY-MALUR-1
7	GD - 1	TAMILNADU	09-10-2024 17:34	09-10-2024 18:40	01:06	98	0	0.22%	0.00%	44726.43	47953.9	Complete Outage of 230kV JSW Savalaperi Wind Station: As per the reports submitted, the triggering incident was RN fault in 230KV- TTGS-JSW_Savalaperi-1. Line tripped on operation of differential protection at both ends. A/r not operated due to receipt of DT from JSW_Savalaperi end. Tripping of the only connected line resulted in the complete outage of 230kV JSW Savalaperi Wind Station.	230KV-TTGS-JSW_Savalaperi-1
8	GD - 1	PONDICHERRY	10-10-2024 12:55	10-10-2024 13:54	00:59	0	74	0.00%	0.14%	49597.49	51523.34	Complete outage of 230kV/110kV Bahoor SS of Pondicherry : During antecedent conditions, 230kV Pondicherry Bahoor was under outage. As per the reports submitted, the triggering incident was R-N fault in 230kV Bahour Karaikal line. Tripping of the only source resulted in complete outage of 230kV/110kV Bahoor SS.	230KV-BAHOOR-KARAIKAL-1
9	GD - 1	ANDHRA PRADESH	10-10-2024 14:22	10-10-2024 20:43	06:21	0	0	0.00%	0.00%	46891.77	49223.67	Complete Outage of 220kV/132kV Borampalli SS, 220kV/33kV Saipuram, 220kV Theta and 220kV Maddelacheru: 220kV/33kV Saipuram, 220kV Theta and 220kV Maddelacheru are being radially fed from 220kV/132kV Borampalli SS. As per the reports submitted, the triggering incident was LBB maloperaion in 220kV Borampalli Kalyandurgam Line-2. subseqeuntly, all elements connected to 220kV Bus-1 and Bus-2 tripped due to erratic isolator status in 220kV Borrampalli Ecoron feeder-1 bay. This led to complete outage of 220kV/132kV Borampalli SS which inturn led to complete outage of 220kV/33kV Saipuram, 220kV Theta and 220kV Maddelacheru.	220KV-BORAMPALLI-URAVAKONDA-2, 220KV-BORAMPALLI-URAVAKONDA-3, 220KV-BORAMPALLI-SAIPURAM-1, 220KV-BORAMPALLI-SAIPURAM-2, 220KV-BORAMPALLI-URAVAKONDA-4, 220KV-BORAMPALLI-MADDELACHERU-2, 220KV-BORAMPALLI-GURUVEPALLI-2, 220KV-BORAMPALLI-GURUVEPALLI-1
10	GD - 1	KARNATAKA	13-10-2024 15:01	13-10-2024 17:14	02:13	120	0	0.28%	0.00%	42922.57	42680	Tripping of 220kV Bus-4 at 400kV/220kV Koppal SS and Complete Outage of 220kV Renew_Surya_Ojas_Koppal_W and 220kV Ayana_Six_Koppal: The triggering incident was 220kV Bus-4 fault at the Koppal end resulting in the tripping of all the elements connected to 220kV Bus-4 of 400kV/220kV Koppal SS. At the same time, 220kV-RSOPL_Koppal-1 and 220kV Ayana Koppal line tripped only at RSOPL and Ayana ends respectively due to suspected maloperation of SOTF protection. This resulted in the complete outage of 220kV Renew_Surya_Ojas_Koppal_W and 220kV Ayana_Six_Koppal.	400KV/220KV KOPPAL-ICT-5, KOPPAL - 220KV - Bus 4, Renew_Surya_Ojas_Koppal_W - 220KV
11	GD - 1	KARNATAKA	16-10-2024 15:59	16-10-2024 16:46	00:47	0	0	0.00%	0.00%	46265.12	43573.59	Complete outage of 220kV Ayana_Six_Koppal: As per the reports submitted, the triggering incident was RY-N fault in 33kV feeder of Ayana_Six_Koppal. At the same time, 220kV Kppal Ayana_Six_Koppal line tripped at Ayana_Six_Koppal on over current protection. Tripping of the only connected line led to complete outage of 220kV Ayana_Six_Koppal.	Ayana_Six_Koppal - 220KV, 220KV-KOPPAL-Ayana_Six_Koppal-1
12	GD - 1	ANDHRA PRADESH	18-10-2024 01:09	18-10-2024 02:14	01:05	0	0	0.00%	0.00%	37366.65	37833.19	Complete Outage 220kV Chinakampalli (Cuddapah) SS of APTRANSCO: As per the reports submitted, the triggering incident is the B-ph CT failure of 220kV Cuddpah-RTPP-1 at Cuddapah end. The fault was sensed in Z1 in the line and BBP operated leading to the tripping of all elements connected to Bus-1. Due to fire from the failed CT coming into the vicinity of 220kV Cuddpah-RTPP-2 at Cuddpah end led to the operation of BBP of 220kV Bus-2 and led to the complete outage of 220kV Cuddapah (Chinkampalli) SS	220KV-CUDDAPAH-RAJAMPET-1, 220KV-CUDDAPAH-RAYALSEEMA TPP-3, 220KV-CUDDAPAH-RENIGUNTA-1, 220KV-CUDDAPAH-RAYALSEEMA TPP-2, 220KV-CUDDAPAH-RAYALSEEMA TPP-4, 220KV-CUDDAPAH-RAYALSEEMA TPP-1, 220KV-CUDDAPAH-THIMAPURAM-1
13	GD - 1	KARNATAKA	22-10-2024 06:04	22-10-2024 10:40	04:36	3	0	0.01%	0.00%	36408.47	40226.14	Complete Outage of 220kV Vena_GadagPS: As per the reports submitted, the triggering incident was R-N fault in 220kV Gadag Vena Line and the line tripped. Tripping of the only connected line led to complete outage of 220kV Gadag PS.	220KV-GADAG_PSS-Vena_GadagPS-1

Details of Grid Events during the Month of Oct 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
14	GD - 1	KARNATAKA	22-10-2024 11:08	22-10-2024 14:46	03:38	0	0	0.00%	0.00%	45666.61	45736.45	Complete Outage of 220kV Vena_GadagPS: As per the reports submitted, the triggering incident was tripping of 220kV Gadag Vena line at Gadag end on receiving DT from Vena end. Tripping of the only connected line to complete outage of 220kV Vena_Gadag PS.	220KV-GADAG_PSS-Vena_GadagPS-1
15	GI-2	ANDHRA PRADESH	02-10-2024 19:11	02-10-2024 21:35	02:24	0	0	0.00%	0.00%	45409.25	44968.23	Tripping of 400kV Bus-2 and 220kV Bus-2 at 400/220kV Podili SS: In the antecedent conditions, 400/220kV Podili substation had only one DC supply as the other DC source was being replaced. As per the reports submitted, due to the station supply failure and complete discharge of the only available DC source led to the tripping of Bus Reactor and 220kV Podili-Podili(old)-1&2 lines. During the supply restoration process, due to control circuit issue led to the tripping of ICT-1,2 &3, 220kV lines and bus coupler other than 220kV Podili-Atmakur-1. This led to the tripping of 400kV Bus-2 and 220kV Bus-2 at 400/220kV Podili SS.	400KV/220KV PODILI-ICT-1, 400KV/220KV PODILI-ICT-2, 400KV/220KV PODILI-ICT-3, 220KV-ATMAKUR-PODILI-2, 220KV-PODILI_OLD-PODILI-2, 220KV-PODILI_OLD-PODILI-1, 220KV-PODILI-KANDUKUR-1, 220KV-PODILI-KANDUKUR-2
16	GI-1	TAMILNADU	04-10-2024 06:00	04-10-2024 06:26	00:26	0	0	0.00%	0.00%	42892.55	46132.19	Tripping of 230kV Bus-2 400kV/230kV Sholinganallur SS of TANTRANSCO: As per the reports submitted, the triggering incident was a momentary Y-N fault in 230kV Sholinganallur Bus-2 with a fault current of approximately 22.78kA. Immediately, 230kV BBP operated and all elements connected to the bus tripped.	SHOLINGANALLUR - 230KV - Bus 2, 400KV/230KV SHOLINGANALLUR-ICT-2, 230KV-OMEGA-SHOLINGANALLUR-1, 230KV-SHOLINGANALLUR-SIRUSERI-1
17	GI-2	ANDHRA PRADESH	11-10-2024 01:33	11-10-2024 18:40	17:07	300	0	0.79%	0.00%	37995.6	39426.67	Tripping of 400kV Bus-1 400kV/220kV HNPCL Generating station: As per the reports submitted, the triggering incident was R-N fault in 400kV Bus-1. Immediately, 400kV Bus-1BBP operated and all elements connected to Bus-1 tripped. At the same time, GT-2 connected to 400kV Bus-2 also tripped on REF protection.	HINDUJA - 400KV - Bus 1, 420KV/21KV HINDUJA-GT-1, 400KV-HINDUJA-KALPAKKA-2, 400KV-GUDDIGUDEM-HINDUJA-1, 420KV/21KV HINDUJA-GT-2
18	GI-1	KARNATAKA	13-10-2024 15:01	13-10-2024 16:37	01:36	0	32	0.00%	0.07%	42922.57	42679.54	Tripping of 220kV Bus-2 of 220kV/66kV Yerrandahally SS of KPTCL: 220kV/66kV Yerrandahally SS was operating with bus split condition at 220kV Yerrandahally with 220kV Yerrandahally Hosur line radially feeding 220kV Bus-2. As per the reports submitted, the triggering incident was Y-N fault in 230kV Yerrandahally Hosur line and the line tripped. Tripping of the only source led to loss of power supply to 220kV Yerrandahally Bus-2.	220KV-YERRAANDAHALLI-HOSUR-1,
19	GI-2	ANDHRA PRADESH	19-10-2024 16:35	19-10-2024 18:57	02:22	0	0	0.00%	0.00%	42933	44466	Tripping of 400kV Bus-2 at 400/220kV Kalpakka : As per the reports submitted, the triggering incident is the R-N bus fault where in TBC isolator in 400kV Kalpakka-Simhadri-4 line bay at 400kV Kalpakka got disconnected and created an R-N fault in Bus-2. This led to the operation of BBP in Bus-2 and tripping of all elements connected to 400kV Bus-2 at 400/220kV Kalpakka	400KV-HINDUJA-KALPAKKA-2 400KV-SIMHADRI-KALPAKKA-4 400KV-MARADAM-KALPAKKA-1 400KV/220KV KALPAKKA-ICT-2
20	GI-1	ANDHRA PRADESH	21-10-2024 06:26	21-10-2024 08:08	01:42	0	0	0.00%	0.00%	37872.1	41271.99	Tripping of 220kV Bus-2 at Nagarjunasagar SS of APTRANSCO: As per the reports submitted, the triggering incident is the Y-B fault in 220kV Nagarjunasagar(Talapalli)-Chalakurthy near Nagarjunasagar end (Loc-1). At Nagarjunasagar end the fault was sensed in Zone-1 and 3ph tripped (initially Y-N fault, then Y-B fault, then B-N fault). During the fault since being near the vicinity of the Nagarjunasagar station led to the tripping of 400/220kV Nagarjunasagar ICT-3 on high set over current and later external LBB operated leading to the tripping of all the elements connected to 220kV Bus-2 due to suspected cable issue. This led to the tripping of 220kV Bus-2 Nagarjunasagar SS.	400KV/220KV NAGARJUNASAGAR_PG-ICT-3, 400KV/220KV NAGARJUNASAGAR_PG-ICT-1, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-INAPARAJUPALLI-2, 220KV-SRISAILAM_RIGHT_BANK-NAGARJUNASAGAR_AP-2, 220KV-NAGARJUNASAGAR_AP-RENTACHINTHALA-1
21	GI-1	TAMILNADU	24-10-2024 17:35	24-10-2024 19:15	01:40	370	257	0.87%	0.56%	42667.65	45757.93	Complete Outage of 230kV TTPS of TANGENDCO: As per the reports submitted, while closing isolator of spare Generator transformer isolator failed causing Bus fault. Immediately, 230kV Bus-1 and Bus-2 BBP operated and all elements connected to the bus tripped. Tripping of all elements connected to the buses resulted in complete outage of 230kV TTPS of TANGENDCO.	230KV-TTPS-AUTO-TTPS-1, 230KV-TTPS-AUTO-TTPS-2, TTPS - 230KV - Bus 1, TTPS - 230KV - Bus 2, 230KV-KAYATHAR(TN)-TTPS-1

Details of Grid Events during the Month of Oct 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-I	BALIMELA PH & BALIMELA	05-10-2024 19:03	05-10-2024 19:34	00:31	00:00	20	1.19%	0.07%	36047	26757	At 19:03 Hrs 220kV-Balimela PH-Jayanagar-1 & 2 tripped on B_N fault simultaneously. Entire generation of Balimela PH around 430 MW was now being evacuated through single line 220kV-Balimela-Jeynagar ckt#3(via Gobindapally). 220 kV Gobindapally-Jayangar tripped on O/c. This led to islanding of generation at Balimela PH (430 MW) and 20 MW load at Balimela S/s. U#2,3,4 at Balimela PH tripped on BackUp impedance protection and U#5,6,7,8 remained on House load operation but could not sustain. Later at 19:06 Hrs, all 4 units were handtripped and total power failed at Balimela PH and Baliemla S/s Generation loss of around 430 MW and load loss of around 20 MW occurred. Power extended at Balimela PH through 220kV- Balimela PH-Jayanagar-1 at 19:22 Hrs and unit#6 was synchronised.	220 KV Balimela-Jayanagar-1 220 KV Balimela-Jayanagar-2 220 KV Balimela-Gobindapally 220 kV Gobindapally-Jayanagar 220 kV Balimela PH-Balimela 220 kV Balimela PH-Upper Sileru (Idle Charged) Balimela Unit #2, 3, 4 Tripped Balimela Unit #5, 6,7 & 8 Hand Tripped
2	GD-I	BARGARH NEW	10-10-2024 19:04	10-10-2024 19:10	00:06	00:00	190	0.00%	0.72%	35559	26521	At 19:04 Hrs on 10.10.2024, 220kV- Bargarh New-Katapalli tripped on over current from Bargarh end. Bargarh New was being radially fed from Katapalli and 220 kV Bolangir (GR)-Bargarh New was kept open to control loading of 220 kV Bolangir (PG)– Bolangir (GR) D/C. Consequently, total power failed at Bargarh New S/s. Around 190 MW load loss occurred. Power extended at 19:10 Hrs through 220kV-Bargarh New-Katapalli.	220 kV Bargarh- Katapalli
3	GD-I	JORETHANG HEP	17-10-2024 10:19	17-10-2024 10:28	00:09	82	0	0.30%	0.00%	27075	23680	At 10:19 Hrs 220kV-Jorethang-New Melli ckt #1 tripped on B phase to earth fault (Jorethang Generation radially connected to New Melli due to breakdown of 220kV-Jorethang-New Melli ckt#2) as a result total generation loss of 82 MW occurred at Jorethang S/s. At 10:28 Hrs power extended through 220kV-Jorethang-New Melli ckt #2 and generation restored at 10:32 Hrs.	220KV-JORETHANG-NEW MELLI-1 220KV-JORETHANG-NEW MELLI-2
4	GD-I	RAMCHANDRAPUR	22-10-2024 05:08	22-10-2024 06:30	01:22	0	319	0.00%	1.42%	31963	22416	At 05:08 hrs, B ph PT of 220 kV Ramchandrapur Bus-2 blast which caused tripping of 220 kV Bus-2 at Ramchandrapur. Simultaneously 220 kV Bus-1 at Ramchandrapur also tripped at the same time causing total power failure at 220kV Ramchandrapur S/s. Total Load loss occurred around 319 MW at Ramchandrapur. Power was extended by charging 220KV-RAMCHANDRAPUR-CHAIBASA(JUSNL)-1 at 06:30 Hrs.	220KV-RAMCHANDRAPUR-JAMSHEDPUR-1 220KV-RAMCHANDRAPUR-JAMSHEDPUR-2 220KV-RAMCHANDRAPUR-JAMSHEDPUR-3 220KV-RAMCHANDRAPUR-CHAIBASA(JUSNL)-D/C 220KV-RAMCHANDRAPUR-CHANDIL-1 220KV-RAMCHANDRAPUR-JODA
5	GD-I	DUMKA, JASIDIH, GIRIDIH , GOVINDPUR, GODDA ,TENUGHAT TPS	29-10-2024 17:50	29-10-2024 18:05	00:15	140	560	0.41%	2.13%	34480	26286	220kV-Maithon Dumka D/c loading touched 210 MW which triggered SPS at Dumka S/s. Tripping command generated for tripping of Pakur load(As per Dumka SPS), simultaneously one tripping command also extended (Due to mal operation of SPS at Dumka) for 220 kV Maithon - Dumka D/C line which got tripped at 17:50 hrs. This led to over loading of 220KV-Tenughat TPS- Biharsarif-1, which also tripped (Tripped on over current from Biharsariff). As a result, a complete power outage occurred at 220 kV Dumka, 220 kV Govindpur, 220 kV Jasidih, 220 kV Giridih, 220 kV Tenughat, 220 kV Godda. Power extended at 18:05 Hrs by charging 220KV-Tenughat TPS- Biharsarif-1.	220KV-MAITHON(PG)-DUMKA-D/C 220KV-TENUGHAT TPS- BIHARSARIF-1 220KV-DUMKA-GOVINDPUR-D/C 220KV-GOVINDPUR-TENUGHAT TPS-D/C 220KV-DUMKA-JASIDIH-D/C 220KV-JASIDIH-GIRIDIH-D/C 220KV-DUMKA-GODDA-D/C 132KV-DUMKA-PAKURPUR-D/C 132KV-DUMKA-DUMKA(old)-D/C TENUGHAT - UNIT 1 400 KV- TENUGHAT-PUVNL
6	GD-I	DUMKA, JASIDIH, GIRIDIH , GOVINDPUR, GODDA ,TENUGHAT TPS	30-10-2024 10:55	30-10-2024 11:15	00:20	145	510	0.49%	2.22%	29782	22968	At 10:56 Hrs 220kV-Maithon-Dumka #2 tripped on B_N fault (A/r attempt failed due to persisting fault) Prior to fault loading in each line was around 180 MW. After tripping of Ckt.-2, flow in 220kV-Maithon-Dumka Ckt#1 went beyond 305 MW (800 A) and SPS operated and 220 kV Maithon-Dumka-1 also tripped after 4 second(SPS current setting of 220kV-Maithon Dumka D/C was changed after disturbance on 29.10.2024).Thereafter, 220 kV Tenughat Biharsariff tripped (on overcurrent from Biharsariff end) which result islanding of Tenughat Unit which collapse due to load generation unbalance resultant total power failure at 220 kV Dumka, 220 kV Govindpur, 220 kV Jasidih, 220 kV Giridih, 220 kV Tenughat, 220 kV Godda. Total loass of 510 MW occurred. Power extended 11:15 Hrs by charging 220KV-Tenughat TPS- Biharsarif-1.	220KV-MAITHON(PG)-DUMKA-D/C 220KV-TENUGHAT TPS- BIHARSARIF-1 220KV-DUMKA-GOVINDPUR-D/C 220KV-GOVINDPUR-TENUGHAT TPS-D/C 220KV-DUMKA-JASIDIH-D/C 220KV-JASIDIH-GIRIDIH-D/C 220KV-DUMKA-GODDA-D/C TENUGHAT - UNIT 1 400 KV- TENUGHAT-PUVNL
7	GD-I	BALIMELA PH & BALIMELA	30-10-2024 09:05	30-10-2024 09:21	00:16	290	20	0.93%	0.06%	31180	30890	At 09:05 bus fault occurred at 220kV Balimela S/s(All feeders and unit connected to 220kV-Main Bus#2) which leads to tripping of all emanating line and all running units at Balimela. This causes total power failure at Balimela S/s.Generation loss of around 290 MW and load loss of around 20 MW occurred.. power extended at 09:21 Hrs through 220 KV BALIMELA-JAYANAGAR-1 and 2.	220 KV Balimela-Jayanagar-1 220 KV Balimela-Jayanagar-2 220 KV Balimela-Gobindapally 220 kV Gobindapally-Jayanagar 220 kV Balimela PH-Balimela 220 kV Balimela PH-Upper Sileru (Idle Charged) All running unit at Balimela HEP

Details of Grid Events during the Month of Oct 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Pailapool area of Assam Power System	02-10-2024 13:21	02-10-2024 13:44	00:23	26	31	1.15%	1.24%	2261	2498	Pailapool area of Assam Power System was connected with rest of NER Power system through 132 kV Pailapool - Srikona Line & 132 kV Pailapool -Jiribam Line. At 13:21 Hrs of 02-10-2024, 132 kV Pailapool - Srikona Line & 132 kV Pailapool -Jiribam Line tripped. Due to tripping of these elements, Pailapool area of Assam Power System was isolated from NER Grid and collapsed due to load-generation mismatch in this area. Power supply was extended to Pailapool area of Assam Power System by charging 132 kV Pailapool - Srikona Line at 13:44 Hrs of 02-10-2024.	132 kV Pailapool - Srikona Line & 132 kV Pailapool - Jiribam Line
2	GD I	Karong area of Manipur Power System	04-10-2024 02:32	04-10-2024 03:16	00:44	0	7	0.00%	0.39%	3061	1812	Karong area of Manipur Power System was connected with rest of NER Grid through 132 kV Kohima Karong line. 132 kV Yurembam –Karong line was under outage condition since 16:35 Hrs of 26.09.2024. At 02:32 Hrs of 04-10-2024, 132 kV Kohima-Karong line tripped. Due to tripping of this element, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Karong area of Manipur Power System by charging 132kV Kohima-Karong line at 03:16 Hrs of 04.10.2024.	132 kV Kohima-Karong line
3	GD I	Karong area of Manipur Power System	13-10-2024 23:37	14-10-2024 00:07	00:30	0	7	0.00%	0.37%	3026	1899	Karong area of Manipur Power System was connected with rest of NER Grid through 132 kV Kohima Karong line and 132 kV Imphal(MA) –Karong line. At 23:37 Hrs of 13-10-2024, 132 kV Kohima-Karong line and 132 kV Imphal(MA) –Karong line tripped. Due to tripping of these elements, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Karong area of Manipur Power System by charging 132 kV Imphal(MA) –Karong line at 00:07 Hrs of 14.10.2024.	132 kV Kohima-Karong line and 132 kV Imphal(MA) –Karong line
4	GD I	Basar, Along and Pasighat areas of Arunachal Pradesh Power System	17-10-2024 14:44	17-10-2024 15:23	00:39	0	8	0.00%	0.34%	2355	2375	Pasighat, Along and Basar areas of Arunachal Pradesh Power System were connected with rest of NER Grid through 132 kV Roing-Pasighat line only. At 14:44 Hrs of 17-10-2024, 132 kV Roing-Pasighat line tripped. Due to tripping of this element, Basar, Along and Pasighat areas of AP Power System were isolated from NER Grid and collapsed due to no source available in this area as there was planned shutdown of 132 kV Daporijo-Basar Line. Power supply was extended to Pasighat area by charging 132 kV Roing –Pasighat line at 15:23 Hrs of 17.10.2024. 132 kV Pasighat-Along was charged at 15:39 Hrs and 132 kV Along-Basar at 16:23 Hrs of 17.10.2024.	32 kV Roing-Pasighat line
5	GD I	Rengpang area of Manipur Power System	19-10-2024 10:28	19-10-2024 10:56	00:28	0	1	0.00%	0.05%	1806	2096	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132kV Loktak Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 10:28 Hrs of 19-10-2024, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area by charging 132kV Loktak-Rengpang line at 10:56 hrs of 19-10-2024.	132 kV Loktak-Rengpang line
6	GD I	Dibrugarh area of Assam Power System	28-10-2024 09:05	28-10-2024 09:41	00:36	0	20	0.00%	0.94%	2101	2135	Dibrugarh area of Assam Power System was connected with rest of NER Grid through 132 kV Behiating- Dibrugarh line. 132kV Tinsukia-Dibrugarh was under S/D for corridor cleaning. At 09:05 Hrs of 28-10-2024, 132 kV Behiating- Dibrugarh line tripped. Due to tripping of this element, Dibrugarh area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Dibrugarh area by charging 132kV Behiating- Dibrugarh line at 09:41 hrs of 28-10-2024.	132 kV Behiating- Dibrugarh line
7	GD I	Imphal(Yurembam) area of Manipur Power System	28-10-2024 13:30	28-10-2024 15:08	01:38	0	50	0.00%	2.24%	2127	2236	Imphal(Yurembam) area of Manipur is connected with rest of the NER grid mainly through 3 numbers of 132 kV Imphal(PG)- Imphal(Yurembam) Lines. Also, Imphal(Yurembam) is connected with Yiangangpokpi SS through 2 numbers of 132 kV Imphal (Yurembam) - Yaingangpokpi 1&2 Lines and connected with Karong SS through 1 number of 132 kV Imphal (MSPCL) - Karong Line. Before the event, 132 kV Imphal(PG)-Imphal(Yurembam) 2 Line and 132 kV Imphal (Yurembam) - Yaingangpokpi 2 Lines was under planned shutdown. At 13:30 Hrs of 28-10-2024, due to heavy fault in Imphal(Yurembam) SS, all the connected lines i.e. 132 kV Imphal(PG)-Imphal(Yurembam) 1 &3 Lines, 132 kV Imphal (Yurembam) - Yaingangpokpi 1 Lines and 132 kV Imphal (MSPCL) - Karong Line tripped resulted into the Grid Disturbance in the Imphal(Yurembam) substation of Manipur power system. Additionally, tripping of 400/132 kV, 315 MVA, ICT I at Imphal(PG), 132 kV Imphal (PG) - Loktak Line and 400 kV Imphal(PG) - New Kohima 1 Line observed during the time. Power supply was extended to Imphal(Yurembam) area by charging 132 kV Imphal(PG)- Imphal(Yurembam) 2 Line at 15:08 hrs of 28-10-2024.	132 kV Imphal(PG)- Imphal(Yurembam) 1 &3 Lines, 132 kV Imphal (Yurembam) - Yaingangpokpi 1 Lines and 132 kV Imphal (MSPCL) - Karong Line
8	GD I	Rengpang area of Manipur Power System	29-10-2024 22:26	29-10-2024 23:27	01:01	0	1	0.00%	0.04%	3091	2577	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132kV Loktak Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 22:26 Hrs of 29-10-2024, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area by charging 132kV Loktak-Rengpang line at 23:27 hrs of 29-10-2024.	132 kV Loktak-Rengpang line

21. NEW ELEMENTS CHARGED IN OCTOBER 2024

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
NR	1	KHURJA	THDC STPP Stage-1	Unit-1	660	660	28.10.2024
	2	Bikaner_2(PBTSL)	TSES1PL	Solar	55.6	55.6	09.10.2024
	3	Fatehgarh Pooling(FBTL)	ACME_Deoghar_SPPL	Solar	253	253	22.10.2024
	4	Bhadla_2(PG)	NTPC_KOLAYAT SL	Solar	32.9	531.68	15.10.2024
	5	Fatehgarh Pooling(FBTL)	ACME_Phalodi_SEPL	Solar	272	272	19.10.2024
	6	Fatehgarh Pooling(FBTL)	ACME_Raisar_SEPL	Solar	192.67	272	23.10.2024
	7	Fatehgarh Pooling(FBTL)	ACME_Dhaulpur_PPL	Solar	192.67	272	30.10.2024
SR	8	Peramium Sub station	JSW_NEO	LOT-5/wind	5.4	151.2	29.10.2024
	9	TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-7/wind	13.5	299.7	25.10.2024
	10	TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-8/wind	21.6	321.3	26.10.2024
	11	TTGS SAVALPERI	JSW Renew Energy Ltd	LOT-9/wind	16.2	337.5	28.10.2024
	12	TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-9/wind	13.5	351	26.10.2024
	13	TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-10/wind	18.9	369.9	24.10.2024
	14	TTGS SAVALPERI	JSW Renew Energy Ltd	LOT-10/wind	18.9	388.8	28.10.2024
	15	TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-11/wind	10.8	399.6	26.10.2024
	16	AMGEPL Wind Substation	AMGEPL	LOT-2/wind	19.8	75.9	08.10.2024
	17	Gadag PS(ISTS) KOPPAL	GADAG_GIWEPL_W	LOT-5/wind	2.1	46.2	29.10.2024
	18	Gadag PS(ISTS) KOPPAL	GADAG_GIWEPL_W	LOT-6/wind	8.4	54.6	29.10.2024
	19	AMGEPL Wind Substation	AMGEPL	LOT-3/wind	46.2	122.1	25.10.2024
	20	YADADRI, TELANGANA	YADADRI THERMAL POWER STATION	UNIT-2	800	1600	21.10.2024
				Total Coal Generation Addition	**1460**		
				Total Solar Generation addition	**999**		
				Total Wind Generation addition	**195**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
NR	1	PSTL	Sikar_2(PSTL)	ICT-2	765/400/33	1500	02.10.2024
	2	DTL	Mundka(DV)	ICT-2	400/220/33	315	04.10.2024
	3	PSTL	Sikar_2(PSTL)	ICT-1	765/400/33	1500	05.10.2024
	4	ACME_Deoghar_SPPL	ACME_Deoghar_Ftgh1(PG)	Power Transformer-4	400/33	315	06.10.2024
	5	ACME_Phalodi_SEPL	ACME_Deoghar_Ftgh1(PG)	Power Transformer-2	400/33	315	09.10.2024
	6	Corneight Parks Pvt. Limited	Corneight Parks Pvt. Limited	ICT-1	400/33	200	11.10.2024
	7	Corneight Parks Pvt. Limited	Corneight Parks Pvt. Limited	ICT-2	400/33	200	11.10.2024
	8	ACME_Raisar_SEPL	ACME_Deoghar_Ftgh1(PG)	Power Transformer-3	400/33	315	19.10.2024
	9	ACME_Dhaulpur_PPL	ACME_Deoghar_Ftgh1(PG)	Power Transformer-1	400/33	315	19.10.2024
WR	10	MSETCL	Warora	ICT-2	400/220	500	10.10.2024
SR	11	TANTRANSCO	ARIYALUR	ICT-1	765/400/33	1500	30.10.2024
	12	TGTRANSCO	VATTEM	ST-1	400/11.5	25	05.10.2024
	13	GREENKO	Pinnapuram PSP	GT-1	400/18	300	19.10.2024
	14	GREENKO	Pinnapuram PSP	ST-1	400/11	31.5	19.10.2024
	15	SEPL_NELLORE	Nellore	Power Transformer-1	400/33	80	31.10.2024
ER	16	JSW ENERGY (UTKAL) LTD	JSW ENERGY (UTKAL) LTD	ST-2	6.9/420	60	04.10.2024
	17	PGCIL	RENGALI(PG)	ICT-2 (Replacement)	400/220	500	11.10.2024
	18	PENTL(Powergrid ER NER Transmission Ltd)	BANKA (PG)	ICT-4	400/220	500	25.10.2024
	19	PENTL(Powergrid ER NER Transmission Ltd)	BANKA (PG)	ICT-5	400/220	500	28.10.2024
					Total (MVA)	**8971.5**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NR	1	PSTL	400kV Sikar_2(PSTL)-Neemrana(PG)-2	133.5	Twin HTLS	01.10.2024
	2	PASTL	765kV Sikar_2(PSTL)-Aligarh(PG)-1	256.9	AL59 Zebra	05.10.2024
	3	ACME_Deoghar_SPPL	400kV Fatehgarh Pooling(FBTL)-ACME_Deoghar_Ftgh1(PG)-1	16.0	AL59 Moose	05.10.2024
	4	PASTL	765kV Sikar_2(PSTL)-Aligarh(PG)-2	256.9	AL59 Zebra	07.10.2024
	5	Corneight Parks Pvt. Limited	400kV Jaisalmer(RS)-Corneight Parks Pvt. Limited -1	15.2	Twin Moose	10.10.2024
	6	PSTL	400kV Sikar_2(PSTL)-Neemrana(PG)-1	133.5	Twin HTLS	11.10.2024
SR	7	GREENKO	400KV-GREENKO_CPSS-GREENKO_PSP-1	7.0	ACSR QUAD MOOSE	18.10.2024
			Total ckt km	**819.1**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NIL						

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
SR	1	APTRANSCO	400KV-VTPS-IV - THALLAYAPALEM Line-1	9.86	ACSR Twin Moose	28.10.2024
	2	APTRANSCO	400KV-SATTENAPALLI-THALLAYAPALEM Line-1	56.56	ACSR Twin Moose	28.10.2024
ER	3	PGCIL	132 kV Rangit-Melli (interim) arrangement.	61	HTLS Panther	22.10.2024
	4	PGCIL	132 KV Siliguri-Kurseong-II (interim) arrangement	93	HTLS Panther	09.10.2024
	5	BSPTCL	220KV-BANKA (PG)-Goradih SS-1	32.667	ACSR Zebra	31.10.2024
WR	6	Kharghar Vikhroli Transmission Ltd.	400 kV Pune-Vikhroli (GIS)	110	1414 A/Twin moose ACSR	07.10.2024
	7	Kharghar Vikhroli Transmission Ltd.	400 kV Kalwa-Vikhroli (GIS)	14	1415 A/Twin moose ACSR	07.10.2024
	8	Mumbai Urja Marg Ltd.	220 kV Navi Mumbai-Apta-1	16.297	ACCC Drake/627	15.10.2024
	9	Mumbai Urja Marg Ltd.	220 kV Navi Mumbai-Apta-2	16.297	ACCC Drake/627	15.10.2024
	10	Mumbai Urja Marg Ltd.	220 kV Navi Mumbai-Taloja	13.197	ACCC Drake/627 MVA/1645 A	15.10.2024
	11	Mumbai Urja Marg Ltd.	220 kV Navi Mumbai-Print house	22.29	ACCC Drake/627 MVA/1645 A	15.10.2024

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
NR	1	PASTL	765 kV, 3 x 110MVAR Switchable Convertable LINE_REACTOR of 765kV Sikar_2(PSTL)-Aligarh(PG)-1 at	765	330	05.10.2024
	2	PASTL	765 kV, 3 x 110MVAR Switchable Convertable LINE_REACTOR of 765kV Sikar_2(PSTL)-Aligarh(PG)-2 at	765	330	07.10.2024
	3	PSTL	765 kV, 240 MVAR Switchable Convertable LINE_REACTOR of 765 KV Bhadla-II - SIKAR-II line ckt-1 at Bhadla_2	765	240	08.10.2024
	4	PSTL	765 kV, 240 MVAR Switchable Convertable LINE_REACTOR of 765 KV Bhadla-II - SIKAR-II line ckt-2 at Bhadla_2	765	240	16.10.2024
	5	POWERGRID	400 kV, 50 Non-Switchable Non-Convertable LINE_REACTOR of 400 KV Kanpur-Agra(PG) Ckt-1 at Kanpur(PG)	400	50	29.10.2024
	6	PSTL	765 kV, 3x110MVAR Switchable Convertable LINE_REACTOR of 765kV Sikar_2(PSTL)-Bhadla_2(PG)-1 at	765	110	30.10.2024
	7	PSTL	765 kV, 3x110MVAR Switchable Convertable LINE_REACTOR of 765kV Sikar_2(PSTL)-Bhadla_2(PG)-2 at	765	110	30.10.2024
	8	PSTL	400kV, 125MVAR Bus Reactor 1 at Sikar_2(PSTL)	400	125	01.10.2024
	9	PSTL	765kV, 3x110 MVAR Bus Reactor 1 at Sikar_2(PSTL)	765	330	06.10.2024
	10	PSTL	765kV, 3x110MVAR Bus Reactor 2 at Sikar_2(PSTL)	765	330	07.10.2024
SR	11	TGTRANSCO	125 MVAR Bus Reactor 2 at DINDI	400	125	23.10.2024
ER	12	PGCIL	125MVAR 400KV B/R-4 AT JAMSHEDPUR(PG)	400	125	06.10.2024
				Total (MVAr)	**2445**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

Voltage Profile

विद्युत विभव रूपरेखा माह - अक्टूबर 2024 VOLTAGE PROFILE - October 2024

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	795	758	777
2		दार्लिपली DARLIPALI	0%	100%	0%	0%	0	791	768	778
3		गया GAYA	0%	100%	0%	0%	0	789	753	770
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	790	737	762
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	801	772	786
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	789	745	770
7		राची RANCHI	0%	100%	0%	0%	0	794	766	781
8		सासाराम SASARAM	0%	100%	0%	0%	1	805	741	769
1		आगरा AGRA	0%	100%	0%	0%	0	803	756	780
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	794	751	774
3		अजमेर AJMER	0%	100%	0%	0%	3	804	747	784
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	798	747	776
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	784	760	771
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	783	756	769
7		अंता ANTA	0%	100%	0%	0%	1	802	764	783
8		बलिया BALLIA	0%	100%	0%	0%	0	790	741	768
9		बारा BARA	0%	100%	0%	0%	0	781	756	767
10		भाडला BHADLA	0%	100%	0%	0%	0	805	724	778
11		भाडला-2 BHADLA-2	0%	100%	0%	0%	0	805	728	779
12		भिवानी BHIWANI	0%	100%	0%	0%	1	803	744	783
13		बीकानेर BIKANER	0%	100%	0%	0%	1	801	723	781
14		बरेली BAREILLY	0%	100%	0%	0%	2	805	750	776
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	3	803	759	784
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	800	718	777
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	798	750	772
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	789	744	767
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	1	803	751	780
20		हापुड़ HAPUR	0%	100%	0%	0%	0	800	744	775
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	803	749	776
22		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	797	740	776
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	796	751	771
24		खेतरी KHETRI	0%	100%	0%	0%	0	800	736	779
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	803	744	775
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	772	744	760
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	797	746	771
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	791	742	770
29		मेरठ MEERUT	0%	100%	0%	0%	3	803	743	779
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	798	744	776
31		मोगा MOGA	0%	100%	0%	0%	2	802	728	780
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	779	751	764
33		उरई ORAI	0%	99%	1%	1%	4	808	764	784
34		फागी PHAGI	0%	100%	0%	0%	0	801	753	782
35		रामपुर RAMPUR	0%	100%	0%	0%	2	803	756	782
36		उन्नाव UNNAO	0%	100%	0%	0%	0	784	741	762
37		वाराणसी VARANASI	0%	100%	0%	0%	0	797	760	775
1		अकोला AKOLA	0%	100%	0%	0%	0	796	734	772
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	800	744	774
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	792	743	769
4		भुज BHUJ	0%	100%	0%	0%	0	793	749	774
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	785	749	769
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	786	754	770
7		बीना BINA	0%	100%	0%	0%	0	801	757	779
8		बनसकठा BANASKANTHA	0%	100%	0%	0%	0	801	756	782
9		चापा CHAMPA	0%	97%	3%	3%	25	808	762	790
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	799	749	773
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	792	757	775
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	796	765	777
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	799	739	772
14		गदरवाड़ा GADARWARA	0%	99%	1%	1%	4	805	766	785
15		ग्वालियर GWALIOR	0%	100%	0%	0%	2	809	759	781
16		इदौर INDORE	0%	100%	0%	0%	0	794	741	769
17		जबलपुर JABALPUR	0%	99%	1%	1%	8	806	766	786
18	पश्चिमी क्षेत्र WR	खडवा KHANDWA	0%	100%	0%	0%	0	793	746	771
19		कोरडी KORADI	0%	100%	0%	0%	0	783	743	764
20		लकाडिया LAKADIYA	0%	100%	0%	0%	1	801	755	778
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	798	773	785
22		पड़घे PADGHE	0%	100%	0%	0%	0	801	730	771
23		परली PARLI	0%	100%	0%	0%	0	798	756	782
24		पुणे PUNE	0%	100%	0%	0%	1	801	742	776
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	4	806	765	784
26		सासन SASAN	0%	100%	0%	0%	0	796	768	780
27		सतना SATNA	0%	99%	1%	1%	6	805	767	785
28		सिवनी SEONI	0%	100%	0%	0%	1	802	757	781
29		सीपत SIPAT	0%	100%	0%	0%	0	787	756	771
30		सोलापुर SOLAPUR	0%	100%	0%	0%	0	797	759	781
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	778	748	763
32		तामनार TAMNAR	0%	100%	0%	0%	0	797	768	782
33		वड़ोदरा VADODARA	0%	100%	0%	0%	0	798	740	771
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	800	770	783
35		वर्धा WARDHA	0%	100%	0%	0%	0	802	753	780
36		वरोरा WARORA	0%	100%	0%	0%	2	804	759	783
1		अरियलूर ARIYALUR	0%	100%	0%	0%	0	793	749	772
2		कड़पा CUDDAPAH	0%	99%	1%	1%	5	804	752	781
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	100%	0%	0%	3	803	750	781
4		कर्नूल KURNOOL	0%	99%	1%	1%	10	805	757	781
5		महेश्वरम MAHESWARAM	0%	94%	6%	6%	42	808	765	788
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	94%	6%	6%	43	805	768	790
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	796	757	778
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	0	801	751	778
9		रायचूर RAICHUR	0%	100%	0%	0%	0	800	761	781
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	0	800	762	783
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	789	737	770
12		वेमगिरी VEMAGIRI	0%	97%	3%	3%	23	802	756	782
13		वारंगल WARANGAL	0%	95%	5%	5%	38	807	765	789
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	411	394	403
2		बिस्वनाथ चरिआलि BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	416	396	406
3		बोंगाईगाव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	414	401	409
4		बोंगाईगाव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	417	403	411
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	416	394	406
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	1	421	403	414
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	410	396	403
8	पूर्वोत्तर क्षेत्र NER	अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	411	402	407
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	412	394	404
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	416	399	407
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	418	387	406
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	413	401	407
13		पबंकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	413	393	402
14		रंगानदी RANGANADI (400 kV)	0%	100%	0%	0%	0	415	396	407
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	396	408
16		सुर्ज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	410	393	402
17		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	414	392	403

All listed stations are 765 kV stations unless otherwise mentione
***Percentage is calculated w.r.t. Time of one month**

23.ALL TIME HIGHEST

31-10-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	186 01-05-2024
WR	74974 01-06-2024	67482 30-05-2024	1648 06-05-2024	167 18-12-2014	310 28-05-2024	105.61 07-10-2024
SR	68735 13-03-2024	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	323 26-07-2024	148.7 31-03-2024
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	4 09-06-2024
NER	3905 19-09-2024	3787 19-09-2024	80 20-09-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	426 30-04-2024

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	17949	20-01-2024	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	2235	20-01-2024	41.2	26-06-2024
	J&K(UT) and Ladakh(UT)	3107	12-01-2024	66.8	26-01-2024
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	17819	29-12-2023	335.9	10-11-2023
	Maharashtra	28969	07-02-2024	648.3	30-04-2024
	Goa	803	19-04-2024	17.6	18-05-2024
	DD & DNH	1390	23-10-2024	32.6	16-10-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	15623	08-03-2024	311.0	13-03-2024
	Karnataka	17220	12-03-2024	336.9	05-04-2024
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	8001	23-09-2024	172.8	30-07-2024
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26-05-2024	3.9	18-06-2024
	Assam	2687	20-09-2024	55.8	20-09-2024
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.4	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24. System Reliability Indices Report for the month of OCTOBER 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	87	21.75	2.92
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	25	6.25	0.84
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
