ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre
कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या : - GRID-INDIA/NLDC/MR/ दिनांक : 23.10.2024

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **सितम्बर 2024**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **सितम्बर 2024** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
वरिष्ठ महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



सितम्बर 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह सितम्बर 2024 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF SEPTEMBER -2024


पृष्ठसूची CONTENTS

1	माह अगस्त 2024 की सारांश रिपोर्ट Summary of report for the month of SEPTEMBER 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	23 सितम्बर के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 23-SEPTEMBER (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह सितम्बर 2023 से तुलना Energy requirement and met comparison with SEPTEMBER 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह सितम्बर 2023 से तुलना Peak demand requirement and met comparison with SEPTEMBER 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-37
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	38-40
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	41
18	पावर मार्केट की सूचना Power market information	42-46
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	47-49
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	50-61
21	नए कमीशंड पारेषण तत्व New elements commissioned	62
22	विभव रूपरेखा Voltage profile	63
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह सितम्बर 2024 तक All Time Highest (Demand & Energy) figures: Till SEPTEMBER 2024	64
24	सितम्बर 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for SEPTEMBER 2024	65

1. SUMMARY OF REPORT FOR THE MONTH OF SEPTEMBER-2024


EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

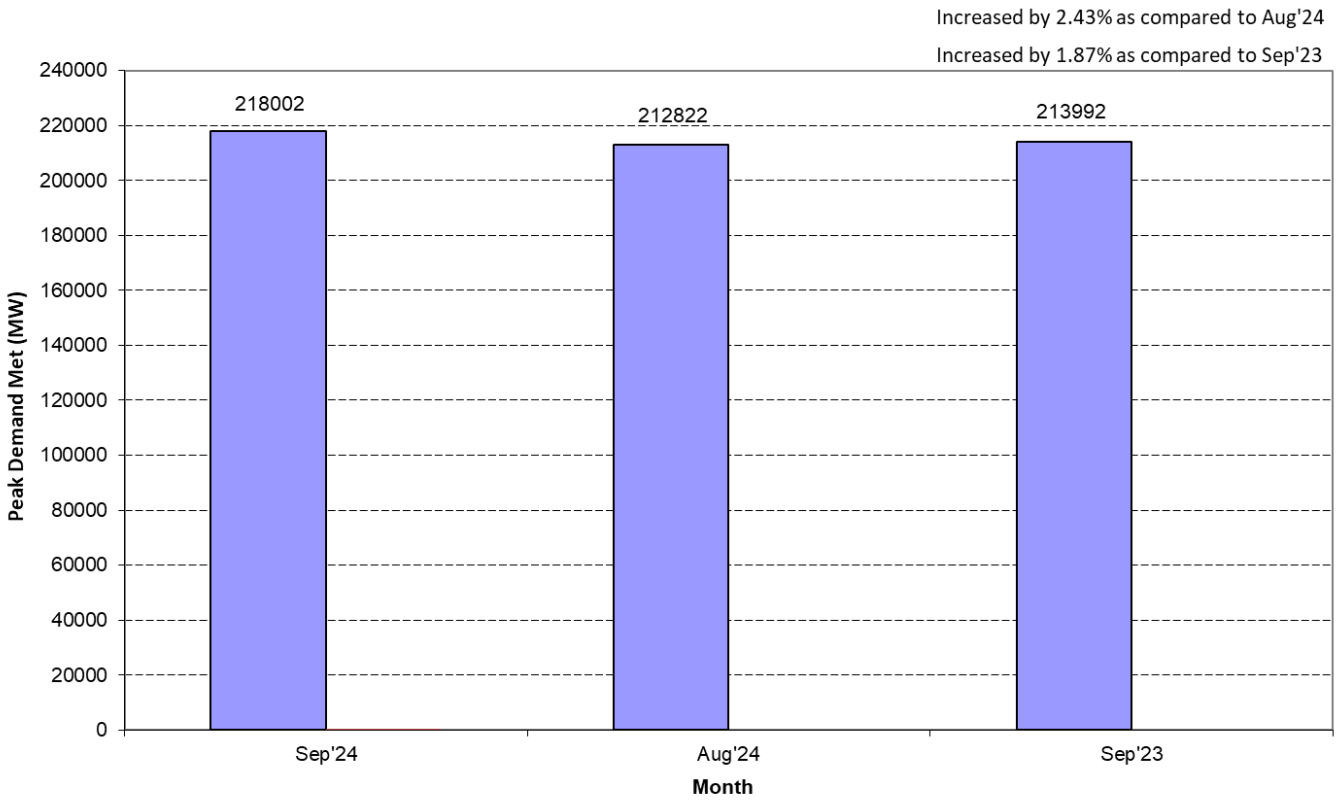


Frequency within IEGC Band

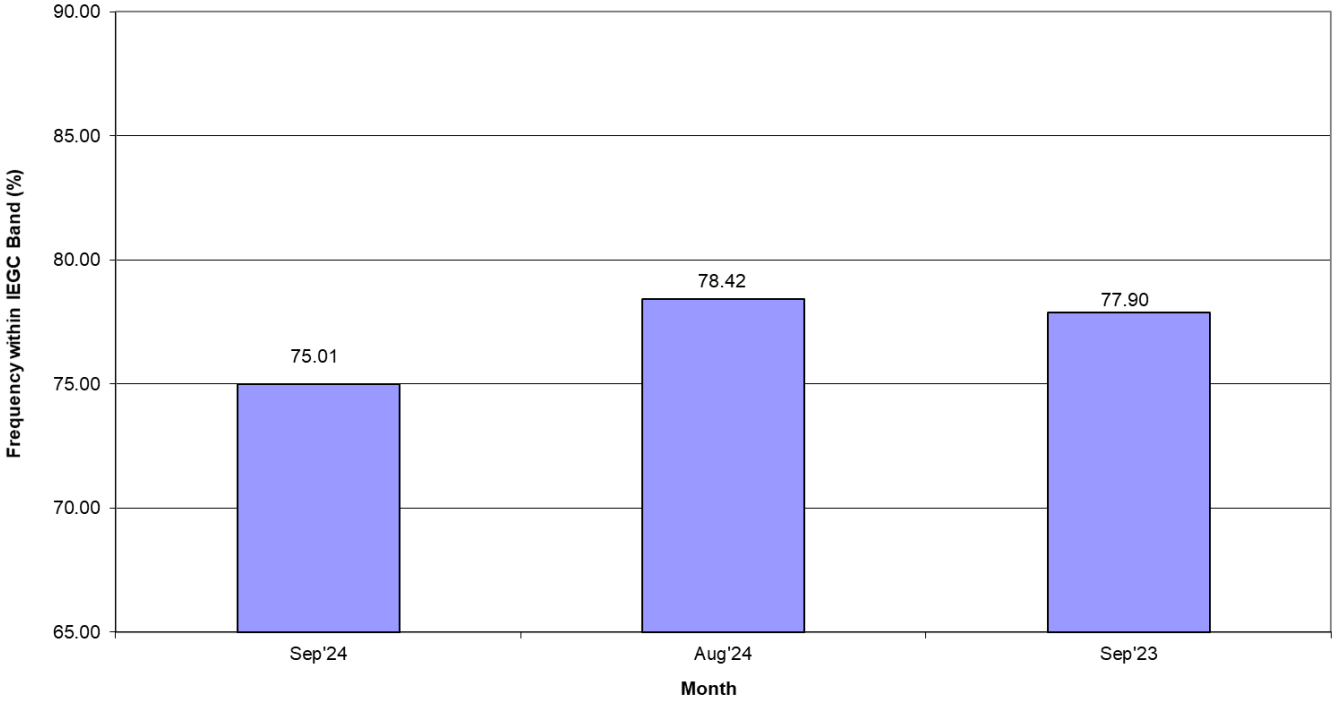


ENERGY MET AT NATIONAL LEVEL (MU)

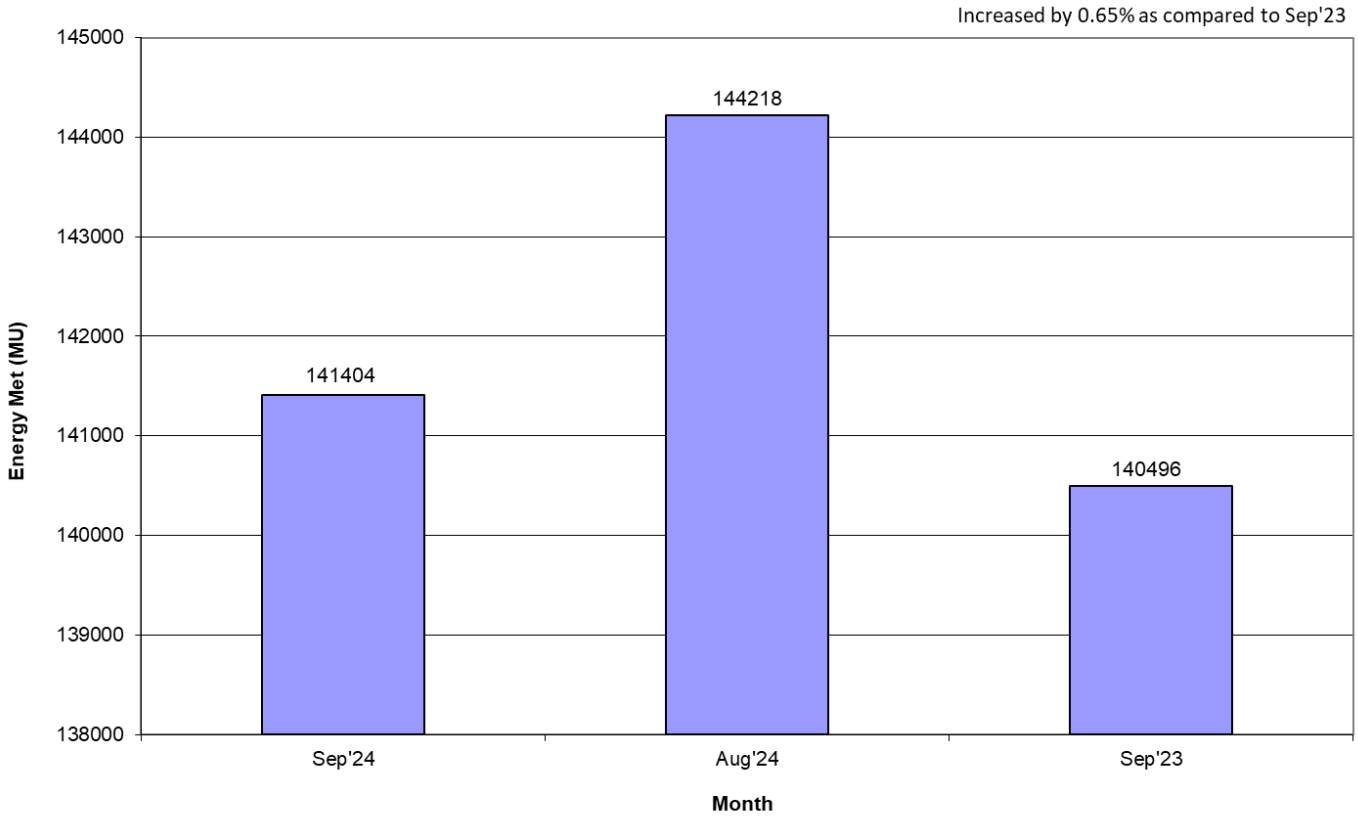


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

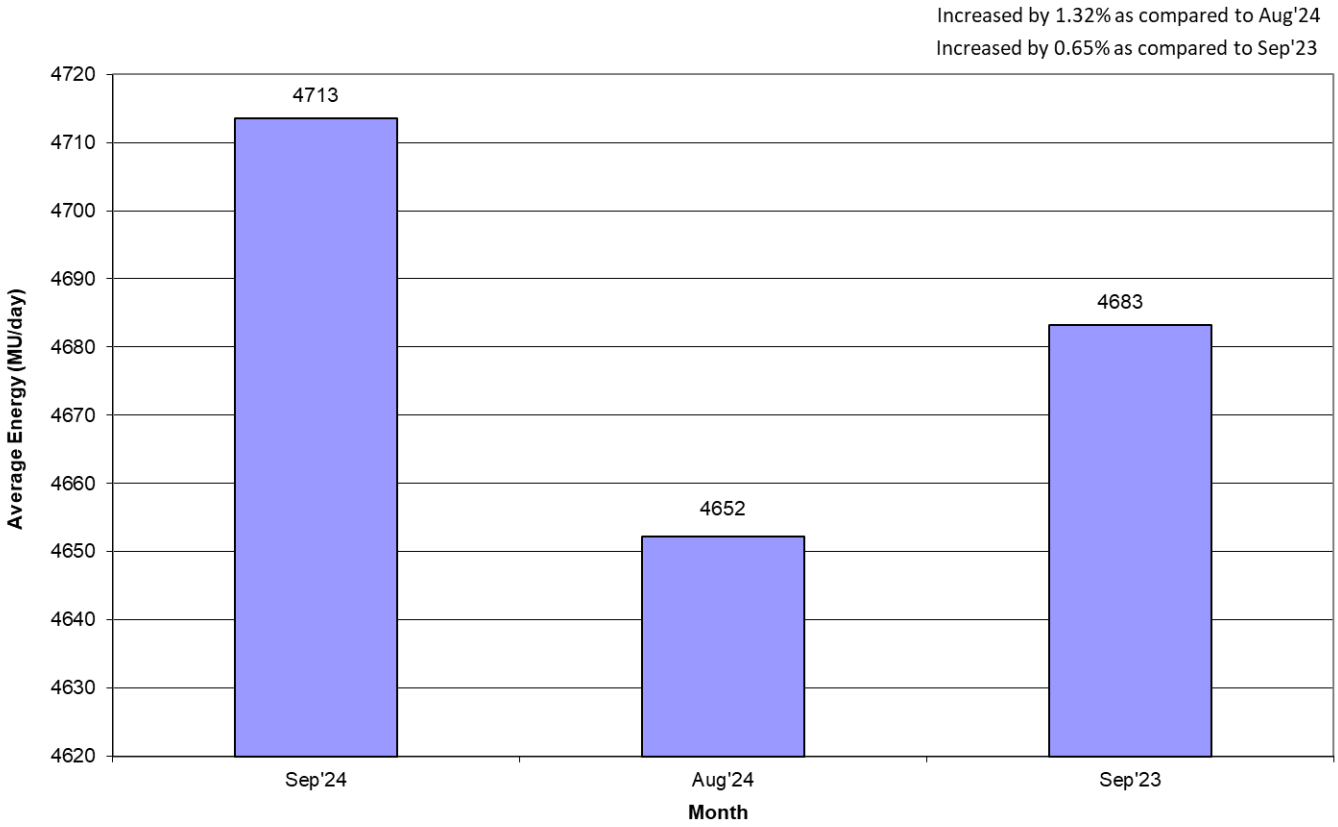


HYDRO GENERATION AT NATIONAL LEVEL (MU)

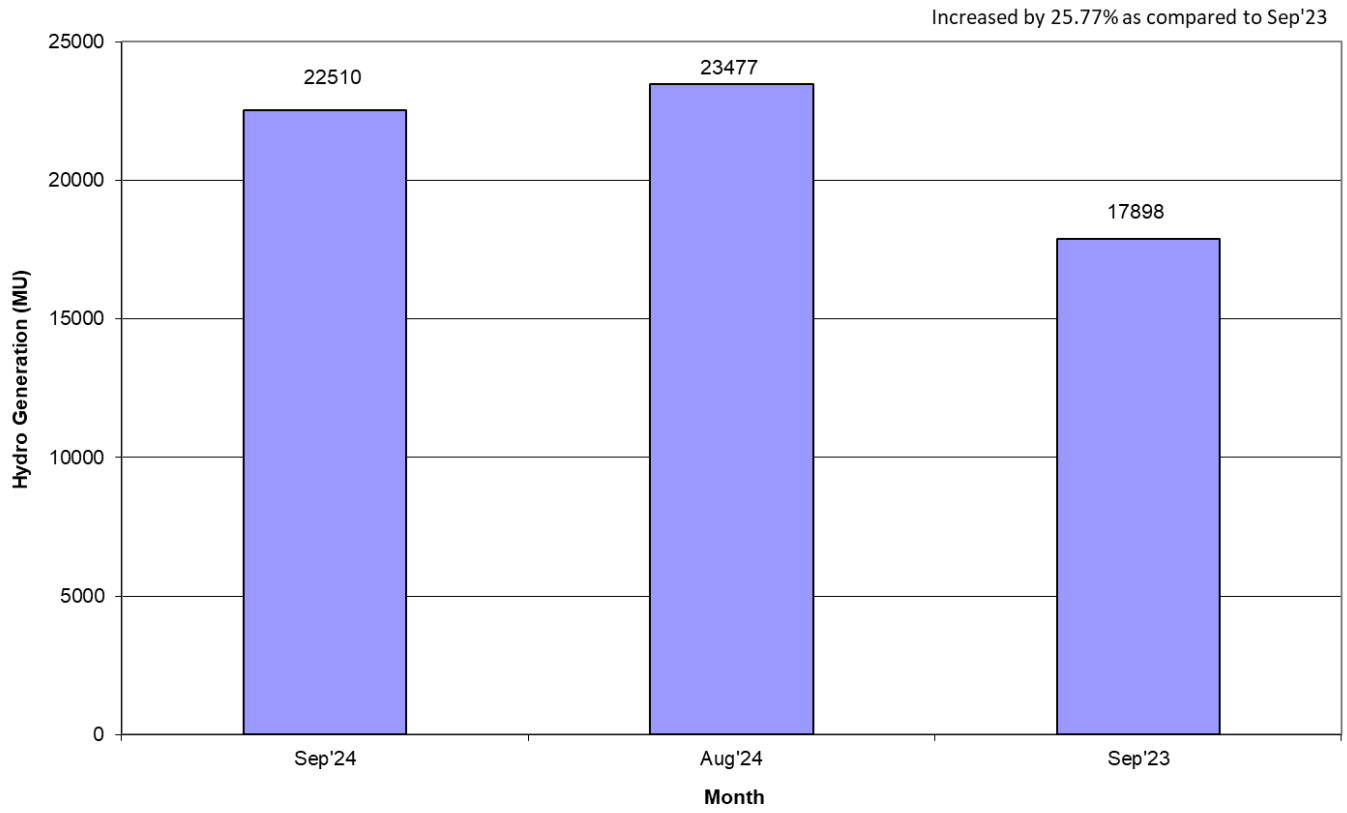


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

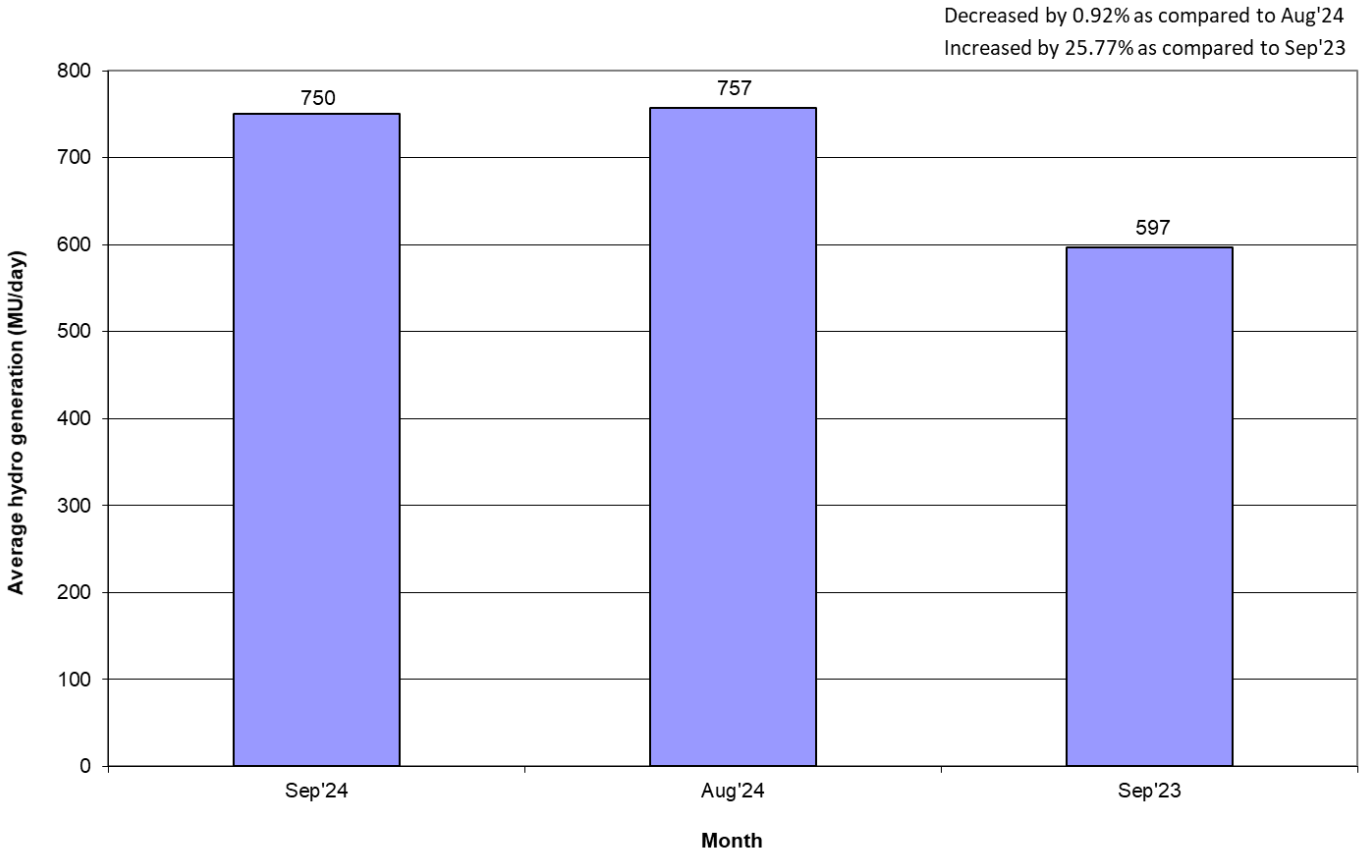


WIND GENERATION AT NATIONAL LEVEL (MU)

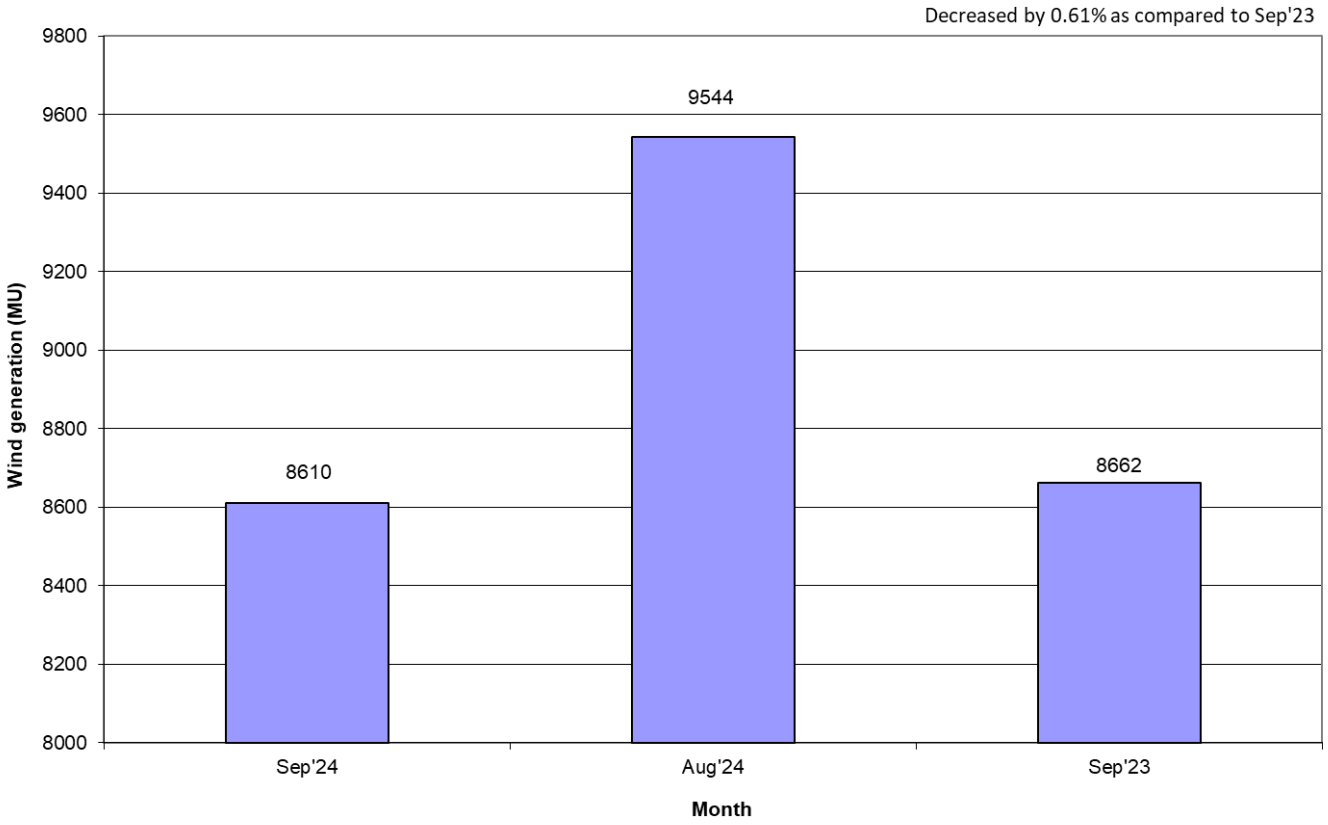


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

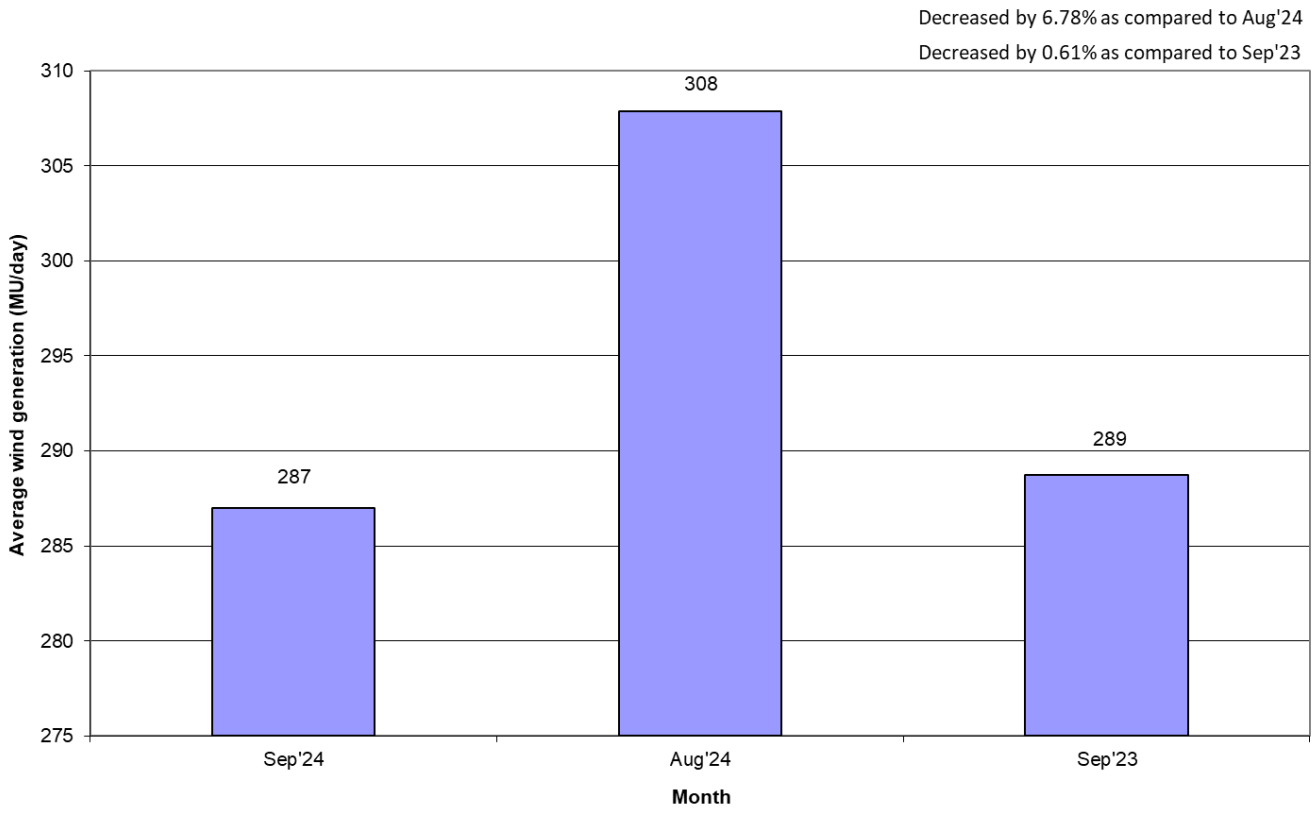

SOLAR GENERATION AT NATIONAL LEVEL (MU)

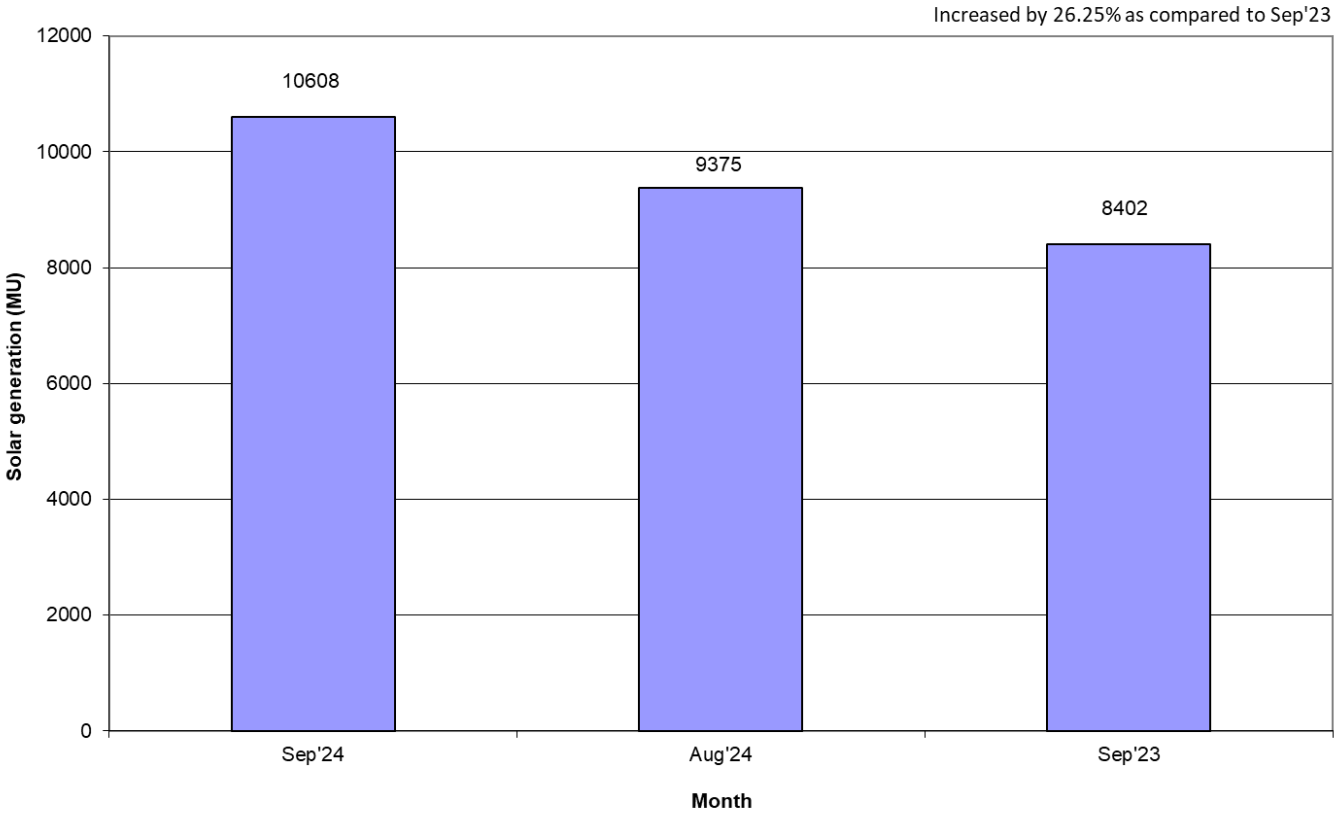

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

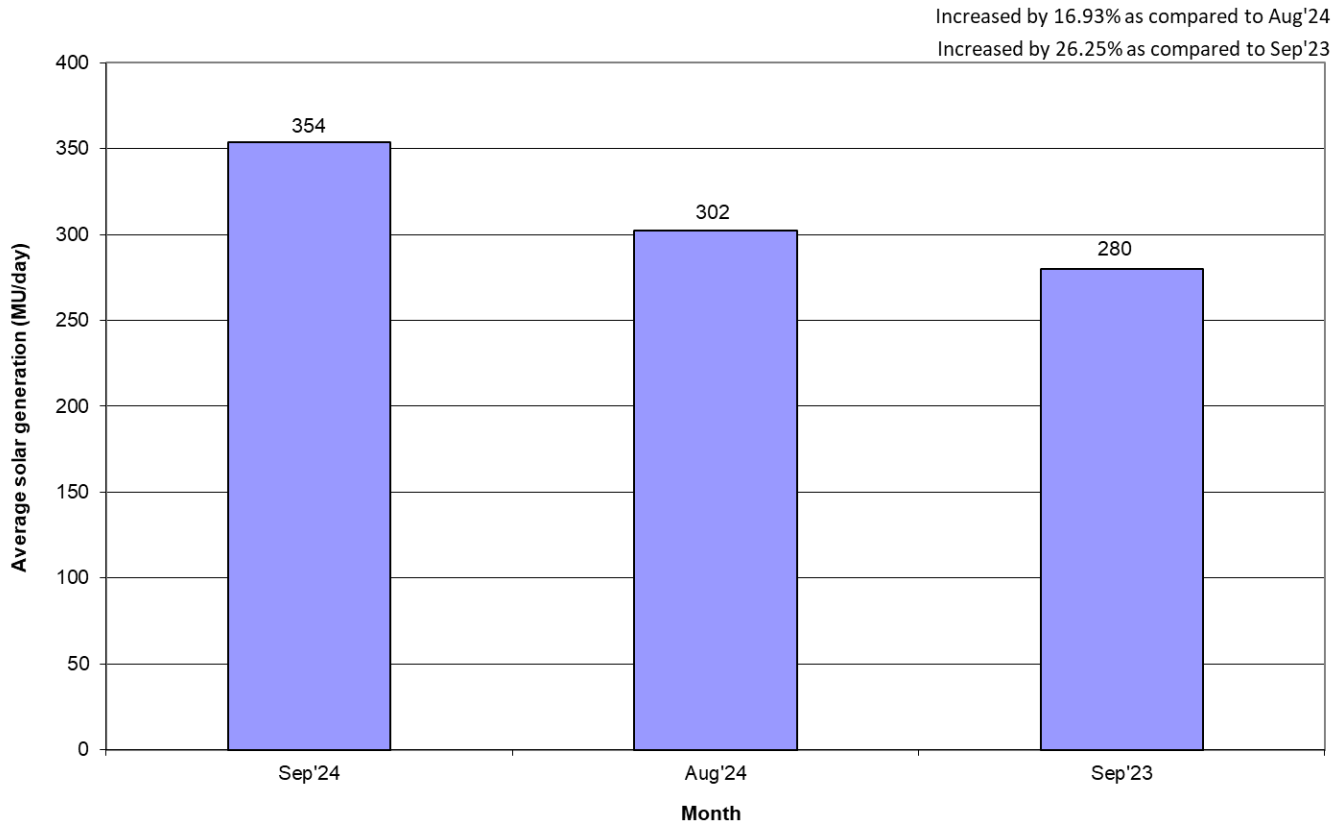

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 30.09.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56658	1580	5995	0	64233	1620	20830	42418	129101
2	WR	74663	1400	10806	0	86869	3240	7563	52586	150258
3	SR	49415	3640	6272	434	59760	3320	11827	56616	131524
4	ER	29052	0	80	0	29132	0	4764	2257	36153
5	NER	1242	0	1665	36	2943	0	1944	613	5500
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	211030	6620	24818	589	243057	8180	46928	154530	452695

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति

EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: सितंबर 2024 MONTH:- SEP 2024


सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Sep-24	73224	53391	39211	26514	3381	195721
2-Sep-24	73457	55500	44287	28058	3516	204818
3-Sep-24	70261	57654	45113	28335	3451	204814
4-Sep-24	67531	57900	46257	28365	3417	203470
5-Sep-24	70492	56789	46958	28369	3532	206140
6-Sep-24	68458	57202	45933	29364	3631	204588
7-Sep-24	69315	54844	42198	28528	3704	198589
8-Sep-24	68908	55420	40098	27176	3543	195145
9-Sep-24	71230	56627	47205	27982	3602	206646
10-Sep-24	71230	56627	47205	27982	3602	206646
11-Sep-24	68198	54808	47779	28764	3412	202961
12-Sep-24	61779	56152	49151	29527	3622	200231
13-Sep-24	62062	56982	48697	27170	3554	198465
14-Sep-24	66870	57816	47786	23336	3347	199155
15-Sep-24	66832	56266	43901	21621	3318	191938
16-Sep-24	71327	58335	48255	22037	3523	203477
17-Sep-24	65755	53396	49732	24297	3536	196716
18-Sep-24	61801	59061	50733	27006	3668	202269
19-Sep-24	65549	62511	50987	28428	3787	211262
20-Sep-24	68266	62866	49761	29134	3753	213780
21-Sep-24	71071	63275	47221	28577	3488	213632
22-Sep-24	71507	59422	44070	29415	3413	207827
23-Sep-24	72711	63003	48358	28325	3445	215842
24-Sep-24	77553	62210	47115	27795	3329	218002
25-Sep-24	76427	58193	47567	25503	3136	210826
26-Sep-24	72698	57390	47985	22778	3101	203952
27-Sep-24	65812	56090	48104	24058	3135	197199
28-Sep-24	63455	56070	47999	25258	3073	195855
29-Sep-24	65535	55907	45076	27272	2979	196769
30-Sep-24	72154	59494	48962	29029	3307	212946
उच्चतम MAXIMUM	77553	63275	50987	29527	3787	218002
निम्नतम MINIMUM	61779	53391	39211	21621	2979	191938
औसत AVERAGE	69049	57707	46790	27000	3444	203989
अब तक का उच्चतम All Time Max.	82312	67482	54798	29695	**3787**	227354
दिनांक Date	23.07.24	30.05.24	29.04.24	29.05.24	**19.09.24**	29.05.24

नोट : सभी आंकड़े 2000 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND(at 2000hrs) MET DURING THE MONTH OF SEPTEMBER' 2024

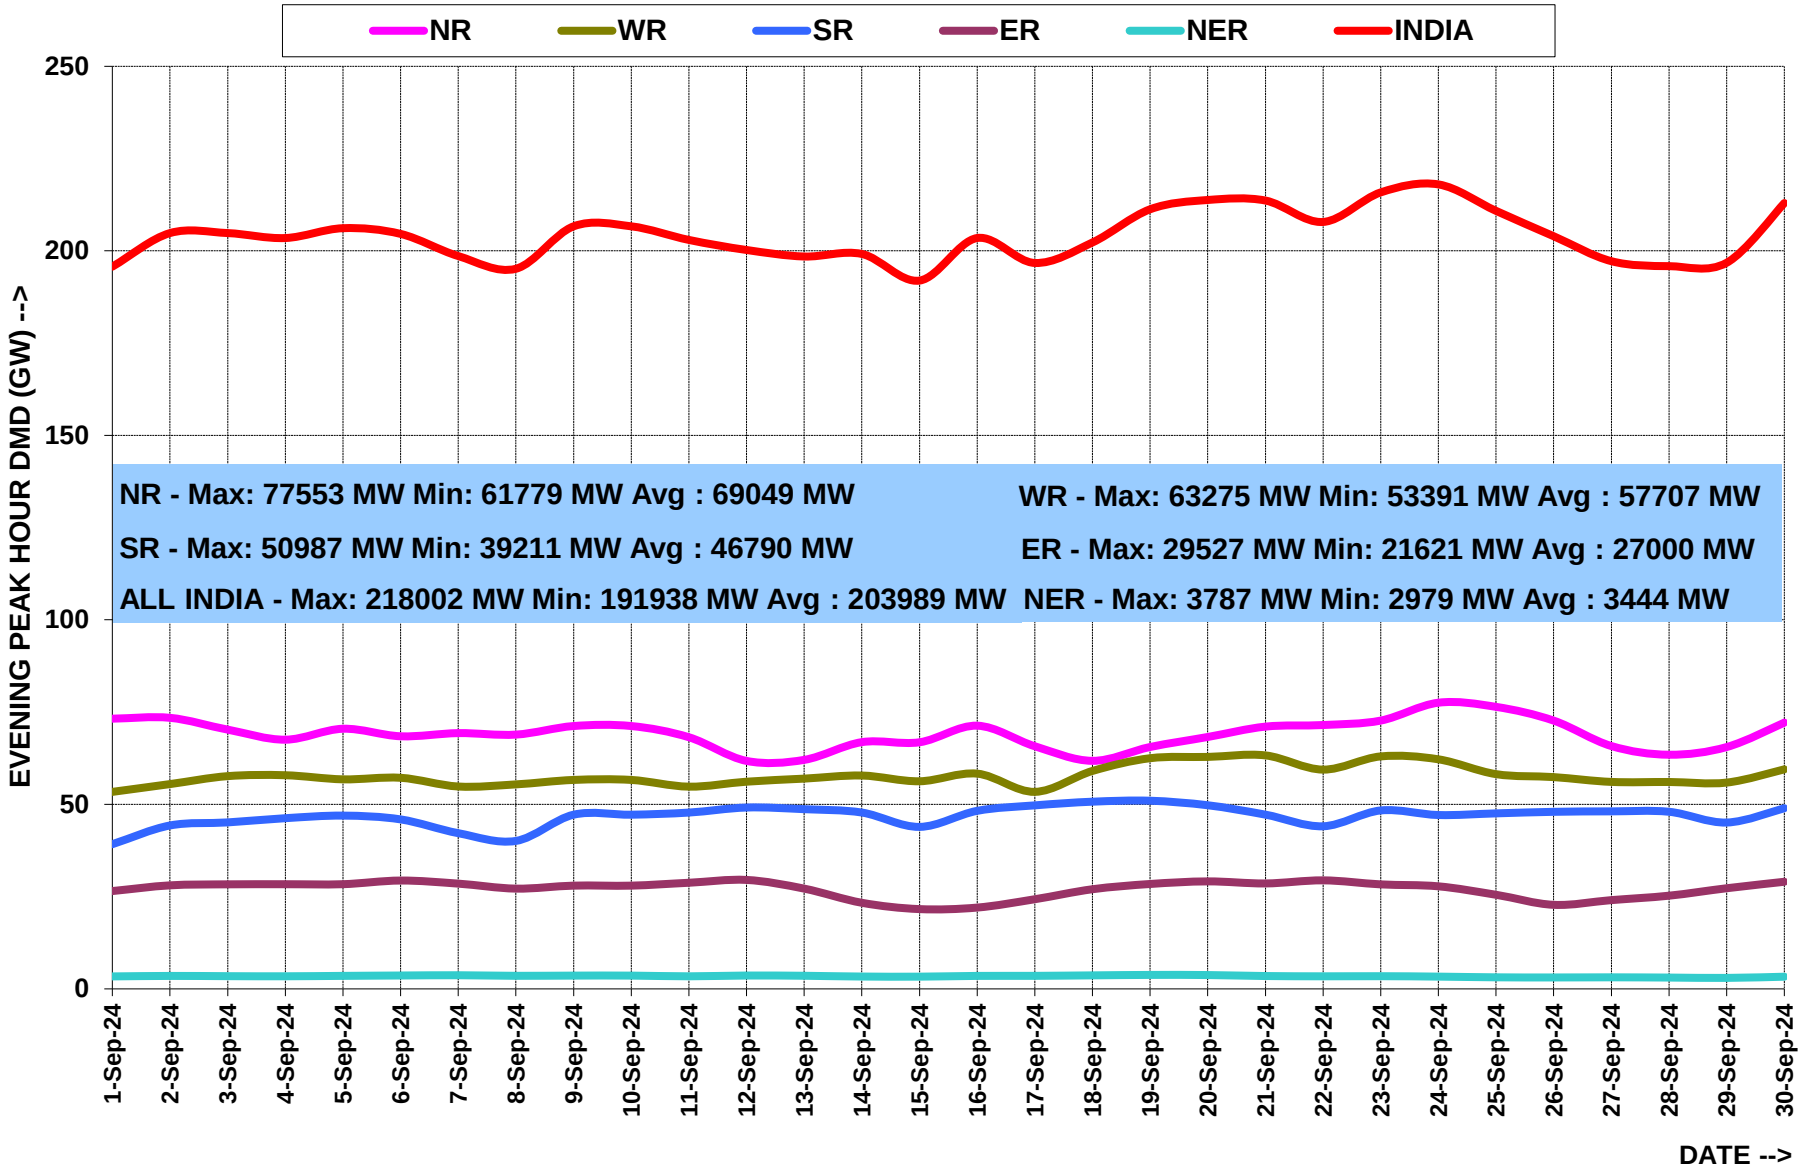


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: सितंबर 2024 MONTH:- SEP 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Sep-24	1627	1271	895	584	65	4443
02-Sep-24	1655	1314	988	608	70	4635
03-Sep-24	1625	1321	1029	624	70	4669
04-Sep-24	1476	1330	1056	624	67	4552
05-Sep-24	1505	1330	1075	608	65	4582
06-Sep-24	1512	1324	1111	627	72	4646
07-Sep-24	1508	1300	1049	642	73	4571
08-Sep-24	1488	1295	973	613	73	4442
09-Sep-24	1578	1349	1102	617	74	4720
10-Sep-24	1578	1349	1102	617	74	4720
11-Sep-24	1514	1304	1159	629	65	4671
12-Sep-24	1423	1297	1200	638	71	4629
13-Sep-24	1378	1338	1235	623	71	4645
14-Sep-24	1441	1355	1238	519	70	4623
15-Sep-24	1456	1342	1180	468	68	4514
16-Sep-24	1528	1384	1257	449	69	4686
17-Sep-24	1506	1320	1292	492	70	4680
18-Sep-24	1440	1363	1312	561	75	4751
19-Sep-24	1433	1446	1328	616	79	4901
20-Sep-24	1501	1500	1330	648	80	5059
21-Sep-24	1605	1504	1230	643	76	5059
22-Sep-24	1625	1455	1140	636	74	4930
23-Sep-24	1703	1497	1192	643	74	5109
24-Sep-24	1797	1479	1159	604	66	5106
25-Sep-24	1793	1434	1127	555	64	4975
26-Sep-24	1676	1372	1131	515	56	4750
27-Sep-24	1529	1333	1167	506	61	4596
28-Sep-24	1430	1297	1196	534	60	4516
29-Sep-24	1418	1289	1133	565	59	4464
30-Sep-24	1540	1351	1200	610	62	4762
कुल TOTAL	46289	40841	34587	17616	2071	141404
उच्चतम MAXIMUM	1797	1504	1330	648	80	5109
निम्नतम MINIMUM	1378	1271	895	449	56	4442
औसत AVERAGE	1543	1361	1153	587	69	4713
संचयी 2024-25 Cumulative 2024-25	292366	262635	212495	110313	11385	889193
अब तक का उच्चतम All Time Max.	1990	1648	1416	692	80	5466
दिनांक Date	18.06.24	06.05.24	05.04.24	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF SEPTEMBER' 2024

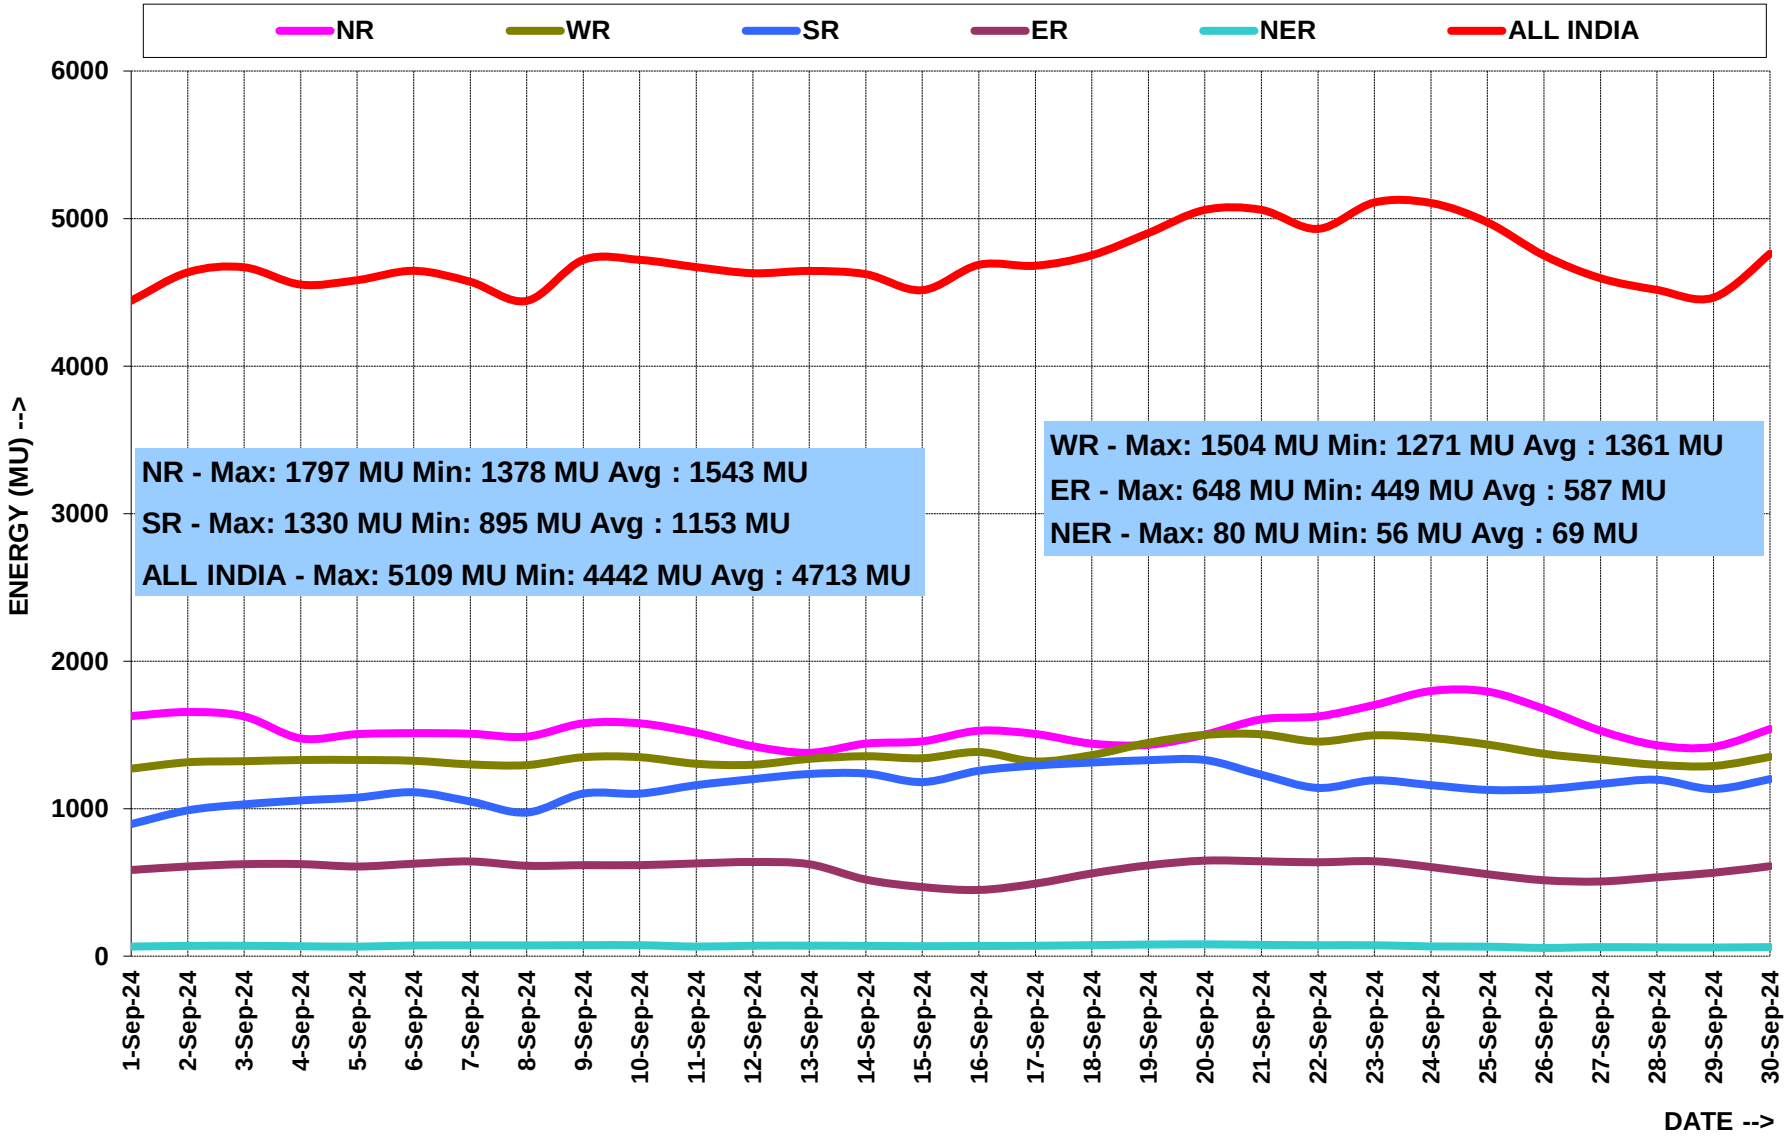

5. वर्ष 2024-25 के लिए आवृति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78		50.38	49.46	50.00
	2024-25 (upto Sep)	All India Grid	**4.89**	**78.05**	**17.05**		**50.67**	**49.46**	**50.00**

5.1 सितंबर 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR SEPTEMBER 2024

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Sep-24	3.65	79.57	16.78		50.31	49.69	50.01	0.06
	02-Sep-24	6.93	78.22	14.85		50.25	49.62	50.00	0.05
	03-Sep-24	5.93	81.08	13.00		50.14	49.62	49.99	0.04
	04-Sep-24	2.63	73.48	23.89		50.26	49.84	50.01	0.04
	05-Sep-24	2.59	74.94	22.47		50.30	49.85	50.01	0.05
	06-Sep-24	6.20	75.46	18.33		50.25	49.78	50.01	0.04
	07-Sep-24	2.71	71.98	25.31		50.22	49.84	50.02	0.03
	08-Sep-24	4.06	67.36	28.58		50.29	49.81	50.03	0.08
	09-Sep-24	3.91	75.72	20.37		50.25	49.78	50.01	0.04
	10-Sep-24	3.69	73.52	22.79		50.35	49.73	50.02	0.06
	11-Sep-24	1.24	86.03	12.73		50.15	49.88	50.01	0.02
	12-Sep-24	1.09	82.30	16.61		50.27	49.86	50.01	0.03
	13-Sep-24	6.96	72.43	20.61		50.31	49.79	50.00	0.05
	14-Sep-24	4.31	71.98	23.72		50.38	49.77	50.01	0.07
	15-Sep-24	1.28	74.40	24.32		50.32	49.84	50.02	0.07
	16-Sep-24	5.67	77.09	17.23		50.20	49.68	50.00	0.04
	17-Sep-24	3.70	83.73	12.57		50.16	49.79	49.99	0.03
	18-Sep-24	15.68	78.11	6.20		50.15	49.46	49.96	0.09
	19-Sep-24	12.96	74.63	12.41		50.18	49.64	49.98	0.07
	20-Sep-24	12.63	76.11	11.26		50.18	49.65	49.98	0.05
	21-Sep-24	6.94	82.87	10.19		50.18	49.82	49.99	0.03
	22-Sep-24	17.55	73.62	8.83		50.15	49.67	49.97	0.07
	23-Sep-24	14.72	73.00	12.28		50.12	49.65	49.98	0.05
	24-Sep-24	3.66	73.69	22.65		50.14	49.78	50.01	0.03
	25-Sep-24	4.63	83.50	11.88		50.17	49.84	50.00	0.03
	26-Sep-24	6.35	76.72	16.92		50.23	49.79	50.00	0.03
	27-Sep-24	5.35	78.56	16.09		50.19	49.72	50.00	0.03
	28-Sep-24	9.44	79.68	10.88		50.16	49.79	49.98	0.04
	29-Sep-24	1.42	84.28	14.29		50.18	49.86	50.01	0.02
	30-Sep-24	4.86	79.72	15.42		50.21	49.60	50.00	0.04

6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन


HYDRO GENERATION AT NATIONAL LEVEL

माह: सितंबर 2024 MONTH:- SEP 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Sep-24	374	109	142	86	30	741
02-Sep-24	375	105	159	89	31	760
03-Sep-24	402	119	166	92	32	811
04-Sep-24	397	115	172	91	31	807
05-Sep-24	401	113	179	90	31	813
06-Sep-24	400	117	177	92	31	817
07-Sep-24	396	112	172	92	28	800
08-Sep-24	390	110	164	89	27	781
09-Sep-24	383	115	176	92	29	795
10-Sep-24	383	115	176	92	29	795
11-Sep-24	375	115	177	92	29	789
12-Sep-24	359	119	179	95	30	781
13-Sep-24	350	117	179	93	27	765
14-Sep-24	366	112	170	93	29	770
15-Sep-24	362	106	160	95	29	752
16-Sep-24	358	113	171	98	28	769
17-Sep-24	340	107	170	101	28	747
18-Sep-24	335	120	174	93	28	751
19-Sep-24	348	131	155	91	28	753
20-Sep-24	335	133	154	93	28	742
21-Sep-24	322	128	139	95	27	711
22-Sep-24	314	118	142	94	26	694
23-Sep-24	321	122	154	88	26	712
24-Sep-24	318	119	148	89	27	699
25-Sep-24	317	110	151	88	28	693
26-Sep-24	318	112	161	92	27	711
27-Sep-24	314	107	156	96	28	702
28-Sep-24	307	107	161	89	30	694
29-Sep-24	284	105	153	98	31	671
30-Sep-24	281	106	172	97	28	683
कुल TOTAL	10525	3439	4908	2776	863	22510
उच्चतम MAXIMUM	402	133	179	101	32	817
निम्नतम MINIMUM	281	105	139	86	26	671
औसत AVERAGE	351	115	164	93	29	750
संचयी 2024-25 Cumulative 2024-25	57469	11902	17561	10603	4936	102471
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

HYDRO ENERGY DURING THE MONTH OF SEPTEMBER' 2024

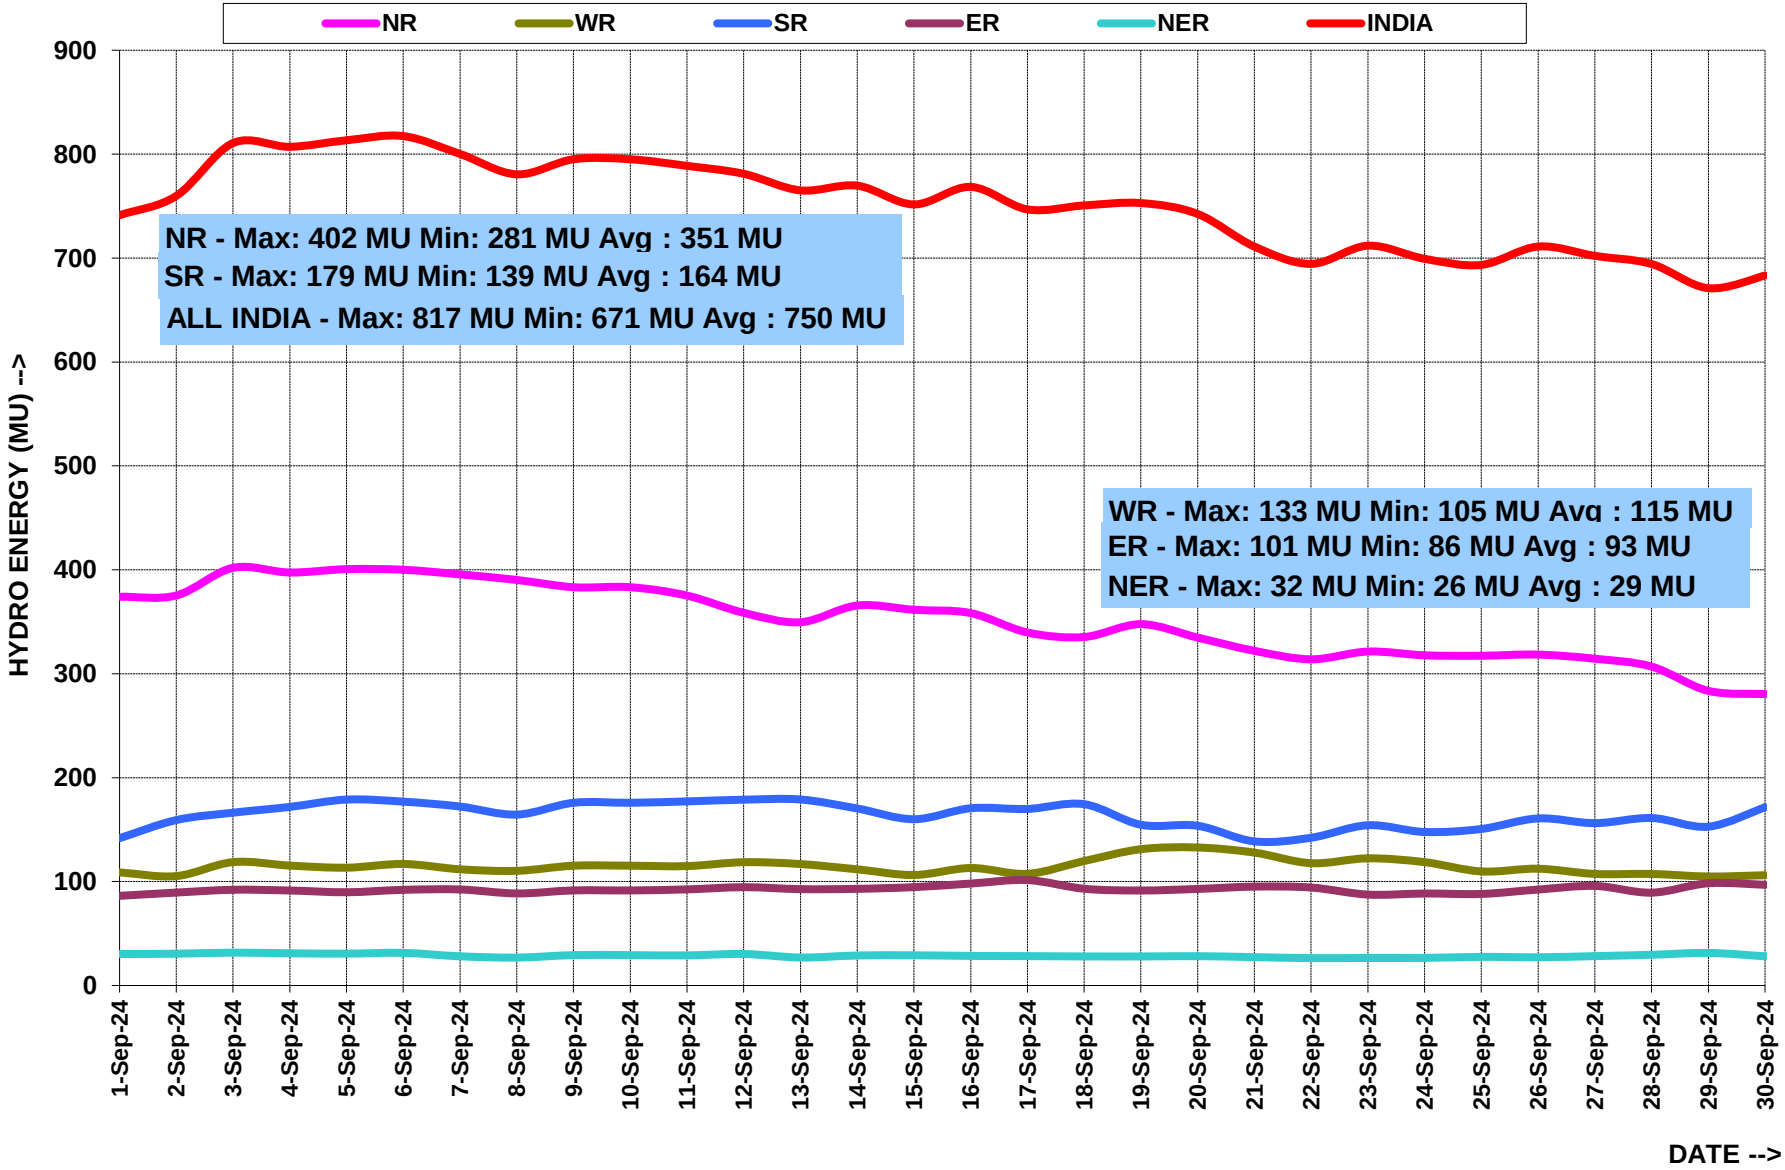

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन

WIND GENERATION AT NATIONAL LEVEL

माह: सितंबर 2024 MONTH:- SEP 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Sep-24	7	80	238	----------	----------	325
02-Sep-24	6	75	241	----------	----------	322
03-Sep-24	8	65	242	----------	----------	315
04-Sep-24	2	100	244	----------	----------	347
05-Sep-24	7	138	220	----------	----------	365
06-Sep-24	11	112	224	----------	----------	347
07-Sep-24	13	83	212	----------	----------	308
08-Sep-24	13	74	228	----------	----------	315
09-Sep-24	10	101	263	----------	----------	374
10-Sep-24	10	101	263	----------	----------	374
11-Sep-24	13	109	225	----------	----------	346
12-Sep-24	35	154	192	----------	----------	382
13-Sep-24	59	157	177	----------	----------	392
14-Sep-24	48	131	182	----------	----------	361
15-Sep-24	20	115	201	----------	----------	336
16-Sep-24	17	91	185	----------	----------	293
17-Sep-24	10	81	175	----------	----------	265
18-Sep-24	11	68	147	----------	----------	226
19-Sep-24	22	65	151	----------	----------	238
20-Sep-24	5	76	156	----------	----------	236
21-Sep-24	9	71	181	----------	----------	260
22-Sep-24	14	66	160	----------	----------	241
23-Sep-24	10	62	176	----------	----------	248
24-Sep-24	11	72	187	----------	----------	269
25-Sep-24	9	76	212	----------	----------	297
26-Sep-24	12	90	174	----------	----------	276
27-Sep-24	9	130	132	----------	----------	270
28-Sep-24	17	85	44	----------	----------	146
29-Sep-24	3	35	30	----------	----------	68
30-Sep-24	9	40	18	----------	----------	67
कुल TOTAL	428	2704	5477	----------	----------	8610
उच्चतम MAXIMUM	59	157	263	----------	----------	392
निम्नतम MINIMUM	2	35	18	----------	----------	67
औसत AVERAGE	14	90	183	----------	----------	287
संचयी 2024-25 Cumulative 2024-25	4355	23307	26618	----------	----------	54280
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: सितंबर 2024 MONTH:- SEP 2024

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Sep-24	149	76	72	2.5	1.0	301
02-Sep-24	138	59	107	3.2	1.2	308
03-Sep-24	105	49	107	3.5	1.1	266
04-Sep-24	97	69	105	3.5	1.0	276
05-Sep-24	143	67	121	2.3	0.9	335
06-Sep-24	149	71	117	3.3	1.2	342
07-Sep-24	163	73	113	3.0	1.3	354
08-Sep-24	165	81	94	2.4	1.3	344
09-Sep-24	155	65	124	2.3	1.0	347
10-Sep-24	155	65	124	2.3	1.0	347
11-Sep-24	152	59	135	3.1	0.7	349
12-Sep-24	158	74	135	3.0	1.1	371
13-Sep-24	167	81	137	2.8	1.2	389
14-Sep-24	167	87	137	1.7	1.1	393
15-Sep-24	168	88	138	2.2	1.0	397
16-Sep-24	171	91	139	1.4	1.2	404
17-Sep-24	171	85	139	1.7	1.2	398
18-Sep-24	160	86	142	3.2	1.1	392
19-Sep-24	150	93	143	3.5	1.3	391
20-Sep-24	153	93	135	3.5	1.2	386
21-Sep-24	157	88	112	3.2	1.0	361
22-Sep-24	166	87	119	3.2	1.2	377
23-Sep-24	167	88	115	2.9	1.2	374
24-Sep-24	164	79	105	2.5	0.8	351
25-Sep-24	157	78	99	2.0	0.8	338
26-Sep-24	155	67	107	1.9	0.5	330
27-Sep-24	149	61	114	2.3	1.0	327
28-Sep-24	146	65	118	3.8	0.8	334
29-Sep-24	159	70	120	3.2	0.5	353
30-Sep-24	162	87	121	3.5	0.6	374
कुल TOTAL	4619	2284	3593	82	31	10608
उच्चतम MAXIMUM	171	93	143	3.8	1.3	404
निम्नतम MINIMUM	97	49	72	1.4	0.5	266
औसत AVERAGE	154	76	120	2.7	1.0	354
संचयी 2024-25 Cumulative 2024-25	27819	14209	21037	534	174.5	63773
अब तक का उच्चतम All Time Max.	186	103	149	**4.1**	2.4	426
दिनांक Date	01.05.24	30.04.24	31.03.24	**09.06.24**	22.06.22	30.04.24

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: सितंबर 2024 MONTH:- SEP 2024

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फ़ैक्टर Diversity Factor*
01-Sep-24	75421	54481	39993	27923	3394	195901	1.027
02-Sep-24	74823	58426	47251	28690	3667	206355	1.032
03-Sep-24	74287	59224	47628	28761	3524	206761	1.032
04-Sep-24	67599	60263	49110	28840	3562	205849	1.017
05-Sep-24	70680	59750	49068	28545	3552	209151	1.012
06-Sep-24	69783	59926	52161	29806	3680	209261	1.029
07-Sep-24	69599	57301	50960	29372	3767	201232	1.049
08-Sep-24	69411	57115	46079	28946	3576	198487	1.033
09-Sep-24	72062	59486	50861	29201	3715	211214	1.019
10-Sep-24	72062	59486	50861	29201	3715	211214	1.019
11-Sep-24	69099	58073	53927	29396	3441	207171	1.033
12-Sep-24	64723	59855	56436	29929	3758	205187	1.046
13-Sep-24	63584	60639	58416	29227	3640	204090	1.056
14-Sep-24	68128	61660	58841	25649	3416	205159	1.061
15-Sep-24	67521	58727	56003	21931	3333	196192	1.058
16-Sep-24	71369	61791	61429	22213	3635	209172	1.054
17-Sep-24	67205	57542	62367	24577	3616	207620	1.037
18-Sep-24	64983	61388	62899	27405	3853	213926	1.031
19-Sep-24	65976	64870	63014	29087	3905	217271	1.044
20-Sep-24	68639	67007	64870	30526	3855	227048	1.035
21-Sep-24	72036	67382	57466	29987	3545	224585	1.026
22-Sep-24	72429	63935	53482	30799	3531	216244	1.037
23-Sep-24	77092	66880	57182	30204	3548	230608	1.019
24-Sep-24	81472	64824	55210	28625	3364	226855	1.029
25-Sep-24	78897	63656	52518	26626	3194	218867	1.028
26-Sep-24	74898	60852	52714	24021	3127	208876	1.032
27-Sep-24	68579	59563	54502	25112	3303	205506	1.027
28-Sep-24	66104	59831	56479	25914	3240	203594	1.039
29-Sep-24	66737	58280	52655	27869	3131	200239	1.042
30-Sep-24	71693	62976	57493	29531	3381	214228	1.051
उच्चतम MAXIMUM	81472	67382	64870	30799	3905	230608	1.061
निम्नतम MINIMUM	63584	54481	39993	21931	3127	195901	1.012
औसत AVERAGE	70563	60840	54396	27931	3532	209929	1.035
अब तक का उच्चतम All Time Max.	91215	74974	68735	32531	**3905**	250070	
दिनांक Date	19.06.24	01.06.24	13.03.24	10.06.24	**19.09.24**	30.05.24	


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 23 SEP (MAXIMUM DEMAND MET)

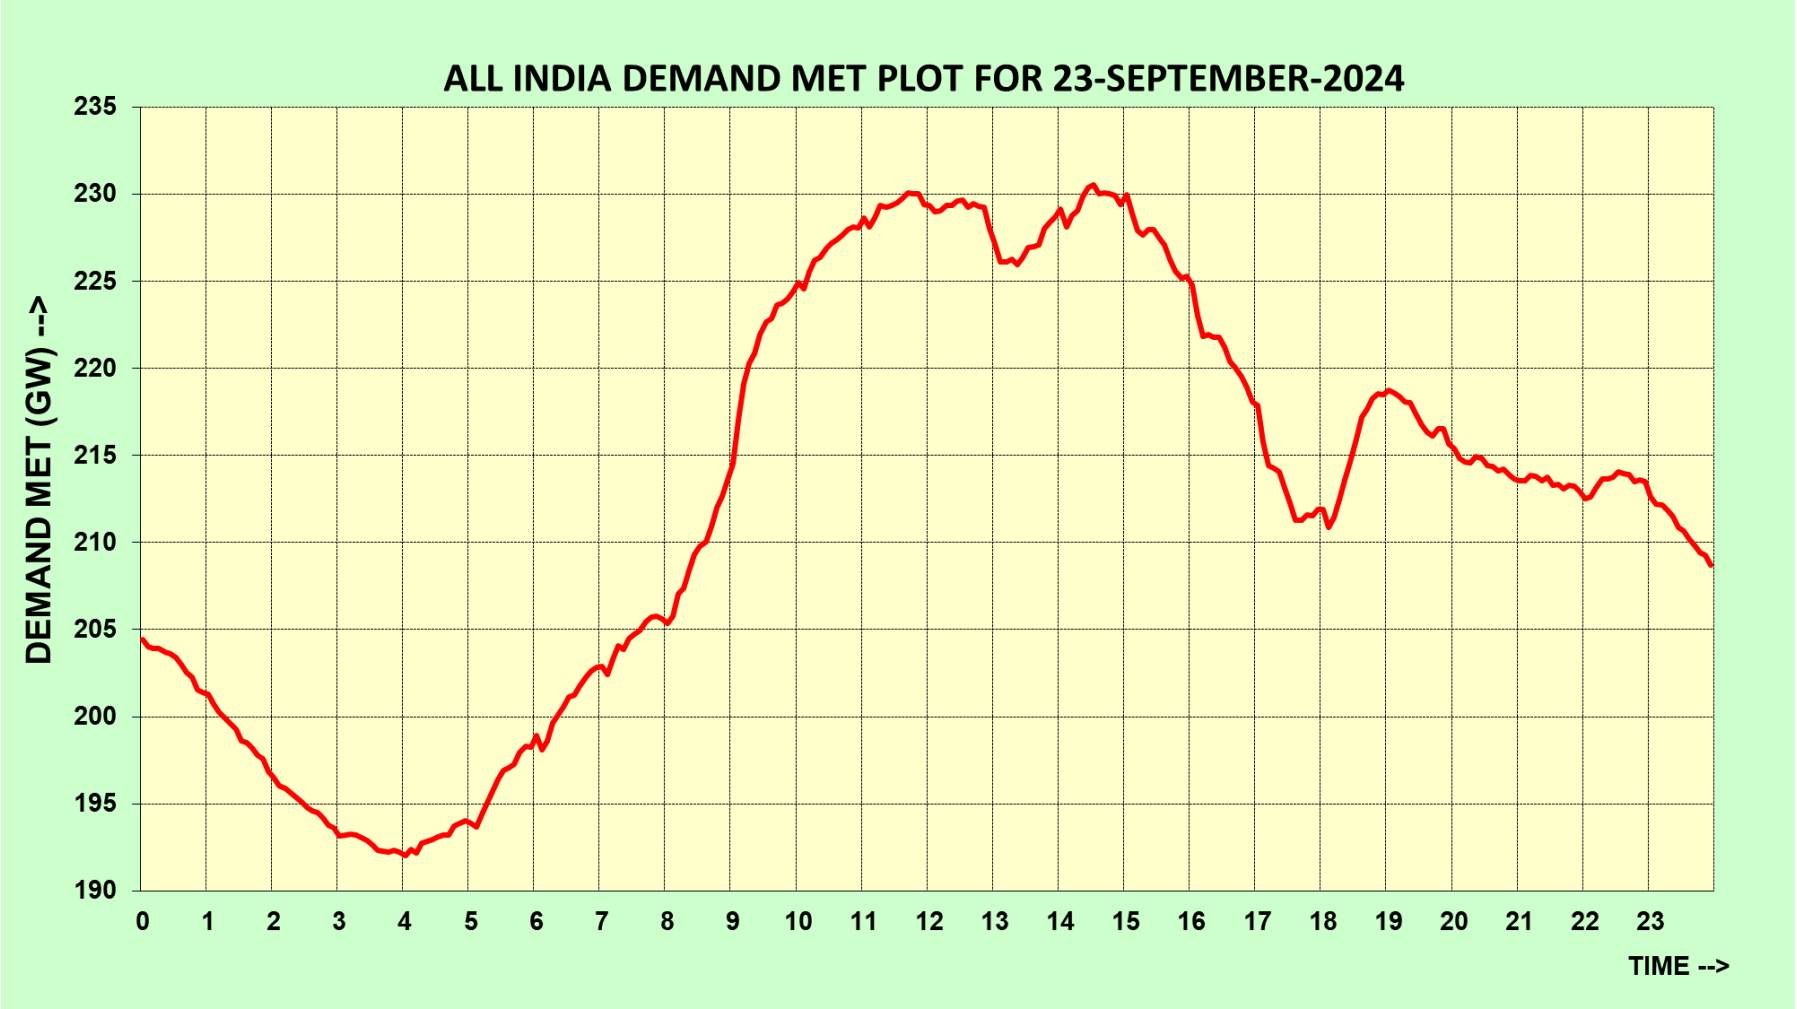

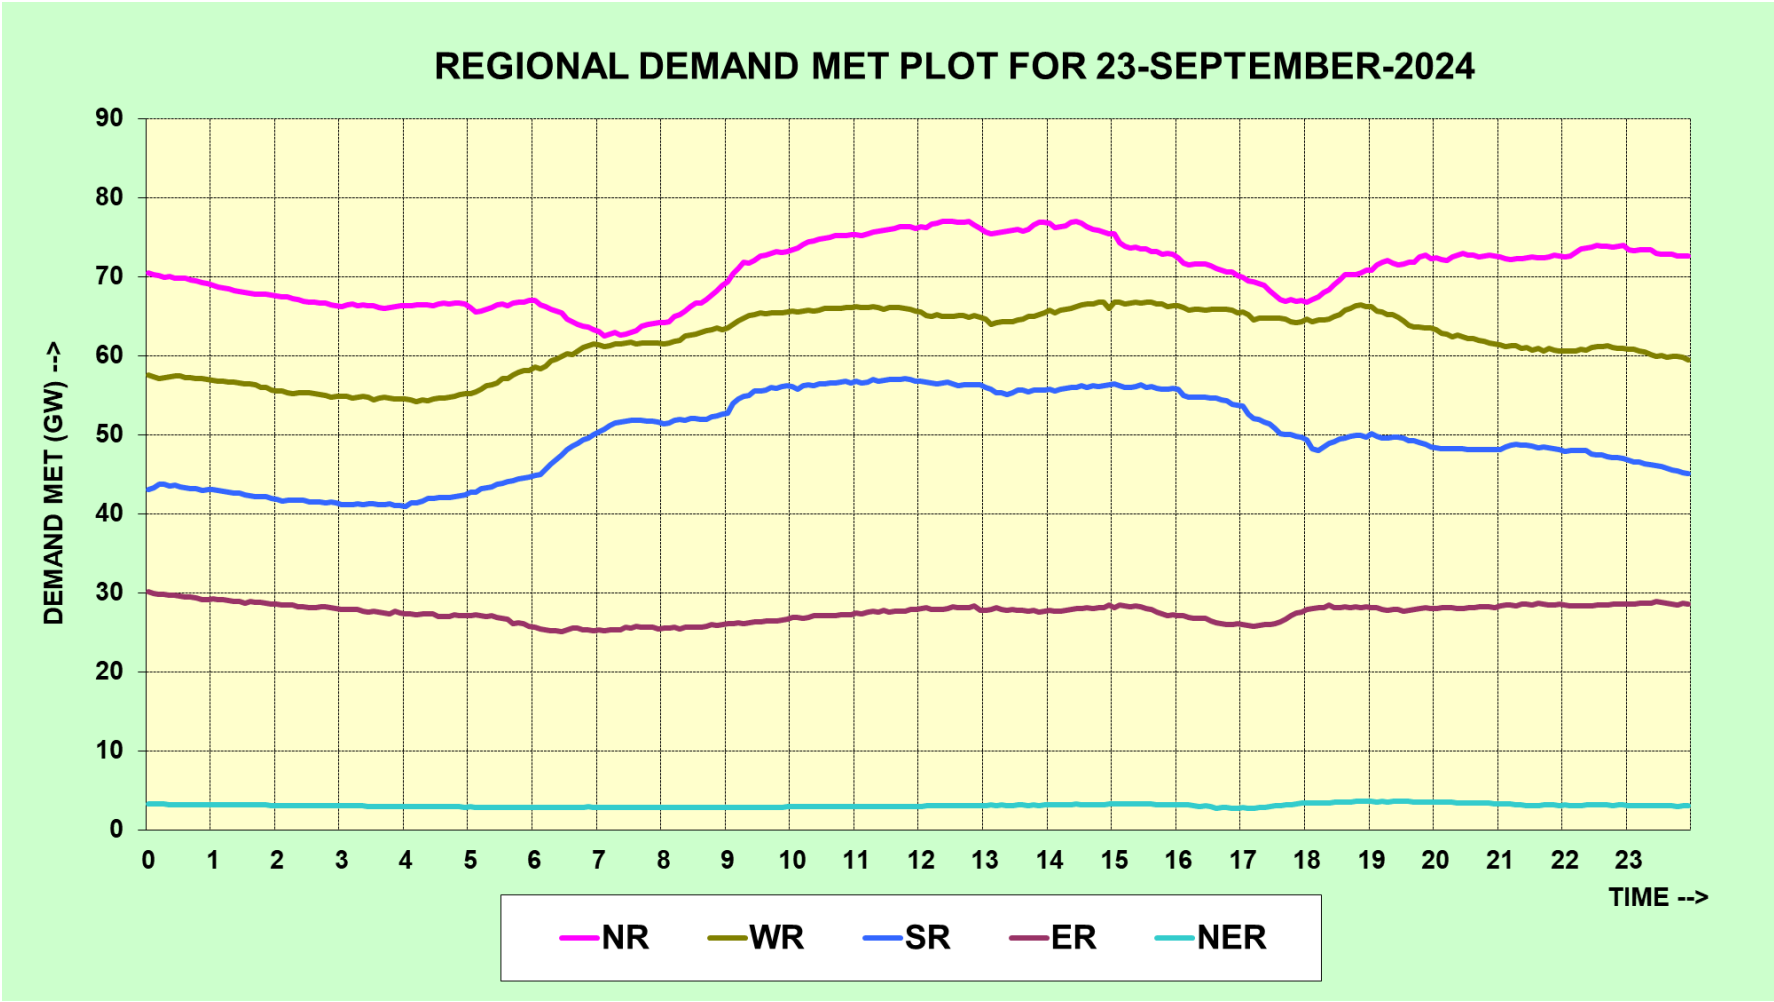
REGIONAL DEMAND MET PLOT FOR 23-SEPTEMBER-2024
DEMAND MET (GW) -->
90
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

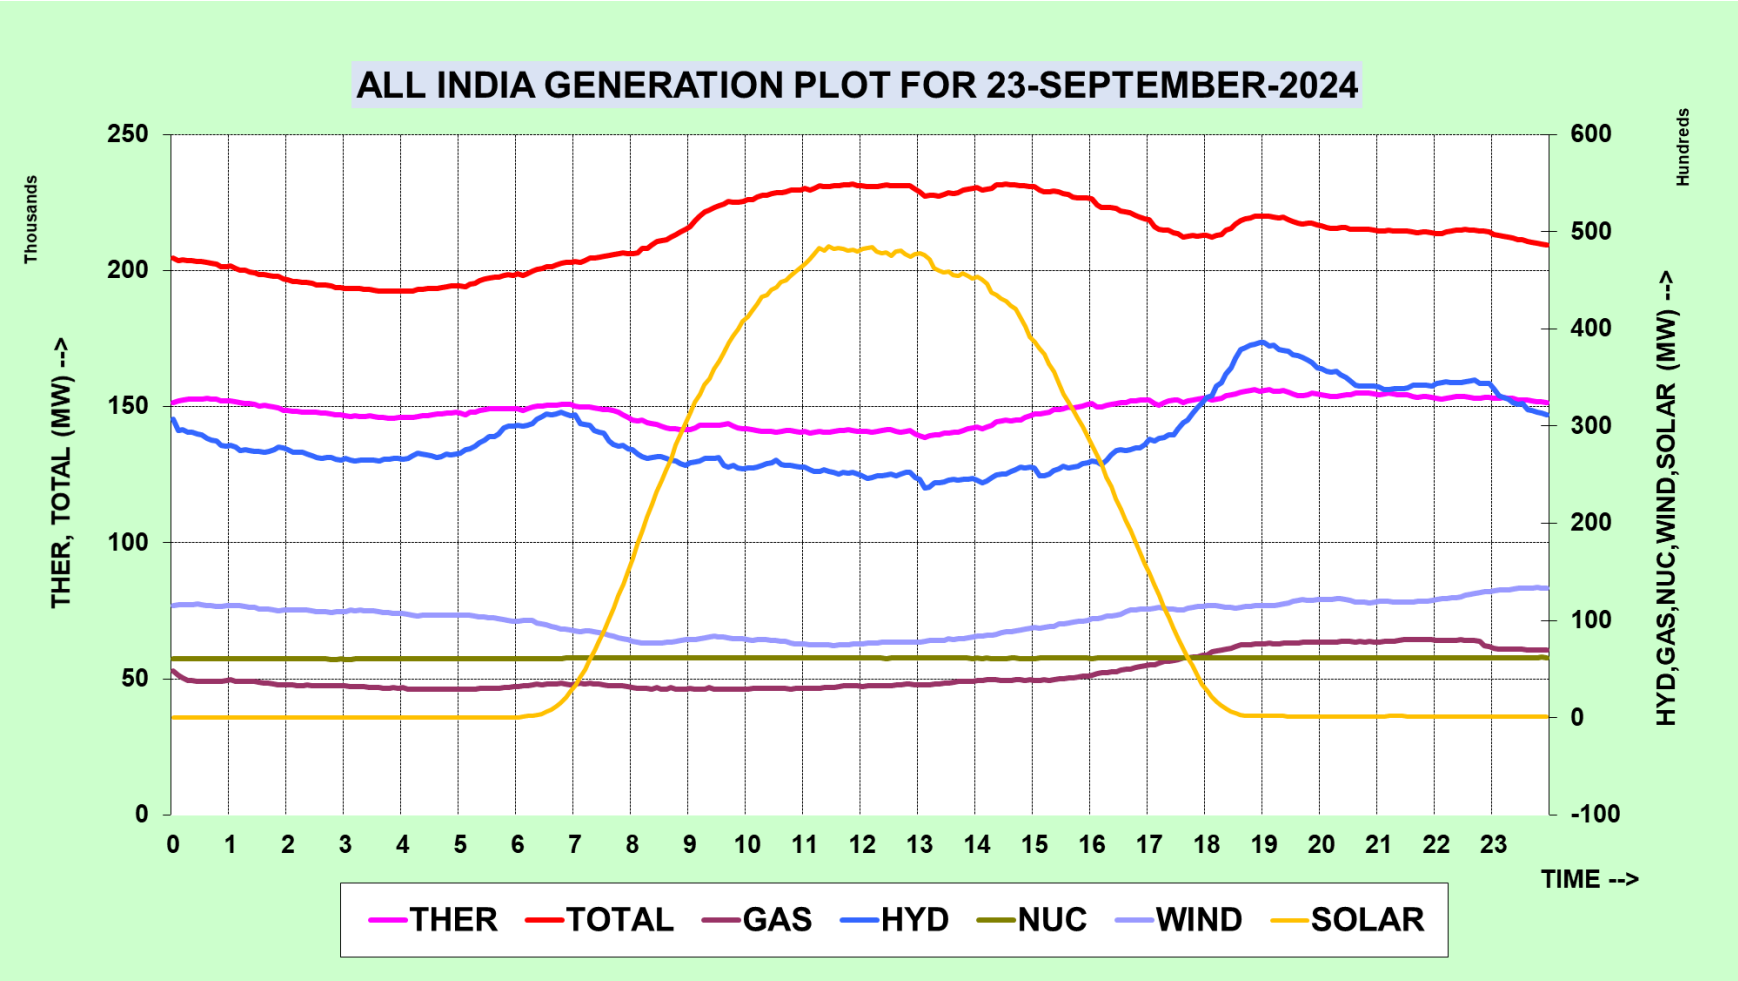
ALL INDIA GENERATION PLOT FOR 23-SEPTEMBER-2024
Thousands
THER, TOTAL (MW) -->
250
200
150
100
50
0
600
500
400
300
200
100
0
-100
Hundreds
HYD,GAS,NUC,WIND,SOLAR (MW) -->
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
THER
TOTAL
GAS
HYD
NUC
WIND
SOLAR

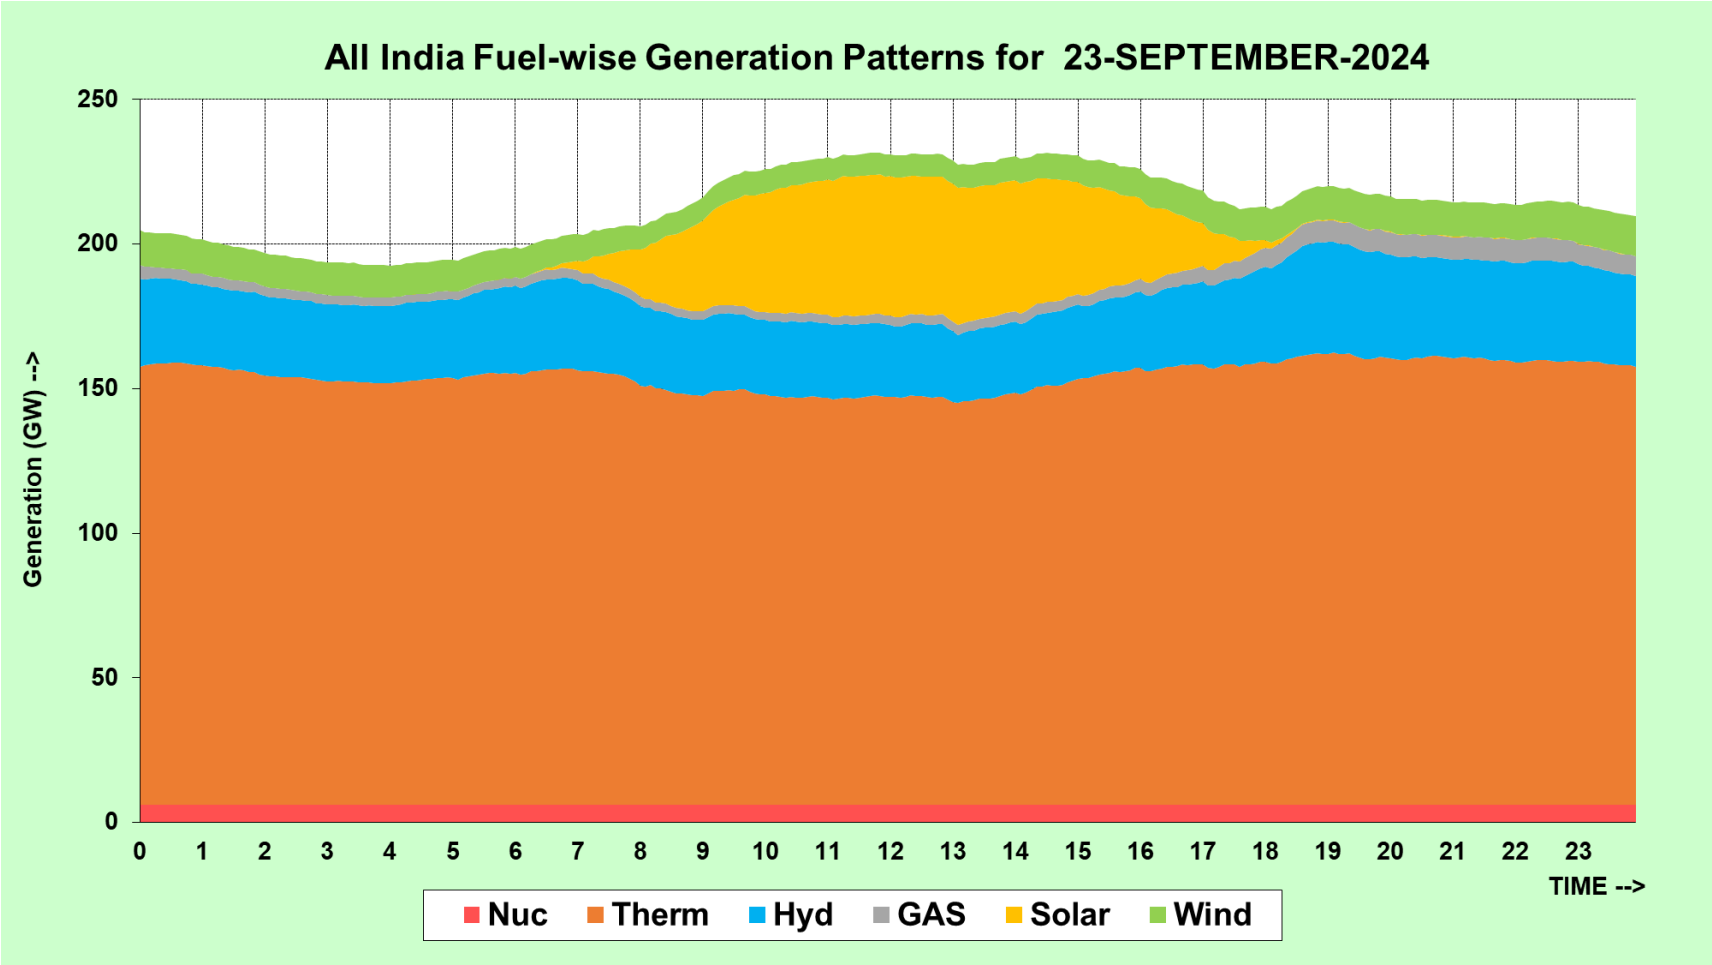
All India Fuel-wise Generation Patterns for 23-SEPTEMBER-2024
Generation (GW) -->
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Nuc
Therm
Hyd
GAS
Solar
Wind

23 सितम्बर 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 23 SEPTEMBER 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	204019		**12:05**	228984
00:20	203722		**12:20**	229336
00:35	202985		**12:35**	229276
00:50	201525		**12:50**	229246
01:05	200721		**13:05**	226094
01:20	199578		**13:20**	225969
01:35	198523		**13:35**	226983
01:50	197595		**13:50**	228373
02:05	196062		**14:05**	228098
02:20	195378		**14:20**	229854
02:35	194590		**14:35**	230019
02:50	193787		**14:50**	229906
03:05	193197		**15:05**	228894
03:20	193053		**15:20**	227982
03:35	192308		**15:35**	227107
03:50	192325		**15:50**	225182
04:05	192371		**16:05**	223048
04:20	192830		**16:20**	221791
04:35	193181		**16:35**	220402
04:50	193871		**16:50**	218886
05:05	193691		**17:05**	215781
05:20	195729		**17:20**	214085
05:35	197047		**17:35**	211297
05:50	198279		**17:50**	211540
06:05	198077		**18:05**	210896
06:20	200085		**18:20**	213587
06:35	201225		**18:35**	217195
06:50	202632		**18:50**	218563
07:05	202410		**19:05**	218571
07:20	203887		**19:20**	218055
07:35	204937		**19:35**	216352
07:50	205779		**19:50**	216536
08:05	205779		**20:05**	214843
08:20	208383		**20:20**	214942
08:35	210031		**20:35**	214388
08:50	212697		**20:50**	213925
09:05	217064		**21:05**	213566
09:20	220867		**21:20**	213561
09:35	222894		**21:35**	213352
09:50	224005		**21:50**	213239
10:05	224577		**22:05**	212603
10:20	226358		**22:20**	213653
10:35	227409		**22:35**	213945
10:50	228099		**22:50**	213588
11:05	228114		**23:05**	212217
11:20	229238		**23:20**	211464
11:35	229775		**23:35**	210216
11:50	230030		**23:50**	209266
Maximum Demand of 230608 MW met@14:28 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - SEPTEMBER 2024

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	6	6	0.0	189	189	0	0.0	397	397	0	0.0
	Delhi	119	119	0.0	3562	3562	0	0.0	6785	6780	-5	-0.1
	Haryana	215	215	0.0	6457	6457	0	0.0	12414	12414	0	0.0
	Himachal Pradesh	36	36	0.0	1074	1074	0	0.0	1884	1884	0	0.0
	J&K(UT) and Ladakh(UT)	52	52	-0.3	1574	1565	-9	-0.5	3236	2836	-400	-12.4
	Punjab	287	287	0.0	8619	8619	0	0.0	15310	15310	0	0.0
	Rajasthan	297	296	-1.3	8920	8880	-40	-0.4	16292	16292	0	0.0
	Uttar Pradesh	480	480	-0.1	14395	14391	-4	0.0	29347	29347	0	0.0
	Uttarakhand	48	48	-0.1	1442	1439	-3	-0.2	2564	2489	-75	-2.9
	Railway	4	4	0.0	126	126	0	0.0	227	227	0	0.0
	NFL	0	0	0.0	3	3	0	0.0	5	5	0	0.0
	TOTAL	1545	1543	-1.8	46360	46305	-55	-0.1	80678	80678	0	0.0
WR	Gujarat	414	414	0.0	12412	12412	0	0.0	24205	24205	0	0.0
	Madhya Pradesh	243	243	-0.1	7295	7293	-2	0.0	12677	12677	0	0.0
	Chhattisgarh	118	118	-0.1	3549	3545	-4	-0.1	5873	5873	0	0.0
	Maharashtra	515	514	-1.4	15459	15419	-41	-0.3	30049	26543	-3506	-11.7
	Goa	14	14	0.0	412	412	0	0.0	718	718	0	0.0
	DNHDDPDCL	30	30	0.0	902	902	0	0.0	1356	1356	0	0.0
	AMNSIL	16	16	0.0	493	493	0	0.0	832	832	0	0.0
	BALCO	13	13	0.0	378	378	0	0.0	530	530	0	0.0
	TOTAL	1363	1362	-1.6	40900	40853	-47	-0.1	69843	68493	-1350	-1.9
SR	Andhra Pradesh	214	214	-0.1	6434	6432	-2	0.0	12714	12710	-4	0.0
	Telangana	236	236	-0.1	7083	7080	-2	0.0	15590	15570	-20	-0.1
	Karnataka	234	233	-0.1	7005	7002	-3	0.0	16055	16050	-5	0.0
	Kerala	82	82	0.0	2472	2471	-1	0.0	4353	4353	0	0.0
	Tamil Nadu	375	375	-0.1	11247	11243	-3	0.0	19399	19393	-6	0.0
	Puducherry	10	10	0.0	315	315	0	0.0	517	517	0	0.0
	TOTAL	1152	1151	-0.4	34556	34544	-12	0.0	64938	64858	-80	-0.1
ER	Bihar	144	144	-0.5	4324	4308	-16	-0.4	8243	8005	-238	-2.9
	Jharkhand	42	42	0.0	1252	1251	-1	-0.1	2194	2194	0	0.0
	DVC	71	71	0.0	2144	2144	0	0.0	3525	3525	0	0.0
	Odisha	121	121	0.0	3632	3632	0	0.0	6300	6300	0	0.0
	West Bengal	213	213	0.0	6401	6401	0	0.0	11845	11845	0	0.0
	Sikkim	1	1	0.0	38	38	0	0.0	98	98	0	0.0
	Railways_ER ISTS	0	0	0.0	4	4	0	0.0	19	19	0	0.0
	TOTAL	593	593	-0.6	17795	17778	-17	-0.1	31321	30843	-478	-1.5
NER	Arunachal Pradesh	3	3	0.0	93	93	0	0.0	194	194	0	0.0
	Assam	47	47	0.0	1400	1399	-1	0.0	2812	2687	-125	-4.4
	Manipur	3	3	0.0	77	77	0	-0.4	235	235	0	0.0
	Meghalaya	5	5	0.0	136	136	0	0.0	317	317	0	0.0
	Mizoram	2	2	0.0	56	56	0	0.0	148	148	0	0.0
	Nagaland	3	3	0.0	85	85	0	0.0	184	184	0	0.0
	Tripura	6	6	0.0	177	177	0	0.0	376	376	0	0.0
	TOTAL	67	67	0.0	2024	2023	-1	0.0	3936	3914	-22	-0.6
ALL INDIA		4721	4717	-4.4	141634	141503	-131	-0.1				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF SEPTEMBER 2024 vs SEPTEMBER 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Sep-23	Sep-24	Difference	% Change	Average MU/day for Sep-24	Sep-23	Sep-24	Difference	% Change	Average MU/day for Sep-24
NR	Chandigarh	194	189	-6	-3	6	194	189	-6	-3	6
	Delhi	3711	3562	-149	-4	119	3711	3562	-149	-4	119
	Haryana	6845	6457	-388	-6	215	6789	6457	-332	-5	215
	Himachal Pradesh	1040	1074	33	3	36	1038	1074	36	3	36
	J&K(UT) and Ladakh(UT)	1521	1574	53	4	52	1476	1565	90	6	52
	Punjab	8135	8619	484	6	287	8135	8619	484	6	287
	Rajasthan	9339	8920	-419	-4	297	9285	8880	-405	-4	296
	Uttar Pradesh	14615	14395	-220	-2	480	14603	14391	-211	-1	480
	Uttarakhand	1408	1442	35	2	48	1397	1439	42	3	48
	Railway/NFL	106	128	22	21	4	106	128	22	21	4
	TOTAL	46914	46360	-554	-1	1545	46734	46305	-430	-1	1543
WR	Gujarat	12677	12412	-265	-2	414	12652	12412	-241	-2	414
	Madhya Pradesh	7575	7295	-281	-4	243	7541	7293	-248	-3	243
	Chhattisgarh	3184	3549	365	11	118	3173	3545	372	12	118
	Maharashtra	15777	15459	-318	-2	515	15756	15419	-337	-2	514
	Goa	403	412	9	2	14	403	412	9	2	14
	DNHDDPDCL	878	902	23	3	30	876	902	25	3	30
	AMNSIL	548	493	-55	-10	16	548	493	-55	-10	16
	BALCO	373	378	6	1	13	373	378	6	1	13
	TOTAL	41415	40900	-515	-1	1363	41321	40853	-468	-1	1362
SR	Andhra Pradesh	6550	6434	-116	-2	214	6550	6432	-118	-2	214
	Telangana	6915	7083	167	2	236	6927	7080	153	2	236
	Karnataka	7168	7005	-163	-2	234	7180	7002	-177	-2	233
	Kerala	2352	2472	121	5	82	2355	2471	116	5	82
	Tamil Nadu	10172	11247	1075	11	375	10187	11243	1057	10	375
	Puducherry	293	315	21	7	10	294	315	21	7	10
	TOTAL	33450	34556	1106	3	1152	33493	34544	1051	3	1151
ER	Bihar	4164	4324	160	4	144	4093	4308	215	5	144
	Jharkhand	1103	1252	148	13	42	1065	1251	186	17	42
	DVC	2288	2144	-144	-6	71	2288	2144	-144	-6	71
	Odisha	3556	3632	76	2	121	3556	3632	76	2	121
	West Bengal	5985	6401	416	7	213	5985	6401	416	7	213
	Sikkim	36	38	2	7	1	36	38	2	7	1
	Railways_ER ISTS	5	4	-1	-15	0	5	4	-1	-15	0
	TOTAL	17137	17795	658	4	593	17028	17778	750	4	593
NER	Arunachal Pradesh	90	93	3	3	3	90	93	3	3	3
	Assam	1368	1400	32	2	47	1332	1399	67	5	47
	Manipur	80	77	-2	-3	3	80	77	-3	-3	3
	Meghalaya	165	136	-28	-17	5	157	136	-21	-13	5
	Mizoram	51	56	5	10	2	51	56	5	10	2
	Nagaland	86	85	-2	-2	3	86	85	-2	-2	3
	Tripura	174	177	3	2	6	174	177	3	2	6
	TOTAL	2013	2024	11	1	67	1970	2023	53	3	67
ALL INDIA		140929	141634	705	1	4721	140546	141503	957	1	4717

13. DEMAND COMPARISON OF SEPTEMBER 2024 vs SEPTEMBER 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Sep-23	Sep-24	Difference	% Change	Sep-23	Sep-24	Difference	% Change
NR	Chandigarh	388	397	9	2.3	388	397	9	2.3
	Delhi	6993	6785	-208	-3.0	6993	6780	-213	-3.0
	Haryana	12753	12414	-339	-2.7	12753	12414	-339	-2.7
	Himachal Pradesh	1758	1884	126	7.2	1758	1884	126	7.2
	J&K(UT) and Ladakh(UT)	2805	3236	431	15.4	2618	2836	218	8.3
	Punjab	15068	15310	242	1.6	15068	15310	242	1.6
	Rajasthan	17956	16292	-1664	-9.3	17840	16292	-1548	-8.7
	Uttar Pradesh	27389	29347	1958	7.1	27389	29347	1958	7.1
	Uttarakhand	2368	2564	196	8.3	2293	2489	196	8.5
	Railway/NFL	206	232	27	13.1	206	232	27	13.1
WR	Gujarat	24829	24205	-624	-3	24544	24205	-339	-1.4
	Madhya Pradesh	14873	12677	-2196	-15	14852	12677	-2175	-14.6
	Chhattisgarh	5836	5873	37	1	5832	5873	41	0.7
	Maharashtra	27678	30049	2371	9	27678	26543	-1135	-4.1
	Goa	704	718	14	2	704	718	14	2.0
	DNHDDPDCL	1306	1356	50	3.8	1306	1356	50	3.8
	AMNSIL	895	832	-63	-7.1	895	832	-63	-7.1
	BALCO	524	530	6	1.2	524	530	6	1.2
SR	Andhra Pradesh	12343	12714	371	3.0	12327	12710	383	3.1
	Telangana	15389	15590	202	1.3	15370	15570	200	1.3
	Karnataka	14698	16055	1357	9.2	14698	16050	1352	9.2
	Kerala	4113	4353	240	5.8	4113	4353	240	5.8
	Tamil Nadu	17074	19399	2324	13.6	17035	19393	2358	13.8
	Puducherry	463	517	54	11.7	462	517	55	11.9
ER	Bihar	7387	8243	856	11.6	7387	8005	618	8.4
	Jharkhand	1818	2194	376	20.7	1818	2194	376	20.7
	DVC	3636	3525	-111	-3.1	3636	3525	-111	-3.1
	Odisha	6070	6300	230	3.8	6070	6300	230	3.8
	West Bengal	10667	11845	1178	11.0	10667	11845	1178	11.0
	Sikkim	98	98	0	0.0	98	98	0	0.0
	Railways_ER ISTS	28	19	-9	-30.5	28	19	-9	-30.5
NER	Arunachal Pradesh	163	194	31	18.7	163	194	31	18.7
	Assam	2413	2812	399	16.5	2413	2687	274	11.3
	Manipur	209	235	26	12.4	209	235	26	12.4
	Meghalaya	331	317	-14	-4.3	331	317	-14	-4.3
	Mizoram	129	148	19	14.8	129	148	19	14.8
	Nagaland	172	184	12	7.0	172	184	12	7.0
	Tripura	344	376	32	9.4	344	376	32	9.4

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - SEPTEMBER 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	188.81	188.77	-0.04	-0.02	6.29	6.29	0.00
	Delhi	3278.81	3266.12	-12.69	-0.39	109.29	108.87	-0.42
	Haryana	4749.99	4698.05	-51.94	-1.09	158.33	156.60	-1.73
	Himachal Pradesh	103.09	84.22	-18.87	-18.30	3.44	2.81	-0.63
	J&K(UT) and Ladakh(UT)	868.91	922.76	53.85	6.20	28.96	30.76	1.80
	Punjab	5117.36	5099.51	-17.85	-0.35	170.58	169.98	-0.60
	Rajasthan	2928.18	2911.07	-17.11	-0.58	97.61	97.04	-0.57
	Uttar Pradesh	6432.85	6414.92	-17.93	-0.28	214.43	213.83	-0.60
	Uttarakhand	689.69	693.79	4.10	0.59	22.99	23.13	0.14
	Railway	116.13	125.68	9.55	8.22	3.87	4.19	0.32
	NFL	2.57	2.52	-0.05	-1.81	0.09	0.08	0.00
	Total	24476.39	24407.42	-68.98	-0.28	815.88	813.58	-2.30
WR	Gujarat	5286.04	5215.71	-70.33	-1.33	176.20	173.86	-2.34
	Madhya Pradesh	3629.87	3552.66	-77.21	-2.13	121.00	118.42	-2.57
	Chhattisgarh	2039.31	2006.58	-32.73	-1.60	67.98	66.89	-1.09
	Maharashtra	5039.61	5035.89	-3.72	-0.07	167.99	167.86	-0.12
	Goa	349.50	404.70	55.20	15.79	11.65	13.49	1.84
	DNHDDPDCL	902.31	901.62	-0.69	-0.08	30.08	30.05	-0.02
	AMNSIL	205.81	213.98	8.17	3.97	6.86	7.13	0.27
	BALCO	377.70	378.10	0.40	0.11	12.59	12.60	0.01
	Total	17830.15	17709.24	-120.91	-0.68	594.34	590.31	-4.03
SR	Andhra Pradesh	1702.85	1682.03	-20.82	-1.22	56.76	56.07	-0.69
	Telangana	3061.24	3064.49	3.25	0.11	102.04	102.15	0.11
	Karnataka	1943.84	1960.59	16.75	0.86	64.79	65.35	0.56
	Kerala	1565.17	1588.36	23.19	1.48	52.17	52.95	0.77
	Tamil Nadu	4811.07	4763.23	-47.84	-0.99	160.37	158.77	-1.59
	Puducherry	304.22	297.17	-7.05	-2.32	10.14	9.91	-0.23
	Goa (SR)	64.46	66.33	1.87	2.90	2.15	2.21	0.06
	Total	13452.85	13422.20	-30.65	-0.23	448.43	447.41	-1.02
ER	Bihar	4025.61	3979.93	-45.68	-1.13	134.19	132.66	-1.52
	Jharkhand	950.04	953.50	3.45	0.36	31.67	31.78	0.12
	DVC	-1183.21	-1192.00	-8.78	0.74	-39.44	-39.73	-0.29
	Odisha	1069.04	1040.99	-28.05	-2.62	35.63	34.70	-0.93
	West Bengal	2509.42	2466.73	-42.69	-1.70	83.65	82.22	-1.42
	Sikkim	43.18	37.94	-5.24	-12.14	1.44	1.26	-0.17
	Railways_ER ISTS	4.31	4.28	-0.03	-0.60	0.14	0.14	0.00
	Total	7418.39	7291.37	-127.02	-1.71	247.28	243.05	-4.23
NER	Arunachal Pradesh	83.91	80.10	-3.81	-4.54	2.80	2.67	-0.13
	Assam	1172.46	1177.79	5.33	0.45	39.08	39.26	0.18
	Manipur	88.27	76.97	-11.30	-12.80	2.94	2.57	-0.38
	Meghalaya	36.53	31.69	-4.84	-13.26	1.22	1.06	-0.16
	Mizoram	20.53	13.84	-6.69	-32.59	0.68	0.46	-0.22
	Nagaland	79.45	71.84	-7.61	-9.58	2.65	2.39	-0.25
	Tripura	161.59	166.52	4.93	3.05	5.39	5.55	0.16
	Total	1642.74	1618.75	-23.99	-1.46	54.76	53.96	-0.80
All India Total		64820.52	64448.97	-371.55	-0.57	2160.68	2148.30	-12.38

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Fin. Year 2024-25
Name of Line							
Import of NR from WR (WR-NR)							
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	**6602.45**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	**2743.69**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	**5954.30**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	**3653.99**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	**13488.59**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	**616.24**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	**228.47**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	**46.02**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	**533.89**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	**364.80**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	**360.86**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	**6411.96**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	**1491.78**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	**11024.83**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	**561.02**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**54099.11**
Export of NR to WR (NR-WR)							
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	**1698.77**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	**490.85**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	**464.69**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	**59.66**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	**224.72**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	**164.00**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	**2908.15**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	**1161.49**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	**195.34**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**7382.66**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Fin. Year 2024-25
Name of Line							
Import of NR from ER (ER-NR)							
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	**662.15**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	**653.85**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	**1792.62**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	**1194.35**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	**1623.78**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	**1331.90**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	**105.09**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	**975.57**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	**10.67**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	**257.50**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	**83.78**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	**126.88**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	**13.57**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	**420.83**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	**346.80**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**9600.95**
Import of NR from NER (NER-NR)							
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55	**1096.79**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**1096.79**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Fin. Year 2024-25
Name of Line							
Export of NR to ER (NR-ER)							
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	**225.17**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	**393.79**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	**19.06**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	**7.13**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	**44.74**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	**3.66**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	**2.78**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	**4.27**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	**99.36**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	**6.54**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**950.23**
Export of NR to NER (NER-NR)							
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	**1365.53**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**1365.53**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Fin. Year 2024-25
Name of Line							
Export of WR to ER (WR-ER)							
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	**4941.92**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	**1726.17**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	**37.11**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	**1053.88**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	**649.66**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	**55.41**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	**14.95**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**8479.09**
Import of WR from ER (ER - WR)							
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	**110.65**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	**1733.90**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	**1413.26**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	**63.51**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	**1259.29**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	**179.55**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	**214.32**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**4974.49**
Export of ER to NER (ER - NER)							
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	**466.86**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	**720.79**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	**159.86**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**1347.51**
Import of ER from NER (NER - ER)							
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	**452.79**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	**713.54**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	**116.69**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**1283.02**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Fin. Year 2024-25
Name of Line							
Export of ER to SR (ER - SR)							
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	**1239.81**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	**5515.47**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	**7238.94**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**13994.22**
Import of ER from SR (SR - ER)							
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**490.92**
Export of WR to SR (WR-SR)							
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	**1215.89**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	**1321.27**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	**4798.09**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	**0.02**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	**6316.79**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	**389.92**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	**147.21**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	**5076.25**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**19265.43**
Import of WR from SR (SR - WR)							
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	**1616.28**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	**2805.21**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	**146.24**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	**5238.91**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	**0.02**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	**158.61**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**10383.94**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**134714**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during September 2024

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Sep-24	44.79	22.05	48.22	18.55	0.00	61.41	2.38	0.00	0.00	7.41	2.02	1.33	0.00		0.00	0.00	63.88	10.42	**282.46**
2-Sep-24	44.47	28.67	49.92	20.63	0.00	64.74	3.85	0.00	0.00	7.38	2.07	1.29	0.00		4.81	0.00	65.50	10.68	**304.01**
3-Sep-24	35.28	24.97	44.28	18.63	0.00	67.45	8.59	0.00	0.00	4.53	2.08	1.45	0.00		9.62	0.00	66.82	8.25	**291.95**
4-Sep-24	30.50	13.70	35.03	15.96	0.00	62.89	1.22	0.00		1.73	2.07	1.44	0.00	0.00	7.36	0.00	69.48	4.84	**246.22**
5-Sep-24	41.50	10.61	36.04	15.42	0.00	35.05	1.60	0.00	0.00	2.31	2.08	1.27	0.00	0.00	7.36	1.22	69.58	4.26	**228.30**
6-Sep-24	37.43	12.10	28.90	15.51	0.00	47.19	4.82	0.00	0.00	1.53	2.03	1.58	0.00		7.36	0.00	67.66	2.37	**228.48**
7-Sep-24	34.73	9.87	31.03	14.66	0.00	47.35	4.80	0.00	0.00	1.32	1.57	1.26	0.00		7.36	0.00	69.55	3.87	**227.37**
8-Sep-24	31.61	7.01	31.33	15.42	0.00	47.51	5.87	0.00	0.94	0.85	1.57	1.27	0.00		9.04	0.00	67.89	3.26	**223.57**
9-Sep-24	34.38	13.63	36.53	18.35	0.00	47.13	10.12	2.19	0.00	1.97	1.57	1.32	0.00		15.23	0.00	66.99	4.03	**253.44**
10-Sep-24	32.54	13.90	36.17	16.03	0.00	47.53	4.25	0.00	1.12	2.24	1.62	1.43	0.00		20.07	0.00	64.92	4.01	**245.83**
11-Sep-24	32.02	18.05	34.28	17.40	0.00	46.34	2.00	0.00		3.52	1.49	1.37	0.00		13.77	0.00	62.92	5.37	**238.53**
12-Sep-24	23.15	13.76	22.75	13.74	0.00	46.61	1.72	0.00	0.00	1.65	1.32	1.39	1.19	0.00	24.23	0.00	59.29	4.49	**215.29**
13-Sep-24	11.61	2.77	12.41	10.48	0.00	48.24	1.22	0.00	0.00	0.00	1.41	1.32	0.00	0.00	24.23	0.00	47.50	0.14	**161.33**
14-Sep-24	7.98	4.93	10.27	9.94	0.00	52.36	1.21	0.00	0.64	0.00	1.52	1.32	0.00		24.97	0.00	27.05	0.00	**142.19**
15-Sep-24	7.26	6.19	10.37	9.51	0.00	78.24	2.47	0.00	0.00	0.00	1.59	1.38	0.00		34.61	0.00	23.19	0.19	**175.00**
16-Sep-24	10.48	16.58	17.97	13.81	0.00	71.19	3.84	0.00	0.00	0.07	1.76	1.37	0.00		29.35	0.00	15.45	2.68	**184.55**
17-Sep-24	15.05	21.84	26.36	15.15	0.00	65.41	7.51	0.00	0.60	2.85	1.66	1.34	0.00		29.96	0.00	21.36	5.41	**214.50**
18-Sep-24	13.98	20.92	23.17	14.08	0.00	31.96	3.00	0.76	0.00	1.76	1.74	0.93	0.00		24.23	0.00	25.64	4.48	**166.65**
19-Sep-24	9.11	14.30	17.45	11.08	0.00	36.16	1.21	0.00		0.00	1.99	0.70	0.00		24.87	0.00	27.37	2.57	**146.81**
20-Sep-24	17.59	21.62	26.65	14.30	0.00	35.27	1.18	0.00	1.92	2.27	2.05	0.96	0.00	0.00	35.38	0.00	42.54	4.39	**206.12**
21-Sep-24	27.12	31.24	45.13	19.01	0.00	18.91	2.27	0.00	2.75	5.80	2.25	1.25	0.00	0.00	49.02	0.00	67.09	8.19	**280.03**
22-Sep-24	30.87	31.89	44.01	19.89	0.00		12.01	0.00	2.90	7.33	2.35	1.14	0.00		60.39	0.00	71.67	10.29	**294.74**
23-Sep-24	33.65	31.35	49.09	20.05	0.00	14.45	10.25	0.00	2.51	6.72	2.42	1.44	0.00		55.87	0.00	73.30	9.68	**310.78**
24-Sep-24	28.36	26.99	41.15	20.93	0.00	97.14	8.05	0.00	3.57	5.16	2.39	1.52	0.00		54.37	0.00	68.18	8.02	**365.83**
25-Sep-24	27.67	33.65	45.01	21.44	0.00	95.94	8.25	0.00	3.76	6.20	2.37	1.65	0.00		48.50	0.00	63.11	9.08	**366.63**
26-Sep-24	22.27	29.75	38.67	20.77	0.00	96.62	7.13	0.00	4.13	4.69	1.75	1.94	0.00		38.53	0.00	52.08	6.07	**324.40**
27-Sep-24	18.58	28.93	31.90	20.60	0.00	60.24	4.72	0.00	3.32	3.53	1.64	2.17	0.00		48.15	0.00	31.01	4.24	**259.03**
28-Sep-24	12.08	24.80	21.76	19.19	0.00	40.91	1.22	0.00	0.34	0.85	1.55	2.12	0.00	0.00	45.61	0.00	23.72	1.37	**195.52**
29-Sep-24	13.05	29.68	25.93	18.76	0.00	43.21	1.22	0.00	0.92	2.27	1.80	1.70	0.00		45.32	0.00	31.20	3.51	**218.57**
30-Sep-24	18.65	28.83	30.30	19.81	0.00	46.18	1.22	0.00	2.25	3.03	2.06	1.72	0.00		44.80	0.00	42.20	5.02	**246.07**
Total	**747.76**	**594.58**	**952.08**	**499.10**	**0.00**	**1553.63**	**129.20**	**2.95**	**31.67**	**88.97**	**55.79**	**42.37**	**1.19**	**0.00**	**844.37**	**1.22**	**1548.14**	**151.18**	**7244.20**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during September 2024

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Sep-24	0.00	0.00	0.00	0.00	10.90	0.00	0.00	0.20	2.20	0.00	0.00	0.00	0.21		0.00	4.74	0.00	0.00	**18.25**
2-Sep-24	0.00	0.00	0.00	0.00	12.41	0.00	0.00	5.20	2.50	0.00	0.00	0.00	0.82		0.00	15.18	0.00	0.00	**36.11**
3-Sep-24	0.00	0.00	0.00	0.00	13.55	0.00	0.00	3.80	7.92	0.00	0.00	0.00	1.42		0.00	23.97	0.00	0.00	**50.66**
4-Sep-24	0.00	0.00	0.00	0.00	10.50	0.00	0.00	9.16		0.00	0.00	0.00	0.81	0.00	0.00	13.62	0.00	0.00	**34.09**
5-Sep-24	0.00	0.00	0.00	0.00	11.97	0.00	0.00	0.51	3.10	0.00	0.00	0.00	0.17	0.00	0.00	0.00	0.00	0.00	**15.75**
6-Sep-24	0.00	0.00	0.00	0.00	13.30	0.00	0.00	1.00	4.57	0.00	0.00	0.00	0.47		0.00	2.36	0.00	0.00	**21.70**
7-Sep-24	0.00	0.00	0.00	0.00	12.33	0.00	0.00	2.45	1.39	0.00	0.00	0.00	0.57		0.00	10.78	0.00	0.00	**27.52**
8-Sep-24	0.00	0.00	0.00	0.00	8.34	0.00	0.00	2.50	0.00	0.00	0.00	0.00	0.72		0.00	11.59	0.00	0.00	**23.15**
9-Sep-24	0.00	0.00	0.00	0.00	9.81	0.00	0.00	0.00	1.40	0.00	0.00	0.00	1.02		0.00	9.28	0.00	0.00	**21.51**
10-Sep-24	0.00	0.00	0.00	0.00	9.80	0.00	0.00	2.30	0.00	0.00	0.00	0.00	0.91		0.00	10.14	0.00	0.00	**23.15**
11-Sep-24	0.00	0.00	0.00	0.00	7.50	0.00	0.00	1.80		0.00	0.00	0.00	-0.39		0.00	14.00	0.00	0.00	**22.91**
12-Sep-24	0.00	0.00	0.00	0.00	6.10	0.00	0.00	3.59	0.62	0.00	0.00	0.00	0.00	0.00	0.00	15.09	0.00	0.00	**25.40**
13-Sep-24	0.00	0.00	0.00	0.00	5.22	0.00	0.00	4.55	0.27	2.80	0.00	0.00	0.14	0.00	0.00	17.84	0.00	0.00	**30.82**
14-Sep-24	0.00	0.00	0.00	0.00	7.70	0.00	0.00	4.70	0.00	3.71	0.00	0.00	1.38		0.00	20.40	0.00	1.42	**39.31**
15-Sep-24	0.00	0.00	0.00	0.00	9.10	0.00	0.00	5.38	0.22	2.84	0.00	0.00	1.63		0.00	25.72	0.00	0.00	**44.89**
16-Sep-24	0.00	0.00	0.00	0.00	10.11	0.00	0.00	5.60	0.10	0.00	0.00	0.00	1.80		0.00	29.10	0.00	0.00	**46.71**
17-Sep-24	0.00	0.00	0.00	0.00	9.23	0.00	0.00	5.00	0.00	0.00	0.00	0.00	0.81		0.00	28.09	0.00	0.00	**43.13**
18-Sep-24	0.00	0.00	0.00	0.00	7.88	0.00	0.00	0.00	5.40	0.00	0.00	0.00	0.28		0.00	26.62	0.00	0.00	**40.18**
19-Sep-24	0.00	0.00	0.00	0.00	8.67	0.00	0.00	5.71		0.69	0.00	0.00	1.76		0.00	32.36	0.00	0.00	**49.19**
20-Sep-24	0.00	0.00	0.00	0.00	10.69	0.00	0.00	3.84	0.00	0.00	0.00	0.00	1.30	0.00	0.00	22.07	0.00	0.00	**37.90**
21-Sep-24	0.00	0.00	0.00	0.00	11.27	0.00	0.46	3.38	0.00	0.00	0.00	0.00	1.35	0.00	0.00	19.54	0.00	0.00	**36.00**
22-Sep-24	0.00	0.00	0.00	0.00	10.81		0.00	3.32	0.00	0.00	0.00	0.00	0.19		0.00	19.97	0.00	0.00	**34.29**
23-Sep-24	0.00	0.00	0.00	0.00	11.00	0.00	0.00	3.79	0.00	0.00	0.00	0.00	0.74		0.00	21.04	0.00	0.00	**36.57**
24-Sep-24	0.00	0.00	0.00	0.00	10.72	0.00	0.00	2.76	0.00	0.00	0.00	0.00	1.63		0.00	17.15	0.00	0.00	**32.26**
25-Sep-24	0.00	0.00	0.00	0.00	12.14	0.00	0.00	2.91	0.00	0.00	0.00	0.00	1.74		0.00	19.28	0.00	0.00	**36.07**
26-Sep-24	0.00	0.00	0.00	0.00	11.65	0.00	0.00	1.81	0.00	0.00	0.00	0.00	2.09		0.00	11.88	0.00	0.00	**27.43**
27-Sep-24	0.00	0.00	0.00	0.00	12.05	0.00	0.00	1.99	0.00	0.00	0.00	0.00	1.52		0.00	10.70	0.00	0.00	**26.26**
28-Sep-24	0.00	0.00	0.00	0.00	12.35	0.00	0.00	4.21	0.00	0.00	0.00	0.00	2.15	0.00	0.00	23.37	0.00	0.00	**42.08**
29-Sep-24	0.00	0.00	0.00	0.00	11.50	0.00	0.00	4.38	0.00	0.00	0.00	0.00	1.60		0.00	25.63	0.00	0.00	**43.11**
30-Sep-24	0.00	0.00	0.00	0.00	11.17	0.00	0.00	3.29	0.00	0.00	0.00	0.00	1.67		0.00	17.69	0.00	0.00	**33.82**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**309.77**	**0.00**	**0.46**	**99.13**	**29.69**	**10.04**	**0.00**	**0.00**	**30.51**	**0.00**	**0.00**	**519.20**	**0.00**	**1.42**	**1000.22**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during September 2024

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Sep-24	2.48	5.64	13.08	17.00	9.58	9.61	0.92	5.64		1.92	0.72	0.23	0.00		0.00	2.68	3.93	**73.43**	12.04	**12.04**
2-Sep-24	2.49	5.45	14.16	17.59	10.44	9.87	0.55	4.98		2.28	0.29	0.48	0.00		0.00	2.65	3.42	**74.65**	12.01	**12.01**
3-Sep-24	1.35	0.00	11.80	16.10	7.23	8.09	0.00	3.51		3.16	0.00	0.40	0.48	0.00	0.00	1.46	1.72	**55.30**	11.60	**11.60**
4-Sep-24	0.00	0.00	9.45	16.45	6.15	5.92	0.00	2.66		2.94	0.00	0.31	0.00	0.00	0.00	1.65	1.05	**46.58**	11.11	**11.11**
5-Sep-24	0.00	0.00	9.63	17.24	6.89	6.54	0.00	3.25		2.30	0.27	0.21	0.00		0.00	1.47	1.06	**48.86**	12.24	**12.24**
6-Sep-24	0.00	0.00	9.17	17.38	8.27	4.67	0.00	3.40		2.70	0.00	1.00	0.00		0.00	1.93	0.60	**49.12**	12.02	**12.02**
7-Sep-24	0.00	0.00	9.73	15.55	8.59	5.88	0.00	4.25		2.87	0.00	0.38		0.00	0.00	1.77	0.40	**49.42**	12.61	**12.61**
8-Sep-24	0.00	0.00	10.50	17.36	7.70	6.00	0.00	3.47		2.72	0.00	0.32			0.00	1.67	0.77	**50.51**	12.01	**12.01**
9-Sep-24	2.10	0.00	13.19	17.60	9.60	5.20	0.00	5.28		2.50	0.03	0.43			0.00	4.30	1.50	**61.73**	12.04	**12.04**
10-Sep-24	0.00	0.00	11.46	17.13	6.48	5.86	0.00	3.34		3.07	0.00	0.71			0.00	1.31	1.36	**50.72**	12.01	**12.01**
11-Sep-24	0.00	0.00	10.43	16.70	6.70	5.01	0.00	3.21		3.07	0.00	0.60		0.00	0.00	1.81	1.02	**48.55**	12.03	**12.03**
12-Sep-24	0.00	0.00	8.34	15.71	4.40	1.91	0.00	2.00		3.18	0.00	1.20		0.00	0.00	0.47	0.23	**37.44**	11.22	**11.22**
13-Sep-24	0.00	0.00	7.01	17.00	3.88	2.35	0.00	2.15		3.46	0.00	1.27	0.00	0.00	0.00	0.36	0.00	**37.48**	12.04	**12.04**
14-Sep-24	1.61	6.07	8.82	16.95	11.31	10.09	0.80	6.59		3.05	0.00	1.29	0.00	0.00	0.00	3.09	3.50	**73.17**	12.16	**12.16**
15-Sep-24	2.73	10.59	9.90	17.02	14.99	12.45	2.95	7.85		2.87	0.00	1.58	0.96		0.00	4.41	4.70	**93.00**	11.98	**11.98**
16-Sep-24	7.04	20.28	12.02	10.37	17.79	15.46	3.61	10.24		2.41	0.35	1.84	0.00		0.00	5.52	6.62	**113.55**	22.32	**22.32**
17-Sep-24	7.41	16.33	11.06	10.36	14.45	13.68	3.17	7.67		1.92	0.63	1.12	0.00		0.00	4.39	4.89	**97.08**	22.02	**22.02**
18-Sep-24	4.43	10.29	8.99	8.60	10.76	8.53	0.53	5.69		2.81	0.00	0.48	0.00		0.00	2.87	3.36	**67.34**	20.39	**20.39**
19-Sep-24		2.61	8.13	8.20	6.57	5.06	0.00	3.70		3.51	0.00		0.75		0.00	1.28	2.19	**42.00**	19.54	**19.54**
20-Sep-24	0.92	3.61	10.47	8.15	9.79	6.07	0.00	5.08		3.49	0.00		1.25	0.00	0.00	2.39	2.50	**53.72**	22.93	**22.93**
21-Sep-24	1.70	1.42	12.12	8.62	13.15	8.10	0.00	5.95	0.00	2.96	0.00				0.00	3.54	3.32	**60.88**	19.80	**19.80**
22-Sep-24	1.95	2.75	15.46	8.42	16.72	8.64	2.61	6.95		2.46	2.48	0.58		0.00	0.00	4.82	1.72	**75.56**	11.95	**11.95**
23-Sep-24	2.16	2.42	15.97	8.62	17.95	8.57	2.80	6.57		2.30	0.54	0.54			0.00	5.08	4.15	**77.67**	12.05	**12.05**
24-Sep-24	3.98	7.29	18.35	8.99	21.22	13.85	4.02	7.95		2.39	0.29	0.83			0.00	6.48	6.15	**101.79**	12.77	**12.77**
25-Sep-24	5.26	10.36	18.26	7.94	21.59	16.06	7.89	9.12		2.23	0.33	0.48	0.48		0.00	6.75	5.95	**112.70**	23.92	**23.92**
26-Sep-24	6.42	10.68	15.04	8.90	21.56	16.44	8.10	9.22		1.34	1.20	0.62	0.00	0.00	0.00	6.42	5.12	**111.06**	21.41	**21.41**
27-Sep-24	9.39	17.58	8.72	8.40	16.13	13.44	4.15	9.05		0.71	1.81	0.79	0.00		0.00	4.79	5.55	**100.51**	16.01	**16.01**
28-Sep-24	7.52	12.86	6.33	8.53	14.05	5.85	0.32	5.13		1.34	1.38	0.52	0.48	0.00	0.00	4.04	3.38	**71.73**	16.58	**16.58**
29-Sep-24	5.73	10.86	7.31	8.69	14.83	7.64	1.25	7.52		1.35	1.20	0.65	0.00		0.00	4.34	3.45	**74.82**	16.76	**16.76**
30-Sep-24	4.64	8.24	9.10	8.40	13.40	6.64	0.00	5.06		2.02	0.39	1.95	0.48		0.00	3.81	3.42	**67.55**	16.98	**16.98**
Total	**81.31**	**165.33**	**334.00**	**383.97**	**352.17**	**253.48**	**43.67**	**166.48**	**0.00**	**75.33**	**11.91**	**20.81**	**4.88**	**0.00**	**0.00**	**97.55**	**87.03**	**2077.92**	**454.55**	**454.55**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.2 Import-Export of NR with ER & NER during September 2024

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Bihar shariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.51	0.00	0.00	**0.51**	0.00	**0.00**
2-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.57	0.00	0.00	**0.57**	0.00	**0.00**
3-Sep-24	0.00	0.17	0.00	0.00	0.00	0.00	0.36	0.00		0.00	0.57	0.00	0.00	0.01	0.64	0.00	0.00	**1.75**	0.00	**0.00**
4-Sep-24	1.46	5.64	0.00	0.00	0.00	0.00	2.31	0.00		0.00	0.40	0.00	0.00	0.07	0.62	0.00	0.00	**10.50**	0.00	**0.00**
5-Sep-24	0.57	4.60	0.00	0.00	0.00	0.00	1.82	0.00		0.00	0.00	0.00	0.00		0.58	0.00	0.00	**7.57**	0.00	**0.00**
6-Sep-24	0.56	4.93	0.00	0.00	0.00	0.00	2.89	0.00		0.00	0.17	0.00	0.00		0.56	0.00	0.00	**9.11**	0.00	**0.00**
7-Sep-24	1.89	7.16	0.00	0.00	0.00	0.00	3.50	0.00		0.00	0.40	0.00		0.07	0.48	0.00	0.00	**13.50**	0.00	**0.00**
8-Sep-24	2.26	5.87	0.00	0.00	0.00	0.00	3.38	0.00		0.00	0.03	0.00			0.35	0.00	0.00	**11.89**	0.00	**0.00**
9-Sep-24	0.00	1.66	0.00	0.00	0.00	0.00	2.80	0.00		0.00	0.00	0.00			0.52	0.00	0.00	**4.98**	0.00	**0.00**
10-Sep-24	0.84	2.42	0.00	0.00	0.00	0.00	3.19	0.00		0.00	0.42	0.00			0.52	0.00	0.00	**7.39**	0.00	**0.00**
11-Sep-24	1.13	3.34	0.00	0.00	0.00	0.00	3.05	0.00		0.00	0.44	0.00		0.07	0.58	0.00	0.00	**8.61**	0.00	**0.00**
12-Sep-24	2.83	6.67	0.00	0.00	0.00	0.00	4.49	0.00		0.00	0.72	0.00		0.69	0.68	0.00	0.00	**16.08**	0.00	**0.00**
13-Sep-24	2.61	6.91	0.00	0.00	0.00	0.00	4.58	0.00		0.00	0.95	0.00	0.00	0.06	0.47	0.00	0.27	**15.85**	0.00	**0.00**
14-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.58	0.00	0.00	0.08	0.45	0.00	0.00	**1.11**	0.00	**0.00**
15-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.13	0.00	0.00		0.24	0.00	0.00	**0.37**	0.00	**0.00**
16-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.11	0.00	0.00	**0.11**	0.00	**0.00**
17-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.15	0.00	0.00	**0.15**	0.00	**0.00**
18-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.20	0.00	0.00		0.40	0.00	0.00	**0.60**	0.00	**0.00**
19-Sep-24		0.00	0.00	0.00	0.00	0.00	2.70	0.00		0.00	0.95		0.00		0.50	0.00	0.04	**4.19**	0.00	**0.00**
20-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	2.23	0.00		0.00	0.92		0.00	0.05	0.62	0.00	0.00	**3.82**	0.00	**0.00**
21-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.05	0.00	0.00	0.00	0.37				0.67	0.00	0.00	**1.09**	0.00	**0.00**
22-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.12	0.69	0.00	0.00	**0.81**	0.00	**0.00**
23-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.57	0.00	0.00	**0.57**	0.00	**0.00**
24-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.47	0.00	0.00	**0.47**	0.00	**0.00**
25-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.42	0.00	0.00	**0.42**	0.00	**0.00**
26-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.41	0.00	0.00	**0.41**	0.00	**0.00**
27-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.11		0.37	0.00	0.00	**0.48**	0.00	**0.00**
28-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.10	0.37	0.00	0.00	**0.47**	0.00	**0.00**
29-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.47	0.00	0.00	**0.47**	0.00	**0.00**
30-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.47	0.00		0.00	0.00	0.00	0.00		0.54	0.00	0.00	**1.01**	0.00	**0.00**
Total	**14.15**	**49.37**	**0.00**	**0.00**	**0.00**	**0.00**	**37.82**	**0.00**	**0.00**	**0.00**	**7.25**	**0.00**	**0.11**	**1.32**	**14.53**	**0.00**	**0.31**	**124.86**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.3 Import and Export of ER with WR & NER during September 2024

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Sep-24	41.9	0.0	0.2	8.2	0.4	0.0	0.0	**50.80**	0.0	20.8	3.6	0.0	7.2	2.2	0.7	**34.54**	5.71	8.06	1.97	**15.74**	0.00	0.00	0.00	**0.00**
2-Sep-24	39.3	0.0	0.0	7.4	0.1	0.0	0.0	**46.85**	0.0	21.8	4.3	0.0	7.5	2.4	1.2	**37.18**	6.33	8.70	2.16	**17.19**	0.00	0.00	0.00	**0.00**
3-Sep-24	38.9	0.1	0.0	7.6	0.0	0.0	0.0	**46.67**	0.0	19.7	3.0	0.0	6.8	2.3	0.9	**32.75**	5.16	6.97	1.83	**13.96**	0.00	0.00	0.00	**0.00**
4-Sep-24	42.2	2.7	0.6	8.3	0.4	0.0	0.0	**54.27**	0.0	9.5	2.0	0.0	6.6	1.6	0.6	**20.23**	5.54	7.23	1.74	**14.51**	0.00	0.00	0.00	**0.00**
5-Sep-24	44.9	5.5	1.5	8.6	0.4	0.0	0.0	**61.03**	0.0	10.6	1.7	0.0	7.2	1.4	1.0	**21.84**	6.49	9.64	2.01	**18.14**	0.00	0.00	0.00	**0.00**
6-Sep-24	42.4	0.9	0.5	8.1	0.2	0.0	0.0	**52.07**	0.0	10.5	1.9	0.0	6.7	1.8	1.6	**22.49**	6.49	9.57	2.26	**18.32**	0.00	0.00	0.00	**0.00**
7-Sep-24	44.7	1.0	1.0	8.8	0.4	0.0	0.0	**55.87**	0.0	11.8	1.3	0.0	5.2	2.7	1.5	**22.60**	7.80	11.42	2.66	**21.88**	0.00	0.00	0.00	**0.00**
8-Sep-24	42.1	2.3	3.4	8.3	1.5	0.0	0.1	**57.80**	0.0	11.2	0.6	0.0	2.4	2.4	1.0	**17.74**	8.17	11.95	2.60	**22.73**	0.00	0.00	0.00	**0.00**
9-Sep-24	37.7	4.9	2.4	6.7	1.0	0.0	0.0	**52.70**	0.0	16.1	0.5	0.1	2.6	1.4	1.2	**22.04**	8.09	11.64	2.63	**22.36**	0.00	0.00	0.00	**0.00**
10-Sep-24	39.6	3.3	0.4	8.1	2.1	0.4	0.0	**53.97**	0.0	13.8	2.3	0.0	2.0	0.3	1.0	**19.43**	8.10	11.59	2.63	**22.32**	0.00	0.00	0.00	**0.00**
11-Sep-24	38.9	8.7	0.1	8.6	1.6	0.5	0.0	**58.34**	0.0	13.3	4.8	0.0	3.2	0.1	1.2	**22.54**	5.00	6.83	1.60	**13.43**	0.00	0.00	0.00	**0.00**
12-Sep-24	34.4	10.9	0.0	8.1	1.0	0.4	0.0	**54.77**	0.0	14.9	5.6	0.0	4.3	0.2	1.3	**26.34**	6.85	9.83	2.24	**18.93**	0.00	0.00	0.00	**0.00**
13-Sep-24	24.2	6.6	0.0	5.7	0.3	0.3	0.0	**37.07**	0.0	15.2	7.5	0.0	6.6	0.3	1.4	**31.11**	7.73	10.63	2.40	**20.76**	0.00	0.00	0.00	**0.00**
14-Sep-24	8.3	3.1	0.0	1.3	0.0	0.0	0.0	**12.66**	2.2	11.6	8.4	1.3	10.5	1.2	1.9	**37.10**	6.51	9.62	2.39	**18.52**	0.00	0.00	0.00	**0.00**
15-Sep-24	4.7	1.2	0.0	0.3	0.0	0.0	0.0	**6.27**	5.7	18.7	9.2	2.9	12.9	1.7	1.9	**52.92**	5.71	8.34	2.19	**16.25**	0.00	0.00	0.00	**0.00**
16-Sep-24	3.2	0.7	0.0	0.2	0.0	0.0	0.0	**4.17**	10.4	21.6	12.0	4.6	14.7	2.3	2.5	**68.13**	8.91	16.13	3.36	**28.39**	0.00	0.00	0.00	**0.00**
17-Sep-24	6.1	0.7	0.0	0.8	0.0	0.0	0.0	**7.58**	5.7	16.5	10.7	2.9	9.1	1.7	2.8	**49.31**	8.90	16.05	3.37	**28.32**	0.00	0.00	0.00	**0.00**
18-Sep-24	10.0	0.4	0.0	0.8	0.0	0.0	0.0	**11.24**	1.6	14.3	11.4	1.6	9.4	1.5	2.9	**42.66**	9.85	16.86	3.44	**30.14**	0.00	0.00	0.00	**0.00**
19-Sep-24	19.0	3.1	0.0	2.0	0.0	0.0	0.0	**24.17**	0.5	10.2	10.7	0.9	10.7	2.2	2.4	**37.63**	11.38	18.68	3.62	**33.69**	0.00	0.00	0.00	**0.00**
20-Sep-24	25.3	1.5	0.0	3.0	0.0	0.0	0.0	**29.76**	0.0	12.0	12.0	0.5	12.2	2.8	2.7	**42.24**	11.35	19.06	3.65	**34.06**	0.00	0.00	0.00	**0.00**
21-Sep-24	35.9	1.7	0.0	5.1	0.0	0.0	0.0	**42.68**	0.0	10.9	9.4	0.3	11.8	3.3	2.1	**37.83**	10.81	17.72	3.55	**32.07**	0.00	0.00	0.00	**0.00**
22-Sep-24	39.6	0.5	0.0	6.1	0.0	0.0	0.0	**46.26**	0.0	13.5	9.6	0.1	12.6	2.9	2.2	**40.87**	7.48	12.47	2.65	**22.61**	0.00	0.00	0.00	**0.00**
23-Sep-24	40.8	0.0	0.0	6.4	0.0	0.0	0.0	**47.16**	0.0	18.2	9.4	0.0	10.3	3.1	2.6	**43.49**	7.61	12.06	2.66	**22.33**	0.00	0.00	0.00	**0.00**
24-Sep-24	22.2	0.0	0.0	2.9	0.0	0.0	0.0	**25.20**	0.1	33.0	13.3	0.4	7.8	2.7	2.5	**59.70**	4.43	8.48	1.85	**14.75**	0.00	0.00	0.00	**0.00**
25-Sep-24	19.2	0.2	0.0	2.6	0.0	0.0	0.0	**22.01**	0.3	29.1	14.2	0.7	7.5	2.7	2.6	**56.99**	7.89	14.00	2.73	**24.62**	0.00	0.00	0.00	**0.00**
26-Sep-24	8.7	0.0	0.0	1.1	0.0	0.0	0.0	**9.81**	1.1	27.2	12.1	1.3	7.5	2.3	2.7	**54.22**	4.68	9.82	1.65	**16.15**	0.00	0.00	0.00	**0.00**
27-Sep-24	5.1	0.0	0.0	0.5	0.0	0.0	0.0	**5.63**	5.7	23.8	12.8	3.4	9.9	2.5	2.8	**60.97**	4.19	8.96	1.58	**14.73**	0.00	0.00	0.00	**0.00**
28-Sep-24	5.6	1.1	0.0	0.4	0.1	0.1	0.0	**7.25**	4.7	13.0	12.2	2.9	8.7	1.5	2.0	**45.00**	3.39	7.32	1.19	**11.89**	0.04	0.00	0.00	**0.04**
29-Sep-24	11.3	1.4	0.0	1.4	0.1	0.0	0.0	**14.28**	1.4	14.2	9.8	1.7	8.9	1.6	1.7	**39.24**	2.65	6.14	1.23	**10.02**	0.22	0.00	0.00	**0.22**
30-Sep-24	17.1	0.6	0.0	2.4	0.2	0.1	0.0	**20.32**	0.5	13.4	8.5	0.7	7.7	1.3	1.5	**33.50**	4.79	9.70	1.90	**16.39**	0.00	0.00	0.00	**0.00**
Total	**793.25**	**63.29**	**10.21**	**140.01**	**9.88**	**1.82**	**0.20**	**1018.66**	**39.73**	**490.66**	**224.89**	**26.30**	**240.04**	**56.53**	**54.49**	**1132.63**	**207.98**	**335.46**	**71.76**	**615.19**	**0.26**	**0.00**	**0.00**	**0.26**

Date	15.4 Import and Export of SR with ER & WR during September 2024																								
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Sep-24	0.00	16.12	15.31	**31.43**	7.83	0.00	0.00	**7.83**	0.00	0.00	0.45	0.00	1.85	2.07	0.00	0.33	**4.70**	17.66	52.23	12.15	47.72	0.00	0.00	0.00	14.34	**144.10**
2-Sep-24	0.00	11.30	22.98	**34.28**	9.18	0.00	0.00	**9.18**	0.00	0.00	2.09	0.00	3.88	1.89	0.01	2.23	**10.09**	23.72	42.27	6.90	47.39	4.98	0.00	0.00	7.49	**132.75**
3-Sep-24	0.00	18.95	24.56	**43.51**	4.69	0.00	0.00	**4.69**	0.00	0.00	5.33	0.00	0.00	1.89	0.00	6.50	**13.73**	23.79	34.20	3.52	43.03	20.36	0.00	0.00	3.48	**128.39**
4-Sep-24	0.00	29.86	29.32	**59.17**	4.71	0.00	0.00	**4.71**	0.00	0.07	8.51	0.00	0.00	1.93	0.00	10.50	**21.02**	14.61	25.45	1.13	40.04	18.44	0.00	0.00	0.85	**100.52**
5-Sep-24	0.00	22.40	30.54	**52.94**	4.12	0.00	0.00	**4.12**	0.00	1.07	11.43	0.00	1.34	2.03	0.00	12.13	**28.00**	11.96	23.87	2.96	39.39	5.49	0.00	0.00	2.49	**86.16**
6-Sep-24	0.32	13.23	34.62	**48.18**	2.50	0.00	0.00	**2.51**	0.00	1.21	15.23	0.00	7.34	2.11	0.00	17.43	**43.32**	11.96	14.51	0.06	35.58	0.00	0.00	0.00	0.00	**62.11**
7-Sep-24	1.15	0.00	30.74	**31.89**	2.08	0.00	0.00	**2.08**	0.00	1.05	10.62	0.00	7.33	2.14	0.00	12.58	**33.73**	11.97	19.43	1.30	36.13	0.00	0.00	0.00	0.96	**69.80**
8-Sep-24	5.10	0.00	21.25	**26.35**	0.00	0.00	0.00	**0.00**	0.00	0.10	6.07	0.00	7.33	2.00	0.00	6.77	**22.27**	11.98	31.36	3.88	40.10	0.00	0.00	0.00	4.51	**91.83**
9-Sep-24	7.31	0.00	27.10	**34.40**	0.00	0.00	0.00	**0.00**	0.00	0.74	12.27	0.00	7.34	2.06	0.00	11.69	**34.10**	18.06	27.36	1.17	41.28	0.00	0.00	0.00	1.63	**89.51**
10-Sep-24	9.96	0.00	24.48	**34.44**	0.00	0.00	0.00	**0.00**	0.00	0.61	9.55	0.00	5.47	2.11	0.00	9.22	**26.96**	20.78	31.00	2.04	42.60	1.62	0.00	0.00	2.98	**101.03**
11-Sep-24	12.38	0.00	33.10	**45.48**	0.00	0.00	0.00	**0.00**	0.00	1.71	19.82	0.00	5.34	2.09	0.00	19.05	**48.01**	12.13	16.91	0.00	37.90	4.95	0.00	0.00	0.01	**71.91**
12-Sep-24	16.10	0.00	35.96	**52.06**	0.00	0.00	0.00	**0.00**	0.00	3.81	28.14	0.00	27.77	2.40	0.00	27.24	**89.37**	7.17	9.71	0.00	32.86	0.00	0.00	0.00	0.00	**49.74**
13-Sep-24	17.42	0.00	37.14	**54.55**	0.00	0.00	0.00	**0.00**	0.00	5.55	32.17	0.00	41.39	2.62	0.00	31.27	**113.00**	7.17	6.98	0.00	26.94	0.00	0.00	0.00	0.00	**41.09**
14-Sep-24	17.42	0.00	45.97	**63.39**	0.00	0.00	0.00	**0.00**	10.52	9.55	39.47	0.00	36.14	2.27	0.00	38.73	**136.68**	1.96	1.33	0.00	21.27	0.00	0.00	0.00	0.00	**24.56**
15-Sep-24	17.41	0.00	40.43	**57.84**	0.00	0.00	0.00	**0.00**	21.44	5.77	26.92	0.00	41.57	2.01	0.00	25.61	**123.32**	0.00	15.46	0.24	26.14	0.00	0.00	0.00	0.08	**41.92**
16-Sep-24	17.42	0.00	49.82	**67.23**	0.00	0.00	0.00	**0.00**	23.87	3.95	33.74	0.00	46.57	1.93	0.00	32.71	**142.78**	0.00	8.80	0.00	21.87	0.00	0.00	0.00	0.00	**30.67**
17-Sep-24	17.42	0.00	50.30	**67.71**	0.00	0.00	0.00	**0.00**	22.48	3.83	36.91	0.00	38.22	2.20	0.00	34.71	**138.36**	0.00	5.35	0.00	19.86	0.00	0.00	0.00	0.00	**25.21**
18-Sep-24	17.42	0.00	54.46	**71.87**	0.00	0.00	0.00	**0.00**	21.23	7.99	44.19	0.00	33.90	2.13	0.00	41.19	**150.62**	0.00	0.46	0.00	20.76	0.00	0.00	0.00	0.00	**21.22**
19-Sep-24	17.44	0.00	51.82	**69.26**	0.00	0.00	0.00	**0.00**	18.64	7.77	41.51	0.00	25.28	2.32	0.00	38.90	**134.43**	0.00	0.91	0.00	20.84	0.00	0.00	0.00	0.00	**21.76**
20-Sep-24	17.42	0.00	44.14	**61.57**	0.00	0.00	0.00	**0.00**	22.61	3.39	30.68	0.00	29.10	2.35	0.00	28.55	**116.69**	0.00	6.75	0.06	24.81	0.00	0.00	0.00	0.02	**31.64**
21-Sep-24	12.63	0.00	37.78	**50.41**	0.00	0.00	0.00	**0.00**	12.11	1.07	17.16	0.00	14.60	2.42	0.00	17.68	**65.04**	0.00	16.81	1.87	28.92	0.00	0.00	0.00	0.92	**48.52**
22-Sep-24	4.87	0.00	30.35	**35.21**	0.00	0.00	0.00	**0.00**	12.13	0.00	7.35	0.00	14.60	2.26	0.00	8.31	**44.65**	0.00	26.44	4.59	36.06	0.00	0.00	0.00	3.56	**70.66**
23-Sep-24	4.87	0.00	26.64	**31.50**	0.00	0.00	0.00	**0.00**	11.90	0.00	4.60	0.00	14.60	2.28	0.00	5.69	**39.07**	0.00	28.14	5.36	37.72	0.00	0.00	0.00	4.20	**75.43**
24-Sep-24	4.88	0.00	22.41	**27.29**	0.00	0.00	0.00	**0.00**	7.29	0.00	3.47	0.00	14.61	2.32	0.00	5.02	**32.71**	0.00	36.64	11.77	39.13	0.00	0.00	0.00	8.69	**96.22**
25-Sep-24	2.67	0.00	25.42	**28.09**	0.00	0.00	0.00	**0.00**	4.41	0.00	3.97	0.00	14.60	2.28	0.00	5.65	**30.91**	2.77	37.73	7.43	43.64	0.00	0.00	0.00	5.63	**97.21**
26-Sep-24	3.55	0.00	36.40	**39.95**	0.00	0.00	0.00	**0.00**	0.00	0.12	12.22	0.00	14.60	2.23	0.00	16.72	**45.89**	7.18	17.31	0.37	37.76	0.00	0.00	0.00	0.21	**62.83**
27-Sep-24	4.83	7.28	48.40	**60.51**	0.00	0.00	0.00	**0.00**	0.00	6.40	30.91	0.00	22.05	2.27	0.00	35.36	**96.98**	7.16	2.85	0.00	27.97	0.00	0.00	0.00	0.00	**37.97**
28-Sep-24	10.49	26.81	51.04	**88.35**	0.00	0.00	0.00	**0.00**	0.00	17.77	39.92	0.00	34.48	2.35	0.00	44.24	**138.77**	6.67	0.26	0.00	22.23	0.00	0.00	0.00	0.00	**29.16**
29-Sep-24	12.59	28.94	40.45	**81.98**	0.00	0.00	0.00	**0.00**	0.00	2.89	25.67	0.00	14.59	2.38	0.00	27.67	**73.20**	7.15	7.45	0.09	28.84	0.00	0.00	0.00	0.00	**43.54**
30-Sep-24	12.60	28.95	41.67	**83.23**	0.00	0.00	0.00	**0.00**	0.00	1.59	27.95	0.00	31.47	2.52	0.00	28.67	**92.19**	7.15	5.29	0.00	28.86	0.00	0.00	0.00	0.00	**41.29**
TOTAL	**265.65**	**203.86**	**1064.60**	**1534.11**	**35.11**	**0.01**	**0.00**	**35.12**	**188.65**	**88.01**	**588.28**	**0.00**	**557.38**	**65.88**	**0.04**	**602.35**	**2090.59**	**233.01**	**553.25**	**66.92**	**997.65**	**55.86**	**0.00**	**0.01**	**62.04**	**1968.74**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 से मार्च 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
कुल Total	**137.84**	**4281.50**	**638.42**	**1634.36**	**4160.53**	**0.00**	**4.89**	**0.00**

* Based on daily operational data

16.1 Import from neighbouring countries during Sep 2024

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Sep-24	13.62	5.52	1.52	0.89	6.55	9.87	1.42	0.88	0.00	0.00	1.36	16.48	0.00	0.00
2-Sep-24	14.05	5.78	2.02	0.92	6.43	9.68	1.18	0.96	0.00	0.00	1.29	16.74	0.00	0.00
3-Sep-24	13.93	5.57	1.91	0.79	6.51	9.81	1.07	0.87	0.00	0.00	1.27	15.90	0.00	0.00
4-Sep-24	14.45	4.91	1.34	0.63	6.21	9.34	1.45	0.82	0.00	0.00	1.38	16.65	0.00	0.00
5-Sep-24	15.03	3.75	1.06	0.43	6.15	11.79	1.54	0.82	0.00	0.00	1.41	17.09	0.00	0.00
6-Sep-24	16.13	3.45	1.96	0.94	4.52	13.54	1.25	0.63	0.00	0.00	1.47	17.51	0.62	0.00
7-Sep-24	14.68	5.06	2.14	0.96	4.40	13.17	1.43	0.72	0.00	0.00	1.46	17.79	0.85	0.00
8-Sep-24	16.09	4.05	1.86	0.77	4.36	13.04	1.30	0.74	0.00	0.00	1.37	16.23	0.88	0.00
9-Sep-24	15.90	3.93	1.62	0.71	4.30	12.87	1.32	0.75	0.00	0.00	1.34	16.18	0.47	0.00
10-Sep-24	15.82	3.88	1.61	0.77	4.30	12.86	1.39	0.67	0.00	0.00	1.30	15.73	0.48	0.00
11-Sep-24	16.34	4.20	1.65	0.52	4.15	13.13	1.23	0.61	0.00	0.00	1.32	15.11	0.40	0.00
12-Sep-24	16.01	3.99	1.69	0.67	4.31	13.18	1.21	0.60	0.00	0.00	0.88	14.53	0.43	0.00
13-Sep-24	15.81	3.87	1.62	0.70	4.09	12.86	1.39	0.66	0.00	0.00	0.87	14.39	1.07	0.00
14-Sep-24	16.24	4.14	1.63	0.51	4.39	13.42	1.38	0.69	0.00	0.00	0.68	15.72	0.99	0.00
15-Sep-24	16.41	4.25	1.58	0.43	4.43	13.52	1.40	0.67	0.00	0.00	1.17	14.75	1.12	0.00
16-Sep-24	16.44	4.20	1.72	0.68	4.30	13.15	1.44	0.83	0.00	0.00	1.19	15.32	1.15	0.00
17-Sep-24	16.64	4.32	1.86	0.95	4.14	12.64	1.44	0.79	0.00	0.00	1.44	18.29	1.38	0.00
18-Sep-24	16.25	4.14	2.03	1.11	3.84	11.37	1.43	0.64	0.00	0.00	1.27	16.66	1.29	0.00
19-Sep-24	13.78	3.28	1.85	0.93	3.57	10.22	1.59	0.81	0.00	0.00	1.12	15.74	1.03	0.00
20-Sep-24	13.64	3.16	1.76	0.81	3.82	11.59	1.54	0.79	0.00	0.00	1.06	15.52	1.33	0.00
21-Sep-24	15.78	3.80	1.72	1.03	3.96	12.05	1.47	0.78	0.00	0.00	1.18	16.26	1.50	0.00
22-Sep-24	16.09	3.99	1.69	0.99	3.51	10.69	1.38	0.60	0.00	0.00	0.95	8.37	2.07	0.00
23-Sep-24	15.36	2.29	1.61	0.94	3.32	10.06	1.44	0.60	0.00	0.00	0.76	12.66	2.16	0.00
24-Sep-24	15.30	3.82	1.66	0.71	4.15	12.63	1.44	0.55	0.00	0.00	0.70	13.96	1.51	0.00
25-Sep-24	16.24	4.19	1.56	0.66	3.92	11.81	1.31	0.69	0.00	0.00	1.00	16.36	0.97	0.00
26-Sep-24	16.67	4.33	1.77	0.55	4.53	13.57	1.17	0.67	0.00	0.00	1.35	17.84	0.70	0.00
27-Sep-24	20.20	1.84	1.33	0.00	4.52	13.52	1.22	0.70	0.00	0.00	1.37	16.79	0.60	0.00
28-Sep-24	15.84	3.84	0.00	0.21	4.42	13.28	1.17	0.62	0.00	0.00	1.25	2.05	0.75	0.00
29-Sep-24	16.72	4.33	1.72	0.36	4.55	13.70	1.27	0.64	0.00	0.00	1.38	5.74	0.04	0.00
30-Sep-24	15.98	4.11	1.87	0.58	4.50	13.56	1.31	0.75	0.00	0.00	1.27	4.73	0.00	0.00
Total	**471.45**	**121.99**	**49.37**	**21.16**	**136.13**	**365.93**	**40.58**	**21.55**	**0.00**	**0.00**	**35.85**	**437.07**	**23.79**	**0.00**

16.2 Export to neighbouring countries during Sep 2024

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.95	1.57	0.00	0.00	0.00	0.01
2-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.20	1.54	0.00	0.00	0.00	0.03
3-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.22	1.58	0.00	0.00	0.00	0.03
4-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.23	1.55	0.00	0.00	0.00	0.03
5-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.17	1.57	0.00	0.00	0.00	0.03
6-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.07	1.30	0.00	0.00	0.00	0.03
7-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.37	1.55	0.00	0.00	0.00	0.03
8-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.33	1.62	0.00	0.00	0.00	0.03
9-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.19	1.78	0.00	0.00	0.00	0.03
10-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.42	1.76	0.00	0.00	0.00	0.02
11-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.95	1.95	0.00	0.00	0.00	0.03
12-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.78	1.74	0.00	0.00	0.00	0.03
13-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.99	1.48	0.00	0.00	0.00	0.03
14-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.86	1.20	0.00	0.00	0.00	0.00
15-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.41	1.14	0.00	0.00	0.00	0.00
16-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.94	1.33	0.00	0.00	0.00	0.03
17-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.55	1.55	0.00	0.00	0.00	0.01
18-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.84	1.87	0.00	0.00	0.00	0.02
19-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.70	1.64	0.00	0.00	0.00	0.03
20-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.87	1.58	0.00	0.00	0.00	0.04
21-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.33	1.45	0.00	0.00	0.00	0.03
22-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.65	1.61	0.00	0.00	0.00	0.02
23-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.41	1.75	0.00	0.00	0.00	0.00
24-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.70	1.58	0.00	0.00	0.00	0.03
25-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.67	1.42	0.00	0.00	0.00	0.03
26-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.67	1.20	0.00	0.00	0.00	0.03
27-Sep-24	0.00	0.00	0.00	0.05	0.00	0.00	0.00	0.00	21.73	1.32	0.00	0.00	0.00	0.01
28-Sep-24	0.00	0.00	0.18	0.00	0.00	0.00	0.00	0.00	21.78	1.49	0.00	0.00	0.00	0.03
29-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.79	1.63	0.00	0.00	0.00	0.03
30-Sep-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.54	1.62	0.00	0.00	0.00	0.03
Total	**0.00**	**0.00**	**0.18**	**0.05**	**0.00**	**0.00**	**0.00**	**0.00**	**585.31**	**46.37**	**0.00**	**0.00**	**0.00**	**0.75**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – सितम्बर 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - SEPTEMBER 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

सितम्बर 2024 SEPTEMBER 2024			Apr'24- Sep'24	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	567	4461	4592	23521
प.क्षे. WR	431	565	2267	3652
द.क्षे. SR	332	428	2161	7843
पू.क्षे. ER	395	2008	2231	10798
पूर्वोत्तर क्षे. NER	23	110	470	459
कुल TOTAL	1748	7572	11721	46273

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
कुल TOTAL	56295	51772	11721	46273

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION ⟹ / सप्ताह WEEK ⇩	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
26.08.24 to 01.09.24	177.16	181.58	14.38	125.74	33.32
02.09.24 to 08.09.24	180.69	167.32	28.33	123.31	39.08
09.09.24 to 15.09.24	185.98	149.20	31.14	125.20	33.47
16.09.24 to 22.09.24	278.04	257.20	47.86	249.31	88.08
23.09.24 to 29.09.24	137.84	283.86	51.04	240.99	88.08^

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- सितम्बर 2024 EXCHANGES THROUGH POWER EXCHANGES -SEPTEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED		66.43	0.02
2	ADANI GREEN ENERGY TWENTY FIVE LIMITED_infirm		22.39	0.00
3	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		25.31	0.00
4	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		9.04	0.00
5	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		41.96	0.00
6	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED (infirm)		3.30	0.00
7	Adept Renewable Technologies Private Limited		27.89	0.00
8	Amp Energy Green Six Private Limited		24.78	0.00
9	Amplus Ages Private Limited		9.16	0.00
10	Ayana Renewable Power Three Private Limited Infirm		10.86	0.00
11	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		6.18	0.02
12	Chandigarh (UT)		32.36	6.53
13	Delhi		213.39	150.00
14	Government of Himachal Pradesh _ Chamera1HEP		23.56	1.26
15	Government of Himachal Pradesh _ Chamera3HEP		15.66	1.32
16	Government of Himachal Pradesh_ CHAMERA2HEP		18.47	1.90
17	Government of Himachal Pradesh_BairasuilHEP		7.40	0.82
18	Government of Himachal Pradesh_Koldam HEP		19.32	4.68
19	Government of Himachal Pradesh_NJHPS		27.38	6.73
20	Government of Himachal Pradesh_Parbati3HEP		12.77	1.57
21	Government of Himachal Pradesh_RampurHEP		26.75	1.35
22	Grian Energy Private Limited		13.88	0.00
23	Haryana		531.10	112.73
24	Himachal Pradesh		198.89	18.81
25	IGSTPS JHAJJAR		14.78	0.00
26	JUNIPER GREEN COSMIC PRIVATE LIMITED_INFIRM		8.70	0.18
27	Jammu Kashmir		118.34	92.60
28	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		100.78	0.30
29	NEA Nepal Upper Chameliya Hydropower Project		16.17	0.00
30	NEA Nepal Upper Kalangagad Hydropower Project new	उत्तरी क्षेत्र NR	24.80	0.00
31	NTPC Dadri Stage I		5.80	0.00
32	NTPC Dadri Stage II		6.59	0.00
33	NTPC Rihand stage I		7.44	0.00
34	NTPC Rihand stage II		15.89	0.00
35	NTPC Rihand stage III		17.06	0.00
36	NTPC Singrauli		32.70	0.00
37	NTPC Tanda Stage II		18.90	0.00
38	NTPC Unchahar Stage I		7.46	0.00
39	NTPC Unchahar Stage II		6.79	0.00
40	NTPC Unchahar Stage III		0.58	0.00
41	NTPC Unchahar Stage IV		10.99	0.00
42	North Central Railway Prayagraj		0.00	40.17
43	Onevolt Energy Private Limited		9.53	0.00
44	Punjab		77.24	867.53

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- सितम्बर 2024 EXCHANGES THROUGH POWER EXCHANGES -SEPTEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	RENEW SURYA PRATAP PRIVATE LIMITED		41.82	0.00
46	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.30	0.00
47	Rajasthan		93.49	818.45
48	ReNew Surya Ravi Private Limited		44.78	0.00
49	SHREE CEMENT LIMITED TPS		50.26	0.70
50	Sainj HEP		33.66	0.80
51	Serentica Renewables India 4 Private Limited		2.35	0.00
52	Singoli Bhatwari HEP		52.21	0.34
53	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		7.80	0.00
54	TPSL 200MW TPTCL Banderwala		18.23	0.00
55	TPSL Banderwala SECI 100_INF		3.59	0.00
56	Transition Energy Services Private Limited		16.13	0.00
57	Transition Green Energy Private Limited		24.97	0.00
58	Uttar Pradesh		666.42	460.66
59	Uttarakhand		66.63	95.45
60	ACB (INDIA) LIMITED		47.19	1.01
61	ADANI GREEN ENERGY TWENTY SIX A LIMITED_infirm		0.47	0.00
62	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_Infirm		21.63	0.00
63	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_infirm		66.31	0.00
64	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		147.37	0.00
65	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		44.92	0.00
66	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		6.10	0.00
67	Adani Green Energy Twenty Five A Limited_Infirm		17.00	0.00
68	Adani Green Energy Twenty Five B Limited_infirm		94.19	0.00
69	Adani Green Energy Twenty Six B Limited_infirm		22.21	0.00
70	Adani Power Limited - Raigarh TPP		114.38	3.59
71	Adani Power Limited-Raipur TPP		149.88	0.00
72	ArcelorMittal Nippon Steel India Limited		0.00	156.45
73	BHARAT ALUMINIUM COMPANY LTD		5.92	0.00
74	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	140.27
75	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		2.53	0.00
76	Chhattisgarh		97.48	174.03
77	D B Power Limited		102.78	0.00
78	DGEN MEGA POWER PROJECT		17.25	0.00
79	DHARIWAL STU OTH		1.23	0.00
80	Daman and Diu - Dadra and Nagar Haveli		0.25	345.86
81	Dhariwal ISTS		0.71	0.00
82	GMR Warora Energy Limited		10.17	0.00
83	Goa WR		4.01	20.95
84	Gujarat		52.49	1088.96
85	Jaypee Nigrie Super Thermal Power Plant		38.49	0.00
86	Jhabua Power Limited		21.38	2.32
87	Jindal Power Limited, Stage-1		104.03	0.00
88	Jindal Power Limited, Stage-2		214.10	15.45

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- सितम्बर 2024 EXCHANGES THROUGH POWER EXCHANGES -SEPTEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
89	Jindal Steel & Power Ltd , DCPP	पश्चिमी क्षेत्र WR	108.91	0.00
90	MAHAN ENERGEN LIMITED U#1		117.52	0.00
91	MAHAN ENERGEN LIMITED U#2		64.27	0.00
92	MB POWER (MADHYA PRADESH) LIMITED		12.13	14.78
93	Madhya Pradesh		640.56	50.94
94	Maharashtra		75.79	521.35
95	Maruti Clean Coal and Power Limited		14.20	0.00
96	NREL-Dayapar Wind		6.91	0.00
97	NTPC Gadarwara		9.40	0.00
98	NTPC Jhanor Gandhar GPS		0.00	0.61
99	NTPC Kawas GPS		0.00	0.65
100	NTPC Korba Stage I &II		10.35	0.00
101	NTPC Korba Stage III		3.91	0.00
102	NTPC Lara Stage I		9.10	0.00
103	NTPC Mouda Stage I		2.80	0.00
104	NTPC Mouda Stage II		1.46	0.00
105	NTPC SAIL POWER COMPANY LIMITED		0.12	0.00
106	NTPC SOLAPUR SOLAR PV Station		0.01	0.00
107	NTPC Sipat Stage I		15.24	0.00
108	NTPC Sipat Stage II		7.80	0.00
109	NTPC Solapur		4.02	0.00
110	NTPC Vindhyachal Stage I		6.00	0.00
111	NTPC Vindhyachal Stage II		5.42	0.00
112	NTPC Vindhyachal Stage III		5.42	0.00
113	NTPC Vindhyachal Stage IV		7.57	0.00
114	NTPC Vindhyachal Stage V		3.93	0.00
115	NTPC khargone		5.58	0.00
116	Nani Virani Wind Energy Private Limited		0.62	0.00
117	R.K.M POWERGEN PRIVATE LIMITED		5.68	0.00
118	Ratnagiri Gas & Power Private Limited		0.00	0.81
119	SKS Power Generation Chhattisgarh Limited		13.97	8.98
120	Sasan Power Limited		26.74	0.00
121	TRN ENERGY PRIVATE LIMITED		25.40	0.00
122	The Tata Power Co Ltd (MTPS)		0.72	8.09
123	WIND FIVE RENERGY LIMITED		8.52	0.00
124	Andhra Pradesh		203.67	308.01
125	COASTAL ENERGEN PRIVATE LIMITED		0.75	0.00
126	Goa SR		0.02	9.20
127	IL&FS TAMIL NADU POWER COMPANY LIMITED		5.05	0.00
128	JINDAL POWER LIMITED SIMHAPURI		29.29	1.18
129	JSW RENEW ENERGY LIMITED INFIRM		5.14	0.00
130	Karnataka		217.33	444.95
131	Kerala		6.85	384.93
132	MEENAKSHI ENERGY LIMITED		27.68	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- सितम्बर 2024 EXCHANGES THROUGH POWER EXCHANGES -SEPTEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
133	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION	दक्षिणी क्षेत्र SR	7.89	0.00
134	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		3.95	0.00
135	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		1.27	0.00
136	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		4.04	0.00
137	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		4.79	0.00
138	NLC Tamilnadu Power Limited		24.93	0.00
139	NTECL VALLUR		2.19	0.00
140	NTPC KUDGI		6.61	0.00
141	NTPC Ramagundam Stage I &II		5.91	0.00
142	NTPC Ramagundam Stage III		1.89	0.00
143	NTPC Simhadri Stage I		1.76	0.00
144	NTPC Simhadri Stage II		8.27	0.00
145	NTPC Talcher Super Thermal Power Station Stage II		26.40	0.00
146	NTPC Telangana		10.33	0.00
147	OSTRO KANNADA POWER PRIVATE LIMITED		20.97	0.00
148	Pondicherry UT		9.16	0.31
149	RENEW SURYA OJAS PRIVATE LIMITED-Wind		99.81	0.00
150	RENEW SURYA OJAS PRIVATE LIMITED_INFIRM		7.54	0.00
151	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		10.61	0.00
152	Ramagundam Floating solar		4.11	0.00
153	SEIL ENERGY INDIA LIMITED		73.59	0.00
154	SEIL Energy India Limited Project II		11.32	0.00
155	SEMBCORP GREEN INFRA PRIVATE LIMITED (INFIRM)		1.65	0.00
156	Serentica Renewables India 1 Private Limited		2.48	0.00
157	Serentica Renewables India 1 Private Limited- Koppal (Infirm)		0.14	0.00
158	Simhadri FSP 15 MW		1.28	0.00
159	Simhadri Floating solar (10 MW)		0.68	0.00
160	Tamil Nadu		323.94	327.38
161	Telangana		127.55	1323.66
162	VENA ENERGY VIDYUTH PRIVATE LIMITED_INFIRM		7.24	0.00
163	VENA ENERGY VIDYUTH PRIVATE LIMITED_SOLAR_INFIRM		0.84	0.00
164	ADHUNIK POWER & NATURAL RESOURCES LIMITED		3.47	0.00
165	Basochhu Hydropower Plant Bhutan		32.45	0.00
166	Bihar		402.54	67.18
167	Chilime Hydro Power Project NEPAL ELECTRICITY AUTHORITY		14.10	0.00
168	Chuzachen HEP		0.04	0.00
169	DEVIGHAT NEPAL ELECTRICITY AUTHORITY		9.49	0.00
170	Damodar Valley Corporation		37.79	137.01
171	GMR KAMALANGA ENERGY LTD-CTU		2.02	0.00
172	IND BARATH ENERGY UTKAL LIMITED		23.14	0.00
173	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		1.07	0.00
174	Jharkhand		71.72	92.50
175	Jindal India Thermal Power Limited		202.30	0.00
176	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		47.87	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- सितम्बर 2024 EXCHANGES THROUGH POWER EXCHANGES -SEPTEMBER 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
177	KANTI BIJLEE UTPADAN NIGAM LIMITED	पूर्वी क्षेत्र ER	23.32	0.00
178	Kabeli B-1 Hydro Power Project NEPAL ELECTRICITY AUTHORITY		15.92	0.00
179	LIKHU-iV NEA		31.69	0.00
180	Lower Modi Hydro Power Project NEPAL ELECTRICITY AUTHORITY		12.79	0.00
181	MAITHON POWER LIMITED		11.32	0.00
182	MARSYANGDI NEPAL ELECTRICITY AUTHORITY		39.07	0.00
183	NABINAGAR POWER GENERATING COMPANY LIMITED		64.68	0.00
184	NEA Nepal Upper Balephi A Hydropower Project1		22.88	0.00
185	NEA Nepal Upper Dordi A Hydropower Project		15.92	0.00
186	NEPAL ELECTRICITY AUTHORITY-MIDDLE MARSYANGDI		38.21	0.00
187	NTPC BARH Stage I		8.69	0.00
188	NTPC BARH Stage II		19.95	0.00
189	NTPC Darlipali		8.17	0.00
190	NTPC Farakka stage I		49.61	0.00
191	NTPC Farakka stage III		11.07	0.00
192	NTPC Kahalgaon stage I		10.53	0.00
193	NTPC Kahalgaon stage II		15.70	0.00
194	NTPC North Karanpura STPS		31.92	0.00
195	NTPC Talcher Stage I		7.21	0.00
196	NTPP BRBCL		7.86	0.00
197	Nikachhu Hydropower Project		18.78	0.00
198	Odisha		432.23	164.63
199	Sikkim		17.69	3.63
200	Solu Hydropower Project NEPAL ELECTRICITY AUTHORITY		15.01	0.00
201	TRISHULI NEPAL ELECTRICITY AUTHORITY		15.15	0.00
202	Tashiding HEP, Shiga Energy Private Limited		1.12	0.00
203	West Bengal		262.48	533.51
204	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	0.47	0.00
205	ASSAM GAS BASED POWER STATION		1.88	0.00
206	Arunachal Pradesh		19.22	0.33
207	Assam		101.00	132.09
208	Bongaigaon Thermal Power Station NTPC		9.88	0.00
209	KAMENG HYDRO POWER STATION		5.29	0.00
210	Manipur		5.32	12.60
211	Meghalaya		18.19	9.02
212	Mizoram		20.80	0.09
213	Nagaland		4.03	0.66
214	Palatana Plant		18.18	0.00
215	Tripura		5.69	18.96
	Total		9212	9212

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : SEPTEMBER 2024

RE Source & Unit wise break up (01.09.2024-30.09.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	0	0	0	0
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1	1	0	1
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1**	**1**	**0**	**1**

RECs Issued (01.09.2024-30.09.2024)

Sr.No.	Non Solar	Solar	Total
1	1275836	85305	1361141

Redemption of REC (01.09.2024-30.09.2024)

Sr.No.	Non Solar	Solar	Total
1	1753428	3719	1757147

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : SEPTEMBER 2024

RE Source & Unit wise break up (Apr'24-Sep'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	19	4	20	5
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	96	17	82	13
5	Small Hydro	24	1	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**139**	**22**	**138**	**20**

RECs Issued (Apr'24-Sep'24)

Sr.No.	Non Solar	Solar	Total
1	27639463	509696	28149159

Redemption of REC (Apr'24-Sep'24)

Sr.No.	Non Solar	Solar	Total
1	14467072	168939	14636011

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : SEPTEMBER 2024

RE Source & Unit wise break up Since Inception to Sep'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3152	534	2997	536
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	1731	591	1562	495
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**6993**	**1299**	**6216**	**1168**

RECs Issued since Inception to Sep'24

Sr.No.	Non Solar	Solar	Total
1	142744501	14050074	156794575

Redemption of REC since Inception to Sep'24

Sr.No.	Non Solar	Solar	Total
1	92971401	12618196	105589597

REC Closing balance as on 30.09.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of Sept 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	Himachal Pradesh	05-09-2024 11:40	05-09-2024 13:30	01:50	0	90	0.000	0.138	58567	65019	i)400/220kV Dehar(BBMB) has double main bus arrangement at 400kV voltage level and single bus arrangement at 220kV voltage level. ii)As reported, at 11:40 hrs, 220 KV Dehar-Gangawal (BBMB) Ckt-2 tripped on R-N phase to earth fault with fault distance of 16.28km and fault current of Ir=~4.8kA from Dehar end. Line tripped on zone-1 distance protection from Dehar end. iii)At the same time 132 KV Dehar(BBMB)-Kangoo(HP) (HPPTCL) Ckt & 220 KV Dehar(BBMB)-Kangoo(HP) (HP) Ckt-1 also tripped from Dehar end. 220 KV Dehar(BBMB)-Kangoo(HP) (HP) Ckt-1 tripped on backup protection. Reason of tripping of 132 KV Dehar(BBMB)-Kangoo(HP) (HPPTCL) Ckt is yet to be received. iv)As per PMU at Panchkula(PG), R-N phase to earth fault with fault clearing time of 120 msec is observed. v)As per SCADA, change in demand of approx. 90 MW is observed in HP control area.	1)220 KV Dehar(BBMB)-Kangoo(HP) (HP) Ckt-1 2)220 KV Dehar-Ganguwal (BBMB) Ckt-2 3)132 KV Dehar(BBMB)-Kangoo(HP) (HPPTCL) Ckt
2	GD-1	Uttarakhand & Himachal Pradesh	05-09-2024 11:54	05-09-2024 12:25	00:31	335	189	0.573	0.290	58456	65133	i)During antecedent condition, all the four 30MW units of Khodri HEP, all four 60 MW units of Chhibro HEP, 11.25MW Unit-2 & Unit-3 of Dhakrani HEP and both 30 MW units of Giri HEP were running and total active power generation of Khodri HEP, Chhibro HEP, Dhakrani HEP & Giri HEP were approx. 90 MW, 200 MW, 19 MW & 58 MW (as per SCADA). Total generation of Chhibro HEP was evacuating through 220 KV Khodri-Chhibro (UK) Ckt-1 & 2. 11.25 MW Unit-1 of Dhakrani HEP and 220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt were not in service during the event. ii)As reported, at 11:54 hrs, 220 KV Khodri(UK)-Sarsawan(UP) (UP) Ckt tripped on R-N phase to earth fault with fault distance of 44 km & 61 km and fault current of 2.5 kA & 2 kA from Khodri(UK) and Sarsawan(UP) end respectively. Line tripped on zone-1 distance protection from both ends. iii)At the same time, 220 KV Khodri(UK)-Majri/Giri(HP) (UK) D/C tripped on over voltage protection from both the ends and 30 MW Giri – Unit-1 & 220 KV Khodri – Jhajra (UK) Ckt also tripped (exact reason of tripping is yet to be received). iv)Due to tripping of 220kV lines from Khodri(UK) end, all the four 30MW units of Khodri(UK), all four 60 MW units of Chhibro(UK) and 11.25MW Unit-2 & Unit-3 of Dhakrani(UK) tripped due to loss of evacuation path. v)As per PMU at Saharanpur(PG), R-N phase to earth fault with fault clearing time of 80msec is observe. vi)Due to tripping all 220kV lines at Khodri(UK) and all generating Units at Khodri HEP(UK), Chhibro HEP(UK) and Dhakrani HEP(UK), blackout occurred at 220kV Khodri(UK), 220kV Chhibro(UK) & 132kV Dhakrani(UK). vii)As per SCADA, change in demand and generation of approx. 50 MW and 308 MW respectively in Uttarakhand control area. However, SLDC-Uttarakhand reported generation loss of approx. 307 MW and load loss of approx. 29 MW in Uttarakhand control area. viii)As per SCADA, change in demand and generation of approx. 140 MW and 28 MW in HP control area. However, SLDC-HP reported load loss of approx. 160 MW in HP control area.	1)220 KV Khodri(UK)-Majri/Giri(HP) (UK) Ckt-1 2)220 KV Khodri(UK)-Majri/Giri(HP) (UK) Ckt-2 3)220 KV Khodri(UK)-Sarsawan(UP) (UP) Ckt 4)220 KV Khodri – Jhajra (UK) Ckt 5)30 MW Khodri Unit-1 6)30 MW Khodri Unit-2 7)30 MW Khodri Unit-3 8)30 MW Khodri Unit-4 9)60 MW Chhibro Unit-1 10)60 MW Chhibro Unit-2 11)60 MW Chhibro Unit-3 12)60 MW Chhibro Unit-4 13)11.25 MW Dhakrani Unit-2 14)11.25 MW Dhakrani Unit-3 15)30 MW Giri – Unit-1
3	GD-1	Uttar Pradesh	10-09-2024 13:18	10-09-2024 14:05	00:47	0	268	0.000	0.407	59493	65808	i)220kV Nara(UP) has main and transfer bus scheme at 220kV level. ii)As reported, at 13:18 hrs, due to lightning and inclement weather conditions, R-N phase to earth fault occurred on 220kV main bus which led to bus bar protection operation at Nara(UP) S/s. iii)Due to bus bar protection operation, all elements connected to 220kV main bus i.e. 220 KV Meerut(PG)-Nara(UP) (PG) Ckt, 220 KV Nara(UP)-Roorkee(UK) (UP) Ckt, 220 KV Nara-Jansath (UP) Ckt, 220 KV Nara-Muzaffarnagar (UP) Ckt, 200/132kV 160MVA ICT-1 & 200MVA ICT-2 tripped at Nara(UP) S/s which led to blackout at 220kV Nara(UP) S/s. iv)As per PMU at Roorkee(PG), R-N phase to earth fault with delayed fault clearance time of 320msec is observed. v)As per SCADA, change in demand of approx. 120 MW & 60 MW in UP and Uttarakhand control area respectively. However, SLDC-UP has reported load loss of approx. 208 MW in UP control area.	1)220 KV Meerut(PG)-Nara(UP) (PG) Ckt 2)220 KV Nara(UP)-Roorkee(UK) (UP) Ckt 3)220 KV Nara-Jansath (UP) Ckt 4)220 KV Nara-Muzaffarnagar (UP) Ckt 5)200/132kV 160MVA ICT-1 at Nara(UP) 6)200/132kV 200MVA ICT-2 at Nara(UP)
4	GD-1	Uttarakhand, Himachal Pradesh & Uttar Pradesh	11-09-2024 08:17	11-09-2024 08:39	00:22	308	233	0.603	0.403	51107	57813	i)During antecedent condition, all the four 30MW units of Khodri HEP, all four 60 MW units of Chhibro HEP, 11.25MW Unit-2 & Unit-3 of Dhakrani HEP and both 30 MW units of Giri HEP were running and total active power generation of Khodri HEP, Chhibro HEP, Dhakrani HEP & Giri HEP were approx. 90 MW, 200 MW, 19 MW & 58 MW (as per SCADA). Total generation of Chhibro HEP was evacuating through 220 KV Khodri-Chhibro (UK) Ckt-1 & 2. 11.25 MW Unit-1 of Dhakrani HEP was not in service during the event.ii)As reported, at 08:17 hrs, B-phase LA of HV side of 220/132kV 100 MVA ICT burst which caused B-N phase to earth fault. On this fault, 220/132kV 100 MVA ICT didn't trip (exact reason yet to be received).iii)On this fault, all four 30MW units of Khodri HEP & all four 60 MW units of Chhibro HEP tripped on over current protection. 220 KV Khodri(UK)-Giri(HP) (UK) Ckt-2 tripped on directional earth fault protection from Giri(HP) end.iv)220kV lines from Khodri(UK) to Giri(HP) ckt-1, Sarsawan(UP), Jhajra(UK), Chibro(UK) ckt-1 & 2 and Saharanpur(UP) ckt tripped on zone-2 distance protection operation from remote end. It is reported that, at Khodri(UK) end, time setting in zone-4 distance protection is kept at 1000msec. Due to more time delay in zone-4 distance protection at Khodri(UK) end as compared to time delay of zone-2 distance protection of remote ends, all 220kV lines (except 220 KV Khodri(UK)-Giri(HP) (UK) Ckt-2) from Khodri(UK) S/s tripped from remote ends. v)At the same time, 11.25 MW Dhakrani Unit-2 & Unit-3 also tripped (exact reason of tripping is yet to be received).vi)As per PMU at Saharanpur(PG), B-N phase to earth fault with delayed fault clearing time of 440 msec is observed. vii)Due to tripping all 220kV lines at Khodri(UK) and all generating Units at Khodri HEP(UK), Chhibro HEP(UK) and Dhakrani HEP(UK), blackout occurred at 220kV Khodri(UK), 220kV Chhibro(UK) & 132kV Dhakrani(UK). viii)As per SCADA, change in demand and generation of approx. 50 MW and 310 MW respectively in Uttarakhand control area. However, SLDC-Uttarakhand reported generation loss of approx. 308 MW and load loss of approx. 38 MW in Uttarakhand control area.ix)As per SCADA, change in demand of approx. 195 MW in HP control area.	1)220 KV Khodri(UK)-Majri/Giri(HP) (UK) Ckt-2 2)220 KV Khodri(UK)-Majri/Giri(HP) (UK) Ckt-1 3)220 KV Khodri(UK)-Sarsawan(UP) (UP) Ckt 4)220 KV Khodri – Jhajra (UK) Ckt 5)220 KV Khodri(UK)-Saharanpur(UP) (UP) Ckt 6)30 MW Khodri Unit-1 7)30 MW Khodri Unit-2 8)30 MW Khodri Unit-3 9)30 MW Khodri Unit-4 10)60 MW Chhibro Unit-1 11)60 MW Chhibro Unit-2 12)60 MW Chhibro Unit-3 13)60 MW Chhibro Unit-4 14)11.25 MW Dhakrani Unit-2 15)11.25 MW Dhakrani Unit-3 16)220kV Khodri-Chibro (UK) Ckt-1 17)220kV Khodri-Chibro (UK) Ckt-2
5	GI-2	Uttar Pradesh	11-09-2024 10:03	11-09-2024 11:05	01:02	350	0	0.597	0.000	58587	64190	i)765/400kV Obra-C TPS(UP) has one and half breaker bus scheme at 400kV & 765kV level.ii)During antecedent condition, 660 MW Unit-1 at Obra-C TPS was generating approx. 350 MW and 400 KV Jaunpur -Obra_C_TPS (UP) Ckt was anti-theft charged from Obra-C end. iii)As reported, at 10:03 hrs, 400 KV Jaunpur -Obra_C_TPS (UP) Ckt tripped on R-N phase to earth fault with fault current of Ir=~6.8kA and fault distance of approx. 35.49km from Obra-C TPS(UP) end. Line tripped on zone-1 distance protection from Obra-C end. iv)At the same time, 400 KV Obra_C_TPS-Obra_B (UP) Ckt tripped on over current protection from Obra-B end. During the event, the current recorded was approx. Ir=~7.5kA at Obra-B end. It is reported that over current protection is enabled with current setting of 2kA and time setting of definite time characteristic without any time delay at Obra-B end for 400 KV Obra_C_TPS-Obra_B (UP) Ckt.v)Due to tripping of 400 KV Obra_C_TPS-Obra_B (UP) Ckt, both 100MVA station transformers became dead with led to tripping of 660 MW Obra C_TPS(UP) – Unit-1 due to disruption in auxiliary supply of Unit-1. It is reported that, auxiliary supply of 660 MW Unit-1 at Obra-C TPS is tapped from both 100 MVA STFs(station transformer) and 40 MVA UAT(Unit auxiliary transformer) which does not provide the redundancy in the auxiliary supply of 660 MW Unit-1 at Obra-C TPS.vi)As per PMU at Anpara(UP), R-N phase to earth fault with fault clearance time of 80 msec is observed.vii)As per DR of Obra-B end of 400 KV Obra_C_TPS-Obra_B (UP) Ckt, line tripped on over current protection with max current observed was approx. Ir=~7.5kA.viii)As per SCADA, no change in demand of UP control area. However, SLDC-UP has reported generation loss of approx. 350 MW at Obra-C TPS (as per SCADA also).	1)400 KV Obra_C_TPS-Obra_B (UP) Ckt 2)400 KV Jaunpur -Obra_C_TPS (UP) Ckt 3)660MW OBRA C_TPS(UP) - UNIT 1

Details of Grid Events during the Month of Sept 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
6	GI-2	Rajasthan	13-09-2024 02:49	13-09-2024 05:01	02:12	1125	0	2.579	0.000	43616	52184	i)400/220kV Akal(RS) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level.ii)During antecedent condition, 400/220 kV 500 MVA ICT-1 & ICT-2 were connected to 400kV bus-1 and 400/220 kV 315 MVA ICT-3 & 500 MVA ICT-4 were connected to 400kV bus-2. iii)As reported, at 02:49 hrs, Y-phase jumper of 220kV bus-1 of 220kV Akal-Bhensara Ckt-1 and R-phase jumper of 220kV bus-2 of 220kV Akal-Bhensara Ckt-2 snapped which created bus fault on both 220kV buses at Akal(RS). iv) On this fault, 400/220 kV 500 MVA ICT-1, ICT-2 tripped on earth fault protection and 400/220 kV 315 MVA ICT-3 & 500 MVA ICT-4 tripped on over current protection at Akal(RS) S/s. 220kV lines from Akal(RS) to Giral & Amarsagar tripped on zone-4 distance protection from Akal(RS) end. v)220kV Akal-Bhensara Ckt-1 tripped only from Bhensara end on zone-2 distance protection on R-Y phase to phase fault with fault distance of 53.2km and with fault current of Ir=~2.87kA & Iy=~2.88kA. vi)220kV Akal-Bhensara Ckt-2 tripped only from Bhensara end on zone-1 distance protection on R-Y-B three phase fault with fault current of Ir=~1.6kA, Iy=~1.2kA & Ib=~5 .9vii)As per PMU at Bhadla(PG), R-B phase to phase fault converted into R-Y-B three phase fault with delayed fault clearance time of 1120 msec is observed.viii)Due to tripping of all four ICTs at Akal(RS), evacuation path lost for all the wind power plants connected at 220kV bus-1 & bus-2 at Akal(RS). On this, both 220kV buses became dead at Akal(RS) S/s. ix)During this event, dip in Rajasthan wind generation of approx. 1295 MW is observed out of which approx. 170 MW recovered within 13 minutes. (As per SCADA).x)As per SCADA, no change in demand is observed in Rajasthan control area.	1)400/220 kV 500 MVA ICT 1 at Akal(RS) 2)400/220 kV 500 MVA ICT 2 at Akal(RS) 3)400/220 kV 315 MVA ICT 3 at Akal(RS) 4)400/220 kV 500 MVA ICT 4 at Akal(RS) 5)220 KV Akal-Giral Ckt 6)220 KV Akal-Amarsagar Ckt 7)220kV Akal-Bhensara Ckt-1 8)220kV Akal-Bhensara Ckt-2
7	GD-1	Rajasthan	13-09-2024 13:15	13-09-2024 20:10	06:55	770	0	1.302	0.000	59120	60174	i)Generation of 220/33kV Azure Power 34 (APTFL) (IP) station evacuates through 220 kV Bhadla(PG)-Azure Power 34 Solar(APTFL) (APTFL) Ckt. During antecedent condition, Azure Power 34 (APTFL) (IP) station was generating approx. 132MW (as per PMU). ii)As reported, at 13:05hrs, 220 kV Bhadla(PG)-Azure Power 34 Solar(APTFL) (APTFL) Ckt tripped due to B-N phase to earth fault (B phase jumper broken); fault sensed in zone-1 from APTFL end (exact reason and location of fault yet to be shared). iii)Due to tripping of 220 kV Bhadla(PG)-Azure Power 34 Solar(APTFL) (APTFL) Ckt, Azure Power 34 (APTFL) (IP) S/s lost its connectivity from grid and blackout occurred at 220/33kV Azure Power 34 (APTFL) (IP) S/s. iv)As per PMU at Bhadla(PG), R-Y phase to phase fault is observed with fault clearing time of 80ms. Voltage dipped upto 0.881 p.u. at Bhadla(PG). v)As per PMU, solar generation loss of approx. 132 MW is observed at Azure Power 34 (APTFL) (IP). vi)As per SCADA, during this event, dip in solar generation of approx. 770 MW is observed in NR control area. vii)Due to a significant dip in RE generation, frequency dropped by 0.13 Hz (from 50.229 Hz to 50.099 Hz). viii)As per SCADA, no change in demand is observed in Rajasthan control area.	1)220 kV Bhadla(PG)-Azure Power 34 Solar(APTFL) (APTFL) Ckt
8	GD-1	Delhi	17-09-2024 15:05	17-09-2024 15:18	00:13	0	290	0.000	0.452	58751	64228	i)220kV Park Street(DTL) S/s has double main bus arrangement at 220kV level. 220kV Dev Nagar(DTL) has only one 220kV line i.e. 220kV Dev Nagar-Park Street (DTL) Ckt. ii)During antecedent condition, incoming power at Park Street(DTL) through 220kV Park Street-Pragati (DTL) Ckt-1 & 2 were approx. 175 MW & 110 MW respectively. 220kV bus coupler was in open condition. iii)As reported, power flow was not equal in 220kV Park Street-Pragati (DTL) Ckt-1 & Ckt-2 before 15:05 hrs. At 15:05 hrs, 220kV bus coupler was attempted to close at Park Street(DTL) S/s to make equal power flow in both circuits and to avoid over loading of 220kV Park Street-Pragati (DTL) Ckt-1. iv)As 220kV bus coupler closed at Park Street(DTL) S/s, 220kV Park Street-Pragati (DTL) Ckt-1 tripped only from Park Street(DTL) end on over current protection which led to complete shifting of power flow of 220kV Park Street-Pragati (DTL) Ckt-1 to 220kV Park Street-Pragati (DTL) Ckt-2. Due to over loading, 220kV Park Street-Pragati (DTL) Ckt-2 also tripped from Pragati(DTL) end on over current protection. v)Due to tripping of 220kV Park Street-Pragati (DTL) Ckt-1 & Ckt-2, blackout occurred at 220kV Park Street(DTL) and 220kV Dev Nagar(DTL). vi)As per PMU at Maharani Bagh(PG), no fault is observed in the system. However, fluctuation in voltage was observed. vii)As per SCADA, change in demand of approx. 330 MW is observed in Delhi control area. However, SLDC-Delhi has reported load loss of approx. 290 MW.	1)220kV Park Street-Pragati (DTL) Ckt-1 2)220kV Park Street-Pragati (DTL) Ckt-2
9	GI-2	Uttar Pradesh	17-09-2024 20:09	17-09-2024 22:15	02:06	0	0	0.000	0.000	48097	65626	i)765/400/220kV Unnao(UP) has double main and transfer bus scheme at 400kV level. ii)During antecedent condition, 400kV lines from Unnao(UP) to Agra(UP), Jehta_Hardoi Road(UP) & Bareilly Ckt-1 and 765/400 kV 1000 MVA ICT-1 & 400/220kV 315 MVA ICT-3 were connected to 400kV bus-2 at unnao(UP) S/s. iii)As reported, at 20:09 hrs, B-N phase to earth fault occurred on 400 KV Agra-Unnao (UP) Ckt with fault distance of approx. 174km & 86km from Agra(UP) and Unnao(UP) end respectively. Line tripped from Agra(UP) end on receiving DT from Unnao(UP) end but B-phase pole of line CB could not properly open from Unnao(UP) end which led to LBB operation in bay of 400 KV Agra-Unnao (UP) Ckt at Unnao(UP) end. iv)On LBB operation at Unnao(UP) S/s, all elements connected to 400kV bus-2 (400kV lines from Unnao(UP) to Agra(UP), Jehta_Hardoi Road(UP) & Bareilly Ckt-1 and 765/400 kV 1000 MVA ICT-1 & 400/220 kV 315 MVA ICT-3) tripped at Unnao(UP) S/s. v)As per PMU at Unnao(UP), B-N phase to earth fault with delayed fault clearance time of 520msec is observed. vi)As per SCADA, no change in demand of UP control area.	1)400 KV Agra-Unnao (UP) Ckt 2)400 KV Unnao(UP)-Jehta_Hardoi Road (UP) (PG) Ckt-1 3)400/220 kV 315 MVA ICT 3 at Unnao(UP) 4)400 KV Bareilly-Unnao (UP) Ckt-2 5)765/400 kV 1000 MVA ICT 1 at Unnao(UP) 6)400KV Bus 2 at Unnao(UP) 7)406 BUS COUPLER BAY - 400KV BUS 1 AT UNNAO(UP) AND 400KV BUS 2 AT UNNAO(UP)
10	GI-1	Delhi	18-09-2024 11:59	18-09-2024 12:05	00:06	0	245	0.000	0.378	61973	64761	i)During antecedent condition, incoming power at Mehrauli(DTL) through 220kV Tughlakabad-Mehrauli (DTL) Ckt-1 & 2 were approx. 90 MW each and outgoing power from Mehrauli(DTL) to DIAL through 220kV Mehrauli (DTL)- DIAL Ckt-1 was approx. 27 MW. 220kV Mehrauli (DTL)- DIAL Ckt-2 was not in service. ii)As reported, at 11:59 hrs, 220kV Mehrauli (DTL)- DIAL Ckt-1 tripped on Y-B phase to phase fault (exact reason and location of fault is yet to be received). iii)Due to this fault, 220kV Tughlakabad-Mehrauli (DTL) Ckt-1 & 2 also tripped sensing the fault in zone-2 at Mehrauli end (exact reason yet to be shared). iv)As per PMU at Ballabhgarh(PG), Y-B phase to phase fault with fault clearing time of 80msec is observed. v)As per SCADA, change in demand of approx. 245MW is observed in Delhi control area. vi)During the same time, a dip in solar generation of approx. 740 MW is also observed in NR control area (as per SCADA) (inverter tripping details yet to be shared). vii)As reported by SLDC Delhi, at 12:05 hrs, supply at Mehrauli restored through 220 kV Vasant Kunj – Mehrauli (DTL) Ckt-1 & 2.	1)220kV Mehrauli (DTL)- DIAL Ckt-1 2)220kV Tughlakabad-Mehrauli (DTL) Ckt-1 3)220kV Tughlakabad-Mehrauli (DTL) Ckt-2
11	GI-1	Uttarakhand & Himachal Pradesh	19-09-2024 11:53	19-09-2024 12:20	00:27	70	160	0.114	0.257	61190	62208	i)During antecedent condition, all the four 30MW units of Khodri HEP & all four 60 MW units of Chhibro HEP were running and total active power generation of Khodri HEP & Chhibro HEP were approx. 90 MW & 200 MW (as per SCADA). Total generation of Chhibro HEP was evacuating through 220 KV Khodri-Chhibro (UK) Ckt-1 & 2. Loading of 220 KV Khodri(UK)-Majri(HP) (UK) D/C was approx. 145 MW. 30 MW Khodri Unit-3, 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-1 & 220kV Khodri-Chibro (UK) Ckt-2 connected to 220kV bus-1 and other elements connected to 220kV bus-2 at Khodri HEP. ii)As reported, at 11:53 hrs, 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 tripped on R-N phase to earth fault with fault current of Ir=~7kA & Ir=~1.7kA and fault distance of approx. 15.7km & 25.4km from Khodri HEP(UK) & Giri(HP) end respectively. iii)On this fault, 30MW Unit-1, 2 & 3 of Khodri HEP tripped on over current protection. Due to tandem connection of Khodri HEP and Chibro HEP, generation at Chibro HEP backed down by approx. 160 MW within 8 minutes. iv)As reported, CB of 30 MW Unit-3 of Khodri HEP took approx. 210 msec in opening process which led to LBB operation of 30 MW Unit-3 bay at Khodri HEP. On LBB operation, 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-1 and 220kV Khodri-Chibro (UK) Ckt-2 also tripped from Khodri HEP end. v)As per PMU at Saharanpur(PG), R-N phase to earth fault with fault clearing time of 80 msec is observed. vi)As per SCADA, generation loss of approx. 70 MW in Uttarakhand control area. vii)As per SCADA and SLDC-HP, load loss of approx. 160 MW in HP control area.	1)220 KV Khodri(UK)-Majri/Giri(HP) (UK) Ckt-2 2)220 KV Khodri(UK)-Majri/Giri(HP) (UK) Ckt-1 3)220kV Khodri-Chibro (UK) Ckt-2 4)30 MW Khodri Unit-1 5)30 MW Khodri Unit-2 6)30 MW Khodri Unit-3

Details of Grid Events during the Month of Sept 2024 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
12	GI-2	Haryana	20-09-2024 16:05	20-09-2024 17:14	01:09	0	0	0.000	0.000	56131	62857	i)During antecedent condition, 800 kV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying approx. 250 MW each and hence total 1000 MW power was flowing from Champa to Kurukshetra. ii)As reported at 16:05 hrs, 800 kV HVDC Kurukshetra (PG) Pole-1 & 2 blocked due to tripping of AC filters at Champa end. (Reason of tripping of filters and bipole-1 only need to be shared.) iii)As 800 kV HVDC Kurukshetra(PG) Pole-1 and Pole-2 blocked, power flow of Pole-1 and Pole-2 shifted on Pole-3 and Pole-4 hence, there was no reduction in power order. iv)As per PMU, no fault is observed in the system. However, fluctuation in voltage was observed. v)As per SCADA, no change in demand of Haryana control area.	1)800 kV HVDC Kurukshetra(PG) Pole-01 2)800 kV HVDC Kurukshetra(PG) Pole-02
13	GI-2	Rajasthan	20-09-2024 12:00	20-09-2024 13:02	01:02	1790	0	4.104	0.000	43616	52184	i)400/220kV Jaisalmer(RS) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii)During antecedent condition, Renew Solar, Fortum Solar, NTPC Renewable, ACME Aklera and Clean solar was injecting approx. 107 MW, 240 MW, 160 MW, 260 MW and 250 MW respectively to Jaislamer(RS) at 220kV level. Active power was going out to Akal(RS) through 220kV Jaisalmer(RS)-Akal Ckt-1 & 2 carrying approx. 235 MW each. 400/220 kV 500 MVA ICT 1 & 2 at Jaisalmer(RS) were carrying approx. 282 MW and 268 MW respectively from 220kV level to 400kV level. iii)As reported, at 12:00 hrs, Y-phase jumper of 220kV Jaisalmer -Akal Ckt-2 broke at Jaisalmer end. iv)At the same time, bus bar protection operated at 220kV level of Jaisalmer and all the elements connected at 220kV level of Jaisalmer tripped and both the 220kV buses became dead. v)As per PMU at Fatehgarh3(PG), Y-N phase to earth fault with delayed fault clearance time of 600 msec is observed. vi)During this event, as per SCADA, solar generation loss of approx. 1070 MW is observed in Rajasthan control area. Dip in total solar generation of approx. 1790 MW is observed in NR control area out of which 980 MW is recovered within 3 minutes. vii)As per SCADA, no change in demand is observed in Rajasthan control area.	1)400/220 kV 500 MVA ICT 1 at Jaisalmer(RS) 2)400/220 kV 500 MVA ICT 2 at Jaisalmer(RS) 3)220kV Jaisalmer(RS)-Renew Solar Ckt 4)220kV Jaisalmer(RS)-Fortum Solar Ckt 5)220kV Jaisalmer(RS)-Akal Ckt-1 6)220kV Jaisalmer(RS)-Akal Ckt-2 7)220kV Jaisalmer(RS)-ACME Aklera Ckt 8)220kV Jaisalmer(RS)-Clean Solar Ckt 9)220kV Jaisalmer(RS)-NTPC Renewable Ckt
14	GD-1	Rajasthan	21-09-2024 02:58	21-09-2024 04:37	01:39	0	0	0.000	0.000	46731	62228	i)220kV Mahindra Solar(IP) S/s has double main bus arrangement at 220kV level. ii)During antecedent condition, no solar generation at 220kV Mahindra Solar(IP). 220/33kV 100MVA ICT-3 and 33kV/415V 300kVA auxiliary transformer were connected on the same 33kV bus at Mahindra Solar(IP). iii)As reported at 02:58 hrs, Y-B doble phase to earth fault occurred on 33kV/415V 300kVA auxiliary transformer which led to tripping of 220/33kV 100MVA ICT-3 on earth fault protection at Mahindra Solar(IP) S/s. iv)At the same time, 220/33kV 100MVA ICT-1 & ICT-2 and 220 KV Bhadla(PG)-Mahindra SL_BHD_PG (MAHINDRA) (MAHINDRA) Ckt tripped on master trip relay operation (exact reason for operation of master trip relay is yet to be received). v)As per PMU at MRPL(IP), Y-B double phase to earth fault is observed with fault clearing time of 80msec. vi)As per SCADA, no generation loss at 220kV Mahindra Solar(IP) S/s and no change in demand of Rajasthan control area (as per SCADA).	1)220/33 kV 100 MVA ICT 3 at Mahindra SL_BHD_PG (MAHINDRA) 2)220 KV Bhadla(PG)-Mahindra SL_BHD_PG (MAHINDRA) (MAHINDRA) Ckt 3)220/33 kV 100 MVA ICT 1 at Mahindra SL_BHD_PG (MAHINDRA) 4)220/33 kV 100 MVA ICT 2 at Mahindra SL_BHD_PG (MAHINDRA)
15	GI-1	Haryana	23-09-2024 09:44	23-09-2024 12:54	03:10	0	75	0.000	0.102	62338	73243	i)220/132/33kV Hissar(BB) S/s has double main bus scheme at 220kV level. ii)As reported, at 09:44hrs, Y-phase clamp of 220 KV Hissar-Sangrur (BB) Ckt-2 burnt and jumper snapped. iii)During the same time, all the lines connected at 220kV Bus-1 at Hissar(BB) also tripped (Exact reason yet to be shared). iv)As per DR and details received, 220 KV Hissar-Sangrur (BB) Ckt-1 & 2 tripped from Sangrur end only sensing the fault in zone-2. Fault current was 966.2A and 1.036kA respectively and fault distance was 169.2km and 167.1km respectively from Sangrur end. v)220 KV Hissar(BB)-Hissar IA(HV) (HVPNL) Ckt-1 tripped from Hissar(BB) end only sensing the fault in zone-4. Fault current was 4.984kA and fault distance was 468.2m from Hissar(BB) end. vi)220 KV Hissar(BB)-Hissar IA(HV) (HVPNL) Ckt-2 tripped from both the ends sensing the fault in zone-4 at Hissar(BB) end and zone-2 at Hissar IA(HV) end. Fault current was 3.676kA and 4.392 kA and fault distance was 0m and 5.022km from Hissar(BB) and Hissar IA(HV) end respectively. vii)Due to tripping of all the elements connected to bus-1, 220kV Bus-1 at Hissar(BB) became dead. viii)As per PMU at Hissar(PG), R-N phase to earth fault (phase sequence issue observed) with delayed fault clearing time of 360ms is observed. ix)As per SCADA, change in demand of approx. 75MW is observed in Haryana control area.	1) 220 KV Hissar(BB)-Hissar IA(HV) (HVPNL) Ckt-1 2) 220 KV Hissar(BB)-Hissar IA(HV) (HVPNL) Ckt-2 3) 220 KV Hissar-Sangrur (BB) Ckt-1 4) 220 KV Hissar-Sangrur (BB) Ckt-2 5) 220kV Bus-1 at Hissar(BB)
16	GD-1	Uttar Pradesh	23-09-2024 19:52	23-09-2024 22:09	02:17	0	700	0.000	0.963	55163	72675	i)During antecedent condition, 400 kV Unnao-Agra(UP) Ckt was charged through transfer bus coupler at Unnao end which was coupled to 400kV Bus-1. ii)As reported, at 19:52 hrs, due to blast in B-phase circuit breaker of transfer bus coupler, bus fault occurred at Unnao, but bus bar protection didn't operate (exact reason yet to be shared and bus bar relay is of static type). iii)As per DR, distance protection relay in most of the lines sensed fault in zone-4 at Unnao end and in 400 kV Unnao(UP)-Jehta_Hardoi Road (UP) (PG) Ckt-1 remote end sensed fault in zone-2. 400 KV Unnao-Panki (UP) Ckt, line tripped on SOTF after unsuccessful A/R from Panki end (reason of the same not identified yet, suspected due to overreach of Z-1 DPR at Panki end as per DR). iv)400/220 kV 315 MVA ICT 1 & 3 and 500 MVA ICT-2 at Unnao(UP) and 765/400 kV 1000 MVA ICT 1, 2 & 3 at Unnao 765(UP) tripped on O/C E/F protection operation (after 700 ms to 900 ms). v)As all the elements connected at both the buses tripped, complete blackout occurred at 400/220kV Unnao(UP) S/s.vi)During the same time, 765kV Unnao-Anpara-C Ckt and 765kV Unnao-Obra-C Ckt tripped on over-voltage protection operation and complete blackout occurred at 765/400kV Unnao 765(UP) S/s. As per DR and event logger details, DT received at Anpara-C and Obra-C end.vii)As per PMU at Abdullapur(PG), B-N phase to earth fault with delayed fault clearing time of 560 ms is observed. Maximum MW loading of 400 kV Anpara-TH-Obra-B Ckt reached upto ~1042 MW as per PMU at Anpara-TH end.viii)Due to contingency related to overloading of 400 kV Anpara-Obra B line, "SPS for safe evacuation of Generation of Anpara Complex" operated and thermal backing of approximately 1200 MW imposed on Anpara-TH, C & D. As per SPS log received from Anpara-D: At 19:52:39:100 hrs: Case-1 of SPS operated, At 19:52:44:100 hrs: Case-2 of SPS operated, At 19:52:45:100 hrs: Again Case-1 of SPS operated.ix)As per information received from Anpara-D, at 19:53:11 hrs, 200 MW backdown started at Unit-7 however, it was not executed as observed from SCADA data (exact reason yet to be received). As per event logger details received, at 19:53:15 hrs, Unit-7 switched to manual mode from Auto mode. x)As reported by Anpara-D, SPS backing command could not be executed in Unit-6 as machine was already kept in manual mode due to disturbance in parameters. During SPS Case-2 execution, Anpara-C GT-1 or GT-2 didn't trip though SPS command was sent (exact reason yet to be received from Anpara-C). xi)As per SCADA, change in demand of approx. 700 MW is observed in UP control area and generation backdown of ~510MW at Anpara C (between 19:52 hrs-20:00 hrs) and ~325MW at Anpara-TH & ~75MW at Anpara-D (between 20:00 hrs-20:15 hrs) are also observed.	1) 400 KV Bareilly-Unnao (UP) Ckt-1 2) 400 KV Bareilly-Unnao (UP) Ckt-2 3) 400 KV Mohanlalganj (PGITL)-Unnao(UP) (PGYTL) Ckt 4) 400 KV Agra-Unnao (UP) Ckt 5) 400 KV Unnao-Panki (UP) Ckt 6) 400 KV Unnao(UP)-Jehta_Hardoi Road (UP) (PG) Ckt-1 7) 400 KV Unnao(UP)-Jehta_Hardoi Road (UP) (PG) Ckt-2 8) 400/220 kV 315 MVA ICT 1 at Unnao(UP) 9) 400/220 kV 500 MVA ICT 2 at Unnao(UP) 10) 400/220 kV 315 MVA ICT 3 at Unnao(UP) 11) 765/400 kV 1000 MVA ICT 1 at Unnao 765(UP) 12) 765/400 kV 1000 MVA ICT 2 at Unnao 765(UP) 13) 765/400 kV 1000 MVA ICT 3 at Unnao 765(UP) 14) 765 KV Obra_C TPS-Unnao 765(UP) Ckt 15) 765 KV Anpara_C(LAN)-Unnao 765(UP) (UP) Ckt
17	GD-1	Delhi	24-09-2024 12:52	24-09-2024 13:01	00:09	0	338	0.000	0.420	65983	80387	i)220kV Narela(DTL) S/s has double main bus arrangement at 220kV level.ii)During antecedent condition, incoming power at Narela(DTL) through 220 KV Mandola(PG)-Narela(DV) (DTL) D/C was approx. 330MW. 220 KV Mandola(PG)-Narela(DV) (DTL) D/C was feeding load of 220kV Narela(DTL) and 220kV DSIDC(DTL). 220 KV Mandola(PG)-Narela(DV) (DTL) D/C, 220kV Narela-DSIDC (DTL) D/C, 220/66kV 100MVA ICT-1, ICT-2 & ICT-3 were connected to 220kV bus-2 at Narela(DTL) S/s. 220kV DSIDC-Bawana (DTL) D/C was not in service. 220kV bus coupler was in open condition at Narela(DTL) S/s.iii)As reported, at 12:52hrs, 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2 tripped on B-N phase to earth fault with fault distance of 8.47km from Narela end. As per DR, 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2 tripped on B-N phase to earth fault with fault current of Ib=~7.9kA & Ic=~8.9kA from Narela(DTL) and Mandaula(PG) end respectively. Line tripped on zone-1 distance protection from both ends. A/R operation not observed from both ends (exact reason of fault is yet to be received).iv)Due to tripping of 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2, complete load shifted on 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1. 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 also tripped approx. 75 seconds after the tripping of 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2 on Y-B-N double phase to earth fault. (exact reason and location of fault is yet to be received).v)As per DR of 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1, B-N phase to earth fault converted into Y-B-N double phase to earth fault is observed with fault current of Ib=~3.7kA & Ic=~2.8kA and Ib=~9.4kA & Ic=~10.6kA from Narela(DTL) and Mandaula(PG) end respectively. Line tripped on zone-1 distance protection from Narela(DTL) end and on zone-2 distance protection from mandaula(PG) end. A/R initiated at Narela(DTL) end.vi)As per PMU at Maharani Bagh(PG), B-N phase to earth fault followed by B-N phase to earth fault converted into Y-B phase to phase fault with fault clearing time of 120msec and 240msec is observed. vii)Due to tripping of 220 KV Mandola(PG)-Narela(DV) (DTL) D/C, 220/66kV 100MVA ICT-1, ICT-2 & ICT-3 at 220kV Narela(DTL) S/s and complete 220kV DSIDC(DTL) S/s became dead which led to blackout of 220kV DSIDC(DTL) S/s.viii)As per SCADA, change in demand of approx. 300 MW is observed in Delhi control area. However, SLDC-Delhi has reported load loss of approx. 338 MW.ix)During the tripping event, 220MW load of 220kV DSIDC Bawana(DTL) and 118MW load of 220kV Narela(DTL) got affected. At 13:01 hrs, 220kV DSIDC-Bawana (DTL) D/C closed and load of 220kV DSIDC(DTL) S/s normalized (as per SLDC-Delhi).	1) 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 2) 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2
18	GD-1	Haryana	29-09-2024 19:41	29-09-2024 20:40	00:59	0	190	0.000	0.285	50716	66734	i)220/132kV Fatehabad(HR) S/s has double main bus scheme at 220kV level. ii)As reported, at 19:41hrs, R phase CT of 220kV Bus Coupler at Fatehabad(HR) blasted which led to bus bar protection operation at both the buses of 220kV level at Fatehabad(HR). iii)Due to tripping of all the connected elements to both the buses at 220kV Fatehabad(HR), supply lost to 132kV level also and complete blackout occurred at 220/132kV Fatehabad(HR) S/s. iv)As per PMU at Hissar(PG), R-N phase to earth fault with fault clearing time of 120ms is observed. v)As per SCADA, change in demand of approx. 190MW is observed in Haryana control area.	1) 220 kV Fatehabad(PG)-Fatehabad(HR) (HVPNL) Ckt-1 2) 220 kV Fatehabad(PG)-Fatehabad(HR) (HVPNL) Ckt-2 3) 220 kV Hissar(PG)-Fatehabad(HR) (HVPNL) Ckt-1 4) 220 kV Hissar(PG)-Fatehabad(HR) (HVPNL) Ckt-2 5) 220 kV Rania-Fatehabad(HR) Ckt 6) 220kV Bus-1 at Fatehabad(HR) 7) 220kV Bus-2 at Fatehabad(HR) 8) 220/132kV ICT-1 at Fatehabad(HR) 9) 220/132kV ICT-2 at Fatehabad(HR) 10) 220/132kV ICT-3 at Fatehabad(HR)

Details of Grid Events during the Month of Sept 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	02-09-2024 00:42	02-09-2024 06:12	05:30	20	-	0.03%	-	60833	49353	At 00:42 Hrs / 02-09-2024, 220 kV Bhuj-Gadhsisa tripped on B-E fault. It is observed from DRs that Autorecloser didn't attempt at Gadhsisa end for single phase fault and three phase tripped observed at Bhuj End. During patrolling spare conductor of other utility was lying on 220 kV Bhuj-Gadhsisa. Generation loss of 20 MW occured at Gashsisa (Renew Power) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa
2	GD-1	WR	03-09-2024 02:37	03-09-2024 06:30	03:53	73	-	0.12%	-	59110	49851	At 02:37 Hrs / 03-09-2024, 220kV Sayali-Vapi II-1 & 2 tripped on R-E fault (ckt-1 tripped from Vapi II end only) and 220kV Sayali Switching Substation became dead. As informed by sterlite fault was in Z-1 220 kV Sayali-Vapi II-1 (1.1 km from Vapi II end). As seen from DRs, 3 phase trip issued for a single phase fault at vapi end of 220 kV Sayali-Vapi II-1 circuit and line tripped from Vapi end only. Also, 220 kV Sayali-Vapi II-2 tripped on Z-3 distance protection operation at Vapi end without any time delay. The trippings were not in order. Load loss of 73 MW occurred at of 220kV Alok Industries Ltd (which is being fed radially through 220 kV Sayli) due to the event.	Tripping of following Elements: 1. 220 kV Vapi II Sayali-1 2. 220 kV Vapi II Sayali-2 3. 220kv Sayali-Alok Industries Ltd 4. Sayali - 220 kV - Bus-1 5. Sayali - 220 kV - Bus-2
3	GI-2	WR	03-09-2024 06:50	03-09-2024 09:42	02:52	1267	-	2.07%	-	61153	55048	At 06:50 hrs / 03-09-2024, 400 kV Kakrapar(3&4)-Navsari-ckt-1 tripped on R-E fault at 400 kV Navsari end. Simultaneously, at 400 kV Kakrapar(3&4), 400 kV Kakrapar(3&4)-Navsari-ckt-1 and 400 kV Kakrapar(3&4)- bus2 tripped on LBB protection operation. As seen from PMU plot, fault did not persist for 200 msec, hence LBB protection operation was not in-order. As informed by NPCIL Kakrapar(3&4), the operation of LBB relay was not as per intent. The LBB current element is set at 20 % of C primary = 20 % of 2000 A = 400 A with a time delay of 200 millisecond. During R-E fault on 400 kV Kakrapar(3&4)-Navsari-ckt-1 at 06:50 Hrs, R phase fault got cleared in 95 milliseconds. However,due to relay's internal CB fail element logic issue, by seeing the other 2 phases (Y&B phases) current more than the set value, the relay has initiated LBB trip after 200 milliseconds of LBB initiation.	Tripping of following Elements: 1. 400 kV Kakrapar(3&4)-Navsari(PG)-1&2 2. Kakrapar(3&4) Unit-3&4 (700 MW) 3. 400/21 kV Kakrapar 3&4-GT3 4. 400 kV Kakrapar 3&4 Bus-2
4	GD-1	WR	03-09-2024 22:40	04-09-2024 15:36	16:56	6	-	0.01%	-	64255	54712	At 22:40 Hrs / 03-09-2024, As informed by Alfanar 220 kV Bhuj-Nanavalka tripped on B-E fault, but is seen from DRs R-B phase to phase fault occurred. During patrolling it was found that the suspension insulator on Tower No. 39/0 B phase and Tower- No 36/0 Y phase Tension insulator had failed. Multiple test charging were taken but line tripped on SOTF it is inferred that thorough patrolling had not been carried out before attempting test charging. Generation loss of 6 MW occured at Nanavalka (Alfanar) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220kV Bhuj-Nanavalka
5	GI-2	WR	04-09-2024 11:42	05-09-2024 15:59	28:17	31	-	0.05%	-	61961	54955	At 11:42 Hrs / 04-09-2024, 220 kV Bhuj II-Morjar (Srijan) tripped on R-E fault. During patrolling it was found that a tension insulator failed at tower number AP-05A .Generation loss of 31 MW occured at Morjar (Srijan) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj II-Morjar (Srijan)
6	GD-1	WR	06-09-2024 13:10	06-09-2024 16:49	03:39	268	-	0.44%	-	60449	53360	At 13:09 hrs / 06-09-2024, 220 kV Bhawsinghpura-Bus-1 and all connected elements tripped on Bus bar protection operation due to actuation of Overcurrent relay (50/51). 220 kV Bhawsingpura-Kanwani-1, 220 kV Bhawsingpura-Khandwa-1 and 220/33 kV Bhawsingpura-ICT-1 tripped leading to generation loss of 118 MW. Prior to the incident, 220/33 kV Bhawsingpura-ICT-1 tripped on over current protection operation at 12:50 hrs. Generation loss of 269 MW Bhawsinghpura and Kanwani (Masaya Solar) Solar Pwer Plant occurred due to the event.	Tripping of following Elements: 1. 220 kV Bhawsingpura-Kanwani-1 2. 220 kV Bhawsingpura-Khandwa-1 3. 220 kV Bhawsingpura-Bus-1 4. 220/33 kV Bhawsingpura-ICT-1
7	GD-1	WR	10-09-2024 00:31	10-09-2024 00:31	00:00	59	-	0.09%	-	65831	54447	At 00:31 Hrs / 10-09-2024, 220 kV Bhuj-Gadhsisa tripped on Y-B fault at Bhuj end. During patrolling it was found that Tower Number 46/0 was damaged from Cage section. Generation loss of 59 MW occured at Gashsisa (Renew Power) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa
8	GD-1	WR	11-09-2024 17:29	11-09-2024 18:58	01:29	80	-	0.12%	-	66030	55745	At 17:29 hrs / 11-09-2024, 400 kV Vapi II-Bus-1&2 tripped on bus bar protection operation due to maloperation of Main Control Unit-2 relay and all elements connected tripped from 400 kkV Vapi II side only. As informed by Sterlite, no abnormalities were found during inspection and the tripping may be due to moisture ingress due to heavy rainfall. 220 kV Sayali station connected to Vapi II became dark due to tripping of 220 kV Vapi II-Sayali-1&2. Load loss of 80 MW occurred at of 220kV Alok Industries Ltd (which is being fed radially through 220 kV Sayli) due to the event.	Tripping of following Elements: 1. 400 kV Vapi II-Bus-1&2 2. 400kV Vapi II-Vapi(PG)-1&2 3. 400 kV Kakrapar(3&4)-Vapi II-1&2 4. 400/220 kV Vapi II-ICT-1&2 (500 MVA) 5. 400 kV Vapi II-Bus Reactor 6. 220 kV Vapi II-Sayali-1&2
9	GD-1	WR	15-09-2024 17:03	15-09-2024 18:39	01:36	65	-	0.10%	-	63084	56252	At 17:03 hrs / 15-09-2024, 220 kV Aurangabad-Shendra tripped at 17:03 hrs due to LA blast of 220 kV Aurangabad-Shendra-1 at Shendra end. Details not received from both ends. As informed by SLDC Maharashtra, 220 kV Aurangabad-Shendra-1&2 tripped. Tripping of 220/132 kV Shendra-ICT-1 (100 MVA) and 220/33 kV Shendra-ICT-1&2 (50 MVA) and 220 kV Aurangabad-Shendra-2 may be due to bus bar protection operation. Load loss of 65 MW occurred due to the event.	Tripping of following Elements: 1. 220 kV Aurangabad-Shendra-1&2 2. 220/132 kV Shendra-ICT-1 (100 MVA) 3. 220/33 kV Shendra-ICT-1&2 (50 MVA)
10	GI-2	WR	17-09-2024 15:31	17-09-2024 18:14	02:43	-	-	-	-	65953	55356	At 15:31 hrs / 17-09-2024, Bus bar protection operated in 400 kV DGEN-Bus-2 due to failure of LA of 400/220 kV DGEN-ICT-1, resulting in tripping of all connected elements to 400 kV DGEN-Bus-2. No generation loss occurred due to the event.	Tripping of following Elements: 1. 400/220 kV DGEN-ICT-1 2. 400 kV DGEN-Bus-2 3. 400 kV DGEN-Bus Reactor 4. 400/22 kV DGEN-GT-1 5. 400 kV Navsari-DGEN-1
11	GD-1	WR	19-09-2024 15:03	19-09-2024 15:52	00:49	30	-	0.04%	-	71847	64660	At 15:03 hrs / 19-09-2024, 220 kV Dayapar sub-station AC supply cable and DC supply cable of 220/33 kV Dayapar-ICT-1 got punctured resulting in tripping of 220 kV Bhuj-Dayapar-1&2 and 220/33 kV Dayapar-ICT-1,2,3&4. Generation loss of 30 MW occurred at Dayapar () Wind Power Plant due to the event.	Tripping of following Elements: 1. 220 kV Bhuj-Dayapar-1&2 2. 220/33 kV Dayapar-ICT-1,2,3&4
12	GD-1	WR	24-09-2024 01:09	30-09-2024 23:59	166:50	72	-	0.10%	-	70692	57265	At 01:03 Hrs / 24-09-2024, 220kV Bhuj- Gadhsisa line tripped on Y-ph to earth fault. During patrolling it was found tower damaged on top section due to conductor theft of spare line on Same tower no T15/0. Generation loss of 59 MW occured at Gashsisa (Renew Power) Wind Power plant due to loss of evacuation path. Remarks- This line is still out	Tripping of following Elements: 1. 220kV Bhuj-Gadhsisa
13	GD-1	WR	30-09-2024 16:36	01-10-2024 08:41	16:05	-	272	-	0.46%	70673	58831	At 16:36 hrs / 30-09-2024, 220 kV Kalwa-Gigaplex tripped on Y-E fault due to snapping of conductor. At the same time raise in frequency from 49.996 Hz to 50.044 Hz, Voltage dip in Pune_PG and Padghe PMU and dip in Mumbai demand observed. Load loss of around 270 MW was observed (from SCADA). However, Maharashtra has reported that no load loss occurred due to the tripping	Tripping of following Elements: 1. 220 kV Kalwa-Gigaplex ckt

Details of Grid Events during the Month of Sept 2024 in Southern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA	01-09-2024 03:15	01-09-2024 04:21	01:06	0	164	0.00%	0.48%	42145.12	33985.58	Tripping of 220kV Bus of 400kV/220kV Kalaburgi SS, 220kV Bus-2 of 220kV/110kV Sedam, 220kV Bus-1 of 220kV/110kV Shahpur SS and complete outage of 220kV/110kV Gangapur SS, 220kV/110kV Humnabad SS, 220kV/110kV Kapanoor SS & 220kV/110kV Halabarga stations and 220kV Avada IPP: During antecedent conditions, due to bus split conditions at 220kV level of 220kV/110kV Sedam SS and 220kV/110kV Shahapur SS, 220kV Bus-2 of 220kV/110kV Sedam, 220kV Bus-1 of 220kV/110kV Shahpur SS, 220kV/110kV Nimbarga SS, 220kV/110kV Humnabad SS, 220kV/110kV Kapanoor SS & 220kV/110kV Halabarga stations and 220kV Avada IPP are being radially fed from 220kV Bus-1 and Bus-2 of Kalaburgi SS. The triggering incident was tripping of 400kV/220kV kalburgi ICT-1 and 2 on operation of over-flux relays on the IV side, leading to 220kV Bus 1 and Bus-2 outage at 400kV/220kV Kalaburgi SS which inturn led to outage of all radial connected buses and stations.	400KV/220KV KALABURAGI-ICT-1, 400KV/220KV KALABURAGI-ICT-2
2	GD - 1	ANDHRA PRADESH , TAMILNADU	05-09-2024 10:14	05-09-2024 10:27	00:13	0	177	0.00%	0.36%	52802.16	48589.41	Complete Outage of 230kV/110kV Gummudipundi SS: During antecedent conditions, Gummidipoondi Substation was radially connected through 230kV Gummidipoondi_ Sulurpet Line. 230V Gummidipoondi_Suryadev and 230kV Gummidipoondi NCTPS were out of service for power regulation. As per the reports submitted, the triggering incident was Y-N fault in 230kV Gummidipoondi_ Sulurpet Line. Tripping of only connected line led to complete outage of 230kV/110kV Gummidipoondi SS. Since 230kV Surya Dev, 230kV ARS, 230kV Mychelin, 230kV Cauvery, 230kV Thervoi Kandigoi, 230kV Kamachi are radially connected to 230kV/110kV Gummidipoondi SS, complete outage of 230kV/110kV Gummidipoondi SS led to complete outage of the radial connected stations also.	220KV-SULURPET-GUMMIDIPOONDI-1, GUMMIDIPOONDI - 230KV - Bus 1, GUMMIDIPOONDI - 230KV - Bus 2
3	GD - 1	TAMILNADU	09-09-2024 10:08	09-09-2024 10:24	00:16	41	73	0.08%	0.15%	51895.43	48620.26	Complete Outage 230kV/110kV Karaikudi SS: 230kV Karaikudi SS has double bus with bus coupler but all elements are connected to single bus. As per the reports submitted, the triggering incident was R-phase jumper cut in 230kV Karaikudi karaikudi_PG Line-2 between breaker and isolator causing a bus fault. Immediately, 230kV BBP operated and all elements connected to the bus tripped. Tripping of all elements connected to 230kV Bus resulted in tripping of 230kV bus of 230kV/110kV Karaikudi SS. Subsequently, other two 110kV source feeders tripped on fault and over current protection. This led to complete outage of 230kV/110kV Karaikudi SS.	230KV-KARAIKUDI-KARAIKUDI(TN)-1, 230KV-KARAIKUDI-KARAIKUDI(TN)-2, KARAIKUDI(TN) - 230KV
4	GD - 1	TAMILNADU	12-09-2024 21:54	12-09-2024 22:00	00:06	0	1463	0.00%	2.98%	48613.17	49013.48	Complete Outage of 400kV/230kV/110kV MANALI, 400kV/230kV PULIYANTHOPE, 230kV VYSARPADI, 230kV/110kV TONDIARPET, 230kV/110kV BASIN_BRIDGE, 230kV/33kV MYLAPORE_GIS, 230kV/110kV CMRL_CENTRAL, 230kV/33kV TNEB_HQ, 230kV/110kV RAPURAM and 230kV/110kV MYLAPORE: During antecedent conditions, 230kV VYSARPADI was radially fed from 400kV/230kV PULIYANTHOPE and due to outage of 230kV Tharamani Rapuram line, 230kV Tharamani Mylapore line, 230kV Tharamani KITZ line, 230kV Rapuram Mambalam line and 230kV Mylapore Mylapore_GIS line on load regulation, 230kV/110kV TONDIARPET, 230kV/110kV BASIN_BRIDGE, and 230kV/33kV MYLAPORE_GIS, 230kV/110kV CMRL_CENTRAL, 230kV/33kV TNEB_HQ, 230kV/110kV RAPURAM and 230kV/110kV MYLAPORE were radially fed from 400kV/230kV/110kV MANALI and 230kV NCTPSC St-1. Due to the tripping of both 400kV connected Manali lines, and 230kV grid connected lines, there was loss of supply to 400kV/230kV/110kV MANALI, 400kV/230kV PULIYANTHOPE, 230kV VYSARPADI, 230kV/110kV TONDIARPET, 230kV/110kV BASIN_BRIDGE, 230kV/33kV MYLAPORE_GIS, 230kV/110kV CMRL_CENTRAL, 230kV/33kV TNEB_HQ, 230kV/110kV RAPURAM and 230kV/110kV MYLAPORE.	400KV NCTSPS STAGE-II MANALI LINE-1 ALAMATHY MANALI LINE-1&2 NCTPS TONDIARPET LINE-1&2 NCTPS KILPAUK LINE-1 KARATTUR KILPAUK_GIS LINE-1 ALAMATHY MOSUR LINE-1&2 KORATTUR MANALI LINE-1 ALAMATHY KOYAMBEDU LINE-1 ALAMATHY MOSUR LINE-1
5	GD - 1	TAMILNADU	12-09-2024 23:36	13-09-2024 01:38	02:02	0	329	0.00%	0.71%	47134.84	46312.54	Complete Outage of 400kV/220kV Tharamani SS of TANTRANSCO: As per the reports submitted, during antecedent conditions, 230kV Mylapore Tharamani line and 230kV RAPuram Tharamani lines were under outage for load regulation. The triggering incident was YN fault in 230kV Sriperumbudur Tharamani line due to Y phase dropper cut at Tharamani end. and the line tripped. At the same time, 230kV Kalventhapattu Tharamani line tripped on operation of DEF protection only at Tharamani end. Tripping of these two lines resulted in the complete outage of 400kV/230kV/110kV Tharamani GIS and 230kV/110kV Tharamani SS.	230KV-SRIPERUMBADUR_TN-THARAMANI-1, 230KV-KALVENDAPATTU-THARAMANI
6	GD - 1	KARNATAKA	18-09-2024 06:10	18-09-2024 10:16	04:06	0	21	0.00%	0.04%	44693.0	50788.0	Complete Outage of 220kV Kalyani SS and 220kV Bus-2 outage at 400kV/220kV Munirabad SS: 220kV Kalyani Steel was being radially fed from 220kV Munirbad Bus-2. As per the reports submitted, the triggering incident R-N fault in 220kV Bus-2. Immediately, 220kV BBP operated and all elements connected to 220kV Bus-2 tripped. This led to outage of 220kV Bus-2 of Munirabad and complete outage of 220kV Kalyani Steel.	220KV-LINGAPUR-MUNIRABAD_KAR-2, 400KV/220KV MUNIRABAD-ICT-2, 220KV-MUNIRABAD-KALYANI-1, MUNIRABAD_KAR - 220KV - Bus 2
7	GD - 1	PONDICHERRY	20-09-2024 13:49	20-09-2024 14:25	00:36	0	128	0.00%	0.21%	56641.7	62248.0	Complete Outage of 230kV/110kV Villianur SS of Puducherry: In the antecedent conditions, 230kV Neyvelli-Villinur was under idle charged condition due to power regulation and hence 230/110kV Villinur was radially connected via 230kV Puducherry-Villinur line. As per the reports submitted, the triggering is the B-N fault in 230kV Puducherry-Villinur line. With the tripping of only radial line connected to 230/110kV Villinur led to the complete outage of 230kV/110kV Villianur SS of Puducherry.	230KV-PUDUCHERRY-VILLIANUR-1
8	GD - 1	KARNATAKA	21-09-2024 19:25	21-09-2024 23:05	03:40	0	296	0.00%	0.61%	51698.17	48571.65	Complete Outage of 220kV/66kV Kolar SS, 220kV/66kV Sarjapura SS, 220kV/66kV Bangarpet SS of KPTCL: 220kV/66kV Malur SS was operating with split bus condition at 220kV level with 220kV Kolar Kolar_PG line-1&2 radially feeding 220kV Malur Bus-2. 20kV/66kV Sarjapura SS was being radially fed from 220kV Malur Bus-2. 220kV/66kV Bangarpet SS was being radially fed from 220kV/66kV Kolar SS. As per the reports submitted, the triggering incident was tripping of 220kV Kolar Kolar_PG line-1&2 on RYB-N fault. Tripping of both these lines led to complete outage of 220kV/66kV Kolar SS which inturn led to complete outage of 220kV/66kV Bangarpet SS, 220 Bus-2 of Malur and 220kV/66kV Sarjapura SS.	220KV-KOLAR_KAR-KOLAR_AC-1, 220KV-KOLAR_KAR-KOLAR_AC-2, KOLAR_KAR - 220KV - Bus 1

Details of Grid Events during the Month of Sept 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD - 1	KARNATAKA	29-09-2024 17:51	29-09-2024 17:58	00:07	0	298	0.00%	0.67%	43568	44624	Complete Outage of 220kV Exora SS, 220kV ITI and 220kV Vikas Tech Park SS and Tripping of 220kV Bus-1 of 400kV/220kV Hoody SS of KPTCL: 400kV/220kV Hoody SS was operating with bus split condition at 220kV level with 220kV Hoody Malur line being the only source. 220kV Exora SS, 220kV ITI and 220kV Vikas Tech Park SS were being radially fed from 220kV Hoody Bus-1. As per the reports submitted, the triggering incident was tripping of 220kV Hoody Malur Line-1 on . Tripping of the only connected line resulted in outage of 220kV Bus-1 of 400kV/220kV Hoody SS which inturn resulted in complete outage of 220kV Exora SS, 220kV ITI and 220kV Vikas Tech Park SS.	220KV-HOODY-MALUR-1
10	GI-1	TELANGANA , ANDHRA PRADESH , TELANGANA	01-09-2024 06:22	01-09-2024 07:50	01:28	640	0	1.57%	0.00%	40698.3	35277.08	Tripping of 220kV Bus-1 and Bus-2 of 220kV/132kV Nsagar PH Generating station of TSGENCO: As per the reports submitted, the triggering incident was Y-N fault in 220kV Nagarjunasagar-Chalakurthy feeder at a distance of 2.4 KM from Nsagar end. At Nsagar end, the fault was sensed in zone-1. The earth fault current recorded was 22.5 KA, and the fault was cleared within 87ms. At the same time, other 220kV Nasagar PH lines except 220kV Nsagar Tallappally Line-2 tripped due to LBB maloperation. After 5mins, 220kV Nsagar Tallappally Line-2 was hand tripped at Tallapally end due to overloading. Subsequently, PTRs of 220kV Nsagar PH tripped on overloading and Units tripped on over frequecy due to loss of evacuation. This led to outage of 220kV Bus-1 and Bus-2 of 220kV/132kV Nsagar PH Generating station. 132kV was in service during the event.	220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_TS-CHALAKURTHY-1, 220KV-SRISAILAM_RIGHT_BANK-NAGARJUNASAGAR_TS-1
11	GI-1	KERALA	04-09-2024 20:17	05-09-2024 01:08	04:51	0	123	0.00%	0.27%	49085.97	46105.16	Tripping of 220kV Bus-2 and 220kV Bus Section-1A of 400kV/220kV Madakathara SS of KSEB: As per the reports submitted, Y-phase insulator on the 220 kV side in Bus Section 2B of the 220/110 Madakathara Transformer-2 experienced a flashover resulting in a bus fault. Immediately, Bus -2 operated tripping all elements connected to 220kV Bus section 2-A and 2-B as both bus sections are connected through an isolator. At the same time, elements connected to 220kV Bus section 1-A also tripped.	400KV/220KV MADAKKATHARA-ICT-3, 220KV-MADAKATHARA-SHORNUR-1, 220KV-MADAKATHARA-CHALAKUDY-1, MADAKATHARA - 220KV - Bus 2, 220KV PALAKKAD-MADAKATHARA-1, 220KV-LOWER PERIYAR MADAKATHARA-1
12	GI-1	TELANGANA , ANDHRA PRADESH	11-09-2024 20:17	11-09-2024 21:21	01:04	172	0	0.35%	0.00%	49287.14	47482.61	Tripping of 220kV Bus-2 of Lower Sileru PH of APGENCO: As per the reports submitted, at 20:16 hours, an internal Y-Phase fault occurred in Unit-2, leading to operation of GT Buchholtz and GT Differential Protections. These protections triggered the master trip relays, causing the unit to trip and the generator breaker to open. However, the LBB Group-B protection relay operated at Lower Sileru because the CT input for the Unit-2 LBB overcurrent relays was being taken from the generator side CTs. Immediately, all elements connected to 220kV Bus-2 got tripped.	220KV-ASUPAKA-LOWER_SILERU-1, 220KV-LOWER_SILERU-Chintur-1, LOWER_SILERU - 220KV - Bus 2
13	GI-1	ANDHRA PRADESH	13-09-2024 10:05	13-09-2024 10:23	00:18	0	0	0.00%	0.00%	55205.93	57984.6	Tripping of 220kV Bus-2 of 220kV Lower Sileru PH of APGENCO: As per the reports submitted, while deparalleling Unit-3, Y-pole failed to open. LBB failed to open and other lines connected to 220kV Bus-2 were handtripped.	220KV-ASUPAKA-LOWER_SILERU-1, 220KV-LOWER_SILERU-Chintur-1
14	GI-1	TAMILNADU	19-09-2024 11:14	19-09-2024 11:34	00:20	308	322	0.55%	0.52%	56151.16	62183.13	Tripping of 230kV Bus-2 of 400kV/230kV Alamathy SS and Complete Outage of 230kV OPG generating staition of TANTRANSCO: As per the reports submitted, a B-phase fault occurred on the LV side, leading to the operation of differential protection. As the fault was not cleared within 200 milliseconds, the LBB protection operated on the 230kV Bus 2. The fault was cleared in approximately 328 milliseconds, hence reverse zone protection operated on the 230kV Alamathy-Manali 1 feeder and the 230kV Alamathy-Koyembedu feeder, both connected to 230kV Bus-1 at the Alamathy end. 230kV Alamathy OPG Line-2 which is connected to 230kV Alamathy Bus-2 tripped on LBB operation. Subsequently, 230KV Alamathy OPG Line-1 tripped on over loading. Tripping of both lines led to complete outage of 230V OPG generating station.	230KV-ALAMATHY-TIRUVERKADU-1, 230KV-ALAMATHY-MANALI-1, 230KV-ALAMATHY-KOYAMBEDU-1, 230KV-ALAMATHY-MANALI-2, 230KV-ALAMATHY-OPG-2, 400KV/230KV ALAMATHY-ICT-5, 230KV-ALAMATHY-MOSUR-2, ALAMATHY - 230KV - Bus 2
15	GI-1	ANDHRA PRADESH , TELANGANA	20-09-2024 17:00	20-09-2024 19:30	02:30	392	0	0.76%	0.00%	51454.83	57035.05	Tripping of 220kV Bus-2 of 220kV Nsagar PH of TGGENCO: As per the reports submitted, the triggering incident was B-N fault in 220kV Nagarjunasagar-Srisailam RB feeder. At the same time, other 220kV Nasagar PH lines connected to 220kV Bus-2 tripped due to LBB maloperation. This led to outage of 220kV Bus-2 of 220kV/132kV Nsagar PH Generating station.	220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-SRISAILAM_RIGHT_BANK-NAGARJUNASAGAR_TS-1, 220KV-NAGARJUNASAGAR_TS-CHALAKURTHY-1
16	GI-1	ANDHRA PRADESH , TELANGANA	20-09-2024 20:30	20-09-2024 21:54	01:24	192	0	0.39%	0.00%	49231.29	49574.77	Tripping of 220kV Bus-2 of 220kV NSagar PH of TGGENCO: As per the reports submitted, the triggering incident was B-N fault in 220kV Nagarjunasagar-Srisailam RB feeder. At the same time, other 220kV Nasagar PH lines connected to 220kV Bus-2 tripped due to LBB maloperation. This led to outage of 220kV Bus-2 of 220kV/132kV Nsagar PH Generating station.	220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-SRISAILAM_RIGHT_BANK-NAGARJUNASAGAR_TS-1, 220KV-NAGARJUNASAGAR_AP-CHALAKURTHY-1
17	GI-2	TAMILNADU	22-09-2024 19:15	22-09-2024 21:39	02:24	133	0	0.27%	0.00%	48495.89	44380.54	Tripping of 400kV Bus-1 of 400kV/230kV NLC St-II: As per the reports submitted, the triggering incident was B-phase insulator failure in 400kV Bus-1 in 400kV/230kV NLC St-II causing a B-N fault in 400kV Bus-1. Immediately, 400kV Bus-1 BBP operated tripping all elements connected to Bus-1.	400KV-NEYVELI_TS2_EXP-PUGALUR-1, 400KV-NAGAPATTNAM_PS-NEYVELI_TS1_EXP-1, 400KV/230KV NEYVELI_TS_II-ICT-1
18	GI-1	TELANGANA , ANDHRA PRADESH	30-09-2024 12:55	30-09-2024 13:27	00:32	160	0	0.31%	0.00%	51330.26	56558.11	Tripping of 220kV Bus-2 of 220kV Lower Sileru PH of APGENCO During antecedent conditions, 220kV Lower Sileru PH was operating with bus split conditions. As per the reports submitted, the triggering incident was tripping of 220kV Asupaka Lower Sileru line on B-N fault and the line tripped. Tripping of the only connected line led to tripping of units on over frequency. This led to outage of 220kV Bus-2 of 220kV Lower Sileru PH.	220KV-ASUPAKA-LOWER_SILERU-1, LOWER_SILERU - 220KV - Bus 2
19	GI-1	TAMILNADU	30-09-2024 17:24	30-09-2024 18:05	00:41	0	0	0.00%	0.00%	47497	50624	Tripping of 230kV Bus-1 of 400kV/230kV Karamadai SS of TANTRANSCO As per the reports submitted, the triggering incident was B-N fault near 400kV/230kV ICT-1. Immediately, differential protection operated and but LV side breaker failed to open. Subsequently, LBB operated and all elements connected to the 230kV Bus-1 tripped.	230KV-PUSHEP-KARAMADAI-1, 230KV-INGUR-KARAMADAI-1, 400KV/230KV KARAMADAI-ICT-1, 230KV-KUNDAH3-KARAMADAI-1, 230KV-KARAMADAI-KARUVALUR-2

Details of Grid Events during the Month of Sept 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
	No GD/GI reported in Eastern region in the month of September 2024												

Details of Grid Events during the Month of Sept 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Mokokchung(PG), Mokokchung(NL) and Longnak area of Nagaland Power System	02-09-2024 15:36	02-09-2024 16:55	01:19	0	23	0.00%	0.76%	2471	3019	Mokokchung(PG), Mokokchung(NL) and Lognak area of Nagaland Power system are connected with rest of NER Grid through 220kV Mariani(PG)-220kV Mokokchung(220kV) ckt 1 and ckt 2 and through 132kV Doyang – Mokochung. 132kV Doyang – Mokochung line tripped at 15:34 hrs of 02-09-2024.At 15:36 Hrs of 02-09-2024, 220kV Mariani(PG)-Mokokchung(PG) ckt 1 and ckt 2. Due to tripping of these elements, Mokokchung(PG), Mokokchung(NL) and Lognak area of Nagaland Power system were isolated from NER Grid. Power was extended to Mokokchung area of Nagaland Power System by charging 220kV Mariani(PG)-Mokokchung(PG) ckt 1 at 16:55hrs of 02-09-2024.	220kV Mariani(PG)-Mokokchung(PG) I & II lines
2	GD I	Gossaigaon Area of Assam Power System	03-09-2024 10:32	03-09-2024 11:11	00:39	0	6	0.00%	0.23%	2518	2622	Gossaigon area of Assam Power System was connected with NER Power system via 132kV Dhaligaon-Gossaigaon-Gauripur link (132 kV Gauripur- Gossaigaon was kept open due to system requirement). At 10:32 Hrs of 03.09.2024, 132 kV Dhaligaon-Gossaigaon line tripped due to which Gosaigaon area of Assam Power System was isolated from NER Grid and collapsed due to no source available in the area. Power supply was extended by charging 132 kV Dhaligaon–Gossaigaon line at 11:11 Hrs of 03.09.2024.	132 kV Dhaligaon-Gossaigaon line
3	GD I	Rengpang area of Manipur Power System	03-09-2024 10:36	03-09-2024 15:29	04:53	0	1	0.00%	0.04%	2531	2627	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 10:36 Hrs of 03-09-2024, 132kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 15:29 Hrs of 03.09.2024.	132 kV Loktak – Rengpang line
4	GD I	Wokha area of Nagaland Power System	05-09-2024 09:31	05-09-2024 09:43	00:12	0	3	0.00%	0.12%	2292	2497	Wokha area of Nagaland Power System was connected with connected to NER Power system via 132kV Wokha-Chiephobozou, and 132 kV Sanis-Wokha lines. At 08:45 Hrs of 05.09.2024, 132 kV Wokha-Chiephobozou line tripped due to whichWokha area of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in these area. Power supply was extended to Wokha area of Nagaland Power System by charging 132kV Wokha-Chiephobozou line at 09:43 Hrs of 05.09.2024.	132 kV Wokha-Chiephobozou line
5	GD I	Rongkhon, Ampati and Phulbari area of Meghalaya Power System and Ganol HEP of Meghalaya Power System	06-09-2024 09:34	06-09-2024 09:47	00:13	0	28	0.00%	1.04%	2384	2688	Rongkhon, Ampati and Phulbari area of Meghalaya Power System and Ganol HEP were connected with rest of NER Grid via 132 kV Nangalbibra-Rongkhon Line. At 09:34 Hrs of 06.09.2024, 132 kV Nangalbibra-Rongkhon Line tripped. Due to tripping of these elements, Rongkhon, Ampati and Phulbari area of Meghalaya Power System and Ganol HEP were isolated from NER Grid and collapsed due to load generation mismatch in these areas. Power was extended to Rongkhon, Ampati and Phulbari area of Meghalaya Power System and Ganol HEP by charging 132 kV Nangalbibra-Rongkhon Line at 09:47 Hrs of 06.09.2024.	132 kV Nangalbibra-Rongkhon Line
6	GD I	Leshka Generating station of Meghalaya Power System	06-09-2024 22:06	06-09-2024 22:24	00:18	25	0	0.74%	0.00%	3380	3397	Leshka Generating station of Meghalaya Power System was connected with rest of NER Grid via 132 kV Myntdu Leshka - Khleihriat D/C Lines. At 22:06 Hrs of 06.09.2024, 132 kV Myntdu Leshka - Khleihriat D/C Lines tripped. Due to tripping of these elements, Leshka Generating station of Meghalaya Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Leska Generating is connected with the rest of the grid by charging 132 kV Myntdu Leshka - Khleihriat 1 at 22:24.	132 kV Myntdu Leshka - Khleihriat D/C Lines

Details of Grid Events during the Month of Sept 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD I	Mokokchung(NL) and Longnak areas of Nagalanad Power System	07-09-2024 15:43	07-09-2024 17:23	01:40	0	29	0.00%	0.90%	2413	3218	Mokokchung(NL) and Longnak areas of Nagaland Power System were connected with connected to NER Power system via 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line, 132 kV Mokochung (PG) -Mokokchung (DoP, Nagaland) 2 Line, 132 kV Doyang - Mokokchung (DoP, Nagaland) Line and 132 kV Mokokchung-Longnak Line. At 08:45 Hrs of 05.09.2024, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 2 Line, 132 kV Doyang - Mokokchung (DoP, Nagaland) Line and 132 kV Mokokchung-Longnak Line tripped due to which Mokokchung(NL) and Longnak areas of Nagaland Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Mokokchung(NL)area of Nagaland Power System by charging 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line at 17:23 Hrs of 07.09.2024. 132 kV Mokochung (PG) -Mokokchung (DoP, Nagaland) 2 Line charged at 17:42 Hrs of 07.09.2024.	132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 2 Line, 132 kV Doyang - Mokokchung (DoP, Nagaland) Line and 132 kV Mokokchung-Longnak Line
8	GD I	Deomali area of Arunachal Pradesh Power System	07-09-2024 17:16	08-09-2024 16:32	23:16	0	1	0.00%	0.03%	2441	3098	Deomali area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV AGBPP-Deomali line. At 17:16 Hrs of 07-09-2024, 220 kV AGBPP-Deomali line tripped. Due to tripping of this element, Deomali area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Deomali area by charging 220 kV AGBPP-Deomali line at 16:32 Hrs of 08.09.2024.	220 kV AGBPP-Deomali line
9	GD I	Ziro, Daporizo, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa, Rupai, Margherita areas of Assam Power System	07-09-2024 18:09	07-09-2024 18:29	00:20	0	72 MW Assam & 42 MW Arunachal Pradesh	-	-	3117	3680	Ziro, Daporizo, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa, Rupai, Margherita areas of Assam Power System were connected with connected to NER Power system via 132 kV Rupai – Tinsukia line and 132 kV Margherita – Tinsukia line. 132kV Ranganadi-Ziro line was under PSD since 08:44 Hrs of 07-09-2024. At 18:19 Hrs of 07-09-2024, 132 kV Rupai – Tinsukia line and 132 kV Margherita –Tinsukia line tripped due to which Ziro, Daporizo, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa, Rupai, Margherita areas of Assam Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Chapakhowa, Rupai, Margherita areas of Assam Power System by charging 132 kV Margherita –Tinsukia line at 18:27 Hrs and by charging 132 kV Rupai – Tinsukia line at 18:29 Hrs of 07.09.24. Subsequently power supply was extended to Ziro area of Arunachal Pradesh Power System by charging 132kV Ranganadi-Ziro line at 18:29 Hrs of 07.09.24. Power supply was extended to Daporizo, Along, Pasighat by charging 132 kV Ziro-Daporizo line at 19:29 Hrs of 07.09.24.Power supply was extended to Roing, Tezu, Namsai areas of Arunachal Pradesh Power System by charging 132 kV Roing Chapakhowa D/C lines at 19:15 Hrs and 132 kV Roing-Tezu and 132 kV Tezu-Namsai lines at 19:38 Hrs and 19:40 Hrs 07.09.24 respectively.	132 kV Rupai – Tinsukia line and 132 kV Margherita –Tinsukia line
10	GD I	Mokokchung(NL) areas of Nagalanad Power System	07-09-2024 21:36	07-09-2024 22:35	00:59	0	33	0.00%	0.93%	3277	3554	Mokokchung(NL) area of Nagaland Power System were connected with NER Power system via 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 2 Line. 132 kV Doyang - Mokokchung (DoP, Nagaland) Line was under emergency shutdown since 19:39 Hrs of 07-09-2024. Also, 132 kV Mokokchung(NL)-Longnak line tripped at 15:43 Hrs of 07.09.2024. At 21:36 Hrs of 07.09.2024, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 2 Line tripped due to which Mokokchung(NL)area of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in this area.	132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 1 Line, 132 kV Mokochung (PG) - Mokokchung (DoP, Nagaland) 2 Line, 132 kV Doyang - Mokokchung (DoP, Nagaland) Line
11	GD I	Rengpang area of Manipur Power System	09-09-2024 02:31	09-09-2024 15:45	13:14	0	1	0.00%	0.04%	2241	2659	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 02:31 Hrs of 09-09-2024, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 15:45 Hrs of 09.09.2024.	132 kV Loktak-Rengpang line
12	GD I	400/220 kV Killing S/S of Meghalaya Power system	10-09-2024 07:21	10-09-2024 10:23	03:02	0	117	0.00%	4.28%	2621	2731	400 kV Killing S/S is connected with rest of NER grid via 400 kV Bongaigaon-Killing line, 400 kV Silchar-Killing line and 400/220 kV ICT at Killing. 220 kV Killing S/S is connected with rest of NER grid through 220 kV Misa-Killing D/C lines, 220 kV Mawngap-Killing D/C lines and 220/132 kV ICT-I&II at Killing. 220/132 kv ICT-I at Killing was under shutdown. At 07:21 Hrs of 10.09.2024, 400 kV Bongaigaon-Killing line, 400 kV Silchar-Killing line, 220 kV Misa-Killing D/C lines, 220 kV Mawngap-Killing D/C lines and 220/132 kV ICT-II at Killing tripped which caused blackout of Killing Bus of Meghalaya Power system. Power was extended to 220 kV Killing S/S by charging 220 kV Mawngap-Killing D/C lines at 10:09 Hrs of 10.09.2024. Power was extended to 400 kV Killing S/S by charging 400 kV Silchar-Killing line at 10:23 hrs of 10.09.2024.	400 kV Bongaigaon-Killing line, 400 kV Silchar-Killing line, 220 kV Misa-Killing D/C lines, 220 kV Mawngap-Killing D/C lines and 220/132 kV ICT-II at Killing
13	GD I	New Shillong Substation of Meghalaya Power System	10-09-2024 14:39	10-09-2024 15:14	00:35	0	0.5	0.00%	0.02%	2537	3018	New Shillong Substation of Meghalaya Power System was connected with rest of NER Grid through 220kV Mawngap-New Shillong line D/C lines. At 14:39 Hrs of 10-09-2024, 220 kV Mawngap-New Shillong line D/C lines tripped. Due to tripping of these elements, New Shillong Substation of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended New Shillong Substation of Meghalaya Power System by charging 220kV Mawngap-New Shillong line D/C line at 15:14 hrs of 10-09-2024.	220 kV Mawngap-New Shillong line D/C lines

Details of Grid Events during the Month of Sept 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
14	GD I	Rengpang area of Manipur Power System	11-09-2024 11:05	12-09-2024 11:53	24:48	0	1	0.00%	0.05%	2433	2222	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 11:05 Hrs of 11-09-2024, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 11:53 Hrs of 12.09.2024.	132 kV Loktak-Rengpang line
15	GD II	AGTCCPP Generating station of Tripura Power System	12-09-2024 13:43	12-09-2024 15:04	01:21	44	0	1.88%	0.00%	2343	2773	AGTCCPP Generating station of Tripura Power System was connected with NER Power system via 132 kV AGTCCPP - KUMARGHAT Line, 132 kV AGARTALA - AGTCCPP 2 Line and 132 kV AGTCCPP - P K Bari D/C lines.132 kV AGTCPP-Agartala 1 Line was in the process of taking ESD and breaker was closed at Agartala end and breaker for this line opened at AGTCCPP end only. At 13:43 Hrs of 12.09.2024, 132 kV AGTCCPP - KUMARGHAT Line, 132 kV AGARTALA - AGTCCPP 2 Line and 132 kV AGTCCPP - P K Bari D/C lines tripped due to which AGTCCPP Generating station of Tripura Power System was blackout due to loss of evacuation path. Power supply was extended to AGTCCPP Generating station of Tripura Power System by charging 132kV AGTCCPP	132 kV AGTCCPP - KUMARGHAT Line, 132 kV AGARTALA - AGTCCPP 2 Line and 132 kV AGTCCPP - P K Bari D/C lines
16	GD I	Rengpang area of Manipur Power System	12-09-2024 23:39	14-09-2024 16:31	40:52	0	1	0.00%	0.05%	2433	2222	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 23:39 Hrs of 12-09-2024, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 16:31 Hrs of 14.09.2024.	132 kV Loktak-Rengpang line
17	GD I	Along area of Arunachal Pradesh Power System	13-09-2024 14:24	13-09-2024 17:45	03:21	0	5	0.00%	0.17%	2324	2929	Along area of Arunachal Pradesh Power System was connected with rest of NER Power system through 132 kV Basar-Along line. 132 kV Along - Pasighat Line was under continuous planned shutdown. At 14:24 Hrs of of 13.09.2024, 132 kV Basar-Along line tripped. Due to tripping of this element, Along area of Arunachal Pradesh Power System was isolated from NER Grid and collapsed due to no source available in this area. Power is restored to the Along area of Arunachal Pradesh Power System by charging 132kV Along-Basar line at 17:45 Hrs of 13.09.2024.	132 kV Basar-Along line
18	GD I	Umiam Stage IV of Meghalaya Power System	16-09-2024 13:38	16-09-2024 14:23	00:45	54	0	2.22%	0.00%	2435	2827	Umiam Stage IV of Meghalaya Power System was connected with rest of NER Grid via 132 KV Umiam Stage IV-Umtru D/C Lines & 132kV Umiam Stage IV- Umiam Stage III D/C Lines. At 13:38 Hrs of 16-09-2024, 132 kV Umiam Stage IV-Umtru D/C Lines & 132kV Umiam Stage IV Umiam Stage III D/C Lines tripped. Due to the tripping of these lines, Umiam Stage IV of Meghalaya Power System was isolated from NER Grid. Power supply was extended to Umiam Stage IV of Meghalaya Power System by charging 132 kV Umiam Stage IV- Umiam Stage III Line 2 at 14:23 Hrs of 16-09-2024.	132 kV Umiam Stage IV-Umtru D/C Lines & 132kV Umiam Stage IV Umiam Stage III D/C Lines
19	GD I	Rengpang area of Manipur Power System	18-09-2024 12:23	18-09-2024 12:47	00:24	0	1	0.00%	0.03%	2388	2976	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 12:23 Hrs of 18-09-2024, 132kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area of Manipur Power system by charging 132 kV Loktak-Rengpang line at 12:47 hrs of 18-09-2024.	132kV Loktak-Rengpang line

Details of Grid Events during the Month of Sept 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
20	GD I	Mariani area of Assam Power System	18-09-2024 18:24	18-09-2024 18:43	00:19	0	1	0.00%	0.03%	3421	3787	132 kV Mariani S/S of Assam power system is connected with rest of NER grid via 132 kV Mariani-Golaghat line, 132 kV Mariani-Jorhat I&II lines and 132 kV Mariani-LTPS line. At 18:24 Hrs of 18.09.2024, all the lines connected to 132 kV Mariani S/S tripped due to spurious LBB operation of 132 kV Mariani-Jorhat I line. Power was extended to 132 kV Mariani S/S by charging 132 kV Mariani-Golaghat line at 18:43 Hrs of 18.09.2024.	132 kV Mariani-Golaghat line, 132 kV Mariani-Jorhat I&II lines and 132 kV Mariani-LTPS line.
21	GD I	Rengpang area of Manipur Power System	19-09-2024 12:40	19-09-2024 16:32	03:52	0	1	0.00%	0.03%	2388	2976	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 12:40 Hrs of 19-09-2024, 132kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 16:32 Hrs of 19.09.2024.	132 kV Loktak - Rengpang line
22	GD I	Lumshnong area of Meghalaya Power System	21-09-2024 14:19	21-09-2024 14:58	00:39	0	20	0.00%	0.73%	2405	2741	Lumshnong area of Meghalaya Power System was connected with connected to NER Power system via 132 kV Lumshnong - Khliehriat Line. 132 kV Lumshnong - Panchgram Line was under outage since 12:58 Hrs of 21.09.2024. At 14:19 Hrs of 21.09.2024, 132 kV Lumshnong - Khliehriat Line tripped due to which Lumshnong area of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Lumshnong area of Meghalaya Power System by charging 132 kV Lumshnong - Panchgram Line at 14:30 Hrs of 21.09.2024.	32 kV Lumshnong - Khliehriat Line
23	GD I	Nongstoin area of Meghalaya Power System	21-09-2024 14:29	21-09-2024 14:58	00:29	0	7	0.00%	0.21%	3261	3358	Nongstoin area of Meghalaya Power System was connected with connected to NER Power system via 132 KV Nangalbibra-Nongstoin line. 132kV Mawngap(Mawphlang)- Nongstoin already tripped at 12:52 Hrs of 21.09.2024 and it is under emergency Shutdown. At 14:29 Hrs of 21.09.2024, 132 kV Nangalbibra-Nongstoin line tripped due to which Nongstoin area of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to : Nongstoin area of Meghalaya Power System by charging 132 KV Nangalbibra-Nongstoin line at 14:58 Hrs of 21.09.2024.	132 kV Nangalbibra-Nongstoin line
24	GD I	Ziro, Daporijo, Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa areas of Assam Power System	24-09-2024 00:18	24-09-2024 01:57	01:39	0	12 MW in Arunachal Pradesh and 4 MW in Assam	-	-	2721	2908	Ziro, Daporijo, Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa areas of Assam Power System are connected with the rest of NER grid via 132 kV Panyor-Ziro line and 132 kV Rupai-Chapakhowa lines. Prior to the event, 132 kV Panyor-Ziro and 132 kV Ziro-Daporijo lines were under forced outage since 22:18 Hrs & 23:27 Hrs of 23.09.2024 respectively. 132 kV Ziro-Daporijo line tripped at 23:27 Hrs resulting in blackout of Ziro S/S as 132 kV Panyor-Ziro line was under outage. At 00:18 Hrs of 24-09-2024, 132 kV Rupai-Chapakhowa line tripped. Due to tripping of this line, Daporijo, Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System and Chapakhowa areas of Assam Power System was isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Chapakhowa area by charging 132 kV Rupai-Chapakhowa line at 01:35 Hrs of 24.09.2024. 132 kV Roing-Chapakhowa 1&2 were charged at 01:44 hrs & 01:57 hrs respectively and power extended to Daporijo, Basar, Along, Pasighat, Tezu, Namasai area of Arunachal Pradesh power system.	132 kV Rupai-Chapakhowa line
25	GD I	Daporijo,Basar,Along and Pasighat area of Arunachal Pradesh Power System	24-09-2024 19:17	24-09-2024 19:55	00:38	0	13	0.00%	0.39%	3415	3345	Daporijo,Basar, Along and Pasighat area of Arunachal Pradesh Power System were connected with rest of NER Power system through 132 kV Chapakhowa-Roing-Pasighat-Along–Basar-Daporijo link. 132 kV Ranganadi-Ziro was under forced outage since 22:18 Hrs of 23-09-2024. At 19:17 Hrs of 24.09.2024, 132 kV Roing-Pasighat line tripped. Due to tripping of this element, Daporijo,Basar, Along and Pasighat area of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Daporijo,Basar, Along and Pasighat areas of Arunachal Power System by charging 132 kV Roing-Pasighat at 19:55 Hrs.	132 kV Roing-Pasighat line

Details of Grid Events during the Month of Sept 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
26	GD I	Ziro area of Arunachal Pradesh Power System	24-09-2024 21:16	25-09-2024 17:16	20:00	0	2	0.00%	0.06%	3401	3317	Ziro area of Arunachal Pradesh Power System was connected with rest of NER Power system through 132 kV Ziro-Daporijo line. 132kV Ranganadi-Ziro was under forced outage since 22:18 Hrs of 23-09-2024. At 21:16 Hrs of of 24.09.2024, 132 kV Ziro-Daporijo line tripped. Due to tripping of this element, Ziro area of Arunachal Pradesh Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Ziro area by charging 132 kV Ziro-Daporijo line at 17:16 Hrs of 25.09.2024.	132 kV Ziro-Daporijo line
27	GD I	Daporijo, Basar, Along and Pasighat area of Arunachal Pradesh Power System	24-09-2024 23:15	24-09-2024 23:59	00:44	0	16	0.00%	0.52%	3089	3086	Daporijo,Basar, Along and Pasighat area of Arunachal Pradesh Power System were connected with rest of NER Power system through 132 kV Roing-Pasighat line. 132kV Ranganadi-Ziro was under forced outage since 22:18 Hrs of 23-09-2024 and 132kV Daporijo-Ziro line declared faulty since 21:16 Hrs of 24-09-2024. At 23:15 Hrs of of 24.09.2024, 132 kV Roing-Pasighat line tripped. Due to tripping of this element, Daporijo, Basar, Along and Pasighat area of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Pasighat area of Arunachal Power System by charging 132 kV Roing-Pasighat at 23:59 Hrs.	132 kV Roing-Pasighat line
28	GD I	Daporijo, Basar, Along and Pasighat area of Arunachal Pradesh Power System	25-09-2024 01:17	25-09-2024 01:56	00:39	0	14	0.00%	0.49%	2751	2834	Daporijo,Basar, Along and Pasighat area of Arunachal Pradesh Power System were connected with rest of NER Power system through 132 kV Roing-Pasighat line. 132kV Ranganadi-Ziro was under forced outage since 22:18 Hrs of 23-09-2024 and 132kV Daporijo-Ziro line declared faulty since 21:16 Hrs of 24-09-2024. At 01:17 Hrs of of 25.09.2024, 132 kV Roing-Pasighat line tripped. Due to tripping of this element, Daporijo, Basar, Along and Pasighat area of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Daporijo, Basar, Along and Pasighat areas of Arunachal Power System by charging 132 kV Roing-Pasighat at 01:56 Hrs of 25.09.2024.	32 kV Roing-Pasighat line
29	GD I	Pasighat area of Arunachal Pradesh Power System	25-09-2024 03:47	25-09-2024 04:32	00:45	0	2	0.00%	0.08%	2542	2509	Pasighat area of Arunachal Pradesh Power System was connected with rest of NER Power system through 132 kV Pasighat – Roing line. 132kV Ranganadi-Ziro was under forced outage since 22:18 Hrs of 23-09-2024 and 132kV Daporijo-Ziro line declared faulty since 21:16 Hrs of 24-09-2024. 132kV Daporijo-Basar-Along-Pasighat link was under outage since 01:56 Hrs of 25.09.24. At 03:47 Hrs of of 25.09.2024, 132 kV Roing-Pasighat line tripped. Due to tripping of this element, Daporijo, Basar, Along and Pasighat area of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Pasighat area of Arunachal Power System by charging 132 kV Roing-Pasighat at 04:32 Hrs of 25.09.2024.	132 kV Roing-Pasighat line
30	GD I	Bokajan area of Assam Power System	25-09-2024 16:24	25-09-2024 16:51	00:27	0	1	0.00%	0.04%	2557	2594	Bokajan area of Assam Power System was connected with rest of NER Power system through 132 kV Sarupathar-Bokajan line & 132 Dimapur-Bokajan line. At 16:24 Hrs of 25.09.2024, 132 kV Sarupathar-Bokajan line & 132 Dimapur-Bokajan line tripped. Due to tripping of these elements, Bokajan area of Assam Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Bokajan area of Assam Power System by charging 132 kV Sarupathar-Bokajan at 16:51 Hrs of 25.09.2024.	132 kV Sarupathar-Bokajan line & 132 Dimapur-Bokajan line

21. NEW ELEMENTS COMMISSIONED* IN SEPTEMBER 2024

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
NR	1	Bhadla-2, Rajasthan	Adani Green Energy Twenty Five Limited	Solar	143	500	08.09.2024
	2	Bhadla-2, Rajasthan	Adani Green Energy Twenty Five Limited	Solar	119	500	14.09.2024
	3	Bikaner-2, Rajasthan	JUNIPER GREEN COSMIC PRIVATE LIMITED	Solar	100	100	14.09.2024
	4	Bhadla-2, Rajasthan	Kolayat Solar Power Plant NTPC Limited	Solar	54.87	498.78	25.09.2024
	5	Bhadla-2, Rajasthan	Serentica Renewables India 5 Pvt Ltd (SRI5PL)	Solar	110	220	28.09.2024
WR	6	Pachora, MP	NTPC REL, Dehripal	Solar	50	220	20.09.2024
SR	7	400/33KV AMGEPL	AMGEPL	LOT-1/Wind	56.1	56.1	25.09.2024
	8	220/33KV VENA PS	VENA_ENERGY	LOT-1/Wind	68.4	68.4	16.09.2024
	9	230kV TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-4/Wind	24.3	232.2	25.09.2024
	10	230kV TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-5/Wind	21.6	253.8	25.09.2024
	11	400/220 kV Gadag PS(ISTS) KOPPAL	GADAG_GIWEPL_W	LOT-1/Wind	12.6	12.6	21.09.2024
	12	400/220 kV Gadag PS(ISTS) KOPPAL	GADAG_GIWEPL_W	LOT-2/Wind	14.7	27.3	21.09.2024
	13	400/220 kV Gadag PS(ISTS) KOPPAL	GADAG_GIWEPL_W	LOT-3/Wind	8.4	35.7	20.09.2024
	14	400/220 kV Gadag PS(ISTS) KOPPAL	GADAG_GIWEPL_W	LOT-4/Wind	8.4	44.1	21.09.2024
	15	230kV TTGS SAVALPERI	JSW Renew Energy Ltd	LOT-8/Wind	13.5	267.3	05.09.2024
	16	230/33KV Peramium S/S	JSW_NEO	LOT-4/Wind	8.1	145.8	11.09.2024
	17	230kV TTGS VILATHIKULAM	JSW Renew Energy Ltd	LOT-6/Wind	18.9	286.2	24.09.2024
	18	220/33KV VENA PS	VENA_ENERGY	LOT-2/Wind	32.4	100.8	19.09.2024
	19	220/33KV VENA PS	VENA_ENERGY	LOT-3/Wind	32.4	133.2	16.09.2024
	20	YTPP, Telangana	TGGENCO/ YADADRI THERMAL POWER STATION	UNIT-2/Coal	800	1600	12.09.2024
				Total Coal Generation Addition	**800**		
				Total Solar Generation addition	**577**		
				Total Wind Generation addition	**320**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
NR	1	POWERGRID	Bhadla_2 (PG)	ICT-4	765/400/33	1500	07.09.2024
	2	AGE25L	AGE25L SL_BHD2_PG	Power Transformer-1	400/33	330	07.09.2024
	3	AGE25L	AGE25L SL_BHD2_PG	Power Transformer-2	400/33	330	08.09.2024
	4	Juniper_GCPL,Juniper_NEPL	JGCPL_SL_BIK2_PG	Power Transformer-1	220/33	160	12.09.2024
	5	POWERGRID	Jind(PG)	ICT-3	400/220/33	500	21.09.2024
	6	UPRVUNL	Obra_C_TPS(UP)	ICT-1	765/400/33	1000	23.09.2024
	7	SERENTICA_RI5PL_Bik2	SRIPL_SL_BIK2_PG	Power Transformer-4	220/33	150	26.09.2024
	8	SERENTICA_RI5PL_Bik2	SRIPL_SL_BIK2_PG	Power Transformer-3	220/33	150	26.09.2024
	9	POWERGRID	Bahadurgarh(PG)	ICT-3	400/220/33	500	30.09.2024
WR	10	POWERGRID	Navi Mumbai GIS	ICT-1	400/220	315	17.09.2024
	11	Rewa Ultra Mega Solar Ltd (RUMSL)	Dehripal RUMSL S/s	ICT-1	220/33	110	19.09.2024
SR	12	AMGEPL	AMGEPL	ICT-1	400/33	160	23.09.2024
	13	AMGEPL	AMGEPL	ICT-2	400/33	160	23.09.2024
	14	VENA_ENERGY	VENA_PS Power Transformer	Power Transformer-1	220/33	160	13.09.2024
	15	GADAG_GIWEPL_W	SEMBCORP Green Infra	ICT-1	220/33	160	17.09.2024
	16	GADAG_GIWEPL_W	SEMBCORP Green Infra I	ICT-2	220/33	160	17.09.2024
	17	YTPP TGTRANSCO	YADADRI TPP	GT-1 (3X330)	400/27	990	21.09.2024
	18	TANTRANSCO	UDHANGUDI	ST-1	400/11/11	110	23.09.2024
	19	PVG_IRCON_S	IRCON Solar PSS	ICT-1	220/33	125	18.09.2024
	20	PVG_IRCON_S	IRCON Solar PSS	ICT-1	220/33	125	18.09.2024
	21	POWERGRID	MYSORE	ICT-4	400/220/33	500	28.09.2024
ER	22	PGCIL	BIRPARA	ICT-2(Replacement)	220KV/132	160	24.09.2024
					Total (MVA)	**7855**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NR	1	GTL,PGYTL	765kV Ghatampur_TPS(UP)-Rampur_PRSTL (UP)-1	406.6	Quad Bersimis	07.09.2024
	2	AGE25L	400kV AGE25L SL_BHD2_PG-Bhadla_2 (PG)-1	11.0	AL59 Moose	07.09.2024
	3	Juniper_GCPL,Juniper_NEPL	220kV JGCPL_SL_BIK2_PG-Bikaner_2 (PBTSL)-1	9.3	HTLS	12.09.2024
WR	4	Mumbai Urja Marg Ltd. (MUML)	400 kV Padhge(PG)-Navi Mumbai (GIS)	67.7	Quad Moose	16.09.2024
	5	Mumbai Urja Marg Ltd. (MUML)	400 kV Padghe(PG) - Kharghar	70.9	Quad Moose	24.09.2024
	6	Mumbai Urja Marg Ltd. (MUML)	400 kV Navi Mumbai (GIS) - Vikhroli	61.3	Quad Moose	27.09.2024
SR	7	AMGEPL	400KV-KURNOOL-CPSS Greenko Line-1	12.1	QUAD MOOSE	21.09.2024
	8	AMGEPL	400KV-CPSS-AMGEPL Wind-PSS-1	50.0	TWIN MOOSE	23.09.2024
	9	TANTRANSCO	400KV-OTTAPIDARAM-UDANGUDI LINE-2	76.0	QUAD MOOSE	13.09.2024
	10	GADAG GIWEPL	220KV-GADAG-SEMBCORP-GREEN INFRA Line-1	54.3	AL59 MOOSE	16.09.2024
	11	TSTRANSCO	220KV-SURYAPET-PULICHINTALA-LINE-1	85.1	MOOSE	06.09.2024
NER	12	Nangalbibra-Bongaigaon Transmission Ltd (NBTL)	132 kV Hatsingimari(Assam)- Ampati(Meghalaya) 1	18.6	ACSR Panther	07.09.2024
	13		132 kV Hatsingimari(Assam)- Ampati(Meghalaya) 2	18.6	ACSR Panther	07.09.2024
			Total ckt km	**941.7**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
SR	1	APTRANSCO	400KV-VEMAGIRI_AP-KAMAVARAPUKOTA-Feeder-1 (from K V KOTA end)	58.142	TWIN MOOSE	30.09.2024
	2	APTRANSCO	400KV-VEMAGIRI_AP-KAMAVARAPUKOTA-Feeder-2 (from K V KOTA end)	58.142	TWIN MOOSE	30.09.2024

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
SR	1	TNTRANSCO	400KV VIRUDHUNAGAR-KAYATHAR Line-1 (400KV KAYATHAR-THENNAMPATTY LILO at VIRUDHUNAGAR)	88.637	QUAD MOOSE	10.09.2024
	2	TNTRANSCO	400KV VIRUDHUNAGAR-THENNAMPATTY Line-1 (400KV KAYATHAR-THENNAMPATTY LILO at VIRUDHUNAGAR)	74.529	QUAD MOOSE	10.09.2024
WR	3	Mumbai Urja Marg Ltd. (MUML)	400 kV Vapi-II-Vapi(PG) Ckt 2 (LILO of 400 kV Vapi(PG)-Kakrapar -1&2 at Vapi-II (MUML))	5.67	AAAC Moose	02.09.2024

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
NR	1	UPRVUNL	125 MVAr Bus Reactor at Jawaharpur_TPS(UP)	400	125	06.09.2024
	2	GTL,PGYTL	330 MVAr Switchable Non-Convertable LR of 765 KV RAMPUR LINE at Ghatampur_TPS(UP)	765	330	06.09.2024
WR	3	POWERGRID	63 MVAR Bus Reactor at 400/220 kV Navi Mumbai GIS	400	63	16.09.2024
	4	MSETCL	80 MVAR Bus Reactor at 400/220 kV Kharghar S/s	400	80	19.09.2024
SR	5	TANTRANSCO	125 MVAR Bus Reactor at UDANGUDI	400	125	21.09.2024
ER	6	BGCL	125 MVAR Bus Reactor-1 AT NAUBATPUR(BH)	400	125	16.09.2024
	7	BGCL	125 MVAR Bus Reactor-2 AT NAUBATPUR(BH)	400	125	16.09.2024
	8	PGCIL	125MVAR Bus Reactor-3 AT ALIPURDUAR (PG)	400	125	24.09.2024
				Total (MVAr)	**1098**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

*Includes first time charging (FTC) as well

विद्युत विभव रूपरेखा माह - सितम्बर 2024 VOLTAGE PROFILE - September 2024

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	794	749	772
2		दारिपली DARLIPALI	0%	100%	0%	0%	0	787	761	775
3		गया GAYA	0%	100%	0%	0%	0	789	748	772
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	793	736	762
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	797	767	784
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	797	743	768
7		रांची RANCHI	0%	100%	0%	0%	0	794	755	779
8		सासाराम SASARAM	0%	100%	0%	0%	0	801	741	768
1		आगरा AGRA	0%	100%	0%	0%	0	800	750	778
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	800	745	776
3		अजमेर AJMER	0%	99%	1%	1%	6	804	749	785
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	796	740	771
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	784	757	770
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	782	751	768
7		अंता ANTA	0%	100%	0%	0%	0	798	763	780
8		बलिया BALLIA	0%	100%	0%	0%	0	792	739	767
9		बारा BARA	0%	100%	0%	0%	0	780	754	768
10		भाड़ला BHADLA	0%	100%	0%	0%	0	809	723	779
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	0	801	729	782
12		भिवानी BHIWANI	0%	100%	0%	0%	0	799	744	781
13		बीकानेर BIKANER	0%	100%	0%	0%	0	801	729	780
14		बरेली BAREILLY	0%	100%	0%	0%	2	803	742	776
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	3	805	759	784
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	798	720	778
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	797	737	773
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	99%	1%	1%	10	802	722	777
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	0	801	744	777
20		हापुड़ HAPUR	0%	100%	0%	0%	0	800	736	773
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	795	735	769
22		झटिकरा JHATIKARA	0%	100%	0%	0%	0	795	740	774
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	792	742	771
24		खेतरी KHETRI	0%	100%	0%	0%	0	801	737	778
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	800	739	774
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	774	742	761
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	795	738	772
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	789	731	765
29		मेरठ MEERUT	0%	100%	0%	0%	2	805	741	778
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	799	738	773
31		मोगा MOGA	0%	100%	0%	0%	1	801	733	781
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	788	748	765
33		उरई ORAI	0%	100%	0%	0%	0	802	750	783
34		फागी PHAGI	0%	100%	0%	0%	0	800	756	783
35		रामपुर RAMPUR	0%	99%	1%	1%	6	808	738	775
36		उन्नाव UNNAO	0%	100%	0%	0%	0	796	731	765
37		वाराणसी VARANASI	0%	100%	0%	0%	0	794	750	776
1		अकोला AKOLA	0%	100%	0%	0%	0	793	750	772
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	1	803	748	776
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	790	753	771
4		भुज BHUJ	0%	100%	0%	0%	0	800	743	779
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	795	744	774
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	788	756	771
7		बीना BINA	0%	100%	0%	0%	0	797	753	779
8		बनसकेंठा BANASKANTHA	0%	99%	1%	1%	4	807	752	785
9		चापा CHAMPA	0%	98%	2%	2%	17	807	760	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	794	750	773
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	788	748	770
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	794	760	779
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	793	745	772
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	3	802	765	786
15		ग्वालियर GWALIOR	0%	100%	0%	0%	0	800	752	781
16		इंदौर INDORE	0%	100%	0%	0%	0	787	750	769
17	पश्चिमी क्षेत्र WR	जबलपुर JABALPUR	0%	99%	1%	1%	4	803	758	786
18		खंडवा KHANDWA	0%	100%	0%	0%	0	788	752	771
19		कोरडी KORADI	0%	100%	0%	0%	0	777	747	763
20		लकाडिया LAKADIYA	0%	98%	2%	2%	11	805	752	784
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	797	767	783
22		पड़घे PADGHE	0%	99%	1%	1%	4	809	746	777
23		परली PARLI	0%	99%	1%	1%	6	806	756	785
24		पुणे PUNE	0%	99%	1%	1%	4	808	744	776
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	3	805	762	787
26		सासन SASAN	0%	100%	0%	0%	0	795	761	780
27		सतना SATNA	0%	98%	2%	2%	13	803	763	786
28		सिवनी SEONI	0%	100%	0%	0%	0	800	758	780
29		सीपत SIPAT	0%	100%	0%	0%	0	787	758	772
30		सोलापुर SOLAPUR	0%	99%	1%	1%	5	806	743	783
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	773	747	760
32		तामनार TAMNAR	0%	100%	0%	0%	0	796	765	782
33		वड़ादरा VADODARA	0%	100%	0%	0%	0	796	748	774
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	798	765	783
35		वर्धा WARDHA	0%	99%	1%	1%	7	806	751	783
36		वरोरा WARORA	0%	100%	0%	0%	3	803	754	786
1		अरियलुर ARIYALUR	0%	96%	4%	4%	27	805	753	787
2		कड़पा CUDDAPAH	0%	97%	3%	3%	25	811	756	784
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	99%	1%	1%	5	806	743	777
4		कर्नूल KURNOOL	0%	100%	0%	0%	3	804	749	780
5		महेश्वरम MAHESWARAM	0%	97%	3%	3%	20	808	750	785
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	87%	13%	13%	91	812	751	789
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	799	752	775
8		नार्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	99%	1%	1%	6	812	750	779
9		रायचूर RAICHUR	0%	100%	0%	0%	2	803	751	779
10		श्रीकाकुलम SRIKAKULAM	0%	98%	2%	2%	18	806	745	780
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	3	800	747	772
12		वेमागिरी VEMAGIRI	0%	97%	3%	3%	24	808	742	781
13		वारंगल WARANGAL	0%	99%	1%	1%	4	811	754	779
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	412	400	406
2		बिस्वनाथ चरियाली BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	418	389	405
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	415	399	407
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	417	397	409
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	414	393	404
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	408	396	402
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	414	394	403
8		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	411	399	406
9	पूर्वोत्तर क्षेत्र NER	मीसा MISA (400 kV)	0%	100%	0%	0%	0	414	394	403
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	415	397	406
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	418	395	406
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	415	402	407
13		पुर्वेकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	412	394	402
14		रंगनदी RANGANADI (400 kV)	0%	100%	0%	0%	0	410	398	403
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	399	407
16		सुबानसिरी SUBANSIRI (400 kV)	0%	100%	0%	0%	0	413	397	404
17		सुर्ज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	411	394	402
18		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	415	384	401

All listed stations are 765 kV stations unless otherwise mentioned
***Percentage is calculated w.r.t. Time of one month.**

23.ALL TIME HIGHEST

30-09-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	186 01-05-2024
WR	74974 01-06-2024	67482 30-05-2024	1648 06-05-2024	167 18-12-2014	310 28-05-2024	102.85 30-04-2024
SR	68735 13-03-2024	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	323 26-07-2024	148.7 31-03-2024
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	4 09-06-2024
NER	3905 19-09-2024	3787 19-09-2024	80 20-09-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	426 30-04-2024

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	17949	20-01-2024	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	4309	02-09-2024	41.2	26-06-2024
	J&K(UT) and Ladakh(UT)	5197	30-09-2024	66.8	26-01-2024
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	17819	29-12-2023	335.9	10-11-2023
	Maharashtra	28969	07-02-2024	648.3	30-04-2024
	Goa	803	19-04-2024	17.6	18-05-2024
	DD & DNH	1356	25-09-2024	32.1	05-06-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	15623	08-03-2024	311.0	13-03-2024
	Karnataka	17220	12-03-2024	336.9	05-04-2024
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	8001	23-09-2024	172.8	30-07-2024
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	195	26-05-2024	3.9	18-06-2024
	Assam	2687	20-09-2024	55.8	20-09-2024
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.4	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24. System Reliability Indices Report for the month of SEPTEMBER 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	124	31.00	4.31
3	Import of NR	14	3.50	0.49
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	34	8.50	1.18
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
