ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre
कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या:- **GRID-INDIA/NLDC/MR/** दिनांक: **25.03.2025**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **फ़रवरी 2025**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **फ़रवरी 2025** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
मुख्य महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



फ़रवरी 2025

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह फ़रवरी2025 के लिए प्रचालन निष्पादन रिपोर्ट


OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF FEBRUARY -2025

पृष्ठसूची **CONTENTS**


1	माह फ़रवरी 2025 की सारांश रिपोर्ट Summary of report for the month of FEBRUARY 2025	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति Evening Peak Hour Demand Met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	07 फ़रवरी के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 07-FEBRUARY (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह फ़रवरी 2024 से तुलना Energy requirement and met comparison with FEBRUARY 2024	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह फ़रवरी 2024 से तुलना Peak demand requirement and met comparison with FEBRUARY 2024	25

14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक)एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-45
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	46-48
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	49-57
21	नए चार्ज किये गए तत्व New elements Charged	58
22	विभव रूपरेखा Voltage profile	59
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह फ़रवरी 2025 तक All Time Highest (Demand & Energy) figures: Till FEBRUARY 2025	60
24	फ़रवरी 2025 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for FEBRUARY 2025	61


1. SUMMARY OF REPORT FOR THE MONTH OF FEBRUARY-2025

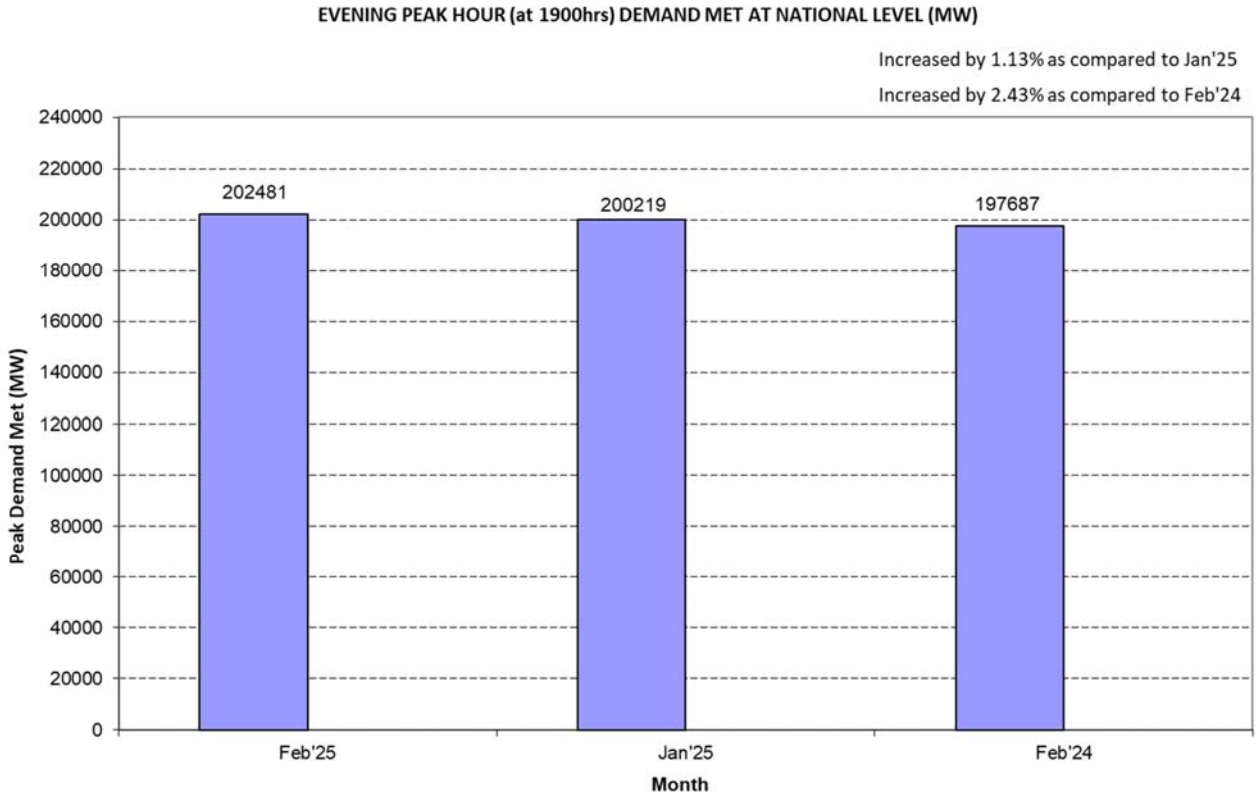


*Source: As per daily data furnished by states

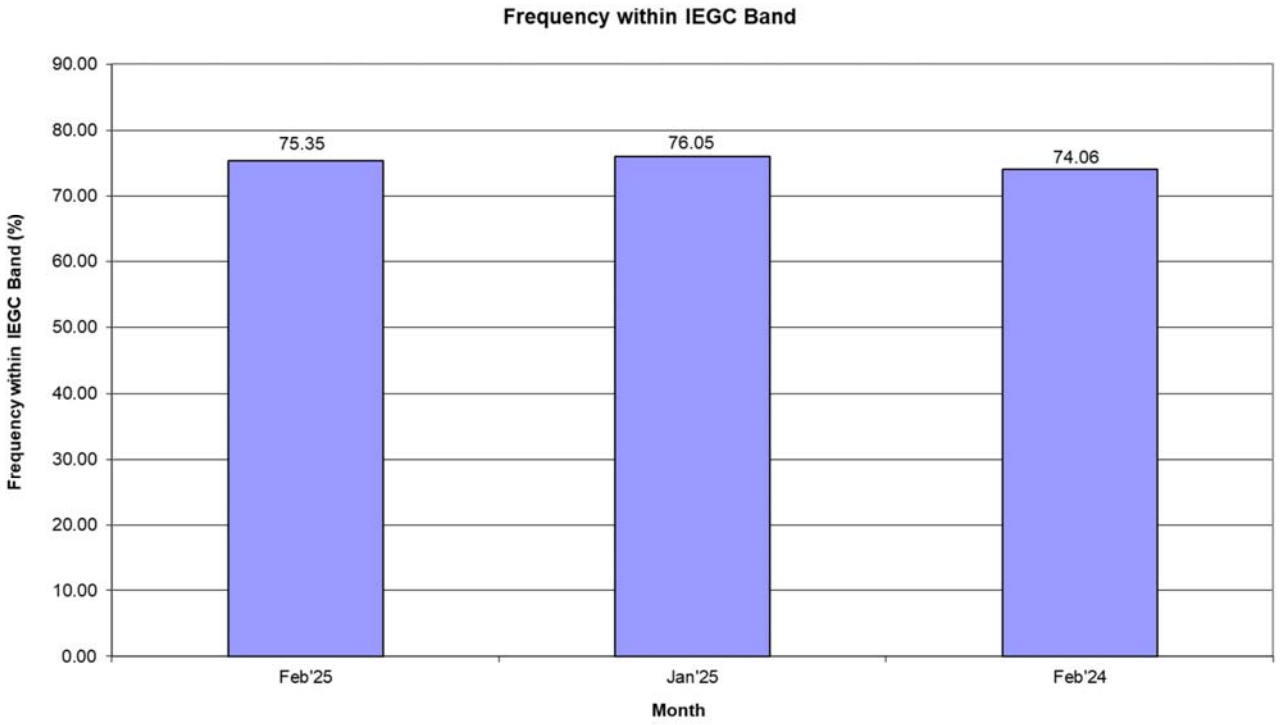


ENERGY MET AT NATIONAL LEVEL (MU)

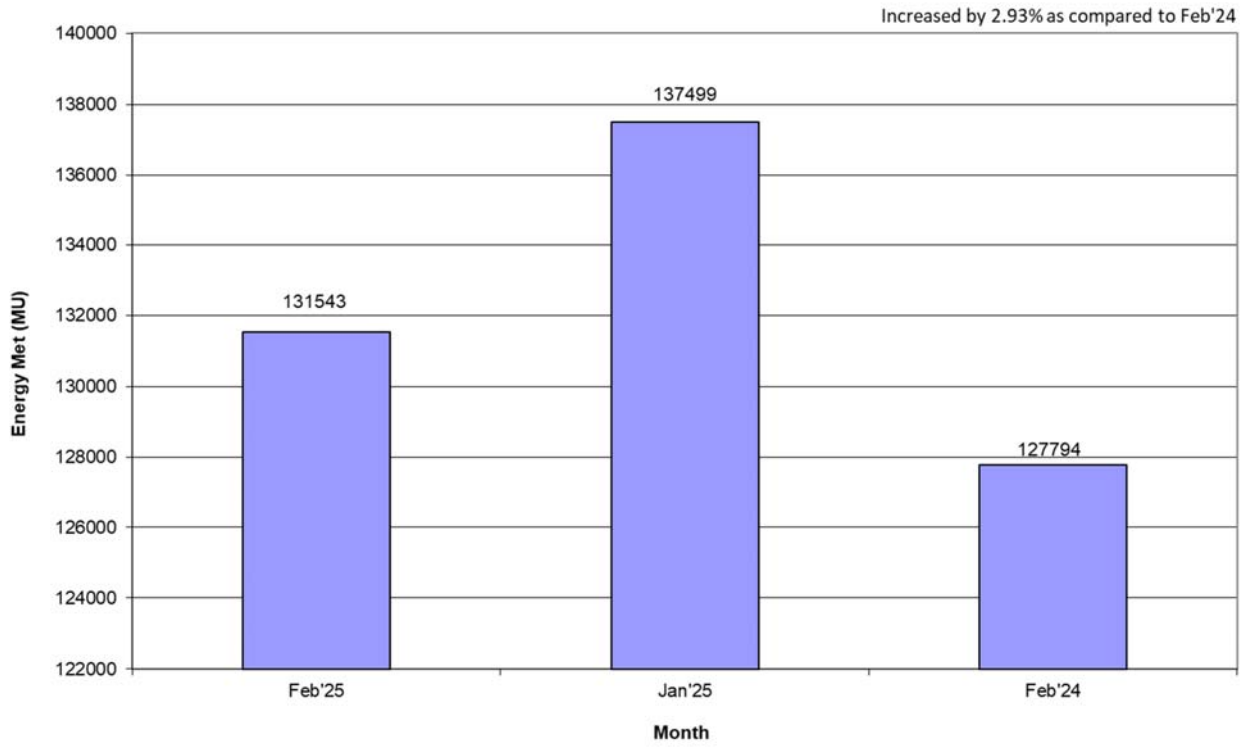


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

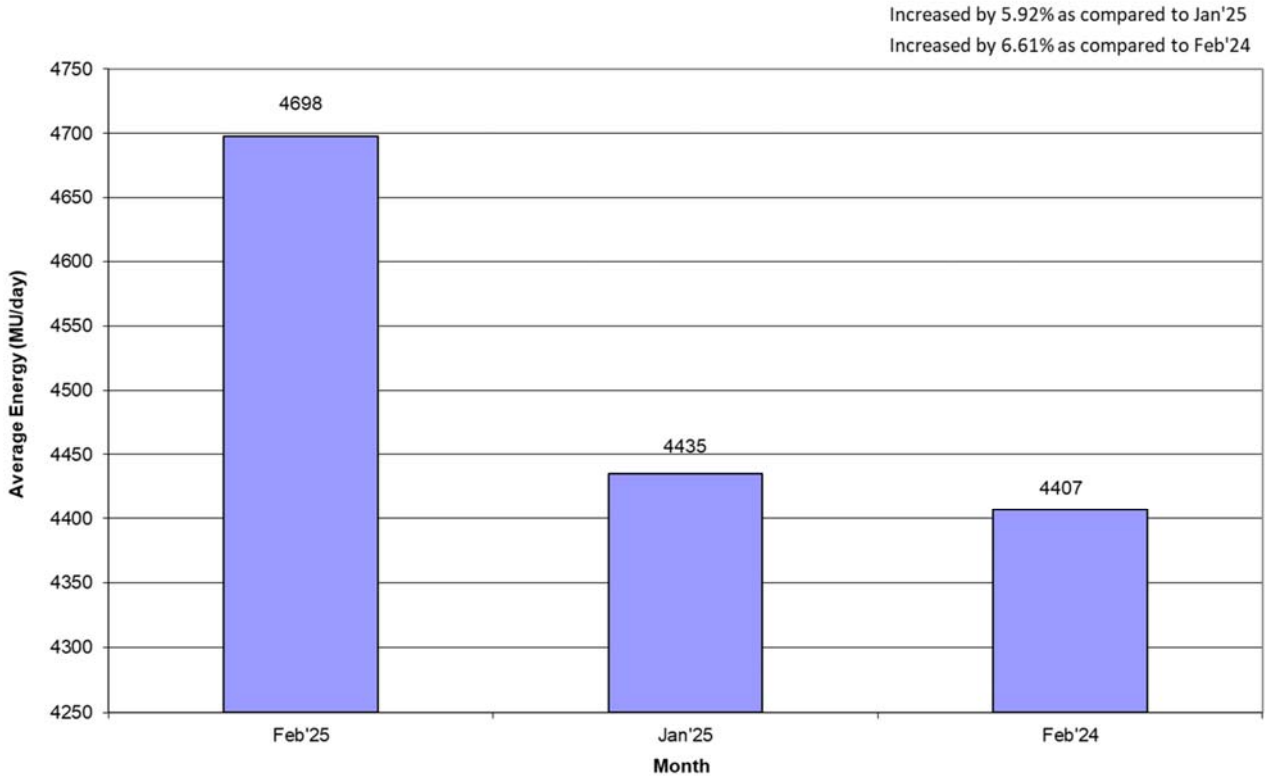


HYDRO GENERATION AT NATIONAL LEVEL (MU)

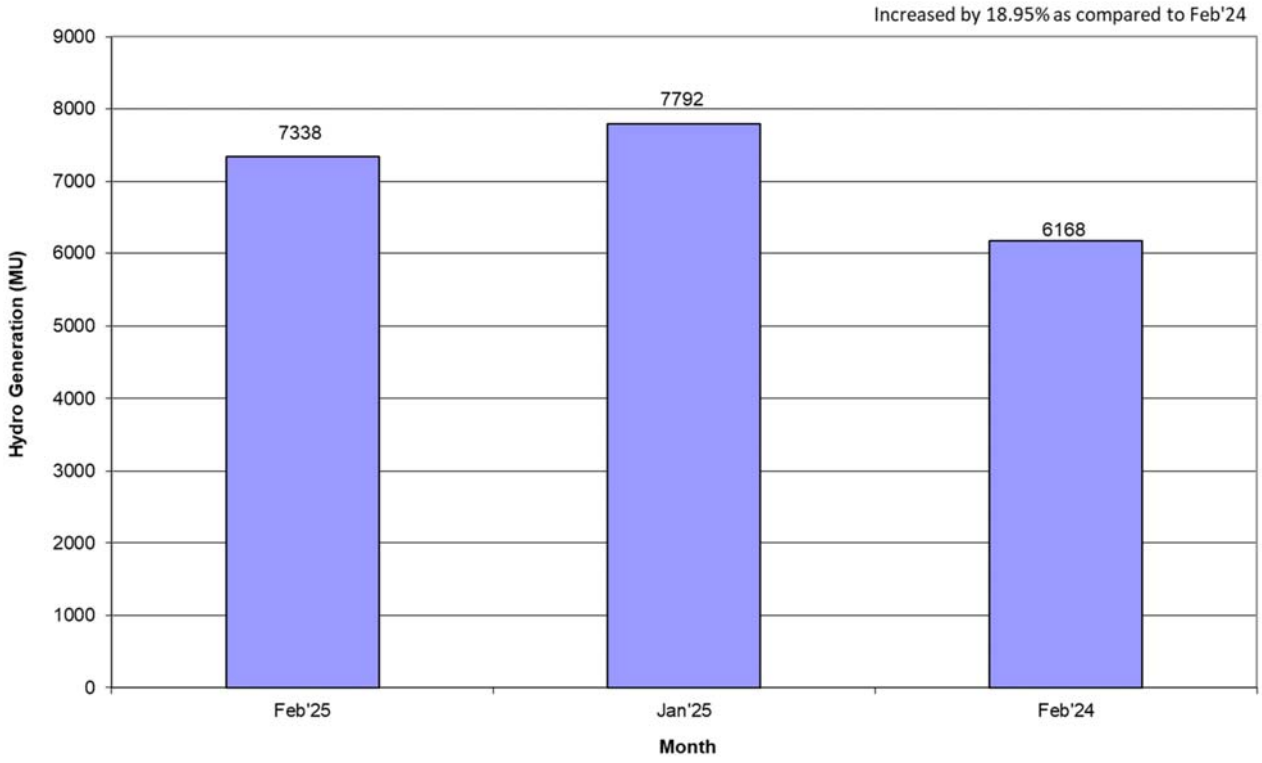


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

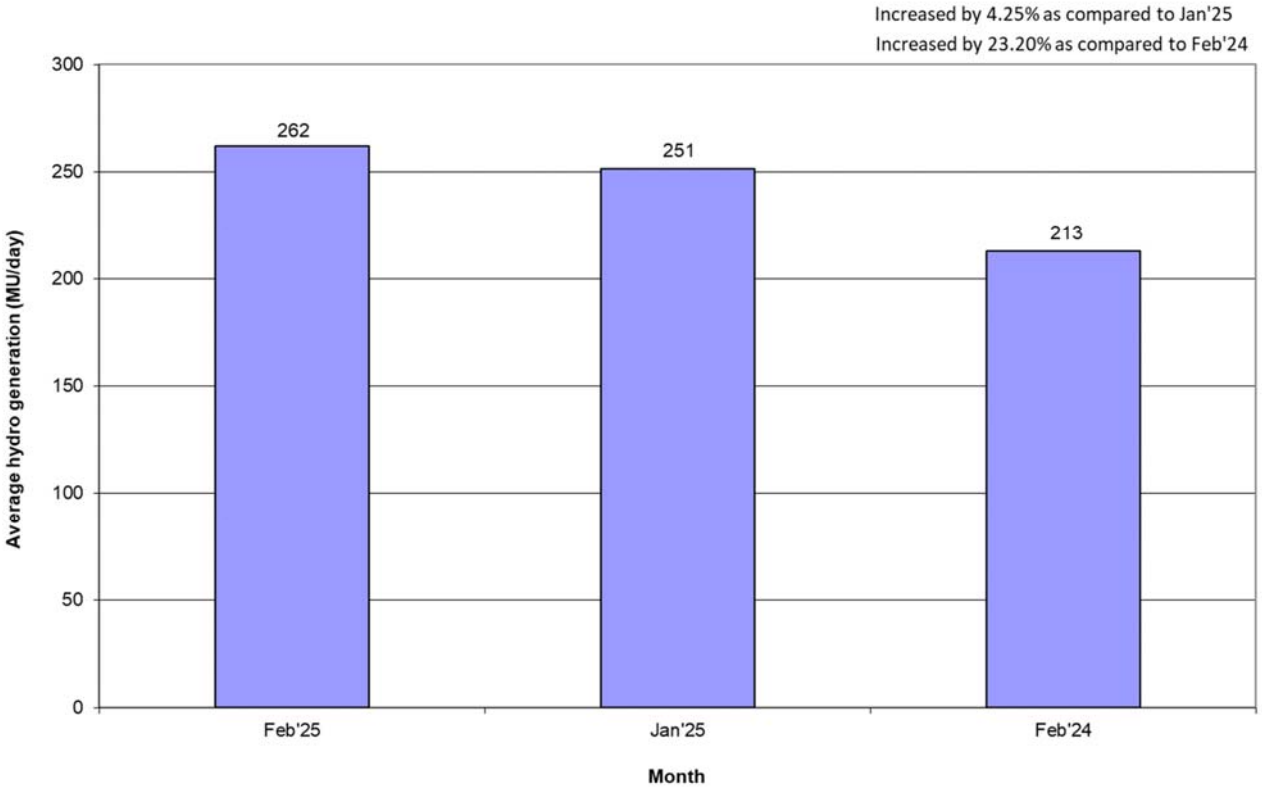


WIND GENERATION AT NATIONAL LEVEL (MU)

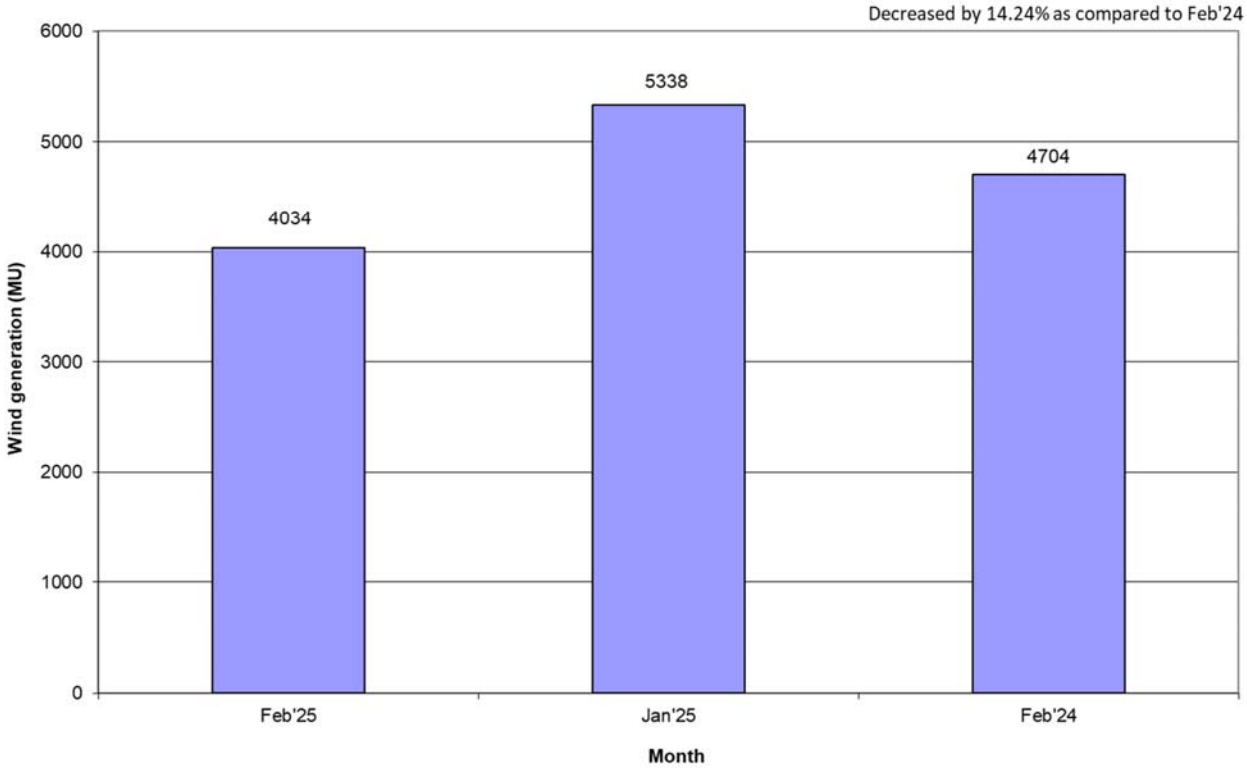


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

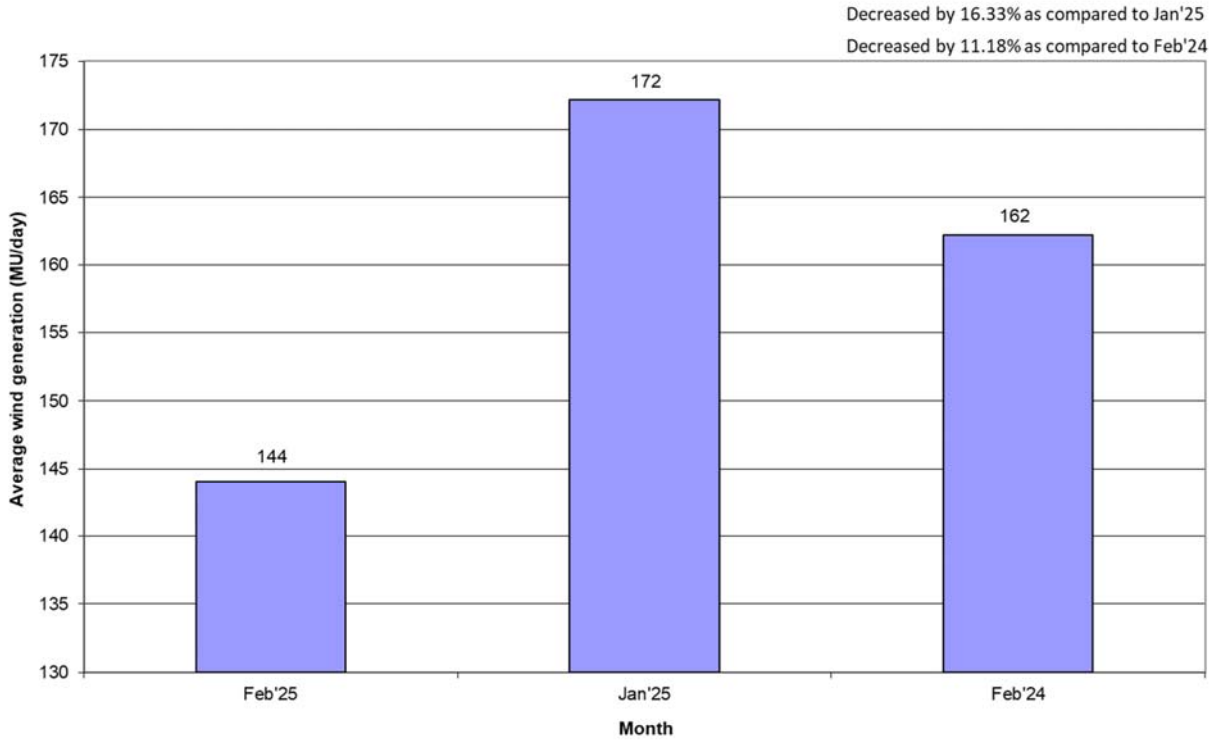

SOLAR GENERATION AT NATIONAL LEVEL (MU)

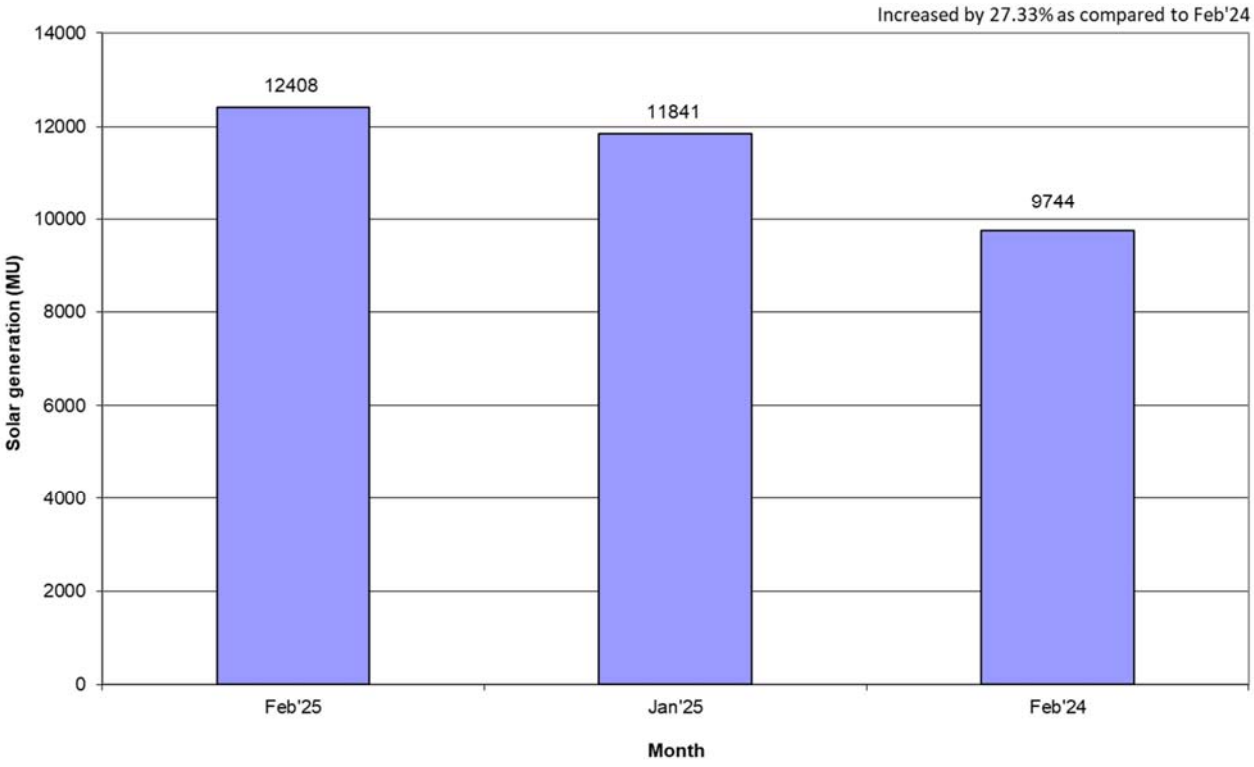

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

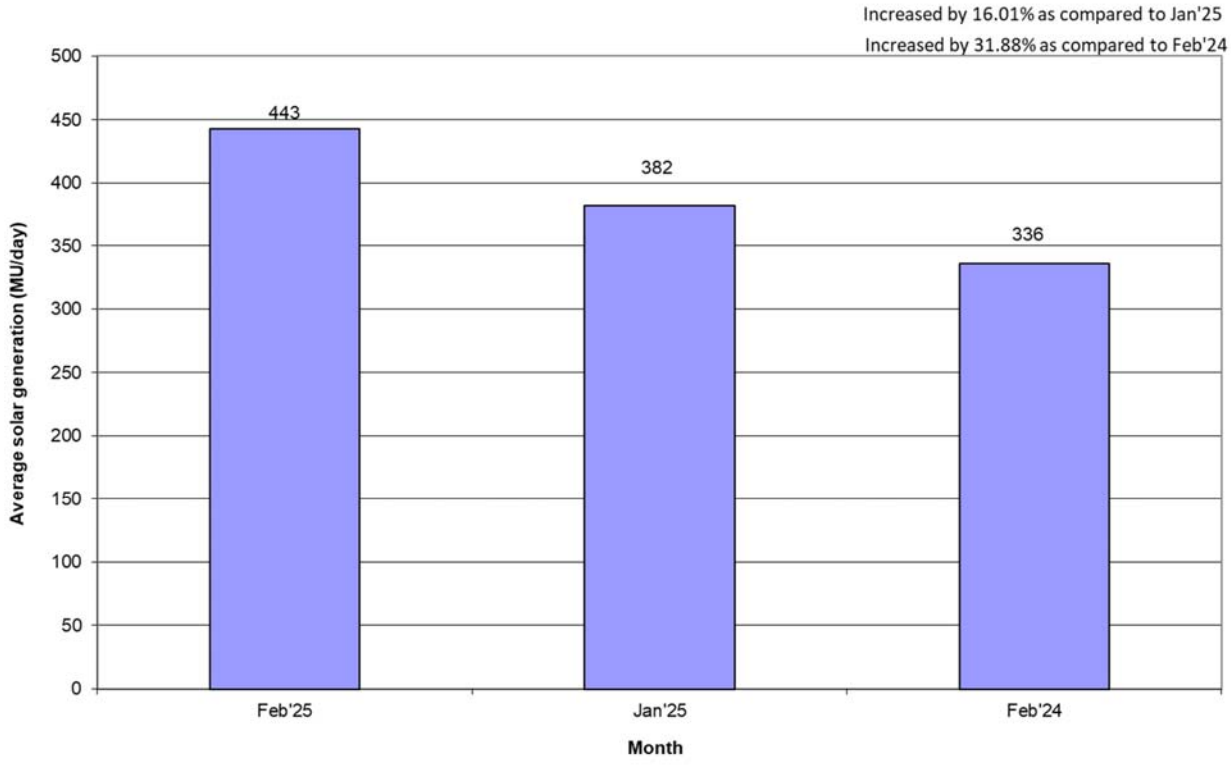

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 28.02.2025
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	59298	1580	5995	0	66873	1620	20830	46239	135562
2	WR	75323	1400	10806	0	87529	3240	7563	59406	157738
3	SR	50456	3640	6642	434	61171	3320	11867	59017	135376
4	ER	28875	0	80	0	28955	0	4764	2382	36101
5	NER	1242	0	1665	36	2943	0	1944	625	5512
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	215193	6620	25188	589	247590	8180	46968	167710	470448

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति
EVENING PEAK HOUR (at 19:00hrs) DEMAND MET AT NATIONAL LEVEL


माह: फरवरी 2025 MONTH:- FEB 2025

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Feb-25	56947	66509	47250	22875	2720	196301
2-Feb-25	54215	63339	43753	22238	2606	186151
3-Feb-25	57467	66573	47766	22807	2684	197297
4-Feb-25	56685	66968	47937	23520	2743	197853
5-Feb-25	57258	67019	48163	23164	2722	198326
6-Feb-25	58984	67498	48668	23003	2737	200890
7-Feb-25	58645	67754	47809	22888	2680	199776
8-Feb-25	58041	68571	47397	22791	2705	199505
9-Feb-25	54629	65245	44111	22067	2553	188605
10-Feb-25	57948	68418	48027	23043	2670	200106
11-Feb-25	57670	68889	48067	22775	2726	200127
12-Feb-25	57595	68707	48650	22977	2692	200621
13-Feb-25	57869	68500	49682	23413	2661	202125
14-Feb-25	57114	68126	49506	23382	2666	200794
15-Feb-25	57236	68246	48617	23366	2714	200179
16-Feb-25	53718	64959	44896	22240	2615	188428
17-Feb-25	56841	68968	49664	23321	2759	201553
18-Feb-25	55835	69244	50592	23342	2682	201695
19-Feb-25	55636	69091	51222	23452	2748	202149
20-Feb-25	54142	68907	51294	22243	2713	199299
21-Feb-25	55671	68526	51144	23129	2685	201155
22-Feb-25	55560	69578	50894	22355	2735	201122
23-Feb-25	52992	66785	46948	22011	2449	191185
24-Feb-25	55782	69618	50976	22778	2710	201864
25-Feb-25	55738	69702	51237	23103	2701	202481
26-Feb-25	53386	66798	49301	22635	2701	194821
27-Feb-25	54855	70350	50554	23261	2689	201709
28-Feb-25	54119	69897	51394	23983	2695	202088
उच्चतम MAXIMUM	58984	70350	51394	23983	2759	202481
निम्नतम MINIMUM	52992	63339	43753	22011	2449	186151
औसत AVERAGE	56164	67957	48769	22934	2684	198507
अब तक का उच्चतम All Time Max.	82312	**70350**	54798	29695	3787	227354
दिनांक Date	23.07.24	**27.02.25**	29.04.24	29.05.24	19.09.24	29.05.24

Source: As per daily data furnished by states

EVENING PEAK HOUR DEMAND(at 1900hrs) MET DURING THE MONTH OF FEBRUARY' 2025

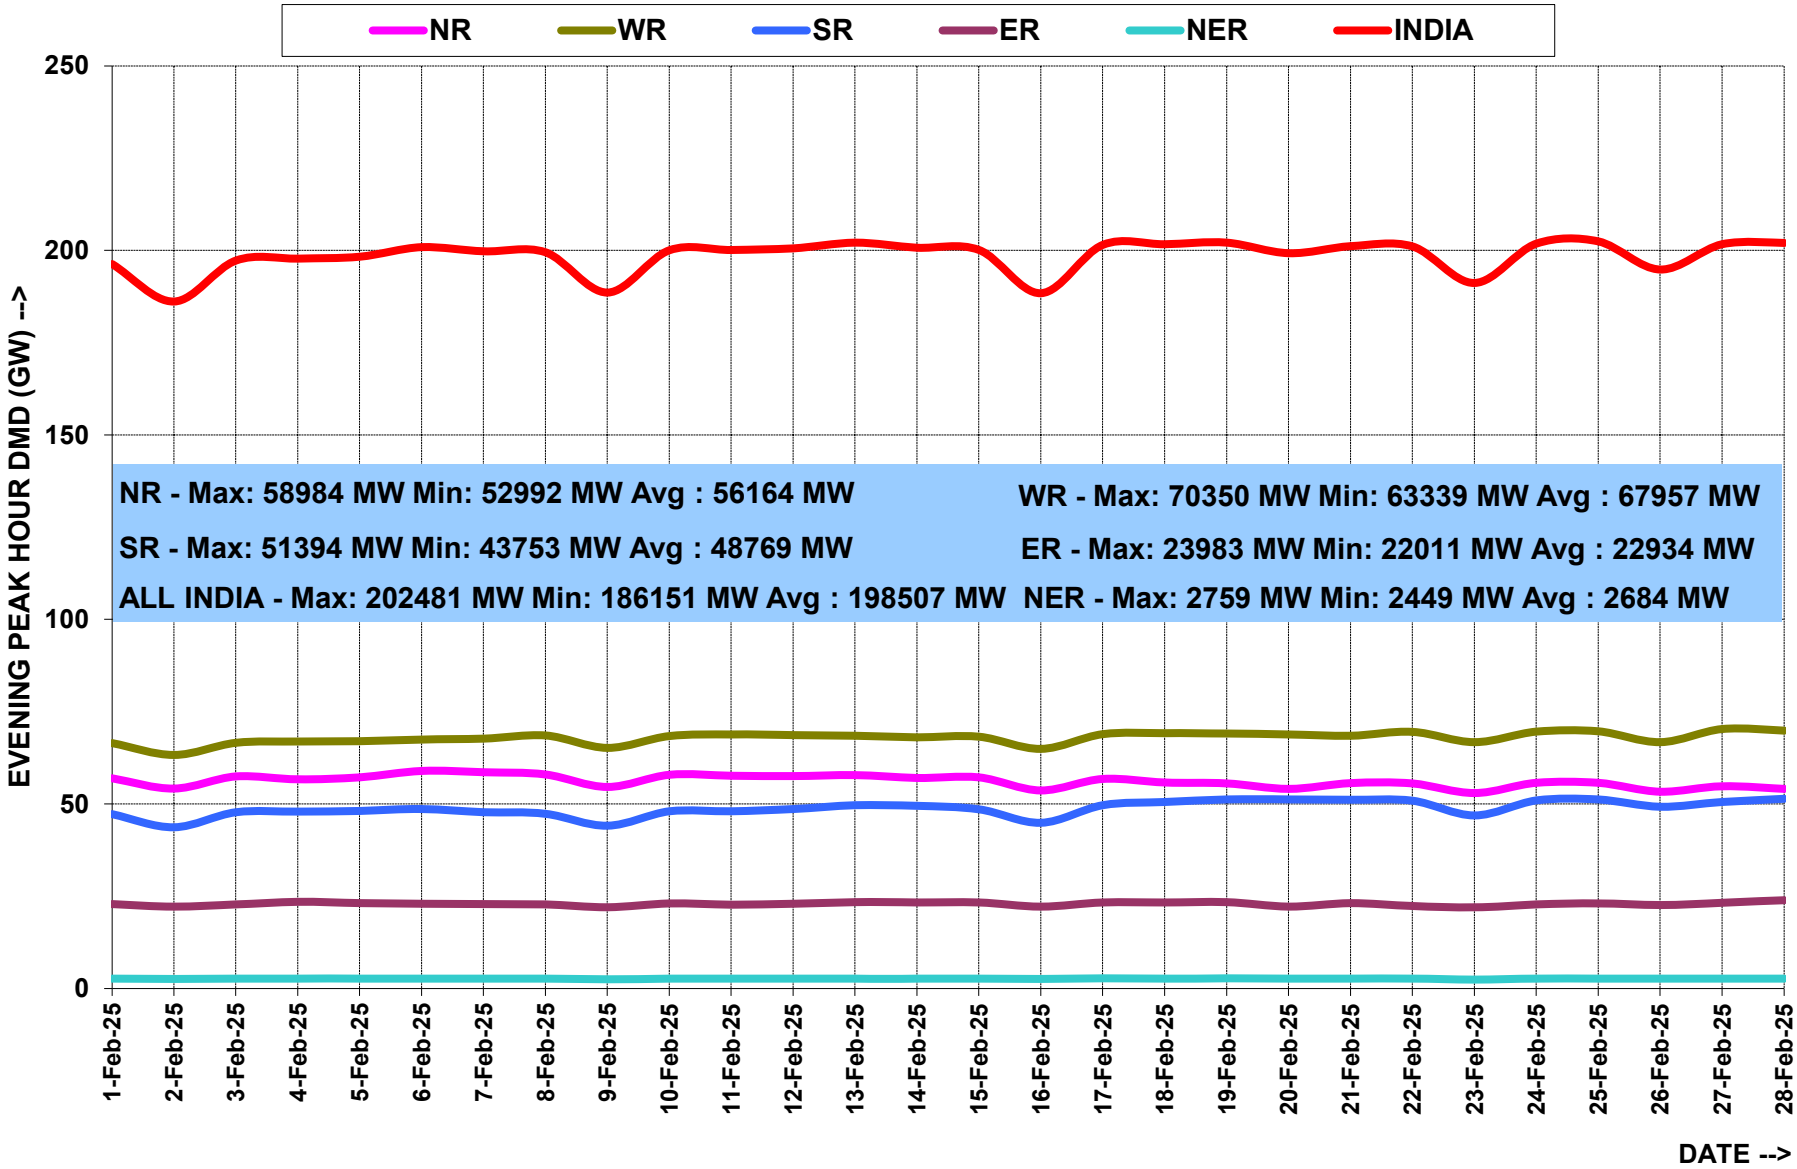


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: फरवरी 2025 MONTH:- FEB 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-25	1236	1594	1274	468	50	4623
02-Feb-25	1192	1551	1204	463	49	4459
03-Feb-25	1241	1594	1262	477	51	4624
04-Feb-25	1254	1604	1284	483	50	4676
05-Feb-25	1245	1594	1302	484	50	4675
06-Feb-25	1264	1601	1306	477	50	4698
07-Feb-25	1280	1605	1319	474	50	4729
08-Feb-25	1280	1629	1295	468	50	4722
09-Feb-25	1223	1594	1230	460	46	4553
10-Feb-25	1252	1637	1292	473	49	4703
11-Feb-25	1261	1645	1318	481	50	4755
12-Feb-25	1266	1633	1332	486	49	4766
13-Feb-25	1233	1631	1338	482	47	4731
14-Feb-25	1243	1629	1337	478	49	4736
15-Feb-25	1245	1624	1310	481	50	4710
16-Feb-25	1213	1583	1253	465	46	4561
17-Feb-25	1237	1630	1325	483	51	4725
18-Feb-25	1245	1648	1353	492	50	4787
19-Feb-25	1233	1651	1365	490	50	4789
20-Feb-25	1140	1644	1379	476	50	4689
21-Feb-25	1198	1645	1389	479	50	4761
22-Feb-25	1202	1659	1373	478	49	4761
23-Feb-25	1163	1615	1303	456	45	4583
24-Feb-25	1209	1645	1344	469	49	4716
25-Feb-25	1216	1658	1375	479	50	4778
26-Feb-25	1213	1634	1367	478	50	4742
27-Feb-25	1170	1664	1359	485	50	4728
28-Feb-25	1162	1675	1386	490	50	4763
कुल TOTAL	34319	45513	36976	13357	1378	131543
उच्चतम MAXIMUM	1280	1675	1389	492	51	4789
निम्नतम MINIMUM	1140	1551	1204	456	45	4459
औसत AVERAGE	1226	1625	1321	477	49	4698
संचयी 2024-25 Cumulative 2024-25	481160	488131	383063	182202	18993	1553549
अब तक का उच्चतम All Time Max.	1990	**1675**	1416	692	80	5466
दिनांक Date	18.06.24	**28.02.25**	05.04.24	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF FEBRUARY' 2025

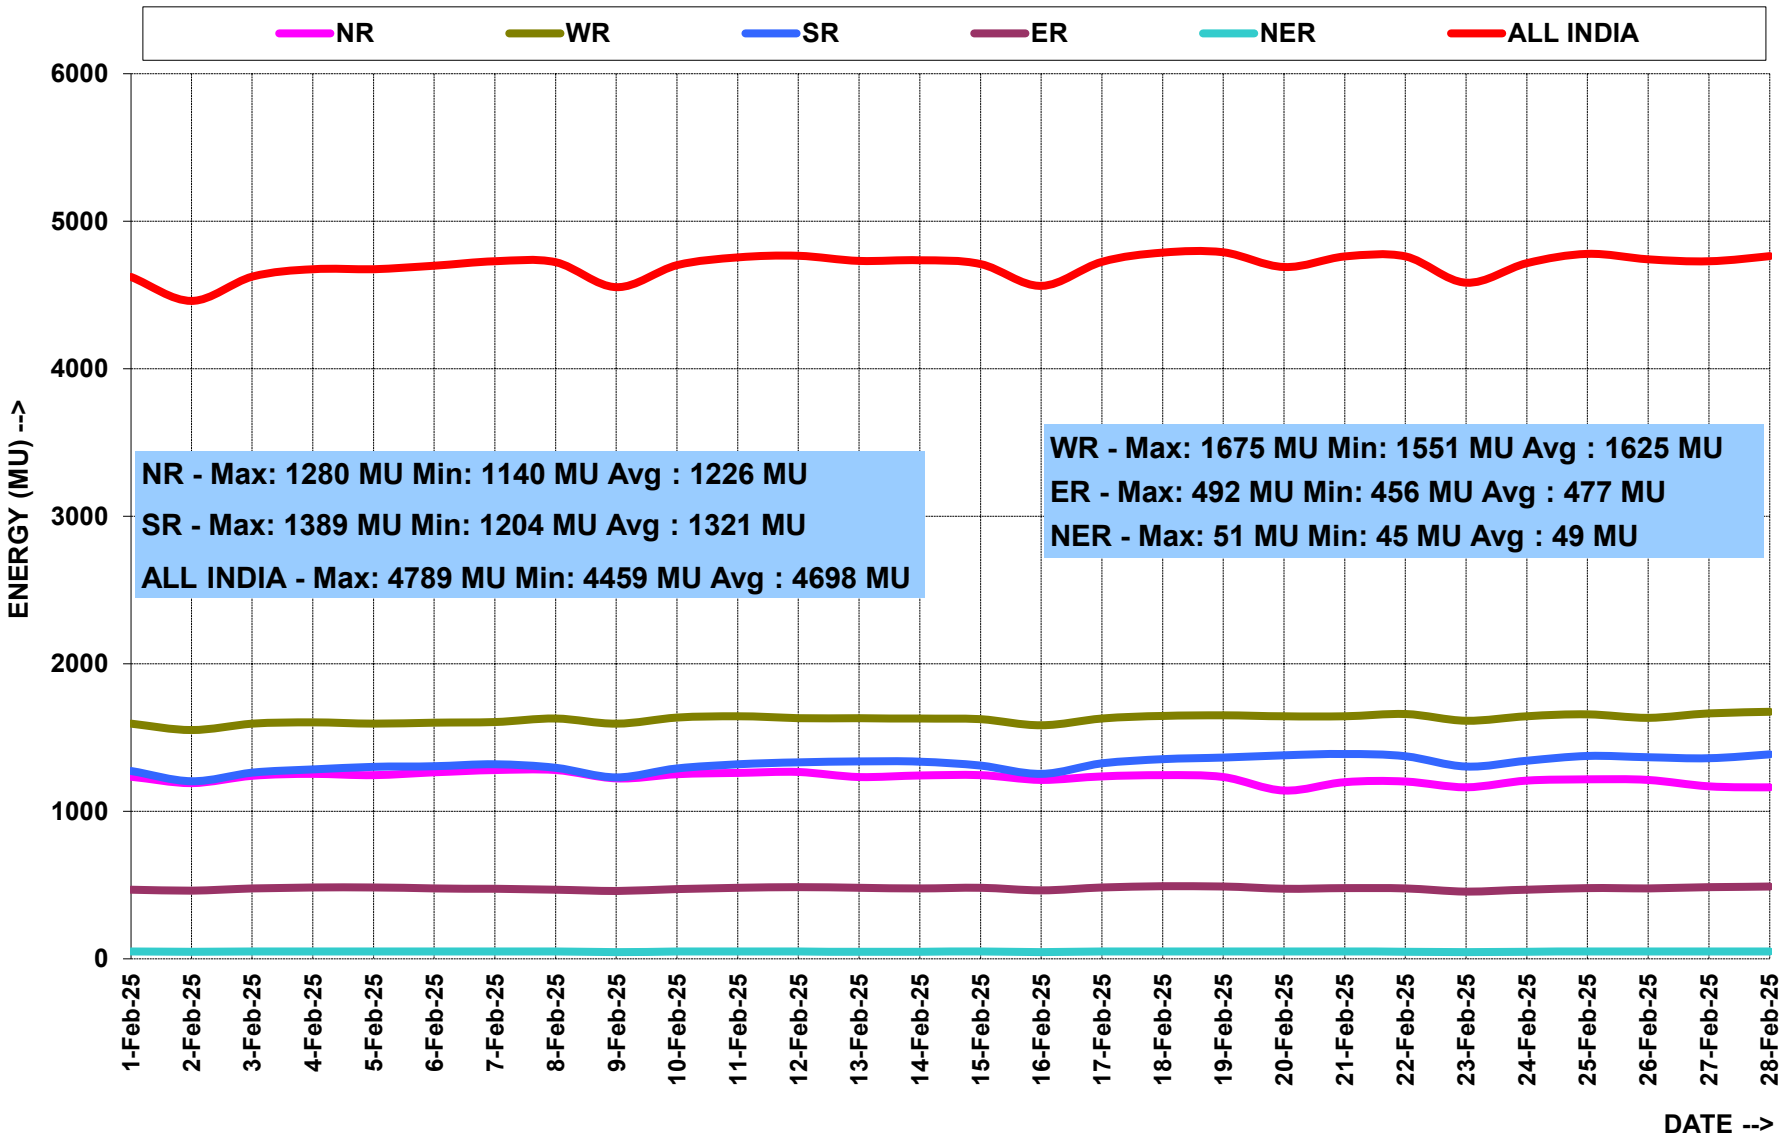

5. वर्ष 2024-25 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78		50.38	49.46	50.00
	Oct-24	All India Grid	4.86	80.27	14.87		50.39	49.58	50.00
	Nov-24	All India Grid	5.15	80.80	14.05		50.32	49.55	50.00
	Dec-24	All India Grid	5.58	76.45	17.97		50.42	49.49	50.00
	Jan-25	All India Grid	5.23	76.05	18.72		50.31	49.60	50.00
	Feb-25	All India Grid	6.24	75.35	18.41		50.33	49.55	50.00
	2024-25 (upto Feb)	**All India Grid**	**5.12**	**77.94**	**16.93**		**50.67**	**49.46**	**50.00**

5.1 फरवरी 2025 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR FEBRUARY 2025

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Feb-25	4.09	80.10	15.81		50.29	49.82	50.00	0.03
	02-Feb-25	2.28	82.43	15.29		50.26	49.79	50.00	0.03
	03-Feb-25	6.46	76.48	17.06		50.23	49.72	50.00	0.04
	04-Feb-25	5.75	78.08	16.17		50.20	49.78	50.00	0.03
	05-Feb-25	9.57	74.84	15.59		50.21	49.60	49.99	0.05
	06-Feb-25	2.23	67.92	29.85		50.33	49.85	50.02	0.05
	07-Feb-25	6.15	77.06	16.79		50.27	49.75	49.99	0.04
	08-Feb-25	6.76	77.16	16.08		50.22	49.69	49.99	0.04
	09-Feb-25	5.01	79.03	15.96		50.25	49.77	50.00	0.03
	10-Feb-25	8.13	74.04	17.84		50.21	49.70	49.99	0.05
	11-Feb-25	4.50	79.91	15.59		50.24	49.80	49.99	0.03
	12-Feb-25	6.83	77.69	15.49		50.21	49.78	49.99	0.03
	13-Feb-25	4.65	79.03	16.32		50.18	49.74	50.00	0.03
	14-Feb-25	4.04	75.76	20.20		50.29	49.80	50.01	0.04
	15-Feb-25	4.02	77.88	18.10		50.25	49.78	50.01	0.03
	16-Feb-25	7.84	70.58	21.59		50.27	49.77	50.01	0.05
	17-Feb-25	8.02	75.65	16.33		50.22	49.79	49.99	0.04
	18-Feb-25	6.85	72.72	20.43		50.25	49.74	50.00	0.04
	19-Feb-25	12.06	70.71	17.23		50.29	49.55	49.98	0.09
	20-Feb-25	11.94	72.67	15.38		50.30	49.55	49.99	0.06
	21-Feb-25	9.05	72.63	18.32		50.23	49.76	49.99	0.05
	22-Feb-25	8.54	77.36	14.10		50.22	49.76	49.99	0.04
	23-Feb-25	3.84	78.18	17.97		50.21	49.80	50.01	0.03
	24-Feb-25	2.72	75.17	22.11		50.33	49.86	50.01	0.04
	25-Feb-25	7.52	74.21	18.26		50.31	49.69	50.00	0.06
	26-Feb-25	3.26	70.54	26.19		50.29	49.76	50.02	0.05
	27-Feb-25	7.11	64.46	28.44		50.30	49.80	50.01	0.05
	28-Feb-25	5.63	77.44	16.93		50.23	49.67	50.00	0.04


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: फरवरी 2025 MONTH:- FEB 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-25	91	52	85	23	10	261
02-Feb-25	92	44	69	21	10	236
03-Feb-25	93	56	87	22	11	268
04-Feb-25	97	59	86	23	10	275
05-Feb-25	95	63	95	22	10	286
06-Feb-25	90	43	76	21	10	241
07-Feb-25	94	48	79	22	10	253
08-Feb-25	95	55	83	22	11	266
09-Feb-25	96	43	71	19	9	239
10-Feb-25	94	66	84	24	8	276
11-Feb-25	94	63	84	26	10	277
12-Feb-25	94	55	90	26	10	274
13-Feb-25	98	51	91	28	10	278
14-Feb-25	103	54	88	26	10	281
15-Feb-25	101	41	61	23	10	235
16-Feb-25	98	40	70	22	6	236
17-Feb-25	98	53	93	27	9	279
18-Feb-25	97	59	96	25	9	286
19-Feb-25	96	57	100	28	9	290
20-Feb-25	96	40	98	24	8	266
21-Feb-25	90	47	95	26	9	267
22-Feb-25	95	49	95	26	8	273
23-Feb-25	93	40	66	21	8	227
24-Feb-25	92	38	68	23	9	229
25-Feb-25	93	41	74	23	9	239
26-Feb-25	98	39	68	21	8	233
27-Feb-25	105	37	83	23	9	256
28-Feb-25	137	51	91	22	10	310
कुल TOTAL	2713	1381	2325	657	262	7338
उच्चतम MAXIMUM	137	66	100	28	11	310
निम्नतम MINIMUM	90	37	61	19	6	227
औसत AVERAGE	97	49	83	23	9	262
संचयी 2024-25 Cumulative 2024-25	75857	19162	32595	15966	7458	151038
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

HYDRO ENERGY DURING THE MONTH OF FEBRUARY' 2025

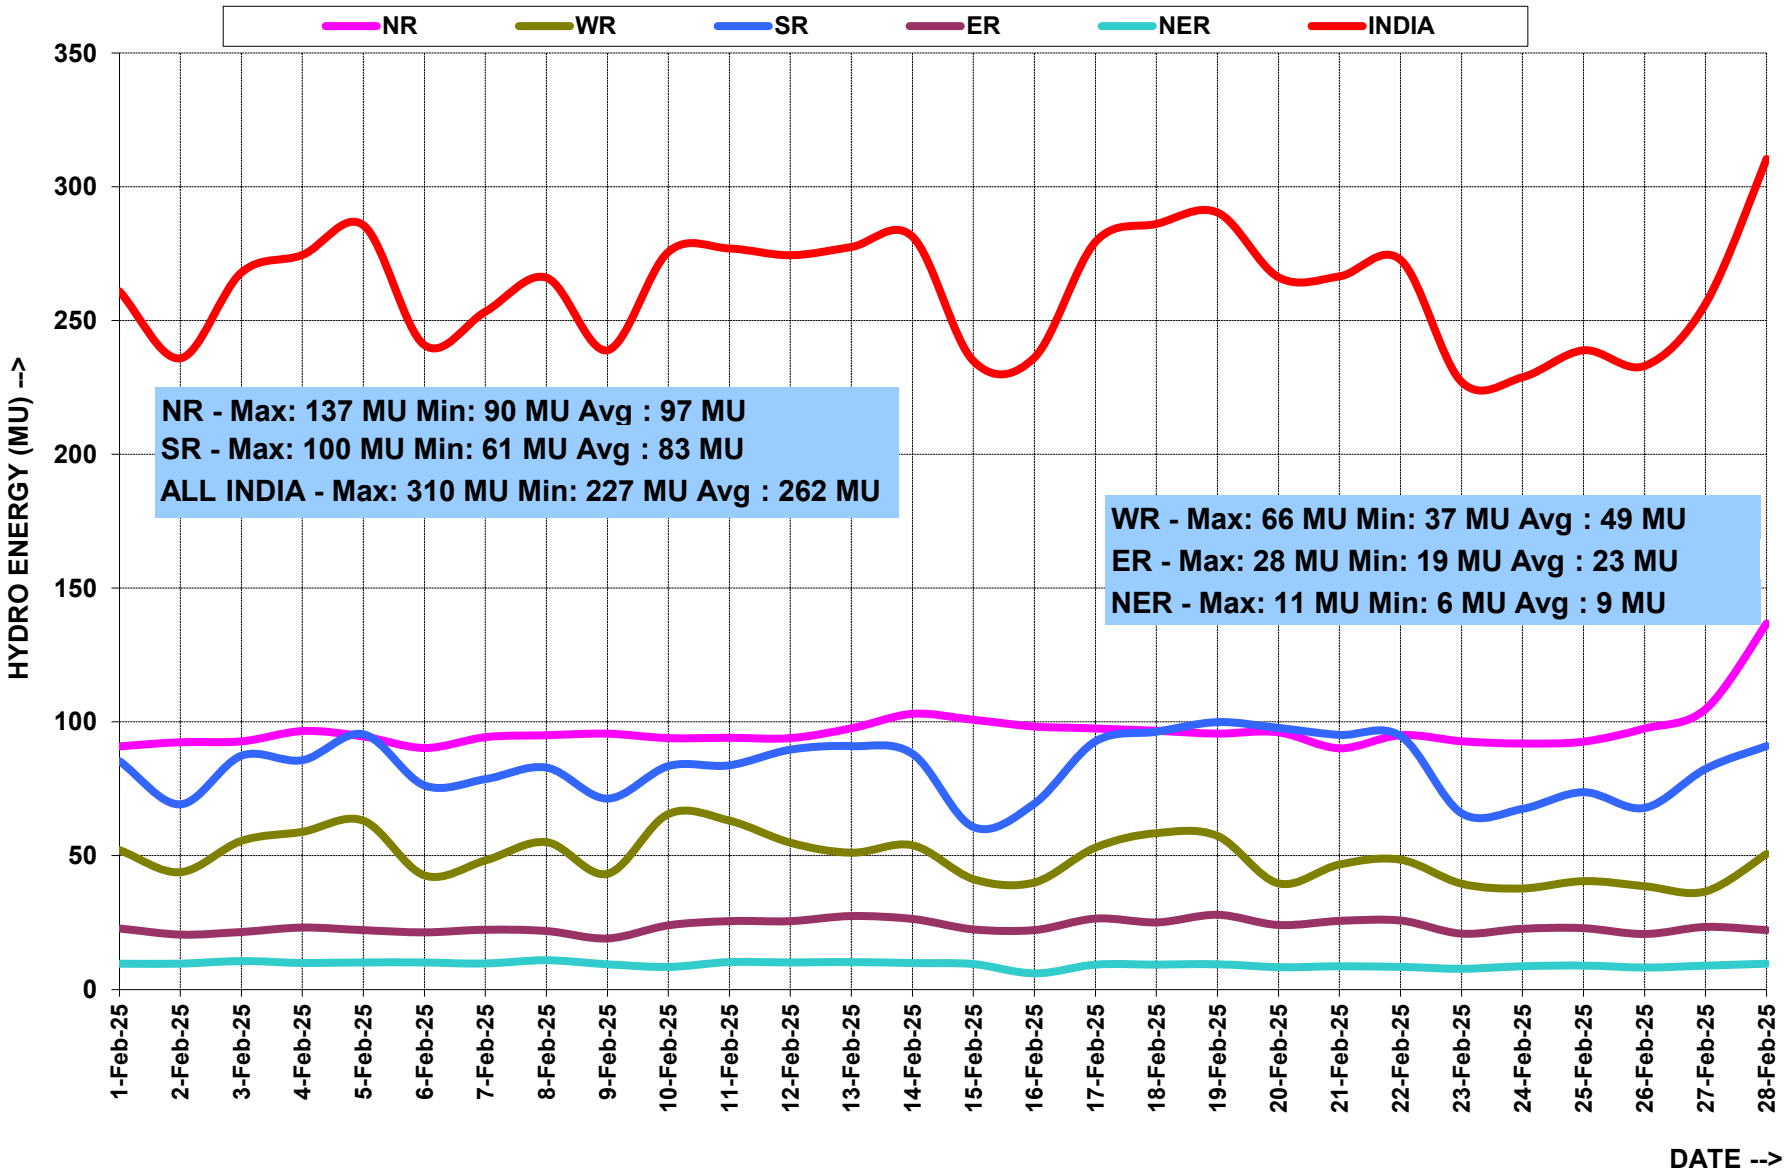

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: फरवरी 2025 MONTH:- FEB 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-25	21	54	39	----------	----------	114
02-Feb-25	31	50	57	----------	----------	138
03-Feb-25	34	39	54	----------	----------	126
04-Feb-25	4	87	58	----------	----------	148
05-Feb-25	4	86	60	----------	----------	150
06-Feb-25	17	173	83	----------	----------	273
07-Feb-25	20	152	80	----------	----------	252
08-Feb-25	14	61	84	----------	----------	159
09-Feb-25	6	23	90	----------	----------	118
10-Feb-25	5	31	63	----------	----------	99
11-Feb-25	12	71	51	----------	----------	134
12-Feb-25	7	65	40	----------	----------	111
13-Feb-25	3	50	36	----------	----------	89
14-Feb-25	7	50	25	----------	----------	81
15-Feb-25	27	113	37	----------	----------	176
16-Feb-25	17	90	51	----------	----------	158
17-Feb-25	11	59	51	----------	----------	121
18-Feb-25	17	67	34	----------	----------	118
19-Feb-25	22	75	29	----------	----------	126
20-Feb-25	12	69	36	----------	----------	116
21-Feb-25	32	47	44	----------	----------	123
22-Feb-25	22	42	31	----------	----------	95
23-Feb-25	11	41	51	----------	----------	103
24-Feb-25	16	54	91	----------	----------	161
25-Feb-25	15	58	102	----------	----------	174
26-Feb-25	20	52	117	----------	----------	188
27-Feb-25	14	57	109	----------	----------	180
28-Feb-25	32	80	90	----------	----------	202
कुल TOTAL	450	1894	1691	----------	----------	4034
उच्चतम MAXIMUM	34	173	117	----------	----------	273
निम्नतम MINIMUM	3	23	25	----------	----------	81
औसत AVERAGE	16	68	60	----------	----------	144
संचयी 2024-25 Cumulative 2024-25	6391	33800	34619	----------	----------	74810
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: फरवरी 2025 MONTH:- FEB 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-25	148	117	140	3.2	0.7	409
02-Feb-25	179	117	148	3.3	0.8	449
03-Feb-25	165	105	150	3.1	0.7	423
04-Feb-25	179	112	153	3.1	1.0	448
05-Feb-25	183	120	144	3.2	0.9	451
06-Feb-25	193	120	143	3.0	0.7	460
07-Feb-25	182	120	149	3.4	0.9	455
08-Feb-25	181	118	144	3.4	1.0	447
09-Feb-25	184	121	139	3.8	1.1	449
10-Feb-25	163	122	138	3.5	0.9	428
11-Feb-25	184	118	146	2.5	0.7	451
12-Feb-25	182	120	145	3.2	0.8	451
13-Feb-25	187	124	151	3.7	1.7	468
14-Feb-25	181	125	153	3.6	0.8	463
15-Feb-25	189	129	153	3.8	1.1	475
16-Feb-25	166	126	155	3.8	0.9	452
17-Feb-25	184	124	154	3.1	1.1	467
18-Feb-25	174	121	148	3.2	0.9	447
19-Feb-25	138	120	144	3.3	1.0	407
20-Feb-25	191	126	141	3.0	1.2	461
21-Feb-25	185	123	142	3.6	1.0	454
22-Feb-25	195	132	142	3.6	1.0	473
23-Feb-25	202	134	144	3.4	0.9	485
24-Feb-25	189	130	148	4.1	1.3	473
25-Feb-25	126	116	136	4.0	1.2	383
26-Feb-25	142	125	140	3.8	1.3	411
27-Feb-25	93	122	146	3.6	1.2	365
28-Feb-25	145	119	133	3.5	1.0	402
कुल TOTAL	4808	3407	4070	96	28	12408
उच्चतम MAXIMUM	202	134	155	4.1	1.7	485
निम्नतम MINIMUM	93	105	133	2.5	0.7	365
औसत AVERAGE	172	122	145	3.4	1.0	443
संचयी 2024-25 Cumulative 2024-25	50730	28939	38517	990	313.2	119489
अब तक का उच्चतम All Time Max.	**202**	**134**	**155**	4.1	3.5	**485**
दिनांक Date	**23.02.25**	**23.02.25**	**16.02.25**	09.06.24	08.09.24	**23.02.25**

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: फरवरी 2025 MONTH:- FEB 2025

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL		विभिन्नता फ़ैक्टर Diversity Factor*
01-Feb-25	65979	79226	63689	23405	2847	232307		1.012
02-Feb-25	64648	76671	60642	22398	2681	224441		1.012
03-Feb-25	66240	78994	63356	23615	2827	231373		1.016
04-Feb-25	65775	78812	64270	24398	2824	232077		1.017
05-Feb-25	67549	77476	65026	24021	2877	233358		1.015
06-Feb-25	67523	78263	64894	23690	2834	234136		1.013
07-Feb-25	69074	78847	66201	23539	2825	238140		1.010
08-Feb-25	67952	80000	64254	23194	2813	234117		1.017
09-Feb-25	65513	78837	61233	22846	2604	228285		1.012
10-Feb-25	67561	79999	64492	23703	2758	234995		1.015
11-Feb-25	66714	79200	65541	23556	2757	234858		1.012
12-Feb-25	69432	78702	65282	23991	2420	236794		1.013
13-Feb-25	66613	78882	66113	23684	2680	234703		1.014
14-Feb-25	66875	79032	65775	23769	2733	234581		1.015
15-Feb-25	66912	78818	65515	23939	2816	233860		1.018
16-Feb-25	65094	76385	61914	23541	2606	225222		1.019
17-Feb-25	66455	78570	65941	23727	2839	234284		1.014
18-Feb-25	67007	79675	65856	24134	2735	236166		1.014
19-Feb-25	66566	79998	66704	23921	2806	236800		1.013
20-Feb-25	58876	78422	67911	23043	2774	227682		1.015
21-Feb-25	62880	78629	68306	23510	2763	232390		1.016
22-Feb-25	61105	78398	67801	23052	2776	229826		1.014
23-Feb-25	59037	75307	63163	22735	2454	218010		1.021
24-Feb-25	63836	78007	65757	23115	2759	229873		1.016
25-Feb-25	62314	78106	68939	23536	2790	231406		1.018
26-Feb-25	65208	77125	68567	23073	2794	233736		1.013
27-Feb-25	58726	79016	66789	23783	2812	227523		1.016
28-Feb-25	60433	79225	68536	24246	2798	231756		1.015
उच्चतम MAXIMUM	69432	80000	68939	24398	2877	238140		1.021
निम्नतम MINIMUM	58726	75307	60642	22398	2420	218010		1.010
औसत AVERAGE	65068	78522	65445	23542	2750	231882		1.015
अब तक का उच्चतम All Time Max.	91215	**80000**	**68939**	32531	3905	250070		
दिनांक Date	19.06.24	**08.02.25**	**25.02.25**	10.06.24	19.09.24	30.05.24		


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 07th FEB (MAXIMUM DEMAND MET)

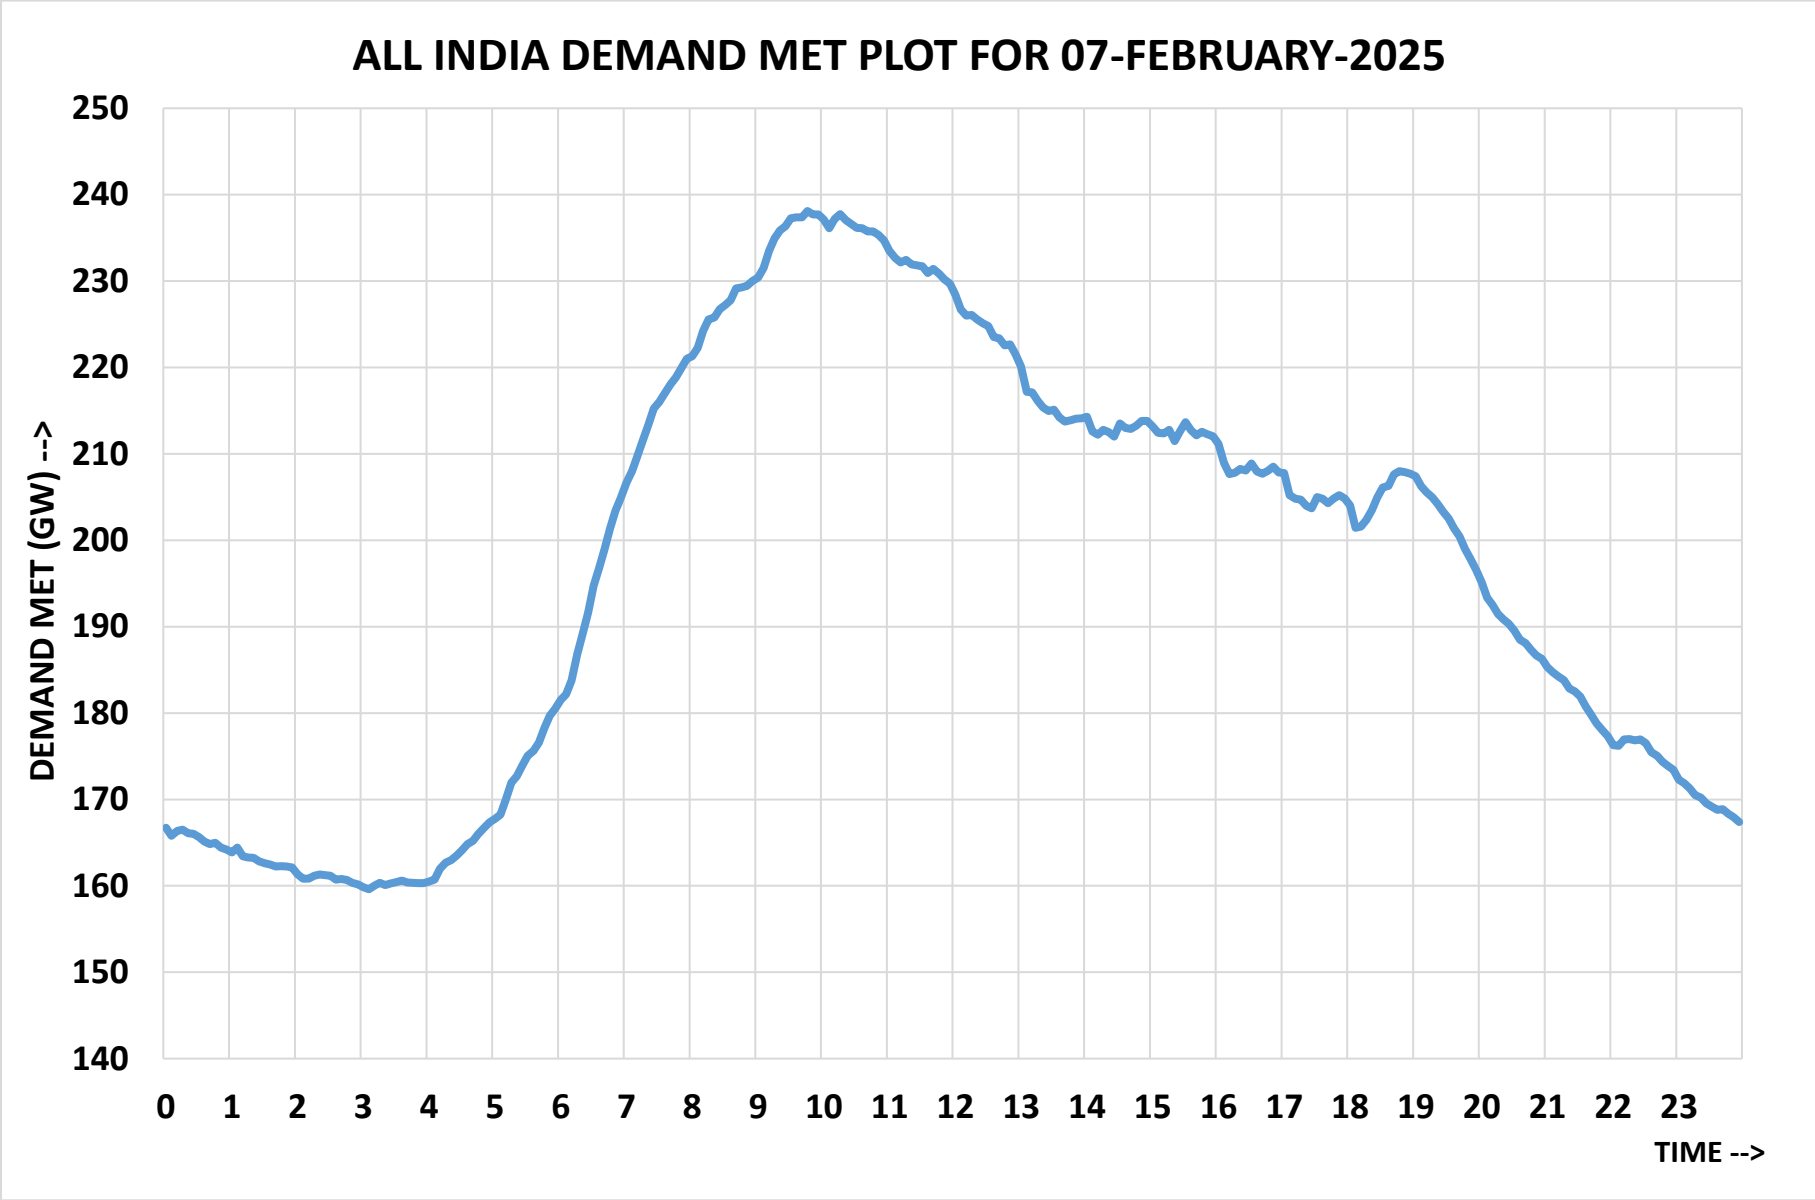

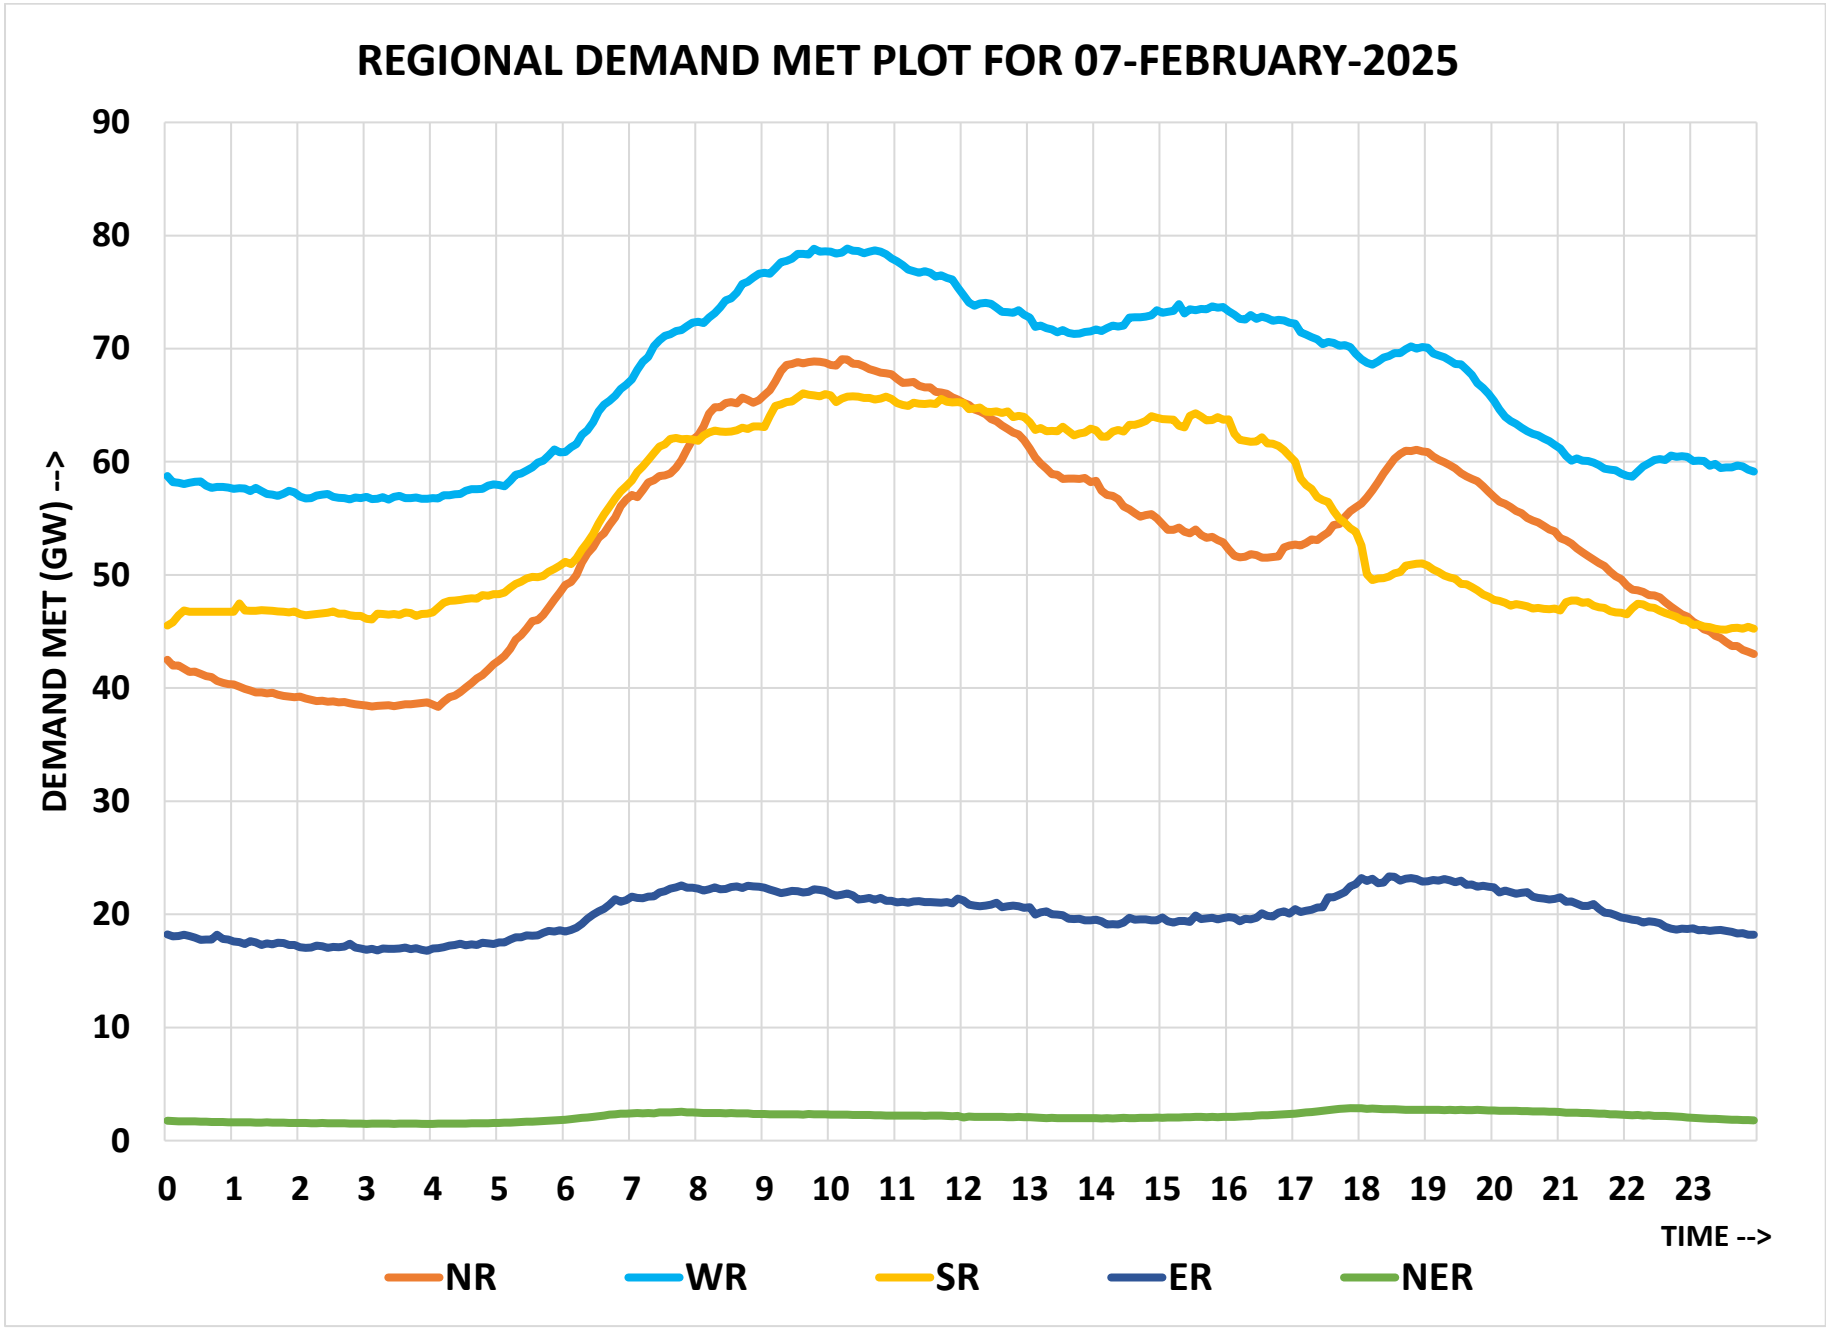
REGIONAL DEMAND MET PLOT FOR 07-FEBRUARY-2025
DEMAND MET (GW) -->
90
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

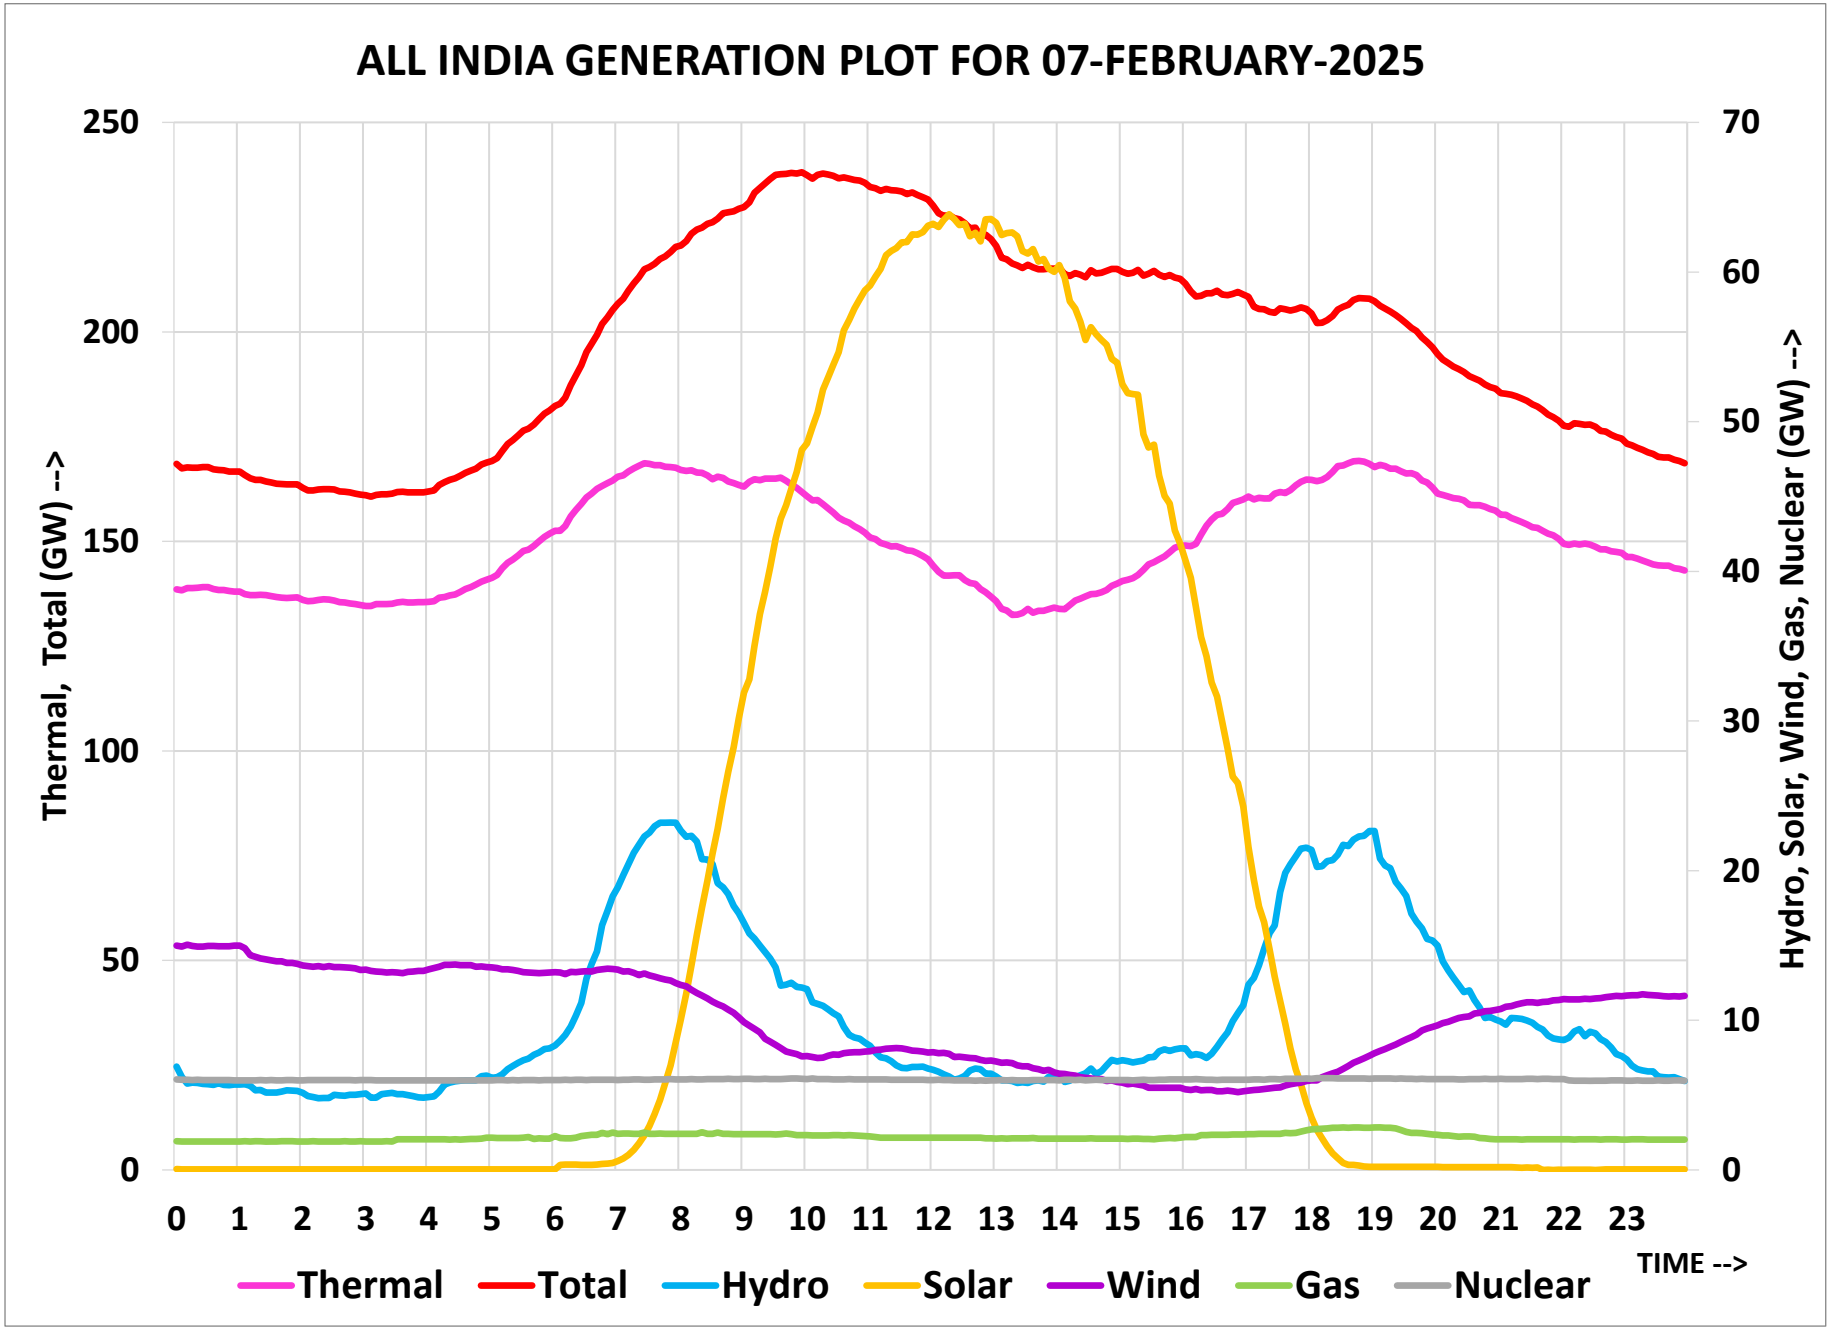
ALL INDIA GENERATION PLOT FOR 07-FEBRUARY-2025
Thermal, Total (GW) -->
Hydro, Solar, Wind, Gas, Nuclear (GW) -->
250
200
150
100
50
0
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Thermal
Total
Hydro
Solar
Wind
Gas
Nuclear

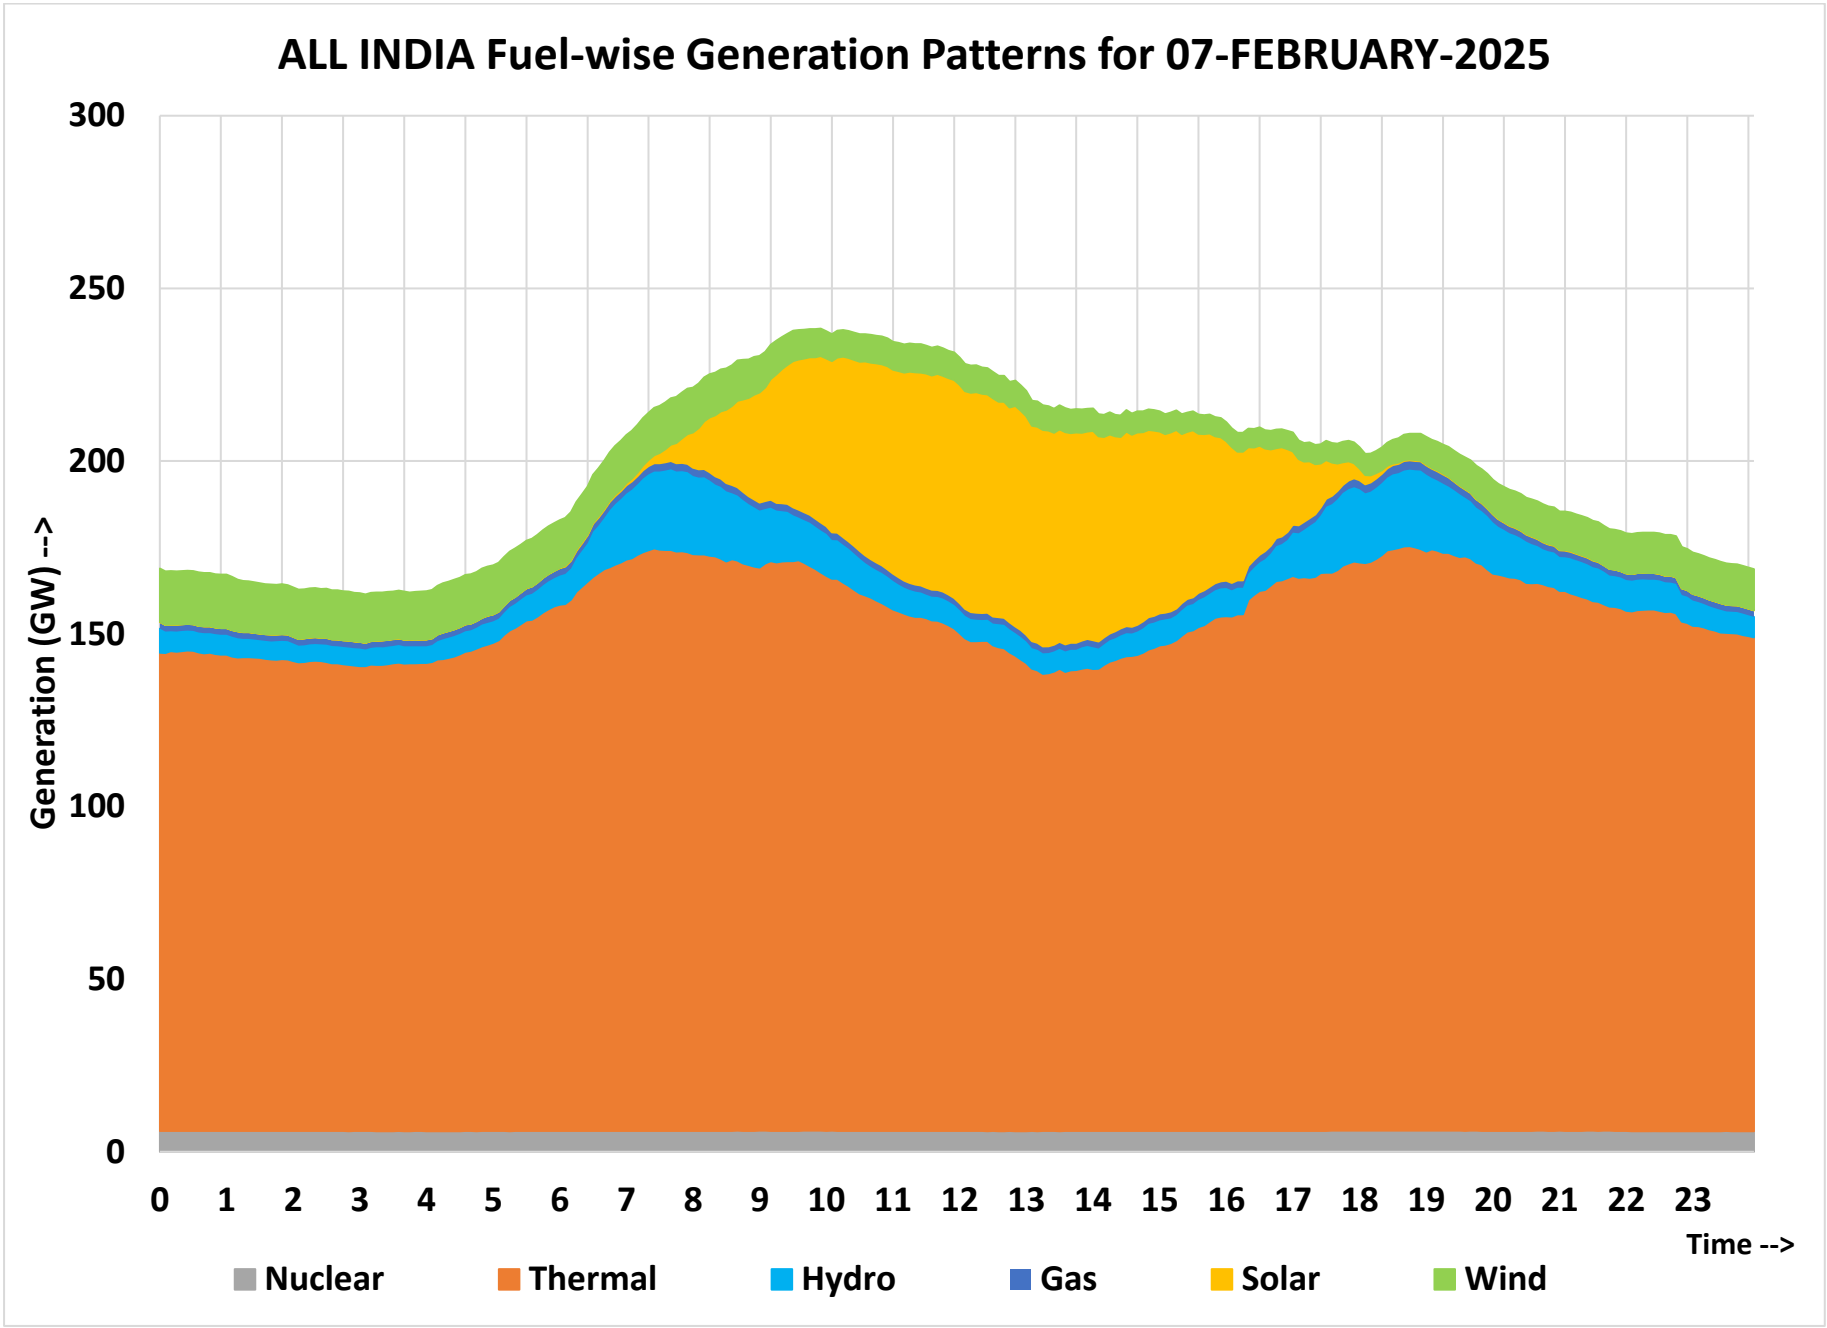
ALL INDIA Fuel-wise Generation Patterns for 07-FEBRUARY-2025
Generation (GW) -->
300
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
Time -->
Nuclear
Thermal
Hydro
Gas
Solar
Wind

07 फ़रवरी 2025 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 07 FEBRUARY 2025 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	165788		**12:05**	226707
00:20	166105		**12:20**	225543
00:35	165123		**12:35**	223505
00:50	164425		**12:50**	222659
01:05	164438		**13:05**	217166
01:20	163252		**13:20**	215366
01:35	162447		**13:35**	214215
01:50	162232		**13:50**	214066
02:05	160844		**14:05**	212589
02:20	161311		**14:20**	212528
02:35	160732		**14:35**	213012
02:50	160357		**14:50**	213822
03:05	159607		**15:05**	212426
03:20	160090		**15:20**	211462
03:35	160612		**15:35**	212737
03:50	160317		**15:50**	212258
04:05	160724		**16:05**	208963
04:20	162994		**16:20**	208271
04:35	164825		**16:35**	207948
04:50	166672		**16:50**	208522
05:05	168232		**17:05**	205211
05:20	172688		**17:20**	203986
05:35	175602		**17:35**	204806
05:50	179674		**17:50**	205207
06:05	182170		**18:05**	201445
06:20	189199		**18:20**	203481
06:35	196761		**18:35**	206292
06:50	203400		**18:50**	207886
07:05	207987		**19:05**	206240
07:20	213359		**19:20**	204172
07:35	217014		**19:35**	201372
07:50	219934		**19:50**	197846
08:05	222260		**20:05**	193366
08:20	225789		**20:20**	190840
08:35	227781		**20:35**	188473
08:50	229458		**20:50**	186666
09:05	231538		**21:05**	184728
09:20	235847		**21:20**	182823
09:35	237377		**21:35**	180771
09:50	237700		**21:50**	178042
10:05	236133		**22:05**	176212
10:20	237039		**22:20**	176841
10:35	236119		**22:35**	175451
10:50	235346		**22:50**	173857
11:05	232677		**23:05**	171883
11:20	231928		**23:20**	170211
11:35	230914		**23:35**	168811
11:50	230194		**23:50**	167927
Maximum Demand of 238140 MW met@09:42 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - FEBRUARY 2025

REGION	STATE	Energy Requirement & Met (MU/Day)			Energy Requirement & Met (MU)				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	108	108	0	0.0	265	265	0	0.0
	Delhi	73	73	0.0	2041	2041	0	0.0	4657	4657	0	0.0
	Haryana	157	157	0.0	4395	4395	0	0.0	9602	9602	0	0.0
	Himachal Pradesh	38	38	0.0	1051	1051	0	0.0	2193	2193	0	0.0
	J&K(UT) and Ladakh(UT)	62	62	-0.1	1730	1728	-2	-0.1	3057	3057	0	0.0
	Punjab	154	154	0.0	4324	4324	0	0.0	10165	10165	0	0.0
	Rajasthan	345	345	0.0	9649	9649	0	0.0	19165	19165	0	0.0
	Uttar Pradesh	347	347	0.0	9715	9714	-1	0.0	20456	20456	0	0.0
	Uttarakhand	43	43	0.0	1195	1195	0	0.0	2477	2477	0	0.0
	Railway_NR ISTS	4	4	0.0	103	103	0	0.0	228	228	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	11	11	0	0.0
	TOTAL	1225	1225	-0.1	34313	34310	-3	0.0	68573	68573	0	0.0
WR	Gujarat	438	438	0.0	12274	12274	0	0.0	23780	23780	0	0.0
	Madhya Pradesh	347	346	-0.5	9713	9700	-13	-0.1	18596	18596	0	0.0
	Chhattisgarh	132	132	-0.3	3709	3701	-9	-0.2	6181	6172	-9	-0.1
	Maharashtra	628	628	0.0	17596	17596	0	0.0	30151	30151	0	0.0
	Goa	15	15	0.0	424	424	0	0.0	766	765	-2	-0.2
	DNHDDPDCL	30	30	0.0	848	848	0	0.0	1356	1356	0	0.0
	AMNSIL	17	17	0.0	490	490	0	0.0	844	844	0	0.0
	BALCO	13	13	0.0	356	356	0	0.0	536	536	0	0.0
	RIL JAMNAGAR*	4	4	0.0	126	126	0	0.0	197	197	0	0.0
	TOTAL	1626	1625	-0.8	45535	45513	-22	0.0	80861	80523	-338	-0.4
SR	Andhra Pradesh	237	235	-1.7	6626	6579	-47	-0.7	12726	12726	0	0.0
	Telangana	306	304	-1.9	8559	8507	-52	-0.6	16601	16601	0	0.0
	Karnataka	321	319	-2.1	9002	8944	-58	-0.6	18350	18350	0	0.0
	Kerala	91	90	-0.7	2538	2519	-18	-0.7	5015	5015	0	0.0
	Tamil Nadu	366	363	-2.5	10242	10171	-70	-0.7	18584	18584	0	0.0
	Puducherry	9	9	-0.1	255	253	-2	-0.8	443	443	0	0.0
	TOTAL	1329	1320	-8.8	37221	36974	-247	-0.7	64940	64845	-95	-0.1
ER	Bihar	96	96	-0.1	2695	2693	-2	-0.1	5386	5386	0	0.0
	Jharkhand	39	39	-0.1	1089	1087	-2	-0.2	2143	2143	0	0.0
	DVC	69	69	0.0	1939	1939	0	0.0	3406	3406	0	0.0
	Odisha	108	108	0.0	3023	3023	0	0.0	5787	5787	0	0.0
	West Bengal	163	163	0.0	4576	4576	0	0.0	8337	8337	0	0.0
	Sikkim	2	2	0.0	57	57	0	0.0	134	134	0	0.0
	Railways_ER ISTS	0	0	0.0	6	6	0	0.0	28	28	0	0.0
	TOTAL	478	478	-0.1	13384	13381	-4	0.0	24235	24235	0	0.0
NER	Arunachal Pradesh	3	3	0.0	94	94	0	0.0	218	191	-27	-12.3
	Assam	28	28	0.0	795	795	0	0.0	1647	1627	-20	-1.2
	Manipur	3	3	-0.2	93	89	-4	-4.6	248	248	0	0.0
	Meghalaya	6	6	0.0	155	155	0	0.0	352	352	0	0.0
	Mizoram	2	2	0.0	60	60	0	0.0	160	160	0	0.0
	Nagaland	2	2	0.0	70	70	0	0.0	173	173	0	0.0
	Tripura	4	4	0.0	124	124	0	0.0	252	252	0	0.0
	TOTAL	50	50	-0.2	1392	1388	-4	-0.3	2890	2890	0	0.0
ALL INDIA		4709	4699	-10.0	131845	131566	-279	-0.2				

* RIL Jamnagar has been added as new entity wef 01.12.2024

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF FEBRUARY 2025 vs FEBRUARY 2024

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Feb-24	Feb-25	Difference	% Change	Average MU/day for Oct-24	Feb-24	Feb-25	Difference	% Change	Average MU/day for Oct-24
NR	Chandigarh	116	108	-8	-7	4	116	108	-8	-7	4
	Delhi	2176	2041	-134	-6	73	2176	2041	-134	-6	73
	Haryana	4273	4395	122	3	157	4255	4395	140	3	157
	Himachal Pradesh	1035	1051	16	2	38	1031	1051	20	2	38
	J&K(UT) and Ladakh(UT)	1703	1730	27	2	62	1672	1728	55	3	62
	Punjab	4518	4324	-194	-4	154	4518	4324	-194	-4	154
	Rajasthan	9161	9649	488	5	345	9157	9649	492	5	345
	Uttar Pradesh	9292	9715	423	5	347	9291	9714	423	5	347
	Uttarakhand	1236	1195	-41	-3	43	1231	1195	-36	-3	43
	Railway_NR ISTS/NFL	106	105	-1	-1	4	106	105	-1	-1	4
	TOTAL	33616	34313	697	2	1225	33554	34310	757	2	1225
WR	Gujarat	11786	12274	488	4	438	11786	12274	488	4	438
	Madhya Pradesh	8635	9713	1078	12	347	8591	9700	1109	13	346
	Chhattisgarh	3457	3709	253	7	132	3453	3701	248	7	132
	Maharashtra	17182	17596	414	2	628	17182	17596	414	2	628
	Goa	378	424	46	12	15	378	424	46	12	15
	DNHDDPDCL	843	848	5	1	30	843	848	5	1	30
	AMNSIL	547	490	-57	-10	17	547	490	-57	-10	17
	BALCO	361	356	-5	-1	13	361	356	-5	-1	13
	RIL JAMNAGAR*	-	126	-	-	-	-	126	-	-	-
	TOTAL	43189	45535	2346	5	1626	43141	45513	2372	5	1625
SR	Andhra Pradesh	6658	6626	-32	0	237	6658	6579	-79	-1	235
	Telangana	7957	8559	602	8	306	7968	8507	539	7	304
	Karnataka	8812	9002	190	2	321	8823	8944	121	1	319
	Kerala	2583	2538	-46	-2	91	2587	2519	-68	-3	90
	Tamil Nadu	10404	10242	-163	-2	366	10419	10171	-247	-2	363
	Puducherry	269	255	-14	-5	9	269	253	-16	-6	9
	TOTAL	36683	37221	538	1	1329	36723	36974	251	1	1320
ER	Bihar	2575	2695	120	5	96	2566	2693	127	5	96
	Jharkhand	1051	1089	38	4	39	1008	1087	79	8	39
	DVC	2052	1939	-113	-6	69	2052	1939	-113	-6	69
	Odisha	3029	3023	-6	0	108	3029	3023	-6	0	108
	West Bengal	4374	4576	202	5	163	4374	4576	202	5	163
	Sikkim	57	57	0	0	2	57	57	0	0	2
	Railways_ER ISTS	4	6	2	42	0	4	6	2	42	0
	TOTAL	13142	13384	242	2	478	13090	13381	290	2	478
NER	Arunachal Pradesh	89	94	5	6	3	89	94	5	6	3
	Assam	817	795	-22	-3	28	804	795	-9	-1	28
	Manipur	91	93	2	3	3	86	89	3	3	3
	Meghalaya	188	155	-33	-17	6	188	155	-33	-17	6
	Mizoram	64	60	-4	-6	2	64	60	-4	-6	2
	Nagaland	69	70	1	1	2	69	70	1	1	2
	Tripura	109	124	14	13	4	109	124	14	13	4
	TOTAL	1428	1392	-36	-2	50	1410	1388	-23	-2	50
ALL INDIA		128058	131845	3787	3	4709	127919	131566	3647	3	4699

* RIL Jamnagar has been added as new entity wef 01.12.2024

13. DEMAND COMPARISON OF FEBRUARY 2025 vs FEBRUARY 2024

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Feb-24	Feb-25	Difference	% Change	Feb-24	Feb-25	Difference	% Change
NR	Chandigarh	304	265	-39	-12.8	304	265	-39	-12.8
	Delhi	5406	4657	-749	-13.9	5406	4657	-749	-13.9
	Haryana	8868	9602	734	8.3	8868	9602	734	8.3
	Himachal Pradesh	2133	2193	60	2.8	2133	2193	60	2.8
	J&K(UT) and Ladakh(UT)	3071	3057	-14	-0.5	3071	3057	-14	-0.5
	Punjab	10307	10165	-142	-1.4	10307	10165	-142	-1.4
	Rajasthan	17867	19165	1298	7.3	17867	19165	1298	7.3
	Uttar Pradesh	20346	20456	110	0.5	19726	20456	730	3.7
	Uttarakhand	2523	2477	-46	-1.8	2328	2477	149	6.4
	Railway_NR ISTS/NFL	205	240	35	16.9	205	240	35	16.9
WR	Gujarat	21248	23780	2532	12	21248	23780	2532	11.9
	Madhya Pradesh	16998	18596	1598	9	16992	18596	1604	9.4
	Chhattisgarh	5819	6181	362	6	5813	6172	359	6.2
	Maharashtra	28969	30151	1182	4	28969	30151	1182	4.1
	Goa	749	766	17	2	749	765	16	2.1
	DNHDDPDCL	1304	1356	52	4.0	1304	1356	52	4.0
	AMNSIL	926	844	-82	-8.9	926	844	-82	-8.9
	BALCO	525	536	11	2.2	525	536	11	2.2
	RIL JAMNAGAR*	-	197	-	-	-	197	-	-
SR	Andhra Pradesh	12216	12726	510	4.2	12216	12726	510	4.2
	Telangana	13829	16601	2772	20.0	13810	16601	2791	20.2
	Karnataka	16632	18350	1717	10.3	16632	18350	1717	10.3
	Kerala	4841	5015	174	3.6	4841	5015	174	3.6
	Tamil Nadu	17045	18584	1539	9.0	17035	18584	1549	9.1
	Puducherry	453	443	-10	-2.2	453	443	-10	-2.2
ER	Bihar	5190	5386	196	3.8	5190	5386	196	3.8
	Jharkhand	1756	2143	387	22.0	1756	2143	387	22.0
	DVC	3291	3406	115	3.5	3291	3406	115	3.5
	Odisha	5421	5787	366	6.8	5421	5787	366	6.8
	West Bengal	7522	8337	815	10.8	7522	8337	815	10.8
	Sikkim	128	134	6	4.7	128	134	6	4.7
	Railways_ER ISTS	23	28	5	21.7	23	28	5	21.7
NER	Arunachal Pradesh	186	218	32	17.2	186	191	5	2.8
	Assam	1634	1647	13	0.8	1634	1627	-7	-0.4
	Manipur	252	248	-4	-1.6	235	248	13	5.5
	Meghalaya	399	352	-47	-11.8	399	352	-47	-11.8
	Mizoram	155	160	5	3.2	155	160	5	3.2
	Nagaland	156	173	17	10.9	156	173	17	10.9
	Tripura	261	252	-9	-3.4	261	252	-9	-3.4

* RIL Jamnagar has been added as new entity wef 01.12.2024

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - FEBRUARY 2025

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	108.94	107.83	-1.11	-1.02	3.89	3.85	-0.04
	Delhi	1791.78	1767.85	-23.93	-1.34	63.99	63.14	-0.85
	Haryana	2849.23	2807.11	-42.12	-1.48	101.76	100.25	-1.50
	Himachal Pradesh	884.63	865.29	-19.34	-2.19	31.59	30.90	-0.69
	J&K(UT) and Ladakh(UT)	1670.17	1624.65	-45.52	-2.73	59.65	58.02	-1.63
	Punjab	1853.11	1835.04	-18.07	-0.98	66.18	65.54	-0.65
	Rajasthan	3201.94	3132.29	-69.65	-2.18	114.36	111.87	-2.49
	Uttar Pradesh	2625.17	2608.43	-16.74	-0.64	93.76	93.16	-0.60
	Uttarakhand	922.77	919.69	-3.08	-0.33	32.96	32.85	-0.11
	Railways_NR ISTS	108.91	114.30	5.39	4.95	3.89	4.08	0.19
	NFL	2.63	2.48	-0.16	-5.91	0.09	0.09	-0.01
	Total	16019.29	15784.96	-234.32	-1.46	572.12	563.75	-8.37
WR	Gujarat	5347.20	5269.10	-78.10	-1.46	190.97	188.18	-2.79
	Madhya Pradesh	6200.50	6107.70	-92.80	-1.50	221.45	218.13	-3.31
	Chhattisgarh	2004.60	2013.90	9.30	0.46	71.59	71.93	0.33
	Maharashtra	6396.00	6346.40	-49.60	-0.78	228.43	226.66	-1.77
	Goa	400.20	415.20	15.00	3.75	14.29	14.83	0.54
	DNHDDPDCL	850.70	847.80	-2.90	-0.34	30.38	30.28	-0.10
	AMNSIL	251.20	256.60	5.40	2.15	8.97	9.16	0.19
	BALCO	355.60	356.10	0.50	0.14	12.70	12.72	0.02
	RIL JAMNAGAR*	128.00	125.90	-2.10	-1.64	4.57	4.50	-0.08
	Total	21934.00	21738.70	-195.30	-0.89	783.36	776.38	-6.98
SR	Andhra Pradesh	1709.11	1705.70	-3.41	-0.20	61.04	60.92	-0.12
	Telangana	4898.14	4882.36	-15.78	-0.32	174.93	174.37	-0.56
	Karnataka	3358.50	3348.68	-9.82	-0.29	119.95	119.60	-0.35
	Kerala	1973.05	1997.63	24.58	1.25	70.47	71.34	0.88
	Tamil Nadu	5900.71	5873.32	-27.39	-0.46	210.74	209.76	-0.98
	Puducherry	244.14	239.45	-4.69	-1.92	8.72	8.55	-0.17
	Goa (SR)	62.65	61.84	-0.81	-1.29	2.24	2.21	-0.03
	Total	18146.30	18108.98	-37.32	-0.21	648.08	646.75	-1.33
ER	Bihar	2453.31	2379.01	-74.30	-3.03	87.62	84.96	-2.65
	Jharkhand	777.59	768.38	-9.21	-1.18	27.77	27.44	-0.33
	DVC	-1220.62	-1228.08	-7.46	0.61	-43.59	-43.86	-0.27
	Odisha	959.41	930.10	-29.31	-3.05	34.26	33.22	-1.05
	West Bengal	883.07	827.43	-55.64	-6.30	31.54	29.55	-1.99
	Sikkim	56.87	56.85	-0.02	-0.03	2.03	2.03	0.00
	Railways_ER ISTS	5.95	5.87	-0.08	-1.32	0.21	0.21	0.00
	Total	3915.58	3739.56	-176.02	-4.50	139.84	133.56	-6.29
NER	Arunachal Pradesh	94.45	91.34	-3.11	-3.29	3.37	3.26	-0.11
	Assam	618.98	629.72	10.74	1.74	22.11	22.49	0.38
	Manipur	88.40	88.95	0.55	0.62	3.16	3.18	0.02
	Meghalaya	128.15	123.34	-4.81	-3.75	4.58	4.41	-0.17
	Mizoram	52.52	47.69	-4.83	-9.20	1.88	1.70	-0.17
	Nagaland	69.53	68.11	-1.42	-2.04	2.48	2.43	-0.05
	Tripura	103.52	101.34	-2.18	-2.11	3.70	3.62	-0.08
	Total	1155.55	1150.49	-5.06	-0.44	41.27	41.09	-0.18
All India Total		61170.72	60522.69	-648.03	-1.06	2184.67	2161.52	-23.14

* RIL Jamnagar has been added as new entity wef 01.12.2024

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Fin. Year 2024-25
Name of Line												
Import of NR from WR (WR-NR)												
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	714.49	611.32	751.39	877.91	330.17	**9887.73**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	840.34	817.51	665.18	664.69	514.09	**6245.50**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	1009.96	819.22	774.41	896.18	415.21	**9869.28**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	583.07	599.61	586.45	592.74	485.93	**6501.79**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	1570.74	720.37	1288.63	1766.28	1731.95	**20566.56**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	0.00	39.19	106.05	66.90	41.66	**870.04**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	0.00	0.00	3.10	6.27	0.00	**237.84**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	17.54	0.00	1.08	0.00	0.00	**64.64**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	60.41	0.08	2.44	3.06	0.44	**600.32**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	60.83	64.26	52.46	55.29	62.04	**659.68**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	58.67	96.18	95.67	89.99	88.29	**789.66**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	0.00	0.00	0.00	0.00	0.00	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	1096.69	827.50	752.53	932.98	840.99	**10862.65**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	0.00	0.00	74.13	63.08	8.74	**1637.73**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	1113.89	1038.27	1036.90	1223.28	522.72	**15959.89**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	89.57	0.00	0.00	2.06	0.00	**652.65**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**7216.20**	**5633.51**	**6190.42**	**7240.71**	**5042.23**	**85422.18**
Export of NR to WR (NR-WR)												
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.80	**1.80**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	0.00	0.00	0.00	0.00	0.00	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	368.54	423.95	433.38	445.77	406.98	**3777.39**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	152.00	95.38	6.70	29.25	68.61	**842.79**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	126.24	173.03	73.94	111.69	140.03	**1089.62**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	31.75	9.91	2.04	0.00	5.00	**108.36**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	1.94	45.97	66.66	68.78	132.39	**540.46**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	51.59	74.53	67.31	56.48	93.53	**507.44**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	0.00	561.44	663.38	663.39	347.14	**5143.50**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	391.69	523.07	148.17	268.25	434.86	**2927.53**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	0.00	51.46	94.50	73.95	145.46	**560.71**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**1123.75**	**1958.74**	**1556.08**	**1717.56**	**1775.80**	**15514.59**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Fin. Year 2024-25
Name of Line												
Import of NR from ER (ER-NR)												
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	139.89	211.26	229.72	252.28	274.76	**1770.06**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	405.62	482.45	443.73	383.69	452.05	**2821.39**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	366.56	351.78	368.50	379.86	251.30	**3510.62**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	250.72	211.75	12.40	0.00	0.00	**1669.22**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	527.53	418.43	523.23	391.61	388.63	**3873.21**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	319.38	212.80	260.15	218.85	112.60	**2455.68**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	95.04	41.13	143.70	118.35	39.80	**543.11**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	259.86	222.85	283.52	223.81	170.64	**2136.25**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	0.00	0.94	0.00	0.00	0.00	**11.61**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	136.66	108.64	109.12	58.92	31.09	**701.93**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	65.13	77.91	68.47	15.73	7.64	**318.66**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	7.45	17.59	22.02	55.47	22.24	**251.65**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	0.53	0.00	0.48	0.00	1.46	**16.04**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	159.57	132.81	163.60	118.51	119.31	**1114.63**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	144.05	156.95	159.21	103.16	157.12	**1067.29**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**2877.99**	**2647.29**	**2787.85**	**2320.24**	**2028.64**	**22262.96**
Import of NR from NER (NER-NR)												
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55	555.71	550.01	30.48	0.00	0.00	**2232.99**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**555.71**	**550.01**	**30.48**	**0.00**	**0.00**	2232.99
Export of NR to ER (NR-ER)												
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	0.00	0.00	0.00	0.00	0.00	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	0.00	0.00	0.00	0.00	0.00	**225.17**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	7.00	8.26	0.00	0.00	1.66	**410.71**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	0.00	0.88	0.00	0.00	0.00	**19.94**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	0.00	0.20	0.00	0.00	0.00	**7.33**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	0.00	0.00	0.00	3.47	3.10	**51.31**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	4.74	0.65	0.00	0.00	0.38	**9.43**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	0.48	0.00	0.60	0.00	0.00	**3.86**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	0.58	0.91	1.34	1.87	1.64	**10.61**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	14.57	14.82	16.20	17.43	15.46	**177.84**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	0.00	0.00	0.00	0.00	0.00	**6.54**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**27.37**	**25.72**	**18.14**	**22.77**	**22.24**	1066.47
Export of NR to NER (NER-NR)												
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	0.00	0.00	445.16	486.19	441.54	**2738.42**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**0.00**	**0.00**	**445.16**	**486.19**	**441.54**	2738.42

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Fin. Year 2024-25
Name of Line												
Export of WR to ER (WR-ER)												
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	308.09	84.78	53.41	160.01	16.05	**5564.26**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	65.67	50.80	64.41	152.97	272.20	**2332.21**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	0.04	0.00	0.00	0.00	0.00	**37.15**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	29.14	9.49	3.76	24.77	1.72	**1122.75**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	0.51	1.58	0.03	0.03	0.00	**651.81**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	4.23	14.85	12.46	29.24	14.43	**130.62**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	0.05	0.60	0.00	0.01	0.12	**15.73**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**407.73**	**162.10**	**134.08**	**367.02**	**304.52**	**9854.54**
Import of WR from ER (ER - WR)												
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	68.03	111.05	218.28	108.43	361.11	**977.55**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	334.28	233.51	328.11	139.52	88.44	**2857.76**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	325.55	520.92	389.23	539.53	582.66	**3771.14**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	59.96	84.87	42.89	57.42	116.14	**424.79**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	380.72	297.88	324.60	320.44	384.61	**2967.53**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	48.12	15.83	17.45	7.12	10.91	**278.98**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	60.23	34.62	45.32	42.62	35.98	**433.09**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**1276.89**	**1298.67**	**1365.88**	**1215.08**	**1579.84**	**11710.85**
Export of ER to NER (ER - NER)												
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	104.89	226.52	18.80	7.46	4.51	**829.04**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	173.82	295.36	19.99	7.41	2.13	**1219.49**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	32.38	44.04	2.57	0.68	0.02	**239.55**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**311.10**	**565.92**	**41.35**	**15.55**	**6.66**	**2288.08**
Import of ER from NER (NER - ER)												
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	18.09	0.00	87.66	87.40	75.85	**721.78**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	17.26	0.00	183.94	165.91	148.37	**1229.03**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	2.72	0.00	38.42	37.89	41.90	**237.62**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**38.07**	**0.00**	**310.02**	**291.19**	**266.13**	**2188.43**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Fin. Year 2024-25
Name of Line												
Export of ER to SR (ER - SR)												
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	217.59	323.46	231.29	195.73	252.18	**2460.06**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	1105.23	1090.58	1197.54	997.29	1098.40	**11004.50**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	1297.13	1542.96	1693.06	1529.00	1505.81	**14806.91**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**2619.95**	**2957.00**	**3121.89**	**2722.02**	**2856.39**	**28271.47**
Import of ER from SR (SR - ER)												
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	0.00	0.00	0.00	0.00	0.00	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	0.00	0.00	0.00	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**490.93**
Export of WR to SR (WR-SR)												
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	231.23	335.29	602.14	331.42	580.23	**3296.19**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	37.08	143.60	280.25	211.67	311.16	**2305.02**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	590.95	779.18	1057.49	959.23	1151.75	**9336.68**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	**0.03**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	574.81	746.92	1396.79	1175.06	1806.06	**12016.42**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	72.89	67.59	70.47	68.17	63.41	**732.45**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	0.03	2.33	0.06	6.57	2.36	**158.57**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	686.47	951.98	1160.41	1022.37	1258.67	**10156.15**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**2193.47**	**3026.89**	**4567.60**	**3774.49**	**5173.64**	**38001.51**
Import of WR from SR (SR - WR)												
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	18.75	0.00	0.00	20.04	0.00	**1655.07**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	410.23	148.25	152.27	240.55	125.15	**3881.67**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	11.46	0.85	0.04	3.92	0.74	**163.25**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	948.20	690.35	704.16	814.52	647.43	**9043.57**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	0.00	0.00	0.00	0.00	0.00	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	0.02	0.01	0.01	0.02	0.02	**0.11**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	6.77	0.01	0.06	1.54	0.04	**167.02**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**1395.43**	**839.47**	**856.54**	**1080.59**	**773.38**	**15329.36**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**20044**	**19665**	**21426**	**21253**	**20271**	**237373**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during February 2025

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Feb-25	14.67	18.83	18.27	16.79	0.00	70.34	2.43	0.00		0.00	2.11	3.24	0.00	0.00	36.24	0.00	24.34	0.00	**207.26**
2-Feb-25	13.61	15.89	15.99	16.51	0.00	57.30	2.43	0.00		0.00	2.07	3.22	0.00	0.00	24.94	0.00	28.28	0.00	**180.24**
3-Feb-25	16.45	21.02	20.28	17.62	0.00	45.88	2.42	0.00		0.00	2.04	3.10	0.00	0.00	23.72	0.00	24.95	0.00	**177.48**
4-Feb-25	11.15	13.57	12.68	16.88	0.00	69.40	2.41	0.00		0.00	2.04	3.11	0.00	0.00	24.19	0.00	17.63	0.00	**173.06**
5-Feb-25	6.60	10.55	11.01	12.39	0.00	70.95	2.41	0.00		0.00	2.00	3.11	0.00	0.00	24.18	0.00	1.75	0.00	**144.95**
6-Feb-25	13.69	10.11	11.00	16.19	0.00	57.20	2.40	0.00		0.00	2.09	3.16	0.00	0.00	28.32	5.20	22.53	0.00	**171.89**
7-Feb-25	20.23	13.76	18.14	19.11	0.00	61.92	2.42	0.00		0.00	2.09	3.29	0.00	0.00	31.98	3.54	31.07	0.00	**207.55**
8-Feb-25	17.63	18.02	16.99	19.41	0.00	71.57	2.44	0.00		0.00	2.10	3.21	0.00	0.00	18.78	0.00	29.43	0.00	**199.58**
9-Feb-25	8.35	17.14	12.58	16.21	0.00	94.70	2.42	0.00		0.00	2.10	3.26	0.00	0.00	30.10	0.00	22.23	0.00	**209.09**
10-Feb-25	11.76	19.13	14.80	16.75	0.00	86.88	2.42	0.00		0.00	2.12	3.18	0.00	0.00	32.04	0.00	17.13	0.00	**206.21**
11-Feb-25	5.60	13.02	9.74	15.69	0.00	78.96	2.42	0.00		0.00	2.17	3.23	0.00	0.00	36.23	0.00	13.57	0.00	**180.63**
12-Feb-25	3.20	13.33	8.00	15.35	0.00	96.51	6.81	0.00		0.00	2.20	3.38	0.00	0.00	36.23	0.00	11.70	0.00	**196.71**
13-Feb-25	8.42	17.02	10.31	15.85	0.00	66.25	5.83	0.00		0.00	2.25	3.37	0.00	0.00	32.63	0.00	11.69	0.00	**173.62**
14-Feb-25	12.91	20.37	16.89	18.97	0.00	57.92	2.40		0.00	0.00	2.29	3.32	0.00	0.00	31.15	0.00	17.53	0.00	**183.75**
15-Feb-25	12.56	16.58	14.64	18.12	0.00	62.23	0.00	0.00		0.00	2.31	3.23	0.00	0.00	33.31	0.00	18.51	0.00	**181.49**
16-Feb-25	18.93	21.21	21.69	17.47	0.00	52.35	0.00	0.00		0.00	2.31	3.18	0.00	0.00	36.23	0.00	12.83	0.00	**186.20**
17-Feb-25	12.44	21.70	15.67	18.63	0.00	76.10	0.00	0.00		0.00	2.28	3.21	0.00	0.00	36.23	0.00	15.42	0.00	**201.68**
18-Feb-25	12.26	20.52	15.99	18.36	0.00	72.95	0.00	0.00		0.00	2.16	3.21	0.00	0.00	36.25	0.00	21.03	0.00	**202.73**
19-Feb-25	13.58	22.78	16.22	18.66	0.00	74.90	0.00	0.00		0.00	2.32	3.25	0.00	0.00	36.25	0.00	20.47	0.00	**208.43**
20-Feb-25	0.00	13.55	2.20	14.56	0.00	69.80	0.00	0.00		0.00	2.45	3.25	0.00	0.00	36.24	0.00	12.26	0.00	**154.31**
21-Feb-25	2.50	19.50	7.18	16.00	0.00	59.33	0.00	0.00		0.00	2.36	3.29	0.00	0.00	32.72	0.00	9.87	0.00	**152.75**
22-Feb-25	4.35	21.53	10.05	16.98	0.00	35.77	0.00	0.00		0.00	2.33	3.13	0.00	0.00	28.98	0.00	14.45	0.00	**137.57**
23-Feb-25	4.21	18.16	10.49	16.12	0.00	30.27	0.00	0.00		0.00	2.36	3.12	0.00	0.00	28.85	0.00	14.45	0.00	**128.03**
24-Feb-25	13.28	21.87	19.50	17.70	0.00	39.70	0.00	0.00		0.00	2.34	3.02	0.00	0.00	28.08	0.00	18.08	0.00	**163.57**
25-Feb-25	21.78	29.82	25.68	22.19	0.00	46.93	0.00	0.00		0.44	2.32	2.93	0.00	0.00	13.14	0.00	25.68	0.00	**190.91**
26-Feb-25	18.98	24.43	22.62	20.27	0.00	44.80	0.00	0.00		0.00	2.24	2.75	0.00	0.00	24.23	0.00	24.08	0.00	**184.40**
27-Feb-25	21.53	26.26	24.84	19.86	0.00	43.89	0.00	0.00		0.00	2.27	2.70	0.00	0.00	31.45	0.00	22.66	0.00	**195.46**
28-Feb-25	9.50	14.42	11.76	17.29	0.00	37.15	0.00	0.00		0.00	2.32	2.84	0.00	0.00	28.30	0.00	19.10	0.00	**142.68**
Total	**330.17**	**514.09**	**415.21**	**485.93**	**0.00**	**1731.95**	**41.66**	**0.00**	**0.00**	**0.44**	**62.04**	**88.29**	**0.00**	**0.00**	**840.99**	**8.74**	**522.72**	**0.00**	**5042.23**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.1 Import-Export of NR with WR during February 2025

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Feb-25	0.00	0.00	0.00	0.00	15.02	0.00	0.00	5.40		5.16	0.00	0.00	3.51	22.30	0.00	14.10	0.00	4.77	**70.26**
2-Feb-25	0.00	0.00	0.00	0.00	14.20	0.00	0.00	4.56		5.97	0.00	0.00	3.05	22.48	0.00	9.42	0.00	6.37	**66.05**
3-Feb-25	0.00	0.00	0.00	0.00	15.40	0.00	0.00	4.60		4.21	0.00	0.00	3.22	22.50	0.00	11.86	0.00	4.25	**66.04**
4-Feb-25	0.00	0.00	0.00	0.00	13.56	0.00	0.00	2.60		6.49	0.00	0.00	3.52	17.83	0.00	7.91	0.00	6.46	**58.37**
5-Feb-25	0.00	0.00	0.00	0.00	13.34	0.00	0.00	4.09		6.78	0.00	0.00	3.55	10.83	0.00	9.28	0.00	6.01	**53.88**
6-Feb-25	0.00	0.00	0.00	0.00	11.45	0.00	0.00	0.77		6.31	0.00	0.00	3.06	10.52	0.00	0.00	0.00	6.54	**38.65**
7-Feb-25	0.00	0.00	0.00	0.00	13.17	0.00	0.00	0.62		4.80	0.00	0.00	2.44	12.42	0.00	0.00	0.00	5.25	**38.70**
8-Feb-25	0.00	0.00	0.00	0.00	14.93	0.00	0.00	1.90		4.70	0.00	0.00	3.06	10.92	0.00	11.70	0.00	4.95	**52.16**
9-Feb-25	0.00	0.00	0.00	0.00	14.68	0.00	0.00	7.70		6.73	0.00	0.00	3.54	11.01	0.00	23.14	0.00	6.58	**73.38**
10-Feb-25	0.00	0.00	0.00	0.00	14.71	0.00	0.00	7.02		6.71	0.00	0.00	3.54	10.95	0.00	19.78	0.00	7.12	**69.83**
11-Feb-25	0.00	0.00	0.00	0.00	14.12	0.00	0.00	6.10		7.46	0.00	0.00	3.64	10.95	0.00	17.05	0.00	7.91	**67.23**
12-Feb-25	0.00	0.00	0.00	0.00	13.99	0.00	0.00	6.40		7.52	0.00	0.00	3.81	11.03	0.00	19.67	0.00	7.19	**69.61**
13-Feb-25	0.00	0.00	0.00	0.00	14.77	0.00	0.00	5.96		6.37	0.00	0.00	3.57	11.00	0.00	19.71	0.00	6.33	**67.71**
14-Feb-25	0.00	0.00	0.00	0.00	14.91	0.00	0.00		5.00	5.37	0.00	0.00	2.56	11.01	0.00	15.06	0.00	5.62	**59.53**
15-Feb-25	0.00	0.00	0.00	0.00	13.97	0.00	0.09	4.50		5.45	0.00	0.00	3.14	10.93	0.00	9.26	0.00	5.45	**52.79**
16-Feb-25	0.00	0.00	0.00	0.00	14.82	0.00	7.91	3.50		2.56	0.00	0.00	3.00	11.04	0.00	9.14	0.00	2.40	**54.37**
17-Feb-25	0.00	0.00	0.00	0.00	15.62	0.00	11.41	6.80		3.53	0.00	0.00	3.37	11.12	0.00	23.23	0.00	4.90	**79.98**
18-Feb-25	0.00	0.00	0.00	0.00	14.80	0.00	6.08	5.60		3.76	0.00	0.00	3.42	11.14	0.00	16.72	0.00	5.05	**66.57**
19-Feb-25	0.00	0.00	0.00	0.00	15.87	0.00	6.10	3.70		2.82	0.00	0.00	2.96	10.95	0.00	9.66	0.00	4.82	**56.88**
20-Feb-25	1.80	0.00	0.00	0.00	13.88	0.00	6.02	8.20		6.68	0.00	0.00	3.99	11.00	0.00	26.30	0.00	7.16	**85.03**
21-Feb-25	0.00	0.00	0.00	0.00	15.70	0.00	4.77	9.70		5.25	0.00	0.00	3.90	11.02	0.00	31.13	0.00	6.15	**87.62**
22-Feb-25	0.00	0.00	0.00	0.00	15.59	0.00	0.61	7.95		4.68	0.00	0.00	3.81	10.99	0.00	25.55	0.00	6.50	**75.68**
23-Feb-25	0.00	0.00	0.00	0.00	14.50	0.00	1.25	7.95		5.07	0.00	0.00	3.84	10.94	0.00	26.49	0.00	6.50	**76.54**
24-Feb-25	0.00	0.00	0.00	0.00	14.83	0.00	4.88	7.40		2.50	0.00	0.00	3.28	10.96	0.00	23.22	0.00	3.00	**70.07**
25-Feb-25	0.00	0.00	0.00	0.00	15.88	0.00	4.87	3.58		0.00	0.00	0.00	2.99	8.52	0.00	15.35	0.00	0.43	**51.62**
26-Feb-25	0.00	0.00	0.00	0.00	14.84	0.00	4.87	3.80		0.64	0.00	0.00	3.06	10.72	0.00	13.35	0.00	1.26	**52.54**
27-Feb-25	0.00	0.00	0.00	0.00	16.08	0.00	4.85	3.98		0.57	0.00	0.00	3.15	10.99	0.00	11.78	0.00	1.49	**52.89**
28-Feb-25	0.00	0.00	0.00	0.00	12.35	0.00	4.90	5.65		4.30	0.00	0.00	3.55	11.07	0.00	15.00	0.00	5.00	**61.82**
Total	**1.80**	**0.00**	**0.00**	**0.00**	**406.98**	**0.00**	**68.61**	**140.03**	**5.00**	**132.39**	**0.00**	**0.00**	**93.53**	**347.14**	**0.00**	**434.86**	**0.00**	**145.46**	**1775.80**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during February 2025

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Feb-25	10.80	16.57	10.04		14.38	6.85	2.90	7.65		0.74	0.39	0.96			0.00	4.42	5.93	**81.63**	0.00	**0.00**
2-Feb-25	8.04	12.21	9.01		11.55	5.30	1.49	6.25		0.95		0.14		0.00	0.00	3.44	5.23	**63.61**	0.00	**0.00**
3-Feb-25	9.66	15.21	9.52		11.66	4.11	1.25	5.21		0.93	0.17	0.65		0.00	0.00	3.48	4.94	**66.79**	0.00	**0.00**
4-Feb-25	9.50	14.98	9.19		10.68	3.69	1.35	4.71		1.40	0.00	0.79		0.00	0.00	3.16	5.19	**64.64**	0.00	**0.00**
5-Feb-25	9.82	18.28	9.06		11.24	3.59	1.79	4.70		1.44	0.00	0.96	0.00		0.00	3.31	5.72	**69.91**	0.00	**0.00**
6-Feb-25	9.82	15.56	10.75		12.20	3.60	1.04	5.60		0.73	0.28	0.92	0.48		0.00	3.76	5.53	**70.27**	0.00	**0.00**
7-Feb-25	9.34	14.13	10.28		11.38	3.82	1.18	5.28		0.71	0.43	0.70			0.00	3.40	5.40	**66.05**	0.00	**0.00**
8-Feb-25	10.05	13.51	9.73		9.81	4.43	2.19	4.59		0.95	0.07	0.70	0.00		0.00	2.85	5.15	**64.03**	0.00	**0.00**
9-Feb-25	9.16	13.24	8.34		9.81	4.35	2.08	4.55		1.11	0.11	0.54	0.00	0.00	0.00	2.85	4.70	**60.84**	0.00	**0.00**
10-Feb-25	10.85	16.23	9.31		10.52	4.95	2.68	4.88		0.52	0.03	0.84	0.00	0.00	0.00	3.05	7.35	**71.21**	0.00	**0.00**
11-Feb-25	10.45	16.06	8.68		10.32	3.25	1.81	4.02		0.60	0.00	0.93		0.00	0.00	2.95	6.02	**65.09**	0.00	**0.00**
12-Feb-25	11.18	17.69	8.84		14.28	3.26	1.61	5.93		0.75	0.00	1.13	0.00	0.00	0.00	4.70	6.43	**75.80**	0.00	**0.00**
13-Feb-25	11.48	17.88	8.00		14.98	4.30	1.94	6.32		0.62	0.00	1.20		0.00	0.00	4.52	6.41	**77.65**	0.00	**0.00**
14-Feb-25	12.55	18.76	8.70		16.19	5.81	2.06	7.28		0.58	0.28	1.10			0.00	5.07	6.67	**85.05**	0.00	**0.00**
15-Feb-25	10.84	17.23	9.97		16.81	4.91	1.06	7.33		0.97	0.13	0.75			0.00	5.25	5.81	**81.06**		**0.00**
16-Feb-25	11.25	19.87	9.87		17.36	4.71	1.67	7.44		0.31	0.00	1.20		0.00	0.00	5.35	6.62	**85.65**	0.00	**0.00**
17-Feb-25	11.52	19.01	8.98		17.81	4.15	1.35	7.77		0.82	0.08	1.10	0.00	0.00	0.00	5.29	6.50	**84.38**	0.00	**0.00**
18-Feb-25	11.75	15.80	8.31		16.57	3.52	1.35	7.31		0.67	0.11	1.05		0.00	0.00	4.92	5.61	**76.97**	0.00	**0.00**
19-Feb-25	10.45	14.77	7.64		15.35	3.19	1.24	6.93		0.75	0.07		0.98		0.00	4.75	5.40	**71.52**	0.00	**0.00**
20-Feb-25	6.24	11.86	4.12		11.15	0.53	0.00	4.30		2.13	0.20	0.82	0.00	0.00	0.00	3.25	3.57	**48.17**	0.00	**0.00**
21-Feb-25	8.00	15.75	6.85		12.00	1.55	0.00	5.00		1.90	0.45	0.25		0.00	0.00	3.83	5.00	**60.58**	0.00	**0.00**
22-Feb-25	8.13	15.03	9.78		13.22	2.67	0.23	5.58		2.07	0.27	0.00			0.00	3.97	4.13	**65.08**	0.00	**0.00**
23-Feb-25	7.40	13.07	10.57		14.71	3.08	0.00	6.35		2.18	0.10	0.10			0.00	4.48	3.63	**65.67**	0.00	**0.00**
24-Feb-25	9.05	16.38	8.22		16.53	4.67	0.82	6.62		1.83	0.54	0.48	0.00	0.00	0.00	5.16	5.13	**75.43**	0.00	**0.00**
25-Feb-25	12.58	18.50	9.00		16.53	5.27	2.20	8.30		1.20	1.14	0.81		0.00	0.00	5.90	6.37	**87.80**	0.00	**0.00**
26-Feb-25	11.98	18.97	10.14		18.22	5.38	1.90	6.53		1.40	0.90	1.02		0.00	0.00	5.75	6.54	**88.73**	0.00	**0.00**
27-Feb-25	5.35	19.39	10.03		17.77	4.51	1.76	7.53		1.17	1.14	1.95			0.00	5.64	6.46	**82.70**	0.00	**0.00**
28-Feb-25	7.52	16.11	8.37		15.60	3.15	0.85	6.68		1.66	0.75	1.15			0.00	4.81	5.68	**72.33**	0.00	**0.00**
Total	**274.76**	**452.05**	**251.30**	**0.00**	**388.63**	**112.60**	**39.80**	**170.64**	**0.00**	**31.09**	**7.64**	**22.24**	**1.46**	**0.00**	**0.00**	**119.31**	**157.12**	**2028.64**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.2 Import-Export of NR with ER & NER during February 2025

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri Karamnasa	NR - ER 132 kV Rihand -Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.41	0.00	0.00	**0.41**	17.15	**17.15**
2-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00		0.00		0.12	0.35	0.00	0.00	**0.47**	15.90	**15.90**
3-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.12	0.61	0.00	0.00	**0.73**	16.99	**16.99**
4-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.28	0.00		0.09	0.50	0.00	0.00	**0.87**	16.88	**16.88**
5-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.35	0.00	0.00		0.40	0.00	0.00	**0.75**	16.98	**16.98**
6-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.62	0.00	0.00	**0.62**	16.98	**16.98**
7-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.57	0.00	0.00	**0.57**	16.57	**16.57**
8-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.56	0.00	0.00	**0.56**	16.73	**16.73**
9-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.14	0.48	0.00	0.00	**0.62**	16.69	**16.69**
10-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.09	0.61	0.00	0.00	**0.70**	16.89	**16.89**
11-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.66	0.00		0.10	0.60	0.00	0.00	**1.36**	17.51	**17.51**
12-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.87	0.00	0.00	0.10	0.60	0.00	0.00	**1.57**	16.89	**16.89**
13-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.72	0.00		0.09	0.66	0.00	0.00	**1.47**	16.75	**16.75**
14-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.70	0.00	0.00	**0.70**	16.57	**16.57**
15-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.60	0.00	0.00	**0.60**		**0.00**
16-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.22	0.00		0.11	0.55	0.00	0.00	**0.88**	16.74	**16.74**
17-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.09	0.57	0.00	0.00	**0.66**	16.74	**16.74**
18-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.58	0.00	0.00	**0.68**	16.10	**16.10**
19-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00		0.00		0.57	0.00	0.00	**0.57**	16.89	**16.89**
20-Feb-25	0.00	0.00	0.00		0.00	0.00	0.67	0.00		0.00	0.00	0.00	0.00	0.10	0.33	0.00	0.00	**1.10**	16.76	**16.76**
21-Feb-25	0.00	0.00	0.00		0.00	0.00	0.90	0.00		0.00	0.00	0.00		0.09	0.55	0.00	0.00	**1.54**	17.05	**17.05**
22-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.38			0.58	0.00	0.00	**0.96**	17.11	**17.11**
23-Feb-25	0.00	0.00	0.00		0.00	0.00	0.09	0.00		0.00	0.00	0.00			0.58	0.00	0.00	**0.67**	16.91	**16.91**
24-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.09	0.58	0.00	0.00	**0.67**	16.65	**16.65**
25-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.10	0.56	0.00	0.00	**0.66**	14.49	**14.49**
26-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.11	0.57	0.00	0.00	**0.68**	11.98	**11.98**
27-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.56	0.00	0.00	**0.56**	12.05	**12.05**
28-Feb-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.61	0.00	0.00	**0.61**	16.59	**16.59**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**1.66**	**0.00**	**0.00**	**0.00**	**3.10**	**0.38**	**0.00**	**1.64**	**15.46**	**0.00**	**0.00**	**22.24**	**441.54**	**441.54**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.3 Import and Export of ER with WR & NER during February 2025

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Feb-25	0.2	3.9	0.0	0.0	0.0	0.4	0.0	**4.51**	13.4	6.5	21.6	5.6	13.7	0.3	0.8	**61.98**	0.10	0.02	0.00	**0.12**	1.92	4.33	0.98	**7.22**
2-Feb-25	2.5	5.1	0.0	0.2	0.0	0.5	0.0	**8.31**	9.0	4.0	19.5	4.1	14.0	0.3	0.8	**51.70**	0.09	0.00	0.00	**0.09**	2.39	5.03	1.12	**8.54**
3-Feb-25	0.7	9.1	0.0	0.0	0.0	0.4	0.0	**10.20**	7.4	1.1	18.6	4.0	13.9	0.4	0.8	**46.36**	0.09	0.00	0.00	**0.09**	2.31	4.90	1.22	**8.44**
4-Feb-25	0.5	15.5	0.0	0.0	0.0	0.6	0.0	**16.62**	11.0	0.5	16.2	4.7	12.0	0.2	0.8	**45.35**	0.10	0.00	0.00	**0.10**	2.62	5.36	1.39	**9.37**
5-Feb-25	0.0	15.1	0.0	0.0	0.0	0.4	0.0	**15.57**	13.7	0.1	15.0	5.2	11.7	0.3	0.7	**46.62**	0.04	0.00	0.00	**0.04**	3.32	6.72	1.46	**11.50**
6-Feb-25	0.9	12.8	0.0	0.0	0.0	0.5	0.0	**14.22**	12.0	0.4	17.1	5.2	13.1	0.3	0.9	**49.02**	0.28	0.07	0.00	**0.35**	2.34	4.92	1.15	**8.42**
7-Feb-25	0.4	5.3	0.0	0.0	0.0	0.8	0.0	**6.52**	10.8	4.8	19.6	4.8	12.5	0.1	1.1	**53.74**	0.08	0.00	0.00	**0.08**	2.59	5.56	1.28	**9.43**
8-Feb-25	0.2	2.7	0.0	0.0	0.0	0.3	0.0	**3.24**	11.0	8.6	21.8	4.7	13.0	0.4	1.5	**61.06**	0.00	0.00	0.00	**0.00**	2.91	6.13	1.35	**10.39**
9-Feb-25	0.9	5.1	0.0	0.3	0.0	0.4	0.0	**6.63**	13.9	8.3	21.2	4.4	14.5	0.3	0.8	**63.43**	0.00	0.00	0.00	**0.00**	3.63	7.42	1.70	**12.75**
10-Feb-25	0.0	6.5	0.0	0.0	0.0	0.3	0.0	**6.82**	14.5	6.3	21.7	3.9	15.9	0.5	1.1	**63.81**	0.00	0.00	0.00	**0.00**	3.72	7.36	1.69	**12.77**
11-Feb-25	0.0	3.8	0.0	0.0	0.0	0.1	0.0	**3.95**	16.1	3.2	21.0	3.8	16.3	0.6	1.4	**62.38**	0.01	0.00	0.00	**0.01**	3.86	7.18	1.94	**12.98**
12-Feb-25	0.0	8.0	0.0	0.0	0.0	0.5	0.0	**8.49**	19.4	4.0	23.4	4.9	15.8	0.3	1.3	**69.15**	0.01	0.00	0.00	**0.01**	3.33	6.29	1.89	**11.52**
13-Feb-25	0.1	7.6	0.0	0.0	0.0	0.3	0.0	**8.10**	15.3	1.8	24.5	4.0	15.5	0.4	1.6	**63.20**	0.00	0.00	0.00	**0.00**	4.24	7.51	2.16	**13.92**
14-Feb-25	0.0	8.3	0.0	0.0	0.0	0.1	0.0	**8.41**	15.7	2.4	24.4	4.1	15.8	0.8	1.9	**65.17**	0.00	0.00	0.00	**0.00**	4.17	7.34	2.10	**13.61**
15-Feb-25	0.3	4.9	0.0	0.1	0.0	0.4	0.0	**5.71**	16.7	3.0	24.9	4.0	14.0	0.3	1.9	**64.63**	0.00	0.00	0.00	**0.00**	3.24	5.93	1.90	**11.06**
16-Feb-25	1.3	4.2	0.0	0.3	0.0	0.5	0.0	**6.28**	12.3	2.9	23.2	3.0	14.1	0.3	1.8	**57.62**	0.03	0.01	0.00	**0.04**	2.47	4.58	1.69	**8.74**
17-Feb-25	0.0	5.6	0.0	0.0	0.0	1.0	0.0	**6.61**	14.9	4.1	24.2	4.1	12.5	0.2	1.3	**61.44**	0.02	0.00	0.00	**0.02**	2.81	5.19	1.70	**9.70**
18-Feb-25	0.6	6.4	0.0	0.0	0.0	0.9	0.0	**7.94**	12.6	4.4	24.0	3.9	10.6	0.2	1.6	**57.14**	0.06	0.00	0.00	**0.06**	3.01	5.60	1.85	**10.46**
19-Feb-25	0.5	9.9	0.0	0.0	0.0	1.0	0.0	**11.43**	11.3	4.5	22.4	3.4	9.1	0.1	1.2	**51.84**	0.01	0.00	0.00	**0.01**	3.29	6.21	1.89	**11.40**
20-Feb-25	0.0	15.1	0.0	0.0	0.0	1.6	0.0	**16.70**	17.6	1.6	23.3	4.3	10.0	0.1	1.1	**58.01**	0.13	0.01	0.00	**0.14**	2.58	4.99	1.70	**9.27**
21-Feb-25	0.0	18.3	0.0	0.0	0.0	0.6	0.0	**18.97**	17.3	1.4	19.6	5.0	12.1	0.6	1.5	**57.51**	0.12	0.00	0.00	**0.12**	2.94	5.49	1.78	**10.21**
22-Feb-25	0.0	17.9	0.0	0.0	0.0	0.0	0.0	**17.91**	16.6	1.1	19.8	5.0	16.5	1.7	1.8	**62.45**	0.09	0.00	0.00	**0.09**	3.42	6.14	1.91	**11.47**
23-Feb-25	1.0	13.1	0.0	0.2	0.0	0.2	0.0	**14.43**	11.9	1.4	19.6	3.5	16.5	0.8	1.5	**55.26**	0.25	0.13	0.00	**0.37**	3.09	5.46	1.77	**10.32**
24-Feb-25	1.1	13.4	0.0	0.2	0.0	0.3	0.0	**14.96**	8.9	1.7	18.3	2.9	15.9	0.4	1.7	**49.99**	0.07	0.00	0.00	**0.07**	2.73	5.35	1.60	**9.68**
25-Feb-25	0.7	14.6	0.0	0.0	0.0	0.6	0.0	**15.86**	9.7	2.3	17.7	3.6	14.2	0.2	1.4	**49.13**	0.44	0.17	0.00	**0.61**	0.92	2.40	0.77	**4.09**
26-Feb-25	0.8	9.9	0.0	0.2	0.0	0.4	0.0	**11.37**	11.8	4.3	19.0	4.0	14.0	0.3	1.6	**54.96**	1.16	0.91	0.02	**2.09**	0.39	1.17	0.49	**2.05**
27-Feb-25	1.6	12.6	0.0	0.1	0.0	0.3	0.0	**14.64**	7.5	2.9	19.2	2.8	15.1	0.4	1.4	**49.39**	1.05	0.78	0.00	**1.83**	0.48	1.28	0.55	**2.31**
28-Feb-25	1.6	17.5	0.0	0.0	0.0	0.9	0.1	**20.12**	8.8	0.9	21.8	3.1	12.1	0.1	0.7	**47.49**	0.29	0.03	0.00	**0.32**	1.12	2.50	0.87	**4.49**
Total	**16.05**	**272.20**	**0.00**	**1.72**	**0.00**	**14.43**	**0.12**	**304.52**	**361.11**	**88.44**	**582.66**	**116.14**	**384.61**	**10.91**	**35.98**	**1579.84**	**4.51**	**2.13**	**0.02**	**6.66**	**75.85**	**148.37**	**41.90**	**266.13**

Date	15.4 Import and Export of SR with ER & WR during February 2025																								
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Feb-25	8.59	34.72	49.38	**92.69**	0.00	0.00	0.00	**0.00**	22.44	7.44	29.25	0.00	77.58	2.25	0.00	34.06	**173.04**	0.00	8.78	0.46	23.87	0.00	0.00	0.00	0.04	**33.14**
2-Feb-25	8.62	30.17	48.15	**86.94**	0.00	0.00	0.00	**0.00**	23.99	6.92	29.16	0.00	68.05	2.13	0.00	34.84	**165.09**	0.00	10.62	0.05	24.30	0.00	0.00	0.00	0.00	**34.97**
3-Feb-25	8.61	30.16	49.93	**88.70**	0.00	0.00	0.00	**0.00**	22.04	8.28	33.67	0.00	56.85	2.28	0.00	38.76	**161.89**	0.00	5.56	0.00	22.91	0.00	0.00	0.00	0.00	**28.48**
4-Feb-25	8.61	30.16	47.78	**86.56**	0.00	0.00	0.00	**0.00**	21.32	11.83	36.49	0.00	53.27	2.20	0.00	43.25	**168.36**	0.00	5.05	0.01	24.80	0.00	0.00	0.00	0.00	**29.87**
5-Feb-25	8.61	30.17	49.56	**88.33**	0.00	0.00	0.00	**0.00**	12.19	13.30	42.57	0.00	46.16	2.24	0.00	47.60	**164.04**	0.00	1.54	0.00	20.88	0.00	0.00	0.00	0.00	**22.42**
6-Feb-25	8.61	31.03	56.11	**95.75**	0.00	0.00	0.00	**0.00**	22.23	14.63	47.71	0.00	59.18	2.26	0.00	51.20	**197.22**	0.00	1.48	0.00	23.11	0.00	0.00	0.00	0.00	**24.58**
7-Feb-25	8.62	37.24	53.82	**99.67**	0.00	0.00	0.00	**0.00**	24.07	10.92	40.49	0.00	79.75	2.28	0.00	44.26	**201.77**	0.00	5.57	0.07	25.48	0.00	0.00	0.00	0.00	**31.12**
8-Feb-25	8.62	30.15	53.10	**91.86**	0.00	0.00	0.00	**0.00**	22.11	6.87	35.94	0.00	62.85	2.26	0.00	40.83	**170.87**	0.00	6.73	0.00	27.32	0.00	0.00	0.00	0.00	**34.06**
9-Feb-25	8.61	30.14	53.79	**92.54**	0.00	0.00	0.00	**0.00**	15.87	9.02	37.97	0.00	43.54	2.13	0.00	42.43	**150.96**	0.00	7.48	0.00	26.58	0.00	0.00	0.00	0.00	**34.06**
10-Feb-25	7.66	31.53	56.24	**95.43**	0.00	0.00	0.00	**0.00**	24.12	9.24	36.29	0.00	42.81	2.18	0.00	43.78	**158.43**	0.00	5.84	0.00	24.69	0.00	0.00	0.00	0.00	**30.54**
11-Feb-25	6.42	42.69	54.36	**103.46**	0.00	0.00	0.00	**0.00**	24.10	6.00	37.12	0.00	80.42	2.31	0.00	42.52	**192.47**	0.00	6.51	0.00	25.26	0.00	0.00	0.00	0.00	**31.77**
12-Feb-25	4.93	42.34	59.91	**107.18**	0.00	0.00	0.00	**0.00**	20.96	14.36	49.98	0.00	61.24	2.15	0.00	51.31	**200.01**	0.00	2.18	0.00	19.99	0.00	0.00	0.00	0.00	**22.17**
13-Feb-25	3.87	41.35	60.14	**105.35**	0.00	0.00	0.00	**0.00**	15.06	15.74	52.86	0.00	54.75	2.19	0.55	50.82	**191.97**	0.00	1.12	0.00	18.38	0.00	0.00	0.00	0.00	**19.50**
14-Feb-25	5.63	43.33	59.45	**108.42**	0.00	0.00	0.00	**0.00**	19.15	16.71	50.45	0.00	58.19	2.26	0.65	49.03	**196.45**	0.00	2.47	0.00	17.79	0.00	0.00	0.00	0.00	**20.26**
15-Feb-25	8.67	39.79	57.37	**105.83**	0.00	0.00	0.00	**0.00**	12.16	12.39	50.00	0.00	83.16	2.33	0.00	48.05	**208.09**	0.00	3.19	0.00	20.94	0.00	0.00	0.00	0.00	**24.14**
16-Feb-25	8.67	39.78	55.51	**103.96**	0.00	0.00	0.00	**0.00**	12.16	10.60	45.44	0.00	58.83	2.33	0.00	45.51	**174.87**	0.00	3.55	0.00	22.99	0.00	0.00	0.00	0.00	**26.55**
17-Feb-25	8.67	39.80	55.21	**103.68**	0.00	0.00	0.00	**0.00**	20.51	10.94	43.84	0.00	71.31	2.32	0.00	45.76	**194.68**	0.00	4.25	0.00	21.74	0.00	0.00	0.00	0.00	**26.00**
18-Feb-25	8.67	39.79	53.60	**102.06**	0.00	0.00	0.00	**0.00**	24.17	10.47	39.11	0.00	80.73	2.29	0.46	42.46	**199.69**	0.00	3.45	0.00	21.35	0.00	0.00	0.00	0.00	**24.81**
19-Feb-25	8.73	46.68	51.93	**107.34**	0.00	0.00	0.00	**0.00**	24.15	12.49	38.05	0.00	84.74	2.01	0.00	42.39	**203.82**	0.00	3.93	0.00	21.53	0.00	0.00	0.00	0.00	**25.46**
20-Feb-25	14.82	48.17	47.06	**110.05**	0.00	0.00	0.00	**0.00**	24.13	18.38	50.06	0.00	99.26	2.24	0.00	52.43	**246.51**	0.00	3.49	0.00	19.84	0.00	0.00	0.00	0.00	**23.33**
21-Feb-25	17.44	43.54	51.67	**112.66**	0.00	0.00	0.00	**0.00**	24.12	13.13	44.51	0.00	84.86	2.57	0.00	50.17	**219.36**	0.00	2.38	0.00	22.20	0.00	0.00	0.00	0.00	**24.58**
22-Feb-25	17.38	39.80	52.75	**109.93**	0.00	0.00	0.00	**0.00**	24.16	12.16	41.73	0.00	80.75	2.52	0.01	48.53	**209.85**	0.00	1.92	0.01	21.02	0.00	0.00	0.00	0.00	**22.95**
23-Feb-25	12.51	39.79	51.69	**103.99**	0.00	0.00	0.00	**0.00**	21.57	11.16	40.18	0.00	67.00	2.51	0.01	46.37	**188.80**	0.00	4.00	0.00	21.10	0.00	0.00	0.00	0.00	**25.10**
24-Feb-25	9.97	45.95	54.14	**110.07**	0.00	0.00	0.00	**0.00**	19.17	8.15	38.94	0.00	50.17	2.55	0.00	46.01	**164.99**	0.00	6.99	0.13	25.40	0.00	0.00	0.00	0.00	**32.53**
25-Feb-25	8.68	48.16	50.80	**107.63**	0.00	0.00	0.00	**0.00**	21.70	9.38	37.70	0.00	40.43	2.46	0.43	42.71	**154.81**	0.00	4.71	0.00	26.04	0.00	0.00	0.00	0.00	**30.75**
26-Feb-25	7.05	48.15	55.48	**110.68**	0.00	0.00	0.00	**0.00**	24.14	7.56	37.19	0.00	56.40	2.30	0.19	42.58	**170.37**	0.00	4.64	0.00	27.81	0.00	0.00	0.00	0.00	**32.46**
27-Feb-25	5.27	48.15	57.58	**111.00**	0.00	0.00	0.00	**0.00**	24.16	7.67	37.29	0.00	45.04	1.33	0.00	41.39	**156.90**	0.00	5.57	0.00	27.85	0.00	0.00	0.00	0.00	**33.42**
28-Feb-25	9.63	45.67	59.32	**114.62**	0.00	0.00	0.00	**0.00**	14.28	15.44	47.77	0.00	58.74	2.51	0.00	49.61	**188.35**	0.00	2.11	0.00	22.26	0.00	0.00	0.00	0.00	**24.37**
TOTAL	**252.18**	**1098.40**	**1505.81**	**2856.39**	**0.00**	**0.00**	**0.00**	**0.00**	**580.23**	**311.16**	**1151.75**	**0.00**	**1806.06**	**63.41**	**2.36**	**1258.67**	**5173.64**	**0.00**	**125.15**	**0.74**	**647.43**	**0.00**	**0.00**	**0.02**	**0.04**	**773.38**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 **से मार्च** 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
अक्तूबर 2024 OCT'24	0.00	918.96	0.00	283.29	695.63	0.00	0.80	0.00
नवंबर 2024 NOV'24	12.24	125.37	0.00	212.20	698.58	0.00	0.71	0.00
दिसम्बर 2024 DEC'24	187.39	0.00	58.60	1.56	521.28	0.00	0.72	0.00
जनवरी 2025 JAN'25	158.13	0.00	252.02	0.00	674.70	0.00	0.67	0.00
फ़रवरी 2025 FEB'25	216.70	0.00	328.10	0.00	635.20	0.00	0.56	0.00
कुल Total	712.30	5325.83	1277.13	2131.41	7385.92	0.00	8.36	0.00

* Based on daily operational data

16.1 Export to neighbouring countries during Feb 2025

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Feb-25	0.00	0.00	0.00	0.00	0.00	1.11	0.02	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-Feb-25	0.00	0.00	0.00	0.00	0.00	1.26	0.19	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-Feb-25	0.00	0.00	0.00	0.00	0.00	1.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-Feb-25	0.00	0.00	0.00	0.00	0.00	1.73	0.11	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-Feb-25	0.00	0.00	0.00	0.00	0.00	0.82	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-Feb-25	0.00	0.00	0.00	0.00	0.00	0.57	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
7-Feb-25	0.00	0.00	0.00	0.00	0.00	0.67	0.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-Feb-25	0.00	0.00	0.00	0.00	0.00	0.84	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-Feb-25	0.00	0.00	0.00	0.00	0.00	0.38	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
10-Feb-25	0.00	0.00	0.00	0.00	0.00	1.36	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Feb-25	0.00	0.00	0.00	0.00	0.00	3.11	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Feb-25	0.00	0.00	0.00	0.00	0.00	3.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-Feb-25	0.00	0.00	0.00	0.00	0.00	4.10	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-Feb-25	0.00	0.00	0.00	0.00	0.00	4.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-Feb-25	0.00	0.00	0.00	0.00	0.00	4.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-Feb-25	0.00	0.00	0.00	0.00	0.00	4.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
17-Feb-25	0.00	0.00	0.00	0.00	0.00	3.91	0.06	0.00	0.00	0.00	0.00	0.00	0.00	0.00
18-Feb-25	0.00	0.00	0.00	0.00	0.00	3.79	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
19-Feb-25	0.00	0.00	0.00	0.00	0.00	3.39	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
20-Feb-25	0.00	0.00	0.00	0.00	0.00	3.22	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00
21-Feb-25	0.00	0.00	0.00	0.00	0.00	3.35	0.11	0.00	0.00	0.00	0.00	0.00	0.00	0.00
22-Feb-25	0.00	0.00	0.00	0.00	0.00	3.76	0.11	0.00	0.00	0.00	0.00	0.00	0.00	0.00
23-Feb-25	0.00	0.00	0.00	0.00	0.00	3.63	0.09	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-Feb-25	0.00	0.00	0.00	0.00	0.00	2.51	0.16	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-Feb-25	0.00	0.00	0.00	0.00	0.00	0.93	0.10	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-Feb-25	0.00	0.00	0.00	0.00	0.00	0.91	0.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00
27-Feb-25	0.00	0.00	0.00	0.00	0.00	1.13	0.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00
28-Feb-25	0.00	0.00	0.00	0.00	0.00	1.80	0.08	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**65.07**	**1.10**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

16.2 Export to neighbouring countries during Feb 2025

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Feb-25	0.76	1.93	3.30	1.63	0.00	0.00	0.00	0.42	19.54	1.47	0.72	4.23	3.28	0.02
2-Feb-25	0.84	1.99	3.33	1.67	0.00	0.00	0.00	0.39	20.09	1.41	0.97	4.86	3.97	0.02
3-Feb-25	0.85	2.01	3.44	1.69	0.00	0.00	0.02	0.35	20.54	1.37	1.07	5.40	3.71	0.02
4-Feb-25	0.92	2.09	4.33	1.51	0.00	0.00	0.00	0.31	20.65	1.27	0.94	5.22	3.49	0.02
5-Feb-25	0.95	2.10	2.94	1.95	0.00	0.00	0.11	0.22	20.56	1.05	0.94	4.84	3.33	0.02
6-Feb-25	0.95	2.13	3.03	1.90	0.00	0.00	0.12	0.00	20.57	0.99	1.04	5.29	3.57	0.02
7-Feb-25	0.79	1.95	3.40	1.68	0.00	0.00	0.00	0.00	20.09	1.00	1.04	5.87	3.57	0.02
8-Feb-25	0.96	2.14	3.49	1.76	0.00	0.00	0.12	0.00	21.12	0.98	1.01	5.20	3.61	0.02
9-Feb-25	0.95	2.10	3.59	1.85	0.00	0.00	0.22	0.00	21.65	1.07	1.02	5.59	3.77	0.02
10-Feb-25	1.00	2.17	4.50	1.52	0.00	0.00	0.15	0.00	21.33	1.04	1.04	5.82	3.53	0.02
11-Feb-25	1.03	2.27	6.20	1.28	0.00	0.00	0.02	0.00	21.40	1.07	1.03	6.13	3.48	0.02
12-Feb-25	1.37	2.62	6.00	1.55	0.00	0.00	0.12	0.00	21.61	1.42	1.09	6.51	3.43	0.02
13-Feb-25	1.31	2.51	6.81	1.19	0.00	0.00	0.23	0.01	21.72	1.55	1.06	6.58	3.59	0.02
14-Feb-25	1.26	2.47	6.71	1.19	0.00	0.00	0.29	0.10	21.50	1.24	1.04	6.61	3.56	0.02
15-Feb-25	1.11	2.35	6.65	1.09	0.00	0.00	0.48	0.05	20.97	1.17	1.02	6.53	3.66	0.02
16-Feb-25	1.24	2.41	6.58	1.03	0.00	0.00	0.41	0.02	21.62	1.47	1.01	6.90	3.88	0.02
17-Feb-25	0.98	2.16	6.57	0.87	0.00	0.00	0.00	0.09	21.55	1.56	1.05	7.28	3.86	0.02
18-Feb-25	0.85	2.11	7.34	0.73	0.00	0.00	0.07	0.17	21.54	1.65	1.08	7.06	3.72	0.02
19-Feb-25	1.54	2.77	7.10	0.57	0.00	0.00	0.02	0.18	22.40	1.64	1.02	7.12	3.70	0.02
20-Feb-25	1.24	2.43	6.90	0.77	0.00	0.00	0.00	0.19	22.37	1.67	1.16	7.53	3.64	0.02
21-Feb-25	1.34	2.50	6.84	0.91	0.00	0.00	0.00	0.18	21.58	1.46	1.09	7.22	3.67	0.02
22-Feb-25	1.17	2.33	6.68	0.91	0.00	0.00	0.00	0.15	21.19	1.36	0.93	6.20	3.53	0.02
23-Feb-25	1.06	2.11	6.71	0.91	0.00	0.00	0.00	0.89	22.23	1.51	1.11	6.73	3.87	0.02
24-Feb-25	0.92	2.05	5.84	1.04	0.00	0.00	0.00	0.25	22.33	1.53	1.06	7.11	3.62	0.02
25-Feb-25	0.65	1.56	3.97	0.86	0.00	0.00	0.00	0.33	22.27	1.51	1.07	7.11	4.01	0.01
26-Feb-25	0.80	1.91	3.97	0.94	0.00	0.00	0.00	0.30	22.34	1.36	1.01	5.47	3.76	0.02
27-Feb-25	1.10	2.19	3.65	1.22	0.00	0.00	0.00	0.28	22.38	1.60	1.00	6.01	3.87	0.02
28-Feb-25	1.05	2.14	3.25	1.41	0.00	0.00	0.00	0.33	16.74	1.54	1.05	5.55	3.85	0.02
Total	**28.99**	**61.51**	**143.12**	**35.64**	**0.00**	**0.00**	**2.38**	**5.21**	**593.89**	**37.97**	**28.64**	**171.95**	**102.53**	**0.56**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – फ़रवरी 2025

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - FEBRUARY 2025

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

फ़रवरी 2025 FEBRUARY 2025			Apr'24- Feb'25	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	327	744	6575	26884
प.क्षे. WR	550	512	4562	5764
द.क्षे. SR	309	1336	3992	10771
पू.क्षे. ER	399	226	3846	12406
पूर्वोत्तर क्षे. NER	102	30	918	594
कुल TOTAL	1687	2848	19893	56417

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
अक्तूबर 2024 Oct'24	12567	8372	1511	2332
नवंबर 2024 Nov'24	11553	9432	1217	963
दिसम्बर 2024 Dec'24	12448	10602	1773	1468
जनवरी 2025 Jan'25	12932	9756	1984	2533
फ़रवरी 2025 Feb'25	11693	8852	1687	2848
कुल TOTAL	117488	98786	19893	56417

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
03.02.25 to 09.02.25	111.32	205.44	17.67	172.75	57.86
10.02.25 to 16.02.25	93.64	224.53	25.98	203.44	58.61
17.02.25 to 23.02.25	145.05	258.58	34.38	243.38	63.82
24.02.25 to 02.03.25	139.15	234.79	16.08	192.83	51.66

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES -FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. में) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED	उत्तरी क्षेत्र NR	9.58	0.00
2	ADANI GREEN ENERGY TWENTY FIVE LIMITED		49.58	0.00
3	ADANI GREEN ENERGY TWENTY FOUR LIMITED		51.64	0.00
4	ADANI GREEN ENERGY TWENTY FOUR LIMITED_infirm		9.46	0.00
5	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		25.78	0.00
6	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		9.07	0.00
7	AMP Energy Green Four Private Limited		6.71	0.00
8	Adept Renewable Technologies Private Limited		18.70	0.00
9	Amp Energy Green Six Private Limited		18.57	0.00
10	Amplus Ages Private Limited		1.80	0.00
11	Ayana Renewable Power Three Private Limited Infirm		0.32	0.00
12	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		0.59	0.00
13	Chandigarh (UT)		25.75	3.67
14	Delhi		299.89	72.52
15	Government of Himachal Pradesh _ Chamera1HEP		5.08	0.05
16	Government of Himachal Pradesh _ Chamera3HEP		2.65	0.10
17	Government of Himachal Pradesh_ CHAMERA2HEP		3.63	0.05
18	Government of Himachal Pradesh_BairasuilHEP		1.46	0.12
19	Government of Himachal Pradesh_Koldam HEP		8.77	0.28
20	Government of Himachal Pradesh_NJHPS		20.30	0.24
21	Government of Himachal Pradesh_Parbati3HEP		1.28	0.06
22	Government of Himachal Pradesh_RampurHEP		6.05	0.07
23	Grian Energy Private Limited		4.52	0.00
24	Haryana		383.44	58.71
25	Himachal Pradesh		32.44	44.07
26	IGSTPS JHAJJAR		1.30	0.00
27	JUNIPER GREEN COSMIC PRIVATE LIMITED		8.91	0.00
28	Jammu Kashmir		42.40	86.84
29	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		13.01	0.00
30	KHURJA STPP		2.20	0.00
31	NEA - UP STU		0.00	26.70
32	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	19.22
33	NTPC Dadri Stage I		9.18	0.00
34	NTPC Dadri Stage II		5.86	0.00
35	NTPC Rihand stage I		4.68	0.00
36	NTPC Rihand stage II		3.79	0.00
37	NTPC Rihand stage III		4.04	0.00
38	NTPC Singrauli		14.00	0.00
39	NTPC Tanda Stage II		11.20	0.00
40	NTPC Unchahar Stage I		2.94	0.00
41	NTPC Unchahar Stage II		3.46	0.00
42	NTPC Unchahar Stage III		2.27	0.00
43	NTPC Unchahar Stage IV		7.99	0.00
44	North Central Railway Prayagraj		0.00	10.05

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES -FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. में) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	Onevolt Energy Private Limited		7.24	0.00
46	Punjab		1.28	980.44
47	RENEW SURYA PRATAP PRIVATE LIMITED		37.90	0.00
48	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.31	0.00
49	Rajasthan		73.90	290.33
50	ReNew Surya Ravi Private Limited		36.93	0.00
51	SHREE CEMENT LIMITED TPS		18.76	4.01
52	Sainj HEP		3.78	0.00
53	Serentica Renewables India 4 Private Limited		1.92	0.00
54	Serentica Renewables India 5 Private Limited		22.47	0.00
55	Singoli Bhatwari HEP		8.00	0.00
56	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		3.17	0.00
57	TPSL 200MW TPTCL Banderwala		15.20	0.00
58	TPSL Banderwala SECI 100_INF		6.72	0.00
59	Transition Cleantech Services Private Limited		2.32	0.00
60	Transition Energy Services Private Limited		10.41	0.00
61	Transition Green Energy Private Limited		4.65	0.00
62	Transition Sustainable Energy Services One Private Limited		10.48	0.00
63	Uttar Pradesh		650.85	356.12
64	Uttarakhand		79.88	67.92
65	ACB (INDIA) LIMITED		49.26	0.13
66	ADANI GREEN ENERGY TWENTY SIX A LIMITED_PSS-3		2.27	0.00
67	ADANI PORTS AND SPECIAL ECONOMIC ZONE LIMITED (PSS-3)		34.14	0.00
68	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS-3 (162.5 MW Hybrid Solar of 187.5MW HPD)		33.28	0.00
69	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.67	0.00
70	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		2.78	0.00
71	ADANI RENEWABLE ENERGY FIFTY SEVEN LIMITED_PSS13		7.21	0.00
72	ADANI RENEWABLE ENERGY FIFTY SIX LIMITED_PSS9		2.82	0.00
73	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS-3		47.17	0.00
74	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS13		5.11	0.00
75	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED_PSS-1		170.37	0.00
76	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		51.71	0.00
77	AMBUJA CEMENTS LIMITED_PSS3		9.66	0.00
78	Adani Green Energy Twenty Five A Limited_PSS-2		71.96	0.00
79	Adani Green Energy Twenty Five B Limited_PSS-2		105.96	0.00
80	Adani Green Energy Twenty Four A Limited_PSS-3		19.32	0.00
81	Adani Green Energy Twenty Six B Limited_PSS-2		17.42	0.00
82	Adani Power Limited - Raigarh TPP		226.36	0.00
83	Adani Power Limited-Raipur TPP		468.46	3.00
84	Adani Renewable Energy Forty Eight Limited (Wind)_PSS-9		23.08	0.00
85	ArcelorMittal Nippon Steel India Limited		0.00	119.25
86	BHARAT ALUMINIUM COMPANY LTD		49.00	0.00
87	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	0.29
88	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		1.56	0.00
89	Chhattisgarh		105.46	147.04
90	D B Power Limited		84.24	0.00
91	DHARIWAL STU OTH		1.10	0.00
92	Daman and Diu - Dadra and Nagar Haveli		0.20	34.51
93	Dhariwal ISTS		11.74	0.00
94	GMR Warora Energy Limited		3.63	0.00
95	Goa WR		24.69	3.08

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES -FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. में) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
96	Gujarat	पश्चिमी क्षेत्र WR	121.99	826.73
97	Jaypee Nigrie Super Thermal Power Plant		134.80	0.00
98	Jhabua Power Limited		8.46	9.21
99	Jindal Power Limited, Stage-1		130.41	12.04
100	Jindal Power Limited, Stage-2		516.47	21.20
101	Jindal Steel & Power Ltd , DCPP		82.56	1.29
102	KSK MAHANADI POWER COMPANY LIMITED		16.77	0.00
103	LANCO AMARKANTAK POWER LIMITED		0.99	0.00
104	MAHAN ENERGEN LIMITED U#1		68.89	0.00
105	MAHAN ENERGEN LIMITED U#2		228.35	0.00
106	MB POWER (MADHYA PRADESH) LIMITED		85.67	5.75
107	Madhya Pradesh		109.15	103.46
108	Maharashtra		71.57	1241.60
109	Maruti Clean Coal and Power Limited		7.90	0.33
110	NREL-Dayapar Wind		4.84	0.00
111	NTPC Gadarwara		10.94	0.00
112	NTPC Jhanor Gandhar GPS		0.00	0.37
113	NTPC Kawas GPS		0.00	0.51
114	NTPC Korba Stage I &II		0.80	0.00
115	NTPC Korba Stage III		0.43	0.00
116	NTPC Lara Stage I		1.32	0.00
117	NTPC Mouda Stage I		7.63	0.00
118	NTPC Mouda Stage II		10.20	0.00
119	NTPC SAIL POWER COMPANY LIMITED		0.31	0.00
120	NTPC SOLAPUR SOLAR PV Station		1.57	0.00
121	NTPC Sipat Stage I		2.09	0.00
122	NTPC Sipat Stage II		1.04	0.00
123	NTPC Solapur		5.70	0.00
124	NTPC Vindhyachal Stage I		4.90	0.00
125	NTPC Vindhyachal Stage II		3.61	0.00
126	NTPC Vindhyachal Stage III		4.25	0.00
127	NTPC Vindhyachal Stage IV		5.33	0.00
128	NTPC Vindhyachal Stage V		2.65	0.00
129	NTPC khargone		8.43	0.00
130	R.K.M POWERGEN PRIVATE LIMITED		48.01	0.00
131	Ratnagiri Gas & Power Private Limited		0.00	3.07
132	SKS Power Generation Chhattisgarh Limited		10.16	8.24
133	Sasan Power Limited		4.77	0.00
134	TRN ENERGY PRIVATE LIMITED		51.84	0.00
135	The Tata Power Co Ltd (MTPS)		13.86	0.00
136	WIND FIVE RENERGY LIMITED		5.25	0.00
137	AM GREEN ENERGY PRIVATE LIMITED Solar		4.07	0.00
138	AM GREEN ENERGY PRIVATE LIMITED Wind		0.12	0.00
139	Andhra Pradesh		61.15	298.94
140	COASTAL ENERGEN PRIVATE LIMITED		12.93	0.00
141	Goa SR		0.01	7.55
142	IL&FS TAMIL NADU POWER COMPANY LIMITED		18.10	0.00
143	JINDAL POWER LIMITED SIMHAPURI		89.82	0.03
144	Karnataka		306.35	165.51
145	Kerala		15.66	269.83
146	MEENAKSHI ENERGY LIMITED		34.67	9.88

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES -FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. में) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
147	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION	दक्षिणी क्षेत्र SR	4.76	0.00
148	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		3.05	0.00
149	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.08	0.00
150	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		1.20	0.00
151	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		0.68	0.00
152	NLC Tamilnadu Power Limited		7.80	0.00
153	NTECL VALLUR		3.07	0.00
154	NTPC KUDGI		6.98	0.00
155	NTPC Ramagundam Stage I &II		10.16	0.00
156	NTPC Ramagundam Stage III		2.55	0.00
157	NTPC Simhadri Stage I		0.32	0.00
158	NTPC Simhadri Stage II		6.28	0.00
159	NTPC Talcher Super Thermal Power Station Stage II		8.46	0.00
160	NTPC Telangana		1.70	0.00
161	OSTRO KANNADA POWER PRIVATE LIMITED		7.87	0.00
162	Pondicherry UT		24.40	0.43
163	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		2.50	0.00
164	Ramagundam Floating solar		8.20	0.00
165	ReNew Surya Roshni Private Limited_Gadag		1.90	0.00
166	SEIL ENERGY INDIA LIMITED		102.02	0.00
167	SEIL Energy India Limited Project II		45.22	0.00
168	Serentica Renewables India 1 Private Limited		0.63	0.00
169	Simhadri FSP 15 MW		1.91	0.00
170	Simhadri Floating solar (10 MW)		1.03	0.00
171	Tamil Nadu		236.77	266.07
172	Telangana		39.73	2131.18
173	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	0.44	0.00
174	Bihar		807.06	1.00
175	Chuzachen HEP		0.01	0.00
176	Damodar Valley Corporation		99.69	192.46
177	Dikchu Hydro Electric Project (Sneha Kinetic Power Projects Pvt. Ltd.)		1.42	0.00
178	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	244.09
179	GMR KAMALANGA ENERGY LTD-CTU		2.02	0.00
180	IND BARATH ENERGY UTKAL LIMITED		32.45	32.29
181	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.02	0.00
182	Jharkhand		103.16	29.60
183	Jindal India Power Limited		52.68	0.00
184	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		0.42	0.00
185	KANTI BIJLEE UTPADAN NIGAM LIMITED		4.34	0.00
186	MAITHON POWER LIMITED		3.45	0.00
187	NABINAGAR POWER GENERATING COMPANY LIMITED		61.68	0.00
188	NEA - Bihar STU		0.00	78.19
189	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	167.43
190	NTPC BARH Stage II		40.79	0.00
191	NTPC Darlipali		5.35	0.00
192	NTPC Farakka stage I		103.59	0.00
193	NTPC Farakka stage III		29.60	0.00
194	NTPC Kahalgaon stage I		18.22	0.00
195	NTPC Kahalgaon stage II		27.68	0.00
196	NTPC North Karanpura STPS		8.09	0.00
197	NTPC Talcher Stage I		1.30	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES -FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. में) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
198	NTPP BRBCL		36.58	0.00
199	Odisha		329.93	84.92
200	Sikkim		6.65	0.03
201	Tashiding HEP, Shiga Energy Private Limited		0.01	0.00
202	West Bengal		220.97	209.77
203	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	10.44	0.00
204	ASSAM GAS BASED POWER STATION		8.25	0.00
205	Arunachal Pradesh		3.61	8.28
206	Assam		161.30	25.91
207	Bongaigaon Thermal Power Station NTPC		1.85	0.00
208	KAMENG HYDRO POWER STATION		6.97	0.00
209	Manipur		8.87	2.74
210	Meghalaya		4.09	53.31
211	Mizoram		0.23	0.13
212	Nagaland		6.38	5.96
213	Palatana Plant		1.39	0.00
214	Tripura		13.20	3.13
	Total		8851	8851

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : FEBRUARY 2025

RE Source & Unit wise break up (01.02.2025-28.02.2025)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	17	8	15	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1216	5	1000	1
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1233**	**13**	**1015**	**2**

RECs Issued (01.02.2025-28.02.2025)

Sr.No.	Non Solar	Solar	Total
1	257181	113891	371072

Redemption of REC (01.02.2025-28.02.2025)

Sr.No.	Non Solar	Solar	Total
1	2764705	70807	2835512

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : FEBRUARY 2025

RE Source & Unit wise break up (Apr'24-Feb'25)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	378	20	92	12
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	2494	27	1268	23
5	Small Hydro	24	1	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**2896**	**48**	**1396**	**37**

RECs Issued (Apr'24-Feb'25)

Sr.No.	Non Solar	Solar	Total
1	40127845	1087411	41215256

Redemption of REC (Apr'24-Feb'25)

Sr.No.	Non Solar	Solar	Total
1	27174693	363202	27537895

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : FEBRUARY 2025

RE Source & Unit wise break up Since Inception to Feb'25

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3425	544	2985	537
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	4122	597	2743	504
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**9657**	**1315**	**7385**	**1178**

RECs Issued since Inception to Feb'25

Sr.No.	Non Solar	Solar	Total
1	155232883	14627789	169860672

Redemption of REC since Inception to Feb'25

Sr.No.	Non Solar	Solar	Total
1	105679022	12812459	118491481

REC Closing balance as on 28.02.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of Feb 2025 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	Uttarakhand	01-02-2025 09:01	01-02-2025 10:57	01:56	0	0	0.000	0.000	50216	60207	i)220KV Khodri(UK) generating station has 4 generating units of 30MW each and has double main bus scheme. The power is evacuated mainly through 220kV Khodri(UK)-Majri(HP) (UK) Ckt-1 & 2, 220kV Saharanpur(UP)-Khodri(UK) (UP) Ckt, 220KV Khodri – Sarsawan Ckt, 220KV Khodri – Jhajra Ckt and 220KV Khodri – Chibro Ckt-1 & 2. ii)As reported, at 09:01 hrs, while stopping of 30MW Unit-4 at Khodri(UK), its R-phase pole of CB stucked and the trip coil of R-phase burnt. Due to this, pole discrepancy operated which as per logic, led to LBB protection operation resulting in tripping of 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2, 220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt and 220 KV Khodri - Chibro (UK) Ckt-2. iii)As per PMU at Dehradun(PG), no fault was found in the system. iv)As per SCADA, no change in demand/generation in Uttarakhand control area was observed. v)As reported by SLDC-UK, testing of Generator CB of Unit -4 by expert service engineer has been carried out and fault has been rectified. As remedial action taken, the stuck pole of R-phase was opened manually and the control valve assembly was replaced with a new one.	i)220 kV Saharanpur(UP)-Khodri(UK) (UP) Ckt ii)220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 iii)220 KV Khodri - Chibro (UK) Ckt-2
2	GI-2	Himachal Pradesh	03-02-2025 03:57	03-02-2025 05:11	01:14	157	0	0.600	0.000	26154	36145	i)220KV Bhakra(BBMB) generating station has 6 generating units of 157MW each. Unit-I , VI and VII were connected to Bus-I of 220KV along with 220 KV Bhakra_R-Ganguwal (BB) Ckt-2 and 220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 . ii)During the antecedent condition only Bhakra HPS - UNIT 6 was operational and generating 157MW. 220 KV Bhakra_R-Ganguwal (BB) Ckt-2 and 220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 were carrying 1 MW and 48MW of load respectively. iii)As reported, at 03:57 hrs, R-N phase to earth fault occurred in 220 kV Bhakra- Jamalpur Ckt-2. At the same time Bus Bar protection for 220KV Bus-I operated. This led to tripping of 220KV Bus-I, 220 KV Bhakra_R-Ganguwal (BB) Ckt-2, 220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 and 157 MW Bhakra HPS - UNIT 6 (Details Awaited) iv)As per PMU at Bhakra(BBMB), R-N phase to earth fault was found in the system. v)As per SCADA, approx 157 MW hydro generation loss is observed at 220 kV Bhakra Dam S/S.	i)220 KV Bhakra_R-Ganguwal (BB) Ckt-2 ii)220KV Bus 1 at Bhakra_R(BB) iii)220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 iv)157 MW Bhakra HPS - UNIT 6
3	GI-2	Himachal Pradesh	03-02-2025 19:35	03-02-2025 23:24	03:49	177	0	0.412	0.000	43002	57934	i)Total generated power of Sainj HEP(HP), Parbati_2(NH) and parbati_3(NH) evacuates through 400 kV Parbati_2(NH)- Banala(PG) (PKTCL) Ckt and 400 kV Parbati_3(NH)- Banala(PG) (PKTCL) Ckt via 400 KV Parbati_2(NH)-Sainj(HP) (PKTCL) Ckt and 400 KV Parbati_3(NH)-Sainj(HP) (PKTCL) Ckt. ii)During antecedent condition, only 50MW Unit-1 at Sainj HEP(HP) was running (generating approx. ~45MW) and 130MW Unit-4 at Parbati-3 HEP(NHPC) (generating approx. ~132MW). iii)As reported, at 06:31 hrs, R-N fault occurred on 400 KV Parbati_3(NH)-Sainj (HP) (PKTCL) Ckt-1 in Z-2 and fault current was 2.92 KA from Sainj end. iv)As per DR of the line of Parabati3 end, fault was sensed in Z-1 and tripping command to R-ph CB was given. However, R-ph pole failed to open leading to operation of LBB protection. This led to tripping of all the elements connected to the Bus (Tripping details awaited) and complete blackout of 400KV Parbati-3 s/stn occurred. v)As per PMU, R-N fault with delayed clearance of fault in 400msec is observed. vi)During this event, Approx 132 MW hydro generation loss is observed at Parbati-III and 45 MW hydro generation loss is observed at Sainj. (As per SCADA).	i)400 KV Parbati_2(NH)-Sainj(HP) (PKTCL) Ckt-1 ii)400 KV Parbati_3(NH)-Parbati Pooling Banala(PG) (PKTCL) Ckt-1 iii)400 KV Parbati_3(NH)-Sainj(HP) (PKTCL) Ckt-1
4	GI-1	Himachal Pradesh	05-02-2025 18:45	05-02-2025 18:56	00:11	427	0	0.882	0.000	48394	59037	i)220KV Bhakra(BBMB) generating station has 6 generating units of 157MW each. Unit-I , VI and VII were connected to Bus-I of 220KV along with 220 KV Bhakra_R-Ganguwal (BB) Ckt-2 and 220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 . ii)During the antecedent condition only Bhakra HPS - UNIT 6 and 7 were operational and generating 156MW and 157MW respectively. 220 KV Bhakra_R-Ganguwal (BB) Ckt-2 and 220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 were carrying 33 MW and 110MW of load respectively. iii)As reported, at 03:57 hrs, Bus Bar protection for 220KV Bus-I operated. This led to tripping of 220KV Bus-I, 220 KV Bhakra_R-Ganguwal (BB) Ckt-2, 220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 and 157 MW Bhakra HPS - UNIT 6 and 7(Details Awaited) iv)As per PMU at Bhakra(BBMB), Y-N phase to earth fault was found in the system. v)As per SCADA, approx 427 MW hydro generation loss is observed at 220 kV Bhakra Dam S/S.	i)220 KV Bhakra_R-Ganguwal (BB) Ckt-2 ii)220KV Bus 1 at Bhakra_R(BB) iii)220 KV Bhakra_R(BB)-Mahilpur(PS) (PS) Ckt-2 iv)157 MW Bhakra HPS - UNIT 6 v)157 MW Bhakra HPS - UNIT 7
5	GI-2	Rajathan	08-02-2025 20:54	08-02-2025 21:40	00:46	0	170	0.000	0.318	40180	53479	i)400/220KV Ajmer substation has One and half breaker scheme in 400KV and Double Main & Transfer bus scheme in 220KV system. ii)During antecedent condition, 400 KV AJMER-BHILWARA (RS) CKT-2 was carrying 23MW, 400/220 KV 315 MVA ICT 1 & 3 were loaded 214 and 223MW each. iii)As reported, at 20:54 hrs, B-N fault occurred on 400 KV AJMER-BHILWARA (RS) CKT-2. As per DR/ EL, two B-N faults occurred. The fault was detected in Z1 and the fault current was 3.88KA. iv)However, at the same time 400/220KV ICT-1 and ICT-3 tripped. As per DR/EL of ICT-1 & 3, 50-N (High Set Overcurrent Earth fault) and 67-N (Directional Overcurrent earth Fault) operated respectively. v)SLDC Rajasthan confirmed that due to low current relay settings of 50N and 67N on ICT 1 & 3, both elements picked up the current earth fault of 400 KV AJMER-BHILWARA (RS) CKT-2 and tripped. RVPNL has confirmed that relay settings have been corrected. vi)During this event, approx 170 MW of demand change was observed in Rajasthan control area. (As per SCADA).	i)400/220 KV 315 MVA ICT 1 AT AJMER(RS) ii)400/220 KV 315 MVA ICT 3 AT AJMER(RS) iii)400 KV AJMER-BHILWARA (RS) CKT-2
6	GI-2	Uttar Pradesh	09-02-2025 00:54	09-02-2025 01:57	01:03	0	0	0.000	0.000	33452	40621	i)400/220/132kV Muradnagar-New(UP) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii)As reported, at 00:54 hrs, 400kV Muradnagar_2-Mathura (UP) Ckt tripped on Y-N phase to earth fault with fault current of 4.084kA from Muradnagar_2 end and fault clearing time of 287 ms; zone-1 distance protection operated (as per DR at Muradnagar_2 end) and DT received at Mathura end (as reported). iii)Due to delayed opening of CB at Muradnagar_2 end of 400kV Muradnagar_2-Mathura (UP) Ckt, LBB protection operated and both main and tie CBs at Muradnagar_2 end of 400 KV MURADNAGAR_2-MATHURA (UP) CKT-1 opened and all the 400kV CBs connected at 400KV Bus-1 of Muradnagar_2 tripped. DT received at remote ends (as reported). iv)As per PMU at Muradnagar1(UP), Y-N phase to earth fault with delayed fault clearing time of 280ms is observed. v)As per SCADA, no change in demand is observed in UP control area.	i)400 KV MURADNAGAR_2-MATHURA (UP) CKT-1 ii)400KV BUS 1 AT MURADNAGAR_2(UP)
7	GI-1	Haryana	11-02-2025 21:13	11-02-2025 23:20	02:07	0	112	0.000	0.216	39527	51916	i)220KV Hissar Sub-station has double main bus system. ii)During antecedent condition, 220 KV Hissar IA(HV) – Narwana Ckt, 220 KV Hissar IA – Masudpur Ckt 1 & 2, 220/132 KV 100 MVA ICT-1 & 160 MVA ICT-2 were connected to 220kV Bus-1 at Hissar IA(HV) and 220 KV Hissar(PG)-Hissar IA(HV) (PG) Ckt-1 & 2 and 220 KV Hissar(BB)-Hissar IA(HV) (HVPNL) Ckt-1 & 2 were connected to 220kV Bus-2 at Hissar IA(HV). 220 kV Bus Coupler at Hissar IA(HV) was in open condition. iii)As reported, at 21:13hrs, Y- phase CT of 220 KV Hissar(BB)-Hissar IA(HV) (BBMB) Ckt-2 got damaged with a heavy blast which caused collateral damage to 220kV L&E isolator. iv)220 KV Hissar(BB)-Hissar IA(HV) (BBMB) Ckt-2 tripped on distance protection operation (zone-1, fault distance=0 km from Hissa IA end; zone-2, fault current=5.18kA and fault distance-=4.06km from Hissar(BB)). v)During the same time, busbar protection operated at 220kV Bus-2 at Hissar IA(HV) end and all the elements connected to Bus-2 tripped. vi)As per PMU at Hissar(PG), Y-N phase to earth fault with fault clearing time of 80ms is observed. vii)As per SCADA, change in demand of approx. 112MW was observed in Haryana control area.	i)220 KV Hissar(BB)-Hissar IA(HV) (BBMB) Ckt-2 ii)220 KV Hissar(BB)-Hissar IA(HV) (HVPNL) Ckt-1 iii)220 KV Hissar(PG)-Hissar IA(HV) (PG) Ckt-2 iv)220 KV Hissar(PG)-Hissar IA(HV) (PG) Ckt-1 v)220 KV Hissar IA(HV) Bus-2

Details of Grid Events during the Month of Feb 2025 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD-1	Delhi	45703.39931	45703.41667	91406.017	0	194	0	0.298825	54149	64921	i)220kV Narela(DTL) S/s has double main bus arrangement at 220kV level. 220/132kV 50MVA ICT-1 and 100MVA ICT-2 at Narela(BB) are connected on the same extended Bus of 220KV Narela(DTL). ii)During antecedent condition, 220 KV Panipat(BB)-Narela(DV) (BBMB) Ckt-1, 2 & 3, 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1& 2 and 220/66kV 100 MVA ICT-1, 2 and 3 at Narela(DTL) were connected to 220kV Bus-1 at Narela(DTL) and 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 & 2, 220 KV DSIDC Bawana-Narela(DV) (DTL) Ckt-1 & 2 and 220/132kV 50MVA ICT-1 and 100MVA ICT-2 at Narela(BB) were connected to 220kV Bus-2 at Narela(DTL). 220kV Bus coupler at Narela(DTL) was in OFF position. iii)As reported, sequence of event is as follows: a.At 09:19 hrs, both CBs at 220kV side of 220/132kV 50MVA and 100 MVA ICT-1 & 2 at Narela(BB) were manually opened for 220kV Bus Isolator changeover operation from Bus-2 to Bus-1. b.At 09:30 hrs, 89A Bus-1 Isolator of 220/132kV 100MVA ICT-2 at Narela(BB) was closed. c.Since the 220kV Bus Coupler CB at Narela(DTL) was already in OFF position since 08.09hrs, the said closure of 89A isolator with 89B Isolator already closed of 220/132kV 100MVA ICT-2 at Narela(BB) resulted in a position to function as a 220kV Bus Coupler. d.At 09:34 hrs, 89B Bus-2 isolator of 220/132kV 100MVA ICT-2 at Narela(BB) was tried to open, but the operation could not be done completely due to 89B isolator struck in between and heavy arcing flames evolved due to said ON load 89B isolator opening operation. e.It caused ionization in air around 89B isolator of 220/132kV 100MVA ICT-2 at Narela(BB) and R-B-N double phase to earth fault occurred due to arcing via isolator structure. f.This resulted in zone-2 busbar protection operation (as confirmed from DR) and all the elements connected to 220kV Bus-2 at Narela(DTL) tripped. g.Since 89B isolator opening operation was not complete, fault continued to be fed from Bus-1 through 220 KV Panipat(BB)-Narela(DV) (BBMB) Ckt-1, 2 & 3 via 89A Bus-1 Isolator of 220/132kV 100MVA ICT-2 at Narela(BB) to faulty 89B Bus-2 Isolator. This led to zone-1 busbar protection operation (as confirmed from DR) and all the elements connected to 220kV Bus-1 at Narela(DTL) also tripped and complete blackout occurred at 220kV Narela(DTL). iv)As per DR at Narela(DTL), Zone 2 Bus Bar protection operated followed Zone 1 Bus Bar protection operation. v)As per PMU at Maharani Bagh(PG), Y-N phase to earth fault followed by Y-B phase to phase fault with fault clearing time of 120msec and 80msec is observed. vi)As per SCADA, change in demand of approx. 58 MW is observed in Delhi control area. However, SLDC-Delhi has reported load loss of approx. 194 MW.	i)220 KV Panipat(BB)-Narela(DV) (BBMB) Ckt-1, 2 & 3 ii)220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 & 2 iii)220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1& 2 iv)220 KV DSIDC Bawana-Narela(DV) (DTL) Ckt-1 & 2 v)220 kV Bus-1 and Bus-2 at Narela(DTL) vi)220/66kV 100 MVA ICT-1, 2 and 3 at Narela(DTL)
9	GD-1	Rajathan	15-02-2025 06:55	15-02-2025 07:56	01:01	228	0	0.496	0.000	45992	54927	i)Generation of 220kV AHEJ4L(IP) station evacuates through 220 KV Adani Renew Park SL_FGARH_FBTL (AREPRL)-AHEJ4L PSS 4 HB_FGRAH_FBTL (AHEJ4L) (AREPRL) Ckt. During antecedent condition, at 220kV AHEJ4L PSS 4 station was generating approx. 228 MW (as per PMU). ii)As reported, at 06:55hrs, transient B-N phase to earth fault occurred at 220 KV Adani Renew Park SL_FGARH_FBTL (AREPRL)-AHEJ4L PSS 4 HB_FGRAH_FBTL (AHEJ4L) (AREPRL) Ckt and line successfully auto-reclosed. iii)However, during the same time, 220/33 kV 150 MVA ICT 1 and 2 at AHEJ4L PSS 4 HB_FGRAH_FBTL (AHEJ4L) tripped (Exact reason and nature of protection operated yet to be shared) which led to complete blackout out of 220kV AHEJ4L PSS4(IP) S/s. iv)As per PMU at Fatehgarh_2(PG), B-N phase to earth fault (voltage dipped upto 0.87 p.u.) is observed with fault clearing time of 120ms. v)As per PMU at AWPS2(IP), wind generation loss of approx. 228 MW is observed at AHEJ4L PSS4(IP).	i)220/33 kV 150 MVA ICT 1 at AHEJ4L PSS 4 HB_FGRAH_FBTL (AHEJ4L) ii)220/33 kV 150 MVA ICT 2 at AHEJ4L PSS 4 HB_FGRAH_FBTL (AHEJ4L)
10	GD-1	Rajathan	16-02-2025 14:27	16-02-2025 16:15	01:48	90	0	0.174	0.000	51756	54965	i)Generation of 220kV JGCPL(IP) station evacuates through 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt. During antecedent condition, 220kV JGCPL(IP) station was generating approx. 90 MW. ii)As reported, at 14:27hrs, 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt tripped on B-N phase to earth fault due to differential protection operation (exact reason and location of fault yet to be shared). iii)Due to tripping of 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt, JGCPL(IP) S/s lost its connectivity from grid and blackout occurred at 220kV JGCPL(IP)S/s. iv)As per PMU at Bikaner_2(PG), B-N phase to earth fault (voltage dipped upto 0.75 p.u.) with unsuccessful A/R is observed with fault clearing time of 80ms. After the fault clearance voltage increased upto 1.04 p.u. v)As per PMU, solar generation loss of approx. 90 MW is observed respectively at JGCPL(IP). vi)As per SCADA, dip in ISTS total solar generation of approx. 211 MW is observed.	i) 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt
11	GI-I	J&K	17-02-2025 14:54	17-02-2025 14:59	00:05	0	210	0.000	0.371	54206	56622	i)220/132kV Delina substation has Double main and transfer bus scheme. ii)During antecedent condition, 220kV Amargarh (INDIGRID) –Delina(JK) D/C was carrying 106 MW each and feeding Delina load. iii)As reported, at 14:54 hrs, 132KV Delina – Pattan line tripped due to broken jumper condition while returning the same line from shutdown (exact reason, nature and location of fault need to be shared). iv)During the same time, 220/132kV 160MVA ICT -1 at Delina(JK) tripped on earth fault (exact nature of protection operated need to be shared). v)Subsequently, this led to overloading of 220/132kV 160MVA ICT -2 & 3 at Delina(JK) and got tripped on over-current protection operation. vi)As per PMU at Amargarh (INDIGRID), R-Y-B 3 phase to earth fault with fault clearing time of 80 msec is observed. vii)As per SCADA, change in demand of approx. 210 MW is observed in J&K control area.	i) 220/132kV 160MVA ICT -1 at Delina (JK) ii) 220/132kV 160MVA ICT -2 at Delina (JK) iii) 220/132kV 160MVA ICT -3 at Delina (JK)
12	GI-2	UP	22-02-2025 17:18	22-02-2025 18:40	01:22	0	106	0.000	0.209	47874	50657	i)400/220kV Moradabad(UP) has double main and transfer bus scheme in both 400KV and 220KV system. 220/132KV Moradabad-2(UP) was connected to the same 220kV bus as that of 400/220kV Moradabad(UP). ii)During the antecedent condition, 400/220 KV 500 MVA ICT 1 at Moradabad(UP), 220/132 KV 160 MVA ICT 2 & ICT 3 at Moradabad-2(UP) were carrying 79MW, 20MW and 20MW. 400/220 KV 240 MVA ICT 3 at Moradabad(UP) was under shutdown. iii)As reported, at 17:18hrs, fault occurred in 132KV Moradabad-2 – Golbari Ckt (Exact reason, nature and location of fault yet to be shared). iv)Since the fault wasn't cleared at 132KV level, it propagated further into 220KV system which led to Bus Bar protection operation at both 220kV Bus-1 & 2 at Moradabad-2(UP) and all the elements connected to both the 220kV buses at Moradabad-2(UP) tripped. v)As per PMU at Bareilly(PG), Y-B phase to phase fault is observed with fault clearing time of 80ms. vi)As per SCADA, change in demand of approx. 106MW is observed in UP control area.	i) 400/220 KV 500 MVA ICT 1 at Moradabad(UP) ii) 220/132 KV 160 MVA ICT 2 at Moradabad-2(UP) iii) 220/132 KV 160 MVA ICT 3 at Moradabad-2(UP) iv) 220KV Moradabad-2 – Amroha (UP) Ckt v) 220KV Muradabad-2 – Sambhal (UP) Ckt

Details of Grid Events during the Month of Feb 2025 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
13	GD-1	Rajasthan	23-02-2025 18:05	23-02-2025 23:18	05:13	29	0	0.068	0.000	42623	49032	i)Generation of 400kV Azure43(IP) (both PSS and RS) evacuates through 400 KV Bikaner(PG)-AzurePSS43 SL_BKN_PG(Azure) (Azure) Ckt. ii)During antecedent condition, Azure43(IP) was generating approx. 29 MW (as per PMU). iii)As reported, at 18:05hrs, 400 KV Bikaner(PG)-AzurePSS43 SL_BKN_PG(Azure) (Azure) Ckt tripped due to DT received at Bikaner(PG) end. (Exact reason yet to be shared) iv)During the same time, 400 KV AzurePSS43 SL_BKN_PG-AzureRS43 SL_BKN_PG (Azure) Ckt, 400/33 kV 150 MVA ICT 1 & 2 at AzurePSS43 SL_BKN_PG(Azure) and 400/33 kV 150 MVA ICT 1 & 2 at AzureRS43 SL_BKN_PG(Azure) also tripped due to loss of evacuation path (Exact reason and nature of protection operated yet to be shared). This led to complete blackout of 400kV Azure43(IP) S/s. v)As per PMU at Bikaner(PG), no fault was observed in the system. vi)As per PMU at Azure43(IP), solar generation loss of approx. 29 MW is observed.	i) 400 KV Bikaner(PG)-AzurePSS43 SL_BKN_PG(Azure) (Azure) Ckt ii) 400 KV AzurePSS43 SL_BKN_PG-AzureRS43 SL_BKN_PG (Azure) Ckt iii) 400/33 kV 150 MVA ICT 1 at AzurePSS43 SL_BKN_PG(Azure) iv) 400/33 kV 150 MVA ICT 2 at AzurePSS43 SL_BKN_PG(Azure) v) 400/33 kV 150 MVA ICT 1 at AzureRS43 SL_BKN_PG(Azure) vi) 400/33 kV 150 MVA ICT 2 at AzureRS43 SL_BKN_PG(Azure)
14	GD-1	Haryana	45715.34097	45715.4	91430.059	0	414	0	0.745234	46503	55553	i)400kV Daulatabad(HV) has one and half breaker bus scheme in 400KV and double main bus transfer for 220KV system. ii)During the antecedent condition, 400 KV GURGAON(PG)-DAULATABAD(HV) (HV) CKT-1&2, 400 KV JHAJJAR(APCL)-DAULATABAD(HV) (HV) CKT-1 & 2 and 400kV DAULTABAD-DHANONDA CKT-1&2 were carrying 228MW (each circuit), 353MW (each circuit) and 138MW (each circuit) respectively. iii)As reported, at 08:11hrs, B-N fault occurred on 400 KV GURGAON(PG)-DAULATABAD(HV) (HV) CKT-2. On this fault, line successfully autoreclosed from Gurgaon(PG) end but CB at Daulatabad end failed to open. During patrolling, flag was found wrapped on phase conductor at tower location no. 54-55. iv)During inspection, both trip coils of 400 KV GURGAON(PG)-DAULATABAD(HV) (HV) CKT-2 at Daulatabad end were found burnt. v)As CB at Daulatabad end failed to open, LBB of Gurgaon Bay should have operated. However, LBB protection also didn't operate. During the inspection, it was found that bus bar relay was in error mode. vi)Further, all the 400kV lines i.e., 400 KV GURGAON(PG)-DAULATABAD(HV) (HV) CKT-1, 400 KV JHAJJAR(APCL)-DAULATABAD(HV) (HV) CKT-1 & 2 and 400kV DAULTABAD-DHANONDA CKT-1&2 tripped on operation of distance protection in Z-2. vii)Further, 400/220kV 315MVA ICT-1,2,3&4 at Daulatabad(HR) tripped on operation of non-directional O/C E/F protection operation and fault got cleared. Tripping of all the elements led to blackout of the 400/220kV Daulatabad(HR) S/s. viii)As per PMU at Gurgaon(PG), B-N phase to earth fault with delayed clearance of ~1080 msec is observed. ix)As per SCADA, change in demand of approx. 414MW is observed in Haryana control area. x)As reported, fault trip coils have been replaced and bus bar relay was reboot. Bus bar relay is working properly however it has been kept under observation and feedback has been given to relay OEM for review of relay.	i)400 KV GURGAON(PG)-DAULATABAD(HV) (HV) CKT-2 ii)400/220 KV 315 MVA ICT 1 AT DAULATABAD(HV) iii)400/220 KV 315 MVA ICT 2 AT DAULATABAD(HV) iv)400/220 KV 315 MVA ICT 3 AT DAULATABAD(HV) v)400/220 KV 315 MVA ICT 4 AT DAULATABAD(HV) vi)400 KV JHAJJAR(APCL)-DAULATABAD(HV) (HV) CKT-2 vii)400 KV JHAJJAR(APCL)-DAULATABAD(HV) (HV) CKT-1 viii)400 KV GURGAON(PG)-DAULATABAD(HV) (HV) CKT-1
15	GD-1	Rajasthan	28-02-2025 11:52	28-02-2025 12:50	00:58	140	0	0.270	0.000	51922	57710	i)Generation of 220kV JUNIPER GREEN COSMIC Pvt Ltd (JGCPL)(IP) evacuates through 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt-1 and 220KV JGCPL_SL_BIK2_PG (Juniper_NEPL) – MSEEPL Ckt. ii)During antecedent condition, 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt-1 was carrying approx. 140 MW of load (as per PMU) and 220KV JGCPL_SL_BIK2_PG (Juniper_NEPL) – MSEEPL Ckt was in shutdown. iii)As reported, at 11:52hrs, 220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt tripped due to relay malfunctioning. (Exact reason yet to be shared) iv)Due to tripping of the line, complete RE generation of JGCPL(IP) got affected due to loss of evacuation path. v)As per PMU at JGCPL(IP), no fault was observed in the system. vi)As per PMU at JGCPL(IP), solar generation loss of approx. 140 MW is observed.	220 KV Bikaner_2 (PBTSL)-JGCPL_SL_BIK2_PG (Juniper_NEPL) Ckt-1
16	GI-1	J&K	28-02-2025 03:30	28-02-2025 06:48	03:18	0	126	0.000	0.344	31699	36679	i)220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. 220kV Amargarh-Ziankote ckt-1&2 are on the same tower (D/C tower) and line length is ~21.4km. ii)During antecedent condition, 220kV Amargarh (INDIGRID) –Ziankote (JK) ckt-2 was carrying 139 MW and feeding Ziankote load. 220kV Amargarh (INDIGRID) –Ziankote (JK) ckt-1 was already tripped at 02:40 hrs on R-N fault. iii)As reported, at 03:30 hrs 220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2 also tripped on R-N fault (details of cause of fault and location of fault yet to be received). iv)As per PMU at Amargarh (INDIGRID), no fault was observed in system. v)As per SCADA, change in demand of approx. 126 MW is observed in J&K control area.	i)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-1 ii)220 KV Amargarh (INDIGRID)-Ziankote(JK) (PDD JK) Ckt-2

Details of Grid Events during the Month of Feb 2025 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	13:12 / 07-02-2025	14:30 / 07-02-2025	01:18	-	541	-	0.75%	82721	72287	At 13:12 Hrs / 07-02-2025, 400 kV Nagothane-Dabhol-2 tripped on R-Y phase fault due to agriculture fire between tower location 150-160. Due to non operation of primary and backup protection, the fault was cleared after 1147 msec on Backup Earthfault Protection of ICTs. After 10 minutes, 220 kV Nagothane became dead at 13:22 Hrs / 07-02-2025 due to tripping of lines from remote end and 400/220 kV Nagothane substation became dead. Load loss of 541 MW occurred at Nagothane area (Maharashtra) due to the event.	Tripping of following Elements: 1 400kV Nagothane-Padghe-1 2 400kV Nagothane-Padghe-2 3 400kV RGPPL-Nagothane-1 4 400kV RGPPL-Nagothane-2 5 400/220 kV Nagothane ICT-1 6 400/220 kV Nagothane ICT-2 7 400/220 kV Nagothane ICT-3
2	GD-1	WR	17:10 / 10-02-2025	18:38 / 10-02-2025	01:28	-	-	-	-	81205	72568	At 17:10 hrs 220kV Umariya (Agar Unit-5) Pachora ckt tripped from Umariya (Agar) end only. No indications observed. No generation loss recorded as the tripping occurred in non solar hours.	Tripping of following Elements: 1. 220kV Umariya (Agar)-Pachora ckt
3	GD-1	WR	19:09 / 10-02-2025	21:34 / 10-02-2025	02:25	-	-	-	-	78849	69066	Jamkhambaliya had requested emergency outage of 220KV-JAMKHAMBALIYA-MANJA for attending SF6 gas pressure low in 203 main breaker at Jamkhambaliya end. Shutdown was availed at 15:20 hrs. After completion of work, line normalised at 18:46 hrs. However at 19:09 hrs. at 220kV Manja end, while charging 220/33kV ICT, the line tripped due to earth fault. Manja has informed that its 202 main breaker of 220/33kV ICT is under forced outage since 06th March 2024. Since then, 220/33kV Manja ICT was kept charged through TBC bay 201. DT has been received at Jamkhambaliya end. There is no generation loss due to this tripping.	Tripping of following Elements: 1 220KV-Jamkhambaliya-Manja 2 220/33kV Manja ICT
4	GD-1	WR	10:25 / 11-02-2025	12:14 / 11-02-2025	01:49	340	-	0.39%	-	87327	79157	At 10:25 hrs 220kV Umariya (Agar Unit-5) Pachora ckt tripped from Umariya (Agar) end only. No indications observed. 330-340MW generation loss recorded due to the loss of evacuation path.	Tripping of following Elements: 1. 220kV Umariya (Agar)-Pachora ckt
5	GD-1	WR	16:28 / 11-02-2025	18:20 / 11-02-2025	01:52	162	-	0.19%	-	83126	74840	At 16:28 hrs 220kV Umariya (Agar Unit-5) Pachora ckt tripped from Umariya (Agar) end only. No indications observed. 162 MW generation loss recorded due to the loss of evacuation path.	Tripping of following Elements: 1. 220kV Umariya (Agar)-Pachora ckt
6	GD-1	WR	16:28 / 11-02-2025	18:20 / 11-02-2025	01:52	111	-	0.13%	-	83126	74840	At 16:28 hrs 220kV Ladwan (Agar Unit-5) Pachora ckt tripped from Ladwan (Agar) end only. Planned outage of 220 KV main bay (204) of 220 KV Ladwan Pachora at Pachora end was availed at 10:27 hrs and normalized at 16:27 hrs. At 16:28 hrs, DT was sent from Pachora SS to Ladwan which is suspected to be extended while changing Bay from Transfer mode to Local Mode. 111 MW generation loss recorded due to the loss of evacuation path.	Tripping of following Elements: 1. 220 kV Agar4(Ladwan)-Pachora ckt
7	GD-1	WR	10:11 / 12-02-2025	11:11 / 12-02-2025	01:00	280	-	0.31%	-	89569	77923	At 10:11 hrs 220kV Umariya (Agar Unit-5) Pachora ckt tripped from Umariya (Agar) end only. No indications observed. 280 MW generation loss recorded due to the loss of evacuation path	Tripping of following Elements: 1. 220kV Umariya (Agar)-Pachora ckt
8	GD-1	WR	10:11 / 12-02-2025	11:14 / 12-02-2025	01:03	138	-	0.15%	-	89569	77923	At 10:11 hrs 220kV Ladwan ICTs 1&2 tripped while availing the planned outage of 220kV Pachora Bus Coupler at 220kV Pachora.. 138 MW generation loss recorded due to the loss of connected 2 ICTs.	Tripping of following Elements: 1. 220 kV Agar4(Ladwan)-Pachora ckt

Details of Grid Events during the Month of Feb 2025 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GI-2	WR	20:42 / 13-02-2025	21:12 / 13-02-2025	00:30	-	-	-	-	74646	63241	At 20:42 hrs/13.02.2025, during relay testing of 765kV Lakadiya Bus-2 (which was already in planned outage), 765kV Lakadiya Bus-1 got tripped. This resulted in tripping of 765kV Lakadiya – Banaskantha-1, 765/400kV Lakadiya ICTs -1&2 and 765kV Lakadiya Bus reactor. 765kV Lakadiya Vadodara Double Circuit lines remained in service, with power flow redirected through the 765kV Bhuj-II Double Circuit via Tie bays.	Tripping of following Elements: 1 765kV Lakadiya Bus-1 2 765kV Lakadiya – Banaskantha -1 3 765/400kV Lakadiya ICTs 1 4 765/400kV Lakadiya ICTs 2 5 765kV Lakadiya Bus reactor
10	GD-1	WR	15:45 / 15-02-2025	19:02 / 15-02-2025	03:17	114		0.14%	-	81824	73847	At 15:45 Hrs/ 15-02-2025, 220 kV Pritamnagar- Indore tripped on R-E fault & resulted in blackout of 220 kV Pritamnagar substation due to radial feeder . Generation loss of 114 MW occurred due to the event.	Tripping of following Elements: 1. 220 kV Pritamnagar- Indore
11	GD-1	WR	15:45 / 15-02-2025	22:52 / 27-02-2025	295:07	97		0.13%	-	75035	60746	At 21:13 Hrs/15-02-2025, 220kV Bhuj-Gadhsisa S/C tripped due to B-Y fault, which resulted in loss of evacuation path. After patrolling team found EHV Line Tower No: 15/3 damaged from top section due to conductor theft case at fault location. About 97 MW generation loss occurred at 220 KV Gadhsisa WPP.	Tripping of following Elements: 1. 220kV Bhuj-Gadhsisa
12	GD-1	WR	11:42 / 22-02-2025	12:09 / 22-02-2025	00:27	-	346	-	0.45%	84237	76472	At 11:42Hrs/22-02-2025, 220kV Kolhapur Bus-1 tripped due to LBB operated at 220 kV Bidri CB at 400 kV Talandge, which resulted in tripping of all elements. About 346MW load loss occurred at 400KV/220 KV Kolhapur SS.	Tripping of following Elements: 1 220kV Kolhapur Bus-1 2 400KV/220KV ICT-1 3 400KV/220KV ICT-2 4 220 kV Kolhapur-Ichakaranji-1 5 220 kV Kolhapur-Hamidwada 6 501 MVA ICT 1 7 220 kV Kolhapur-Mudshingi 1 8 220 KV Bus Coupler 9 220 kV Kolhapur-Bidri
13	GD-1	WR	15:38 / 22-02-2025	19:26 / 22-02-2025	03:48	44		0.05%	-	82323	75362	At 15:38 Hrs/22-02-2025, 400kV Khavda PS I-Khavda PSS9 S/C tripped on differential relay protection, which resulted in loss of evacuation path. It was confirmed that wrong operation made by testing & commissioning project team in 428 tie bay of 429 which lead to tripping. About 44 MW generation loss occurred at 400 kV Khavda PSS9 WPP.	Tripping of following Elements: 1. 400kV Khavda PS I-Khavda PSS9 S/C

Details of Grid Events during the Month of Feb 2025 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA	07-02-2025 14:52	07-02-2025 15:31	1:18	0	152	0.00%	0.24%	54730.89	62729.53	Complete Outage of 220kV/66kV Nittur SS of KPTCL: During antecedent conditons, 220kV Nittur Arasikere was under outage as per SLDC instructions. 220kV/66kV Nittur was being radially fed through 220kV Nittur Neamangala line. As per the reports submitted, the triggering incident was B-N fault in 220kV Nittur Nelamangala line and the line tripped. Tripping of the only connected line led to complete outage of 220kV/66kV Nittur SS.	220KV-NITTUR-NELAMANGALA-1
2	GD - 1	KARNATAKA	11-02-2025 13:42	11-02-2025 14:30	00:48	0	472	0.00%	0.75%	54101.3	62994.34	Tripping of 220kV Bus-1 of 400kV/220kV Nelamangala SS, 220kV Bus-2 of 220kV/66kV Penya SS, Complete outage of 220kV/66kV Brindavan SS, 20kV/110kV Nittur SS, 220kV/110kV Anchepalya SS of KPTCL: As per the reports submitted, the triggering incident was B-N fault in 66kV Anchepalya BG Pura line. At the same time, 220kV Nelamangala Bus-1 BBP maloperated and all elements connected to 220kV Nelamangala Bus-1 tripped. Tripping of 220kV Bus-1 of 400kV/220kV Nelamangala SS led to loss of power supply to 220kV Bus-2 of 220kV/66kV Penya SS, 220kV/66kV Brindavan SS, 20kV/110kV Nittur SS and 220kV/110kV Anchepalya SS of KPTCL.	220KV-ANCHEPALYA-NAGAMANGALA-2, 220KV-NELAMANGALA-BRINDAVAN-1, 220KV-NELAMANGALA-DODDABALLAPUR-1, 220KV-NITTUR-NELAMANGALA-1, 220KV-PEENYA-NELAMANGALA-1, 400KV/220KV NELAMANGALA-ICT-1, 400KV/220KV NELAMANGALA-ICT-2
3	GD - 1	ATAKA , TELAN	12-02-2025 17:04	12-02-2025 18:20	01:16	0	0	0.00%	0.00%	48743.45	61000.08	Tripping of 220kV Bus-2 of 220kV/110kV RAICHUR_KA SS of KPTCL and Complete outage of 220kV Upper Jurala PH of TGGENCO: Triggering incident was YB fault in 220kV RAICHUR_KA Upper Jurala line-2 . At Upper Jurala end, line tripped on operation of Zone-2 carrier aided protection. At the same time, 220kV Bus-2 BBP maloperated at 220kV RAICHUR_KA end . At Upper Jurala end, during antecedent, 220kV Jurala lines were kept open and hence it was radial on 220kV RAICHUR_KA. Therefore, due to tripping of both connected Upper Jurala lines there was complete outage at 220kV Upper Jurala PH.	220KV-JURALA-RAICHUR_KA-1, 220KV-RTPS-RAICHUR_KA-2, 220KV-JURALA-RAICHUR_KA-2
4	GD - 1	ANDHRA PRADESH	13-02-2025 11:53	13-02-2025 12:08	00:15	0	130	0.00%	0.20%	56261.04	65431.98	Complete outage of 220kV/132kV Nuziveedu SS of APTRANSCO: During antecedent conditions, 220kV Nuziveedu KV_Kota_old line was under outage on load management (to control the loading of 220kV KV_Kota_old KV_Kota line of 400kV/220kV KV_kota SS). Hence from 220kV side, 220kV/132kV Nuziveedu SS was radially fed from 220kV VTPS and from 132kV side, the grid connected line was 132kV Nuziveedu Kanumolu line. Triggering incident was BN fault in 220kV Nuziveedu VTPS line. Due to the tripping of 220kV Nuziveedu VTPS line, 132kV Nuziveedu Kanumolu line got overloaded and tripped on operation of OC protection at Kanumolu end. This resulted in complete outage of 220kV/132kV Nuziveedu SS.	NUZVID - 220KV, 220KV-VTPS-NUZVID-1
5	GD - 1	KARNATAKA	19-02-2025 08:55	19-02-2025 09:10	00:15	1196	487	2.19%	0.75%	54517.62	64600.44	Complete Outage of 220kV/110kV Kavoor SS, 220kV/110kV MSEZ(Bajpe) SS, tripping of 220kV Bus-1 of 220kV/110kV Kemar SS of KPTCL and tripping of 400kV Bus-1 and 220kV Bus-1 and 2 at 400kV/220kV UPCL of Adani: During antecedent conditions, there was bus split operation at 220kV Kemar SS. The triggering incident was opening of Main Bay of 400kV/220kV ICT#1 at UPCL for planned maintenance coincided with the LV breaker tripping, leading to an overload on ICT#2. The UPCL SPS operated and tripped U#2 despite 400kV lines being in service, and 400kV/220kV ICT#2 later tripped on backup OC protection, causing complete outage of 220kV/110kV Kavoor SS, 220kV/110kV MSEZ(Bajpe) SS, tripping of 220kV Bus-1 of 220kV/110kV Kemar SS of KPTCL and tripping of 400kV Bus-1 and 220kV Bus-1 and 2 at 400kV/220kV UPCL of Adani.	400KV/220KV UPCL-ICT-1, 400KV/220KV UPCL-ICT-2, UPCL - UNIT 2, UPCL - UNIT 1
6	GD - 1	KARNATAKA	19-02-2025 14:01	19-02-2025 14:45	0:44	782	1072	1.39%	1.68%	56444	63967.66	Grid Disturbance in North Karnataka: At 220kV Narendra_KA SS, during antecedent conditions, isolators of both buses were under closed condition. While carrying out 100MVA Trafo-1 CB dismantling work crane came in arcing zone (B phase) of 220kV Narendra_KA Bus resulting in a BN fault. 220kV Bus zone-1 & 2 operated (since isolators of both buses were in closed condition). This resulted in the tripping of all the elements connected to 220kV Narendra_KA SS. This eventually led to complete outage of 220kV/110kV Narendra_KA SS, 220kV/110kV Ambewadi SS, 220kV Naghjeri PH, 220kV/ Kanabargi SS, 220kV/110kV Soudatti SS, 220kV/110kV Bidnal SS, 220kV/110kV Hubli SS, 220kV/110kV Belagaum SS, 220kV/110kV Athani SS, 220kV/110kV Kudachi SS, 220kV/110kV Haveri SS, 220kV/66kV Shiggaon SS, 220kV/110kV Mughalkod SS, 220kV/110kV Chikkodi SS, 220kV/110kV Kanagala SS, 220kV/110kV Aequs, 220kV/110kV Indal, 220kV/33kV Tadas SS.	220KV-GHATPRABHA-MUGHALKHOD-1, 220KV-GHATPRABHA-MUGHALKHOD-2, 220KV-NARENDRA-MAHALINGAPURA-1, 220KV-NARENDRA-MAHALINGAPURA-2, 220KV-AMBEWADI-PONDA-1, 220KV-AMBEWADI-PONDA-2

Details of Grid Events during the Month of Feb 2025 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD - 1	KARNATAKA	20-02-2025 10:52	20-02-2025 11:59	01:07	0	254	0.00%	0.38%	55541.17	67121.5	Complete Outage of 220kV/66kV Bidadi_KA SS, 220kV Toyota and Tripping of 220kV Bus-2 of 220kV/66kV Somanahalli_KA SS of KPTCL: During antecedent conditions, 220kV Somanahalli_KA Bidadi_KA line-1 was under outage and there was bus split operation at 220kV Somanahalli_KA SS with 220kV Somanahalli Bus-2 being fed from 220kV Bidadi Somanahalli Line-2. 220kV Toyota is being radially fed from 220kV/66kV Bidadi SS. The triggering incident was 220kV Bus-1 fault at 220kV/110kV Bidadi_KA SS due to failure of isolator rigid bus clamp in 220kV Somanahalli_KA Bidadi_KA line-2 bay. Due to non-operation of 220kV Bus-1 BBP at 220kV/110kV Bidadi_KA SS, the fault was cleared by tripping of 220kV Bidadi connected lines from remote ends in zone-2, and in few lines on zone-4. Tripping of all connected lines led to complete outage of 220kV/66kV Bidadi_KA SS , 220kV Toyota and Tripping of 220kV Bus-2 of 220kV/66kV Somanahalli_KA SS.	220KV-BIDADI_PG-BIDADI-2, 220KV-BIDADI_PG-BIDADI-1, 220KV-BIDADI-KOTHIPURA-1, 220KV-BIDADI-KOTHIPURA-2, 220KV-BIDADI-SOMANAHALLI-2
8	GD - 1	KARNATAKA	21-02-2025 15:10	21-02-2025 16:52	01:42	0	200	0.00%	0.30%	52582.68	66603.05	Complete Outage of 220kV/66kV Dobbaspet SS of KPTCL: During antecedent conditions, 220kV Dobaspet Kadur line was under outage. Hence 220kV Dobaspet SS was radially fed from 400kV/220kV Neelamangala SS. The triggering incident was BN fault in 220kV Dobaspet Neelamangala line and the line tripped. Due to tripping of the only connected line, there was complete loss of supply at 220kV/66kV Dobaspet SS.	220KV-DOBBASPET-NELAMANGALA-1
9	GD - 1	KARNATAKA	22-02-2025 16:28	22-02-2025 16:32	00:04	0	670	0.00%	1.03%	51470.0	65249.35	Tripping of 220kV Bus-1 of 400kV/220kV Kolar_PG, complete outage of 220kV/66kV Kolar SS, 220kV Bus-2 of 220kV/66kV Malur SS, 220kV/66kV T Gollahalli SS, 220kV/66kV Chinthamani SS, 220kV/66kV Srinivasapura SS of KPTCL: During antecedent conditions, 220kV Kolar_PG Bus-2 was under outage. The triggering incident was failure of B-pole post insulator causing a fault in 220kV Kolar_PG Bus-1. Immediately, 220kV Bus-1 BBP operated and all elements connected to Bus-1 tripped. Since, 220kV/66kV Kolar SS, 220kV Bus-2 of 220kV/66kV Malur SS, 220kV/66kV T Gollahalli SS, 220kV/66kV Chinthamani SS, 220kV/66kV Srinivasapura SS are being radially fed from 220kV Kolar_PG Bus-2. Tripping of 220kV kolar Bus-2 led to loss of power supply to these stations.	220KV-KOLAR_AC-CHINTAMANAI-1, 220KV-KOLAR_AC-CHINTAMANAI-2, 220KV-KOLAR_AC-T GOLLAHALLI-1, 220KV-KOLAR_AC-T GOLLAHALLI-2, 220KV-KOLAR_KAR-KOLAR_AC-1, 220KV-KOLAR_KAR-KOLAR_AC-2, KOLAR_AC - 220KV - Bus 1, 400KV/220KV KOLAR_AC-ICT-2, 400KV/220KV KOLAR_AC-ICT-3, 400KV/220KV KOLAR_AC-ICT-1
10	GD - 1	KARNATAKA	26-02-2025 11:09	26-02-2025 11:23	00:14	31	320	0.05%	0.48%	59271.59	66978.68	Tripping of 220kV Bus-1 of 220kV Infosys Switching Station and Complete Outage of 220kV/66kV Infosys Pooling Station, 220kV/66kV Gowribidanur SS, 220kV/66kV Mittemari SS, 220kV/66kV Sira SS and 220kV/66kV KIADB-DBPura SS: During antecedent conditions, 220kV KIADB DB Pura were under outage. As per the reports submitted, the triggering incident was R-N fault in 220kV Hiriyur Infosys Line-1. At the same time, 220kV Sira Infosys Line-2, 220kV bus coupler of 220kV Infosys Switching Station and 220kV Madhugiri Gowribidanur line tripped. Tripping of all these lines led to complete outage of 220kV/66kV Infosys Pooling Station, 220kV/66kV Gowribidanur SS, 220kV/66kV Mittemari SS, 220kV/66kV Sira SS and 220kV/66kV KIADB-DBPura SS.	220KV-HIRIYUR-INFOSYS-1, 220KV-SIRA-INFOSYS-2, 220KV-GOWRIBIDANUR-MADHUGIRI-1

Details of Grid Events during the Month of Feb 2025 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-I	GMR	04.02.2025 16:49	04.02.2025 17:04	00:15	655	0	2.34%	0.00%	27938	20555	At 16:49 Hrs, 400KV Angul-GMR-2 tripped due to B-Earth fault (B-Ph conductor snapped at 21 km from GMR). 400KV-Angul-GMR Ckt-1 was under planned shutdown. Both Bus at 400 kV GMR(IPP) became dead as it was radially connected to 400 kV Angul S/S and total generation loss of 655 MW occurred. 400 kV GMR-Angul-1 charged at 17:04 Hrs	400 kV GMR-Angul-2 350 MW U#1, U#2 at GMR
2	GI-I	Indravati	15.02.2025 16:49	15.02.2025 18:23	01:34	200	0	0.65%	0.00%	30943	20241	At 16:49 Hrs on 15.02.2025, while synchronizing U#2 at Indravati, bus bar protection operated for 220 kV Bus-1 which resulted in tripping of all elements connected to 220 kV Bus-1 at Indravati. Running units (U#1, U#4) at Indravati tripped leading to generation loss of around 200 MW.	220 KV Main Bus - 1 at Indravati 150 MW U#1, U#2, U#4 at Indravati 315 MVA 400/220 kV ICT#1, ICT2 at Indravati 220 KV Therubali-Indravati-1,2,3
3	GD-I	PVUNL	20.02.2025 02:33	21.02.2025 22:13	43:40	0	0	0.00%	0.00%	26983	18664	At 02:33 Hrs on 20.02.2025, 400KV Tenughat-PVUNL tripped due to Y_N fault. At present PVUNL is drawing start up power radially through this line. As the line tripped, 400 kV PVUNL S/s became dead. Around 32 MW start up power was being drawn at that instance.	400 KV Tenughat-PVUNL-1
4	GD-I	Angul, GMR, JIPL	20.02.2025 16:20	20.02.2025 17:57	01:37	1777	0	6.15%	0.00%	28913	27136	At 16:20 Hrs on 20.02.2025, 400 kV Bus-1 & 2 and 765 kV Bus 1 & 2 at 765/400 kV Angul S/s tripped. All elements except 765 kV Jharsuguda-Angul-1&2, 765/400 kV ICT-1&2, 400 kV Angul-Bolangir (these elements remained charged through tie bay) tripped. Generation loss of 1777 MW occurred at GMR and JIPL due to loss of evacuation path. GMR and JIPL S/s also became dead. Inclement weather with localized storm was reported around Angul S/s.	765 kV Bus-1 and Bus-2 at Angul 400 kV Bus-1 and Bus-2 at Angul 765 kV Angul-Jharsuguda-3 765 kV Angul-Srikakulam D/c 765/400 kV ICT-3,4 330 MVAr 765 kV Bus Reactor-2 at Angul 125 MVAr 400 kV Bus Reactor-1,2,3 at Angul 600 MW U#1, U#2 at JIPL 350 MW U#1, U#2 at GMR 400 kV Angul-JIPL D/c 400 kV Angul-GMR D/c

Details of Grid Events during the Month of Feb 2025 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Along, Pasighat, Napit & Niglok areas of Arunachal Pradesh Power System	05-02-2025 11:15	05-02-2025 12:17	01:02:00	0	21	0.00%	1.02%	1751	2057	Along, Pasighat, Napit & Niglok areas of Arunachal Pradesh Power System were connected with rest of NER Grid through 132 kV Basar-Along & 132 kV Roing - Pasighat lines. At 11:15 Hrs of 05-02-2025, 132 kV Along-Basar, 132 kV Along-Pasighat & 132 kV Roing - Pasighat lines tripped. Due to tripping of these elements, Along, Pasighat, Napit & Niglok areas of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Along, Pasighat, Napit & Niglok areas of Arunachal Pradesh Power System by charging 132 kV Roing - Pasighat line at 12:17 Hrs of 05-02-2025.	132 kV Along-Basar, 132 kV Along-Pasighat & 132 kV Roing - Pasighat lines
2	GD I	Khuppi and Seppa areas of Arunachal Pradesh Power System	13-02-2025 15:25	13-02-2025 18:22	02:57:00	0	1.2	0.00%	0.06%	1785	2038	Khuppi and Seppa areas of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Kameng - Khupi & 132 kV Tenga - Khupi lines. At 15:25 Hrs of 13-02-2025, 132 kV Kameng - Khupi, 132 kV Tenga - Khupi lines & 132 kV Bus Coupler at Kameng tripped. Due to tripping of these elements, Khuppi and Seppa areas of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Khuppi and Seppa areas by charging 132 kV Kameng - Khupi line at 18:22 Hrs of 13-02-2025.	132 kV Kameng - Khupi, 132 kV Tenga - Khupi lines & 132 kV Bus Coupler at Kameng.
3	GD I	Rengpang area of Manipur Power System	14-02-2025 05:51	14-02-2025 10:19	04:28:00	0	1	0.00%	0.06%	2058	1693	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. 132 kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 05:51 Hrs of 14-02-2025, 132 kV Loktak-Rengpang line tripped due to maloperation of 132 kV Bus coupler at Loktak. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area of Manipur Power System by charging 132 kV Loktak-Rengpang line at 10:19 Hrs of 14-02-2025.	132kV Loktak-Rengpang line & 132 kV Bus coupler at Loktak
4	GD I	Along area of Arunachal Pradesh Power System	15-02-2025 00:38	15-02-2025 03:44	03:06:00	0	4	0.00%	0.25%	1768	1631	Along area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Basar & 132 kV Along-Pasighat lines. At 00:38 Hrs of 15-02-2025, 132 kV Along-Pasighat and 132kV Along-Basar lines tripped. Due to tripping of these elements, Along area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Along area by charging 132 kV Along –Pasighat line at 03:44 Hrs of 15-02-2025	132 kV Along-Basar & 132 kV Along-Pasighat lines
5	Near Miss	Doyang S/S of NEEPCO	16-02-2025 19:59	16-02-2025 20:32	00:33:00	20	0	0.86%	0.00%	2335	2581	Doyang S/S of NEEPCO was connected with rest of NER Grid through 132 kV Dimapur-Doyang D/C lines, 132 kV Doyang-Sanis line and 132 kV Doyang-Mokokchung Line. Prior to the event, 132 kV Doyang-Dimapur I line, 132 kV Doyang-Sanis line, Doyang Unit-2 & 3 were connected to Bus-I. And, 132 kV Doyang-Dimapur II line and 132 kV Doyang-Mokokchung line were connected Doyang Bus-II. Doyang Unit-I was under planned shutdown. At 19:59 Hrs of 16-02-2025, during desynchronization of Doyang Unit-2, 132 kV Bus-I at Doyang tripped on operation of bus bar protection resulting in tripping of all elements connected to Doyang Bus-I. Due to tripping of these elements, 132	132 kV Doyang-Dimapur I line, 132 kV Doyang-Sanis line, Doyang Unit-2 & 3 & 132 kV Bus coupler at Doyang
6	GD I	Panchgram area of Assam Power System	20-02-2025 12:30	20-02-2025 12:48	00:18:00	0	18	0.00%	0.89%	2491	2031	Panchgram area of Assam Power System was connected with rest of NER Grid through 132 kV Panchgram-Hailakandi, 132 kV Panchgram-Badarpur & 132 kV Lumshnong-Panchgram lines. 132 kV Panchgram-Srikona line was under long outage since 14.01.2019. At 12:30 Hrs of 20-02-2025, 132 kV Panchgram-Hailakandi, 132 kV Panchgram-Badarpur & 132 kV Lumshnong-Panchgram lines tripped. Due to tripping of these elements, Panchgram area of Assam Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Panchgram area of Assam Power System by charging 132 kV Panchgram-Badarpur line at 12:48 Hrs of 20-02-2025.	132 kV Panchgram-Hailakandi, 132 kV Panchgram-Badarpur & 132 kV Lumshnong-Panchgram lines
7	GD I	Panchgram area of Assam Power System	22-02-2025 14:26	22-02-2025 15:05	00:39:00	0	20	0.00%	1.00%	1605	1995	Panchgram area of Assam Power System was connected with rest of NER Grid through 132 kV Panchgram-Hailakandi, 132 kV Panchgram-Badarpur & 132 kV Lumshnong-Panchgram lines. 132 kV Panchgram-Srikona line was under long outage since 14.01.2019. At 14:26 Hrs of 22-02-2025, 132 kV Panchgram-Hailakandi, 132 kV Panchgram-Badarpur & 132 kV Lumshnong-Panchgram lines tripped. Due to tripping of these elements, Panchgram area of Assam Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Panchgram area of Assam Power System by charging 132 kV Panchgram-Hailakandi line at 15:05 Hrs of 22-02-2025.	132 kV Panchgram-Hailakandi, 132 kV Panchgram-Badarpur & 132 kV Lumshnong-Panchgram lines

21. NEW ELEMENTS CHARGED IN FEBRUARY 2025

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
NR	1	Bikaner_2(PG)	Juniper Nirjara Energy Private Limited	Solar	50	50	24.02.2025
	2	Fatehgarh_2	Adani Green Energy Twenty Four Limited	Solar	60	500	12.02.2025
	3	Bhadla_2(PG)	Adani Green Energy Twenty Five Limited	Solar	95	500	05.02.2025
WR	4	400/33 kV Khavda PSS-2	Adani Green Energy Twenty Five A Limited (AGE25AL)	Solar	112.5	500/500	05.02.2025
	5	400/33 kV Khavda PSS-3	Adani Green Energy Twenty Four A Limited (AGE24AL)	Solar	87.5	200/400	28.02.2025
	6	400/33 kV Khavda PSS-13	Adani Renewable Energy Forty One Limited (ARE41L)	Wind	46.8	98.8/124.8	12.02.2025
	7	400/33 kV Khavda PSS-13	Adani Renewable Energy Forty One Limited (ARE41L)	Wind	15.6	114.4/124.8	28.02.2025
	8	400/33 kV Khavda PSS-2	Adani Green Energy Twenty Six B Limited (AGE26BL)	Solar	67	167/167	04.02.2025
	9	400/220 kV Pachora SEZ	NTPC Renewable Energy Limited Burlay	Solar	50	105/105	27.02.2025
	10	400/33 kV Khavda PSS-2	Adani Green Energy Twenty Five B Limited (AGE25BL)	Solar	83	583/583	05.02.2025
SR	11	230kV/33kV Vilathikulam S/S	JSW Renew Energy Ltd (JSW_540MW)	Wind	5.4	472.6	21.02.2025
	12	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Wind	35.1	507.7	21.02.2025
	13	400KV KURNOOL	AMGEPL	Wind	13.7	294.2	24.02.2025
				Total Solar Generation addition	**605**		
				Total Wind Generation addition	**117**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
NR	1	PBTSL	Bikaner_2 (PBTSL)	ICT-7	400/220/33	500	01.02.2025
	2	UPRVUNL	Jawaharpur_TPS(UP)	ICT-2	765/400/33	1500	08.02.2025
	3	POWERGRID	Fatehgarh_II(PG)	ICT-10	400/220/33	500	08.02.2025
	4	RSDCL	RSDCL(PSS2)_SL_BHD2_PG	ICT-2	220/33	100	14.02.2025
	5	RSDCL	RSDCL(PSS2)_SL_BHD2_PG	ICT-3	220/33	100	14.02.2025
	6	RSDCL	RSDCL(PSS2)_SL_BHD2_PG	ICT-1	220/33	100	14.02.2025
	7	THDC	Khurja(UP)	ICT-1	400/11.5	120	24.02.2025
SR	8	MEENAKSHI ENERGY LIMITED	MEENAKSHI ENERGY LIMITED Ph2 (2x350MW)	GT-3	400/20	435	14.02.2025
	9	MEENAKSHI ENERGY LIMITED	MEENAKSHI ENERGY LIMITED Ph2 (2x350MW)	GT-4	400/20	435	20.02.2025
	10	TGTRANSCO	YADADRI TPS 400KV SS	ST-2	400/11.5	135	26.02.2025
WR	11	KPS1 Transmission Ltd	765/400 kV KPS1	ICT-5	765/400	1500	26.02.2025
	12	Reliance Industries Limited	400/220 kV Jamnagar RIL	ICT-3	400/220	500	28.02.2025
	13	KPS1 Transmission Ltd	765/400 kV KPS1	ICT-4	765/400	1500	21.02.2025
	14	Reliance Industries Limited	400/220 kV Jamnagar RIL	ICT-4	400/220	500	07.02.2025
ER	15	Sneha Kinetic Power Projects Pvt. Ltd	DIKCHU HEP	ICT-1	400/132	270	22-02-2025
NER	16	NEEPCO	132 kV Loktak SS (Replaced with same rating)	ST	132/11	5	06.02.2025
	17	AEGCL	220/132 kV Namrup SS	ICT-1	220/132/11	100	18.02.2025
					Total (MVA)	**8300**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name		Length (KM)	Conductor Type	DATE
NR	1	RSDCL	220kV Bhadla_2 (PG)-RSDCL(PSS2)_SL_BHD2_PG-1		29.9	AL59 Moose	14.02.2025
WR	2	Adani Green Energy Limited	400 kV AGEL Khavda PSS-4 - KPS1 line		9.7	AL 59 Moose	26.02.2025
				Total length (km)	**39.6**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NER	1	Department of Power Nagaland	Idle charging of 220 kV Mokokchung (POWERGRID)- New Kohima (Zhadima) from Mokokchung end	91.1	Zebra	12.02.2025

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
ER	1	LILO Portion -10.3 Km(BSPTCL)	400KV-BARH-BAKHTIYARPUR(BH)-2 {LILO of D/C 400 kV Patna(PG) - Barh at BAKHTIYARPUR(BH)}	62.20	QUAD MOOSE	01-02-2025
	2	LILO Portion -10.45 Km(BSPTCL)	400KV-PATNA-BAKHTIYARPUR(BH)-2 {LILO of D/C 400 kV Patna(PG) - Barh at BAKHTIYARPUR(BH)}	51.04	QUAD MOOSE	01-02-2025
	3	PGCIL	220KV-DALKHOLA (WB)-PURNEA(OLD)-1 {220kV Purnea(PG) - Dalkhola (WB) line -1 &2 (through ERS) on bypassing Dalkhola (PG)}	41.4	Single Zebra	04-02-2025
	4	PGCIL	220KV-DALKHOLA (WB)-PURNEA(OLD)-2 {220kV Purnea(PG) - Dalkhola (WB) line -1 &2 (through ERS) on bypassing Dalkhola (PG)}	41.4	Single Zebra	03-02-2025
	5	PGCIL	132KV-RANGPO-GANGTOK-1 {Reconductoring of 132 KV Rangpo-Gangtok-I (Gapped Type HTLS)	28	HTLS	24-02-2025
	6	WBSETCL	132KV-NBU-PGCIL{SLG) ckt-2 {(Reconfiguration of Siliguri (PG) – NJP (WBSETCL) S/C and NBU(WB)-NJP(WB) S/C)}	10.62	Panther	31-01-2025
	7	PGCIL ODISHA PROJECT	400KV-ROURKELA-JHARSUGUDA-4 {Reconductoring of Jharsuguda/Sundargarh (PG) – Rourkela (PG) with Twin HTLS conductor (with ampacity equivalent to single HTLS 1228 A at nominal voltage) with bay upgradation at Rourkela S/S.}	126.07	HTLS	28-02-2025
NER	8	NERTS, POWERGRID	132 kV Khandong (NEEPCO)- Khliehriat (POWERGRID)-2 after HTLS reconductoring and upgradation of CTs at both ends	40.93	HTLS ACCC	09.02.2025
	9	NERTS, POWERGRID	132 kV Badarpur- Khliehriat line after HTLS reconductoring and upgradation of CTs at both ends	76.64	HTLS ACCC	20.02.2025

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
SR	1	APTRANSCO	125 MVAR Bus Reactor 2 at 400KV HINDUPUR	400	125	27.02.2025
	2	APTRANSCO	125 MVAR Bus Reactor 2 at 400KV URAVAKONDA	400	125	14.02.2025
WR	3	MSETCL	125 MVAR, 400 kV Bus reactor at Taptitanda	400	125	21.02.2025
	4	MSETCL	125 MVAR, 400 kV Bus reactor at Bableshwar (changing from earlier 80 MVAR)	400	125	24.02.2025
ER	5	BSPTCL	125MVAR 400KV B/R-1 AT BAKHTIYARPUR(BH)	400	125	01.02.2025
	6	BSPTCL	125MVAR 400KV B/R-2 AT BAKHTIYARPUR(BH)	400	125	01.02.2025
NER	7	MePTCL	420 kV Bus Reactor at Byrnihat(Killing) SS (Upgraded from 63 MVAr TO 80 MVAr)	420	80	17.02.2025
				Total (MVAr)	**830**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

Voltage Profile

विद्युत विभव रूपरेखा माह - फरवरी 2025 VOLTAGE PROFILE - Febuary 2025

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	804	749	768
2		दार्लिपली DARLIPALI	0%	100%	0%	0%	0	789	761	773
3		गया GAYA	0%	100%	0%	0%	0	784	746	763
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	782	736	758
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	798	765	781
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	788	744	766
7		राची RANCHI	0%	100%	0%	0%	0	794	761	778
8		सासाराम SASARAM	0%	100%	0%	0%	2	797	720	762
1		आगरा AGRA	0%	100%	0%	0%	0	800	748	779
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	801	745	777
3		अजमेर AJMER	0%	99%	1%	1%	6	807	752	783
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	798	748	777
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	784	760	772
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	781	757	768
7		अंता ANTA	0%	100%	0%	0%	0	799	754	779
8		बलिया BALLIA	0%	100%	0%	0%	0	789	742	767
9		बारा BARA	0%	100%	0%	0%	0	784	753	769
10		भाडला BHADLA	0%	100%	0%	0%	0	796	757	777
11		भाडला-2 BHADLA-2	0%	100%	0%	0%	0	801	751	780
12		भिवानी BHIWANI	0%	99%	1%	1%	8	805	751	783
13		बीकानेर BIKANER	0%	100%	0%	0%	0	802	744	780
14		बरेली BAREILLY	0%	100%	0%	0%	0	808	739	777
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	7	805	751	782
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	796	748	776
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	791	743	767
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	791	738	773
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	3	803	750	782
20		हापुड़ HAPUR	0%	100%	0%	0%	1	808	741	778
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	793	734	770
22		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	800	748	779
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	791	745	771
24		खेतरी KHETRI	0%	100%	0%	0%	0	802	752	781
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	801	738	772
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	775	735	761
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	795	743	766
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	793	730	767
29		मेरठ MEERUT	0%	99%	1%	1%	8	804	745	781
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	806	741	778
31		मोगा MOGA	0%	100%	0%	0%	1	802	739	777
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	777	753	765
33		उरई ORAI	0%	100%	0%	0%	2	804	760	785
34		फागी PHAGI	0%	100%	0%	0%	1	803	731	781
35		रामपुर RAMPUR	0%	95%	3%	3%	23	812	750	786
36		उन्नाव UNNAO	0%	100%	0%	0%	0	789	742	769
37		वाराणसी VARANASI	0%	100%	0%	0%	0	790	754	772
1		अकोला AKOLA	0%	100%	0%	0%	0	793	745	773
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	800	749	775
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	789	745	768
4		भुज BHUJ	0%	100%	0%	0%	0	799	748	775
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	795	745	771
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	777	747	762
7		बीना BINA	0%	100%	0%	0%	0	795	757	778
8		बनसकठा BANASKANTHA	0%	99%	1%	1%	5	805	749	783
9		चापा CHAMPA	0%	100%	0%	0%	2	802	766	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	797	747	772
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	785	753	769
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	794	760	779
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	790	740	769
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	795	756	778
15		ग्वालियर GWALIOR	0%	100%	0%	0%	0	799	753	781
16		इंदौर INDORE	0%	100%	0%	0%	0	792	741	770
17		जबलपुर JABALPUR	0%	100%	0%	0%	0	798	762	782
18	पश्चिमी क्षेत्र WR	खंडवा KHANDWA	0%	100%	0%	0%	0	796	746	772
19		कोरडी KORADI	0%	100%	0%	0%	0	783	748	767
20		लकाडिया LAKADIYA	0%	99%	1%	1%	9	811	705	781
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	791	766	780
22		पड़घे PADGHE	0%	100%	0%	0%	0	803	747	775
23		परली PARLI	0%	100%	0%	0%	2	804	751	778
24		पुणे PUNE	0%	100%	0%	0%	2	806	751	779
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	0	801	760	781
26		सासन SASAN	0%	100%	0%	0%	0	788	762	775
27		सतना SATNA	0%	100%	0%	0%	0	798	763	781
28		सिवनी SEONI	0%	100%	0%	0%	0	790	750	772
29		सीपत SIPAT	0%	100%	0%	0%	0	774	748	763
30		सोलापुर SOLAPUR	0%	100%	0%	0%	2	804	753	780
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	776	751	764
32		तामनार TAMNAR	0%	100%	0%	0%	0	790	766	778
33		वड़ोदरा VADODARA	0%	100%	0%	0%	2	803	741	777
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	792	764	778
35		वर्धा WARDHA	0%	100%	0%	0%	1	806	752	778
36		वरोरा WARORA	0%	100%	0%	0%	0	799	748	775
1		अरियलूर ARIYALUR	0%	100%	0%	0%	0	801	743	774
2		कड़पा CUDDAPAH	0%	98%	2%	2%	16	808	759	778
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	100%	0%	0%	0	800	740	774
4		कर्नूल KURNOOL	0%	100%	0%	0%	0	797	741	771
5		महेश्वरम MAHESWARAM	0%	96%	4%	4%	25	811	743	779
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	90%	10%	10%	65	814	745	781
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	793	746	771
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	1	802	737	778
9		रायचूर RAICHUR	0%	100%	0%	0%	0	801	747	776
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	0	801	736	770
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	798	747	773
12		वेमगिरी VEMAGIRI	0%	100%	0%	0%	0	801	742	772
13		वारंगल WARANGAL	0%	98%	2%	2%	10	805	748	779
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	414	394	404
2		बिस्वनाथ चरिआलि BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	415	394	404
3		बोंगाईगाव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	416	402	409
4		बोंगाईगाव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	417	403	410
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	417	395	405
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	2	421	399	411
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	416	394	403
8	पूर्वोत्तर क्षेत्र NER	अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	412	403	408
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	413	393	402
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	417	396	406
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	419	394	406
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	413	401	406
13		पबंकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	411	393	402
14		रंगानदी RANGANADI (400 kV)	0%	100%	0%	0%	0	415	392	403
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	418	400	408
16		सुर्ज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	409	394	401
17		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	407	399	403

All listed stations are 765 kV stations unless otherwise mentione
***Percentage is calculated w.r.t. Time of one month**

23.ALL TIME HIGHEST

28-02-2025

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	202 23-02-2025
WR	80000 08-02-2025	70350 27-02-2025	1675 28-02-2025	167 18-12-2014	310 28-05-2024	134.04 23-02-2025
SR	68939 25-02-2025	54798 29-04-2024	1416 05-04-2024	208 31-08-2018	323 26-07-2024	154.8 16-02-2025
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	4 09-06-2024
NER	3905 19-09-2024	3787 19-09-2024	80 20-09-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	485 23-02-2025

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	18985	12-02-2025	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	2273	17-01-2025	41.3	20-12-2024
	J&K(UT) and Ladakh(UT)	3200	07-01-2025	70.3	04-02-2025
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05-04-2024	144.4	06-04-2024
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	18888	20-12-2024	353.8	14-02-2025
	Maharashtra	30151	27-02-2025	656.7	28-02-2025
	Goa	803	19-04-2024	17.6	18-05-2024
	DD & DNH	1390	23-10-2024	32.6	16-10-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	16601	26-02-2025	318.1	28-02-2025
	Karnataka	18350	21-02-2025	340.0	28-02-2025
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	8001	23-09-2024	172.8	30-07-2024
	DVC	3674	14-06-2024	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26-05-2024	3.9	18-06-2024
	Assam	2687	20-09-2024	55.8	20-09-2024
	Manipur	271	16-01-2025	4.2	10-01-2025
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.4	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

Note: DVC has reported revised maximum demand met.

24. System Reliability Indices Report for the month of February 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	4	1.00	0.15
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
