ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre
कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या:- **GRID-INDIA/NLDC/MR/** दिनांक: **25.02.2025**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **जनवरी 2025**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **जनवरी 2025** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
मुख्य महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



जनवरी 2025

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

ग्रिड-इंडिया
GRID-INDIA

माह जनवरी 2025 के लिए प्रचालन निष्पादन रिपोर्ट


OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF JANUARY -2025

पृष्ठसूची CONTENTS


1	माह जनवरी 2025 की सारांश रिपोर्ट Summary of report for the month of JANUARY 2025	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति Evening Peak Hour Demand Met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	29 जनवरी के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 29-JANUARY (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह जनवरी 2024 से तुलना Energy requirement and met comparison with JANUARY 2024	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह जनवरी 2024 से तुलना Peak demand requirement and met comparison with JANUARY 2024	25

14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक)एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-45
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	46-48
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	49-56
21	नए चार्ज किये गए तत्व New elements Charged	57
22	विभव रूपरेखा Voltage profile	58
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह जनवरी 2025 तक All Time Highest (Demand & Energy) figures: Till JANUARY 2025	59
24	जनवरी 2025 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for JANUARY 2025	60


1. SUMMARY OF REPORT FOR THE MONTH OF JANUARY-2025

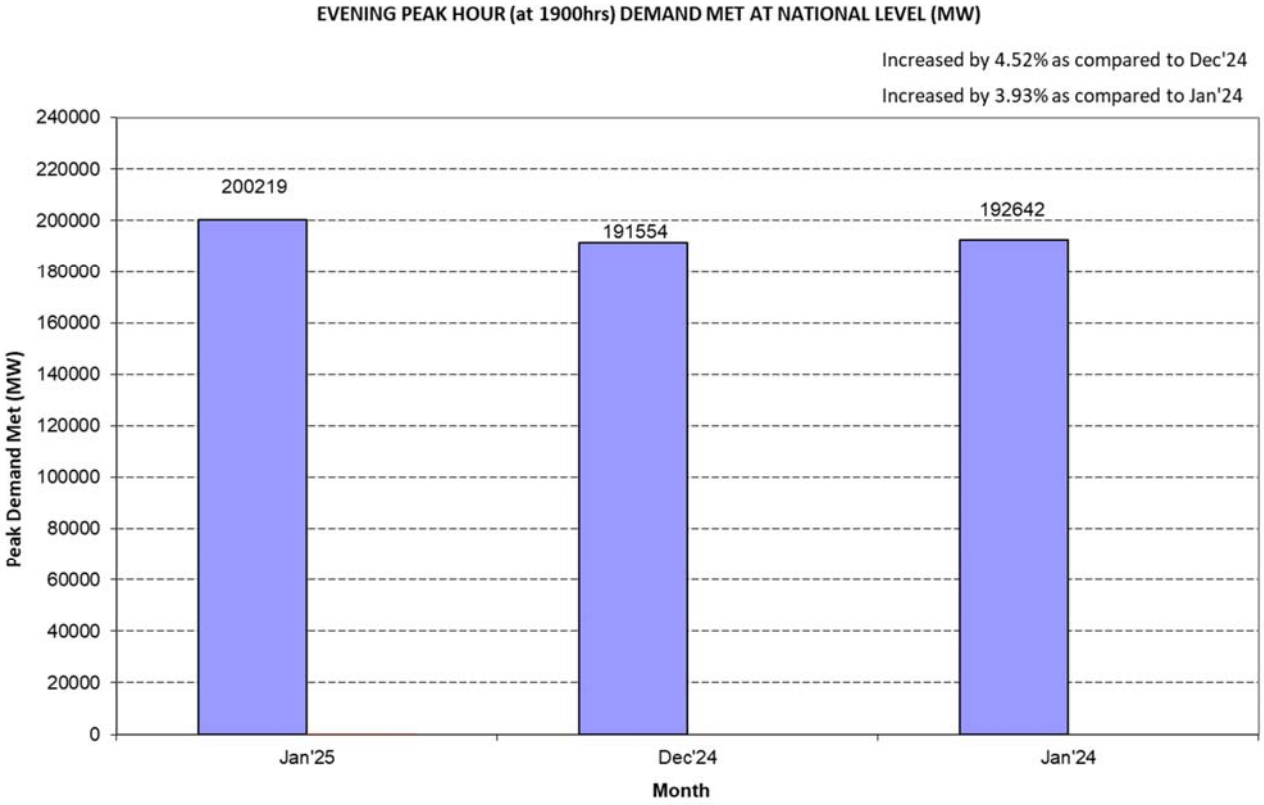


*Source: As per daily data furnished by states

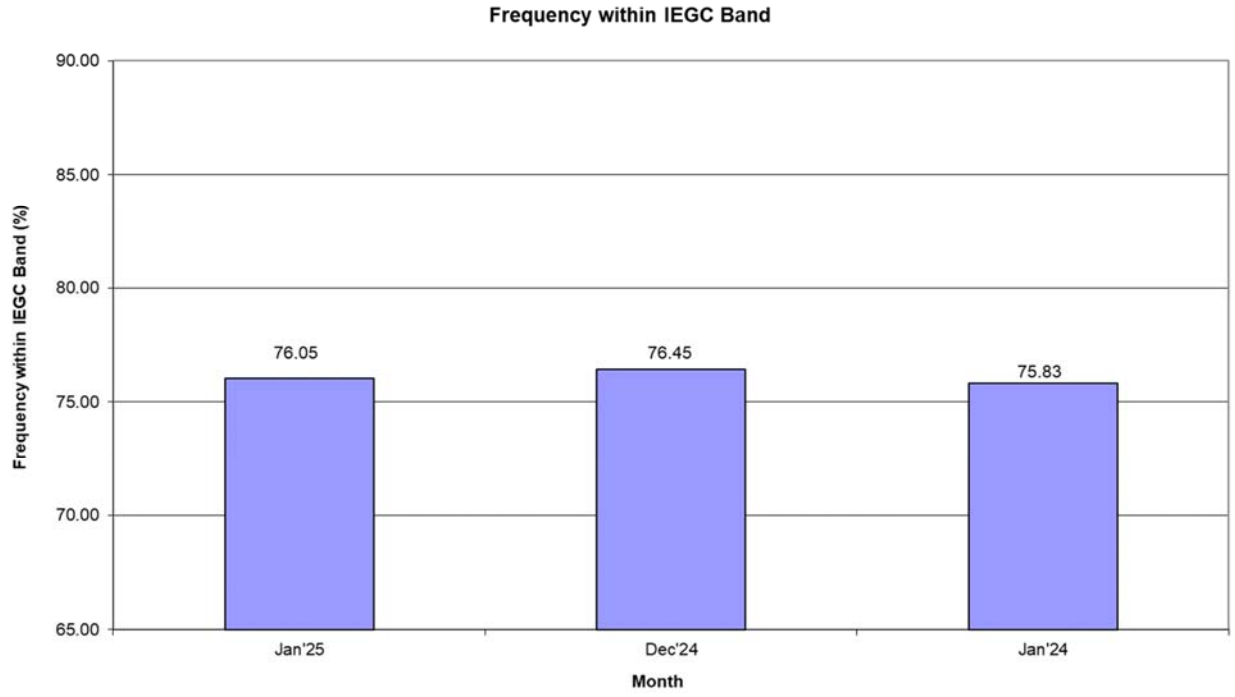


ENERGY MET AT NATIONAL LEVEL (MU)

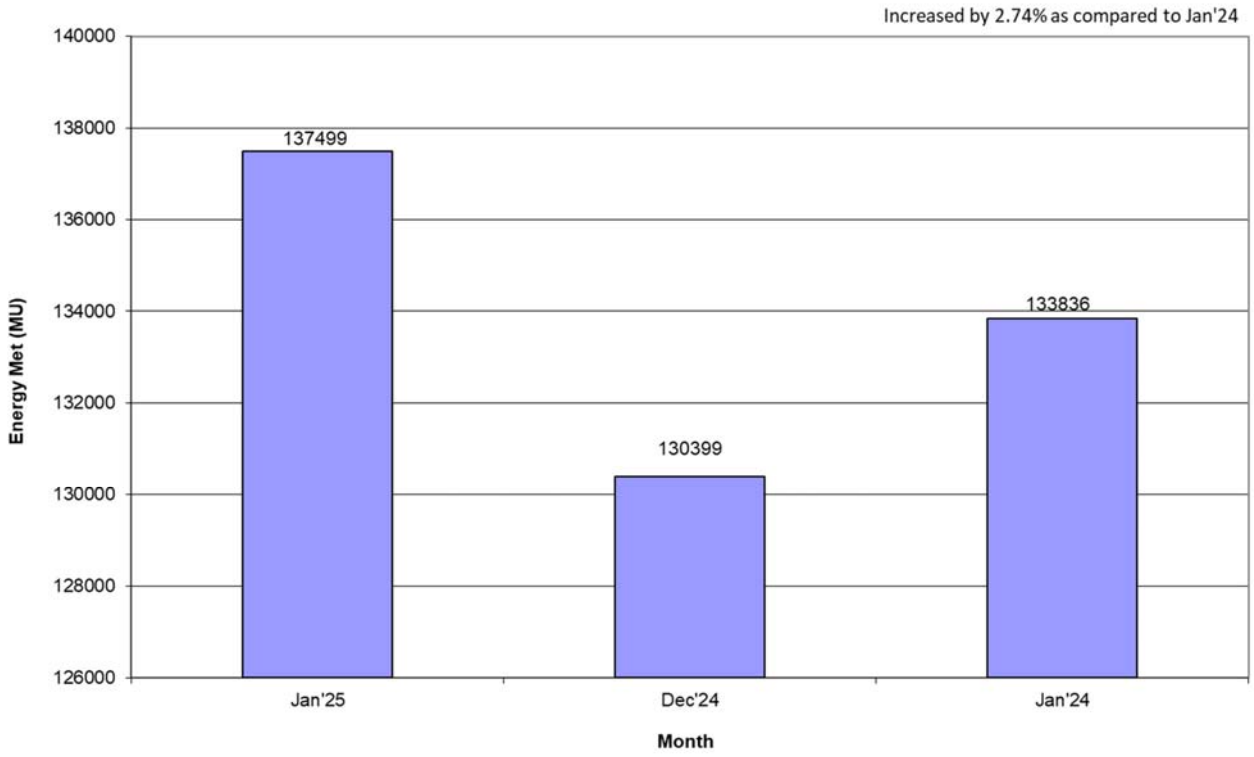


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

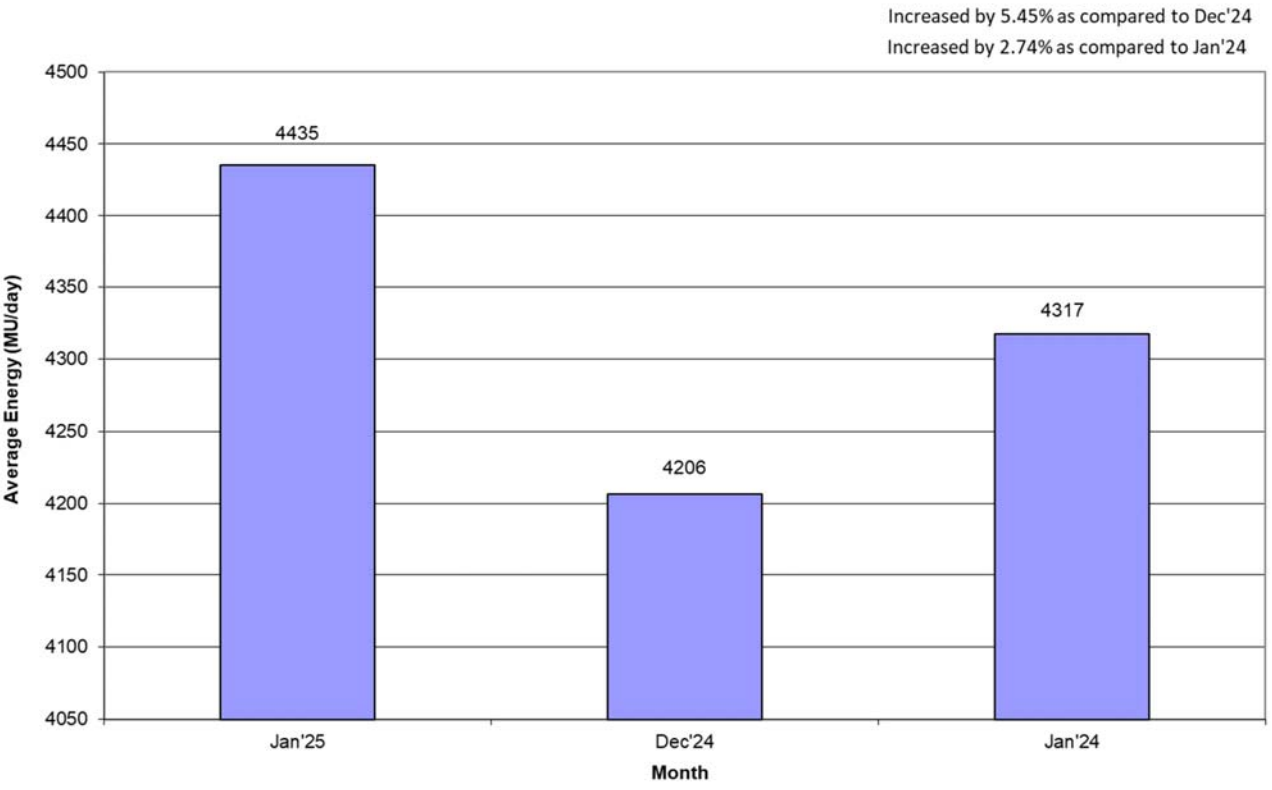


HYDRO GENERATION AT NATIONAL LEVEL (MU)

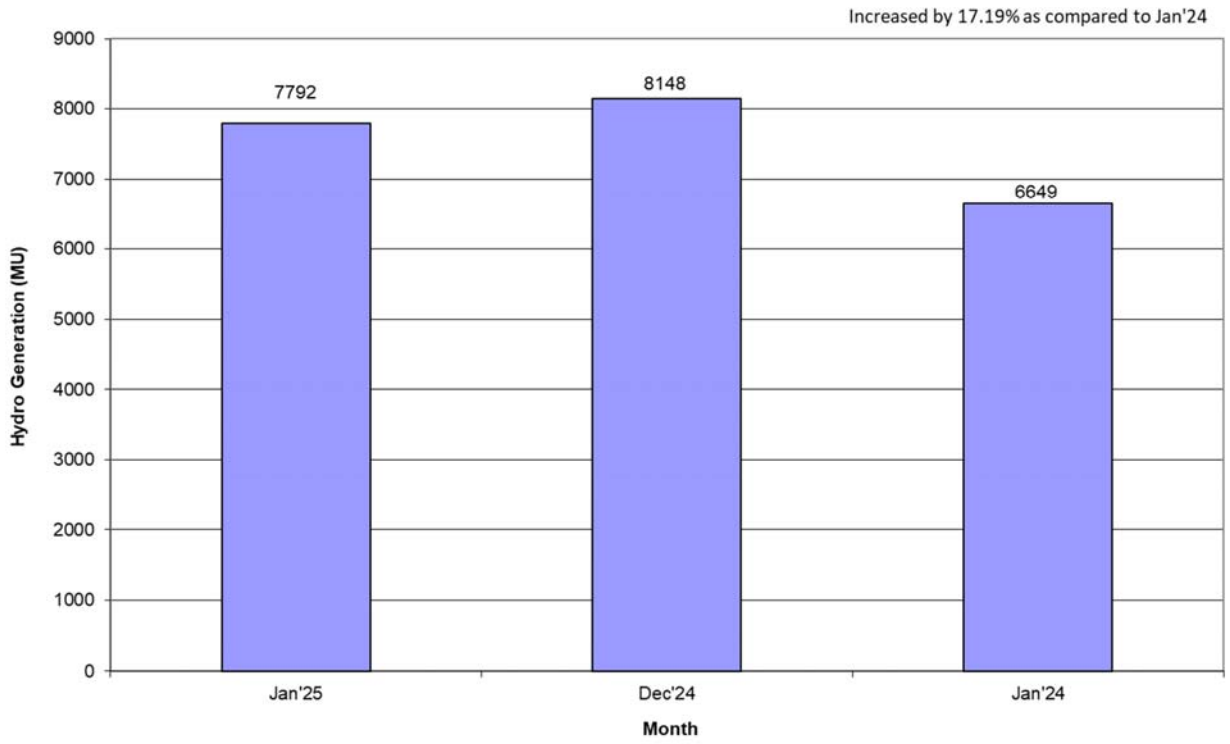


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

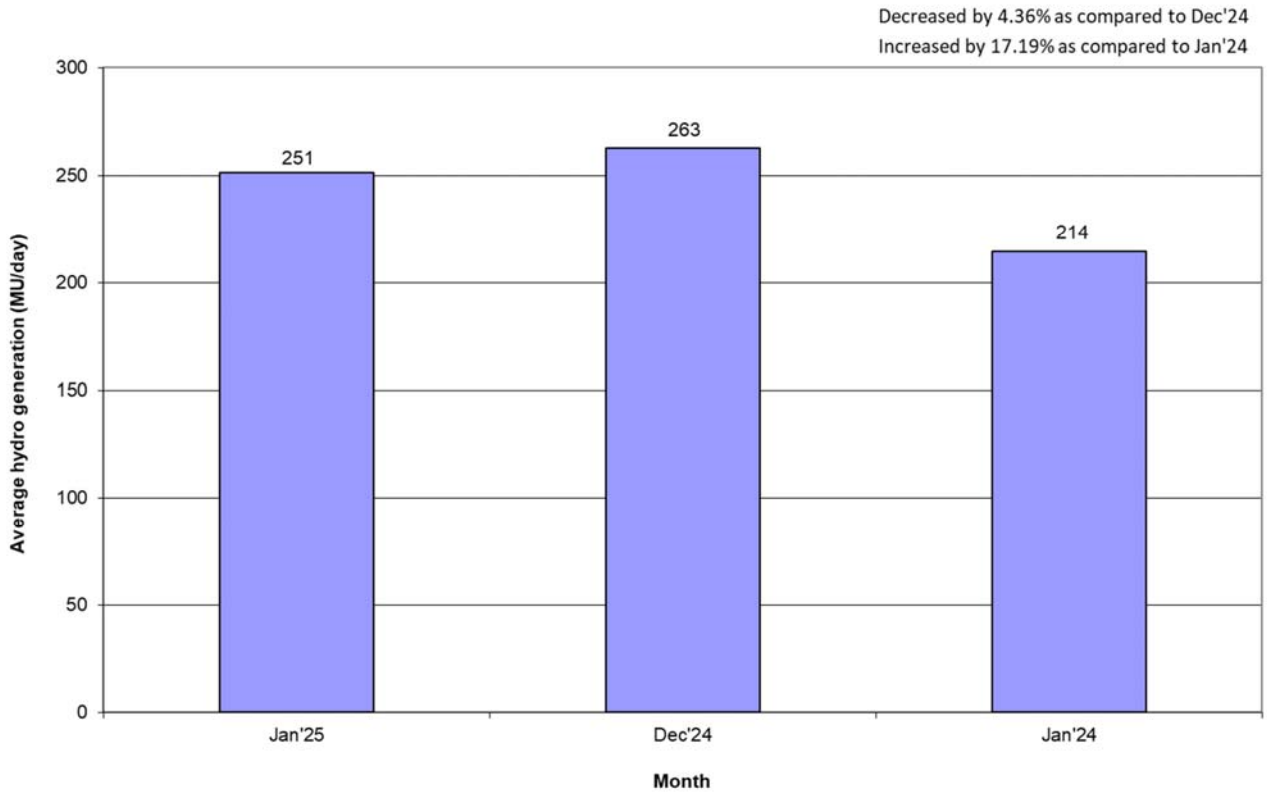


WIND GENERATION AT NATIONAL LEVEL (MU)

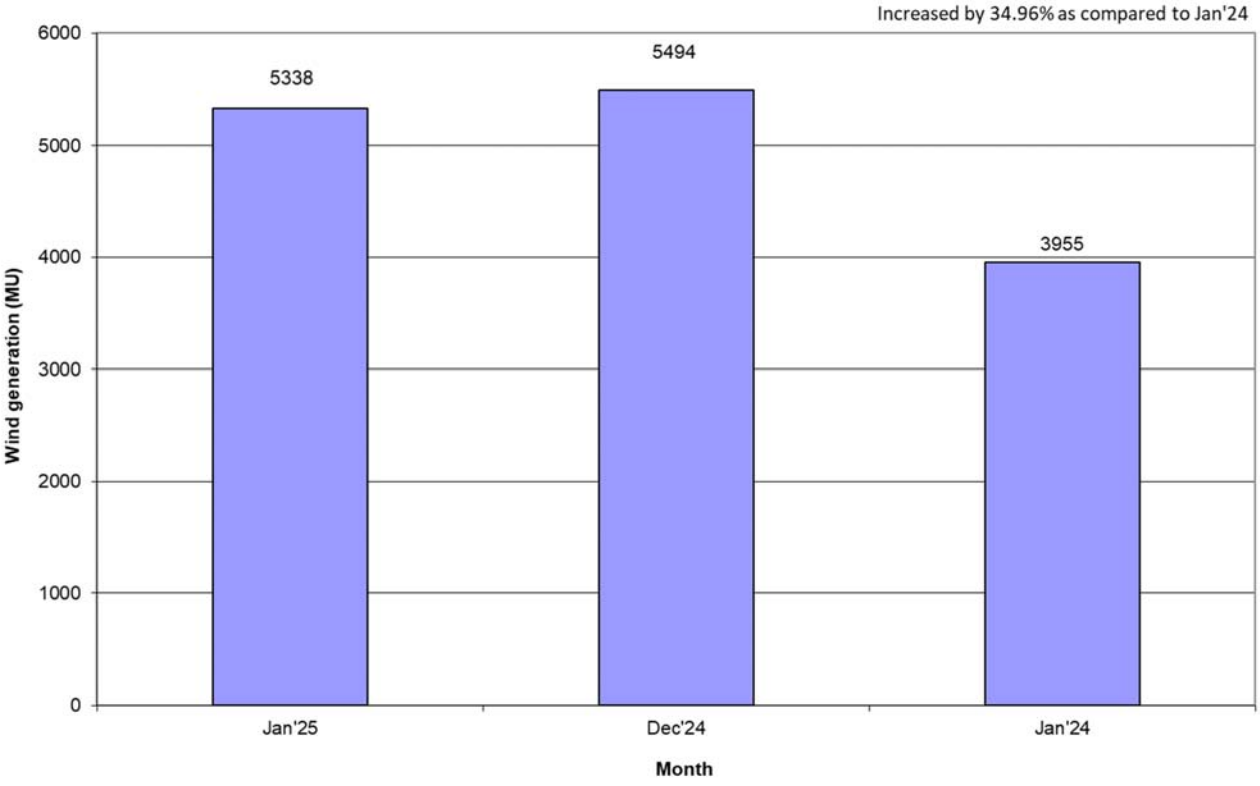


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

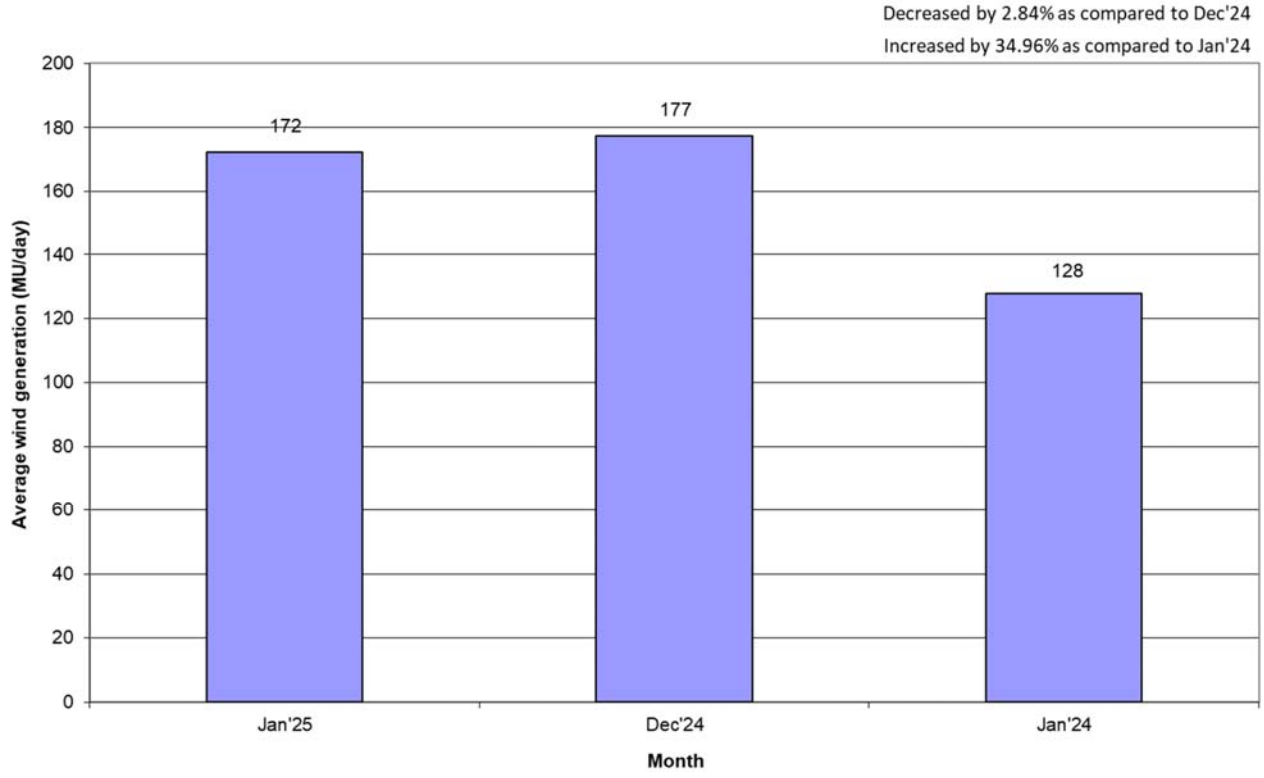

SOLAR GENERATION AT NATIONAL LEVEL (MU)

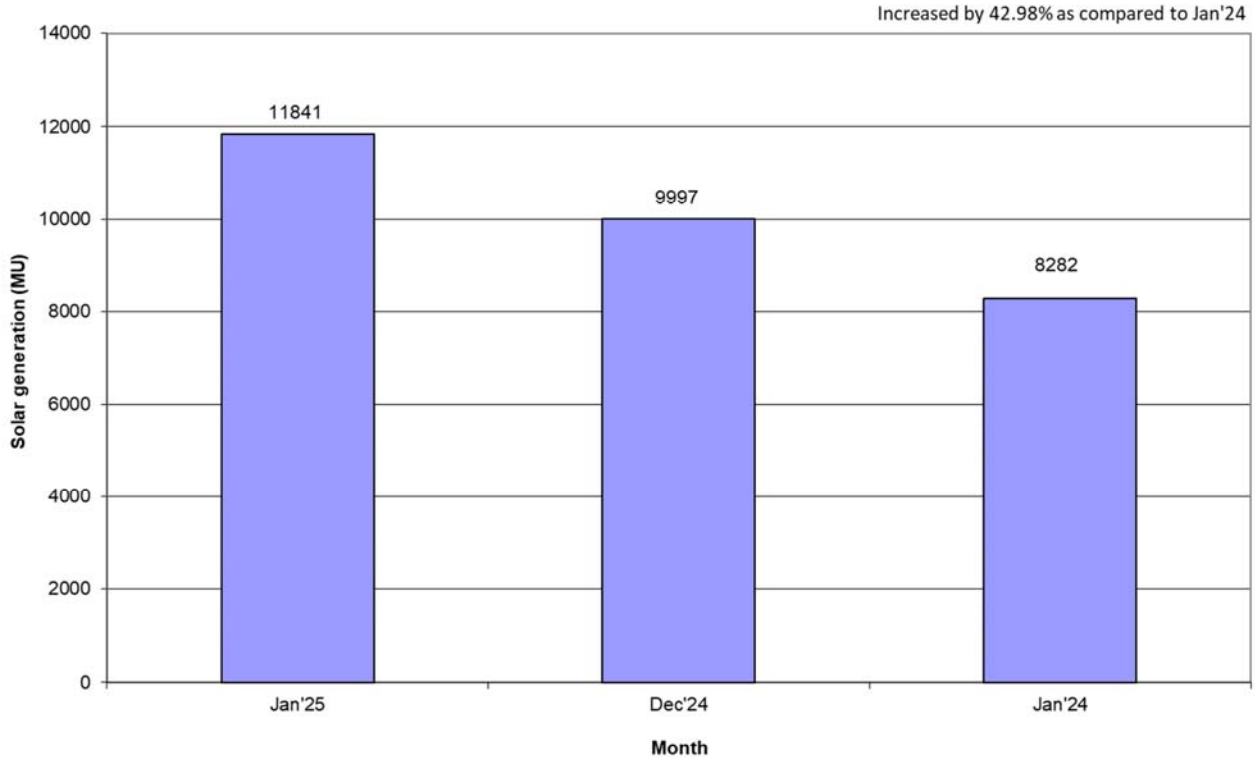

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

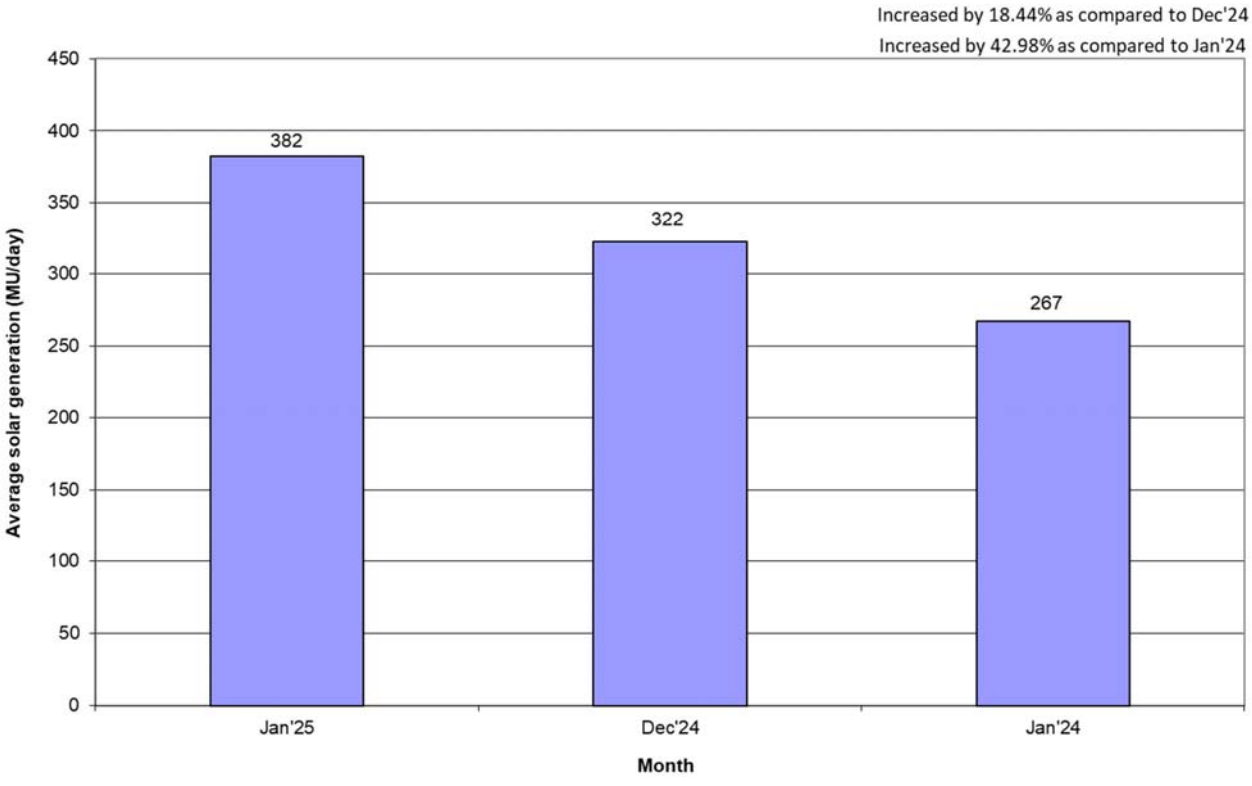

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.01.2025
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	58638	1580	5995	0	66213	1620	20830	45880	134542
2	WR	74663	1400	10806	0	86869	3240	7563	58157	155829
3	SR	50456	3640	6272	434	60801	3320	11867	58135	134123
4	ER	28875	0	80	0	28955	0	4764	2369	36088
5	NER	1242	0	1665	36	2943	0	1944	622	5509
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	213873	6620	24818	589	245900	8180	46968	165202	466251

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति
EVENING PEAK HOUR (at 19:00hrs) DEMAND MET AT NATIONAL LEVEL


माह: जनवरी 2025 MONTH:- JAN 2025

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Jan-25	57033	58374	40889	21245	2482	180023
2-Jan-25	60809	62928	43914	21862	2658	192171
3-Jan-25	58986	62965	43771	22179	2680	190581
4-Jan-25	60004	63404	44045	22253	2701	192407
5-Jan-25	57489	60536	40553	21807	2636	183021
6-Jan-25	61296	63599	44997	22446	2685	195023
7-Jan-25	61983	64773	45817	22517	2632	197722
8-Jan-25	61926	64849	45561	23093	2727	198156
9-Jan-25	61849	65764	45195	22437	2726	197971
10-Jan-25	61849	65258	44457	22376	2715	196655
11-Jan-25	57713	64884	43540	22640	2705	191482
12-Jan-25	56988	61290	41400	21780	2575	184033
13-Jan-25	58955	63385	41887	22739	2593	189558
14-Jan-25	58700	57252	36432	22491	2458	177333
15-Jan-25	60875	61015	39010	22634	2609	186143
16-Jan-25	60916	63898	42817	22584	2718	192933
17-Jan-25	61452	65127	43568	22625	2674	195446
18-Jan-25	60733	65313	43574	22681	2703	195004
19-Jan-25	56788	61795	40176	22321	2588	183668
20-Jan-25	58623	65415	44795	23210	2662	194705
21-Jan-25	58109	65597	45029	23347	2673	194755
22-Jan-25	58474	66486	45843	22489	2702	195994
23-Jan-25	58346	66732	46519	22715	2764	197076
24-Jan-25	59205	66770	45975	23208	2797	197955
25-Jan-25	59315	67039	46911	23051	2774	199090
26-Jan-25	53134	60185	40872	21857	2526	178574
27-Jan-25	59422	67097	46387	22870	2793	198569
28-Jan-25	59538	67296	47306	22857	2775	199772
29-Jan-25	54915	66981	46685	23800	2773	195154
30-Jan-25	58979	66863	47916	23708	2753	200219
31-Jan-25	58903	66787	48186	23078	2760	199714
उच्चतम MAXIMUM	61983	67296	48186	23800	2797	200219
निम्नतम MINIMUM	53134	57252	36432	21245	2458	177333
औसत AVERAGE	59139	64182	44001	22610	2678	192610
अब तक का उच्चतम All Time Max.	82312	67482	54798	29695	3787	227354
दिनांक Date	23.07.24	30.05.24	29.04.24	29.05.24	19.09.24	29.05.24

Source: As per daily data furnished by states

EVENING PEAK HOUR DEMAND(at 1900hrs) MET DURING THE MONTH OF JANUARY' 2025

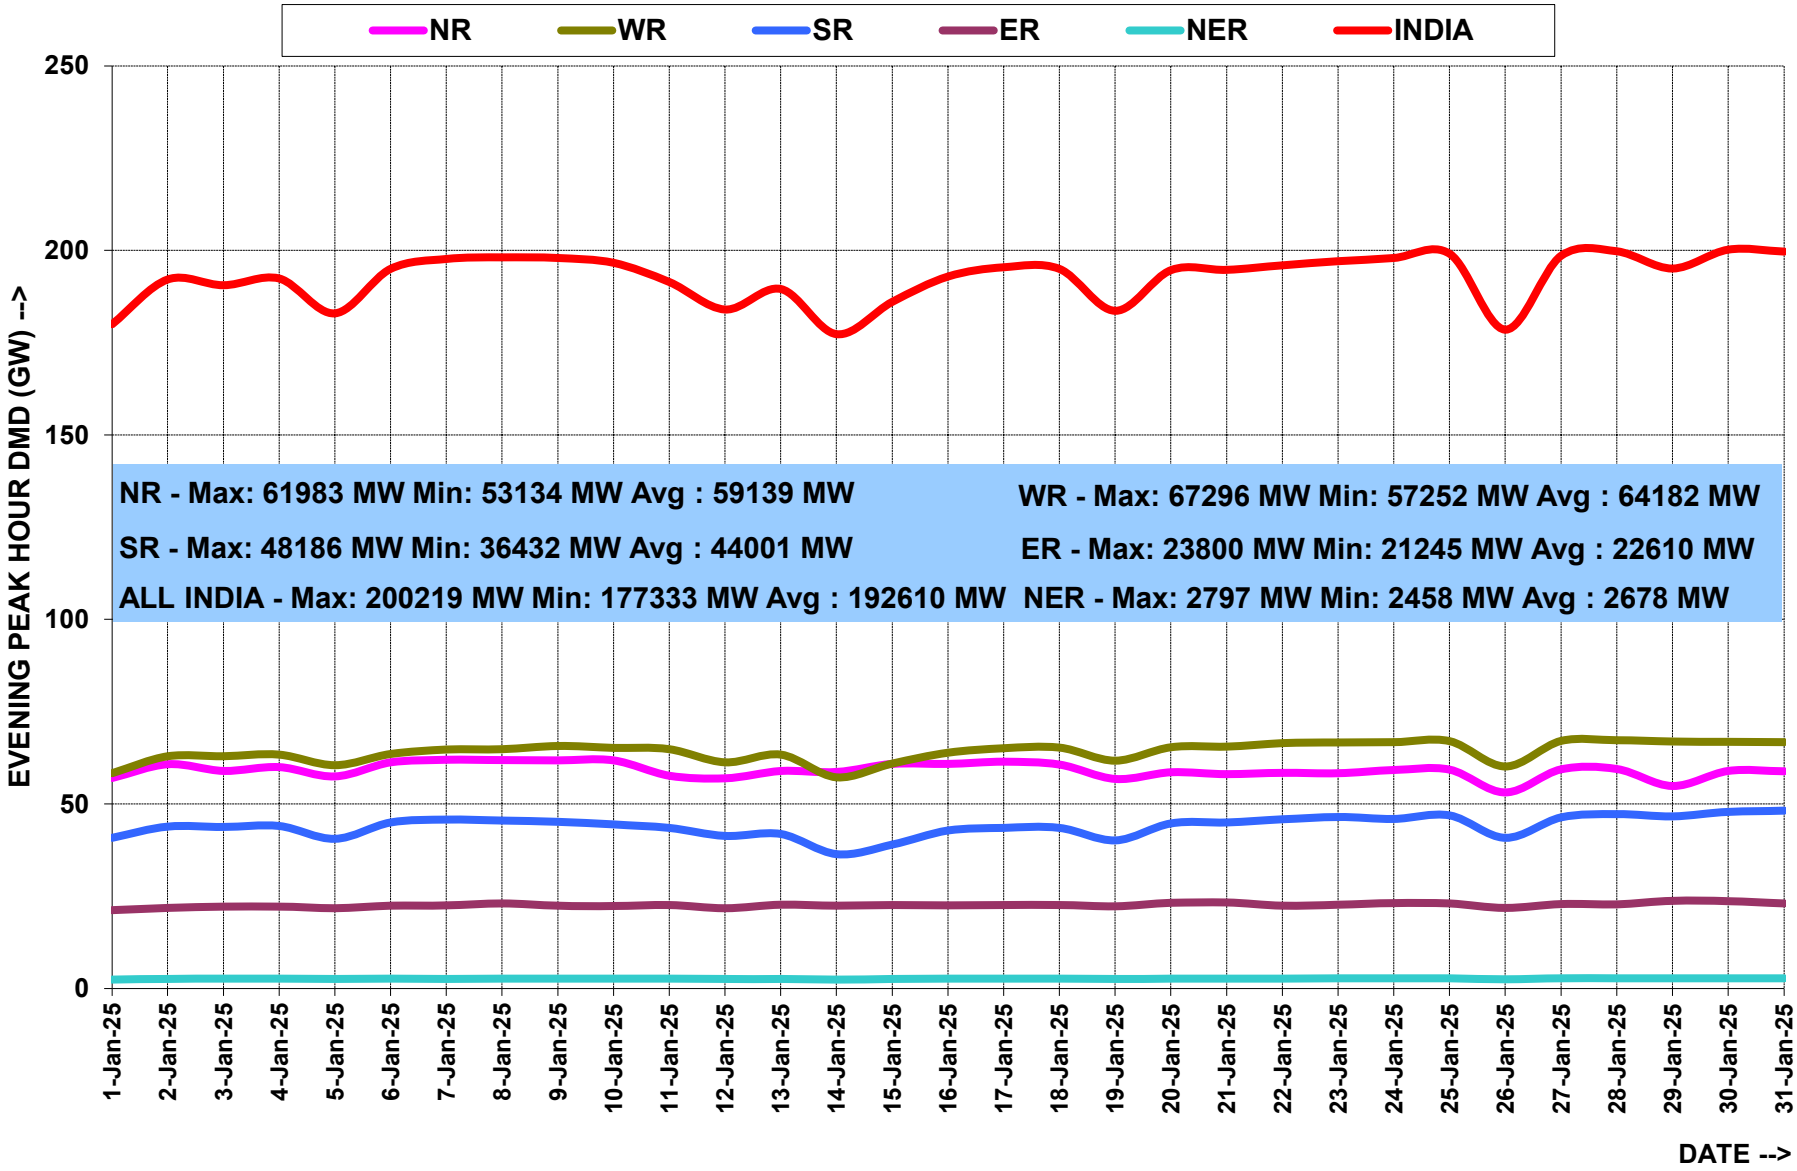


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: जनवरी 2025 MONTH:- JAN 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jan-25	1209	1378	1106	438	47	4178
02-Jan-25	1218	1420	1132	436	47	4253
03-Jan-25	1259	1456	1158	450	49	4371
04-Jan-25	1240	1470	1147	452	49	4358
05-Jan-25	1199	1446	1098	448	47	4238
06-Jan-25	1248	1479	1161	456	49	4394
07-Jan-25	1286	1505	1193	465	48	4497
08-Jan-25	1281	1494	1197	472	48	4491
09-Jan-25	1272	1518	1196	476	50	4512
10-Jan-25	1298	1541	1199	477	50	4565
11-Jan-25	1224	1549	1178	473	50	4474
12-Jan-25	1141	1488	1123	458	48	4260
13-Jan-25	1195	1499	1135	466	48	4344
14-Jan-25	1210	1413	1045	464	47	4179
15-Jan-25	1224	1447	1039	462	47	4219
16-Jan-25	1224	1503	1097	464	49	4336
17-Jan-25	1245	1537	1143	463	49	4437
18-Jan-25	1239	1542	1148	462	49	4440
19-Jan-25	1178	1507	1076	460	48	4269
20-Jan-25	1202	1552	1133	468	49	4403
21-Jan-25	1226	1572	1161	477	50	4487
22-Jan-25	1237	1576	1184	470	51	4518
23-Jan-25	1218	1576	1210	463	51	4518
24-Jan-25	1247	1586	1209	473	51	4567
25-Jan-25	1248	1593	1205	481	52	4578
26-Jan-25	1209	1495	1118	459	48	4328
27-Jan-25	1248	1575	1198	466	50	4537
28-Jan-25	1291	1613	1233	477	51	4665
29-Jan-25	1289	1611	1250	477	52	4679
30-Jan-25	1288	1620	1259	482	52	4699
31-Jan-25	1280	1614	1280	482	51	4706
कुल TOTAL	38374	47172	36008	14419	1527	137499
उच्चतम MAXIMUM	1298	1620	1280	482	52	4706
निम्नतम MINIMUM	1141	1378	1039	436	47	4178
औसत AVERAGE	1238	1522	1162	465	49	4435
संचयी 2024-25 Cumulative 2024-25	446841	442617	346088	168845	17615	1422006
अब तक का उच्चतम All Time Max.	1990	1648	1416	692	80	5466
दिनांक Date	18.06.24	06.05.24	05.04.24	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF JANUARY' 2025

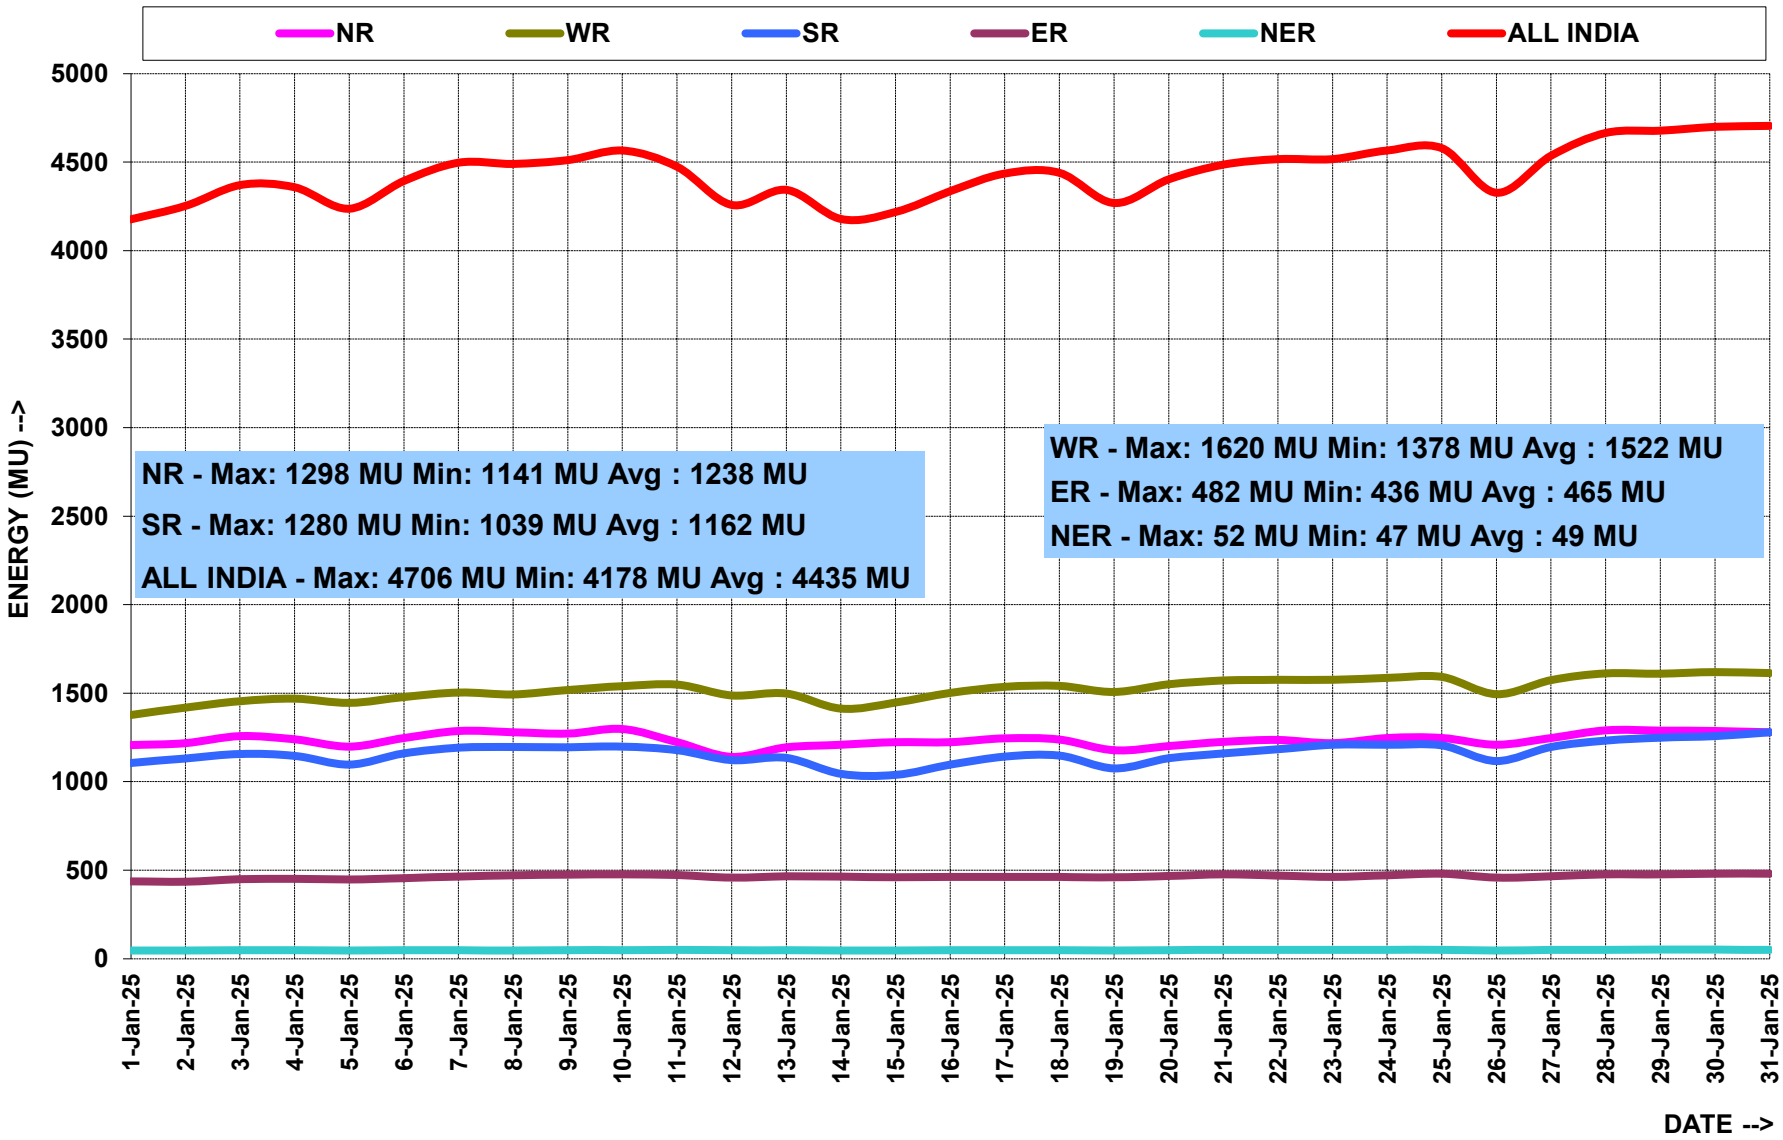

5. वर्ष 2024-25 के लिए आवृति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78		50.38	49.46	50.00
	Oct-24	All India Grid	4.86	80.27	14.87		50.39	49.58	50.00
	Nov-24	All India Grid	5.15	80.80	14.05		50.32	49.55	50.00
	Dec-24	All India Grid	5.58	76.45	17.97		50.42	49.49	50.00
	Jan-25	All India Grid	5.23	76.05	18.72		50.31	49.60	50.00
	2024-25 (upto Jan)	**All India Grid**	**5.02**	**78.18**	**16.80**		**50.67**	**49.46**	**50.00**

5.1 जनवरी 2025 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR JANUARY 2025


फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Jan-25	3.92	75.28	20.80		50.30	49.79	50.01	0.04
	02-Jan-25	5.94	74.97	19.10		50.30	49.68	50.00	0.05
	03-Jan-25	6.96	76.30	16.75		50.19	49.67	49.99	0.04
	04-Jan-25	9.73	72.88	17.38		50.18	49.70	49.99	0.05
	05-Jan-25	6.85	63.37	29.78		50.23	49.60	50.01	0.07
	06-Jan-25	1.24	68.92	29.84		50.29	49.86	50.03	0.04
	07-Jan-25	1.98	76.25	21.77		50.25	49.80	50.02	0.03
	08-Jan-25	1.57	76.71	21.71		50.23	49.81	50.02	0.03
	09-Jan-25	1.12	78.63	20.24		50.19	49.82	50.01	0.02
	10-Jan-25	7.14	77.88	14.98		50.24	49.68	49.99	0.03
	11-Jan-25	14.63	74.00	11.37		50.23	49.60	49.97	0.07
	12-Jan-25	5.35	69.99	24.66		50.22	49.67	50.01	0.05
	13-Jan-25	5.47	71.04	23.48		50.24	49.63	50.01	0.05
	14-Jan-25	3.46	66.12	30.42		50.30	49.84	50.02	0.04
	15-Jan-25	3.02	82.60	14.38		50.23	49.83	50.00	0.03
	16-Jan-25	2.22	80.07	17.71		50.21	49.86	50.00	0.03
	17-Jan-25	4.72	72.89	22.38		50.21	49.77	50.01	0.04
	18-Jan-25	2.43	82.03	15.54		50.22	49.85	50.00	0.03
	19-Jan-25	1.92	80.56	17.52		50.27	49.83	50.00	0.03
	20-Jan-25	3.43	72.57	24.00		50.27	49.84	50.01	0.04
	21-Jan-25	4.76	77.93	17.31		50.20	49.76	50.00	0.03
	22-Jan-25	6.34	85.05	8.61		50.18	49.81	49.99	0.03
	23-Jan-25	1.11	79.24	19.65		50.23	49.84	50.01	0.03
	24-Jan-25	2.73	80.81	16.46		50.31	49.81	50.00	0.03
	25-Jan-25	6.30	77.53	16.17		50.18	49.63	49.99	0.04
	26-Jan-25	2.50	80.80	16.70		50.31	49.78	50.01	0.04
	27-Jan-25	4.77	80.31	14.92		50.19	49.80	50.00	0.03
	28-Jan-25	11.03	77.33	11.64		50.18	49.64	49.98	0.05
	29-Jan-25	3.74	82.40	13.87		50.19	49.66	50.00	0.03
	30-Jan-25	14.97	69.36	15.67		50.24	49.64	49.98	0.07
	31-Jan-25	10.75	73.60	15.65		50.25	49.71	49.99	0.06

6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: जनवरी 2025 MONTH:- JAN 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jan-25	97	26	72	13	12	220
02-Jan-25	99	30	84	17	13	242
03-Jan-25	99	31	85	18	12	245
04-Jan-25	95	35	94	18	12	254
05-Jan-25	92	25	81	18	12	228
06-Jan-25	91	32	96	19	12	249
07-Jan-25	91	36	101	18	11	257
08-Jan-25	88	35	94	22	11	249
09-Jan-25	93	38	92	21	12	256
10-Jan-25	90	41	103	19	11	265
11-Jan-25	89	56	107	20	11	284
12-Jan-25	88	39	79	20	10	235
13-Jan-25	90	48	86	18	11	253
14-Jan-25	88	42	72	17	11	230
15-Jan-25	88	47	83	20	11	249
16-Jan-25	90	47	91	20	11	258
17-Jan-25	90	49	75	24	11	250
18-Jan-25	89	47	90	23	11	260
19-Jan-25	87	30	74	20	10	220
20-Jan-25	89	46	80	23	10	247
21-Jan-25	88	46	82	23	10	248
22-Jan-25	87	47	87	22	10	253
23-Jan-25	86	44	91	17	10	249
24-Jan-25	89	42	83	22	10	246
25-Jan-25	92	42	86	22	11	253
26-Jan-25	92	37	64	21	10	224
27-Jan-25	93	42	87	21	10	253
28-Jan-25	98	53	95	25	10	280
29-Jan-25	97	52	89	24	10	272
30-Jan-25	95	51	93	23	10	273
31-Jan-25	93	61	101	24	11	290
कुल TOTAL	2831	1297	2695	632	337	7792
उच्चतम MAXIMUM	99	61	107	25	13	290
निम्नतम MINIMUM	86	25	64	13	10	220
औसत AVERAGE	91	42	87	20	11	251
संचयी 2024-25 Cumulative 2024-25	73144	17781	30270	15308	7197	143701
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

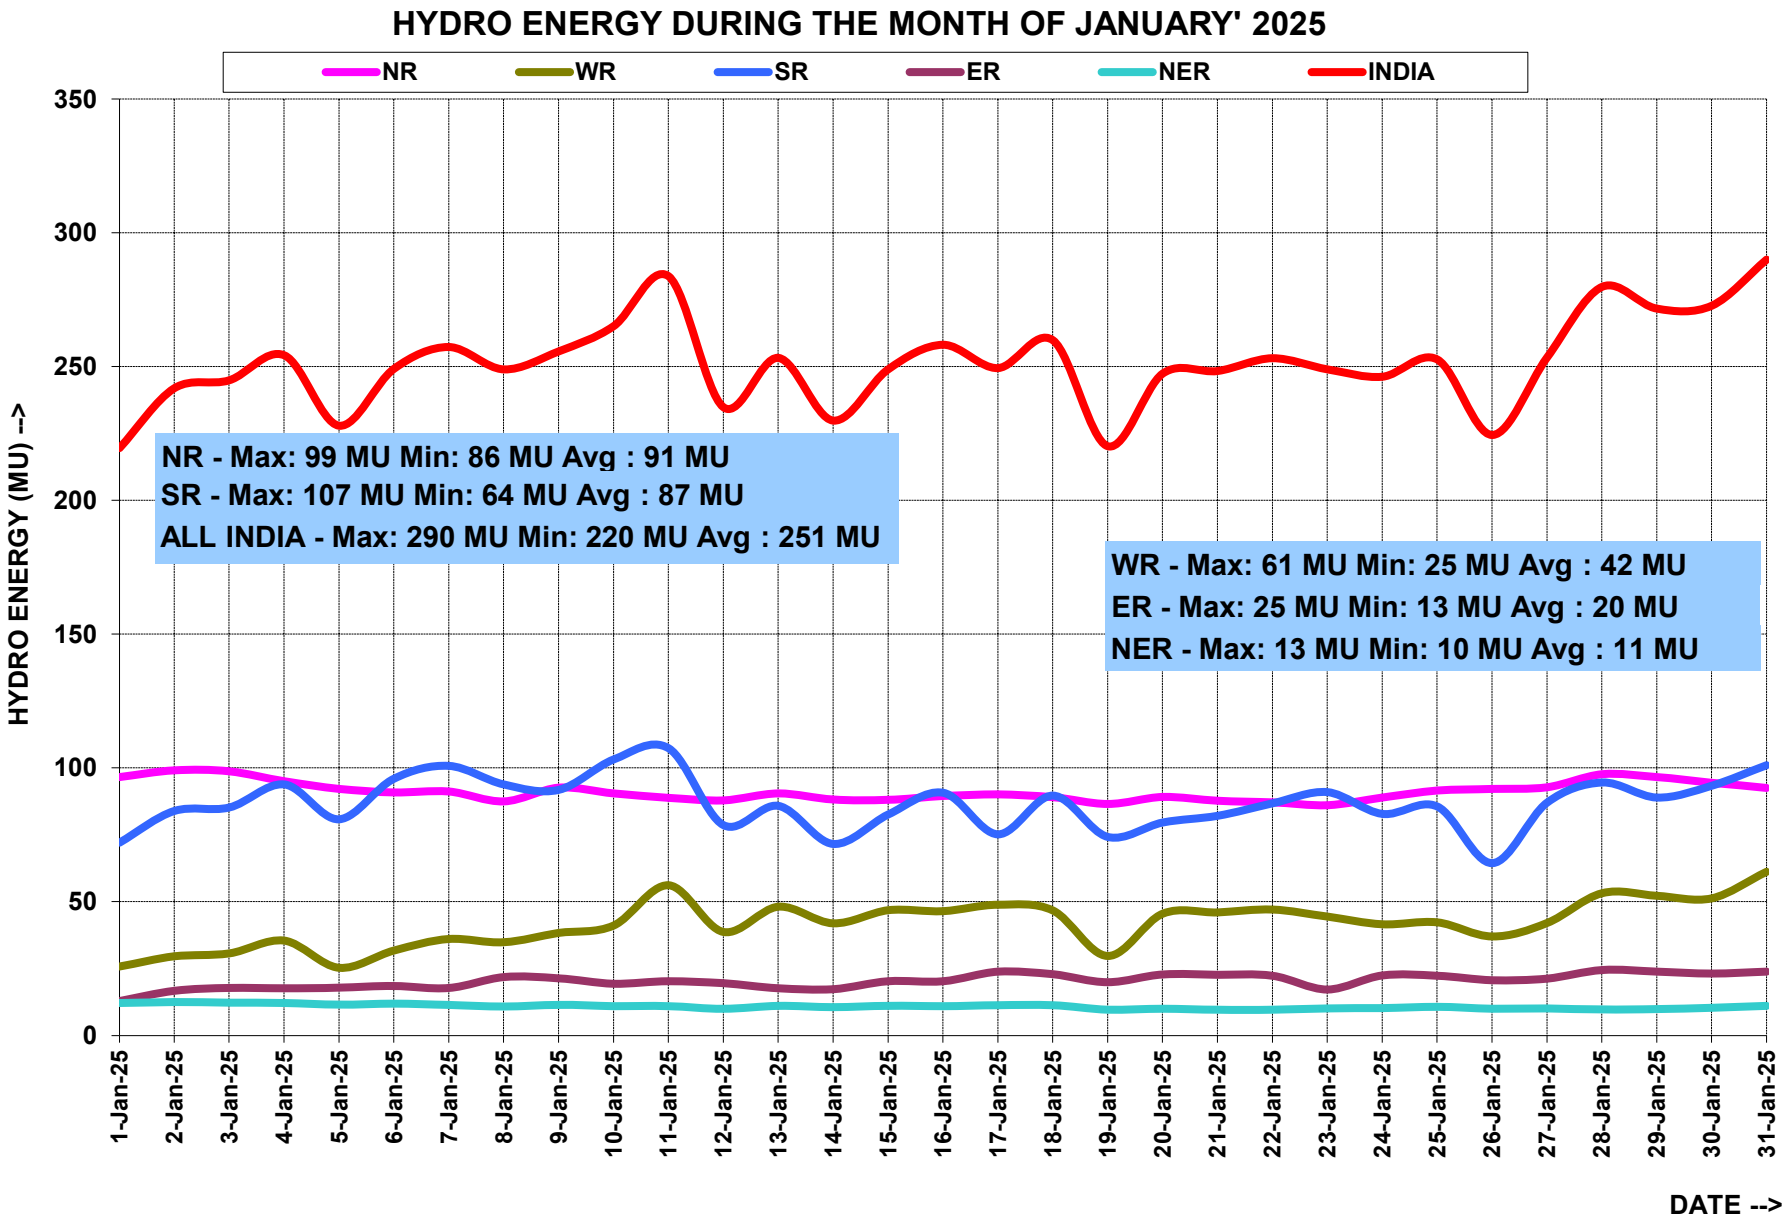
HYDRO ENERGY DURING THE MONTH OF JANUARY' 2025
NR
WR
SR
ER
NER
INDIA
HYDRO ENERGY (MU) -->
350
300
250
200
150
100
50
0
NR - Max: 99 MU Min: 86 MU Avg : 91 MU
SR - Max: 107 MU Min: 64 MU Avg : 87 MU
ALL INDIA - Max: 290 MU Min: 220 MU Avg : 251 MU
WR - Max: 61 MU Min: 25 MU Avg : 42 MU
ER - Max: 25 MU Min: 13 MU Avg : 20 MU
NER - Max: 13 MU Min: 10 MU Avg : 11 MU
1-Jan-25
2-Jan-25
3-Jan-25
4-Jan-25
5-Jan-25
6-Jan-25
7-Jan-25
8-Jan-25
9-Jan-25
10-Jan-25
11-Jan-25
12-Jan-25
13-Jan-25
14-Jan-25
15-Jan-25
16-Jan-25
17-Jan-25
18-Jan-25
19-Jan-25
20-Jan-25
21-Jan-25
22-Jan-25
23-Jan-25
24-Jan-25
25-Jan-25
26-Jan-25
27-Jan-25
28-Jan-25
29-Jan-25
30-Jan-25
31-Jan-25
DATE -->

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: जनवरी 2025 MONTH:- JAN 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jan-25	13	62	114	----------	----------	190
02-Jan-25	10	53	81	----------	----------	144
03-Jan-25	8	46	102	----------	----------	156
04-Jan-25	9	52	58	----------	----------	119
05-Jan-25	15	69	55	----------	----------	139
06-Jan-25	22	143	46	----------	----------	211
07-Jan-25	18	163	45	----------	----------	227
08-Jan-25	4	93	60	----------	----------	157
09-Jan-25	13	64	78	----------	----------	155
10-Jan-25	19	64	91	----------	----------	174
11-Jan-25	20	60	69	----------	----------	149
12-Jan-25	18	105	65	----------	----------	188
13-Jan-25	16	156	72	----------	----------	244
14-Jan-25	20	126	103	----------	----------	248
15-Jan-25	26	128	112	-	-	266
16-Jan-25	14	129	97	----------	----------	240
17-Jan-25	38	153	116	----------	----------	307
18-Jan-25	20	83	96	----------	----------	199
19-Jan-25	12	55	50	----------	----------	116
20-Jan-25	17	41	57	----------	----------	114
21-Jan-25	19	40	56	----------	----------	115
22-Jan-25	21	65	61	----------	----------	146
23-Jan-25	27	134	70	----------	----------	231
24-Jan-25	22	163	80	----------	----------	265
25-Jan-25	5	99	65	----------	----------	168
26-Jan-25	4	57	83	----------	----------	144
27-Jan-25	4	31	57	----------	----------	93
28-Jan-25	7	24	49	----------	----------	79
29-Jan-25	13	36	69	----------	----------	117
30-Jan-25	21	50	49	----------	----------	120
31-Jan-25	10	65	41	----------	----------	116
कुल TOTAL	483	2608	2247	----------	----------	5338
उच्चतम MAXIMUM	38	163	116	----------	----------	307
निम्नतम MINIMUM	4	24	41	----------	----------	79
औसत AVERAGE	16	84	72	----------	----------	172
संचयी 2024-25 Cumulative 2024-25	5942	31906	32928	----------	----------	70776
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: जनवरी 2025 MONTH:- JAN 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jan-25	145	96	126	2.9	0.9	371
02-Jan-25	131	103	124	3.1	0.9	361
03-Jan-25	145	103	136	3.2	1.0	389
04-Jan-25	144	103	143	3.0	1.1	394
05-Jan-25	120	92	142	2.6	1.1	358
06-Jan-25	147	96	138	2.7	1.0	385
07-Jan-25	152	101	133	2.5	0.8	389
08-Jan-25	163	106	135	3.1	0.5	408
09-Jan-25	159	106	126	2.7	0.9	395
10-Jan-25	152	90	110	3.1	1.1	356
11-Jan-25	127	86	84	3.2	1.1	301
12-Jan-25	103	87	108	2.8	1.1	302
13-Jan-25	92	92	109	2.7	0.9	296
14-Jan-25	143	95	95	2.6	0.9	336
15-Jan-25	142	84	97	2.3	1.2	327
16-Jan-25	153	95	111	3.0	1.2	363
17-Jan-25	150	100	123	2.6	1.1	377
18-Jan-25	149	101	100	2.9	1.1	354
19-Jan-25	151	105	84	3.6	1.1	344
20-Jan-25	134	104	125	3.3	1.0	368
21-Jan-25	163	104	140	3.2	1.0	411
22-Jan-25	165	105	122	3.6	0.9	396
23-Jan-25	170	108	128	3.2	0.8	409
24-Jan-25	184	110	142	3.0	0.5	439
25-Jan-25	188	113	141	3.4	0.8	447
26-Jan-25	188	119	149	3.4	0.9	461
27-Jan-25	184	114	145	3.5	0.9	447
28-Jan-25	182	112	140	3.4	0.8	438
29-Jan-25	178	115	135	3.3	0.7	432
30-Jan-25	155	116	125	3.2	0.6	399
31-Jan-25	142	108	135	2.9	0.6	388
कुल TOTAL	4698	3169	3852	94	28	11841
उच्चतम MAXIMUM	188	119	149	3.6	1.2	461
निम्नतम MINIMUM	92	84	84	2.3	0.5	296
औसत AVERAGE	152	102	124	3.0	0.9	382
संचयी 2024-25 Cumulative 2024-25	45922	25532	34447	895	285.4	107081
अब तक का उच्चतम All Time Max.	**188**	**119**	**149**	4.1	3.5	**461**
दिनांक Date	**25.01.25**	**26.01.25**	**26.01.25**	09.06.24	08.09.24	**26.01.25**

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: जनवरी 2025 MONTH:- JAN 2025

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फ़ैक्टर Diversity Factor*
01-Jan-25	66290	68262	57353	22228	2577	214654	1.010
02-Jan-25	64717	70295	57767	23179	2853	215044	1.018
03-Jan-25	68397	71889	58823	22979	2905	221646	1.015
04-Jan-25	64701	73377	57703	23810	2796	219312	1.014
05-Jan-25	62835	72160	56020	22645	2686	213661	1.013
06-Jan-25	66048	74247	60056	23032	2765	223964	1.010
07-Jan-25	68022	75968	60527	23461	2731	228072	1.012
08-Jan-25	67855	74487	60835	23940	2843	227199	1.012
09-Jan-25	66234	75743	60915	23571	2901	226967	1.011
10-Jan-25	68515	77085	61537	23624	2842	230846	1.012
11-Jan-25	65377	77613	59204	23940	2794	226006	1.013
12-Jan-25	58925	75231	57868	23217	2653	214043	1.018
13-Jan-25	62575	75999	58580	23639	2761	220650	1.013
14-Jan-25	64276	71236	56293	23449	2657	215557	1.011
15-Jan-25	64882	74075	54933	23654	2765	216777	1.016
16-Jan-25	63745	76019	57421	23527	3000	220355	1.015
17-Jan-25	66397	77797	59663	23261	2866	227245	1.012
18-Jan-25	65288	78120	59402	23521	2877	225118	1.018
19-Jan-25	63463	76931	55526	22802	2753	218369	1.014
20-Jan-25	63805	77786	57595	24358	2895	222178	1.019
21-Jan-25	65090	78593	58668	24570	2779	226044	1.016
22-Jan-25	65740	78896	59569	24239	2905	228085	1.014
23-Jan-25	64555	78735	60609	23599	2878	227352	1.013
24-Jan-25	66133	79254	61891	24373	2895	231215	1.014
25-Jan-25	65469	79214	60963	24446	2903	229686	1.014
26-Jan-25	66446	71834	56183	22823	2596	217830	1.009
27-Jan-25	66891	78710	61268	23541	2900	230451	1.012
28-Jan-25	68592	79772	62267	23450	2896	234950	1.009
29-Jan-25	70208	79919	63519	24196	2929	237309	1.015
30-Jan-25	67960	79688	62950	23972	2916	234525	1.013
31-Jan-25	68711	79132	64875	23493	2871	236822	1.010
उच्चतम MAXIMUM	70208	79919	64875	24570	3000	237309	1.019
निम्नतम MINIMUM	58925	68262	54933	22228	2577	213661	1.009
औसत AVERAGE	65746	76067	59380	23566	2819	224578	1.013
अब तक का उच्चतम All Time Max.	91215	**79919**	68735	32531	3905	250070	
दिनांक Date	19.06.24	**29.01.25**	13.03.24	10.06.24	19.09.24	30.05.24	


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 29th JAN (MAXIMUM DEMAND MET)

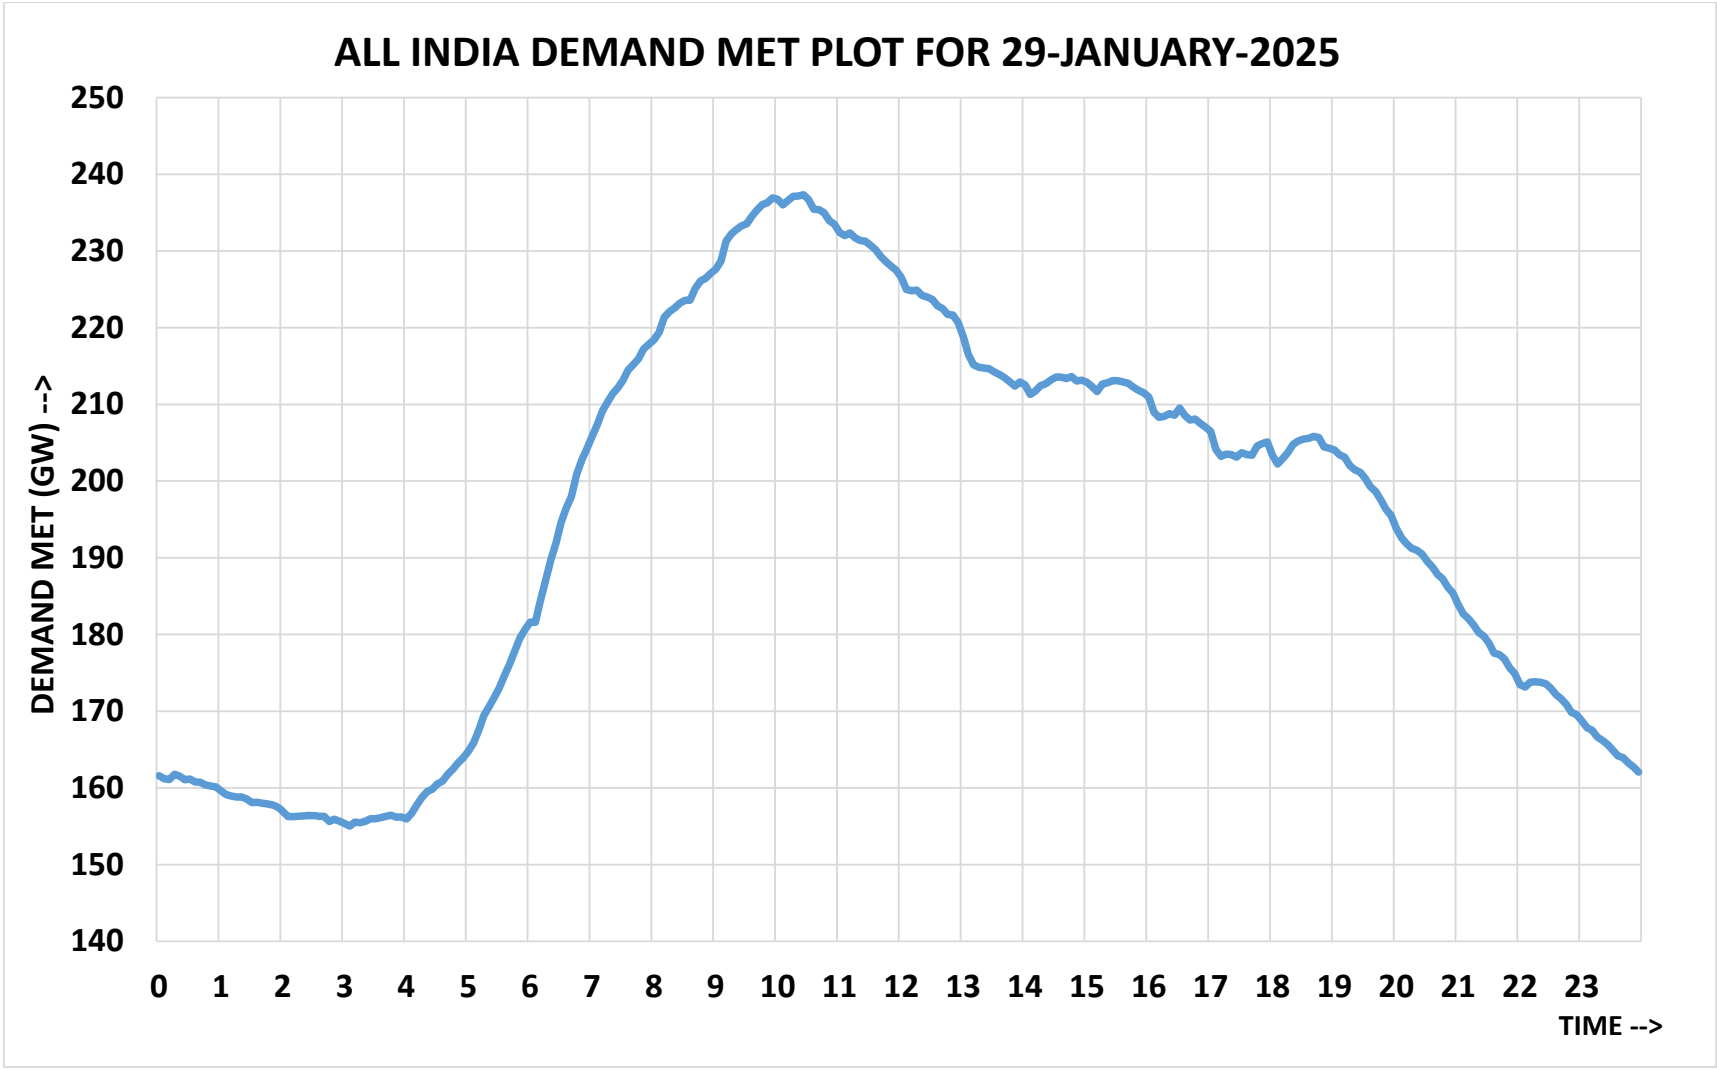

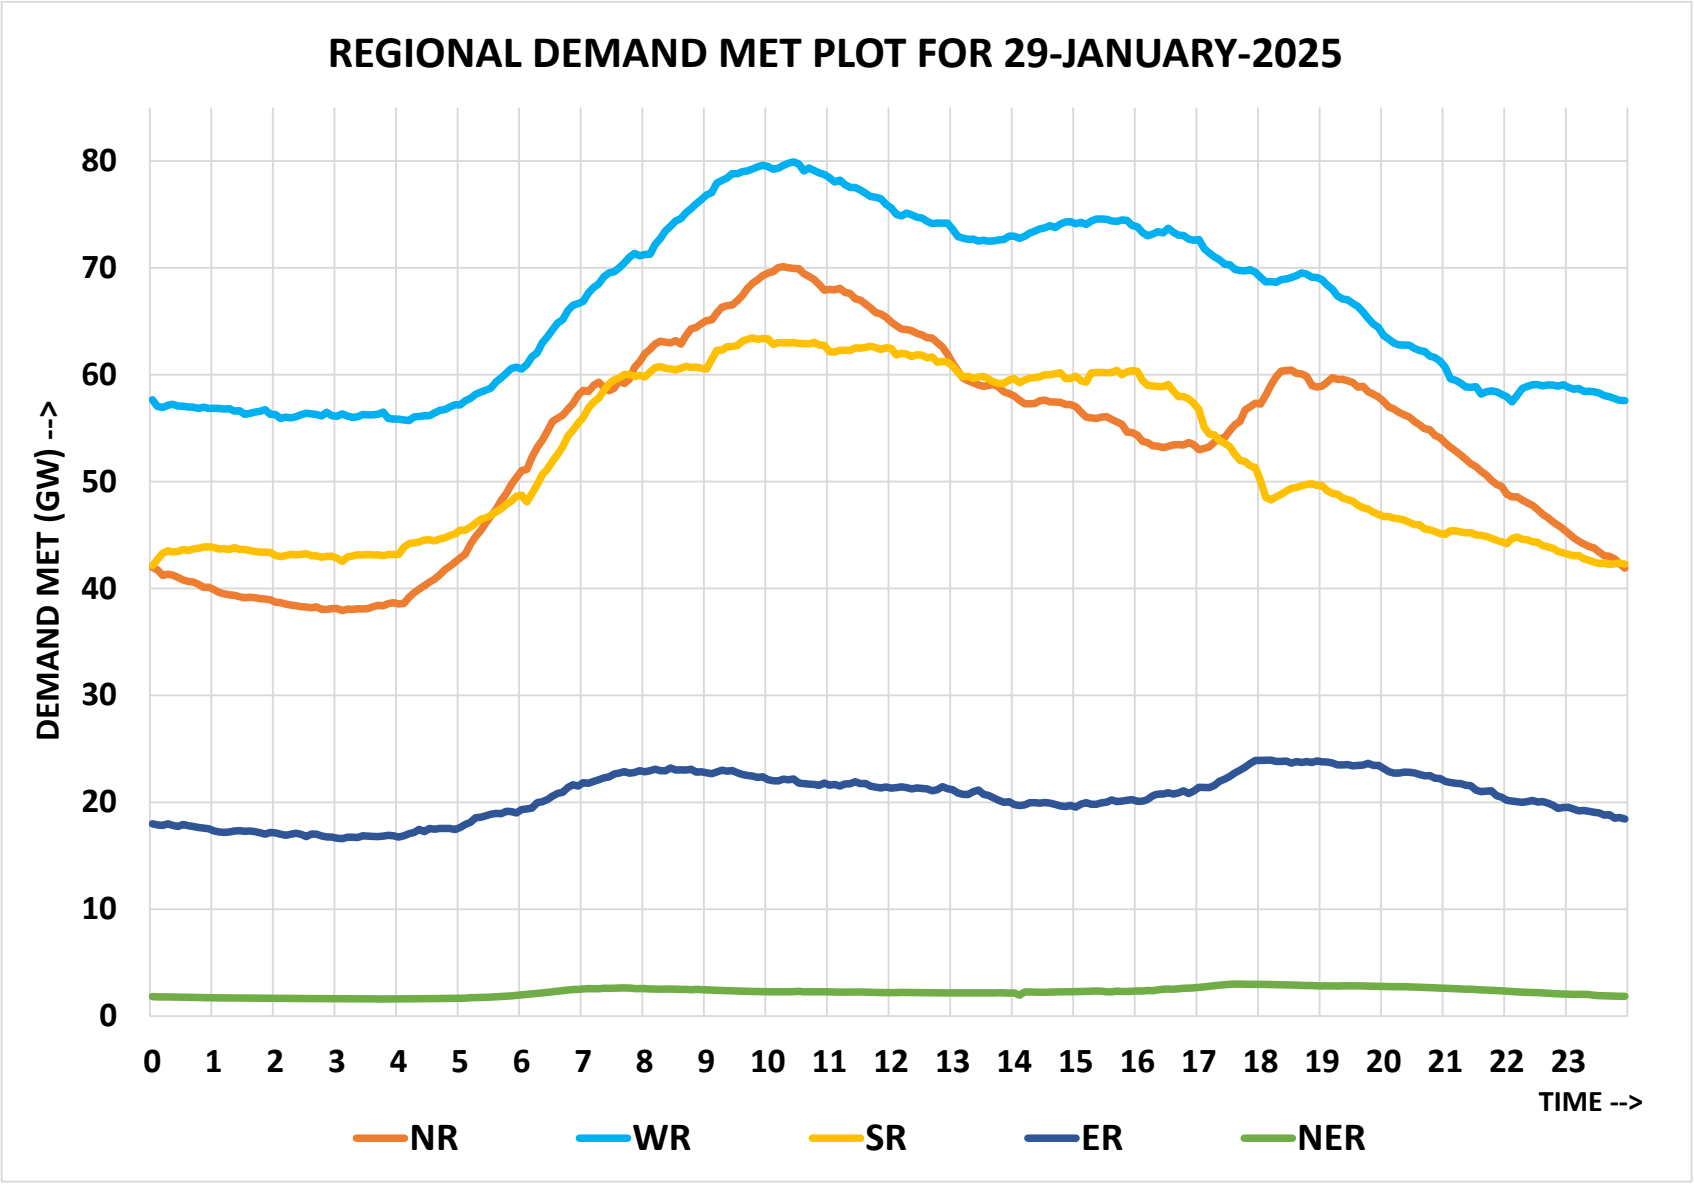
REGIONAL DEMAND MET PLOT FOR 29-JANUARY-2025
DEMAND MET (GW) -->
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

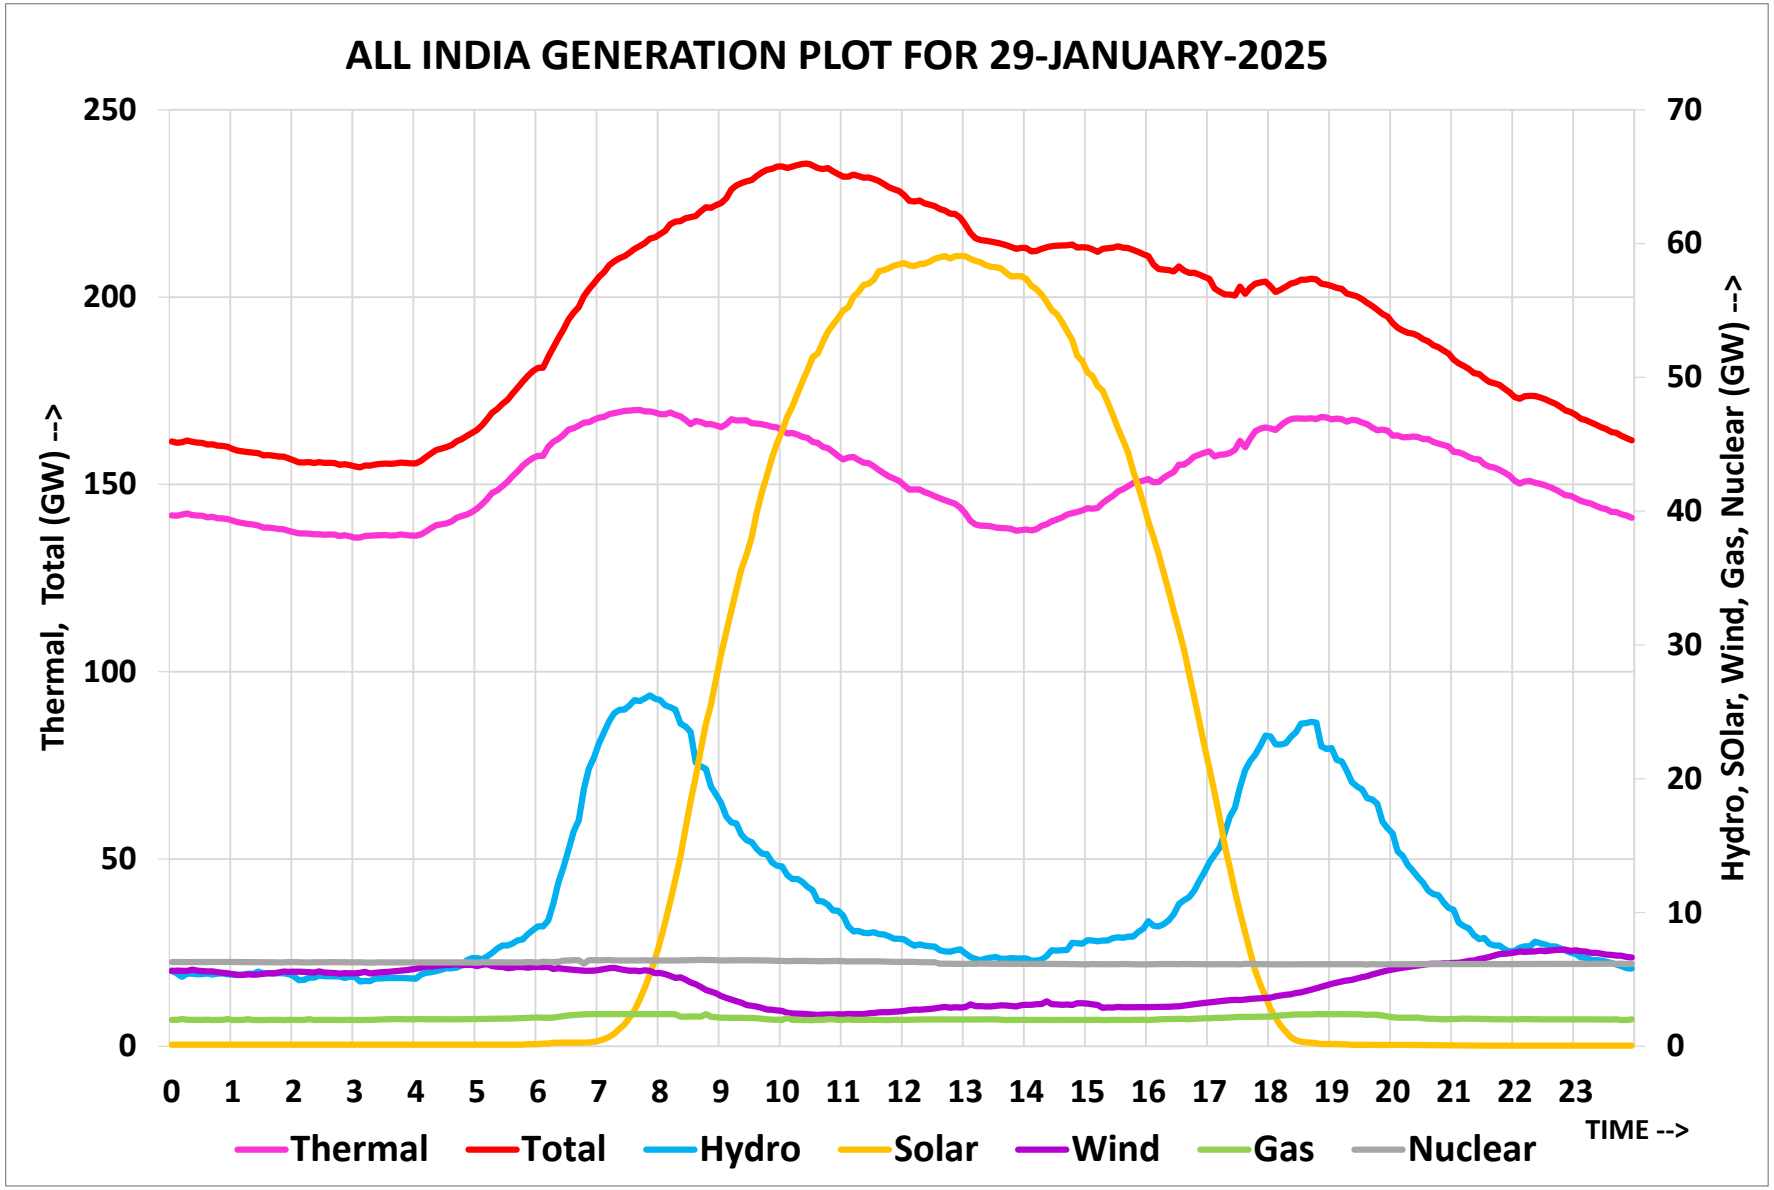
ALL INDIA GENERATION PLOT FOR 29-JANUARY-2025
Thermal, Total (GW) -->
Hydro, SOlar, Wind, Gas, Nuclear (GW) -->
250
200
150
100
50
0
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Thermal
Total
Hydro
Solar
Wind
Gas
Nuclear

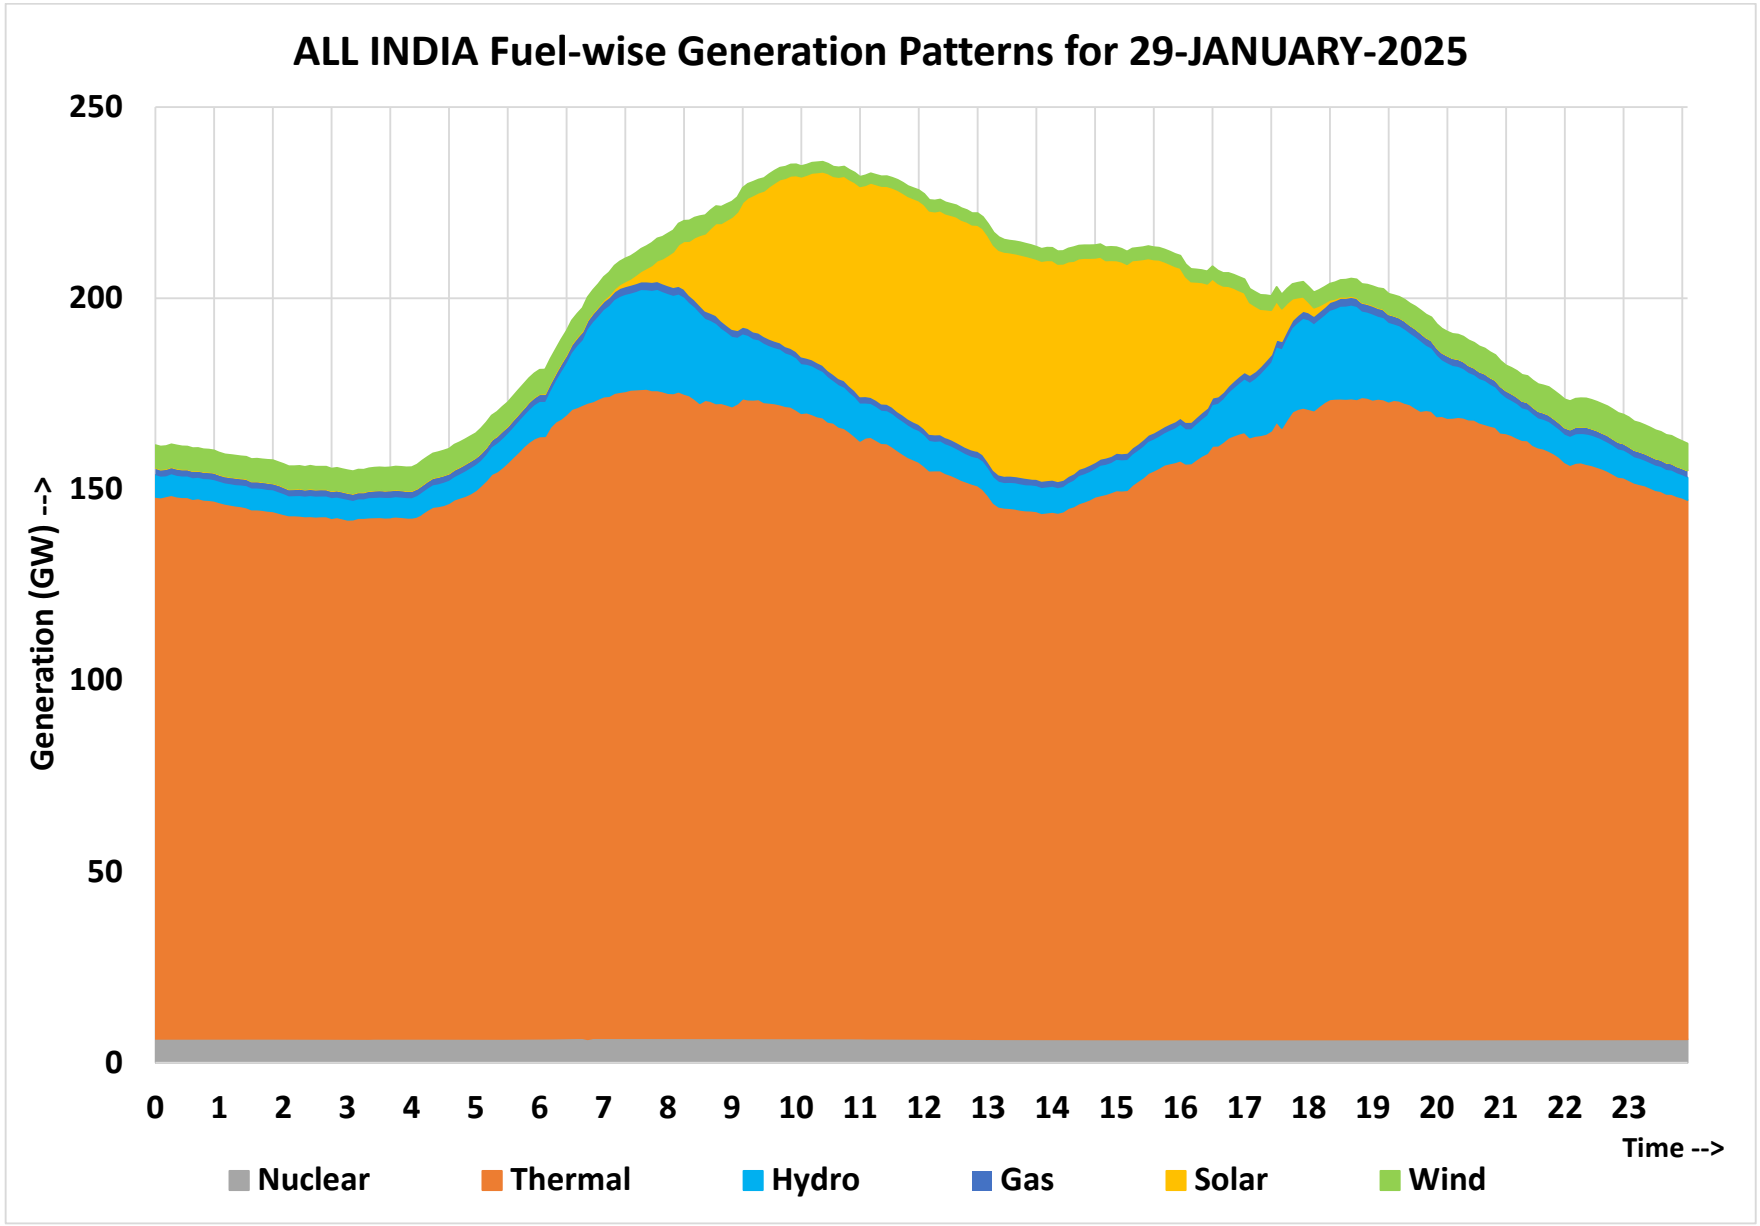
ALL INDIA Fuel-wise Generation Patterns for 29-JANUARY-2025
Generation (GW) -->
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
Time -->
Nuclear
Thermal
Hydro
Gas
Solar
Wind

29 जनवरी 2025 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 29 JANUARY 2025 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	161177		**12:05**	224999
00:20	161524		**12:20**	224211
00:35	160775		**12:35**	222844
00:50	160250		**12:50**	221653
01:05	159119		**13:05**	216520
01:20	158800		**13:20**	214750
01:35	158121		**13:35**	213895
01:50	157809		**13:50**	212400
02:05	156252		**14:05**	211290
02:20	156356		**14:20**	212696
02:35	156297		**14:35**	213541
02:50	155903		**14:50**	213060
03:05	155021		**15:05**	212334
03:20	155640		**15:20**	212831
03:35	156111		**15:35**	212927
03:50	156185		**15:50**	211850
04:05	156685		**16:05**	208981
04:20	159512		**16:20**	208792
04:35	160862		**16:35**	208535
04:50	163253		**16:50**	207523
05:05	165859		**17:05**	204146
05:20	170599		**17:20**	203467
05:35	174652		**17:35**	203465
05:50	179506		**17:50**	204895
06:05	181600		**18:05**	202217
06:20	189751		**18:20**	204786
06:35	196494		**18:35**	205552
06:50	202748		**18:50**	204470
07:05	207361		**19:05**	203440
07:20	211383		**19:20**	201457
07:35	214483		**19:35**	199267
07:50	217237		**19:50**	196330
08:05	219422		**20:05**	192621
08:20	222566		**20:20**	190981
08:35	223592		**20:35**	188812
08:50	226427		**20:50**	186177
09:05	228686		**21:05**	182689
09:20	232776		**21:20**	180255
09:35	234518		**21:35**	177572
09:50	236301		**21:50**	175667
10:05	236012		**22:05**	173127
10:20	237163		**22:20**	173767
10:35	235437		**22:35**	172150
10:50	233965		**22:50**	169822
11:05	232019		**23:05**	167846
11:20	231372		**23:20**	166188
11:35	230148		**23:35**	164168
11:50	228043		**23:50**	162741
Maximum Demand of 237309 MW met@10:24 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - JANUARY 2025

REGION	STATE	Energy Requirement & Met (MU/Day)			Energy Requirement & Met (MU)				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	138	138	0	0.0	312	312	0	0.0
	Delhi	83	83	0.0	2584	2584	0	0.0	5655	5655	0	0.0
	Haryana	153	152	0.0	4728	4727	0	0.0	9157	9157	0	0.0
	Himachal Pradesh	38	38	0.0	1178	1178	0	0.0	2273	2273	0	0.0
	J&K(UT) and Ladakh(UT)	67	67	-0.1	2080	2076	-4	-0.2	3148	3148	0	0.0
	Punjab	154	154	0.0	4759	4759	0	0.0	10142	10142	0	0.0
	Rajasthan	326	326	0.0	10114	10114	0	0.0	18572	18572	0	0.0
	Uttar Pradesh	365	364	-0.1	11301	11299	-2	0.0	22034	22034	0	0.0
	Uttarakhand	44	44	0.0	1376	1376	0	0.0	2568	2568	0	0.0
	Railway_NR ISTS	4	4	0.0	124	124	0	0.0	228	228	0	0.0
	NFL	0	0	0.0	3	3	0	0.0	5	5	0	0.0
	TOTAL	1238	1238	-0.2	38383	38377	-6	0.0	69164	69109	-55	-0.1
WR	Gujarat	414	414	0.0	12839	12839	0	0.0	23929	23929	0	0.0
	Madhya Pradesh	325	324	-0.5	10071	10055	-17	-0.2	18591	18580	-11	-0.1
	Chhattisgarh	113	113	-0.1	3514	3511	-3	-0.1	5906	5890	-16	-0.3
	Maharashtra	593	593	0.0	18397	18397	0	0.0	29826	29826	0	0.0
	Goa	14	14	0.0	444	444	0	0.0	754	754	0	0.0
	DNHDDPDCL	30	30	0.0	922	922	0	0.0	1353	1353	0	0.0
	AMNSIL	17	17	0.0	518	518	0	0.0	806	806	0	0.0
	BALCO	13	13	0.0	393	393	0	0.0	535	535	0	0.0
	RIL JAMNAGAR*	3	3	0.0	94	94	0	0.0	188	188	0	0.0
	TOTAL	1474	1522	48.2	45679	47173	1494	3.3	80613	80585	-28	0.0
SR	Andhra Pradesh	207	205	-1.7	6408	6357	-52	-0.8	12027	12027	0	0.0
	Telangana	269	267	-1.9	8330	8272	-58	-0.7	15205	15205	0	0.0
	Karnataka	286	284	-2.1	8866	8802	-64	-0.7	17691	17691	0	0.0
	Kerala	85	84	-0.7	2622	2602	-20	-0.8	4520	4520	0	0.0
	Tamil Nadu	316	313	-2.5	9795	9717	-78	-0.8	17279	17279	0	0.0
	Puducherry	8	8	-0.1	260	258	-2	-0.8	451	450	-1	-0.3
	TOTAL	1170	1162	-8.8	36282	36008	-274	-0.8	64940	64845	-95	-0.1
ER	Bihar	99	99	-0.6	3084	3065	-19	-0.6	5672	5672	0	0.0
	Jharkhand	39	39	0.0	1215	1215	0	0.0	2161	2161	0	0.0
	DVC	70	70	0.0	2176	2176	0	0.0	3475	3475	0	0.0
	Odisha	101	101	0.0	3130	3130	0	0.0	5598	5598	0	0.0
	West Bengal	153	153	0.0	4740	4740	0	0.0	7843	7843	0	0.0
	Sikkim	2	2	0.0	60	60	0	0.0	134	134	0	0.0
	Railways_ER ISTS	0	0	0.0	6	6	0	0.0	36	36	0	0.0
	TOTAL	465	464	-0.6	14411	14392	-19	-0.1	24616	24616	0	0.0
NER	Arunachal Pradesh	3	3	0.0	95	95	0	0.0	196	196	0	0.0
	Assam	28	28	0.0	853	853	0	0.0	1581	1561	-20	-1.3
	Manipur	4	4	0.0	114	114	0	0.0	267	267	0	0.0
	Meghalaya	7	7	0.0	204	204	0	0.0	393	393	0	0.0
	Mizoram	2	2	0.0	70	70	0	0.0	168	168	0	0.0
	Nagaland	2	2	0.0	75	75	0	0.0	172	159	-13	-7.6
	Tripura	4	4	0.0	128	128	0	0.0	234	234	0	0.0
	TOTAL	50	50	0.0	1539	1539	0	0.0	2941	2941	0	0.0
ALL INDIA		4397	4435	38.5	136293	137488	1195	0.9				

* RIL Jamnagar has been added as new entity wef 01.12.2024

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF JANUARY 2025 vs JANUARY 2024

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Jan-24	Jan-25	Difference	% Change	Average MU/day for Oct-24	Jan-24	Jan-25	Difference	% Change	Average MU/day for Oct-24
NR	Chandigarh	158	138	-20	-13	4	117	138	20	17	4
	Delhi	2732	2584	-148	-5	83	2211	2584	373	17	83
	Haryana	4991	4728	-263	-5	153	4446	4727	281	6	152
	Himachal Pradesh	1148	1178	30	3	38	1125	1178	53	5	38
	J&K(UT) and Ladakh(UT)	2032	2080	47	2	67	1809	2076	267	15	67
	Punjab	4942	4759	-183	-4	154	4402	4759	356	8	154
	Rajasthan	10171	10114	-57	-1	326	9339	10114	775	8	326
	Uttar Pradesh	11619	11301	-318	-3	365	9799	11299	1501	15	364
	Uttarakhand	1439	1376	-62	-4	44	1277	1376	99	8	44
	Railway_NR ISTS/NFL	106	126	20	19	4	108	126	18	17	4
	TOTAL	39337	38383	-954	-2	1238	34634	38377	3743	11	1238
WR	Gujarat	12383	12839	456	4	414	11958	12839	880	7	414
	Madhya Pradesh	9588	10071	483	5	325	8772	10055	1282	15	324
	Chhattisgarh	3203	3514	311	10	113	2782	3511	729	26	113
	Maharashtra	17476	18397	921	5	593	16295	18397	2102	13	593
	Goa	401	444	44	11	14	414	444	30	7	14
	DNHDDPDCL	879	922	43	5	30	881	922	41	5	30
	AMNSIL	578	518	-61	-10	17	587	518	-70	-12	17
	BALCO	386	393	7	2	13	386	393	7	2	13
	RIL JAMNAGAR*	-	-	-	-	-	-	-	-	-	-
	TOTAL	44895	45679	784	2	1474	42076	47173	5097	12	1522
SR	Andhra Pradesh	6482	6408	-74	-1	207	5756	6357	600	10	205
	Telangana	7663	8330	667	9	269	6526	8272	1746	27	267
	Karnataka	8389	8866	477	6	286	7892	8802	910	12	284
	Kerala	2550	2622	72	3	85	2547	2602	55	2	84
	Tamil Nadu	9658	9795	137	1	316	9278	9717	439	5	313
	Puducherry	257	260	3	1	8	263	258	-5	-2	8
	TOTAL	34999	36282	1282	4	1170	32261	36008	3747	12	1162
ER	Bihar	3077	3084	7	0	99	2589	3065	476	18	99
	Jharkhand	1052	1215	163	16	39	923	1215	292	32	39
	DVC	2207	2176	-31	-1	70	2181	2176	-5	0	70
	Odisha	2925	3130	205	7	101	2961	3130	169	6	101
	West Bengal	4428	4740	312	7	153	4053	4740	688	17	153
	Sikkim	61	60	-1	-1	2	52	60	8	15	2
	Railways_ER ISTS	4	6	2	55	0	4	6	2	51	0
	TOTAL	13754	14411	657	5	465	12762	14392	1630	13	464
NER	Arunachal Pradesh	89	95	6	7	3	83	95	12	14	3
	Assam	837	853	16	2	28	816	853	37	4	28
	Manipur	104	114	10	10	4	91	114	23	25	4
	Meghalaya	201	204	4	2	7	198	204	7	3	7
	Mizoram	70	70	0	0	2	52	70	18	34	2
	Nagaland	71	75	4	5	2	72	75	2	3	2
	Tripura	122	128	6	5	4	121	128	8	6	4
	TOTAL	1493	1539	46	3	50	1433	1539	105	7	50
ALL INDIA		134478	136293	1816	1	4397	123167	137488	14321	12	4435

* RIL Jamnagar has been added as new entity wef 01.12.2024

13. DEMAND COMPARISON OF JANUARY 2025 vs JANUARY 2024

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Jan-24	Jan-25	Difference	% Change	Jan-24	Jan-25	Difference	% Change
NR	Chandigarh	348	312	-36	-10.3	201	312	111	55.2
	Delhi	5816	5655	-161	-2.8	4582	5655	1073	23.4
	Haryana	9530	9157	-373	-3.9	8225	9157	932	11.3
	Himachal Pradesh	2181	2273	92	4.2	2162	2273	111	5.1
	J&K(UT) and Ladakh(UT)	3181	3148	-33	-1.0	2904	3148	244	8.4
	Punjab	9370	10142	772	8.2	8041	10142	2101	26.1
	Rajasthan	18128	18572	444	2.4	17570	18572	1002	5.7
	Uttar Pradesh	22703	22034	-669	-2.9	19874	22034	2160	10.9
	Uttarakhand	2635	2568	-67	-2.5	2417	2568	151	6.2
	Railway_NR ISTS/NFL	212	233	21	9.7	222	233	11	5.0
WR	Gujarat	21861	23929	2068	9	21408	23929	2521	11.8
	Madhya Pradesh	18252	18591	339	2	17819	18580	761	4.3
	Chhattisgarh	5338	5906	569	11	4833	5890	1057	21.9
	Maharashtra	28651	29826	1175	4	27755	29826	2071	7.5
	Goa	721	754	34	5	704	754	51	7.2
	DNHDDPDCL	1294	1353	59	4.6	1281	1353	72	5.6
	AMNSIL	1083	806	-277	-25.6	901	806	-95	-10.6
	BALCO	526	535	9	1.8	532	535	3	0.5
	RIL JAMNAGAR*	-	-	-	-	-	-	-	-
SR	Andhra Pradesh	11052	12027	975	8.8	12085	12027	-58	-0.5
	Telangana	12666	15205	2539	20.0	11857	15205	3348	28.2
	Karnataka	15668	17691	2022	12.9	15005	17691	2686	17.9
	Kerala	4354	4520	166	3.8	4275	4520	245	5.7
	Tamil Nadu	15920	17279	1359	8.5	16099	17279	1180	7.3
	Puducherry	439	451	12	2.7	418	450	32	7.7
ER	Bihar	5625	5672	47	0.8	4963	5672	709	14.3
	Jharkhand	1805	2161	356	19.7	1827	2161	334	18.3
	DVC	3251	3475	224	6.9	3493	3475	-18	-0.5
	Odisha	5051	5598	547	10.8	5578	5598	20	0.4
	West Bengal	7281	7843	562	7.7	7096	7843	747	10.5
	Sikkim	137	134	-3	-2.2	115	134	19	16.5
	Railways_ER ISTS	20	36	16	80.0	27	36	9	33.3
NER	Arunachal Pradesh	181	196	15	8.0	163	196	33	20.0
	Assam	1538	1581	43	2.8	1553	1561	8	0.5
	Manipur	258	267	9	3.5	235	267	32	13.6
	Meghalaya	405	393	-12	-3.1	349	393	44	12.5
	Mizoram	162	168	6	3.6	140	168	28	19.9
	Nagaland	162	172	10	6.0	157	159	2	1.1
	Tripura	235	234	-1	-0.6	239	234	-5	-2.3

* RIL Jamnagar has been added as new entity wef 01.12.2024

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - JANUARY 2025

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	140.85	141.62	0.77	0.55	4.54	4.57	0.02
	Delhi	2491.01	2460.54	-30.47	-1.22	80.36	79.37	-0.98
	Haryana	3202.84	3182.70	-20.14	-0.63	103.32	102.67	-0.65
	Himachal Pradesh	986.95	964.75	-22.20	-2.25	31.84	31.12	-0.72
	J&K(UT) and Ladakh(UT)	2003.12	1952.30	-50.82	-2.54	64.62	62.98	-1.64
	Punjab	2077.66	2026.57	-51.09	-2.46	67.02	65.37	-1.65
	Rajasthan	3367.32	3304.32	-63.00	-1.87	108.62	106.59	-2.03
	Uttar Pradesh	3838.43	3805.01	-33.42	-0.87	123.82	122.74	-1.08
	Uttarakhand	1110.81	1114.11	3.30	0.30	35.83	35.94	0.11
	Railways_NR ISTS	116.29	123.60	7.32	6.29	3.75	3.99	0.24
	NFL	2.98	2.79	-0.19	-6.23	0.10	0.09	-0.01
	Total	19338.25	19078.31	-259.94	-1.34	623.81	615.43	-8.39
WR	Gujarat	5748.18	5639.75	-108.43	-1.89	185.43	181.93	-3.50
	Madhya Pradesh	6295.90	6228.37	-67.53	-1.07	203.09	200.92	-2.18
	Chhattisgarh	1946.20	1951.30	5.10	0.26	62.78	62.95	0.16
	Maharashtra	6445.30	6474.01	28.71	0.45	207.91	208.84	0.93
	Goa	421.65	430.64	8.99	2.13	13.60	13.89	0.29
	DNHDDPDCL	927.91	921.75	-6.16	-0.66	29.93	29.73	-0.20
	AMNSIL	220.06	235.68	15.62	7.10	7.10	7.60	0.50
	BALCO	393.50	392.95	-0.55	-0.14	12.69	12.68	-0.02
	RIL JAMNAGAR*	95.03	94.09	-0.94	-0.99	3.07	3.04	-0.03
	Total	22493.73	22368.55	-125.18	-0.56	725.60	721.57	-4.04
SR	Andhra Pradesh	1598.66	1581.59	-17.07	-1.07	51.57	51.02	-0.55
	Telangana	4473.55	4445.05	-28.50	-0.64	144.31	143.39	-0.92
	Karnataka	2791.30	2781.82	-9.48	-0.34	90.04	89.74	-0.31
	Kerala	2058.76	2088.73	29.97	1.46	66.41	67.38	0.97
	Tamil Nadu	5367.18	5320.55	-46.63	-0.87	173.13	171.63	-1.50
	Puducherry	246.79	240.02	-6.77	-2.74	7.96	7.74	-0.22
	Goa (SR)	71.74	68.64	-3.10	-4.32	2.31	2.21	-0.10
	Total	16607.98	16526.40	-81.58	-0.49	535.74	533.11	-2.63
ER	Bihar	2824.84	2704.05	-120.79	-4.28	91.12	87.23	-3.90
	Jharkhand	875.87	870.99	-4.87	-0.56	28.25	28.10	-0.16
	DVC	-1187.11	-1196.63	-9.52	0.80	-38.29	-38.60	-0.31
	Odisha	1050.62	995.50	-55.12	-5.25	33.89	32.11	-1.78
	West Bengal	704.93	658.01	-46.92	-6.66	22.74	21.23	-1.51
	Sikkim	59.26	59.78	0.52	0.88	1.91	1.93	0.02
	Railways_ER ISTS	5.11	5.70	0.59	11.57	0.16	0.18	0.02
	Total	4333.50	4097.40	-236.10	-5.45	139.79	132.17	-7.62
NER	Arunachal Pradesh	94.67	90.88	-3.79	-4.00	3.05	2.93	-0.12
	Assam	637.32	654.48	17.16	2.69	20.56	21.11	0.55
	Manipur	119.86	114.28	-5.58	-4.66	3.87	3.69	-0.18
	Meghalaya	166.97	162.37	-4.60	-2.75	5.39	5.24	-0.15
	Mizoram	57.51	53.05	-4.46	-7.76	1.86	1.71	-0.14
	Nagaland	73.97	72.29	-1.68	-2.27	2.39	2.33	-0.05
	Tripura	101.03	102.67	1.64	1.62	3.26	3.31	0.05
	Total	1251.33	1250.02	-1.31	-0.10	40.37	40.32	-0.04
All India Total		64024.79	63320.68	-704.11	-1.10	2065.32	2042.60	-22.71

* RIL Jamnagar has been added as new entity wef 01.12.2024

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Fin. Year 2024-25
Name of Line											
Import of NR from WR (WR-NR)											
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	714.49	611.32	751.39	877.91	**9557.56**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	840.34	817.51	665.18	664.69	**5731.41**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	1009.96	819.22	774.41	896.18	**9454.07**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	583.07	599.61	586.45	592.74	**6015.86**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	1570.74	720.37	1288.63	1766.28	**18834.61**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	0.00	39.19	106.05	66.90	**828.38**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	0.00	0.00	3.10	6.27	**237.84**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	17.54	0.00	1.08	0.00	**64.64**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	60.41	0.08	2.44	3.06	**599.88**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	60.83	64.26	52.46	55.29	**597.64**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	58.67	96.18	95.67	89.99	**701.37**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	0.00	0.00	0.00	0.00	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	1096.69	827.50	752.53	932.98	**10021.66**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	0.00	0.00	74.13	63.08	**1628.99**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	1113.89	1038.27	1036.90	1223.28	**15437.17**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	89.57	0.00	0.00	2.06	**652.65**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**7216.20**	**5633.51**	**6190.42**	**7240.71**	**80379.95**
Export of NR to WR (NR-WR)											
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	0.00	0.00	0.00	0.00	**14.99**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	368.54	423.95	433.38	445.77	**3370.41**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	152.00	95.38	6.70	29.25	**774.18**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	126.24	173.03	73.94	111.69	**949.59**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	31.75	9.91	2.04	0.00	**103.36**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	1.94	45.97	66.66	68.78	**408.07**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	51.59	74.53	67.31	56.48	**413.91**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	0.00	561.44	663.38	663.39	**4796.36**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	391.69	523.07	148.17	268.25	**2492.67**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	0.00	51.46	94.50	73.95	**415.25**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**1123.75**	**1958.74**	**1556.08**	**1717.56**	**13738.79**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Fin. Year 2024-25
Name of Line											
Import of NR from ER (ER-NR)											
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	139.89	211.26	229.72	252.28	**1495.30**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	405.62	482.45	443.73	383.69	**2369.34**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	366.56	351.78	368.50	379.86	**3259.32**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	250.72	211.75	12.40	0.00	**1669.22**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	527.53	418.43	523.23	391.61	**3484.58**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	319.38	212.80	260.15	218.85	**2343.08**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	95.04	41.13	143.70	118.35	**503.31**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	259.86	222.85	283.52	223.81	**1965.61**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	0.00	0.94	0.00	0.00	**11.61**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	136.66	108.64	109.12	58.92	**670.84**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	65.13	77.91	68.47	15.73	**311.02**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	7.45	17.59	22.02	55.47	**229.41**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	0.53	0.00	0.48	0.00	**14.58**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	0.00	0.00	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	159.57	132.81	163.60	118.51	**995.32**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	144.05	156.95	159.21	103.16	**910.17**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**2877.99**	**2647.29**	**2787.85**	**2320.24**	**20234.32**
Import of NR from NER (NER-NR)											
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55	555.71	550.01	30.48	0.00	**2232.99**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**555.71**	**550.01**	**30.48**	**0.00**	**2232.99**
Export of NR to ER (NR-ER)											
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	0.00	0.00	0.00	0.00	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	0.00	0.00	0.00	0.00	**225.17**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**119.80**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	7.00	8.26	0.00	0.00	**409.05**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	0.00	0.88	0.00	0.00	**19.94**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	0.00	0.20	0.00	0.00	**7.33**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	0.00	0.00	0.00	3.47	**48.21**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	4.74	0.65	0.00	0.00	**9.05**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	0.48	0.00	0.60	0.00	**3.86**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	0.58	0.91	1.34	1.87	**8.97**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	14.57	14.82	16.20	17.43	**162.38**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	0.00	0.00	0.00	0.00	**6.54**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**27.37**	**25.72**	**18.14**	**22.77**	**1044.23**
Export of NR to NER (NER-NR)											
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	0.00	0.00	445.16	486.19	**2296.88**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**0.00**	**0.00**	**445.16**	**486.19**	**2296.88**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Fin. Year 2024-25
Name of Line											
Export of WR to ER (WR-ER)											
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	308.09	84.78	53.41	160.01	**5548.21**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	65.67	50.80	64.41	152.97	**2060.02**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	0.04	0.00	0.00	0.00	**37.15**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	29.14	9.49	3.76	24.77	**1121.04**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	0.51	1.58	0.03	0.03	**651.81**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	4.23	14.85	12.46	29.24	**116.19**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	0.05	0.60	0.00	0.01	**15.61**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**407.73**	**162.10**	**134.08**	**367.02**	**9550.03**
Import of WR from ER (ER - WR)											
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	68.03	111.05	218.28	108.43	**616.45**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	334.28	233.51	328.11	139.52	**2769.32**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	325.55	520.92	389.23	539.53	**3188.49**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	59.96	84.87	42.89	57.42	**308.65**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	380.72	297.88	324.60	320.44	**2582.92**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	48.12	15.83	17.45	7.12	**268.07**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	60.23	34.62	45.32	42.62	**397.12**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**1276.89**	**1298.67**	**1365.88**	**1215.08**	**10131.01**
Export of ER to NER (ER - NER)											
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	104.89	226.52	18.80	7.46	**824.53**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	173.82	295.36	19.99	7.41	**1217.37**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	32.38	44.04	2.57	0.68	**239.53**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**311.10**	**565.92**	**41.35**	**15.55**	**2281.42**
Import of ER from NER (NER - ER)											
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	18.09	0.00	87.66	87.40	**645.93**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	17.26	0.00	183.94	165.91	**1080.65**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	2.72	0.00	38.42	37.89	**195.72**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**38.07**	**0.00**	**310.02**	**291.19**	**1922.30**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Fin. Year 2024-25
Name of Line											
Export of ER to SR (ER - SR)											
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	217.59	323.46	231.29	195.73	**2207.88**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	1105.23	1090.58	1197.54	997.29	**9906.10**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	1297.13	1542.96	1693.06	1529.00	**13301.09**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**2619.95**	**2957.00**	**3121.89**	**2722.02**	**25415.08**
Import of ER from SR (SR - ER)											
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	0.00	0.00	0.00	0.00	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	0.00	0.00	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**0.00**	**0.00**	**0.00**	**0.00**	**490.93**
Export of WR to SR (WR-SR)											
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	231.23	335.29	602.14	331.42	**2715.96**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	37.08	143.60	280.25	211.67	**1993.86**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	590.95	779.18	1057.49	959.23	**8184.93**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	0.00	0.00	0.01	0.00	**0.03**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	574.81	746.92	1396.79	1175.06	**10210.37**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	72.89	67.59	70.47	68.17	**669.04**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	0.03	2.33	0.06	6.57	**156.20**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	686.47	951.98	1160.41	1022.37	**8897.48**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**2193.47**	**3026.89**	**4567.60**	**3774.49**	**32827.87**
Import of WR from SR (SR - WR)											
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	18.75	0.00	0.00	20.04	**1655.07**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	410.23	148.25	152.27	240.55	**3756.51**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	11.46	0.85	0.04	3.92	**162.51**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	948.20	690.35	704.16	814.52	**8396.14**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	0.00	0.00	0.00	0.00	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	0.02	0.01	0.01	0.02	**0.09**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	6.77	0.01	0.06	1.54	**166.99**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**1395.43**	**839.47**	**856.54**	**1080.59**	**14555.98**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**20044**	**19665**	**21426**	**21253**	**217102**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during January 2025

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Jan-25	33.31	24.21	32.25	19.74	0.00	48.42	1.24	0.00		0.08	1.31	2.39	0.00	0.00	36.24	0.00	42.28	0.00	**241.47**
2-Jan-25	33.40	26.83	32.68	21.16	0.00	46.51	1.24	0.00		0.70	1.31	2.36	0.00	0.00	36.24	0.00	46.21	0.51	**249.15**
3-Jan-25	36.75	28.86	40.24	21.37	0.00	40.53	1.23	0.00		0.56	1.26	2.45	0.00	0.00	34.96	0.00	44.62	1.12	**253.95**
4-Jan-25	32.99	24.51	36.80	18.37	0.00	41.71	1.24	0.00			1.34	2.72	0.00	0.00	38.25	0.00	34.00	0.43	**232.36**
5-Jan-25	34.62	26.22	38.90	20.33	0.00	36.50	1.23	0.00		0.57	1.31	2.75	0.00	0.00	36.39	0.00	49.34	0.00	**248.16**
6-Jan-25	34.50	20.58	31.29	21.16	0.00	35.17	1.23	0.31			1.32	2.60	0.00	0.00	35.44	8.81	52.30	0.00	**244.71**
7-Jan-25	32.88	19.40	32.63	19.80	0.00	47.96	1.24	3.45		0.00	1.39	2.75	0.00	0.00	24.89	17.26	47.40	0.00	**251.05**
8-Jan-25	31.78	21.04	30.54	20.57	0.00	71.78	1.24	0.00		0.00	1.56	2.45	0.00	0.00	24.19	0.00	45.10	0.00	**250.25**
9-Jan-25	30.58	19.98	29.72	19.92	0.00	80.57	1.24	0.00		0.00	1.68	2.67	0.00	0.00	24.19	0.00	46.90	0.00	**257.45**
10-Jan-25	30.50	23.25	32.51	19.21	0.00	70.85	1.22	0.00		0.00	1.73	2.81	0.00	0.00	31.49	0.00	39.80	0.00	**253.37**
11-Jan-25	26.25	19.85	27.93	17.83	0.00	62.25	1.16	0.00		0.00	1.72	2.84	0.00	0.00	30.07	0.00	35.46	0.00	**225.36**
12-Jan-25	25.44	17.43	23.07	17.76	0.00	61.78	1.24	0.00		0.00	1.67	2.76	0.00	0.00	15.57	0.00	40.40	0.00	**207.12**
13-Jan-25	33.46	21.41	33.39	19.86	0.00	37.20	1.22	1.05		0.00	1.72	2.79	0.00	0.00	28.68	11.47	43.37	0.00	**235.62**
14-Jan-25	37.51	19.09	35.21	18.52	0.00	35.29	1.24	0.66		0.23	1.68	2.49	0.00	0.00	29.58	8.29	48.51	0.00	**238.30**
15-Jan-25	39.93	22.87	40.08	20.44	0.00	48.44	1.25	0.80		0.92	1.49	2.44	0.00	0.00	11.76	8.19	50.63	0.00	**249.24**
16-Jan-25	33.63	19.09	34.00	20.04	0.00	50.27	2.34	0.00		0.00	1.58	2.75	0.00	0.00	36.67	2.30	53.07	0.00	**255.74**
17-Jan-25	32.54	16.39	27.90	19.39	0.00	56.20	7.23	0.00		0.00	1.79	2.94	0.00	0.00	38.10	1.03	49.44	0.00	**252.95**
18-Jan-25	30.25	24.21	29.89	20.87	0.00	49.93	7.21	0.00		0.00	1.84	2.96	0.00	0.00	30.21	0.00	41.15	0.00	**238.52**
19-Jan-25	21.33	20.75	25.24	17.82	0.00	58.23	9.87	0.00		0.00	1.88	3.10	0.00	0.00	28.44	0.00	39.28	0.00	**225.94**
20-Jan-25	25.88	24.39	26.99	18.48	0.00	56.36	4.81	0.00		0.00	2.04	3.17	0.00	0.00	27.80	0.00	35.39	0.00	**225.31**
21-Jan-25	23.47	23.60	25.00	19.32	0.00	66.42	1.60	0.00		0.00	2.08	3.08	0.00	0.00	36.25	0.00	36.40	0.00	**237.22**
22-Jan-25	28.87	22.81	27.78	20.01	0.00	52.88	0.00	0.00		0.00	2.09	3.40	0.00	0.00	29.11	0.00	43.72	0.00	**230.67**
23-Jan-25	30.94	18.06	28.86	19.39	0.00	37.24	0.00	0.00		0.00	2.06	3.35	0.00	0.00	24.90	4.95	46.64	0.00	**216.39**
24-Jan-25	26.38	15.30	23.16	17.96	0.00	73.15	0.00	0.00		0.00	2.17	3.26	0.00	0.00	29.08	0.78	43.27	0.00	**234.51**
25-Jan-25	20.37	19.10	21.02	19.60	0.00	79.22	0.89	0.00		0.00	2.17	3.22	0.00	0.00	31.32	0.00	34.19	0.00	**231.10**
26-Jan-25	22.09	19.53	22.47	18.32	0.00	58.98	2.42	0.00		0.00	2.05	3.31	0.00	0.00	33.72	0.00	39.30	0.00	**222.19**
27-Jan-25	18.08	22.01	20.85	18.84	0.00	76.65	2.41	0.00		0.00	2.27	3.09	0.00	0.00	27.35	0.00	25.35	0.00	**216.90**
28-Jan-25	13.04	21.74	18.26	16.84	0.00	95.00	2.41	0.00		0.00	2.21	3.33	0.00	0.00	30.93	0.00	13.88	0.00	**217.64**
29-Jan-25	16.95	20.32	18.60	17.23	0.00	80.60	2.40	0.00		0.00	2.23	3.24	0.00	0.00	29.00	0.00	20.35	0.00	**210.92**
30-Jan-25	20.95	22.55	26.08	16.87	0.00	47.13	2.42	0.00		0.00	2.19	3.25	0.00	0.00	28.79	0.00	18.35	0.00	**188.58**
31-Jan-25	19.24	19.31	22.84	15.72	0.00	63.06	2.43	0.00		0.00	2.15	3.27	0.00	0.00	33.37	0.00	17.18	0.00	**198.57**
Total	**877.91**	**664.69**	**896.18**	**592.74**	**0.00**	**1766.28**	**66.90**	**6.27**	**0.00**	**3.06**	**55.29**	**89.99**	**0.00**	**0.00**	**932.98**	**63.08**	**1223.28**	**2.06**	**7240.71**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during January 2025

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Jan-25	0.00	0.00	0.00	0.00	14.56	0.00	0.00	3.61		0.00	0.00	0.00	1.33	22.02	0.00	6.65	0.00	0.79	**48.96**
2-Jan-25	0.00	0.00	0.00	0.00	15.69	0.00	0.00	4.13		0.00	0.00	0.00	1.28	20.95	0.00	9.84	0.00	0.00	**51.89**
3-Jan-25	0.00	0.00	0.00	0.00	16.07	0.00	0.00	4.38		0.00	0.00	0.00	0.95	22.36	0.00	11.75	0.00	0.00	**55.51**
4-Jan-25	0.00	0.00	0.00	0.00	15.73	0.00	0.00	4.34			0.00	0.00	1.21	22.36	0.00	10.70	0.00	0.00	**54.34**
5-Jan-25	0.00	0.00	0.00	0.00	16.51	0.00	0.00	2.80		0.00	0.00	0.00	1.17	21.96	0.00	5.26	0.00	0.34	**48.04**
6-Jan-25	0.00	0.00	0.00	0.00	12.22	0.00	0.00	0.00			0.00	0.00	1.54	21.50	0.00	0.00	0.00	2.10	**37.36**
7-Jan-25	0.00	0.00	0.00	0.00	11.55	0.00	0.00	0.00		0.50	0.00	0.00	1.30	22.21	0.00	0.00	0.00	2.17	**37.73**
8-Jan-25	0.00	0.00	0.00	0.00	13.40	0.00	0.00	1.25		1.66	0.00	0.00	1.72	22.10	0.00	1.40	0.00	2.41	**43.94**
9-Jan-25	0.00	0.00	0.00	0.00	14.12	0.00	0.00	3.58		1.83	0.00	0.00	1.87	22.11	0.00	9.19	0.00	1.51	**54.21**
10-Jan-25	0.00	0.00	0.00	0.00	14.62	0.00	0.00	4.90		1.12	0.00	0.00	2.02	22.36	0.00	14.10	0.00	0.18	**59.30**
11-Jan-25	0.00	0.00	0.00	0.00	14.08	0.00	0.00	5.80		3.16	0.00	0.00	2.34	11.17	0.00	13.96	0.00	3.15	**53.66**
12-Jan-25	0.00	0.00	0.00	0.00	12.53	0.00	0.00	1.80		3.36	0.00	0.00	1.82	13.21	0.00	0.10	0.00	4.16	**36.98**
13-Jan-25	0.00	0.00	0.00	0.00	13.20	0.00	0.00	0.00		0.31	0.00	0.00	2.03	21.57	0.00	0.00	0.00	2.94	**40.05**
14-Jan-25	0.00	0.00	0.00	0.00	12.47	0.00	0.00	0.00		0.00	0.00	0.00	1.09	21.46	0.00	0.00	0.00	0.84	**35.86**
15-Jan-25	0.00	0.00	0.00	0.00	13.12	0.00	0.00	0.00		0.00	0.00	0.00	0.57	20.61	0.00	0.00	0.00	1.37	**35.67**
16-Jan-25	0.00	0.00	0.00	0.00	13.27	0.00	0.00	1.16		1.84	0.00	0.00	0.97	22.41	0.00	0.00	0.00	3.58	**43.23**
17-Jan-25	0.00	0.00	0.00	0.00	13.34	0.00	0.00	2.56		3.87	0.00	0.00	1.22	22.18	0.00	0.00	0.00	4.53	**47.70**
18-Jan-25	0.00	0.00	0.00	0.00	14.76	0.00	0.00	6.37		2.49	0.00	0.00	1.51	22.40	0.00	15.18	0.00	2.18	**64.89**
19-Jan-25	0.00	0.00	0.00	0.00	14.21	0.00	0.00	6.65		3.31	0.00	0.00	2.25	21.85	0.00	17.49	0.00	3.20	**68.96**
20-Jan-25	0.00	0.00	0.00	0.00	16.04	0.00	0.00	5.45		2.25	0.00	0.00	2.21	22.18	0.00	15.54	0.00	1.92	**65.59**
21-Jan-25	0.00	0.00	0.00	0.00	16.04	0.00	6.68	6.78		3.25	0.00	0.00	2.17	22.32	0.00	18.81	0.00	3.34	**79.39**
22-Jan-25	0.00	0.00	0.00	0.00	15.20	0.00	12.14	4.37		3.46	0.00	0.00	1.77	22.46	0.00	9.05	0.00	3.32	**71.77**
23-Jan-25	0.00	0.00	0.00	0.00	13.62	0.00	6.48	1.19		4.10	0.00	0.00	1.62	22.24	0.00	0.00	0.00	4.27	**53.52**
24-Jan-25	0.00	0.00	0.00	0.00	13.70	0.00	2.43	2.31		4.56	0.00	0.00	1.80	22.42	0.00	0.00	0.00	3.33	**50.55**
25-Jan-25	0.00	0.00	0.00	0.00	14.20	0.00	1.52	4.92		4.92	0.00	0.00	2.42	22.01	0.00	11.52	0.00	3.85	**65.36**
26-Jan-25	0.00	0.00	0.00	0.00	14.52	0.00	0.00	5.60		3.73	0.00	0.00	2.40	21.60	0.00	15.69	0.00	2.43	**65.97**
27-Jan-25	0.00	0.00	0.00	0.00	15.54	0.00	0.00	6.35		3.80	0.00	0.00	2.80	22.38	0.00	22.85	0.00	3.75	**77.47**
28-Jan-25	0.00	0.00	0.00	0.00	16.19	0.00	0.00	7.39		4.00	0.00	0.00	3.08	22.41	0.00	24.88	0.00	4.65	**82.60**
29-Jan-25	0.00	0.00	0.00	0.00	16.05	0.00	0.00	6.70		4.91	0.00	0.00	2.72	21.95	0.00	16.07	0.00	3.50	**71.90**
30-Jan-25	0.00	0.00	0.00	0.00	14.80	0.00	0.00	4.40		2.79	0.00	0.00	2.31	22.13	0.00	11.29	0.00	1.22	**58.94**
31-Jan-25	0.00	0.00	0.00	0.00	14.42	0.00	0.00	2.90		3.56	0.00	0.00	2.99	22.50	0.00	6.93	0.00	2.92	**56.22**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**445.77**	**0.00**	**29.25**	**111.69**	**0.00**	**68.78**	**0.00**	**0.00**	**56.48**	**663.39**	**0.00**	**268.25**	**0.00**	**73.95**	**1717.56**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during January 2025

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Jan-25	6.45	10.83	13.05		14.16	9.00	3.45	7.92		3.00	2.26	2.61		0.00	0.00	4.39	3.41	**80.53**	0.00	**0.00**
2-Jan-25	6.76	11.15	13.16		15.30	9.30	5.51	7.89		1.74	4.17	2.57	0.00	0.00	0.00	4.82	3.69	**86.06**	0.00	**0.00**
3-Jan-25	8.05	13.35	13.80		15.28	10.40	6.07	9.11		3.52	2.24	2.50	0.00	0.00	0.00	4.76	4.06	**93.14**	0.00	**0.00**
4-Jan-25	6.23	16.15	11.25		14.14	9.15	6.85	8.25		3.75	1.97	2.65		0.00	0.00	4.44	3.91	**88.74**	0.00	**0.00**
5-Jan-25	6.25	8.25	14.24		8.69	8.27	5.65	4.49		3.81	1.87	4.03			0.00	1.35	2.96	**69.86**	0.00	**0.00**
6-Jan-25	4.60	4.95	12.32		8.32	5.84	3.23	5.36		4.90	0.87	2.10	0.00	0.00	0.00	2.30	1.65	**56.44**	0.00	**0.00**
7-Jan-25	4.70	5.90	13.58		9.13	5.18	3.59	4.92		5.93	0.06	2.70			0.00	2.63	2.20	**60.52**	0.00	**0.00**
8-Jan-25	6.08	8.61	12.58		12.10	6.12	3.90	6.70		5.45	0.33	2.78			0.00	3.74	2.20	**70.59**	0.00	**0.00**
9-Jan-25	7.60	9.05	12.95		10.91	5.27	3.19	5.54		0.64	0.07	2.98		0.00	0.00	3.19	0.26	**61.65**	0.00	**0.00**
10-Jan-25	8.24	11.98	13.79	0.00	11.56	6.51	5.23	6.14		2.10	0.90	3.25			0.00	3.78		**73.48**	0.00	**0.00**
11-Jan-25	7.88	12.73	13.03		12.25	6.39	5.32	5.88		2.41	0.57	3.16			0.00	3.75		**73.37**	0.00	**0.00**
12-Jan-25	7.31	11.06	12.29		12.42	6.40	4.88	5.84		1.21	0.00	3.15	0.00	0.00	0.00	3.82		**68.38**	0.00	**0.00**
13-Jan-25	8.67	12.52	13.43		15.50	7.36	5.52	7.68		1.17	0.00	3.15	0.00		0.00	4.92		**79.92**	0.00	**0.00**
14-Jan-25	6.70	9.46	13.56		13.89	7.48	5.12	7.53		1.26	0.00	1.65	0.00		0.00	4.31		**70.96**	0.00	**0.00**
15-Jan-25	8.78	13.03	15.00		16.24	9.57	6.63	9.07		1.00	0.00	2.90	0.00		0.00	5.25		**87.47**	0.00	**0.00**
16-Jan-25	8.78	12.21	13.70		15.01	8.28	5.45	8.27		0.62	0.00	2.21	0.00		0.00	4.74	0.08	**79.35**	0.00	**0.00**
17-Jan-25	7.90	8.80	12.72		13.55	6.80	3.95	7.60		1.13	0.00	0.71		0.00	0.00	4.15	3.45	**70.76**	0.00	**0.00**
18-Jan-25	9.54	14.94	13.45		15.75	8.26	4.53	9.03		1.15	0.00	0.85			0.00	4.91	6.02	**88.43**	0.00	**0.00**
19-Jan-25	9.31	12.76	9.64		12.00	8.85	3.05	8.78		1.34	0.00	0.73		0.00	0.00	3.46	5.24	**75.16**	0.00	**0.00**
20-Jan-25	10.29	13.85	10.46		12.43	8.20	3.43	8.63		1.18	0.00	1.46		0.00	0.00	3.76	5.80	**79.49**	0.00	**0.00**
21-Jan-25	9.45	10.50	9.76		11.48	7.33	2.71	5.20		1.38	0.00	0.58			0.00	3.46	5.16	**67.01**	0.00	**0.00**
22-Jan-25	8.50	10.65	7.73		10.36	6.02	2.14	6.98		1.18	0.00	0.45		0.00	0.00	2.66	4.79	**61.46**	0.00	**0.00**
23-Jan-25	7.39	10.08	11.35		8.87	4.85	0.75	5.85	0.00	0.97	0.07	0.26			0.00	2.52	4.13	**57.09**	0.00	**0.00**
24-Jan-25	6.84	8.85	10.94		7.91	3.04	0.09	4.59		1.14	0.00	0.52	0.00		0.00	2.27	3.83	**50.02**	0.00	**0.00**
25-Jan-25	8.25	12.40	10.30		10.12	3.67	0.33	5.70		0.97		0.37			0.00	2.90	3.56	**58.57**	0.00	**0.00**
26-Jan-25	6.63	10.54	13.25		10.59	5.04	0.85	6.82		1.11	0.00	0.31	0.00		0.00	3.15	4.31	**62.60**	0.00	**0.00**
27-Jan-25	9.85	17.15	11.09		13.45	5.45	2.35	7.61		0.88	0.21	0.39	0.00		0.00	4.13	5.85	**78.41**	0.00	**0.00**
28-Jan-25	11.15	21.25	11.39		15.98	6.42	3.08	8.02		1.13	0.00	1.04	0.00		0.00	4.81	6.49	**90.76**	0.00	**0.00**
29-Jan-25	11.30	20.13	11.85		15.95	8.11	3.14	9.43		1.07	0.01	1.10	0.00		0.00	4.75	6.38	**93.22**	0.00	**0.00**
30-Jan-25	11.40	21.51	13.00		15.78	7.46	4.17	10.07	0.00	0.93	0.00	1.01			0.00	4.83	7.10	**97.26**	0.00	**0.00**
31-Jan-25	11.40	19.05	11.20		12.49	8.83	4.19	8.91		0.85	0.13	1.30	0.00		0.00	4.56	6.63	**89.54**	0.00	**0.00**
Total	**252.28**	**383.69**	**379.86**	**0.00**	**391.61**	**218.85**	**118.35**	**223.81**	**0.00**	**58.92**	**15.73**	**55.47**	**0.00**	**0.00**	**0.00**	**118.51**	**103.16**	**2320.24**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.2 Import-Export of NR with ER & NER during January 2025

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.14	0.53	0.00	0.00	**0.67**	16.45	**16.45**
2-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.10	0.51	0.00	0.00	**0.61**	16.91	**16.91**
3-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.10	0.57	0.00	0.00	**0.67**	16.96	**16.96**
4-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.09	0.61	0.00	0.00	**0.70**	16.80	**16.80**
5-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.50	0.00	0.00	**0.50**	17.50	**17.50**
6-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.10	0.48	0.00	0.00	**0.58**	13.03	**13.03**
7-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.50	0.00	0.00	**0.50**	11.78	**11.78**
8-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.53	0.00	0.00	**0.53**	16.78	**16.78**
9-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00		0.83	0.56	0.00	0.00	**1.39**	16.28	**16.28**
10-Jan-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.58	0.00		**0.58**	16.40	**16.40**
11-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.53	0.00		**0.53**	17.80	**17.80**
12-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.64	0.00	0.00	0.10	0.50	0.00		**1.24**	16.09	**16.09**
13-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.04	0.00	0.00		0.74	0.00		**0.78**	17.43	**17.43**
14-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.13	0.00	0.00		0.36	0.00		**0.49**	16.72	**16.72**
15-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.02	0.00	0.00		0.65	0.00		**0.67**	16.67	**16.67**
16-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.53	0.00	0.00		0.70	0.00	0.00	**1.23**	16.96	**16.96**
17-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.77	0.00		0.09	0.70	0.00	0.00	**1.56**	16.30	**16.30**
18-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.15	0.00			0.51	0.00	0.00	**0.66**	15.98	**15.98**
19-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.23	0.00		0.11	0.54	0.00	0.00	**0.88**	16.92	**16.92**
20-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.07	0.00		0.11	0.55	0.00	0.00	**0.73**	16.89	**16.89**
21-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.52	0.00			0.68	0.00	0.00	**1.20**	16.96	**16.96**
22-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.15	0.00		0.10	0.51	0.00	0.00	**0.76**	16.99	**16.99**
23-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.55	0.00	0.00	**0.55**	12.65	**12.65**
24-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.12	0.00	0.00		0.60	0.00	0.00	**0.72**	9.79	**9.79**
25-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00		0.00			0.55	0.00	0.00	**0.55**	9.58	**9.58**
26-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.02	0.00	0.00		0.56	0.00	0.00	**0.58**	9.21	**9.21**
27-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.56	0.00	0.00	**0.56**	16.06	**16.06**
28-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.05	0.00	0.00		0.57	0.00	0.00	**0.62**	17.15	**17.15**
29-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.57	0.00	0.00	**0.57**	16.65	**16.65**
30-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.03	0.00			0.55	0.00	0.00	**0.58**	17.30	**17.30**
31-Jan-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.58	0.00	0.00	**0.58**	17.20	**17.20**
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**3.47**	**0.00**	**0.00**	**1.87**	**17.43**	**0.00**	**0.00**	**22.77**	**486.19**	**486.19**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

Date	15.3 Import and Export of ER with WR & NER during January 2025																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda-2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda-2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Jan-25	5.5	2.2	0.0	0.6	0.0	0.0	0.0	**8.33**	2.4	4.9	11.5	1.9	10.7	1.0	1.9	**34.41**	0.00	0.00	0.00	**0.00**	3.54	6.26	1.41	**11.22**
2-Jan-25	4.5	3.1	0.0	0.4	0.0	0.1	0.0	**8.13**	2.0	3.6	15.8	1.7	10.3	0.5	2.0	**35.89**	0.01	0.00	0.00	**0.01**	3.12	5.91	1.40	**10.43**
3-Jan-25	5.7	3.5	0.0	0.9	0.0	0.1	0.0	**10.16**	3.1	7.0	20.1	1.8	12.9	0.7	2.0	**47.64**	0.02	0.00	0.00	**0.02**	2.80	5.76	1.16	**9.72**
4-Jan-25	6.1	4.9	0.0	0.8	0.0	0.4	0.0	**12.21**	2.6	4.3	18.1	1.5	11.4	0.5	1.5	**39.94**	0.00	0.00	0.00	**0.00**	3.00	5.65	1.31	**9.96**
5-Jan-25	8.9	5.8	0.0	1.5	0.0	0.7	0.0	**16.94**	1.2	4.0	16.4	0.7	10.5	0.2	1.4	**34.35**	0.00	0.00	0.00	**0.00**	3.35	6.17	1.33	**10.85**
6-Jan-25	9.4	10.1	0.0	1.9	0.0	1.4	0.0	**22.86**	0.5	2.9	14.3	0.5	8.3	0.0	1.4	**27.94**	0.28	0.15	0.00	**0.43**	1.59	3.07	0.78	**5.43**
7-Jan-25	9.8	8.9	0.0	2.1	0.0	1.4	0.0	**22.23**	0.4	1.6	14.1	0.3	8.3	0.0	1.7	**26.33**	0.59	0.51	0.02	**1.12**	1.27	2.60	0.76	**4.63**
8-Jan-25	5.6	5.0	0.0	1.2	0.0	1.4	0.0	**13.24**	3.0	3.9	15.9	1.1	8.5	0.0	1.8	**34.12**	0.01	0.00	0.00	**0.01**	3.51	6.50	1.64	**11.66**
9-Jan-25	5.6	4.6	0.0	0.9	0.0	1.7	0.0	**12.79**	3.1	4.5	16.0	1.4	7.9	0.0	1.8	**34.70**	0.00	0.00	0.00	**0.00**	3.42	6.38	1.50	**11.30**
10-Jan-25	6.3	3.7	0.0	0.9	0.0	1.6	0.0	**12.61**	1.5	3.9	13.7	0.9	8.2	0.0	1.7	**29.91**	0.00	0.00	0.00	**0.00**	4.08	7.29	1.53	**12.89**
11-Jan-25	4.7	3.9	0.0	0.6	0.0	1.4	0.0	**10.54**	2.5	3.9	16.0	1.4	8.8	0.0	1.6	**34.30**	0.00	0.00	0.00	**0.00**	4.23	7.73	1.58	**13.54**
12-Jan-25	4.8	5.2	0.0	0.9	0.0	1.3	0.0	**12.20**	2.5	3.5	14.4	1.3	9.5	0.0	0.9	**32.14**	0.00	0.00	0.00	**0.00**	4.06	7.46	1.55	**13.07**
13-Jan-25	9.1	6.7	0.0	1.4	0.0	1.4	0.0	**18.56**	0.9	3.5	14.8	0.8	9.0	0.1	1.0	**30.08**	0.00	0.00	0.00	**0.00**	4.31	7.98	1.46	**13.76**
14-Jan-25	15.9	7.8	0.0	2.8	0.0	1.6	0.0	**28.16**	0.2	3.7	12.6	0.2	7.2	0.0	0.9	**24.91**	0.00	0.00	0.00	**0.00**	4.33	7.69	1.74	**13.75**
15-Jan-25	12.1	3.6	0.0	2.0	0.0	0.8	0.0	**18.47**	0.1	4.4	14.7	0.4	7.6	0.2	0.8	**28.15**	0.00	0.00	0.00	**0.00**	4.54	8.14	1.80	**14.48**
16-Jan-25	7.2	2.3	0.0	1.3	0.0	1.0	0.0	**11.75**	1.0	3.8	17.0	0.7	9.9	0.0	1.2	**33.65**	0.00	0.00	0.00	**0.00**	3.88	7.22	1.61	**12.71**
17-Jan-25	7.4	3.0	0.0	1.3	0.0	1.1	0.0	**12.84**	1.1	4.9	19.8	0.6	10.8	0.1	1.2	**38.43**	0.01	0.00	0.00	**0.01**	3.42	6.40	1.46	**11.29**
18-Jan-25	2.3	2.6	0.0	0.2	0.0	0.8	0.0	**5.94**	4.2	4.5	21.9	2.2	11.6	0.3	1.6	**46.41**	0.00	0.00	0.00	**0.00**	3.70	6.97	1.54	**12.21**
19-Jan-25	0.3	5.8	0.0	0.0	0.0	1.0	0.0	**7.13**	6.1	2.5	21.2	2.9	12.1	0.1	1.6	**46.51**	0.00	0.00	0.00	**0.00**	3.59	6.71	1.51	**11.80**
20-Jan-25	0.7	4.5	0.0	0.0	0.0	0.9	0.0	**6.08**	4.6	7.0	19.8	2.8	12.0	0.1	1.6	**47.92**	0.01	0.00	0.00	**0.01**	3.17	6.00	1.46	**10.63**
21-Jan-25	1.6	4.0	0.0	0.2	0.0	1.7	0.0	**7.40**	6.3	10.7	19.3	2.6	9.5	0.0	1.4	**49.90**	0.07	0.00	0.00	**0.07**	3.13	6.09	1.36	**10.58**
22-Jan-25	3.6	3.9	0.0	0.2	0.0	1.3	0.0	**9.03**	2.1	7.0	19.5	1.7	11.5	0.0	1.4	**43.27**	0.04	0.00	0.00	**0.04**	2.84	5.60	1.31	**9.75**
23-Jan-25	6.6	5.5	0.0	0.7	0.0	1.3	0.0	**14.16**	1.4	2.4	17.2	1.1	11.4	0.1	1.3	**34.81**	0.95	1.01	0.12	**2.09**	1.61	3.07	0.69	**5.36**
24-Jan-25	4.9	4.8	0.0	0.7	0.0	1.3	0.0	**11.63**	2.3	4.5	17.9	1.3	10.1	0.1	0.8	**36.91**	1.21	1.71	0.27	**3.19**	0.57	1.21	0.35	**2.12**
25-Jan-25	1.6	2.9	0.0	0.1	0.0	0.8	0.0	**5.46**	4.7	4.6	19.8	2.2	10.2	0.2	1.2	**42.96**	1.36	1.37	0.16	**2.88**	0.34	0.97	0.30	**1.61**
26-Jan-25	6.0	7.1	0.0	1.0	0.0	0.8	0.0	**14.85**	3.1	1.5	16.1	1.7	10.1	0.3	1.0	**33.75**	1.45	1.64	0.07	**3.15**	0.38	0.91	0.36	**1.65**
27-Jan-25	0.2	9.0	0.0	0.0	0.0	0.6	0.0	**9.75**	7.9	3.9	19.2	3.8	10.4	0.3	1.2	**46.62**	0.14	0.04	0.00	**0.18**	2.02	4.11	0.98	**7.11**
28-Jan-25	0.0	5.5	0.0	0.0	0.0	0.6	0.0	**6.16**	13.2	9.1	22.3	5.4	11.9	0.3	1.5	**63.67**	0.20	0.09	0.01	**0.30**	2.39	4.71	1.03	**8.13**
29-Jan-25	1.0	5.1	0.0	0.0	0.0	0.7	0.0	**6.85**	10.5	5.8	19.9	4.4	11.7	0.2	1.3	**53.76**	0.20	0.10	0.00	**0.30**	2.14	4.46	1.14	**7.74**
30-Jan-25	1.4	3.7	0.0	0.0	0.0	0.2	0.0	**5.35**	5.8	2.9	20.5	3.5	14.5	0.7	1.2	**49.09**	0.93	0.79	0.03	**1.75**	0.58	1.56	0.55	**2.69**
31-Jan-25	1.0	4.2	0.0	0.0	0.0	0.0	0.0	**5.20**	8.6	4.7	19.6	4.6	13.6	0.8	0.7	**52.61**	0.00	0.00	0.00	**0.00**	2.51	5.32	1.29	**9.12**
Total	**160.01**	**152.97**	**0.00**	**24.77**	**0.03**	**29.24**	**0.01**	**367.02**	**108.43**	**139.52**	**539.53**	**57.42**	**320.44**	**7.12**	**42.62**	**1215.08**	**7.46**	**7.41**	**0.68**	**15.55**	**87.40**	**165.91**	**37.89**	**291.19**

15.4 Import and Export of SR with ER & WR during January 2025

Date	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)								
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Jan-25	5.10	31.87	54.21	**91.18**	0.00	0.00	0.00	**0.00**	23.32	6.61	33.84	0.00	29.11	2.29	0.00	34.53	**129.70**	0.00	7.47	0.00	27.21	0.00	0.00	0.00	0.00	**34.68**
2-Jan-25	5.10	41.08	53.68	**99.86**	0.00	0.00	0.00	**0.00**	21.92	7.27	32.64	0.00	41.04	2.34	0.00	35.09	**140.31**	0.00	6.32	0.02	28.08	0.00	0.00	0.00	0.00	**34.41**
3-Jan-25	5.10	36.96	51.79	**93.84**	0.00	0.00	0.00	**0.00**	24.01	6.16	28.99	0.00	53.13	2.23	0.00	30.48	**145.01**	0.00	11.48	0.01	30.46	0.00	0.00	0.00	0.00	**41.95**
4-Jan-25	5.10	39.77	50.47	**95.34**	0.00	0.00	0.00	**0.00**	18.39	4.56	29.14	0.00	39.41	2.14	0.00	31.96	**125.60**	0.00	8.13	0.00	26.43	0.00	0.00	0.00	0.00	**34.56**
5-Jan-25	5.10	37.53	50.13	**92.75**	0.00	0.00	0.00	**0.00**	9.07	5.10	32.26	0.00	25.87	2.08	0.00	31.91	**106.29**	0.00	10.78	0.00	23.67	0.00	0.00	0.00	0.00	**34.46**
6-Jan-25	5.10	40.08	45.45	**90.62**	0.00	0.00	0.00	**0.00**	8.71	11.11	36.88	0.00	44.74	2.08	0.00	37.73	**141.26**	0.00	7.63	0.01	24.87	0.00	0.00	0.00	0.00	**32.51**
7-Jan-25	5.10	33.30	51.15	**89.55**	0.00	0.00	0.00	**0.00**	7.33	15.77	45.89	0.00	32.12	2.13	0.00	44.63	**147.87**	0.00	2.35	0.00	21.03	0.00	0.00	0.00	0.00	**23.38**
8-Jan-25	5.10	30.15	50.73	**85.98**	0.00	0.00	0.00	**0.00**	18.55	9.69	33.18	0.00	47.40	2.06	0.00	35.26	**146.16**	0.00	7.41	0.36	25.52	0.00	0.00	0.00	0.08	**33.37**
9-Jan-25	5.10	30.15	52.64	**87.88**	0.00	0.00	0.00	**0.00**	12.17	7.86	32.52	0.00	34.21	2.02	0.00	35.51	**124.30**	0.00	5.43	0.01	26.72	0.00	0.00	0.00	0.00	**32.16**
10-Jan-25	5.07	30.15	50.17	**85.39**	0.00	0.00	0.00	**0.00**	12.17	5.51	29.90	0.00	36.62	2.29	0.00	28.62	**115.12**	0.00	8.01	0.09	29.95	0.00	0.00	0.00	0.14	**38.18**
11-Jan-25	5.07	34.31	49.75	**89.13**	0.00	0.00	0.00	**0.00**	12.17	10.19	32.24	0.00	30.84	2.25	0.00	33.96	**121.66**	0.00	6.44	0.06	25.97	0.00	0.00	0.00	0.00	**32.47**
12-Jan-25	5.06	33.04	45.55	**83.65**	0.00	0.00	0.00	**0.00**	12.17	5.14	28.02	0.00	31.41	2.15	0.00	29.30	**108.21**	0.00	7.18	0.11	25.30	0.00	0.00	0.00	0.00	**32.59**
13-Jan-25	5.07	28.97	46.95	**80.99**	0.00	0.00	0.00	**0.00**	10.48	6.96	30.40	0.00	32.96	2.24	0.22	30.99	**114.25**	0.96	7.13	0.15	25.44	0.00	0.00	0.00	0.01	**33.70**
14-Jan-25	5.07	28.97	45.53	**79.58**	0.00	0.00	0.00	**0.00**	0.00	6.72	31.47	0.00	14.61	2.34	0.00	30.25	**85.39**	7.22	11.09	0.06	28.12	0.00	0.00	0.00	0.02	**46.50**
15-Jan-25	5.07	28.97	40.65	**74.70**	0.00	0.00	0.00	**0.00**	0.00	1.07	24.31	0.00	17.05	2.31	0.00	23.19	**67.93**	7.22	14.98	0.74	32.91	0.00	0.00	0.00	0.56	**56.42**
16-Jan-25	5.07	28.97	48.90	**82.94**	0.00	0.00	0.00	**0.00**	2.59	4.00	32.50	0.00	21.81	2.19	0.00	30.62	**93.71**	4.64	6.02	0.15	28.21	0.00	0.00	0.00	0.10	**39.10**
17-Jan-25	5.08	31.52	52.46	**89.05**	0.00	0.00	0.00	**0.00**	12.24	9.40	32.50	0.00	23.77	2.05	0.00	35.24	**115.21**	0.00	3.58	0.00	27.45	0.00	0.00	0.00	0.00	**31.03**
18-Jan-25	5.08	21.86	55.44	**82.38**	0.00	0.00	0.00	**0.00**	12.18	9.60	31.06	0.00	31.14	2.14	0.00	34.54	**120.66**	0.00	3.35	0.18	24.69	0.00	0.00	0.00	0.01	**28.23**
19-Jan-25	5.08	30.16	55.84	**91.08**	0.00	0.00	0.00	**0.00**	12.17	9.93	32.77	0.00	40.85	2.11	0.00	36.52	**134.35**	0.00	1.53	0.00	22.59	0.00	0.00	0.00	0.00	**24.12**
20-Jan-25	5.07	30.15	50.34	**85.56**	0.00	0.00	0.00	**0.00**	12.17	6.07	27.77	0.00	45.71	2.21	0.00	31.18	**125.12**	0.00	6.93	0.00	23.79	0.00	0.00	0.00	0.00	**30.72**
21-Jan-25	8.05	34.12	41.85	**84.02**	0.00	0.00	0.00	**0.00**	12.17	7.57	25.65	0.00	63.69	2.14	0.00	29.01	**140.23**	0.00	14.06	1.13	27.70	0.00	0.00	0.00	0.52	**43.40**
22-Jan-25	8.58	30.16	50.57	**89.31**	0.00	0.00	0.00	**0.00**	12.16	7.01	29.94	0.00	38.51	2.10	0.00	33.62	**123.34**	0.00	6.23	0.00	25.68	0.00	0.00	0.00	0.00	**31.91**
23-Jan-25	8.59	30.17	48.77	**87.53**	0.00	0.00	0.00	**0.00**	7.96	7.69	34.25	0.00	48.50	2.15	0.00	35.53	**136.08**	0.00	4.49	0.16	25.30	0.00	0.00	0.00	0.04	**29.99**
24-Jan-25	8.60	30.17	48.16	**86.93**	0.00	0.00	0.00	**0.00**	3.78	8.20	34.63	0.00	47.20	2.29	0.00	36.56	**132.66**	0.00	6.57	0.01	26.99	0.00	0.00	0.00	0.00	**33.57**
25-Jan-25	8.60	30.17	50.10	**88.87**	0.00	0.00	0.00	**0.00**	3.78	4.07	28.86	0.00	57.15	2.34	0.00	32.21	**128.42**	0.00	8.91	0.09	27.54	0.00	0.00	0.00	0.00	**36.54**
26-Jan-25	8.60	30.17	47.07	**85.84**	0.00	0.00	0.00	**0.00**	3.75	3.17	25.19	0.00	29.33	2.15	0.00	27.71	**91.31**	0.00	12.67	0.00	27.91	0.00	0.00	0.00	0.00	**40.57**
27-Jan-25	8.60	40.02	47.35	**95.97**	0.00	0.00	0.00	**0.00**	8.79	5.51	27.26	0.00	27.01	2.18	0.86	31.41	**103.03**	0.00	11.64	0.24	24.67	0.00	0.00	0.00	0.04	**36.60**
28-Jan-25	8.60	30.16	47.30	**86.06**	0.00	0.00	0.00	**0.00**	7.35	4.83	28.44	0.00	38.48	2.32	1.09	32.60	**115.10**	0.00	7.66	0.08	23.71	0.00	0.00	0.00	0.00	**31.46**
29-Jan-25	8.61	30.17	46.89	**85.66**	0.00	0.00	0.00	**0.00**	7.38	3.69	28.72	0.00	48.50	2.29	1.59	32.17	**124.35**	0.00	10.73	0.21	26.51	0.00	0.00	0.00	0.03	**37.48**
30-Jan-25	8.61	30.17	49.06	**87.84**	0.00	0.00	0.00	**0.00**	12.55	4.17	27.52	0.00	42.83	2.24	1.64	33.71	**124.66**	0.00	7.57	0.06	25.86	0.00	0.00	0.00	0.00	**33.48**
31-Jan-25	8.61	33.87	50.03	**92.51**	0.00	0.00	0.00	**0.00**	9.92	7.02	30.46	0.00	60.04	2.33	1.11	36.34	**147.21**	0.00	6.80	0.00	24.25	0.00	0.00	0.00	0.00	**31.05**
TOTAL	**195.73**	**997.29**	**1529.00**	**2722.02**	**0.00**	**0.00**	**0.00**	**0.00**	**331.42**	**211.67**	**959.23**	**0.00**	**1175.06**	**68.17**	**6.57**	**1022.37**	**3774.49**	**20.04**	**240.55**	**3.92**	**814.52**	**0.00**	**0.00**	**0.02**	**1.54**	**1080.59**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय
INTERNATIONAL EXCHANGE WITH BHUTAN, NEPAL, BANGLADESH AND MYANMAR

वित्तीय वर्ष 2024-25 के लिए (जनवरी'25 तक)
For FY 2024-25(till Jan'25)

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']
Transnational Exchange ('Export from' / 'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported from India (In MU)	Energy Imported to India (In MU)	Energy Exported from India (In MU)	Energy Imported to India (In MU)	Energy Exported from India (In MU)	Energy Imported to India (In MU)	Energy Exported from India (In MU)	Energy Imported to India (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
अक्तूबर 2024 OCT'24	0.00	918.96	0.00	283.29	695.63	0.00	0.80	0.00
नवंबर 2024 NOV'24	12.24	125.37	0.00	212.20	698.58	0.00	0.71	0.00
दिसम्बर 2024 DEC'24	187.39	0.00	58.60	1.56	521.28	0.00	0.72	0.00
जनवरी 2025 JAN'25	158.13	0.00	252.02	0.00	674.70	0.00	0.67	0.00
कुल Total	495.60	5325.83	949.03	2131.41	6750.72	0.00	7.80	0.00

* Based on daily operational data

16.1 Export to neighbouring countries during Jan 2025

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Jan-25	0.04	0.00	0.00	0.00	0.00	2.77	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-Jan-25	0.00	0.00	0.00	0.00	0.00	2.12	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-Jan-25	0.34	0.00	0.00	0.00	0.00	0.59	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-Jan-25	0.00	0.00	0.00	0.00	0.00	2.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-Jan-25	0.00	0.00	0.00	0.00	0.00	2.21	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-Jan-25	0.00	0.00	0.00	0.00	0.00	2.35	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
7-Jan-25	0.00	0.00	0.00	0.00	0.00	1.70	0.12	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-Jan-25	0.00	0.00	0.00	0.00	0.00	2.16	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-Jan-25	0.00	0.00	0.00	0.00	0.00	2.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
10-Jan-25	0.00	0.00	0.00	0.00	0.00	2.28	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Jan-25	0.00	0.00	0.00	0.00	0.00	1.81	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Jan-25	0.00	0.00	0.00	0.00	0.00	1.72	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-Jan-25	0.19	0.00	0.00	0.00	0.00	1.55	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-Jan-25	0.00	0.00	0.00	0.00	0.00	2.30	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-Jan-25	0.00	0.00	0.00	0.00	0.00	1.99	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-Jan-25	0.00	0.00	0.00	0.00	0.00	1.73	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00
17-Jan-25	0.00	0.00	0.00	0.00	0.00	1.97	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
18-Jan-25	0.00	0.00	0.00	0.00	0.00	1.64	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
19-Jan-25	0.00	0.00	0.00	0.00	0.00	1.60	0.07	0.00	0.00	0.00	0.00	0.00	0.00	0.00
20-Jan-25	0.00	0.00	0.00	0.00	0.00	1.52	0.18	0.00	0.00	0.00	0.00	0.00	0.00	0.00
21-Jan-25	0.00	0.00	0.00	0.00	0.00	1.31	0.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00
22-Jan-25	0.00	0.00	0.00	0.00	0.00	1.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
23-Jan-25	0.00	0.00	0.00	0.00	0.00	1.54	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-Jan-25	0.00	0.00	0.00	0.00	0.00	1.63	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-Jan-25	0.00	0.00	0.00	0.00	0.00	1.52	0.12	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-Jan-25	0.00	0.00	0.00	0.00	0.00	1.85	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
27-Jan-25	0.00	0.00	0.00	0.00	0.00	1.72	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
28-Jan-25	0.00	0.00	0.00	0.00	0.00	1.63	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
29-Jan-25	0.00	0.00	0.00	0.00	0.00	1.42	0.13	0.00	0.00	0.00	0.00	0.00	0.00	0.00
30-Jan-25	0.00	0.00	0.00	0.00	0.00	1.29	0.13	0.00	0.00	0.00	0.00	0.00	0.00	0.00
31-Jan-25	0.00	0.00	0.00	0.00	0.00	1.35	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total	**0.56**	**0.00**	**0.00**	**0.00**	**0.00**	**55.22**	**0.84**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**

16.2 Export to neighbouring countries during Jan 2025

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Jan-25	0.00	1.13	3.11	1.63	0.00	0.00	0.10	0.43	19.42	1.17	0.74	2.53	1.69	0.02
2-Jan-25	0.32	1.49	3.09	1.59	0.00	0.00	0.01	0.43	19.27	1.21	0.84	2.19	1.97	0.02
3-Jan-25	0.00	0.84	2.80	1.38	0.00	0.00	0.04	0.49	17.90	1.24	0.91	2.21	1.96	0.02
4-Jan-25	0.77	1.86	3.29	1.72	0.00	0.00	0.01	0.44	18.57	1.17	0.86	2.09	1.72	0.02
5-Jan-25	0.15	1.28	3.03	1.63	0.00	0.00	0.01	0.44	19.53	1.20	1.02	2.75	1.70	0.02
6-Jan-25	0.23	1.38	3.06	1.51	0.00	0.00	0.26	0.30	19.39	1.27	0.94	2.75	1.84	0.02
7-Jan-25	0.36	1.50	3.04	1.51	0.00	0.00	0.00	0.38	19.58	1.27	1.08	3.37	1.90	0.02
8-Jan-25	0.32	1.49	3.07	1.58	0.00	0.00	0.09	0.45	20.89	1.25	1.15	3.13	2.00	0.02
9-Jan-25	0.41	1.49	3.02	1.52	0.00	0.00	0.01	0.45	20.77	1.28	1.14	3.62	1.90	0.02
10-Jan-25	0.09	1.13	2.75	1.29	0.00	0.00	0.19	0.39	19.15	1.25	1.02	3.58	1.88	0.02
11-Jan-25	0.12	1.16	2.84	1.35	0.00	0.00	0.06	0.52	19.86	1.20	0.86	3.00	1.82	0.03
12-Jan-25	0.18	1.20	2.81	1.40	0.00	0.00	0.00	0.44	20.36	1.27	0.96	3.60	1.95	0.02
13-Jan-25	0.00	0.95	2.87	1.44	0.00	0.00	0.02	0.49	20.91	1.31	1.08	3.60	1.87	0.02
14-Jan-25	0.15	1.21	2.89	1.46	0.00	0.00	0.16	0.39	20.94	1.29	1.07	3.72	1.77	0.02
15-Jan-25	0.29	1.33	2.93	1.53	0.00	0.00	0.16	0.41	21.02	1.22	0.90	3.53	1.80	0.02
16-Jan-25	0.34	1.39	2.94	1.44	0.00	0.00	0.00	0.43	21.17	1.21	1.00	3.87	1.91	0.02
17-Jan-25	0.37	1.39	2.81	1.33	0.00	0.00	0.18	0.38	19.92	1.13	0.93	4.24	2.05	0.02
18-Jan-25	0.37	1.41	2.87	1.39	0.00	0.00	0.01	0.49	20.45	1.19	1.05	4.64	2.01	0.02
19-Jan-25	0.28	1.27	2.80	1.26	0.00	0.00	0.00	0.48	21.14	1.17	1.20	5.94	2.21	0.02
20-Jan-25	0.24	1.31	2.92	1.42	0.00	0.00	0.00	0.50	21.36	1.25	1.17	3.94	1.95	0.02
21-Jan-25	0.34	1.43	2.88	1.49	0.00	0.00	0.00	0.42	21.55	1.17	1.11	4.56	2.11	0.02
22-Jan-25	0.71	1.78	3.14	1.56	0.00	0.00	0.14	0.38	21.43	1.30	1.01	5.42	1.96	0.02
23-Jan-25	0.74	1.68	2.16	0.92	0.00	0.00	0.14	0.29	21.05	1.28	1.13	5.88	1.90	0.02
24-Jan-25	0.32	1.72	3.32	0.90	0.00	0.00	0.00	0.48	20.39	1.24	1.06	6.16	1.90	0.02
25-Jan-25	0.82	2.00	3.55	0.91	0.00	0.00	0.00	0.45	20.71	1.20	1.10	4.29	3.37	0.02
26-Jan-25	0.78	1.88	3.21	1.53	0.00	0.00	0.09	0.09	21.53	1.28	0.92	4.04	3.70	0.02
27-Jan-25	0.87	2.10	3.42	1.72	0.00	0.00	0.08	0.31	21.61	1.31	0.87	4.57	3.74	0.02
28-Jan-25	0.85	2.00	3.31	1.57	0.00	0.00	0.05	0.31	21.61	1.31	0.88	4.69	3.74	0.01
29-Jan-25	0.87	2.03	3.07	1.77	0.00	0.00	0.00	0.39	21.64	1.33	0.81	3.59	3.49	0.03
30-Jan-25	0.99	2.16	3.34	1.55	0.00	0.00	0.00	0.32	20.50	1.24	0.85	4.26	3.40	0.02
31-Jan-25	0.74	1.90	3.30	1.65	0.00	0.00	0.01	0.31	19.42	1.27	0.84	5.02	3.40	0.02
Total	**13.02**	**46.89**	**93.64**	**44.93**	**0.00**	**0.00**	**1.82**	**12.48**	**633.04**	**38.48**	**30.49**	**120.78**	**70.64**	**0.67**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – जनवरी 2025

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - JANUARY 2025

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

जनवरी 2025 JANUARY 2025			Apr'24- Jan'25	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	504	1178	6248	26139
प.क्षे. WR	550	563	4012	5252
द.क्षे. SR	440	508	3683	9435
पू.क्षे. ER	390	234	3447	12180
पूर्वोत्तर क्षे. NER	100	50	816	564
कुल TOTAL	1984	2533	18206	53570

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
अक्तूबर 2024 Oct'24	12567	8372	1511	2332
नवंबर 2024 Nov'24	11553	9432	1217	963
दिसम्बर 2024 Dec'24	12448	10602	1773	1468
जनवरी 2025 Jan'25	12932	9756	1984	2533
कुल TOTAL	105795	89934	18206	53570

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
30.12.24 to 05.01.25	78.33	270.37	15.58	205.94	58.48
06.01.25 to 12.01.25	102.65	297.83	28.73	213.04	65.74
13.01.25 to 19.01.25	76.56	253.13	22.07	209.86	64.89
20.01.25 to 26.01.25	75.97	192.45	20.01	154.52	43.52
27.01.25 to 02.02.25	78.25	229.42	26.79	190.77	60.91

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जनवरी 2025
EXCHANGES THROUGH POWER EXCHANGES -January 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED	उत्तरी क्षेत्र NR	12.37	0.00
2	ADANI GREEN ENERGY TWENTY FIVE LIMITED		48.57	0.00
3	ADANI GREEN ENERGY TWENTY FOUR LIMITED		39.63	0.00
4	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		24.62	0.00
5	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		9.48	0.00
6	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		26.36	0.00
7	Adept Renewable Technologies Private Limited		17.25	0.00
8	Amp Energy Green Six Private Limited		17.83	0.00
9	Amplus Ages Private Limited		1.87	0.00
10	Ayana Renewable Power Three Private Limited Infirm		0.34	0.00
11	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		0.83	0.00
12	Chandigarh (UT)		12.62	12.75
13	Delhi		243.20	208.25
14	Government of Himachal Pradesh _ Chamera1HEP		4.56	0.08
15	Government of Himachal Pradesh _ Chamera3HEP		3.01	0.18
16	Government of Himachal Pradesh_ CHAMERA2HEP		3.57	0.21
17	Government of Himachal Pradesh_BairasuilHEP		1.51	0.01
18	Government of Himachal Pradesh_Koldam HEP		9.86	0.14
19	Government of Himachal Pradesh_NJHPS		24.62	0.65
20	Government of Himachal Pradesh_Parbati3HEP		1.59	0.19
21	Government of Himachal Pradesh_RampurHEP		7.23	0.19
22	Grian Energy Private Limited		4.36	0.00
23	Haryana		366.83	53.52
24	Himachal Pradesh		33.57	79.54
25	IGSTPS JHAJJAR		2.48	0.00
26	JUNIPER GREEN COSMIC PRIVATE LIMITED		10.32	0.00
27	Jammu Kashmir		35.25	151.99
28	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		16.39	0.00
29	KHURJA STPP		10.98	0.00
30	NEA - UP STU		0.00	29.26
31	NEA Nepal Upper Chameliya Hydropower Project		0.00	0.00
32	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	19.54
33	NTPC Dadri Stage I		20.26	0.00
34	NTPC Dadri Stage II		7.94	0.00
35	NTPC Rihand stage I		10.11	0.00
36	NTPC Rihand stage II		7.97	0.00
37	NTPC Rihand stage III		13.40	0.00
38	NTPC Singrauli		23.79	0.00
39	NTPC Tanda Stage II		2.94	0.00
40	NTPC Unchahar Stage I		1.55	0.00
41	NTPC Unchahar Stage II		1.73	0.00
42	NTPC Unchahar Stage III		1.31	0.00
43	NTPC Unchahar Stage IV		4.77	0.00
44	North Central Railway Prayagraj		0.00	11.27

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जनवरी 2025 EXCHANGES THROUGH POWER EXCHANGES -January 2025				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	Onevolt Energy Private Limited		6.01	0.00
46	Punjab		0.76	1027.92
47	RENEW SURYA PRATAP PRIVATE LIMITED		38.76	0.00
48	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.26	0.00
49	Rajasthan		180.13	151.71
50	ReNew Surya Ravi Private Limited		37.09	0.00
51	SHREE CEMENT LIMITED TPS		34.90	0.34
52	Sainj HEP		3.78	0.00
53	Serentica Renewables India 4 Private Limited		3.21	0.00
54	Serentica Renewables India 5 Private Limited		19.73	0.00
55	Singoli Bhatwari HEP		8.59	0.00
56	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		7.23	0.00
57	TPSL 200MW TPTCL Banderwala		14.30	0.00
58	TPSL Banderwala SECI 100_INF		4.73	0.00
59	Transition Cleantech Services Private Limited		0.50	0.00
60	Transition Energy Services Private Limited		7.94	0.00
61	Transition Green Energy Private Limited		10.22	0.00
62	Transition Sustainable Energy Services One Private Limited		8.86	0.00
63	Uttar Pradesh		665.16	561.85
64	Uttarakhand		88.75	118.76
65	ACB (INDIA) LIMITED		41.30	0.49
66	ADANI GREEN ENERGY TWENTY SIX A LIMITED_PSS-3		2.41	0.00
67	ADANI PORTS AND SPECIAL ECONOMIC ZONE LIMITED (PSS-3)		16.22	0.00
68	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS-3 (162.5 MW Hybrid Solar of 187.5MW HPD)		34.26	0.00
69	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.86	0.00
70	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		1.04	0.00
71	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS-3		53.90	0.00
72	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED_PSS-1		148.10	0.00
73	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		66.31	0.00
74	AMBUJA CEMENTS LIMITED_PSS3		9.09	0.00
75	Adani Green Energy Twenty Five A Limited_PSS-2		53.11	0.00
76	Adani Green Energy Twenty Five B Limited_PSS-2		89.33	0.00
77	Adani Green Energy Twenty Four A Limited_PSS-3		17.81	0.00
78	Adani Green Energy Twenty Six B Limited_PSS-2		14.51	0.00
79	Adani Power Limited - Raigarh TPP		282.64	0.59
80	Adani Power Limited-Raipur TPP		438.11	0.00
81	Adani Renewable Energy Forty Eight Limited (Wind)_PSS-9		25.93	0.00
82	ArcelorMittal Nippon Steel India Limited		0.00	179.08
83	BHARAT ALUMINIUM COMPANY LTD		51.11	0.00
84	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	0.39
85	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		2.19	0.00
86	Chhattisgarh		210.37	38.72
87	D B Power Limited		69.81	0.00
88	DHARIWAL STU OTH		5.68	0.00
89	Daman and Diu - Dadra and Nagar Haveli		0.94	47.15
90	Dhariwal ISTS		7.30	0.00
91	GMR Warora Energy Limited		10.41	0.00
92	Goa WR		34.57	0.87
93	Gujarat		50.26	1125.75
94	Jaypee Nigrie Super Thermal Power Plant		202.83	0.00
95	Jhabua Power Limited		30.50	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जनवरी 2025
EXCHANGES THROUGH POWER EXCHANGES -January 2025

क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
96	Jindal Power Limited, Stage-1	पश्चिमी क्षेत्र WR	223.98	0.00
97	Jindal Power Limited, Stage-2		633.02	5.96
98	Jindal Steel & Power Ltd , DCPP		77.30	3.18
99	KSK MAHANADI POWER COMPANY LIMITED		12.07	0.00
100	LANCO AMARKANTAK POWER LIMITED		2.01	0.00
101	MAHAN ENERGEN LIMITED U#1		85.21	0.00
102	MAHAN ENERGEN LIMITED U#2		256.57	2.73
103	MB POWER (MADHYA PRADESH) LIMITED		6.06	19.00
104	Madhya Pradesh		254.32	86.04
105	Maharashtra		88.12	928.65
106	Maruti Clean Coal and Power Limited		10.56	0.50
107	NREL-Dayapar Wind		5.38	0.00
108	NTPC Gadarwara		18.40	0.00
109	NTPC Jhanor Gandhar GPS		0.00	0.52
110	NTPC Kawas GPS		0.00	0.67
111	NTPC Korba Stage I &II		5.61	0.00
112	NTPC Korba Stage III		2.87	0.00
113	NTPC Lara Stage I		4.33	0.00
114	NTPC Mouda Stage I		8.07	0.00
115	NTPC Mouda Stage II		10.66	0.00
116	NTPC SAIL POWER COMPANY LIMITED		0.73	0.00
117	NTPC SOLAPUR SOLAR PV Station		1.47	0.00
118	NTPC Sipat Stage I		1.01	0.00
119	NTPC Sipat Stage II		0.50	0.00
120	NTPC Solapur		13.46	0.00
121	NTPC Vindhyachal Stage I		10.82	0.00
122	NTPC Vindhyachal Stage II		11.77	0.00
123	NTPC Vindhyachal Stage III		12.34	0.00
124	NTPC Vindhyachal Stage IV		9.42	0.00
125	NTPC Vindhyachal Stage V		5.76	0.00
126	NTPC khargone		14.70	0.00
127	R.K.M POWERGEN PRIVATE LIMITED		21.02	0.00
128	Ratnagiri Gas & Power Private Limited		0.00	2.68
129	SKS Power Generation Chhattisgarh Limited		33.83	0.00
130	Sasan Power Limited		8.13	0.00
131	TRN ENERGY PRIVATE LIMITED		42.43	0.00
132	The Tata Power Co Ltd (MTPS)		25.89	0.00
133	WIND FIVE RENERGY LIMITED		6.30	0.00
134	AM GREEN ENERGY PRIVATE LIMITED Wind		0.00	0.00
135	Andhra Pradesh		115.04	365.39
136	COASTAL ENERGEN PRIVATE LIMITED		43.81	0.00
137	Goa SR		0.22	7.38
138	IL&FS TAMIL NADU POWER COMPANY LIMITED		3.15	0.00
139	JINDAL POWER LIMITED SIMHAPURI		47.33	1.69
140	Karnataka		359.21	146.34
141	Kerala		36.17	280.67
142	MEENAKSHI ENERGY LIMITED		8.21	0.00
143	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		8.17	0.00
144	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		3.47	0.00
145	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.16	0.00
146	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		1.07	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जनवरी 2025
EXCHANGES THROUGH POWER EXCHANGES -January 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
147	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II	दक्षिणी क्षेत्र SR	1.06	0.00
148	NLC Tamilnadu Power Limited		4.93	0.00
149	NTECL VALLUR		6.01	0.00
150	NTPC KUDGI		9.49	0.00
151	NTPC Ramagundam Stage I &II		8.00	0.00
152	NTPC Ramagundam Stage III		2.20	0.00
153	NTPC Simhadri Stage I		0.80	0.00
154	NTPC Simhadri Stage II		2.56	0.00
155	NTPC Talcher Super Thermal Power Station Stage II		0.00	0.00
156	NTPC Telangana		2.76	0.00
157	OSTRO KANNADA POWER PRIVATE LIMITED		15.46	0.00
158	Pondicherry UT		36.65	0.05
159	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		2.82	0.00
160	Ramagundam Floating solar		7.06	0.00
161	ReNew Surya Roshni Private Limited_Gadag		0.74	0.00
162	SEIL ENERGY INDIA LIMITED		122.61	0.00
163	SEIL Energy India Limited Project II		34.74	0.00
164	SEMBCORP GREEN INFRA PRIVATE LIMITED (INFIRM)		1.59	0.00
165	Serentica Renewables India 1 Private Limited		1.01	0.00
166	Simhadri FSP 15 MW		1.92	0.00
167	Simhadri Floating solar (10 MW)		1.26	0.00
168	Tamil Nadu		327.18	339.66
169	Telangana		98.05	2627.30
170	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	0.05	0.00
171	Bihar		581.93	14.13
172	Damodar Valley Corporation		53.66	236.36
173	Dikchu Hydro Electric Project (Sneha Kinetic Power Projects Pvt. Ltd.)		2.17	0.00
174	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	193.77
175	GMR KAMALANGA ENERGY LTD-CTU		1.79	0.00
176	IND BARATH ENERGY UTKAL LIMITED		73.35	6.33
177	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.03	0.00
178	Jharkhand		101.94	42.74
179	Jindal India Power Limited		141.83	0.00
180	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		0.59	0.00
181	KANTI BIJLEE UTPADAN NIGAM LIMITED		15.32	0.00
182	MAITHON POWER LIMITED		6.64	0.00
183	NABINAGAR POWER GENERATING COMPANY LIMITED		67.32	0.00
184	NEA - Bihar STU		0.00	36.58
185	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	107.92
186	NTPC BARH Stage I		1.67	0.00
187	NTPC BARH Stage II		43.59	0.00
188	NTPC Darlipali		5.38	0.00
189	NTPC Farakka stage I		49.39	0.00
190	NTPC Farakka stage III		9.70	0.00
191	NTPC Kahalgaon stage I		7.52	0.00
192	NTPC Kahalgaon stage II		18.65	0.00
193	NTPC North Karanpura STPS		14.80	0.00
194	NTPC Talcher Stage I		10.08	0.00
195	NTPP BRBCL		24.68	0.00
196	Odisha		413.32	213.62
197	Sikkim		6.57	0.23

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जनवरी 2025 EXCHANGES THROUGH POWER EXCHANGES -January 2025				
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
198	Tashiding HEP, Shiga Energy Private Limited		0.00	0.00
199	West Bengal		369.01	127.57
200	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	14.69	0.00
201	ASSAM GAS BASED POWER STATION		1.63	0.00
202	Arunachal Pradesh		5.72	7.40
203	Assam		201.52	47.10
204	Bongaigaon Thermal Power Station NTPC		3.27	0.00
205	KAMENG HYDRO POWER STATION		8.46	0.00
206	Manipur		6.22	9.45
207	Meghalaya		9.76	65.81
208	Mizoram		0.88	0.04
209	Nagaland		4.75	5.54
210	Palatana Plant		17.35	0.00
211	Tripura		22.73	1.36
	Total		9756	9756

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : JANUARY 2025

RE Source & Unit wise break up (01.01.2025-31.01.2025)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	250	1	35	4
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	0	0	5	4
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**250**	**1**	**40**	**8**

RECs Issued (01.01.2025-31.01.2025)

Sr.No.	Non Solar	Solar	Total
1	5607753	111044	5718797

Redemption of REC (01.01.2025-31.01.2025)

Sr.No.	Non Solar	Solar	Total
1	6229556	36708	6266264

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : JANUARY 2025

RE Source & Unit wise break up (Apr'24-Jan'25)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	361	12	77	11
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	1279	22	268	22
5	Small Hydro	24	1	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1664**	**35**	**381**	**35**

RECs Issued (Apr'24-Jan'25)

Sr.No.	Non Solar	Solar	Total
1	39870664	973520	40844184

Redemption of REC (Apr'24-Jan'25)

Sr.No.	Non Solar	Solar	Total
1	24409988	292395	24702383

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : JANUARY 2025

RE Source & Unit wise break up Since Inception to Jan'25

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3409	536	2970	536
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	2906	592	1743	503
5	Small Hydro	869	43	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**8425**	**1302**	**6370**	**1176**

RECs Issued since Inception to Jan'25

Sr.No.	Non Solar	Solar	Total
1	154975702	14513898	169489600

Redemption of REC since Inception to Jan'25

Sr.No.	Non Solar	Solar	Total
1	102914317	12741652	115655969

REC Closing balance as on 31.12.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of Jan 2025 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Punjab	06-01-2025 09:32	06-01-2025 18:15	08:43	225	521	0.452	0.816	49743	63846	i) 220/132 KV Ropar (GGSTP) has double main bus system in 220KV and 132KV side. ii) During antecedent condition, 210 MW Guru Gobind Singh TPS (Ropar) - UNIT 3, Unit 4 and Unit 6 generating 180MW, 167MW and 176MW respectively. iii) As reported at 09:32 hrs, during the synchronization of the 210 MW Unit-5 at Guru Gobind Singh Thermal Power Station (Ropar), the R- phase limb of the 220 kV generator transformer circuit breaker for Unit-5 ruptured. This incident triggered the tripping of Units 3, 4, and 6, each with a capacity of 210 MW. Consequently, a blackout occurred at the 220 kV Guru Gobind Singh TPS substation. (Details of protection operation yet to be received). iv) As observed from PMU at Abdullapur (PG) S/s, R-N phase to earth fault was observed. Fault clearance time of 120 msec can be seen in the PMU. v) During this event, a total generation loss of 521MW was observed in Punjab control area . (As per SCADA). vi) As per SCADA, 225MW of change in demand is observed in Punjab control area.	(i) 210 MW Guru Gobind Singh TPS (Ropar) - UNIT 6 (ii) 210 MW Guru Gobind Singh TPS (Ropar) - UNIT 3 (iii) 210 MW Guru Gobind Singh TPS (Ropar) - UNIT 4
2	GI-2	Rajasthan	08-01-2025 13:38	08-01-2025 23:17	09:39	1450	0	2.714	0.000	53435	58056	i) 400KV Fatehgarh (Adani) pooling station has one and half breaker scheme with 400KV Fatehgarh (Adani) – Fatehgarh II Ckt 1 & 2, 400KV Fatehgarh (Adani) – Acme, 400KV Fatehgarh (Adani) – Fatehgarh PSS Ckt. 1 & 2. ii) As reported, at 13:38hrs, 400 KV Fatehgarh_II(PG)-Fatehgarh Pooling (FBTL) (FBTL) Ckt-1 tripped on R-Y phase to phase fault with fault distance of 45.8Km and fault current of 8.1KA from Fatehgarh (Adani) end. iii) As per PMU at Fatehgarh, R-Y phase to phase fault (voltage dipped upto 0.514 p.u.) is observed with fault clearing time of 80ms. After the fault clearance voltage increased upto .99 p.u. iv) As per PMU at Bassi (PG), a sharp drop in frequency is observed from 49.97 Hz to 49.83 Hz and frequency recovered to 49.99 Hz within 1 min. v) As per PMU, solar generation loss of approx., 719MW, 30MW, 218MW and 98MW are observed respectively at ASHPL (IP), AHEJ3 (IP), RSUPL (IP) and CSPJP (IP). vi) As per SCADA, dip in NR total solar generation of approx. 1450 MW is observed with change in Rajasthan solar generation of approx. 177 MW.	(i) 400 KV Fatehgarh_II(PG)-Fatehgarh Pooling (FBTL) (FBTL) Ckt-1
3	GI-2	Rajasthan	09-01-2025 23:35	10-01-2025 01:23	01:48	523	171	1.614	0.389	32407	43996	i) 400/220kV Akal(RS) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii) During antecedent condition, 400/220 kV 500 MVA ICT-1 & ICT-2 were connected to 400kV bus-1 and 400/220 kV 315 MVA ICT-3 & 500 MVA ICT-4 were connected to 400kV bus-2. iii) As reported, at 23:35 hrs, Y-phase jumper of 220kV bus-1 of 220kV Akal-Bhensara Ckt-1 snapped which created bus fault on both 220kV buses at Akal(RS). iv) As per PMU at Bhadla(PG), Y-N phase to earth fault with delayed fault clearance time of 720 msec is observed. v) Bus bar protection is not in service at 220kV side of Akal S/s. Therefore, fault cleared with the operation of back up protection i.e., 400/220kV ICTs at Akal. All four ICTs tripped on O/C E/F protection operation. vi) Due to tripping of all four ICTs at Akal(RS), evacuation path lost for all the wind power plants connected at 220kV bus-1 & bus-2 at Akal(RS). On this, both 220kV buses became dead at Akal(RS) S/s. vii) During this event, dip in Rajasthan wind generation of approx. 523 MW is observed out of which approx. 232 MW recovered within 6 minutes. (As per SCADA). viii) As per SCADA, about 171MW demand change is observed in Rajasthan control area.	i) 220 kV Akal – Bhainsara Ckt-1 ii) 220 kV Akal – Bhainsara Ckt-2 iii) 400/220 KV 500 MVA ICT 1 AT AKAL(RS) iv) 400/220 KV 500 MVA ICT 2 AT AKAL(RS) v) 400/220 KV 500 MVA ICT 3 AT AKAL(RS) vi) 400/220 KV 500 MVA ICT 4 AT AKAL(RS) vii) 220 kV Akal(RS) BUS-1 viii) 220 kV Akal(RS) BUS-2 ix) 220 kV AKAL-GIRAL x) 220kV AKAL-BARMER xi) 220 AKAL- AMARSAGAR xii) 220 AKAL- MADA xiii) 220 AKAL- AKAL(SUZLON) ckt-1 xiv) 220 AKAL- AKAL(SUZLON) ckt-2 xv) 220 AKAL- RAJGARH xvi) 220 AKAL- JAJIYA xvii) 220 AKAL- BHU ckt-1 xviii) 220 AKAL- BHU ckt-2 xix) 220 AKAL- DANGRI ckt-1 xx) 220 AKAL- DANGRI ckt-2 xxi) 220 AKAL- MOOLANA xxii) 220 AKAL- LALA
4	GI-2	Rajasthan	10-01-2025 13:35	10-01-2025 14:15	00:40	0	320	0.000	0.529	55872	60517	i) 400/220KV Heerapura sub-station has one and half breaker scheme in the 400KV side and Double main & transfer scheme in the 220 KV side. ii) As reported at 13:35hrs, a kite thread fell on the 220KV side of the ICTs. As a result Bus- Bar protection operated on the 220KV side led to tripping 400/220 kV 250 MVA ICT 1 and 3 at Heerapura(RS). (exact reason and nature of protection operated yet to be shared). iii) As per PMU at Heerapura (RS), R-N fault (delayed fault clearance in R-ph) is observed with delayed fault clearing time of 320ms. iv) As per SCADA, change in demand of approx. 320MW in Rajasthan control area is observed.	(i) 400/220 kV 250 MVA ICT 1 at Heerapura(RS) (ii) 400/220 kV 250 MVA ICT 3 at Heerapura(RS)
5	GD-1	Rajasthan	12-01-2025 06:31	12-01-2025 09:42	03:11	340	206	0.957	0.466	35522	44202	i) 400/220kV Akal(RS) has one and half breaker scheme at 400kV level and double main and transfer bus scheme at 220kV level. ii) During antecedent condition, 400/220 kV 500 MVA ICT-1 & ICT-2 were connected to 400kV bus-1 and 400/220 kV 315 MVA ICT-3 & 500 MVA ICT-4 were connected to 400kV bus-2. iii) As reported, at 06:31 hrs, B-N fault occurred on 400 KV Akal-Barmer (RS) Ckt, fault distance was 99.62KM and fault current was 2.42 KA from Barmer end. iv) However, as observed from PMU at Bhadla (PG) S/s, B-N fault was observed and subsequently it converted to Y-B-N double phase to earth fault. Delayed fault clearance time of 2120 msec can be seen in the PMU. v) On this fault, line tripped from Barmer end but breaker of Akal end got stuck due to issue in SF6 gas pressure. Due to non opening of breaker of Akal end, LBB protection would have operated. vi) However, all the 400kV lines and 400/220kV ICTs at Akal tripped during the event. Exact details of protection operation not received yet from SLDC-Rajasthan. vii) Due to tripping of all four ICTs at Akal(RS), evacuation path lost for all the wind power plants connected at 220kV bus-1 & bus-2 at Akal(RS). On this, both 400 and 220kV buses became dead at Akal(RS) S/s. viii) During this event, a dip in Rajasthan wind generation of approx. 340 MW is observed which recovered completely within 5 minutes. (As per SCADA). ix) As per SCADA, 206MW of change in demand is observed in Rajasthan control area.	(i) 400/220 KV 500 MVA ICT 1 AT AKAL(RS) (ii) 400/220 KV 500 MVA ICT 2 AT AKAL(RS) (iii) 400/220 KV 500 MVA ICT 3 AT AKAL(RS) (iv) 400/220 KV 500 MVA ICT 4 AT AKAL(RS) (v) 400/220 KV 500 MVA ICT 2 AT RAMGARH(RS) (vi) 400 KV AKAL-JODHPUR (RS) CKT-1 (vii) 400 KV AKAL-BARMER (RS) CKT-1 (viii) 400 KV AKAL-JAISALMER (RS) CKT-1 (ix) 400 KV AKAL-RAMGARH (RS) CKT-1 (x) 400 KV AKAL-RAMGARH (RS) CKT-2 (xi) 400 KV AKAL-KANKANI (RS) CKT-1
6	GD-1	Rajasthan	13-01-2025 14:04	14-01-2025 00:31	10:27	280	0	0.587	0.000	47735	52615	i) Generation of 220 KV AHEJ4L PSS 2 (ASPS2) (IP) station evacuates through 220 KV AHEJ4L PSS 2 HB_FGRAH_FBTL (AHEJ4L)-Adani RenewPark_SL_FGARH_FBTL (AREPRL) (AHEJ4L) Ckt. During antecedent condition, 220 KV AHEJ4L PSS 2 (ASPS2) (IP) was generating approx. 280 MW (as per PMU). ii) As reported, at 14:04hrs, 220 KV AHEJ4L PSS 2 HB_FGRAH_FBTL (AHEJ4L)-Adani RenewPark_SL_FGARH_FBTL (AREPRL) (AHEJ4L) Ckt tripped on R-Y phase to phase fault with fault distance of 14km and fault current of 6.7kA from Adani Fatehgarh Solar Park end. During inspection, broken insulator was found at 220 KV AHEJ4L PSS 2 (ASPS2) (IP) gantry. iii) Due to tripping of 220 KV AHEJ4L PSS 2 HB_FGRAH_FBTL (AHEJ4L)-Adani RenewPark_SL_FGARH_FBTL (AREPRL) (AHEJ4L) Ckt, 220 KV AHEJ4L PSS 2 (ASPS2) (IP) S/s lost its connectivity from grid and blackout occurred at 220 KV AHEJ4L PSS 2 (ASPS2) (IP) S/s. iv) As per PMU at 400kV Adani Fatehgarh(IP), R-Y phase to phase fault (voltage dipped upto 0.823 p.u.) is observed with fault clearing time of 120ms. v) As per PMU, solar generation loss of approx. 280 MW was observed at 220 KV AHEJ4L PSS 2 (ASPS2) (IP).	1) 220 KV AHEJ4L PSS 2 HB_FGRAH_FBTL (AHEJ4L)-Adani RenewPark_SL_FGARH_FBTL (AREPRL) (AHEJ4L) Ckt

Details of Grid Events during the Month of Jan 2025 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD-1	Rajasthan	14-01-2025 13:13	14-01-2025 14:36	01:23	473	0	0.899	0.000	52585	57053	i)Generation of 220kV Nokhra (IP) and 220kV RSDCL-4(IP) stations evacuate through 220 KV Nokhra SL_BHD2 (NTPC)-Bhadla_2 (PG) (NTPC_NOKHRA) Ckt and 220 KV Bhadla_2 (PG)-RSDCL(PSS4)_SL_BHD2_PG (RSDCL) Ckt respectively. ii)During antecedent condition, 220kV Nokhra (IP) and 220kV RSDCL-4(IP) were generating approx. 295 MW and 178 MW respectively (as per PMU). iii)As reported, at 13:13hrs, 220 KV Bhadla_2 (PG)-RSDCL(PSS4)_SL_BHD2_PG (RSDCL) Ckt tripped on B-N phase to earth fault with fault distance of 1.3km and fault current of 23.4kA from Bhadla2(PG) end. During inspection it was found that jumper snapped out at tower location no. 8. iv)During the same time, 220 KV Nokhra SL_BHD2 (NTPC)-Bhadla_2 (PG) (NTPC_NOKHRA) Ckt along with 220/33 kV 100 MVA ICT 1, 2 and 3 at Nokhra SL_BHD2 (NTPC) also tripped. Line tripped from Nokhra(NTPC) end only (exact reason of tripping and nature of protection operated yet to be shared). v)Due to tripping of 220 KV Nokhra SL_BHD2 (NTPC)-Bhadla_2 (PG) (NTPC_NOKHRA) Ckt and 220 KV Bhadla_2 (PG)-RSDCL(PSS4)_SL_BHD2_PG (RSDCL) Ckt , 220kV Nokhra (IP) and 220kV RSDCL-4(IP) S/s lost their connectivity from grid and blackout occurred at 220kV Nokhra (IP) and 220kV RSDCL-4(IP) S/s. vi)As per PMU at 220kV Nokhra(NTPC), B-N phase to earth fault (voltage dipped upto 0.269 p.u.) is observed with fault clearing time of 80ms. vii)As per PMU, solar generation loss of approx. 295 MW at Nokhra(IP) and 178 MW at RSDCL-4(IP) were observed.	1) 220 KV Bhadla_2 (PG)-RSDCL(PSS4)_SL_BHD2_PG (RSDCL) Ckt 2) 220 KV Nokhra SL_BHD2 (NTPC)-Bhadla_2 (PG) (NTPC_NOKHRA) Ckt 3) 220/33 kV 100 MVA ICT 1 at Nokhra SL_BHD2 (NTPC) 4) 220/33 kV 100 MVA ICT 2 at Nokhra SL_BHD2 (NTPC) 5) 220/33 kV 100 MVA ICT 3 at Nokhra SL_BHD2 (NTPC)
8	GD- I	Rajasthan	22-01-2025 09:13	22-01-2025 11:54	02:41	54	0	0.103	0.000	52270	64710	i)Generation of 220kV Anta station evacuate through 220 KV Anta(NT)-Sakatpura(RS) (RS) Ckt-1, 220 KV SAWAIMADHOPUR(RS)- Anta(NT) (PG) CKT-1, 220 KV ANTA(NT)-BHILWARA(RS) (PG) CKT-1 & 2, 220 KV LALSOTE(RS)-Anta(NT) (PG) CKT-1 and 220 KV RAPS_C(NP)-ANTA(NT) (PG) CKT-1 respectively. ii)During antecedent condition, GT-I, II & III, 220 KV ANTA(NT)-BHILWARA(RS) (PG) CKT-1 & 2, 220 KV RAPS_C(NP)-ANTA(NT) (PG) CKT-1 were under shutdown respectively (as per PMU). iii)As reported, at 09:13hrs, 220 KV Anta(NT)-Sakatpura(RS) (RS) Ckt-1 tripped on B-N phase to earth fault with fault distance of 54.5km and fault current of 1.07kA from Anta end(Z2 Operated). During the inspection it was found that B-Phase CT of 220 KV Anta(NT)-Sakatpura(RS) (RS) Ckt-1 failed on Sakatpura end . iv)Again at 10:10 hrs, 220 KV SAWAIMADHOPUR(RS)- Anta(NT) (PG) CKT-1 which was carrying 52MW load tripped due to high voltage (details of tripping awaited). And this led to the blackout of 220KV Anta substation. v)As per PMU at 400KV Kota(PG), B-N phase to earth fault (voltage dipped upto 0.71 p.u.) is observed with fault clearing time of 120ms. vi)As per PMU, solar generation loss of approx. 38 MW at 09:13 hrs and 54 MW at 10:10 hrs occurred in Anta was observed.	i) 220 KV Anta(NT)-Sakatpura(RS) (RS) Ckt-1 ii) 220 KV SAWAIMADHOPUR(RS)- Anta(NT) (PG) CKT-1
9	GD- I	Haryana	23-01-2025 06:09	23-01-2025 07:50	01:41	0	0	0.000	0.000	35877	48363	i)220/132/33KV HUKMAWALI S/stn sub-station has double main bus scheme in all voltage level. ii)During antecedent condition, 220 KV Fatehabad(PG)-Hukmawali (HV) (HVPNL) Ckt-1, 220 KV Fatehabad(PG)-Hukmawali (HV) (HVPNL) Ckt-2, and 220 kV HUKMAWALI(HV)-CHORMAR(HV) CKT-1 were carrying 27MW, 28MW and 19MW load respectively. iii)As reported at 06:09hrs, B-phase CT of 220 kV HUKMAWALI(HV)-CHORMAR(HV) CKT-1 exploded and thereby led to Bus bar protection operation. This resulted in tripping of all the elements connected to 220KV Bus bar. As a result, the Sub-station lost its connectivity to the Grid and Blackout occurred. iv)As per DR and EL of 220 KV Fatehabad(PG)-Hukmawali (HV) (HVPNL) Ckt-1 at 220KV Fatehabad, the line tripped due to Main-1, Zone-2 protection operation. The fault current in B phase was 6.8KA and Y phase was 7.4KA. v)As per PMU at 400 Fatehabad (PG), B-N fault converted to Y-B-N fault is observed with delayed fault clearing time of 400ms. vi)As per SCADA, no change in demand in Haryana control area is observed.	i) 220 KV Fatehabad(PG)-Hukmawali (HV) (HVPNL) Ckt-1 ii) 220 KV Fatehabad(PG)-Hukmawali (HV) (HVPNL) Ckt-2 iii) 220 kV HUKMAWALI(HV)-CHORMAR(HV) CKT-1 iv) 220 kV HUKMAWALI(HV)-CHORMAR(HV) CKT-2
10	GI-I	Rajasthan	24-01-2025 16:38	24-01-2025 18:31	01:53	269	0	0.515	0.000	52270	64710	i)Generation of 220kV Tata Power Saurya Banderwala evacuate through 220 KV BTPSL_SL_BIK2_PG-Bikaner_2 (PBTSL) (BANDERWALA_TPSL) Ckt. ii)During antecedent condition, 220 KV BTPSL_SL_BIK2_PG-Bikaner_2 (PBTSL) (BANDERWALA_TPSL) Ckt was evacuating 126MW of load (as per PMU). iii)As reported, at 16:38hrs, 220 KV BTPSL_SL_BIK2_PG-Bikaner_2 (PBTSL) (BANDERWALA_TPSL) Ckt tripped on B-N phase to earth fault. (exact reason of tripping and nature of protection operated yet to be shared). Due to tripping of the evacuation path, the sub-station lost its connectivity from grid and blackout occurred at 220 kV Tata Power Saurya Banderwala S/S. iv)As per PMU at TPSB, B-N phase to earth fault (voltage dipped upto 0.02 p.u.) is observed with unsuccessful A/R operation is observed. v)As per PMU, solar generation loss of approx. 126MW of Generation loss had occurred in TPSB and 269 MW of change in NR Solar generation was observed.	i) 220 KV BTPSL_SL_BIK2_PG-Bikaner_2 (PBTSL) (BANDERWALA_TPSL) Ckt-1
11	GI-2	Uttar Pradesh	29-01-2025 12:09	29-01-2025 12:58	00:49	0	252	0.000	0.392	56638	64270	i)400/220/132KV Jehta S/stn sub-station has double main bus scheme in all voltage level. ii)During antecedent condition, 400/220 kV 500 MVA ICT-1 & ICT-2 were connected to 400kV bus-1 and bus-2 respectively carrying 107MW of load each. 220/132KV ICT-3 and ICT-4 were carrying 35MW load each. iii)As reported at 12:09 hrs, 400/220KV ICT -1 and ICT-2 tripped due to Bus Bar protection. This led to further tripping of 220/132KV ICT-3 and ICT-4 downstream along with tripping of both 220KV Bus-I and Bus-II. As a result, all the elements connected to 220KV Bus Bar tripped. iv)DR and EL submitted by SLDC for 400/220KV ICT-1 and 2, shows Bus Bar protection operation. However as per PMU no fault was observed. Reason of operation of bus bar protection need to be shared. v)As per SCADA, 252MW of change in demand is observed in Rajasthan control area.	(i)400/220 kV 500 MVA ICT 1 at Jehta_Hardoi Road (UP) (ii)400/220 kV 500 MVA ICT 2 at Jehta_Hardoi Road (UP) (iii)220/132kV 200 MVA ICT-1 at Jehta(UP) (iv)220/132kV 200 MVA ICT-2 at Jehta(UP) (v)220kV Jehta-Hardoi road (UP) ckt-1 (vi)220kV Jehta-Hardoi road (UP) ckt-2 (vii)220kV Jehta-Mallawan (UP) ckt-1 (viii)220kV Jehta-Mallawan (UP) ckt-2 (ix)220kV Bus coupler at Jehta(UP)

Details of Grid Events during the Month of Dec 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	23:46 / 09-01-2025	03:00 / 15-01-2025	123:14	95	-	0.14%	-	65864	52860	At 23:46 hrs / 09-01-2025, 220 kV Bhuj-Gadhsisa tripped on R-B phase to phase fault. During patrolling, it was found that the top cage section of tower 15/1 was damaged due to conductor theft. Due to loss of single evacuation transmission line 220 kV Gadhsisa substation became dead. Generation loss of 95 MW occurred at Gadhsisa (Renew Power) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1.220 kV Bhuj-Gadhsisa-1
2	GD-1	WR	11:13 / 11-01-2025	12:28 / 11-01-2025	01:15	35	-	0.04%	-	85437	76571	At 11:13 hrs / 11-01-2025, 220 kV Bhuj-Kotda Madh-1 tripped from Kotda Madh end only due to receipt of DT signal from Bhuj end. The tripping was due to maloperation as there were no relay indications reported at Bhuj end. PMU stopped reporting after the tripping. Due to loss of single evacuation transmission line 220 kV Kotda Madh substation became dead. Generation loss of 35 MW occurred at Kotda Madh (Alfanar) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1.220 kV Bhuj-Kotda Madh-1
3	GD-1	WR	15:08 / 12-01-2025	15:55 / 12-01-2025	00:47	76	-	0.10%	-	75422	68599	At 15:08 hrs / 12-01-2025, 220 kV Bhuj-Kotda Madh-1 tripped from Kotda Madh end only due to receipt of DT signal from Bhuj end. The tripping was due to maloperation as there were no relay indications reported at Bhuj end. PMU stopped reporting after the tripping. Due to loss of single evacuation transmission line 220 kV Kotda Madh substation became dead. Similar tripping due to receipt of false DT signal occurred at 15:08 hrs / 12-01-2025. Generation loss of 76 MW occurred at Kotda Madh (Alfanar) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1.220 kV Bhuj-Kotda Madh-1
4	GD-1	WR	11:57 / 14-01-2025	14:02 / 14-01-2025	02:05	18	-	0.02%	-	75743	66419	At 11:57 hrs / 14-01-2025, 220 kV Nakhtrana-Dedhiya-1 line tripped on R-Y fault on Z-1 from Nakhatrana and Dedhiya end. Simaltaneously, 220 kV Nakhtrana-Bhuj II-1 tripped from nakhatrana end which was undesirable. Due to loss of single evacuation transmission line 220 kV Nakhatrana and Dedhiya (Adani) substations became dead. Generation loss of 18 MW occurred at Nakhatrana and Dedhiya (Adani) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1.220 kV Nakhtrana-Dedhiya-1 2.220kV Nakhtrana-Bhuj II-1
5	GD-1	WR	02:40 / 18-01-2025	04:50 / 18-01-2025	02:10	-	180	-	0.35%	62688	51635	At 02:40 hrs / 18.01.2025, 220 kV side R-phase CT of 220/132 kV Raigarh-ICT-2 at 220kV-Raigargh (CG) failed. After 600 msec R phase of jumper of auxilary bus section side of 220/132 kV Raigarh-ICT-2 got disconnected resulting in tripping of all connected elements at 220 kV Raigarh(CG). Load loss of about 180 MW occurred at Raigarh(CG) and down stream network due to the event.	Tripping of following Elements: 1. 220 kV Raigarh(CG)-Raigarh(PG)-1,2&3 2. 220 kV Raigarh(CG)-Bus-1&2 3. 220 kV Raigarh(CG)-Saraipali-1 4. 220 kV Raigarh-Korba(E)-1 5. 220/132 kV Raigarh-ICT-1,2&3 (160 MVA)
6	GD-1	WR	04:22 / 19-01-2025	04:55 / 19-01-2025	00:33	-	300	-	0.57%	65705	52637	At 04:22 hrs / 19-01-2024, 220 kV Morbi-Hadala-1 tripped on R-E fault due to R-phase CVT blast at Morbi. Simaltaneously, bus bar protection operated due to flames of blasted CVT coming in induction zone of 220 kV Morbi-Bus-1 (Single main and transfer bus) which lead to tripping of all connected elements. Load loss of 300 MW occurred at Morbi and related downstraem network due to the event.	Tripping of following Elements: 1.220 kV Morbi -Hadala-1 2.220 kV Morbi-Bus-1 3.220 kV Morbi-Vondh-1 4.220/66 kV Morbi-ICT-1,2&3 5.220 kV Morbi-Shivlakha-1&2 6.220 kV Morbi-Lalpar-1 7.220 kV Morbi-Bhimasar-1
7	GD-1	WR	13:12 / 24-01-2025	13:26 / 24-01-2025	00:14	-	200	-	0.28%	79809	71897	At 13:12 hrs / 24-01-2025, 220 kV Ponda-Bus-1 tripped on Bus bar protection mal-operation during closing of 220 kV Amona Buscoulper. Prior to the incident, 220 kV Ponda-Bus-2 (which was feeding 220 kV Tillari and 220 kV Mahalaxmi through 220 kV Amona) became dead due to tripping of 220 kV Tillari-Amona-1 and 220 kV Mahalaxmi-Amona-1 at 12:55 / 24-01-2025. Further during closing of bus coupler at 220 kV Amona (for restoration works), 220 kV Ponda-Bus-1 Bus bar protection mal-operation. Load loss of 200 MW occurred at Ponda due and near by network in Goa due to the event.	Tripping of following Elements: 1. 220 kV Ponda-Bus-1 2. 220 kV Mapusa-Ponda-1 3. 220/33 kV Ponda ICT-1 4. 220/110 kV Ponda ICT-2 (100 MVA)
8	GD-1	WR	10:09 / 27-01-2025	12:57 / 27-01-2025	02:48	200	-	0.24%	-	84790	78146	At 10:09 hrs / 27-01-2025, 400/33 kV Khirsara-ICT-1 (300 MVA) tripped on Over Excitation. 400 kV Khirsara-Varsana-1 tripped on AC directional over current relay operation which was undesireable. The line was 400 kV Khirsara-Varsana-1 without attending the issue at 12:57 hrs / 27-01-2025 which was resolved by taking emergency shutdown of 400 kV Khirsara-Varsana-1 at 20:25 hrs / 27-01-2025 for checking wiring of CTs and IR values measurement. Generation loss of 200 MW occurred at Khirsara (Gaya Solar-Adani) Solar power plant due to loss of evacuation path.	Tripping of following Elements: 1. 400 kV Khirsara-Varsana-1 2. 400/33 kV Khirsara-ICT-1 (300 MVA)

Details of Grid Events during the Month of Dec 2024 in Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD-1	WR	03:01 / 28-01-2025	04:29 / 28-01-2025	01:28	56	-	0.09%	-	63265	55237	At 03:01 hrs / 28-01-2025, 220 kV Indore(PG)-Pritamnagar-1 tripped on R-E fault from Pritam Nagar end only. Autorecloser successful at Indore (PG) end. During patrolling no abnormalities were found. Due to loss of single evacuation transmission line 220 kV Pritam Nagar substation became dead. Generation loss of 56 MW occurred at Pritam Nagar (Adani) Wind power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Indore(PG)-Pritamnagar-1
10	GD-1	WR	13:12 / 28-01-2025	13:57 / 28-01-2025	00:45	-	186	-	0.25%	79067	73125	At 13:12 hrs / 28-01-2025, 220 kV Tivim-Bus-1 (Main and Transfer bus scheme) tripped on Bus bar protection operation resulting in tripping 220 kV Mapusa-Tivim-1&2. An object coming in induction zone of bus due to high wind resulted in busbar protection operation and substation became dead. Due to loss of both evacuation transmission lines 220 kV Tivim (Goa) substation became dead. Load loss of 186 MW occurred at Tivim due to the event.	Tripping of following Elements: 1. 220 kV Mapusa-Tivim-1&2 2. 220/110 kV Tivim-ICT-1,2&3
11	GD-1	WR	13:19 / 30-01-2025	21:27 / 30-01-2025	08:08	1	-	0.00%	-	63265	55237	At 13:19 hrs / 30-01-2025, 220 kV Bhuj-Gadhsisa tripped on Y-B phase to phase fault. During patrolling, tree was found in induction zone. The line was test charged at 14:58 hrs / 30-01-2025 and didn't hold. Due to loss of single evacuation transmission line 220 kV Gadhsisa substation became dead. Generation loss of 1 MW occurred at Gadhsisa (Renew Power) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Gadhsisa-1
12	GD-1	WR	17:20 / 30-01-2025	18:20 / 30-01-2025	01:00	-	888	-	1.24%	78134	71885	At 17:20 hrs / 30-01-2025, multiple trippings occurred at 400/220 kV Kansari substation during charging of 400 kV Kansari-Bus Reactor-2 (125 MVAr) which was out on voltage regulation. Y-phase pole 400 kV Kansari-Bus Reactor-2 circuit breaker didn't close properly while charging causing increased current in R and B phases, which resulted in flashover. Busbar protection didn't operate and elements connected to 400/220 kV Kansari tripped due to persisting fault. Load loss of 888 MW occurred at Kansari and downstream network due to the event. Detailed inspection is in progress.	Tripping of following Elements: 1. 220 kV Kansari-Bus-1&2 2. 400/220 kV Kansari-ICT-1,2,3&4 (315 MVA) 3. 400 kV Kansari-Veluda-1 4. 400 kV Charanka-Kansari-1&2 5. 400 kV Kansari-Bus Coupler 6. 400 kV Soja-Kansari-1,2&3 7. 400 kV Banaskantha-Kansari-1 8. 400 kV Kankroli-Kansari-1 9. 220/66 kV Kansari-ICT-1,2,3&4 (100 MVA) 10. 400 kV Kansari-Bus Reactor-2 (125 MVAr) 11. 220 kV Kansari-Deodar-1&2 12. 220 kV Kansari-Tharad-1 13. 220 kV Kansari-Agthala-1 14. 220 kV Kansari-Thaver-1&2 15. 220 kV Kansari-Jangral-1&2 16. 220 kV Kansari-Palanpur-1&2 17. 220 kV Deodhar-Radhanpur-1 18. 220 kV Deodhar-Mera-1&2 19. 220 kV Tharad-Mera-1&2 20. 220 kV Tharad-Thavar-1&2 21. 220 kV Tharad-Amarpur-1&2

Details of Grid Events during the Month of Dec 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA	04-01-2025 13:51	05-01-2025 05:27	15:36	50	0	0.10%	0.00%	49353.0	53613.91	Complete Outage of 220kV RSRPL Koppal: As per the reports submitted, the triggering incident was B-N fault in 220kV KNTL RSRPL line and the line tripped at both ends. Tripping of the only connected line led to complete outage of 220kV RSRPL Koppal.	220KV-KOPPAL-Renew_Surya_Koppal-1
2	GD - 1	KARNATAKA	06-01-2025 21:37	06-01-2025 22:48	01:11	0	0	0.00%	0.00%	36774.05	42975.43	Complete Outage of 220kV KSPDCL SS-4 Generating station: As per the submitted reports, the triggering incident was a B-N fault in the 220kV connecting cable of the 400kV/220kV Pavagada ICT-6. Immediately, the Main-1 differential protection of the ICT operated, resulting in the tripping of the ICT. Simultaneously, the 220kV Pavagada KSPDCL-4 line tripped at the KSPDCL end due to suspected maloperation. The tripping of the only connected line led to the complete outage of the 220kV KSPDCL-4 generating station.	KSPDCL4 - 220KV, KSPDCL4 - 220KV - Bus 1, 220KV-PAVAGADA_PG-KSPDCL4
3	GD - 1	ANDHRA PRADE	12-01-2025 14:16	12-01-2025 14:55	00:39	0	49	0.00%	0.09%	46935.54	53647.11	Complete Outage of 220kV/132kV Rajampet SS: As per the reports submitted, the triggering incident was B-N fault in 220kV Rajampet Koduru line. At Kuduru end, the fault was sensed in zone-2, carrier received, A/R operated and the line was holding. At Rajampet end, the fault was sensed in zone-1 but R-pole tripped instead of B-pole due to interchange of trip circuit wiring between R-Ph and B-Ph CB. Subsequently, 220kV Rajampet Cuddapah line tripped only at Cuddapah end on zone-2 distance protection. This resulted in the complete outage of 220kV/132kV Rajampet SS.	220KV-CUDDAPAH-RAJAMPET-1, 220KV-RAJAMPET-KODURU-1
4	GD - 1	KARNATAKA	23-01-2025 13:02	23-01-2025 13:32	00:30	0	112	0.00%	0.19%	50589.15	58407.23	Complete Outage of 220kV/66kV Exora SS, 220kV/66kV Vikas Tech and 220kV Bus-1 Outage at 220kV/66kV Malur SS of KPTCL: 220kV Malur SS was operating with split bus condition with 220kV Hoody Malur line feeding 220kV Malur Bus-1. 220kV/66kV Exora and 220kV/66kV Vikas Tech Park were being radially fed from 220kV Malur Bus-1. As per the reports submitted, the triggering incident was tripping of 220kV Hoody Malur line on DEF maloperation at Malur end. Tripping of this line led to loss of power supply to 220kV Malur Bus-1 which intrun led to complete outage of 220kV/66kV Exora SS and 220kV/66kV Vikas Tech Park.	220KV-HOODY-MALUR-1
5	GD - 1	KARNATAKA	26-01-2025 10:07	26-01-2024 12:33	02:26	0	78	0.00%	0.14%	53360.79	55139.43	Complete Outage of 220kV/66kV Exora SS, 220kV/66kV Vikas Tech and 220kV Bus-1 Outage at 220kV/66kV Malur SS of KPTCL: 220kV Malur SS was operating with split bus condition with 220kV Hoody Malur line feeding 220kV Malur Bus-1. 220kV/66kV Exora and 220kV/66kV Vikas Tech Park were being radially fed from 220kV Malur Bus-1. As per the reports submitted, the triggering incident was Y-N fault in 220kV Hoody Malur line. Tripping of this line led to loss of power supply to 220kV Malur Bus-1 which intrun led to complete outage of 220kV/66kV Exora SS and 220kV/66kV Vikas Tech Park.	220KV-HOODY-MALUR-1
6	GD - 1	KERALA	27-01-2025 15:38	27-01-2025 15:42	00:04	0	259	0.00%	0.44%	50671.88	59276.69	Complete Outage of 220kV/110kV Thlassery SS, 220kV/110kV Kanhirode SS, 220kV/110kV Ambalathara SS, 220kV/110kV Mylatti SS, 220kV/110kV Taliparamba SS and 220kV/110kV Orkattery SS of KSEB: 220kV/110kV Thlassery SS, 220kV/110kV Kanhirode SS, 220kV/110kV Ambalathara SS, 220kV/110kV Mylatti SS, 220kV/110kV Taliparamba SS and 220kV/110kV Orkattery SS are being radially connected through 220kV Areakode Orkattery line and 220kV Areakode Kanhirode line. During antecedent conditions, 220kV Areakode Kanhirode was under outage. The triggering incident was B-N fault in 220kV Areakode orakattery Line and the line tripped. Tripping of the only connected line led to complete outage of 220kV/110kV Thlassery SS, 220kV/110kV Kanhirode SS, 220kV/110kV Ambalathara SS, 220kV/110kV Mylatti SS, 220kV/110kV Taliparamba SS and 220kV/110kV Orkattery SS.	220KV-AREACODE-ORKKATTERY-1

Details of Grid Events during the Month of Dec 2024 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD - 1	ANDHRA PRADESH	31-01-2025 02:13	31-01-2025 03:49	01:36	0	0	0.00%	0.00%	35732.4	44445.14	Complete Outage of 220kV Nagarjun Sagar AP SWS of APTRANSCO: As per the reports submitted, due to operation of 220kV Bus-1 and Bus-2 BBP there was complete outage of 220kV Nagarjun Sagar AP SWS.	220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3, 220KV-NAGARJUNASAGAR_TS-CHALAKURTHY-1, 400KV/220KV NAGARJUNASAGAR_PG-ICT-1, 400KV/220KV NAGARJUNASAGAR_PG-ICT-2, 400KV/220KV NAGARJUNASAGAR_PG-ICT-3, 220KV-NAGARJUNASAGAR_AP-RENTACHINTHALA-1, 220KV-NAGARJUNASAGAR_AP-RENTACHINTHALA-2, 220KV-NAGARJUNASAGAR_AP-INAPARAJUPALLI-1, 220KV-NAGARJUNASAGAR_AP-INAPARAJUPALLI-2
8	GD - 1	TAMILNADU	31-01-2025 15:27	31-01-2025 19:55	04:28	0	0	0.00%	0.00%	53705.05	62784.57	Complete Outage of 230kV JSW_Dharapuram Wind Station: As per the reports submitted, the triggering incident was tripping of 230kV Karur JSW_Dharapuram-1 line at Karur end on DEF protection and DT was received at Dharapuram end. Tripping of the only connected line led to complete outage of 230kV JSW_Dharapuram Wind Station.	KARUR_JSW_Dharapuram_1 - 230KV
9	GI-1	TAMILNADU	04-01-2025 02:26	04-01-2025 07:12	04:46	0	0	0.00%	0.00%	31675.11	39089.73	Tripping of 230kV Bus-1 of 400kV/230kV Kudankulam Generating Station: As per the reports submitted, the triggering incident was LBB maloperation in Kudankulam GT-1. All elements connected to 230kV Bus-1 tripped resulting in the outage of 230kV Bus-1 of 400kV/230kV Kudankulam Generating Station.	230KV-KUDANKULAM-S R PUDUR, 400KV/230KV KUDANKULAM-ICT-1
10	GI-1	KARNATAKA	19-01-2025 10:33	19-01-2025 16:17	05:44	0	55	0.00%	0.10%	48059.26	53959.64	Tripping of 220kV Bus-2 at 220/66kV YERRAANDAHALLI SS: In the antecedent conditions, 220/66kV YERRAANDAHALLI is operating in Bus split condition at 220kV level, where in 220kV Bus-2 was radially connected to 220kV Yerrahandalli Hosur line. The tripping of the only line connected to Bus-2 led to the tripping of 220kV Bus-2 at 220/66kV YERRAANDAHALLI SS.	YERRAANDAHALLI Hosur - 220KV
11	GI-1	ANDHRA PRADESH	25-01-2025 08:14	25-01-2025 08:57	00:43	0	0	0.00%	0.00%	49169.59	57892.52	Tripping of 220kV Bus-2 of 220kV Lower Sileru PH of APGENCO: As per the reports submitted, the triggering incident was Unit-1 LBB operation due to spurious current in Unit-1 CB though the CB is open. Immediately, all elements connected to 220kV Bus-2 tripped.	220KV-ASUPAKA-LOWER_SILERU-1, 220KV-LOWER_SILERU-Chintur-1, LOWER_SILERU - 220KV - Bus 2
12	GI-2	ANDHRA PRADESH	27-01-2025 12:24	27-01-2025 13:14	00:50	600	0	1.08%	0.00%	55321.79	60170.0	Tripping of 400kV Bus-2 of 400kV VTPS Generating station of APGENCO: As per the reports submitted, the triggering incident was LBB maloperation in GT-8 of VTPS Generating station. Immediately, LBB operated and all elements connected to 400kV VTPS Bus-2 tripped.	400KV-NELLORE_AP-VTPS_IV-1
13	GI-1	ANDHRA PRADESH	27-01-2025 15:53	27-01-2025 19:21	03:28	0	0	0.00%	0.00%	46774.4	55723.01	Tripping of 220kV Bus-1 of 220kV Gooty SWS of APTRANSCO: As per the reports submitted, the triggering incident was YN fault in 220kV Bus-1 Gooty SWS. Immediately Bus-1 BBP operated and all elements connected to 220kV Gooty SWS Bus-1 got tripped.	400KV/220KV GOOTY-ICT-3, GOOTY-SWS - 220KV - Bus 1
14	GI-1	TELANGANA	27-01-2025 17:22	27-01-2025 17:47	00:25	0	0	0.00%	0.00%	46247.29	53478.61	Tripping of 220kV Bus-2 of 220kV Nagarjun Sagar PH of TGGENCO: As per the reports submitted, the triggering incident was R-N fault in the stator of Unit-8 while synchronising Unit-8 to the Grid. Immediately, Class A Generator protection operated. However, R-pole failed to open causing LBB to operate. Immediately, all elements connected to 220kV Bus-2 of Nagarjun Sagar PH tripped.	220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-2, 220KV-NAGARJUNASAGAR_AP-NAGARJUNASAGAR_TS-3

Details of Grid Events during the Month of Dec 2024 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-I	NTPC BARH	04.01.2025 19:23	04.01.2025 19:47	00:24	1800	0	5.91%	0.00%	30472	23247	Pre event: (400 kV Barh-Kahalgaon-2 & 400 kV Barh-Patna-1&2 Under continuous S/d) (400 KV Barh-Patna-4 Under breakdown) (400 kV Barh-Motihari-2 Under emergency S/d for rectification of B/D line). Event: At 19:17 Hrs, 400 KV Barh-Patna-3 tripped from Barh on O/c. After six minutes at 19:23 Hrs, 400 kV Barh-Motihari-1 tripped due to Y_N fault . Subsequently, after 9 seconds, 400 kV Barh-Kahalgaon-1 also tripped on O/c from Barh. This led to total power failure at Barh at 19:23 Hrs. Generation loss of around 1800 MW occurred.	400 kV Barh-Patna-3 400 kV Barh-Motihari-1 400 kV Barh-Kahalgaon-1
3	GD-I	GODDA	16.01.2025 17:17	16.01.2025 17:40	00:23	0	120	0.00%	0.52%	30073	23247	At 17:17 Hrs, Tenughat unit-2 tripped due to turbine vibration issue. Unit-1 was already under forced outage since 14/01/2025 on Boiler tube leakage. Outage of both the units of Tenughat led to overloading of 220 kV Maithon - Dumka D/C which further resulted in SPS operation at dumka. As Godda is radially fed from Dumka, SPS operation at Dumka S/s resulted in tripping of 220 kV Dumka-Godda D/C and 132kV-Dumka-Pakur D/C. Total load loss of 120 MW occurred at 220 kV Godda S/s and 132 kV Pakur S/s.	220 kV Dumka- Godda-1 220 kV Dumka- Godda-2 132 Kv Godda-Pakur D/C
4	GD-I	JSPL(CPP)	25.01.2025 05:13	25.01.2025 05:40	00:27	420	445	1.57%	2.46%	26701	18065	400KV-MEERAMUNDALI-JSPL D/C tripped at 05:13 Hrs due to Y-B fault. Both Bus at 400 kV JSPL became dead as it was radially connected to 400 kV Meramundali S/S. Captive power plant JSPL has 6 units of 135 MW capacity each. Unit-1 with emergency load of 90 MW was separately connected with 220 kV Bus-1 (220 kV bus-coupler remaining open). Unit-2 of JSPL was under overhauling and other 4 units (unit-3,4,5,6) connected to 220 kV Bus-2 were generating around 420 MW and rest around 25 MW was imported from grid for its captive load. As both evacuating lines tripped, the captive island didn't survive. 420 MW generation loss and 445 MW load loss occurred at JSPL.	400 kV JSPL-Meeramundali-1 400 kV JSPL-Meeramundali-2 U#3,4,5,6 (135 MW) each at JSPL
5	GD-I	JSPL(CPP)	25.01.2025 06:49	25.01.2025 13:26	06:37	0	40	0.00%	0.19%	30173	21506	400KV-MEERAMUNDALI-JSPL-1 tripped at 06:49 Hrs due to 3 ph fault(Insulator decapping in B Phase of JSPL-Meramandalli-1). Ckt-2 was under breakdown condition. Both Bus at 400 kV JSPL became dead as it was radially connected to 400 kV Meramundali S/S. All units of JSPL under tripped condition and JSPL was imported 40 MW from grid. Total load loss of around 40 MW occurred.	400 kV JSPL-Meeramundali-1
6	GD-I	JSPL(CPP)	26.01.2025 06:06	26.01.2025 13:26	07:20	320	335	1.08%	1.74%	29633	19228	400KV-MEERAMUNDALI-JSPL-1 tripped at 06:06 Hrs due to R-ph Pilot insulator decapped at Loc No 97(Ckt-2 was under breakdown condition due to R-B Ph Insulator decapped at Loc No 96 from 05:31 Hrs). Both Bus at 400 kV JSPL became dead as it was radially connected to 400 kV Meramundali S/S. .Captive power plant JSPL has 6 units of 135 MW capacity each. Unit-1 with emergency load of 90 MW was separately connected with 220 kV Bus-1 (220 kV bus-coupler remaining open). Unit-2 of JSPL was under overhauling and other 4 units (unit-3,4,5,6) connected to 220 kV Bus-2 were generating around 320 MW and rest around 15 MW was imported from grid for its captive load. As both evacuating lines tripped, the captive island didn't survive. 320 MW generation loss and 335 MW load loss occurred at JSPL.	400 kV JSPL-Meeramundali-1 U#3,4,5,6 (135 MW) each at JSPL

Details of Grid Events during the Month of Dec 2024 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Napit and Niglok areas of Arunachal Pradesh Power System	07-01-2025 22:25	08-01-2025 13:12	14:47:00	0	5	0.00%	0.24%	1886	2061	Napit and Niglok areas of Arunachal Pradesh Power System were connected with rest of NER Grid via 132 kV Pasighat- Napit D/C Lines. At 22:25 Hrs of 07-01-2025, 132 kV Pasighat-Napit D/C Lines tripped. Due to tripping of these elements, Napit and Niglok areas of Arunachal Pradesh Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Napit and Niglok areas of Arunachal Pradesh Power System by charging 132 kV Pasighat-Napit line 1 at 13:12 Hrs of 08.01.2025	132 kV Pasighat- Napit D/C Lines
2	GD I	Daporijo area of Arunachal Pradesh Power System	13-01-2025 15:45	13-01-2025 17:27	01:42:00	0	3	0.00%	0.14%	2010	2090	Daporijo area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Daporijo-Basar line. 132 kV Ziro – Daporijo line tripped at 15:00 Hrs of 13-01-2025. At 15:45 Hrs of 13-01-2025, 132 kV Daporijo-Basar line tripped. Due to tripping of this element, Daporijo area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area Power supply was extended to Daporijo area of Arunachal Pradesh Power System by charging 132 kV Ziro – Daporijo line at 17:27 Hrs of 13-01-2025.	132 kV Daporijo-Basar line
3	GD I	Leshka HEP of Meghalaya Power System	20-01-2025 09:16	20-01-2025 09:36	00:20:00	62	0	2.71%	0.00%	2291	2267	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132kV Mynkre-Myntdu Leshka D/C lines At 09:16 Hrs of 20-01-2025, 132kV Mynkre-Myntdu Leshka D/C lines tripped. Due to tripping of these elements, Leshka HEP area of Meghalaya Power System was isolated due to loss of evacuation path. Also, during the same time Umiam stg1 Unit 1, Unit 2 and Unit 4 also tripped. Power supply was extended to Leshka HEP of Meghalaya Power System by charging 1132kV Mynkre-Myntdu Leshka 1 line at 09:36 Hrs of 20-01-2025.	132kV Mynkre-Myntdu Leshka D/C lines and Umiam stg1 Unit 1, Unit 2 and Unit 4 also tripped.
4	GD I	Along area of Arunachal Pradesh Power System	23-01-2025 18:36	23-01-2025 19:27	00:51:00	0	5	0.00%	0.18%	2914	2786	Along area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Basar & 132 kV Along-Pasighat lines At 18:36 Hrs of 23-01-2025, 132 kV Along-Pasighat and 132kV Along-Basar line tripped. Due to tripping of these elements, Along area of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in this area Power supply was extended to Along area of Arunachal Pradesh Power System by charging 132 kV Along-Pasighat line at 19:27 Hrs of 23-01-2025.	132 kV Along-Basar & 132 kV Along-Pasighat lines

21. NEW ELEMENTS CHARGED IN JANUARY 2025

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
NR	1	Bhadla_2(PG)	AMP Energy Green Four Private Limited	Solar	53.85	100	23.01.2025
	2	Fatehgarh_2	Adani Green Energy Twenty Four Limited	Solar	107	500	25.01.2025
	3	Bhadla_2(PG)	Kolayat Solar Power Plant NTPC Limited	Solar	18.32	550	31.01.2025
WR	4	400/33 kV Khavda PSS-9/ 765/400kV KPS-1	Adani Renewable Energy Fifty Six Limited (ARE56L)	Solar	50	50/400	29.01.2025
	5	400/33 kV Khavda PSS-13/ 765/400kV KPS-1	Adani Renewable Energy Fifty Seven Limited (ARE57L)	Solar	100	100/1200	24.01.2025
	6	400/33 kV Khavda PSS-13/ 765/400kV KPS-1	Adani Renewable Energy Forty One Limited (ARE41L)	Wind	52	52/124.8	24.01.2025
	7	400/33 kV Khavda PSS-3/ 765/400kV KPS-1	Adani Ports & Special Economic Zone (APSEZ)	Solar	7.5	200/200	22.01.2025
	8	400/33 kV RGESPL PSS-4/ 765/400kV Solapur PG	Renew Green MHS One Private Limited (RGMHSOPL)	Solar	100	100/281.5	21.01.2025
SR	9	230/33KV JSW DHARAPURAM PSS/ 400 kV Karur	JSW NEO Energy Ltd.	Wind	59.4	59.4	02.01.2025
	10	220/33KV RSPPL PSS GADAG /400 kV Koppal	Renew Surya Power Private Limited (RSRPL)	Wind	52.8	145.2	17.01.2025
	11	400/33KV AMGEPL Wind/ 400 kV Kurnool	AMGEPL Wind	Wind	131.67	270.27	08.01.2025
	12	400KV AMGEPL Solar /400 kV Kurnool	AMGEPL Solar	Solar	50	340	20.01.2025
	13	230/33KV RSRPL PSS KOPPAL	Renew Surya Roshini Private Limited (RSRPL)	Wind	3.465	300	30.01.2025
ER	14	JSWEUL-400 kV	JSW Energy (Utkal) Limited - UNIT 2 (350MW)	Unit-2/Coal	350	700	15.01.2025
				Total Coal Generation Addition	**350**		
				Total Solar Generation addition	**487**		
				Total Wind Generation addition	**299**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
NR	1	RRVPNL	Hindaun(RS)	ICT-3	400/220/33	500	15.01.2025
	2	UPPTCL	Noida Sec 123(UP)	ICT-3	400/132/33	200	23.01.2025
	3	UPPTCL	Sahupuri(UP)	ICT-1	400/220/33	500	29.01.2025
ER	4	Adani Green Energy Limited	400/33 kV Khavda PSS-13	ICT-1	400/33	330	20.01.2025
	5	Adani Green Energy Limited	400/33 kV Khavda PSS-13	ICT-2	400/33	330	20.01.2025
	6	Renew Green Energy Solutions Pvt Ltd	400/33 kV RGESPL PSS-4	ICT-1	400/33	100	20.01.2025
SR	7	Renew Green Energy Solutions Pvt Ltd	400/33 kV RGESPL PSS-4	ICT-2	400/33	125	20.01.2025
	8	WBPDCL	SAGARDIGHI	ST- 5	400/11	130	15.01.2025
					Total (MVA)	**2215**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
WR	1	Renew Green Energy Solutions Pvt Ltd	400 kV RGESPL PSS-4 - Solapur PG line	13.3	Twin HTLS	20.01.2025
	2	Adani Green Energy Limited	400 kV AGEL Khavda PSS-13 - KPS1 line	10.2	AL 59 Moose	20.01.2025
ER	3	OCPL	33KV-DARLIPALLI (NTPC)-MANOHARPUR-2 (Dedicated for Manoharpur mines(OCPL))	12.2	AAAC (11.7 km OH line +0.5 km U/G XLPE Cable)	06.01.2025
NER	4	MSPCL	132 kV Imphal - Ningthoukhong Ckt 2	32.5	ACSR Panther	21.01.2025
	5	MSPCL	132 kV Imphal - Ningthoukhong Ckt 3	32.5	ACSR Panther	21.01.2025.
			Total length (km)	**100.7**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
ER	1	Power Department , Govt. of Sikkim	220KV-TASHIDING- Legship -1	9.51	Single ZEBRA ACSR	01-01-2025

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
ER	1	LILO Portion -10.5 Km(BSPTCL)	400KV-BARH-BAKHTIYARPUR(BH)-1 {LILO of D/C 400 kV Patna(PG) - Barh at BAKHTIYARPUR(BH)}	51.04	QUAD MOOSE	31-01-2025
	2	LILO Portion -10.5 Km(BSPTCL)	400KV-PATNA-BAKHTIYARPUR(BH)-1 {LILO of D/C 400 kV Patna(PG) - Barh at BAKHTIYARPUR(BH)}	62.20	QUAD MOOSE	31-01-2025
	3	WBSETCL	400KV-ARAMBAGH-PPSP-2 {Reconfiguration of 400KV-PPSP-NEW PPSP-2 and 400KV-NEW PPSP-ARAMBAGH-2 as 400KV-PPSP-ARAMBAGH}	209	ACSR MOOSE	06-01-2025

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
WR	1	Kallam Transmission Limited	125 MVAR, 400 kV Bus Reactor-2 at Kallam PS, Maharashtra	400	125	01.01.2025
SR				**Total (MVAr)**	**125**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

Voltage Profile

विद्युत विभव रूपरेखा माह - जनवरी 2025 VOLTAGE PROFILE - January 2025

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगुल ANGUL	0%	100%	0%	0%	0	788	746	768
2		दालिपली DARLIPALI	0%	100%	0%	0%	0	787	761	775
3		गया GAYA	0%	100%	0%	0%	0	786	741	767
4		जीरत JEERAT	0%	100%	0%	0%	0	785	730	759
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	798	767	783
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	789	742	769
7		राची RANCHI	0%	100%	0%	0%	0	797	759	781
8		सासाराम SASARAM	0%	100%	0%	0%	0	792	739	763
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	0	800	748	779
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	800	745	778
3		अजमेर AJMER	0%	99%	1%	1%	9	806	754	784
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	801	742	777
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	790	758	773
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	788	756	771
7		अंता ANTA	0%	100%	0%	0%	0	795	755	779
8		बलिया BALLIA	0%	100%	0%	0%	0	790	738	769
9		बारा BARA	0%	100%	0%	0%	0	784	754	769
10		भाडला BHADLA	0%	100%	0%	0%	0	796	756	778
11		भाडला-2 BHADLA-2	0%	100%	0%	0%	0	801	748	782
12		भिवानी BHIWANI	0%	99%	1%	1%	10	806	754	784
13		बीकानेर BIKANER	0%	100%	0%	0%	0	801	751	782
14		बरेली BAREILLY	0%	99%	1%	1%	6	807	744	779
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	8	805	749	783
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	799	756	778
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	792	740	768
18		घाटमपुर GHATAMPUR	0%	100%	0%	0%	2	811	725	772
19		ग्रेटर नोएडा GREATER NOIDA	0%	98%	2%	2%	12	806	749	783
20		हापुड़ HAPUR	0%	100%	0%	0%	2	805	738	778
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	795	735	770
22		झाटिकरा JHATIKARA	0%	100%	0%	0%	1	802	747	779
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	793	742	772
24		खेतरी KHETRI	0%	99%	1%	1%	6	806	753	783
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	2	803	732	771
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	779	741	762
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	797	737	773
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	793	731	767
29		मेरठ MEERUT	0%	99%	1%	1%	10	808	747	781
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	1	802	743	778
31		मोगा MOGA	0%	100%	0%	0%	1	804	739	776
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	783	752	767
33		उरई ORAI	0%	94%	6%	6%	43	807	753	785
34		फागी PHAGI	0%	100%	0%	0%	1	802	735	782
35		रामपुर RAMPUR	0%	87%	10%	10%	74	809	744	785
36		उन्नाव UNNAO	0%	100%	0%	0%	0	791	733	768
37		वाराणसी VARANASI	0%	100%	0%	0%	0	789	754	772
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	794	746	774
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	799	743	774
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	799	744	771
4		भुज BHUJ	0%	100%	0%	0%	0	796	737	774
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	791	742	771
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	782	750	765
7		बीना BINA	0%	100%	0%	0%	1	801	746	779
8		बनसकठा BANASKANTHA	0%	97%	3%	3%	20	808	741	783
9		चापा CHAMPA	0%	97%	3%	3%	19	807	761	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	798	747	775
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	786	755	769
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	790	760	776
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	794	739	770
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	3	802	761	782
15		ग्वालियर GWALIOR	0%	99%	1%	1%	6	803	749	782
16		इंदौर INDORE	0%	100%	0%	0%	0	793	740	771
17		जबलपुर JABALPUR	0%	97%	3%	3%	19	805	757	784
18		खंडवा KHANDWA	0%	100%	0%	0%	0	795	746	773
19		कोरडी KORADI	0%	100%	0%	0%	0	784	748	768
20		लकाडिया LAKADIYA	0%	99%	1%	1%	4	805	748	782
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	795	768	781
22		पड़घे PADGHE	0%	100%	0%	0%	0	802	741	778
23		परली PARLI	0%	100%	0%	0%	0	799	754	781
24		पुणे PUNE	0%	100%	0%	0%	3	802	743	781
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	0	801	762	782
26		सासन SASAN	0%	100%	0%	0%	0	793	759	777
27		सतना SATNA	0%	99%	1%	1%	7	801	757	783
28		सिवनी SEONI	0%	100%	0%	0%	0	796	749	775
29		सीपत SIPAT	0%	100%	0%	0%	0	782	751	766
30		सोलापुर SOLAPUR	0%	100%	0%	0%	0	801	753	781
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	779	749	764
32		तामनार TAMNAR	0%	100%	0%	0%	0	793	767	780
33		वड़ोदरा VADODARA	0%	99%	1%	1%	7	806	741	780
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	796	762	780
35		वर्धा WARDHA	0%	100%	0%	0%	0	799	750	778
36		वरोरा WARORA	0%	100%	0%	0%	0	799	754	780
1	दक्षिणी क्षेत्र SR	अरियलूर ARIYALUR	0%	99%	1%	1%	8	805	752	783
2		कड़पा CUDDAPAH	0%	99%	1%	1%	5	810	758	784
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	99%	1%	1%	6	808	742	777
4		कर्नूल KURNOOL	0%	100%	0%	0%	0	794	746	773
5		महेश्वरम MAHESWARAM	0%	100%	0%	0%	3	806	751	780
6		निज़ामाबाद NIZAMABAD	0%	97%	3%	3%	24	809	752	783
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	795	748	773
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	0	797	734	769
9		रायचूर RAICHUR	0%	100%	0%	0%	0	797	748	776
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	0	799	742	775
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	793	744	771
12		वेमगिरी VEMAGIRI	0%	97%	3%	3%	23	808	744	779
13		वारंगल WARANGAL	0%	100%	0%	0%	0	796	741	768
1	पूर्वोत्तर क्षेत्र NER	बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	415	394	404
2		बिस्वनाथ चरिआलि BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	416	393	404
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	417	399	408
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	419	400	409
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	416	396	407
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	414	392	404
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	414	392	404
8		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	413	402	408
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	413	392	404
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	415	396	407
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	418	394	408
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	414	396	407
13		पबंकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	413	392	402
14		रंगानदी RANGANADI (400 kV)	0%	100%	0%	0%	0	415	393	404
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	418	400	409
16		सुर्ज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	412	392	402
17		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	412	394	404

All listed stations are 765 kV stations unless otherwise mentione
***Percentage is calculated w.r.t. Time of one month**

23.ALL TIME HIGHEST

31/01/2025

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19/06/2024	82312 23/07/2024	1990 18/06/2024	443 01/08/2023	86 07/08/2023	188 25/01/2025
WR	79919 29/01/2025	67482 30/05/2024	1648 06/05/2024	167 18/12/2014	310 28/05/2024	119.43 26/01/2025
SR	68735 13/03/2024	54798 29/04/2024	1416 05/04/2024	208 31/08/2018	323 26/07/2024	149.3 26/01/2025
ER	32531 10/06/2024	29695 29/05/2024	692 10/06/2024	157 14/09/2022	-	4 09/06/2024
NER	3905 19/09/2024	3787 19/09/2024	80 20/09/2024	43 27/06/2024	-	2 22/06/2022
All India	250070 30/05/2024	227354 29/05/2024	5466 30/05/2024	877 30/08/2022	619 28/05/2024	461 26/01/2025

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29/06/2024	366.8	21/07/2024
	Haryana	14524	31/07/2024	293.4	19/06/2024
	Rajasthan	18572	28/01/2025	379.1	30/05/2024
	Delhi	8568	18/06/2024	177.7	18/06/2024
	UP	30032	13/06/2024	658.8	17/06/2024
	Uttarakhand	2863	14/06/2024	62.1	14/06/2024
	HP	2273	17/01/2025	41.3	20/12/2024
	J&K(UT) and Ladakh(UT)	3200	07/01/2025	69.3	10/01/2025
	Chandigarh	443	13/06/2024	9.1	18/06/2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6347	05/04/2024	144.4	06/04/2024
	Gujarat	25502	07/06/2024	514.2	07/06/2024
	MP	18888	20/12/2024	349.3	20/12/2024
	Maharashtra	29826	30/01/2025	648.3	30/04/2024
	Goa	803	19/04/2024	17.6	18/05/2024
	DD & DNH	1390	23/10/2024	32.6	16/10/2024
	AMNSIL	1083	10/01/2024	21.0	31/05/2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04/05/2024	263.8	16/06/2023
	Telangana*	15623	08/03/2024	311.0	13/03/2024
	Karnataka	17691	31/01/2025	336.9	05/04/2024
	Kerala	5797	02/05/2024	116.1	03/05/2024
	Tamil Nadu	20830	02/05/2024	443.6	30/04/2024
	Pondy	530	31/05/2024	11.8	31/05/2024
ER	Bihar	8001	23/09/2024	172.8	30/07/2024
	DVC	3674	14/06/2024	81.2	22/04/2022
	Jharkhand	2351	09/07/2024	50.4	10/06/2024
	Odisha	7104	13/07/2023	148.5	19/04/2024
	West Bengal	12756	30/04/2024	264.0	30/04/2024
	Sikkim	137	03/02/2022	2.5	28/01/2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26/05/2024	3.9	18/06/2024
	Assam	2687	20/09/2024	55.8	20/09/2024
	Manipur	271	16/01/2025	4.2	10/01/2025
	Meghalaya	415	09/02/2022	7.8	31/01/2022
	Mizoram	162	27/01/2024	2.6	02/03/2024
	Nagaland	188	22/07/2024	3.4	29/07/2024
	Tripura	386	04/05/2024	7.3	02/06/2024
*SR	Andhra Pradesh (Undivided)	13162	23/03/2014	284.8	22/03/2014

Note: DVC has reported revised maximum demand met.

24. System Reliability Indices Report for the month of January 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	2	0.50	0.07

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
