ग्रिड-इंडिया
GRID-INDIA

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 40234672

संदर्भ संख्या:- **GRID-INDIA/NLDC/MR/**

दिनांक: **24.04.2025**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **मार्च 2025**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **मार्च 2025** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
मुख्य महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033

10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly Operation Report



मार्च 2025

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह मार्च 2025 के लिए प्रचालन निष्पादन रिपोर्ट


OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF MARCH -2025

पृष्ठसूची **CONTENTS**


1	माह मार्च 2025 की सारांश रिपोर्ट Summary of report for the month of MARCH 2025	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति Evening Peak Hour Demand Met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	11 मार्च के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 11-MARCH (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह मार्च 2024 से तुलना Energy requirement and met comparison with MARCH 2024	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह मार्च 2024 से तुलना Peak demand requirement and met comparison with MARCH 2024	25

14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक)एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-45
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	46-48
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	49-57
21	नए चार्ज किये गए तत्व New elements Charged	58 - 59
22	विभव रूपरेखा Voltage profile	60
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह मार्च 2025 तक All Time Highest (Demand & Energy) figures: Till MARCH 2025	61
24	मार्च 2025 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for MARCH 2025	62


1. SUMMARY OF REPORT FOR THE MONTH OF MARCH-2025

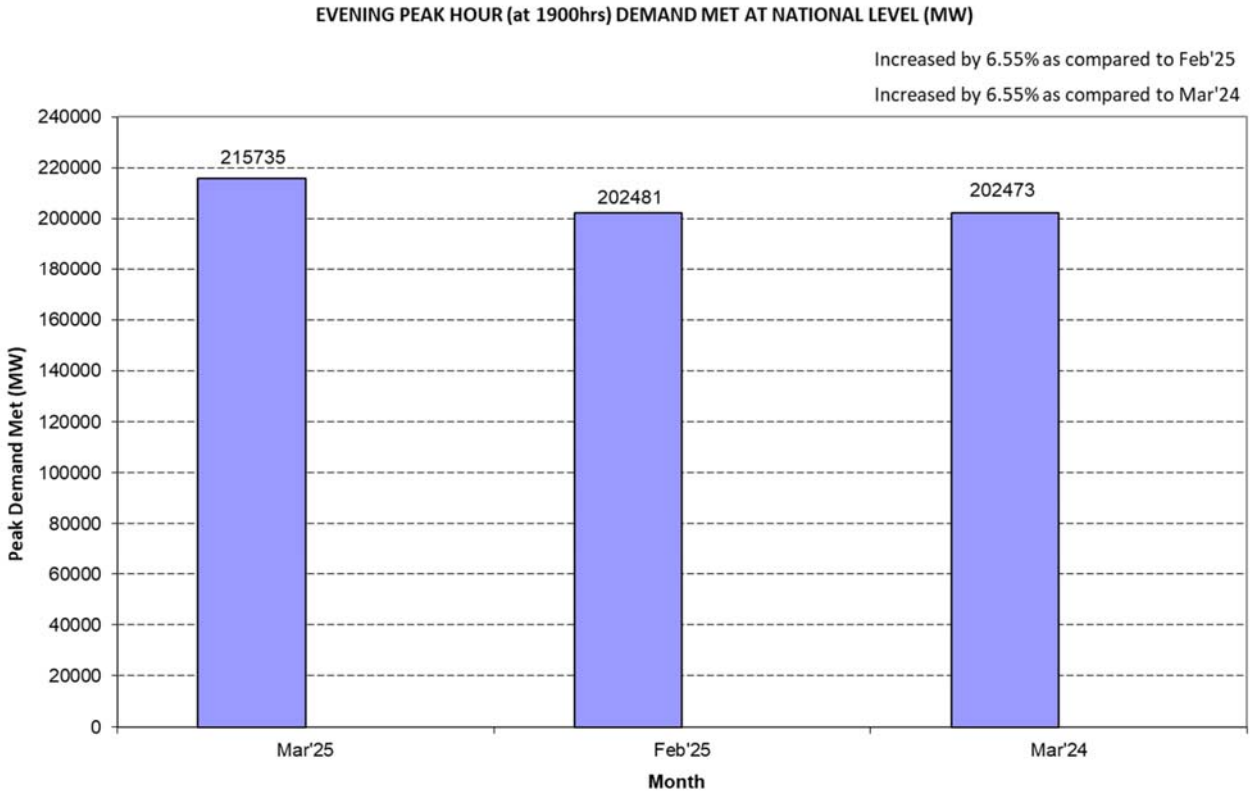


*Source: As per daily data furnished by states

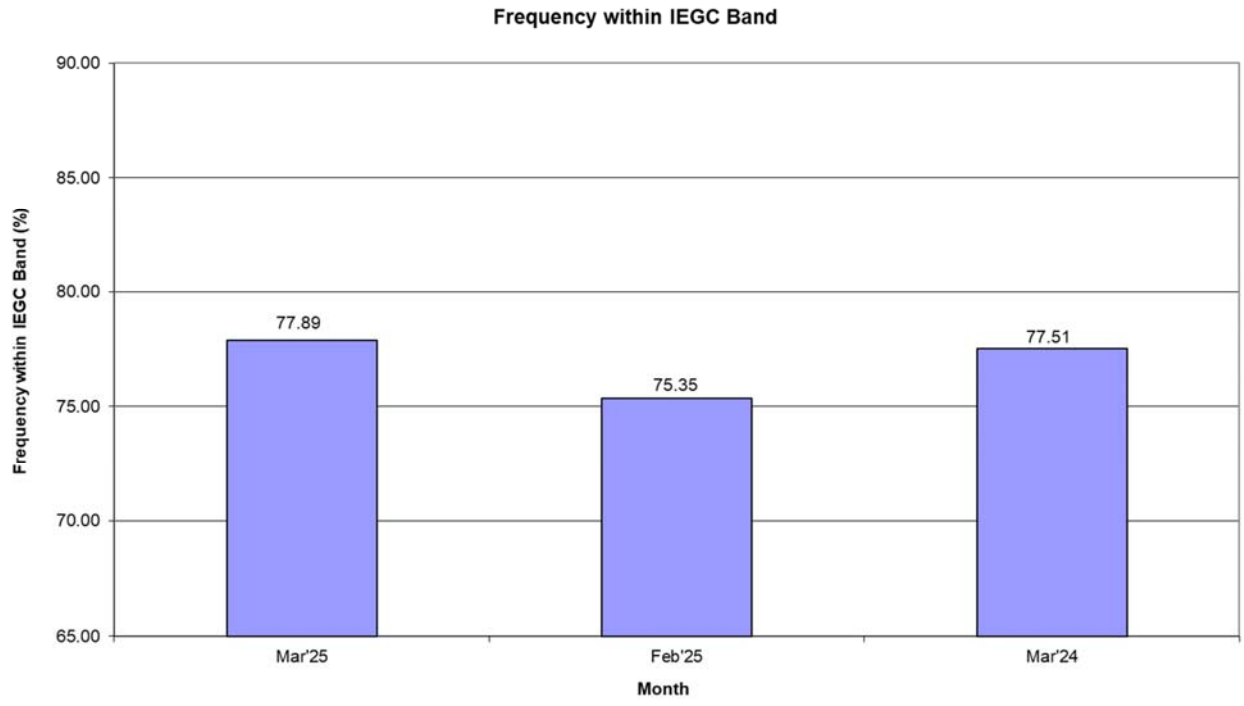


ENERGY MET AT NATIONAL LEVEL (MU)

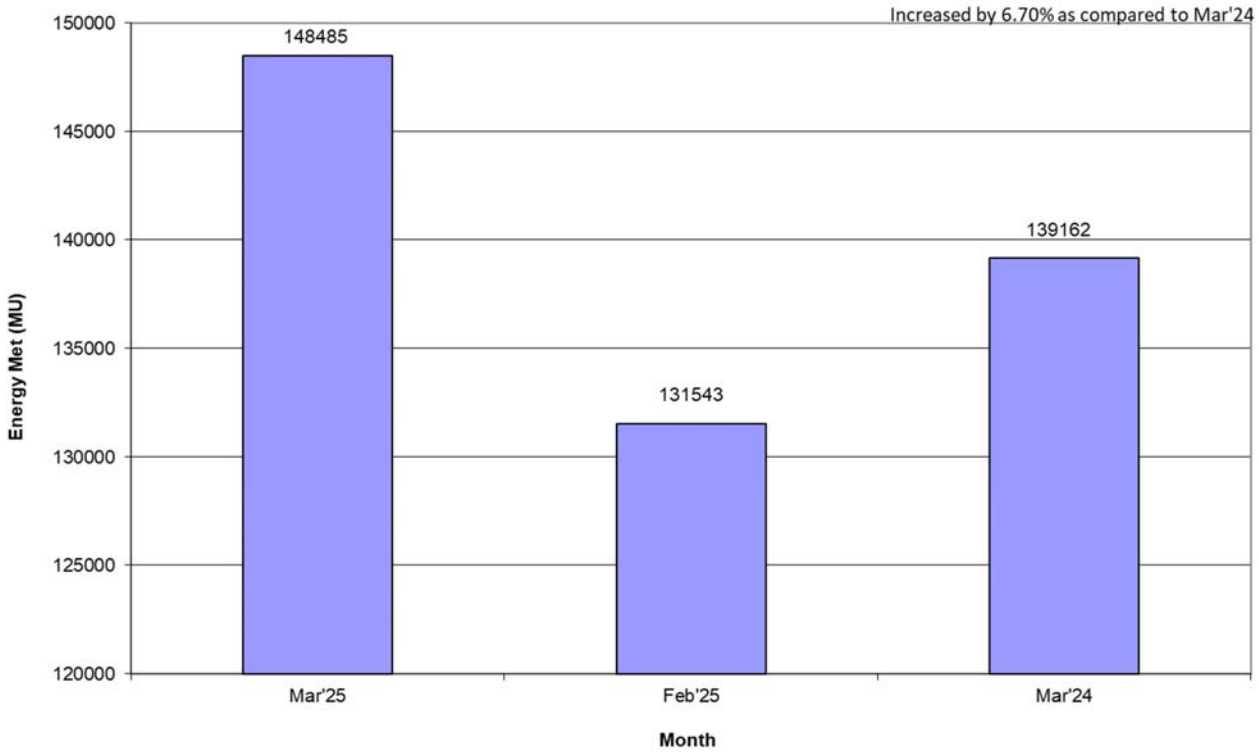


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

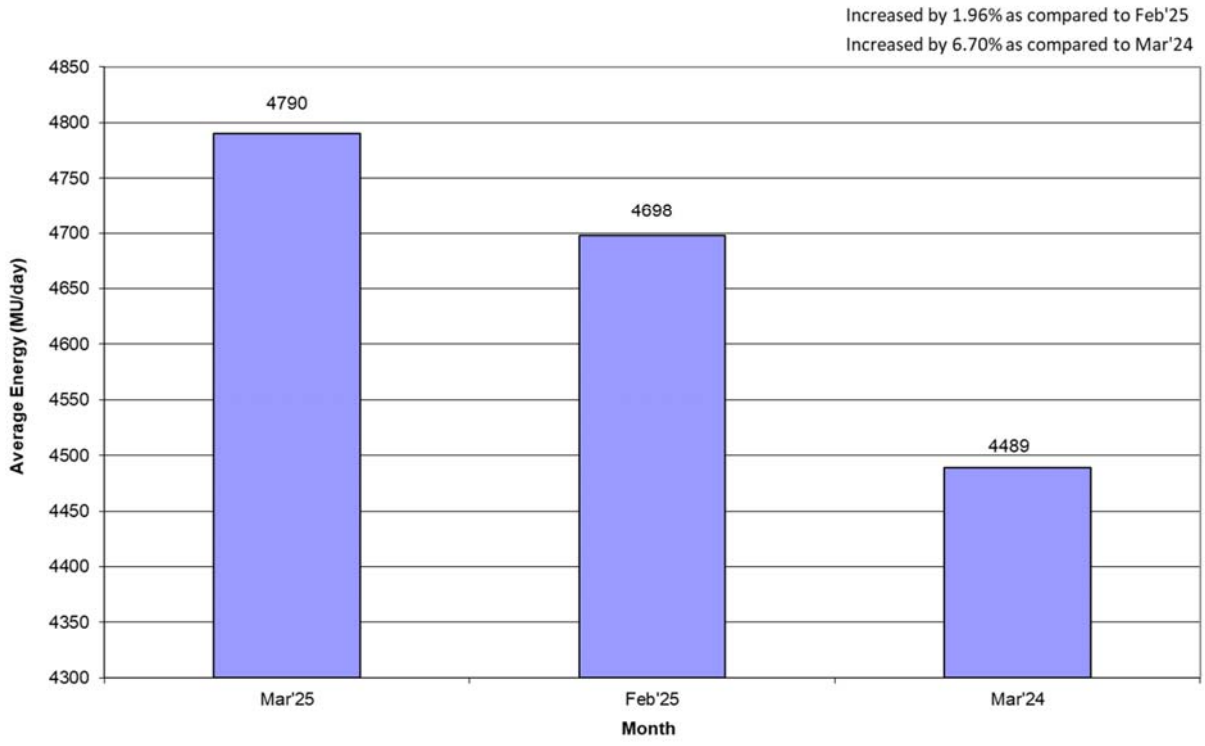


HYDRO GENERATION AT NATIONAL LEVEL (MU)

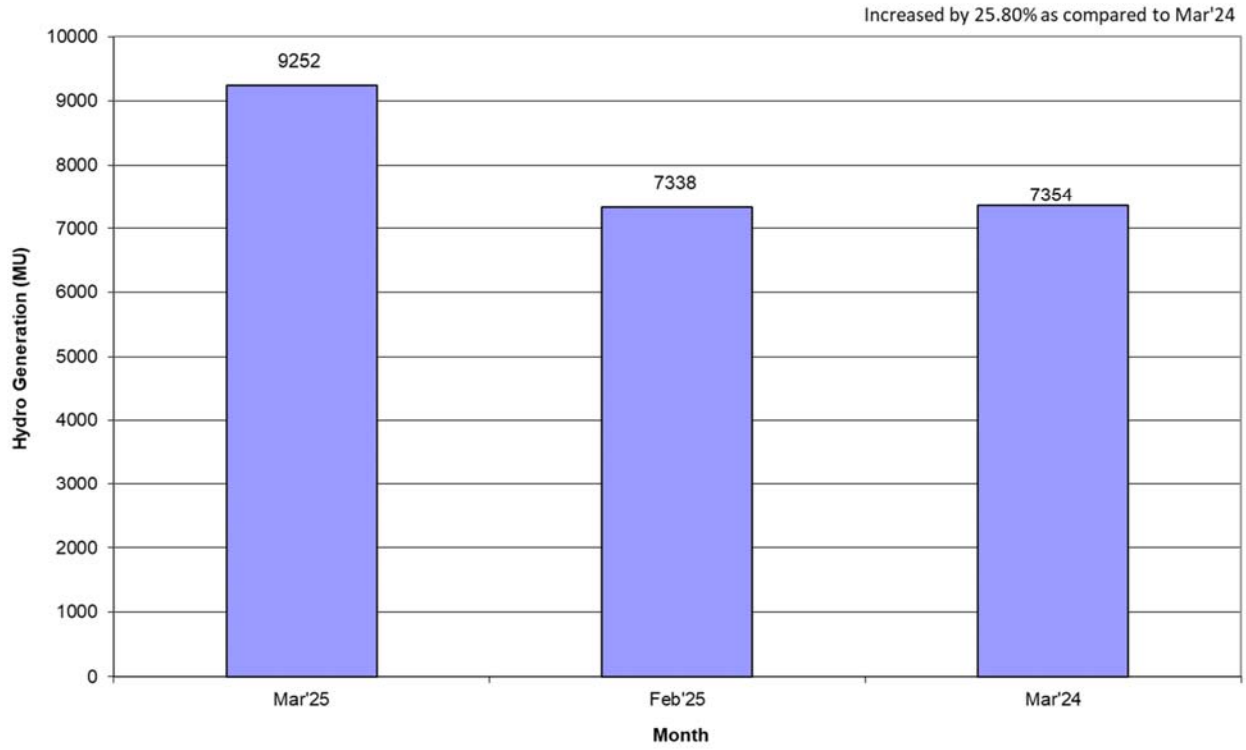


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

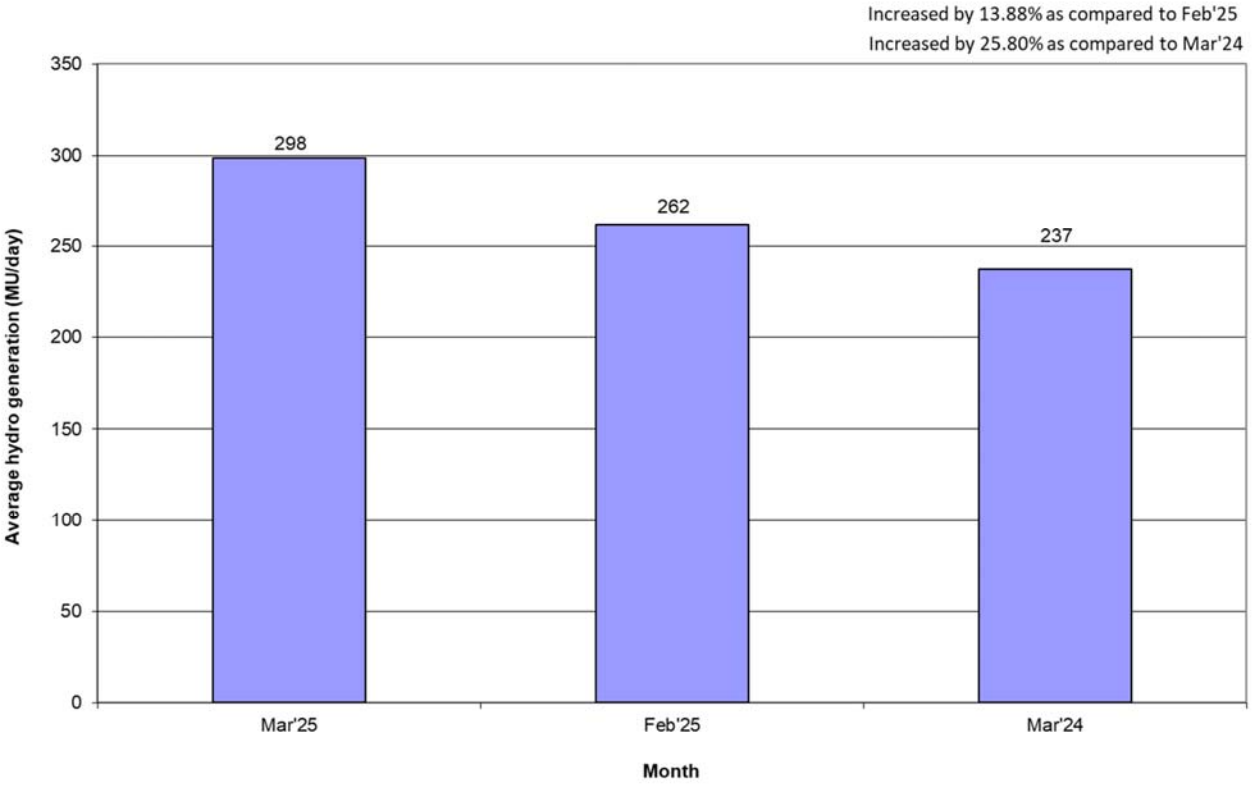


WIND GENERATION AT NATIONAL LEVEL (MU)

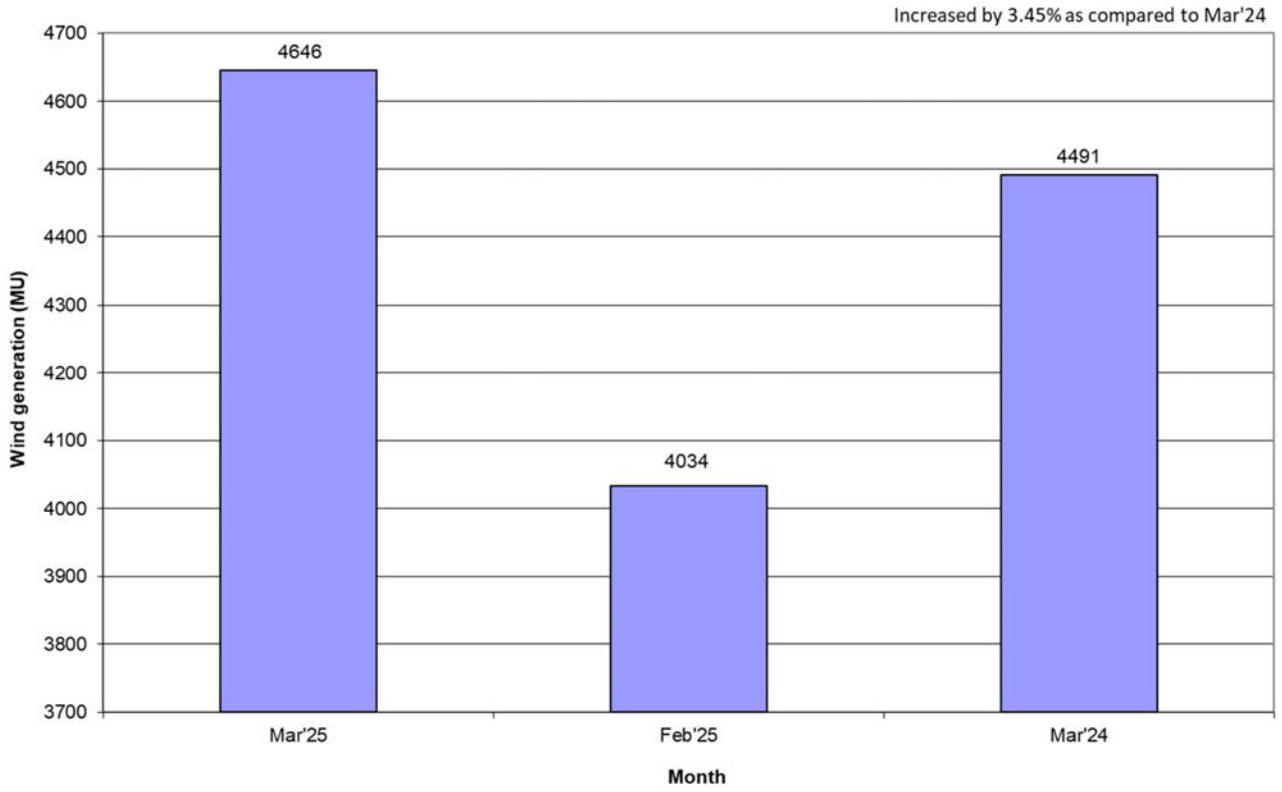


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

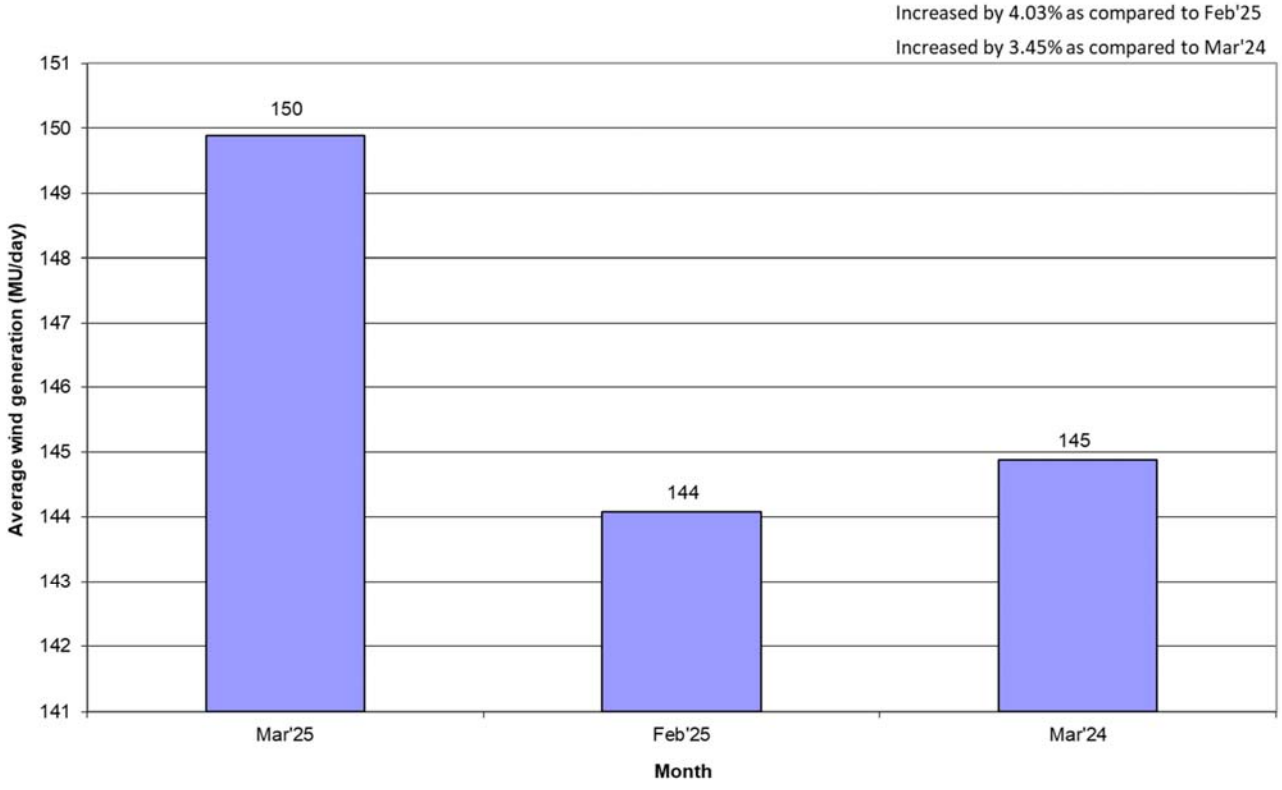

SOLAR GENERATION AT NATIONAL LEVEL (MU)

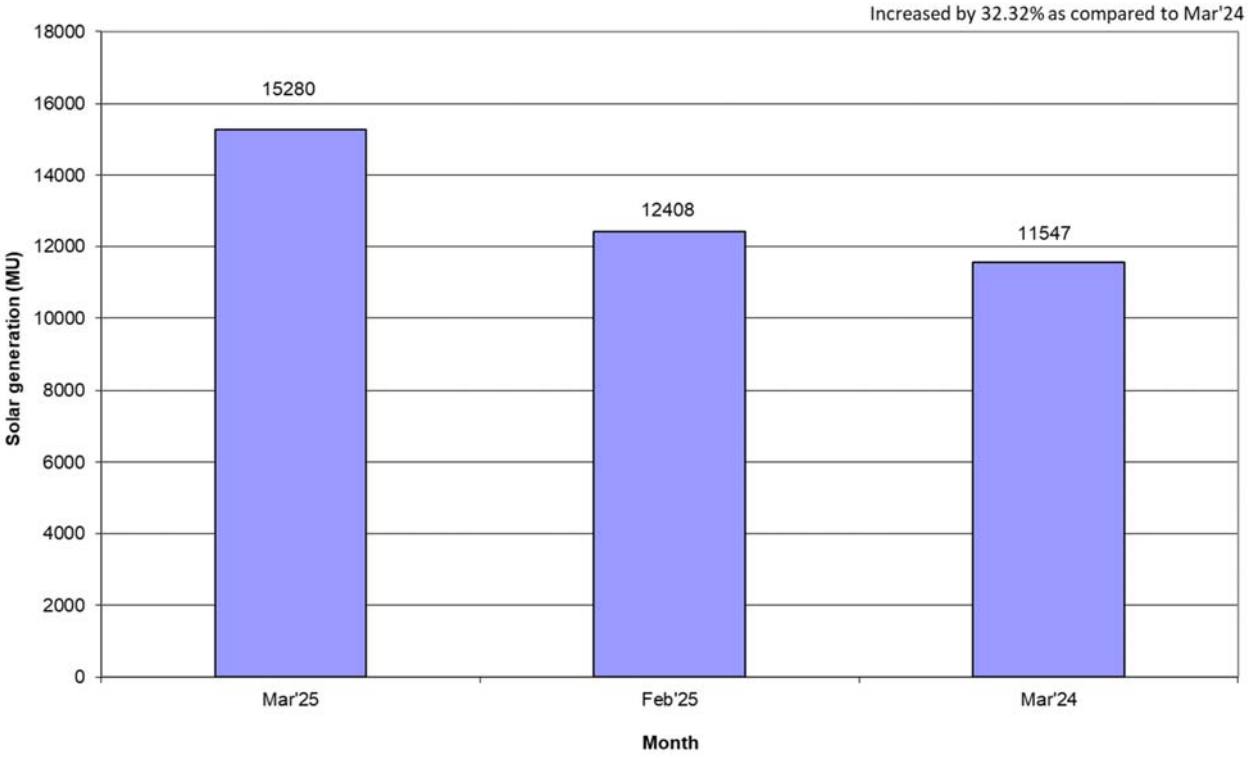

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

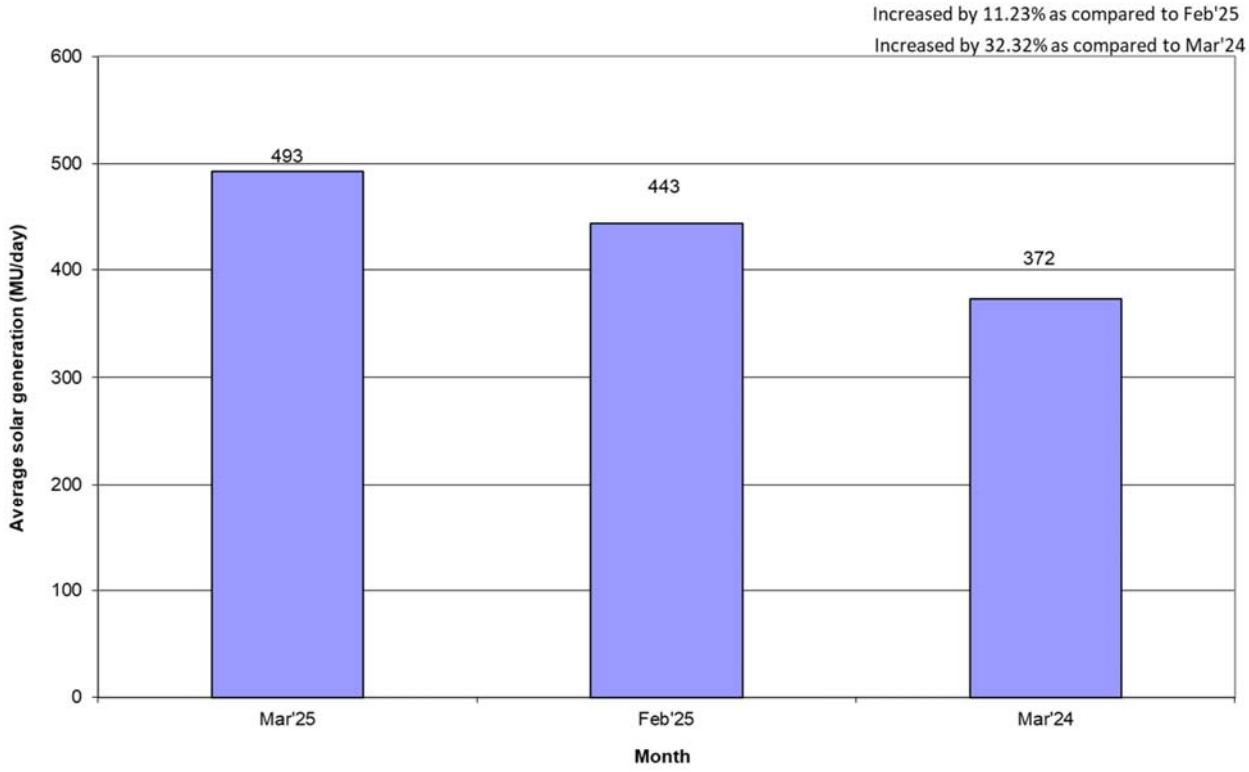

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.03.2025
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	59298	1580	5995	0	66873	1620	21426	47057	136975
2	WR	75323	1400	10151	0	86874	3240	7593	61169	158876
3	SR	50456	3640	6642	434	61171	3320	11927	61072	137490
4	ER	28875	0	80	0	28955	0	4838	2401	36194
5	NER	1242	0	1665	36	2943	0	1944	629	5516
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	215193	6620	24533	589	246935	8180	47728	172368	475212

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति

EVENING PEAK HOUR (at 19:00hrs) DEMAND MET AT NATIONAL LEVEL


माह: मार्च 2025 MONTH:- MAR 2025

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Mar-25	52669	69565	50493	23875	2642	199244
2-Mar-25	51154	66732	47390	24084	2499	191859
3-Mar-25	53937	69134	52214	24500	2655	202440
4-Mar-25	54614	70934	52980	25345	2714	206587
5-Mar-25	54198	70573	53180	24504	2688	205143
6-Mar-25	54785	68695	52868	23392	2689	202429
7-Mar-25	56932	69556	52758	23508	2673	205427
8-Mar-25	56448	70077	52130	23834	2711	205200
9-Mar-25	55222	68190	47886	23991	2576	197865
10-Mar-25	57168	71178	52133	24949	2691	208119
11-Mar-25	58170	71512	49690	24614	2741	206727
12-Mar-25	57510	70726	49664	25789	2618	206307
13-Mar-25	51167	67768	52618	26110	2700	200363
14-Mar-25	41411	56696	49317	23332	2540	173296
15-Mar-25	50245	67177	51547	24676	2613	196258
16-Mar-25	51822	66941	48617	24097	2620	194097
17-Mar-25	54568	70722	53194	25888	2728	207100
18-Mar-25	55146	70729	54478	26070	2765	209188
19-Mar-25	56494	69580	54510	26302	2893	209779
20-Mar-25	56113	69803	54383	24191	2821	207311
21-Mar-25	56914	69014	54134	22954	2752	205768
22-Mar-25	55154	69209	51082	22499	2786	200730
23-Mar-25	53685	67034	48744	22458	2576	194497
24-Mar-25	57414	70648	53978	24664	2877	209581
25-Mar-25	60489	71044	53335	25440	2969	213277
26-Mar-25	60293	70295	53698	26400	2983	213669
27-Mar-25	59555	71104	55344	26770	2962	215735
28-Mar-25	57298	70452	55925	27349	3137	214161
29-Mar-25	55210	70062	54885	27213	3100	210470
30-Mar-25	52772	66057	49956	26138	2915	197838
31-Mar-25	54214	67817	51239	26685	3029	202984
उच्चतम MAXIMUM	60489	71512	55925	27349	3137	215735
निम्नतम MINIMUM	41411	56696	47390	22458	2499	173296
औसत AVERAGE	54928	69001	52076	24891	2763	203660
अब तक का उच्चतम All Time Max.	82312	**71512**	**55925**	29695	3787	227354
दिनांक Date	23.07.24	**11.03.25**	**28.03.25**	29.05.24	19.09.24	29.05.24

Source: As per daily data furnished by states

EVENING PEAK HOUR DEMAND(at 1900hrs) MET DURING THE MONTH OF MARCH' 2025

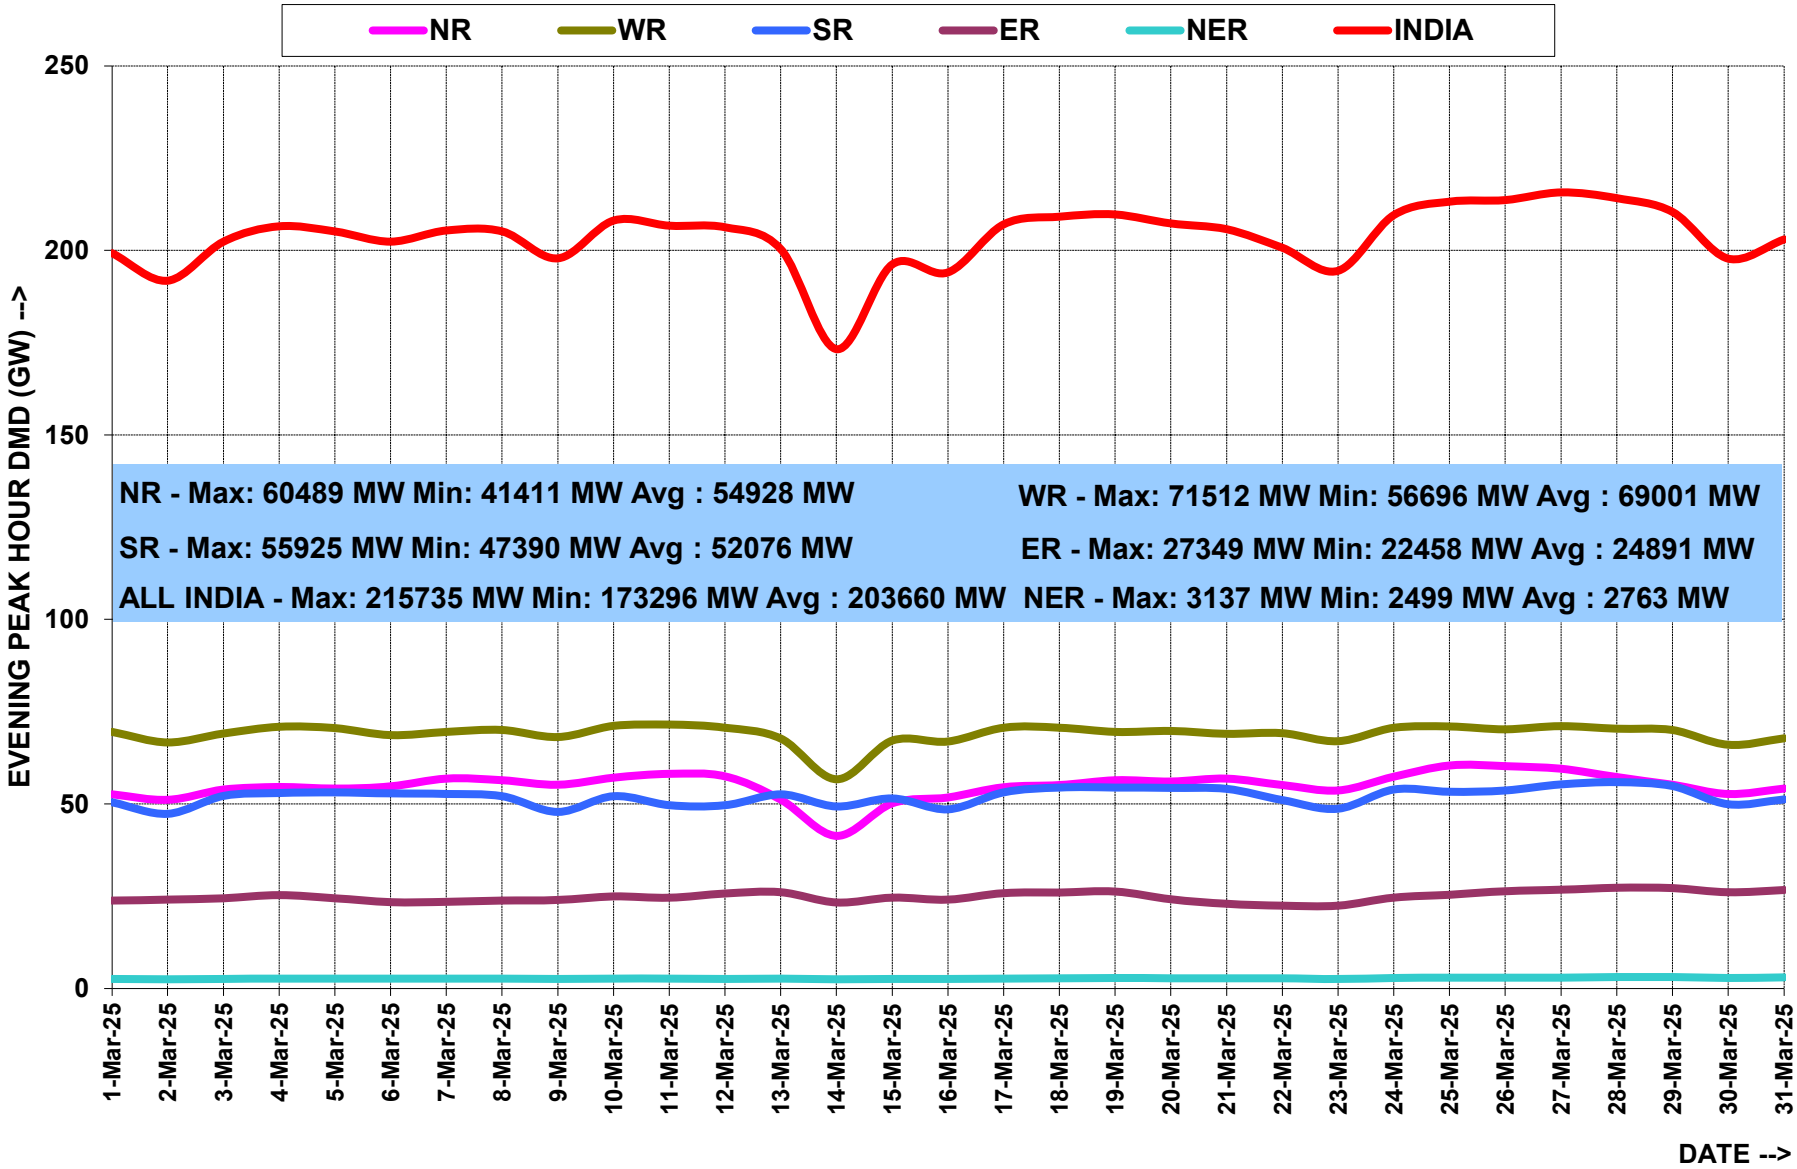


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: मार्च 2025 MONTH:- MAR 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-25	1135	1652	1367	497	49	4701
02-Mar-25	1101	1610	1302	503	44	4559
03-Mar-25	1163	1644	1379	519	49	4754
04-Mar-25	1177	1653	1417	527	50	4824
05-Mar-25	1129	1622	1428	510	50	4739
06-Mar-25	1177	1611	1420	494	51	4751
07-Mar-25	1257	1628	1431	487	51	4854
08-Mar-25	1280	1640	1414	499	50	4883
09-Mar-25	1252	1618	1341	507	48	4766
10-Mar-25	1277	1672	1380	527	49	4906
11-Mar-25	1300	1690	1372	529	52	4943
12-Mar-25	1293	1644	1351	537	50	4875
13-Mar-25	1250	1659	1365	555	47	4876
14-Mar-25	1045	1435	1352	521	46	4399
15-Mar-25	1017	1535	1359	532	46	4489
16-Mar-25	1106	1590	1328	536	47	4607
17-Mar-25	1192	1645	1416	546	49	4847
18-Mar-25	1212	1644	1451	549	48	4904
19-Mar-25	1239	1640	1460	561	54	4953
20-Mar-25	1227	1631	1456	538	53	4905
21-Mar-25	1231	1616	1457	499	53	4857
22-Mar-25	1203	1606	1386	460	52	4707
23-Mar-25	1150	1581	1297	457	49	4535
24-Mar-25	1206	1640	1383	503	52	4784
25-Mar-25	1219	1662	1410	532	54	4876
26-Mar-25	1245	1657	1416	553	55	4927
27-Mar-25	1241	1665	1438	572	57	4973
28-Mar-25	1204	1647	1458	595	59	4963
29-Mar-25	1127	1627	1452	598	58	4863
30-Mar-25	1089	1591	1374	583	58	4694
31-Mar-25	1130	1613	1376	595	57	4771
कुल TOTAL	36874	50364	43237	16421	1589	148485
उच्चतम MAXIMUM	1300	1690	1460	598	59	4973
निम्नतम MINIMUM	1017	1435	1297	457	44	4399
औसत AVERAGE	1189	1625	1395	530	51	4790
संचयी 2024-25 Cumulative 2024-25	518034	538495	426300	198623	20581	1702034
अब तक का उच्चतम All Time Max.	1990	**1690**	**1460**	692	80	5466
दिनांक Date	18.06.24	**11.03.25**	**19.03.25**	10.06.24	20.09.24	30.05.24

ENERGY MET DURING THE MONTH OF MARCH' 2025

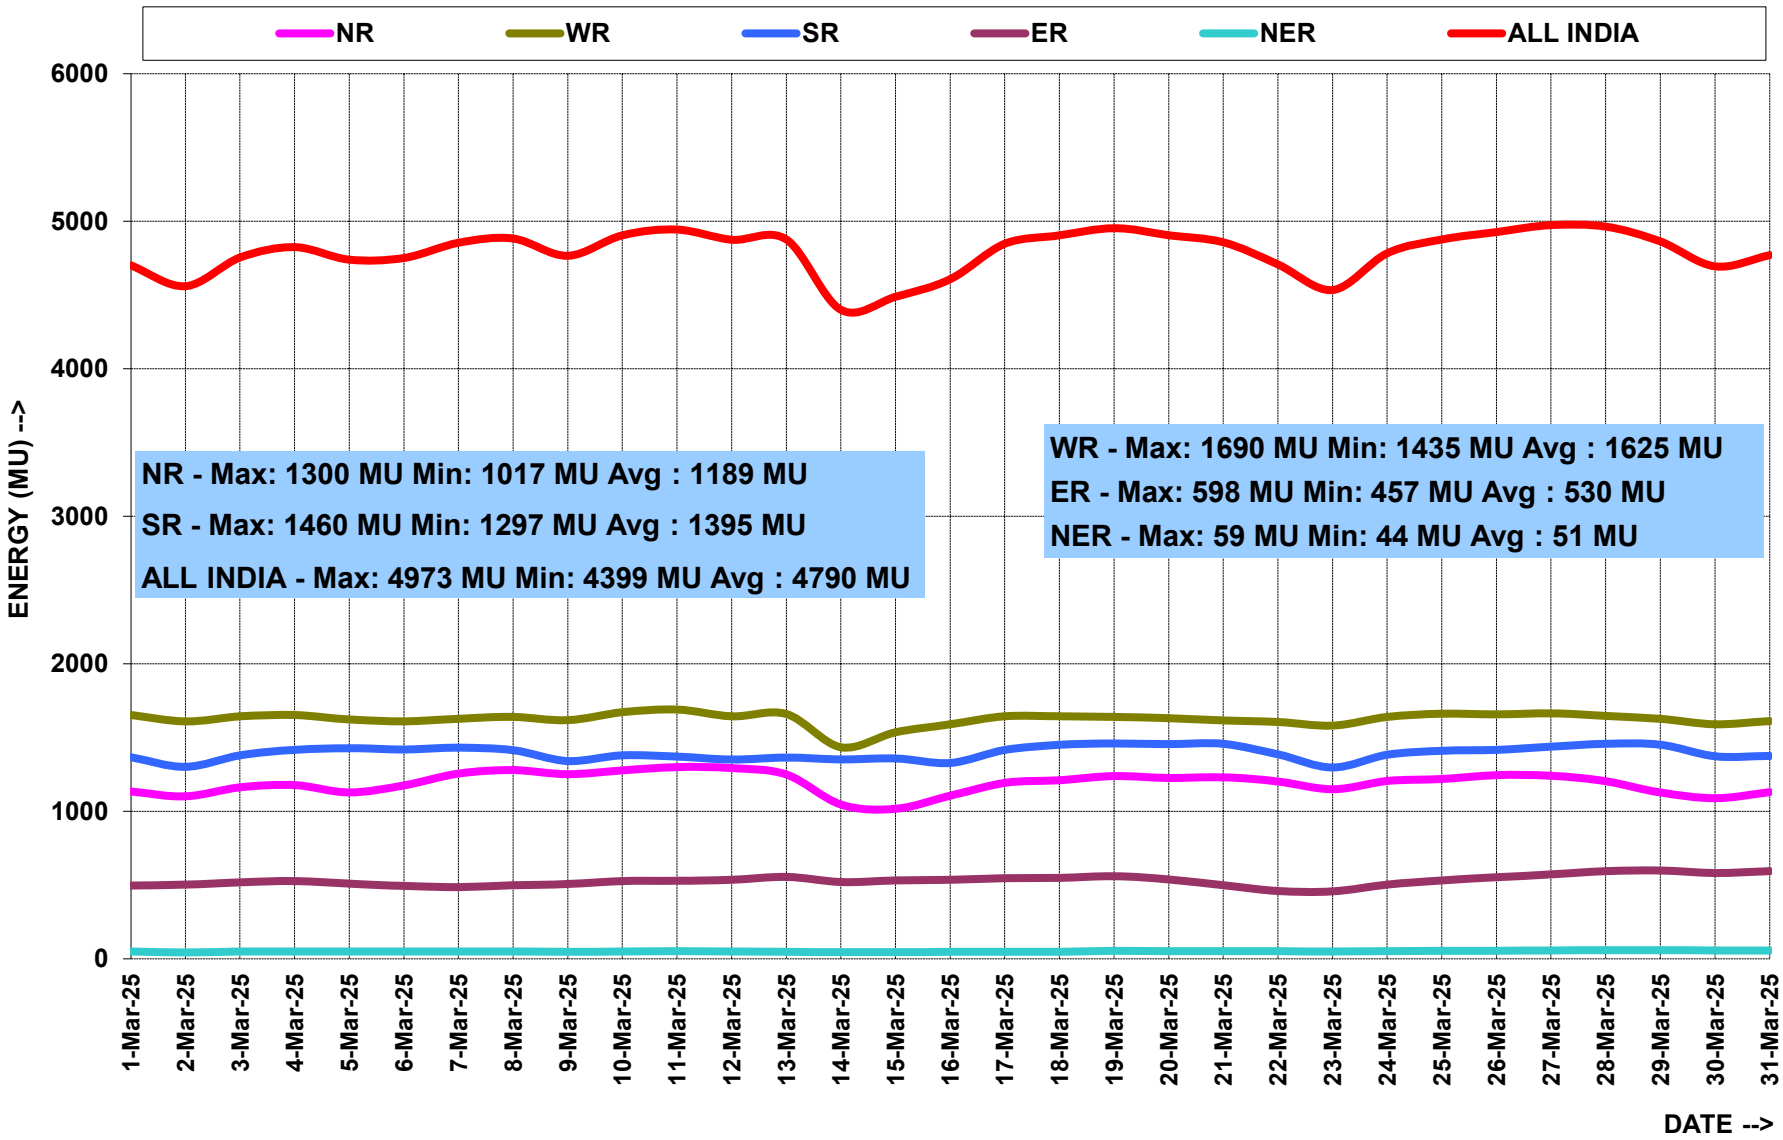

5. वर्ष 2024-25 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2024-25

राष्ट्रीय ग्रिड NATIONAL GRID									
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-24	All India Grid	5.25	78.56	16.19		50.43	49.55	50.00
	May-24	All India Grid	2.49	80.04	17.47		50.46	49.72	50.01
	Jun-24	All India Grid	4.50	79.18	16.32		50.67	49.63	50.00
	Jul-24	All India Grid	6.41	78.42	15.17		50.37	49.64	50.00
	Aug-24	All India Grid	4.66	75.01	20.33		50.45	49.56	50.01
	Sep-24	All India Grid	6.09	77.13	16.78		50.38	49.46	50.00
	Oct-24	All India Grid	4.86	80.27	14.87		50.39	49.58	50.00
	Nov-24	All India Grid	5.15	80.80	14.05		50.32	49.55	50.00
	Dec-24	All India Grid	5.58	76.45	17.97		50.42	49.49	50.00
	Jan-25	All India Grid	5.23	76.05	18.72		50.31	49.60	50.00
	Feb-25	All India Grid	6.24	75.35	18.41		50.33	49.55	50.00
	Mar-25	All India Grid	5.32	77.89	16.79		50.46	49.62	50.00
	2024-25 (upto Mar)	**All India Grid**	**5.14**	**77.94**	**16.92**		**50.67**	**49.46**	**50.00**

5.1 मार्च 2025 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR MARCH 2025

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05		उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Mar-25	6.76	75.20	18.04		50.22	49.75	50.00	0.04
	02-Mar-25	3.34	79.50	17.15		50.26	49.85	50.00	0.03
	03-Mar-25	16.16	72.19	11.66		50.28	49.68	49.98	0.06
	04-Mar-25	3.31	68.00	28.69		50.25	49.71	50.02	0.04
	05-Mar-25	3.94	72.63	23.44		50.46	49.69	50.02	0.08
	06-Mar-25	4.72	78.07	17.21		50.23	49.65	50.00	0.04
	07-Mar-25	4.22	76.66	19.12		50.32	49.72	50.01	0.04
	08-Mar-25	6.77	78.68	14.55		50.23	49.70	49.99	0.04
	09-Mar-25	6.18	81.68	12.14		50.40	49.72	49.99	0.04
	10-Mar-25	5.63	69.93	24.44		50.30	49.79	50.01	0.05
	11-Mar-25	7.62	74.79	17.59		50.17	49.69	50.00	0.04
	12-Mar-25	5.31	72.51	22.18		50.26	49.64	50.01	0.04
	13-Mar-25	4.90	74.47	20.64		50.29	49.73	50.00	0.04
	14-Mar-25	6.19	71.28	22.52		50.42	49.74	50.01	0.06
	15-Mar-25	7.12	76.71	16.17		50.22	49.69	50.00	0.04
	16-Mar-25	5.64	79.43	14.93		50.24	49.78	50.00	0.03
	17-Mar-25	4.28	79.41	16.31		50.21	49.82	50.00	0.03
	18-Mar-25	3.62	79.06	17.31		50.23	49.74	50.00	0.03
	19-Mar-25	6.69	82.89	10.42		50.28	49.77	49.99	0.03
	20-Mar-25	8.32	80.10	11.57		50.20	49.65	49.99	0.04
	21-Mar-25	4.34	82.66	13.00		50.19	49.78	49.99	0.03
	22-Mar-25	5.93	76.33	17.74		50.29	49.63	50.00	0.05
	23-Mar-25	0.82	85.53	13.65		50.22	49.87	50.00	0.02
	24-Mar-25	4.43	81.69	13.88		50.26	49.77	50.00	0.03
	25-Mar-25	3.24	83.70	13.06		50.22	49.78	50.00	0.02
	26-Mar-25	2.85	86.42	10.73		50.28	49.82	50.00	0.02
	27-Mar-25	4.91	82.06	13.03		50.19	49.78	50.00	0.03
	28-Mar-25	3.31	81.31	15.38		50.29	49.79	50.01	0.03
	29-Mar-25	4.29	73.31	22.40		50.30	49.70	50.01	0.05
	30-Mar-25	5.28	77.06	17.66		50.31	49.62	50.00	0.05
	31-Mar-25	4.77	81.40	13.83		50.26	49.76	50.00	0.03


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: मार्च 2025 MONTH:- MAR 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-25	146	53	95	24	8	327
02-Mar-25	124	44	75	20	7	271
03-Mar-25	120	73	98	22	9	322
04-Mar-25	123	58	94	24	10	310
05-Mar-25	118	55	93	22	9	297
06-Mar-25	118	46	89	19	10	283
07-Mar-25	121	53	91	21	8	294
08-Mar-25	121	53	88	24	8	295
09-Mar-25	122	46	75	22	7	271
10-Mar-25	126	49	70	22	8	276
11-Mar-25	129	48	77	22	9	286
12-Mar-25	129	65	80	20	10	304
13-Mar-25	137	53	77	22	8	297
14-Mar-25	129	37	64	17	11	258
15-Mar-25	132	46	75	21	11	284
16-Mar-25	134	39	79	24	11	287
17-Mar-25	136	52	85	25	13	311
18-Mar-25	127	52	100	24	11	314
19-Mar-25	125	58	103	28	11	325
20-Mar-25	125	51	95	25	9	305
21-Mar-25	121	53	101	21	9	305
22-Mar-25	116	50	88	24	10	288
23-Mar-25	119	36	72	23	18	268
24-Mar-25	122	53	89	23	12	298
25-Mar-25	133	53	89	23	11	310
26-Mar-25	143	56	87	24	11	321
27-Mar-25	134	50	98	28	11	320
28-Mar-25	139	58	87	26	11	321
29-Mar-25	136	67	79	25	11	318
30-Mar-25	136	40	71	24	13	283
31-Mar-25	133	51	74	31	15	304
कुल TOTAL	3973	1598	2642	719	319	9252
उच्चतम MAXIMUM	146	73	103	31	18	327
निम्नतम MINIMUM	116	36	64	17	7	258
औसत AVERAGE	128	52	85	23	10	298
संचयी 2024-25 Cumulative 2024-25	79830	20761	35236	16685	7777	160290
अब तक का उच्चतम All Time Max.	443	167	208	157	43	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	27.06.24	30.08.22

HYDRO ENERGY DURING THE MONTH OF MARCH' 2025

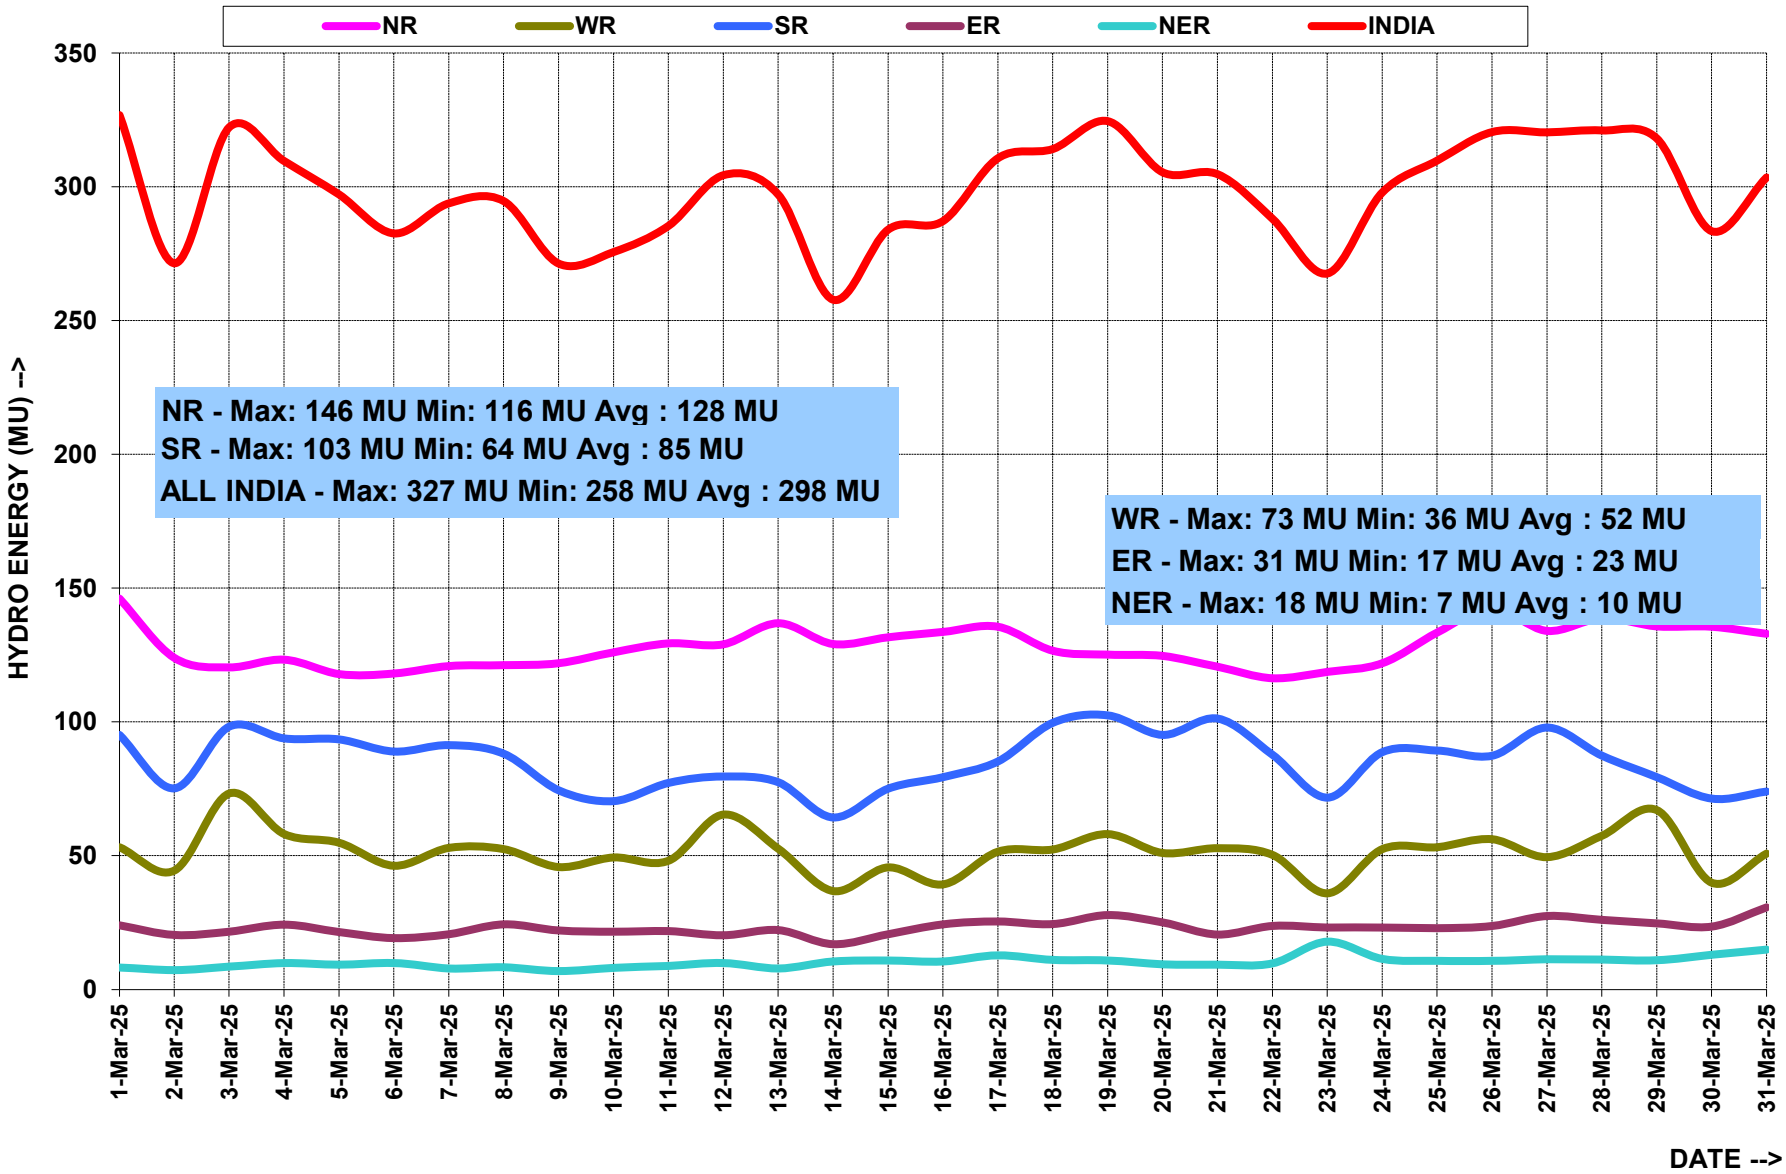

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: मार्च 2025 MONTH:- MAR 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-25	18	81	81	----------	----------	180
02-Mar-25	23	66	46	----------	----------	135
03-Mar-25	44	76	31	----------	----------	151
04-Mar-25	42	182	35	----------	----------	258
05-Mar-25	18	172	31	----------	----------	221
06-Mar-25	6	52	30	----------	----------	88
07-Mar-25	9	50	28	----------	----------	87
08-Mar-25	8	59	22	----------	----------	88
09-Mar-25	6	51	57	----------	----------	114
10-Mar-25	6	55	110	----------	----------	171
11-Mar-25	15	56	109	----------	----------	180
12-Mar-25	6	73	47	----------	----------	127
13-Mar-25	7	131	36	----------	----------	174
14-Mar-25	15	131	36	----------	----------	182
15-Mar-25	29	78	46	----------	----------	153
16-Mar-25	23	87	36	----------	----------	146
17-Mar-25	4	86	29	----------	----------	119
18-Mar-25	8	100	36	----------	----------	144
19-Mar-25	10	101	44	----------	----------	155
20-Mar-25	15	93	50	----------	----------	158
21-Mar-25	18	86	36	----------	----------	140
22-Mar-25	3	81	40	----------	----------	125
23-Mar-25	5	68	36	----------	----------	109
24-Mar-25	18	80	36	----------	----------	133
25-Mar-25	29	85	34	----------	----------	148
26-Mar-25	61	87	33	----------	----------	181
27-Mar-25	46	92	29	----------	----------	167
28-Mar-25	23	105	33	----------	----------	161
29-Mar-25	23	124	38	----------	----------	185
30-Mar-25	3	88	35	----------	----------	126
31-Mar-25	6	98	36	----------	----------	140
कुल TOTAL	547	2773	1327	----------	----------	4646
उच्चतम MAXIMUM	61	182	110	----------	----------	258
निम्नतम MINIMUM	3	50	22	----------	----------	87
औसत AVERAGE	18	89	43	----------	----------	150
संचयी 2024-25 Cumulative 2024-25	6938	36573	35945	----------	----------	79456
अब तक का उच्चतम All Time Max.	86	310	323	----------	----------	619
दिनांक Date	07.08.23	28.05.24	26.07.24	----------	----------	28.05.24

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: मार्च 2025 MONTH:- MAR 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-25	180	131	136	4.0	0.7	452
02-Mar-25	204	133	138	3.7	0.9	479
03-Mar-25	198	133	134	3.5	1.1	470
04-Mar-25	214	140	133	4.1	1.3	491
05-Mar-25	221	144	147	4.5	1.2	518
06-Mar-25	216	151	156	4.2	1.2	527
07-Mar-25	209	146	153	4.3	1.1	513
08-Mar-25	206	142	145	4.3	1.0	498
09-Mar-25	203	142	147	4.0	1.1	496
10-Mar-25	194	136	148	3.8	1.1	484
11-Mar-25	180	138	114	3.7	1.0	436
12-Mar-25	189	136	127	4.0	0.5	457
13-Mar-25	193	145	150	4.1	0.6	492
14-Mar-25	177	139	150	3.6	0.8	471
15-Mar-25	202	134	148	3.8	0.9	489
16-Mar-25	190	138	141	3.3	0.8	473
17-Mar-25	215	143	141	3.6	1.1	504
18-Mar-25	218	147	145	5.7	1.1	517
19-Mar-25	216	144	144	3.7	1.1	509
20-Mar-25	185	135	151	3.1	0.8	474
21-Mar-25	207	141	138	2.4	0.7	490
22-Mar-25	214	148	124	3.3	0.7	489
23-Mar-25	208	148	131	3.4	1.2	492
24-Mar-25	214	145	143	4.1	1.4	508
25-Mar-25	212	145	141	4.2	1.4	505
26-Mar-25	207	147	145	4.2	1.3	504
27-Mar-25	216	149	139	4.2	1.0	510
28-Mar-25	226	149	136	4.1	0.8	516
29-Mar-25	207	144	141	4.0	0.8	496
30-Mar-25	224	153	141	4.1	1.1	522
31-Mar-25	221	143	129	3.8	1.1	498
कुल TOTAL	6366	4408	4354	121	31	15280
उच्चतम MAXIMUM	226	153	156	5.7	1.4	527
निम्नतम MINIMUM	177	131	114	2.4	0.5	436
औसत AVERAGE	205	142	140	3.9	1.0	493
संचयी 2024-25 Cumulative 2024-25	57095	33347	42871	1111	343.9	134769
अब तक का उच्चतम All Time Max.	**226**	**153**	**156**	**5.7**	3.5	**527**
दिनांक Date	**28.03.25**	**30.03.25**	**06.03.25**	**18.03.25**	08.09.24	**06.03.25**

* **Source**: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: मार्च 2025 MONTH:- MAR 2025

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फ़ैक्टर Diversity Factor*
01-Mar-25	57890	77308	66557	23250	2766	223488	1.019
02-Mar-25	54799	74329	62601	23324	2642	212879	1.023
03-Mar-25	59734	77526	67634	24951	2813	226800	1.026
04-Mar-25	61078	76070	68797	26256	2867	229569	1.024
05-Mar-25	58273	72875	68399	25176	2837	221972	1.025
06-Mar-25	60283	75288	67811	23490	2772	226229	1.015
07-Mar-25	65078	75978	68871	24002	2734	233009	1.016
08-Mar-25	65179	75955	67522	24619	2760	229961	1.026
09-Mar-25	64020	73455	63213	24513	2638	223311	1.020
10-Mar-25	66638	77520	66816	25433	2789	233616	1.024
11-Mar-25	66052	77716	67543	25028	2846	235224	1.017
12-Mar-25	65644	77633	66097	26025	2790	233408	1.020
13-Mar-25	64014	76535	65290	26317	2782	230513	1.019
14-Mar-25	51525	65327	64884	23965	2618	199143	1.046
15-Mar-25	51512	71164	65608	25460	2662	209995	1.031
16-Mar-25	52646	70660	62873	25049	2677	209163	1.023
17-Mar-25	57372	73197	69104	26316	2765	222988	1.026
18-Mar-25	58304	73187	69242	26276	2835	223113	1.030
19-Mar-25	59038	73358	68990	27027	3057	226688	1.021
20-Mar-25	59046	73230	69389	24922	2949	225884	1.016
21-Mar-25	60832	72545	69942	23561	2886	226152	1.016
22-Mar-25	58499	71865	66862	22738	2910	218033	1.022
23-Mar-25	54872	69637	60579	23343	2720	204563	1.032
24-Mar-25	58078	73581	67016	24951	3010	220441	1.028
25-Mar-25	59176	73970	66761	25914	3478	221847	1.034
26-Mar-25	59972	73751	68183	27136	3128	223731	1.038
27-Mar-25	58799	73908	68542	27744	3200	224229	1.036
28-Mar-25	57851	72460	69695	28112	3257	221062	1.047
29-Mar-25	55487	72161	68901	28058	3268	215865	1.056
30-Mar-25	53937	69568	64315	27419	3045	209537	1.042
31-Mar-25	55181	72256	66091	28137	3173	215421	1.044
उच्चतम MAXIMUM	66638	77716	69942	28137	3478	235224	1.056
निम्नतम MINIMUM	51512	65327	60579	22738	2618	199143	1.015
औसत AVERAGE	59058	73678	66907	25436	2893	221866	1.028
अब तक का उच्चतम All Time Max.	91215	**80000**	**69942**	32531	3905	250070	
दिनांक Date	19.06.24	**08.02.25**	**21.03.25**	10.06.24	19.09.24	30.05.24	


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 11thMAR (MAXIMUM DEMAND MET)

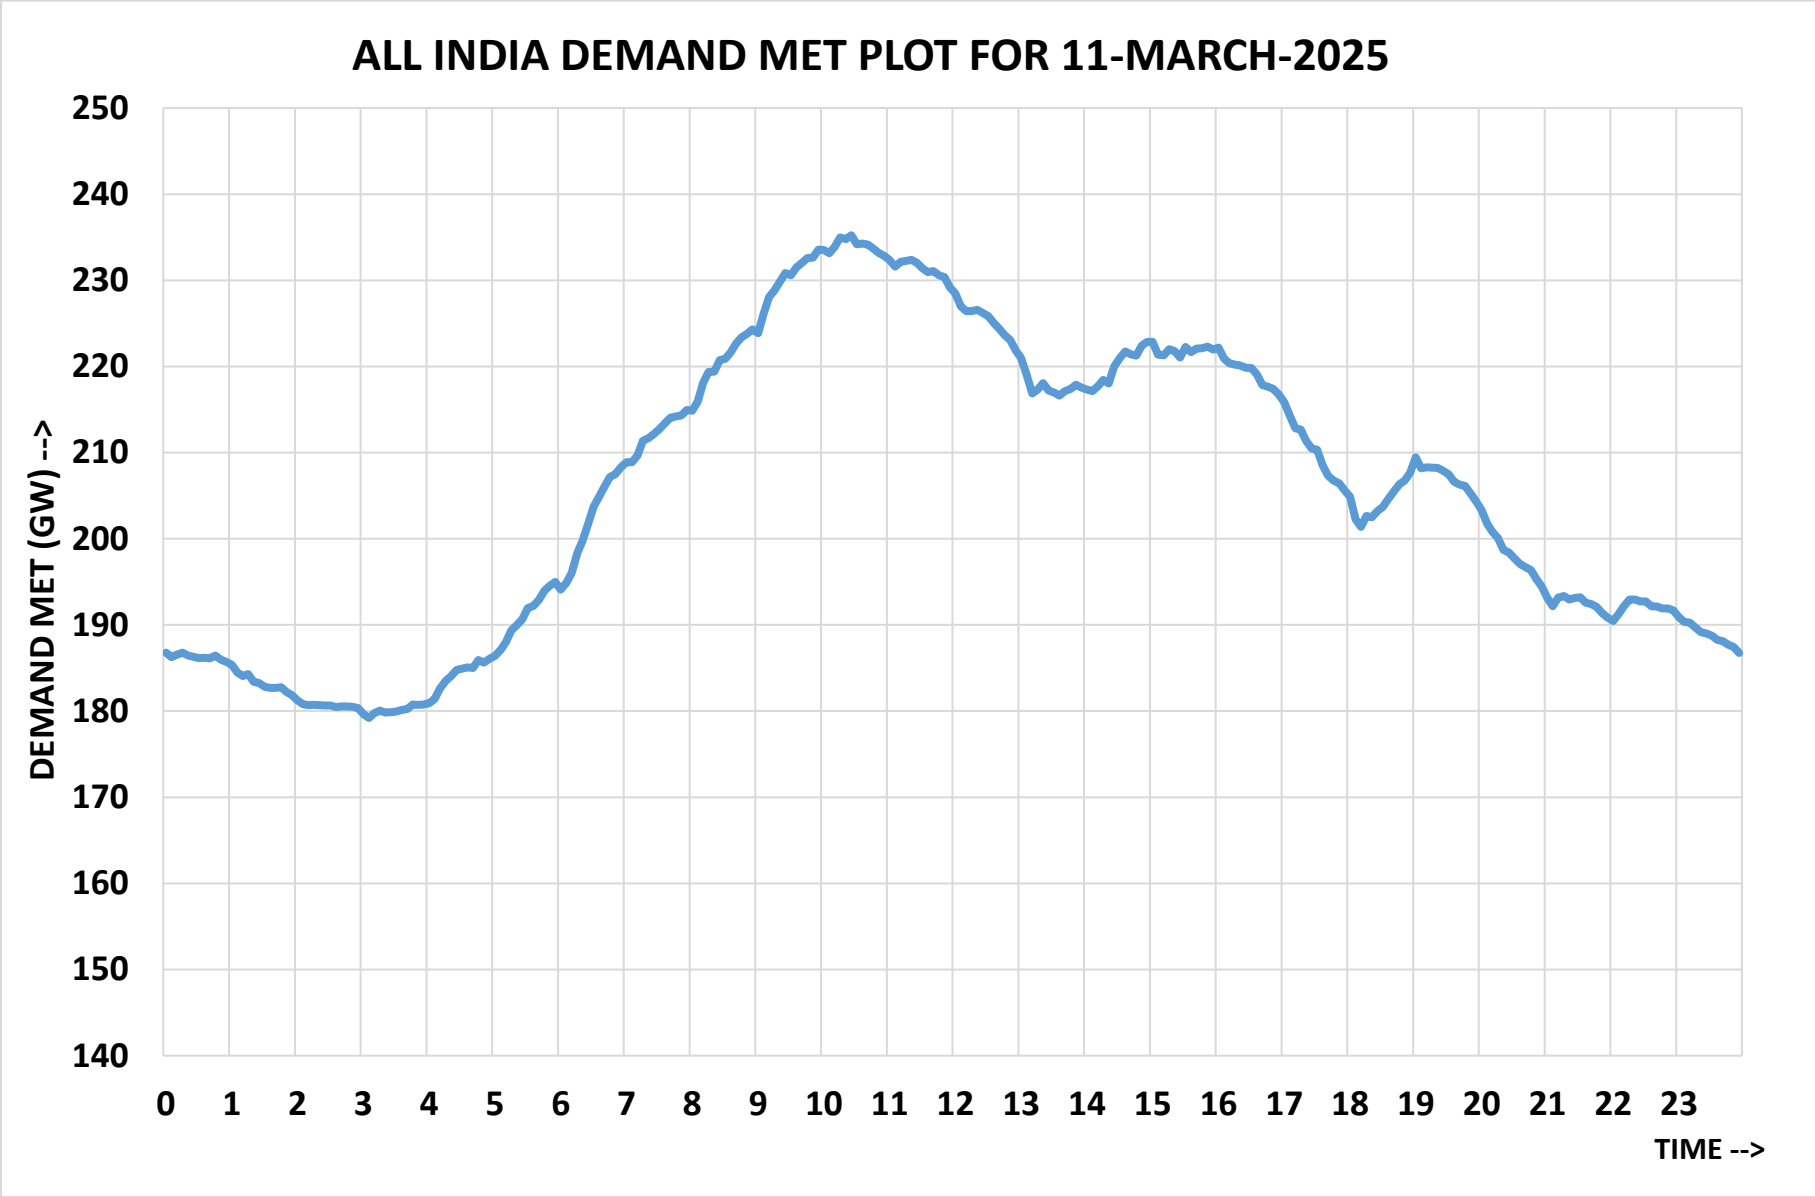

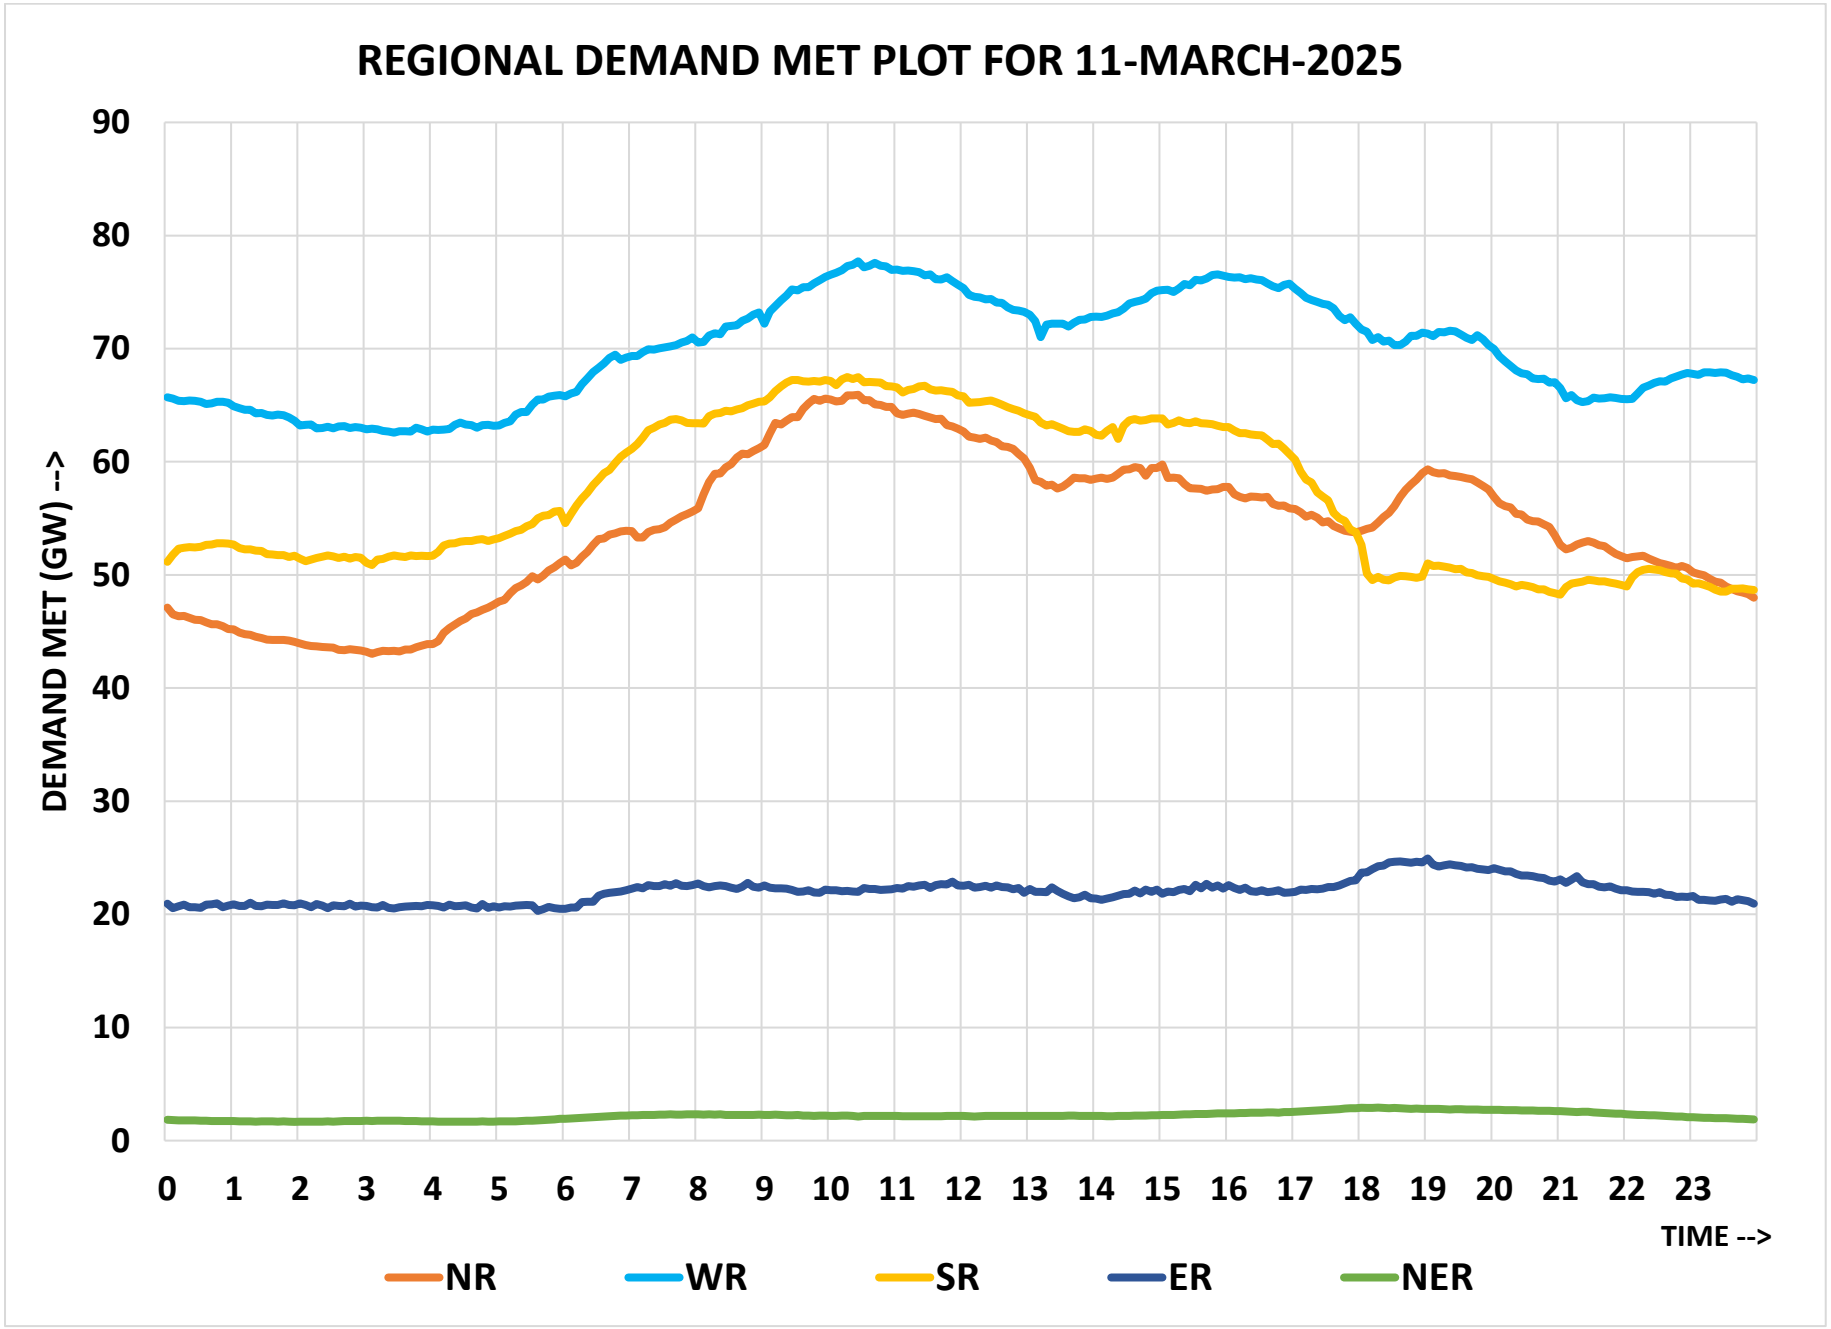
REGIONAL DEMAND MET PLOT FOR 11-MARCH-2025
DEMAND MET (GW) -->
90
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

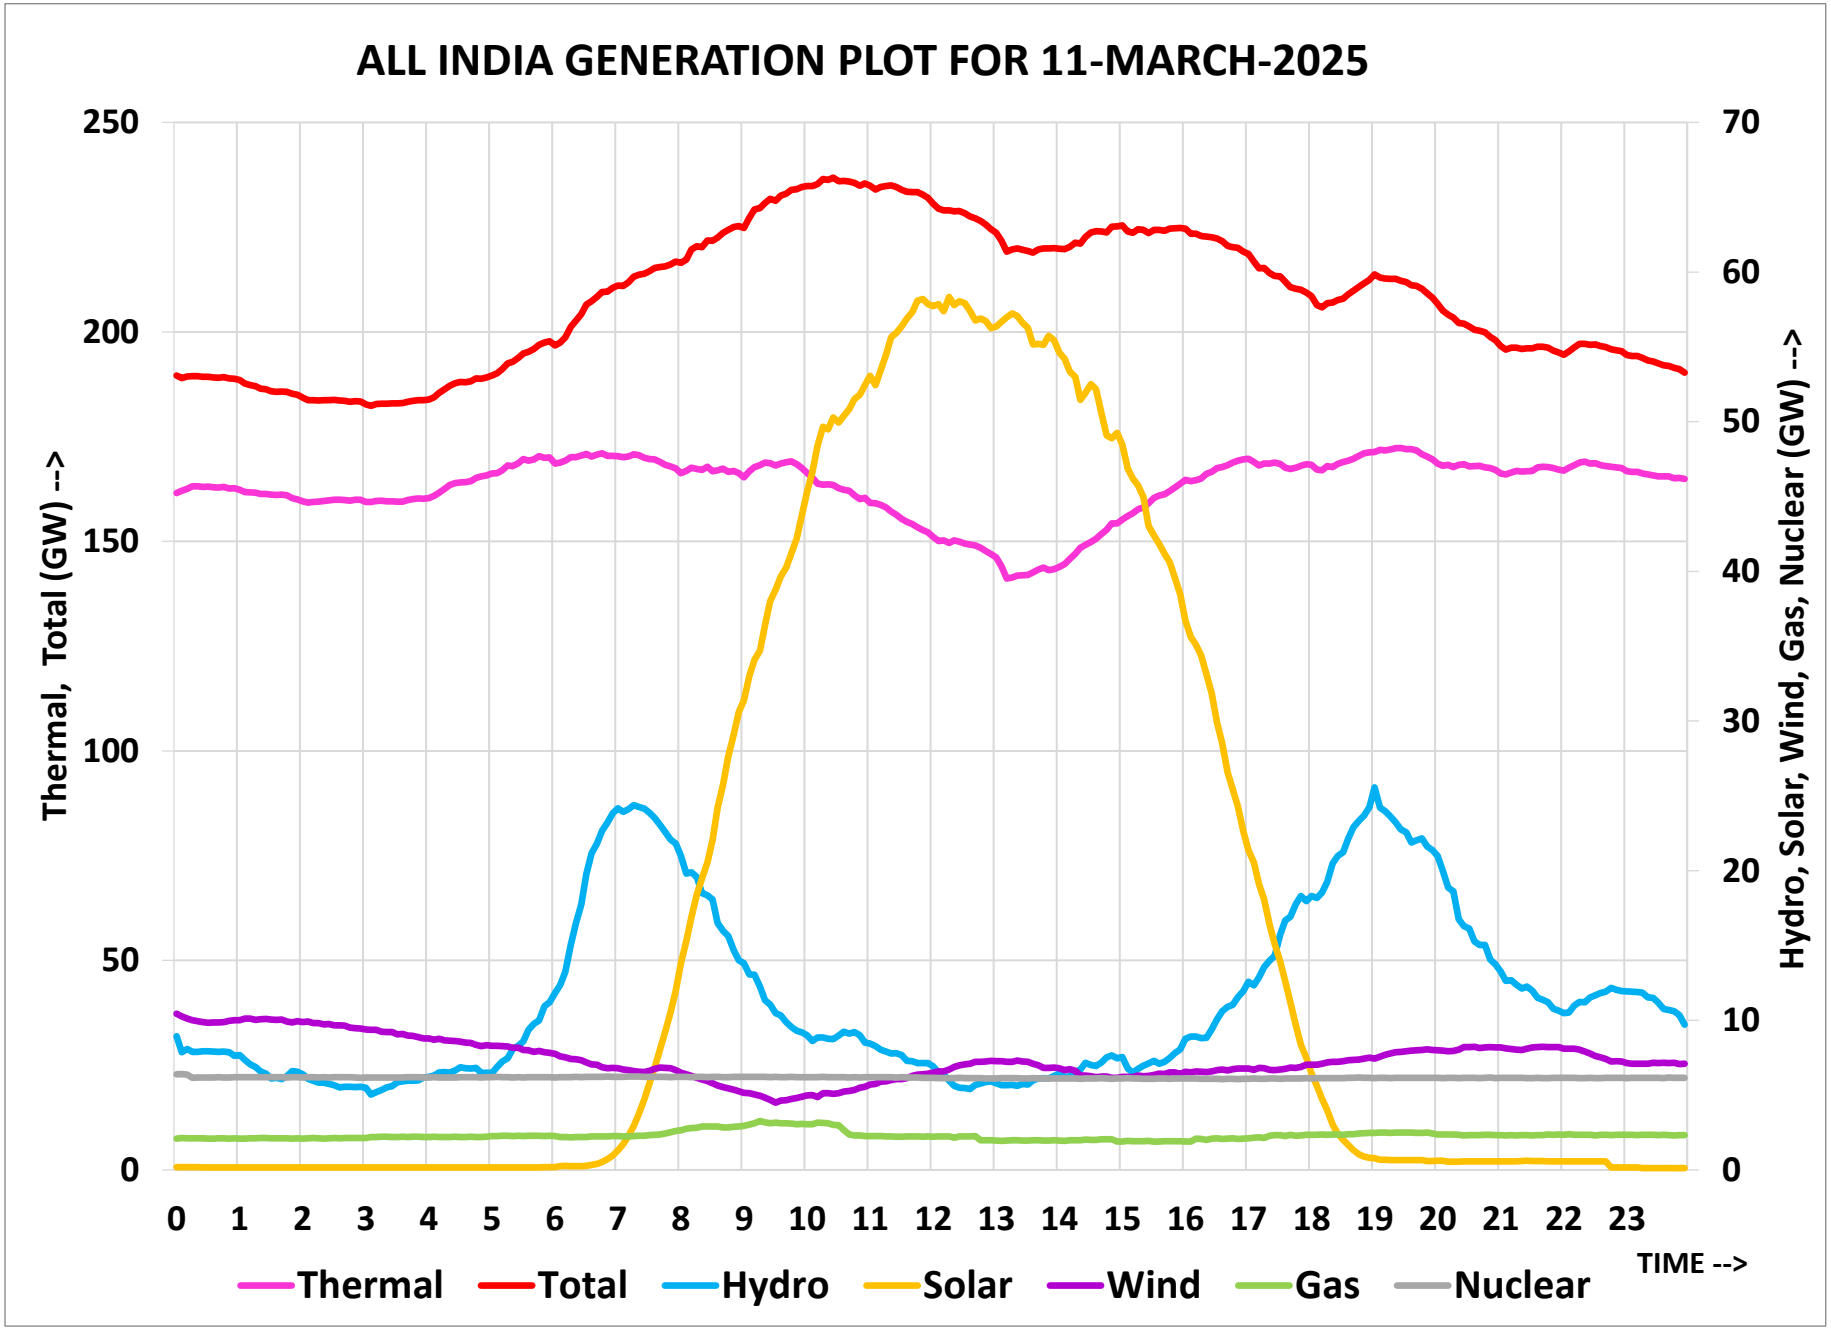
ALL INDIA GENERATION PLOT FOR 11-MARCH-2025
Thermal, Total (GW) -->
Hydro, Solar, Wind, Gas, Nuclear (GW) -->
250
200
150
100
50
0
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Thermal
Total
Hydro
Solar
Wind
Gas
Nuclear

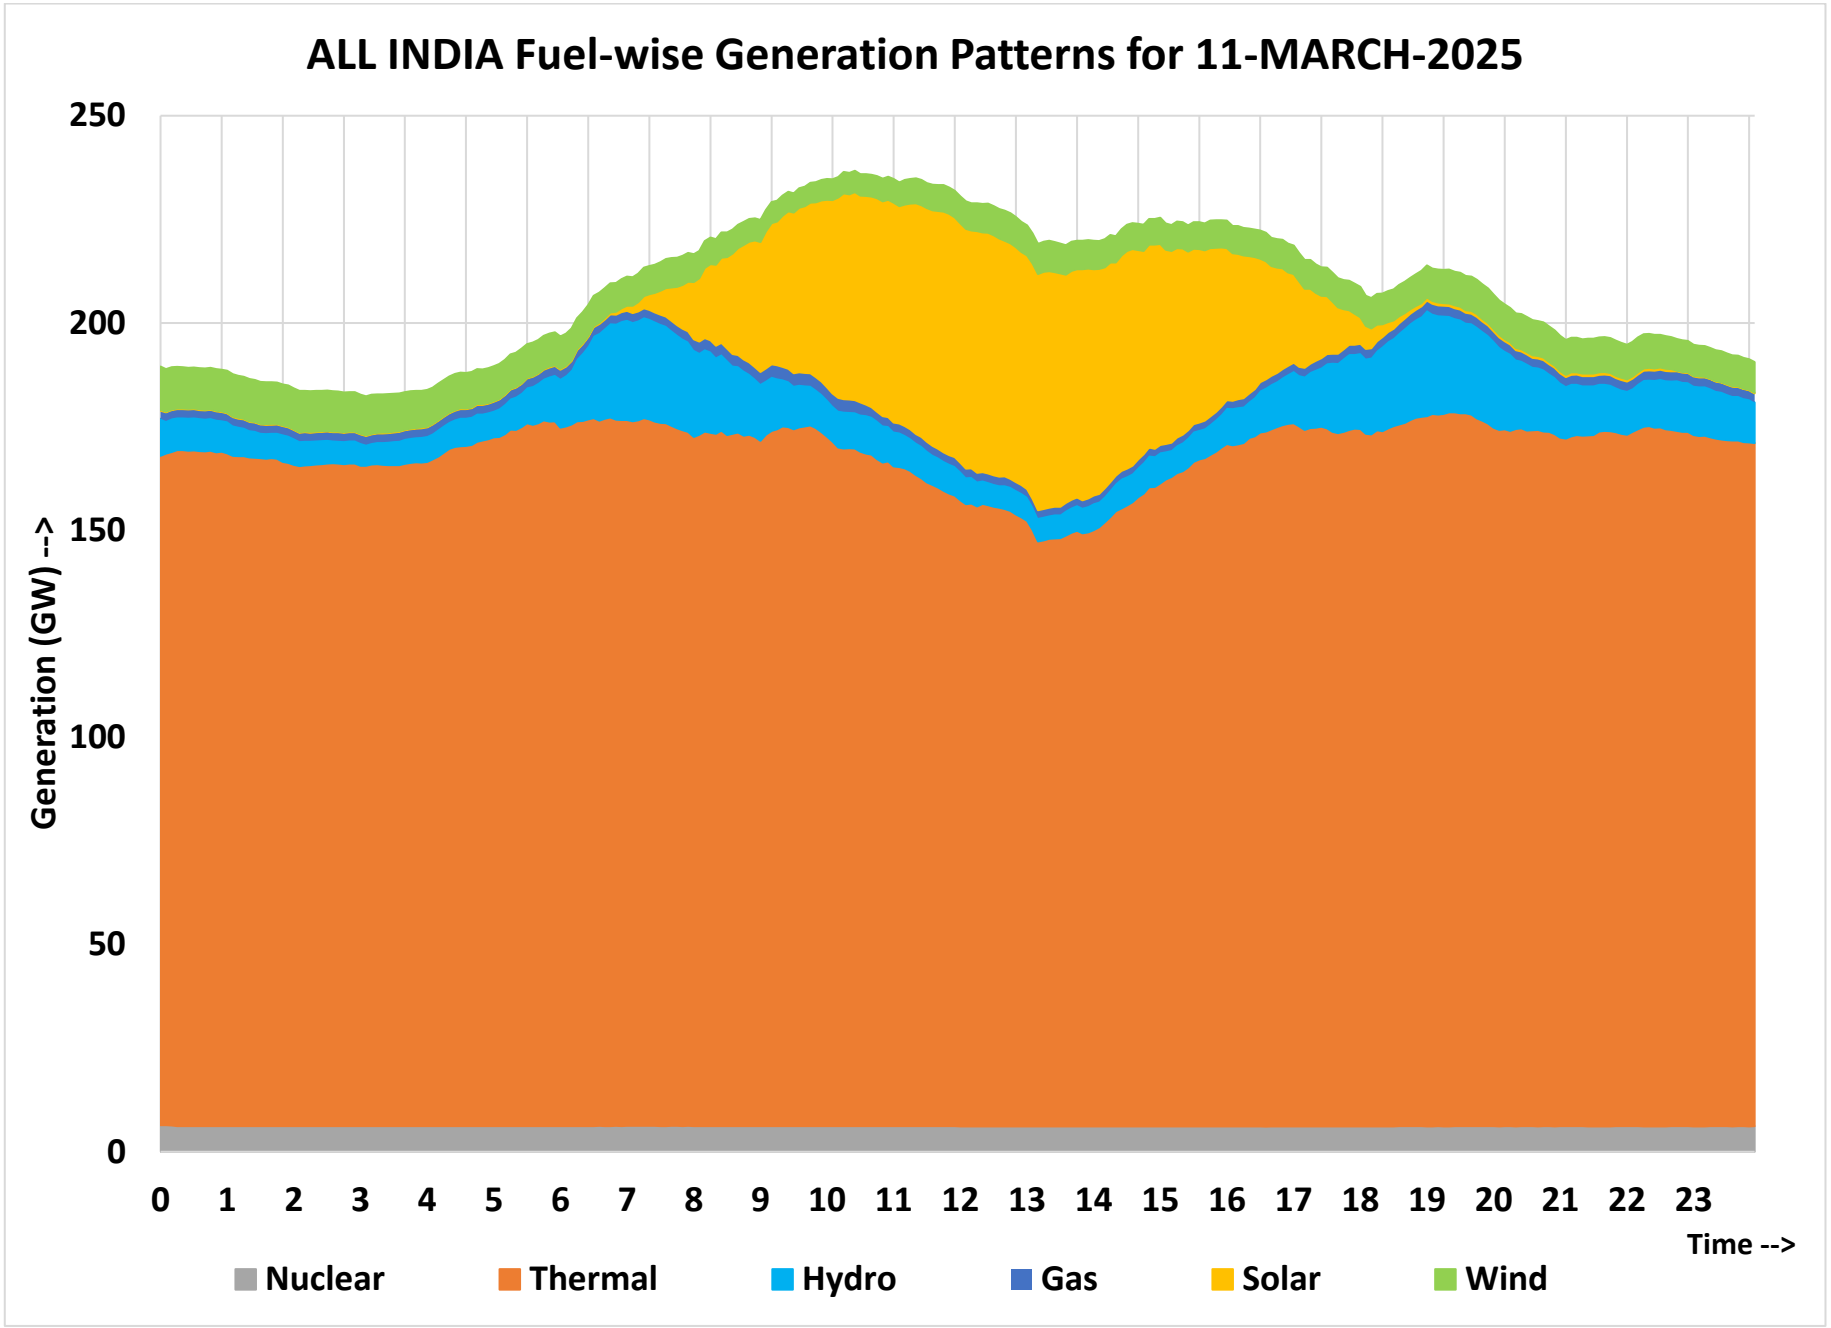
ALL INDIA Fuel-wise Generation Patterns for 11-MARCH-2025
Generation (GW) -->
250
200
150
100
50
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
Time -->
Nuclear
Thermal
Hydro
Gas
Solar
Wind

11 मार्च 2025 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति

ALL INDIA DEMAND MET FOR 11 MARCH 2025 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	186246		**12:05**	226984
00:20	186454		**12:20**	226577
00:35	186183		**12:35**	225040
00:50	185956		**12:50**	223083
01:05	184465		**13:05**	218975
01:20	183407		**13:20**	218078
01:35	182677		**13:35**	216621
01:50	182212		**13:50**	217871
02:05	180782		**14:05**	217144
02:20	180683		**14:20**	218034
02:35	180461		**14:35**	221732
02:50	180481		**14:50**	222412
03:05	179195		**15:05**	221360
03:20	179845		**15:20**	221774
03:35	180130		**15:35**	221666
03:50	180725		**15:50**	222294
04:05	181390		**16:05**	220913
04:20	184075		**16:20**	220115
04:35	185072		**16:35**	219079
04:50	185633		**16:50**	217377
05:05	187090		**17:05**	214358
05:20	189980		**17:20**	211347
05:35	192199		**17:35**	208566
05:50	194529		**17:50**	206417
06:05	194856		**18:05**	202275
06:20	199833		**18:20**	202510
06:35	204855		**18:35**	204657
06:50	207522		**18:50**	206770
07:05	208873		**19:05**	208167
07:20	211687		**19:20**	208207
07:35	213392		**19:35**	206628
07:50	214299		**19:50**	205277
08:05	215900		**20:05**	201768
08:20	219417		**20:20**	198721
08:35	221610		**20:35**	197067
08:50	223789		**20:50**	195305
09:05	226129		**21:05**	192155
09:20	229830		**21:20**	192938
09:35	231457		**21:35**	192557
09:50	232620		**21:50**	191391
10:05	233138		**22:05**	191290
10:20	234771		**22:20**	192931
10:35	234251		**22:35**	192183
10:50	233184		**22:50**	191896
11:05	231598		**23:05**	190347
11:20	232371		**23:20**	189144
11:35	230955		**23:35**	188274
11:50	230366		**23:50**	187447
Maximum Demand of 235224 MW met@ 10:26 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instanteneous demand

11. ACTUAL POWER SUPPLY POSITION - MARCH 2025

REGION	STATE	Energy Requirement & Met (MU/Day)			Energy Requirement & Met (MU)				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	109	109	0	0.0	229	229	0	0.0
	Delhi	75	75	0.0	2321	2321	0	0.0	4361	4361	0	0.0
	Haryana	147	147	0.0	4547	4547	0	0.0	8750	8750	0	0.0
	Himachal Pradesh	33	33	0.0	1028	1028	0	0.0	2075	2075	0	0.0
	J&K(UT) and Ladakh(UT)	60	59	-0.1	1848	1844	-3	-0.2	3095	3024	-71	-2.3
	Punjab	159	159	0.0	4931	4931	0	0.0	10083	10083	0	0.0
	Rajasthan	299	299	0.0	9277	9277	0	0.0	17763	17763	0	0.0
	Uttar Pradesh	369	369	-0.1	11445	11443	-3	0.0	21869	21869	0	0.0
	Uttarakhand	40	40	0.0	1230	1230	0	0.0	2202	2202	0	0.0
	Railway_NR ISTS	4	4	0.0	130	130	0	0.0	226	226	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	10	10	0	0.0
	TOTAL	1189	1189	-0.2	36868	36862	-6	0.0	65384	65384	0	0.0
WR	Gujarat	451	451	-0.1	13982	13980	-3	0.0	24395	24378	-17	-0.1
	Madhya Pradesh	292	292	-0.3	9064	9054	-10	-0.1	16622	16622	0	0.0
	Chhattisgarh	142	142	0.0	4392	4392	0	0.0	6511	6511	0	0.0
	Maharashtra	658	658	0.0	20400	20400	0	0.0	30675	30675	0	0.0
	Goa	16	16	0.0	504	504	0	0.0	810	810	0	0.0
	DNHDDPDCL	30	30	0.0	924	924	0	0.0	1377	1377	0	0.0
	AMNSIL	17	17	0.0	534	534	0	0.0	854	854	0	0.0
	BALCO	13	13	0.0	395	395	0	0.0	538	538	0	0.0
	RIL JAMNAGAR*	6	6	0.0	181	181	0	0.0	269	269	0	0.0
	TOTAL	1625	1625	-0.4	50377	50364	-13	0.0	78082	78082	0	0.0
SR	Andhra Pradesh	245	245	0.0	7597	7597	0	0.0	13110	13110	0	0.0
	Telangana	321	321	0.0	9951	9951	0	0.0	17162	17162	0	0.0
	Karnataka	339	339	0.0	10496	10496	0	0.0	18395	18395	0	0.0
	Kerala	97	97	0.0	3019	3019	0	0.0	5347	5347	0	0.0
	Tamil Nadu	383	383	0.0	11864	11864	0	0.0	19939	19939	0	0.0
	Puducherry	10	10	0.0	308	308	0	0.0	473	473	0	0.0
	TOTAL	1395	1395	0.0	43235	43235	0	0.0	69934	69934	0	0.0
ER	Bihar	104	104	-0.1	3219	3216	-3	-0.1	6518	6305	-213	-3.3
	Jharkhand	40	40	0.0	1253	1253	-1	-0.1	2223	2223	0	0.0
	DVC	70	70	0.0	2170	2170	0	0.0	3466	3466	0	0.0
	Odisha	119	119	0.0	3683	3683	0	0.0	6192	6192	0	0.0
	West Bengal	197	197	0.0	6094	6094	0	0.0	10702	10702	0	0.0
	Sikkim	2	2	0.0	53	53	0	0.0	126	126	0	0.0
	Railways_ER ISTS	0	0	0.0	5	5	0	0.0	25	25	0	0.0
	TOTAL	532	531	-0.1	16478	16474	-4	0.0	28332	28119	-213	-0.8
NER	Arunachal Pradesh	3	3	0.0	94	94	0	0.0	180	180	0	0.0
	Assam	31	31	0.0	946	946	0	0.0	1917	1897	-20	-1.0
	Manipur	3	3	-0.2	90	85	-6	-6.1	213	213	0	0.0
	Meghalaya	6	6	0.0	172	172	0	0.0	354	354	0	0.0
	Mizoram	2	2	0.0	63	63	0	0.0	151	151	0	0.0
	Nagaland	2	2	0.0	73	73	0	0.0	164	164	0	0.0
	Tripura	5	5	0.0	159	159	0	0.0	322	322	0	0.0
	TOTAL	52	51	-0.2	1598	1592	-6	-0.3	3273	3273	0	0.0
ALL INDIA		4792	4791	-0.9	148556	148528	-28	0.0				

* RIL Jamnagar has been added as new entity wef 01.12.2024

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF MARCH 2025 vs MARCH 2024

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Mar-24	Mar-25	Difference	% Change	Average MU/day for Oct-24	Mar-24	Mar-25	Difference	% Change	Average MU/day for Oct-24
NR	Chandigarh	109	109	1	1	4	109	109	1	1	4
	Delhi	2204	2321	117	5	75	2204	2321	117	5	75
	Haryana	4289	4547	258	6	147	4289	4547	258	6	147
	Himachal Pradesh	953	1028	75	8	33	949	1028	78	8	33
	J&K(UT) and Ladakh(UT)	1714	1848	134	8	60	1707	1844	137	8	59
	Punjab	4698	4931	233	5	159	4698	4931	233	5	159
	Rajasthan	8937	9277	340	4	299	8937	9277	340	4	299
	Uttar Pradesh	10440	11445	1005	10	369	10439	11443	1004	10	369
	Uttarakhand	1220	1230	10	1	40	1219	1230	10	1	40
	Railway_NR ISTS/NFL	119	132	13	11	4	119	132	13	11	4
	TOTAL	34683	36868	2185	6	1189	34672	36862	2190	6	1189
WR	Gujarat	12947	13982	1035	8	451	12947	13980	1032	8	451
	Madhya Pradesh	7813	9064	1251	16	292	7813	9054	1242	16	292
	Chhattisgarh	3948	4392	445	11	142	3948	4392	444	11	142
	Maharashtra	18796	20400	1604	9	658	18795	20400	1604	9	658
	Goa	448	504	56	12	16	448	504	56	12	16
	DNHDDPDCL	866	924	58	7	30	866	924	58	7	30
	AMNSIL	595	534	-60	-10	17	595	534	-60	-10	17
	BALCO	387	395	8	2	13	387	395	8	2	13
	RIL JAMNAGAR*	-	181	-	-	-	-	181	-	-	-
	TOTAL	45799	50377	4578	10	1625	45799	50364	4566	10	1625
SR	Andhra Pradesh	6679	7597	918	14	245	6658	7597	940	14	245
	Telangana	7993	9951	1957	24	321	7968	9951	1983	25	321
	Karnataka	8848	10496	1648	19	339	8823	10496	1673	19	339
	Kerala	2595	3019	424	16	97	2587	3019	432	17	97
	Tamil Nadu	10452	11864	1412	14	383	10419	11864	1445	14	383
	Puducherry	270	308	38	14	10	269	308	39	14	10
	TOTAL	36837	43235	6398	17	1395	36723	43235	6511	18	1395
ER	Bihar	2883	3219	336	12	104	2879	3216	337	12	104
	Jharkhand	1146	1253	108	9	40	1120	1253	132	12	40
	DVC	2190	2170	-19	-1	70	2190	2170	-19	-1	70
	Odisha	3794	3683	-111	-3	119	3794	3683	-111	-3	119
	West Bengal	5256	6094	838	16	197	5256	6094	838	16	197
	Sikkim	54	53	-1	-1	2	54	53	-1	-1	2
	Railways_ER ISTS	4	5	1	30	0	4	5	1	30	0
	TOTAL	15327	16478	1152	8	532	15297	16474	1177	8	531
NER	Arunachal Pradesh	89	94	5	6	3	89	94	5	6	3
	Assam	882	946	64	7	31	882	946	64	7	31
	Manipur	91	90	-1	-1	3	91	85	-6	-7	3
	Meghalaya	181	172	-9	-5	6	181	172	-9	-5	6
	Mizoram	60	63	2	4	2	60	63	2	4	2
	Nagaland	69	73	4	6	2	69	73	4	6	2
	Tripura	124	159	35	29	5	124	159	35	29	5
	TOTAL	1496	1598	101	7	52	1496	1592	96	6	51
ALL INDIA		134143	148556	14413	11	4792	133988	148528	14540	11	4791

* RIL Jamnagar has been added as new entity wef 01.12.2024

13. DEMAND COMPARISON OF MARCH 2025 vs MARCH 2024

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Mar-24	Mar-25	Difference	% Change	Mar-24	Mar-25	Difference	% Change
NR	Chandigarh	237	229	-8	-3.4	237	229	-8	-3.4
	Delhi	4482	4361	-121	-2.7	4482	4361	-121	-2.7
	Haryana	7747	8750	1003	12.9	7747	8750	1003	12.9
	Himachal Pradesh	1982	2075	93	4.7	1982	2075	93	4.7
	J&K(UT) and Ladakh(UT)	2896	3095	199	6.9	2896	3024	128	4.4
	Punjab	10214	10083	-131	-1.3	10214	10083	-131	-1.3
	Rajasthan	17030	17763	733	4.3	17030	17763	733	4.3
	Uttar Pradesh	21243	21869	626	2.9	21243	21869	626	2.9
	Uttarakhand	2260	2202	-58	-2.6	2260	2202	-58	-2.6
	Railway_NR ISTS/NFL	218	236	18	8.3	218	236	18	8.3
WR	Gujarat	21843	24395	2552	12	21843	24378	2535	11.6
	Madhya Pradesh	13594	16622	3028	22	13594	16622	3028	22.3
	Chhattisgarh	6148	6511	363	6	6148	6511	363	5.9
	Maharashtra	28795	30675	1880	7	28735	30675	1940	6.8
	Goa	767	810	44	6	767	810	44	5.7
	DNHDDPDCL	1283	1377	94	7.3	1283	1377	94	7.3
	AMNSIL	928	854	-74	-8.0	928	854	-74	-8.0
	BALCO	527	538	12	2.2	527	538	12	2.2
	RIL JAMNAGAR*	-	269	-	-	-	269	-	-
SR	Andhra Pradesh	12216	13110	894	7.3	12216	13110	894	7.3
	Telangana	13829	17162	3333	24.1	13810	17162	3352	24.3
	Karnataka	17220	18395	1175	6.8	17220	18395	1175	6.8
	Kerala	5302	5347	45	0.8	5301	5347	46	0.9
	Tamil Nadu	17045	19939	2894	17.0	17035	19939	2904	17.0
	Puducherry	453	473	20	4.4	453	473	20	4.4
ER	Bihar	5758	6518	760	13.2	5758	6305	547	9.5
	Jharkhand	1870	2223	354	18.9	1870	2223	354	18.9
	DVC	3403	3466	63	1.9	3403	3466	63	1.9
	Odisha	6133	6192	59	1.0	6133	6192	59	1.0
	West Bengal	10188	10702	514	5.0	10188	10702	514	5.0
	Sikkim	118	126	8	6.4	118	126	8	6.4
	Railways_ER ISTS	17	25	8	47.1	17	25	8	47.1
NER	Arunachal Pradesh	177	180	3	1.7	177	180	3	1.7
	Assam	1814	1917	103	5.7	1782	1897	115	6.5
	Manipur	226	213	-13	-5.8	226	213	-13	-5.8
	Meghalaya	398	354	-44	-11.1	398	354	-44	-11.1
	Mizoram	136	151	15	11.0	136	151	15	11.0
	Nagaland	158	164	6	3.8	157	164	7	4.5
	Tripura	288	322	34	11.8	288	322	34	11.8

* RIL Jamnagar has been added as new entity wef 01.12.2024

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - MARCH 2025

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	110.26	111.23	0.97	0.88	3.56	3.59	0.03
	Delhi	2092.91	2085.22	-7.69	-0.37	67.51	67.27	-0.25
	Haryana	2999.69	2982.07	-17.62	-0.59	96.76	96.20	-0.57
	Himachal Pradesh	705.19	690.13	-15.06	-2.14	22.75	22.26	-0.49
	J&K(UT) and Ladakh(UT)	1673.46	1628.85	-44.61	-2.67	53.98	52.54	-1.44
	Punjab	1974.33	1847.28	-127.05	-6.43	63.69	59.59	-4.10
	Rajasthan	2587.09	2458.75	-128.34	-4.96	83.45	79.31	-4.14
	Uttar Pradesh	2733.73	2679.28	-54.45	-1.99	88.18	86.43	-1.76
	Uttarakhand	908.45	902.25	-6.20	-0.68	29.30	29.10	-0.20
	Railways_NR ISTS	119.60	129.95	10.36	8.66	3.86	4.19	0.33
	NFL	2.58	2.34	-0.24	-9.28	0.08	0.08	-0.01
	Total	15907.29	15517.36	-389.93	-2.45	513.14	500.56	-12.58
WR	Gujarat	5717.03	5625.85	-91.18	-1.59	184.42	181.48	-2.94
	Madhya Pradesh	5248.05	5149.41	-98.64	-1.88	169.29	166.11	-3.18
	Chhattisgarh	2441.39	2438.81	-2.58	-0.11	78.75	78.67	-0.08
	Maharashtra	7505.95	7500.03	-5.92	-0.08	242.13	241.94	-0.19
	Goa	477.54	488.90	11.36	2.38	15.40	15.77	0.37
	DNHDDPDCL	928.47	924.47	-4.00	-0.43	29.95	29.82	-0.13
	AMNSIL	301.89	307.57	5.68	1.88	9.74	9.92	0.18
	BALCO	393.78	394.79	1.01	0.26	12.70	12.74	0.03
	RIL JAMNAGAR*	184.19	180.79	-3.40	-1.85	5.94	5.83	-0.11
	Total	23198.29	23010.61	-187.68	-0.81	748.33	742.28	-6.05
SR	Andhra Pradesh	2316.83	2308.82	-8.01	-0.35	74.74	74.48	-0.26
	Telangana	5737.42	5717.64	-19.78	-0.34	185.08	184.44	-0.64
	Karnataka	4312.58	4299.93	-12.65	-0.29	139.12	138.71	-0.41
	Kerala	2428.71	2453.89	25.18	1.04	78.35	79.16	0.81
	Tamil Nadu	7668.11	7612.15	-55.96	-0.73	247.36	245.55	-1.81
	Puducherry	295.84	290.65	-5.19	-1.75	9.54	9.38	-0.17
	Goa (SR)	72.73	69.08	-3.65	-5.02	2.35	2.23	-0.12
	Total	22832.22	22752.16	-80.06	-0.35	736.52	733.94	-2.58
ER	Bihar	3042.89	3012.19	-30.70	-1.01	98.16	97.17	-0.99
	Jharkhand	938.27	926.65	-11.62	-1.24	30.27	29.89	-0.37
	DVC	-1375.56	-1384.14	-8.58	0.62	-44.37	-44.65	-0.28
	Odisha	1081.15	1057.86	-23.29	-2.15	34.88	34.12	-0.75
	West Bengal	1700.04	1631.51	-68.53	-4.03	54.84	52.63	-2.21
	Sikkim	53.88	53.37	-0.52	-0.96	1.74	1.72	-0.02
	Railways_ER ISTS	5.34	5.31	-0.02	-0.45	0.17	0.17	0.00
	Total	5446.00	5302.76	-143.25	-2.63	175.68	171.06	-4.62
NER	Arunachal Pradesh	96.75	91.26	-5.49	-5.67	3.12	2.94	-0.18
	Assam	748.00	761.80	13.80	1.84	24.13	24.57	0.45
	Manipur	82.07	84.89	2.82	3.44	2.65	2.74	0.09
	Meghalaya	141.12	138.16	-2.96	-2.10	4.55	4.46	-0.10
	Mizoram	56.33	52.65	-3.68	-6.54	1.82	1.70	-0.12
	Nagaland	72.46	71.39	-1.08	-1.48	2.34	2.30	-0.03
	Tripura	133.02	139.14	6.12	4.60	4.29	4.49	0.20
	Total	1329.75	1339.29	9.54	0.72	42.90	43.20	0.31
All India Total		68713.55	67922.17	-791.38	-1.15	2216.57	2191.04	-25.53

* RIL Jamnagar has been added as new entity wef 01.12.2024

15. INTER REGIONAL EXCHANGES 2024-25

(All figures in MU)

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Mar'25	Fin. Year 2024-25
Name of Line													
Import of NR from WR (WR-NR)													
WR - NR 765 kV Gwalior - Agra 2xS/C	529.65	1235.15	1669.21	1351.99	1068.69	747.76	714.49	611.32	751.39	877.91	330.17	77.39	**9965.12**
WR-NR 765 kV Gwalior - Phagi 2xS/C	157.44	396.56	594.39	585.50	415.22	594.58	840.34	817.51	665.18	664.69	514.09	200.75	**6446.25**
WR-NR 765 kV Jabalpur-Orai D/C	304.53	976.67	1388.19	1346.63	986.20	952.08	1009.96	819.22	774.41	896.18	415.21	78.16	**9947.44**
WR-NR 765 kV Satna-Orai	535.85	669.33	731.25	645.38	573.08	499.10	583.07	599.61	586.45	592.74	485.93	442.65	**6944.44**
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Champa - Kurukshetra	1525.63	2816.73	3112.34	2430.48	2049.78	1553.63	1570.74	720.37	1288.63	1766.28	1731.95	1319.40	**21885.96**
WR - NR HVDC Vindhyachal	0.00	100.25	234.97	96.45	55.37	129.20	0.00	39.19	106.05	66.90	41.66	50.55	**920.59**
WR - NR 400 kV Zerda Kankroli	0.00	35.28	83.46	65.18	41.60	2.95	0.00	0.00	3.10	6.27	0.00	0.00	**237.84**
WR - NR 400 kV Zerda Bhinmal	0.00	1.38	0.00	4.10	8.87	31.67	17.54	0.00	1.08	0.00	0.00	0.00	**64.64**
WR - NR 400 kV RAPP C - Shujalpur D/C	0.00	60.74	171.23	154.47	58.48	88.97	60.41	0.08	2.44	3.06	0.44	0.00	**600.32**
WR - NR 220 kV Bhanpura - Ranpur	55.64	76.03	72.42	62.97	41.95	55.79	60.83	64.26	52.46	55.29	62.04	50.93	**710.61**
WR - NR 220 kV Bhanpura - Modak	69.87	76.33	55.61	69.42	47.26	42.37	58.67	96.18	95.67	89.99	88.29	75.12	**864.78**
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	3.05	7.54	1.83	2.61	1.19	0.00	0.00	0.00	0.00	0.00	0.00	**16.22**
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR HVDC Mundra - Mohindergarh	717.97	1144.70	1159.61	1529.31	1016.00	844.37	1096.69	827.50	752.53	932.98	840.99	1053.73	**11916.38**
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.67	262.23	420.74	391.70	415.22	1.22	0.00	0.00	74.13	63.08	8.74	0.00	**1637.73**
WR-NR 765 kV Varanasi-Vindhyachal	1373.47	2029.86	2265.31	2036.99	1771.06	1548.14	1113.89	1038.27	1036.90	1223.28	522.72	658.67	**16618.56**
WR -NR765 kV Neemach - Chittorgarh D/C	0.00	35.36	144.70	146.03	83.75	151.18	89.57	0.00	0.00	2.06	0.00	0.00	**652.65**
Total WR - NR	**5270.72**	**9919.65**	**12110.97**	**10918.43**	**8635.14**	**7244.20**	**7216.20**	**5633.51**	**6190.42**	**7240.71**	**5042.23**	**4007.35**	**89429.53**
Export of NR to WR (NR-WR)													
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.80	36.80	**38.60**
NR - WR 765 kV Gwalior - Phagi 2xS/C	10.49	1.42	0.00	0.00	3.08	0.00	0.00	0.00	0.00	0.00	0.00	2.15	**17.14**
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.39	**22.39**
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Gwalior-Orai	245.97	283.52	291.19	326.07	242.25	309.77	368.54	423.95	433.38	445.77	406.98	357.03	**4134.42**
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	259.46	128.55	20.24	47.84	34.30	0.46	152.00	95.38	6.70	29.25	68.61	22.97	**865.76**
NR - WR 400 kV Zerda Kankroli	240.09	83.35	1.32	18.52	22.28	99.13	126.24	173.03	73.94	111.69	140.03	291.82	**1381.44**
NR - WR 400 kV Zerda Bhinmal	8.05	0.00	1.50	0.00	20.42	29.69	31.75	9.91	2.04	0.00	5.00	3.46	**111.82**
NR - WR 400 kV RAPP C - Shujalpur D/C	159.07	31.59	0.21	3.55	20.26	10.04	1.94	45.97	66.66	68.78	132.39	230.47	**770.93**
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	59.69	31.06	9.61	10.21	22.92	30.51	51.59	74.53	67.31	56.48	93.53	97.94	**605.38**
NR-WR 400 kV Rihand-Vindhyachal D/C	609.68	680.87	661.37	675.02	281.21	0.00	0.00	561.44	663.38	663.39	347.14	500.35	**5643.85**
NR - WR HVDC Mundra - Mohindergarh	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Banaskata-Chittorgarh D/C	463.90	132.00	0.70	25.41	20.28	519.20	391.69	523.07	148.17	268.25	434.86	773.67	**3701.20**
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	7.77	**7.77**
NR -WR765 kV Chittorgarh-Neemach D/C	139.03	35.99	2.22	7.43	9.25	1.42	0.00	51.46	94.50	73.95	145.46	227.58	**788.29**
Total NR - WR	**2195.43**	**1408.35**	**988.36**	**1114.05**	**676.25**	**1000.22**	**1123.75**	**1958.74**	**1556.08**	**1717.56**	**1775.80**	**2574.40**	**18088.99**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Mar'25	Fin. Year 2024-25
Name of Line													
Import of NR from ER (ER-NR)													
ER - NR 765 kV Sasaram - Fatehpur	111.08	133.89	160.45	97.00	78.42	81.31	139.89	211.26	229.72	252.28	274.76	185.81	**1955.87**
ER - NR 765 kV Gaya - Varanasi 2*S/C	50.67	114.34	92.48	120.98	110.05	165.33	405.62	482.45	443.73	383.69	452.05	207.04	**3028.43**
ER - NR 765 kV Gaya - Balia	213.79	293.69	320.79	327.83	302.52	334.00	366.56	351.78	368.50	379.86	251.30	159.76	**3670.38**
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00	344.72	465.66	383.97	250.72	211.75	12.40	0.00	0.00	0.00	**1669.22**
ER-NR 400 kV Patna - Balia D/C	192.05	288.47	317.66	235.85	237.58	352.17	527.53	418.43	523.23	391.61	388.63	324.49	**4197.70**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	3.14	135.70	339.63	320.97	278.98	253.48	319.38	212.80	260.15	218.85	112.60	21.91	**2477.59**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	10.98	26.88	8.44	15.12	43.67	95.04	41.13	143.70	118.35	39.80	1.05	**544.16**
ER - NR 400 kV Motihari - Gorakhpur D/C	63.12	164.75	249.69	181.64	149.89	166.48	259.86	222.85	283.52	223.81	170.64	129.71	**2265.96**
ER - NR 400 kV Biharshariff - Varanasi D/C	3.31	1.28	6.08	0.00	0.00	0.00	0.00	0.94	0.00	0.00	0.00	0.00	**11.61**
ER - NR 400 kV Sasaram -Varanasi	41.13	16.74	11.73	41.85	70.72	75.33	136.66	108.64	109.12	58.92	31.09	69.36	**771.29**
ER - NR 400 kV Sasaram -Allahabad	0.13	1.97	22.79	26.07	20.91	11.91	65.13	77.91	68.47	15.73	7.64	4.82	**323.48**
ER - NR 220 kV Sahupuri-Karamnasa	26.02	26.80	20.84	18.12	14.29	20.81	7.45	17.59	22.02	55.47	22.24	10.66	**262.31**
ER - NR 132 kV Sahupuri - Karamnasa	2.88	2.88	1.01	1.44	0.48	4.88	0.53	0.00	0.48	0.00	1.46	5.28	**21.32**
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.66**
ER - NR 132 kV Rihand - Garhwa	0.00	0.72	0.00	0.23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.95**
ER-NR 400 kV Naubatpur - Balia D/C	44.01	81.16	88.27	54.33	55.51	97.55	159.57	132.81	163.60	118.51	119.31	92.25	**1206.88**
ER-NR 400 kV Biharshriff - Sahupuri D/C	2.89	29.05	73.37	83.48	70.98	87.03	144.05	156.95	159.21	103.16	157.12	74.64	**1141.93**
Total ER-NR	**754.22**	**1303.08**	**1731.67**	**1862.95**	**1871.11**	**2077.92**	**2877.99**	**2647.29**	**2787.85**	**2320.24**	**2028.64**	**1286.78**	23549.74
Import of NR from NER (NER-NR)													
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00	371.98	270.26	454.55	555.71	550.01	30.48	0.00	0.00	0.00	**2232.99**
Total NER - NR	**0.00**	**0.00**	**0.00**	**371.98**	**270.26**	**454.55**	**555.71**	**550.01**	**30.48**	**0.00**	**0.00**	**0.00**	2232.99
Export of NR to ER (NR-ER)													
NR - ER 765 kV Sasaram - Fatehpur	0.00	0.46	0.00	0.40	6.31	14.15	0.00	0.00	0.00	0.00	0.00	0.00	**21.32**
NR - ER 765 kV Gaya - Varanasi 2*S/C	65.96	56.17	23.53	10.09	20.05	49.37	0.00	0.00	0.00	0.00	0.00	22.37	**247.54**
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	87.39	32.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	45.96	**165.76**
NR - ER 400 kV Biharshariff - Balia D/C	148.68	86.56	34.72	43.49	42.52	37.82	7.00	8.26	0.00	0.00	1.66	90.60	**501.31**
ER - NR 400 kV Motihari - Gorakhpur D/C	0.29	1.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.30**
NR - ER 400 kV Biharshariff - Varanasi D/C	19.06	0.00	0.00	0.00	0.00	0.00	0.00	0.88	0.00	0.00	0.00	0.00	**19.94**
NR - ER 400 kV Sasaram -Varanasi	0.00	2.63	4.50	0.00	0.00	0.00	0.00	0.20	0.00	0.00	0.00	0.00	**7.33**
NR - ER 400 kV Sasaram -Allahabad	10.41	12.82	11.40	0.10	2.76	7.25	0.00	0.00	0.00	3.47	3.10	3.94	**55.25**
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	1.38	2.28	0.00	4.74	0.65	0.00	0.00	0.38	1.29	**10.72**
NR - ER 132 kV Sahupuri - Karamnasa	1.44	1.23	0.00	0.00	0.00	0.11	0.48	0.00	0.60	0.00	0.00	0.48	**4.34**
NR - ER 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.92	0.33	1.70	1.32	0.58	0.91	1.34	1.87	1.64	0.76	**11.37**
ER - NR 132 kV Rihand - Garhwa	18.99	19.86	16.50	16.68	12.80	14.53	14.57	14.82	16.20	17.43	15.46	17.84	**195.68**
NR-ER 400 kV Balia- Naubatpur D/C	0.00	1.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**1.31**
NR-ER 400 kV Sahupuri- Biharshariff D/C	0.00	1.60	2.33	1.30	1.00	0.31	0.00	0.00	0.00	0.00	0.00	15.13	**21.67**
Total NR - ER	**352.22**	**216.06**	**93.90**	**73.77**	**89.42**	**124.86**	**27.37**	**25.72**	**18.14**	**22.77**	**22.24**	**198.37**	1264.84
Export of NR to NER (NER-NR)													
NR-NER HVDC Biswanath Chariali - Agra	433.33	466.77	450.41	15.02	0.00	0.00	0.00	0.00	445.16	486.19	441.54	610.46	**3348.88**
Total NR - NER	**433.33**	**466.77**	**450.41**	**15.02**	**0.00**	**0.00**	**0.00**	**0.00**	**445.16**	**486.19**	**441.54**	**610.46**	3348.88

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Mar'25	Fin. Year 2024-25
Name of Line													
Export of WR to ER (WR-ER)													
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	388.72	751.76	1168.90	1091.31	747.98	793.25	308.09	84.78	53.41	160.01	16.05	75.10	**5639.36**
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	721.67	524.74	158.97	147.48	110.03	63.29	65.67	50.80	64.41	152.97	272.20	238.44	**2570.65**
WR - ER 765 kV Durg - Jharsuguda D/C	0.05	1.25	9.28	8.12	8.20	10.21	0.04	0.00	0.00	0.00	0.00	0.00	**37.15**
WR - ER 400 kV Sipat - Ranchi D/C	51.26	216.17	285.29	228.90	132.26	140.01	29.14	9.49	3.76	24.77	1.72	9.76	**1132.51**
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	3.12	46.71	321.05	240.61	28.29	9.88	0.51	1.58	0.03	0.03	0.00	0.02	**651.83**
WR - ER 220 kV Korba - Budhipadar D/C	8.86	26.39	12.71	1.56	4.06	1.82	4.23	14.85	12.46	29.24	14.43	9.58	**140.20**
WR - ER 220 kV Raigarh - Budhipadar	7.90	2.55	1.47	0.43	2.41	0.20	0.05	0.60	0.00	0.01	0.12	0.35	**16.08**
Total WR - ER	**1181.58**	**1569.56**	**1957.67**	**1718.40**	**1033.22**	**1018.66**	**407.73**	**162.10**	**134.08**	**367.02**	**304.52**	**333.25**	**10187.79**
Import of WR from ER (ER - WR)													
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	48.43	15.64	0.11	0.81	5.93	39.73	68.03	111.05	218.28	108.43	361.11	325.15	**1302.70**
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	2.75	169.79	403.73	491.76	175.21	490.66	334.28	233.51	328.11	139.52	88.44	94.20	**2951.96**
ER - WR 765 kV Durg - Jharsuguda D/C	376.32	377.94	175.66	129.22	129.22	224.89	325.55	520.92	389.23	539.53	582.66	554.73	**4325.87**
ER - WR 400 kV Sipat - Ranchi D/C	22.01	4.57	0.14	0.92	9.58	26.30	59.96	84.87	42.89	57.42	116.14	127.00	**551.79**
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	195.37	120.88	235.08	300.81	167.11	240.04	380.72	297.88	324.60	320.44	384.61	373.30	**3340.83**
ER - WR 220 kV Korba - Budhipadar D/C	1.27	8.92	26.67	47.83	38.33	56.53	48.12	15.83	17.45	7.12	10.91	31.00	**309.98**
ER - WR 220 kV Raigarh - Budhipadar	15.69	25.32	47.74	55.61	15.46	54.49	60.23	34.62	45.32	42.62	35.98	54.78	**487.87**
Total ER - WR	**661.85**	**723.06**	**889.13**	**1026.96**	**540.85**	**1132.63**	**1276.89**	**1298.67**	**1365.88**	**1215.08**	**1579.84**	**1560.14**	**13270.99**
Export of ER to NER (ER - NER)													
ER - NER 400 kV Binaguri - Bongaigaon D/C	20.06	23.09	0.13	105.85	109.75	207.98	104.89	226.52	18.80	7.46	4.51	10.70	**839.74**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	16.74	47.75	0.06	174.13	146.64	335.46	173.82	295.36	19.99	7.41	2.13	7.89	**1227.39**
ER - NER 220 kV Birpara - Salakati D/C	2.74	6.73	0.18	40.66	37.80	71.76	32.38	44.04	2.57	0.68	0.02	0.35	**239.90**
Total ER - NER	**39.54**	**77.57**	**0.38**	**320.64**	**294.19**	**615.19**	**311.10**	**565.92**	**41.35**	**15.55**	**6.66**	**18.95**	**2307.03**
Import of ER from NER (NER - ER)													
NER - ER 400 kV Binaguri - Bongaigaon D/C	79.80	122.93	220.43	26.32	3.04	0.26	18.09	0.00	87.66	87.40	75.85	77.07	**798.85**
NER - ER 400 kV Alipurduar - Bongaigaon D/C	164.15	208.72	302.14	30.00	8.53	0.00	17.26	0.00	183.94	165.91	148.37	139.02	**1368.05**
NER - ER 220 kV Birpara - Salakati D/C	18.58	38.63	53.31	5.56	0.61	0.00	2.72	0.00	38.42	37.89	41.90	38.51	**276.13**
Total NER - ER	**262.52**	**370.28**	**575.88**	**61.88**	**12.19**	**0.26**	**38.07**	**0.00**	**310.02**	**291.19**	**266.13**	**254.60**	**2443.03**

	Apr'24	May'24	June'24	July'24	Aug'24	Sep'24	Oct'24	Nov'24	Dec'24	Jan'25	Feb'25	Mar'25	Fin. Year 2024-25
Name of Line													
Export of ER to SR (ER - SR)													
ER - SR HVDC Gazuwaka	413.69	249.41	22.79	26.22	262.06	265.65	217.59	323.46	231.29	195.73	252.18	439.09	**2899.15**
ER - SR HVDC Talchar - Kolar	1069.04	1104.35	1220.43	999.65	918.13	203.86	1105.23	1090.58	1197.54	997.29	1098.40	1238.70	**12243.20**
ER - SR 765 kV Angul- Srikakulam D/C	1640.93	1313.30	1089.30	1030.39	1100.43	1064.60	1297.13	1542.96	1693.06	1529.00	1505.81	1820.32	**16627.23**
Total ER - SR	**3123.66**	**2667.05**	**2332.52**	**2056.26**	**2280.62**	**1534.11**	**2619.95**	**2957.00**	**3121.89**	**2722.02**	**2856.39**	**3498.11**	**31769.58**
Import of ER from SR (SR - ER)													
SR - ER HVDC Gazuwaka	0.00	16.28	175.68	241.91	21.93	35.11	0.00	0.00	0.00	0.00	0.00	0.00	**490.91**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	0.00	0.00	0.00	0.00	**0.01**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total SR - ER	**0.00**	**16.28**	**175.68**	**241.91**	**21.93**	**35.12**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**490.93**
Export of WR to SR (WR-SR)													
WR - SR HVDC Bhadrawati	601.92	221.20	27.24	0.00	176.88	188.65	231.23	335.29	602.14	331.42	580.23	680.67	**3976.87**
WR - SR 765 kV Sholapur - Raichur 2xS/C	802.05	292.07	41.83	26.71	70.59	88.01	37.08	143.60	280.25	211.67	311.16	415.80	**2720.82**
WR - SR 765 kV Wardha - Nizamabad D/C	1407.32	763.52	504.48	602.22	932.26	588.28	590.95	779.18	1057.49	959.23	1151.75	1474.65	**10811.33**
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.02	0.00	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	0.06	**0.09**
WR-SR HVDC Raigarh-Pugalur	2668.37	1464.59	692.13	375.04	559.27	557.38	574.81	746.92	1396.79	1175.06	1806.06	3384.00	**15400.43**
WR-SR 220kV Xeldem - Ambewadi S/C	73.01	75.81	61.15	50.36	63.71	65.88	72.89	67.59	70.47	68.17	63.41	73.10	**805.55**
WR-SR 220kV Ponda - Ambewadi S/C	43.06	54.26	44.46	5.32	0.08	0.04	0.03	2.33	0.06	6.57	2.36	1.22	**159.78**
WR-SR 765 kV Warora - Warangal D/C	1603.13	954.21	557.06	549.21	810.28	602.35	686.47	951.98	1160.41	1022.37	1258.67	1516.46	**11672.61**
Total WR - SR	**7198.86**	**3825.69**	**1928.36**	**1608.85**	**2613.07**	**2090.59**	**2193.47**	**3026.89**	**4567.60**	**3774.49**	**5173.64**	**7545.96**	**45547.48**
Import of WR from SR (SR - WR)													
SR - WR HVDC Bhadrawati	2.36	182.40	422.51	566.72	209.29	233.01	18.75	0.00	0.00	20.04	0.00	0.00	**1655.07**
SR - WR 765 kV Raichur - Sholapur 2xS/C	0.55	262.88	727.33	826.50	434.69	553.25	410.23	148.25	152.27	240.55	125.15	63.72	**3945.39**
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	6.86	32.86	33.19	6.41	66.92	11.46	0.85	0.04	3.92	0.74	0.27	**163.52**
SR - WR 400KV Kolhapur-Kudgi D/C	429.02	646.95	994.86	1212.56	957.87	997.65	948.20	690.35	704.16	814.52	647.43	612.19	**9655.76**
SR-WR HVDC Pugalur-Raigarh	0.00	0.00	22.86	291.64	48.31	55.86	0.00	0.00	0.00	0.00	0.00	0.00	**418.67**
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00	0.00	0.01	0.01	0.02	0.01	0.01	0.02	0.02	0.01	**0.12**
SR-WR 765 kV Warangal - Warora D/C	0.00	6.90	27.23	50.82	11.61	62.04	6.77	0.01	0.06	1.54	0.04	0.14	**167.16**
Total SR - WR	**431.93**	**1105.99**	**2227.65**	**2981.43**	**1668.19**	**1968.74**	**1395.43**	**839.47**	**856.54**	**1080.59**	**773.38**	**676.34**	**16005.69**
TOTAL ALL INDIA	**21906**	**23669**	**25463**	**24373**	**20006**	**19297**	**20044**	**19665**	**21426**	**21253**	**20271**	**22565**	**259937**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

15.1 Import-Export of NR with WR during March 2025

Import of NR from WR (WR-NR)

Date	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Neemach - Chittorgarh D/C	Total WR - NR
1-Mar-25	1.87	8.83	5.38	15.08	0.00	35.33	0.20	0.00		0.00	2.29	2.86	0.00	0.00	18.19	0.00	21.14	0.00	**111.17**
2-Mar-25	0.00	5.09	0.27	10.17	0.00	29.81	1.23	0.00		0.00	2.27	2.87	0.00	0.00	17.47	0.00	11.15	0.00	**80.33**
3-Mar-25	0.00	4.69	0.00	10.55	0.00	31.54	1.25	0.00		0.00	2.26	2.83	0.00	0.00	24.21	0.00	0.00	0.00	**77.33**
4-Mar-25	0.00	0.23	0.00	13.43	0.00	32.57	3.10	0.00		0.00	2.15	2.70	0.00	0.00	26.11	0.00	12.33	0.00	**92.62**
5-Mar-25	0.00	1.48	0.00	12.82	0.00	35.00	5.95	0.00		0.00	2.19	2.67	0.00	0.00	28.60	0.00	9.95	0.00	**98.66**
6-Mar-25	1.26	9.89	2.15	11.71	0.00	29.79	6.30	0.00		0.00	2.14	2.67	0.00	0.00	24.35	0.00	0.00	0.00	**90.26**
7-Mar-25	5.57	12.21	8.16	15.48	0.00	34.52	5.96	0.00		0.00	2.17	2.57	0.00	0.00	26.17	0.00	13.92	0.00	**126.73**
8-Mar-25	0.36	11.35	3.57	15.43	0.00	63.95	2.62	0.00		0.00	2.13	2.70	0.00	0.00	31.50	0.00	16.92	0.00	**150.53**
9-Mar-25	0.00	8.00	1.24	11.00	0.00	88.37	1.92	0.00		0.00	2.09	2.78	0.00	0.00	34.73	0.00	2.75	0.00	**152.88**
10-Mar-25	3.10	13.72	7.71	15.49	0.00	87.50	5.94	0.00		0.00	2.72	2.01	0.00	0.00	36.28	0.00	21.02	0.00	**195.49**
11-Mar-25	7.96	16.41	11.53	17.40	0.00	58.40	6.01	0.00	0.00	0.00	2.08	2.59	0.00	0.00	36.28	0.00	21.69	0.00	**180.35**
12-Mar-25	0.92	9.69	4.57	15.02	0.00	71.02	4.28	0.00		0.00	1.94	2.60	0.00	0.00	46.79	0.00	16.33	0.00	**173.16**
13-Mar-25	0.00	4.74	0.00	14.69	0.00	75.46	0.00	0.00		0.00	1.68	2.35	0.00	0.00	53.87	0.00	24.46	0.00	**177.25**
14-Mar-25	0.00	0.00	6.50	11.60	0.00	39.39	0.00	0.00		0.00	1.34	2.11	0.00	0.00	51.51	0.00	21.77	0.00	**134.22**
15-Mar-25	0.00	6.14	0.00	12.24	0.00	28.47	0.00	0.00		0.00	1.47	2.17	0.00	0.00	36.27	0.00	19.15	0.00	**105.91**
16-Mar-25	0.93	8.26	0.54	14.47	0.00	32.31	0.00	0.00		0.00	1.64	2.30	0.00	0.00	36.28	0.00	22.48	0.00	**119.21**
17-Mar-25	0.20	8.72	0.00	15.03	0.00	35.35	0.00	0.00		0.00	0.22	2.14	0.00	0.00	36.28	0.00	22.25	0.00	**120.19**
18-Mar-25	0.37	6.22	1.17	14.93	0.00	33.56	0.00	0.00		0.00	1.18	1.97	0.00	0.00	36.28	0.00	23.96	0.00	**119.64**
19-Mar-25	0.45	2.29	0.00	14.64	0.00	53.21	0.00	0.00		0.00	1.35	1.94	0.00	0.00	36.28	0.00	28.00	0.00	**138.16**
20-Mar-25	3.97	4.97	0.82	15.73	0.00	40.13	0.00	0.00		0.00	1.42	2.00	0.00	0.00	36.27	0.00	24.25	0.00	**129.56**
21-Mar-25	0.78	7.10	0.00	15.50	0.00	50.59	0.00	0.00		0.00	1.50	2.45	0.00	0.00	36.33	0.00	18.38	0.00	**132.63**
22-Mar-25	10.10	12.50	7.41	17.82	0.00	26.23	0.00	0.00		0.00	1.30	2.39	0.00	0.00	43.52	0.00	23.01	0.00	**144.28**
23-Mar-25	8.25	10.96	6.19	16.52	0.00	27.85	0.00	0.00		0.00	1.24	2.39	0.00	0.00	24.23	0.00	23.85	0.00	**121.48**
24-Mar-25	2.76	9.65	1.34	15.96	0.00	56.10	0.00	0.00		0.00	1.37	2.39	0.00	0.00	39.35	0.00	24.65	0.00	**153.57**
25-Mar-25	2.62	6.13	1.26	15.49	0.00	44.42	0.00	0.00		0.00	1.43	2.46	0.00	0.00	40.69	0.00	25.57	0.00	**140.07**
26-Mar-25	1.55	4.40	0.34	14.62	0.00	46.72	0.00	0.00		0.00	1.50	2.52	0.00	0.00	36.27	0.00	29.40	0.00	**137.32**
27-Mar-25	6.50	1.60	3.68	14.27	0.00	38.96	0.81	0.00		0.00	1.32	2.60	0.00	0.00	33.78	0.00	33.05	0.00	**136.57**
28-Mar-25	6.87	1.10	2.42	14.37	0.00	23.21	1.25	0.00		0.00	0.97	2.19	0.00	0.00	29.59	0.00	40.00	0.00	**121.97**
29-Mar-25	5.92	0.65	1.91	14.33	0.00	23.14	1.24	0.00		0.00	1.01	2.35	0.00	0.00	36.30	0.00	39.04	0.00	**125.89**
30-Mar-25	0.72	0.86	0.00	12.99	0.00	23.14	1.25	0.00		0.00	1.29	2.21	0.00	0.00	35.67	0.00	32.50	0.00	**110.63**
31-Mar-25	4.36	2.87	0.00	13.87	0.00	23.36	1.24	0.00		0.00	1.27	2.34	0.00	0.00	24.28	0.00	35.70	0.00	**109.29**
Total	**77.39**	**200.75**	**78.16**	**442.65**	**0.00**	**1319.40**	**50.55**	**0.00**	**0.00**	**0.00**	**50.93**	**75.12**	**0.00**	**0.00**	**1053.73**	**0.00**	**658.67**	**0.00**	**4007.35**

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

15.1 Import-Export of NR with WR during March 2025

Export of NR to WR (NR- WR)

Date	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa-Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda-Kankroli	NR - WR 400 kV Zerda-Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand-Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi-Vindhyachal	WR -NR 765 kV Chittorgarh-Neemach D/C	Total NR - WR
1-Mar-25	0.00	0.00	0.00	0.00	12.31	0.00	4.05	6.10		6.70	0.00	0.00	3.94	11.08	0.00	16.61	0.00	7.33	**68.12**
2-Mar-25	6.25	0.00	0.00	0.00	10.84	0.00	0.00	7.29		8.46	0.00	0.00	4.34	10.65	0.00	21.05	0.00	9.19	**78.07**
3-Mar-25	7.57	0.00	2.21	0.00	11.41	0.00	0.00	7.25		8.90	0.00	0.00	4.40	11.16	0.00	18.61	2.57	9.28	**83.36**
4-Mar-25	1.87	0.00	2.21	0.00	9.38	0.00	0.00	2.78		8.97	0.00	0.00	3.90	10.84	0.00	0.57	0.00	10.70	**51.22**
5-Mar-25	2.00	0.00	4.10	0.00	10.50	0.00	0.00	4.30		8.60	0.00	0.00	4.11	10.41	0.00	6.90	0.00	9.85	**60.77**
6-Mar-25	0.00	0.00	0.00	0.00	13.33	0.00	0.00	9.70		7.17	0.00	0.00	4.39	10.98	0.00	28.65	5.20	7.25	**86.67**
7-Mar-25	0.00	0.00	0.00	0.00	14.15	0.00	0.00	9.27		5.89	0.00	0.00	3.68	10.92	0.00	27.54	0.00	5.89	**77.34**
8-Mar-25	0.00	0.00	0.00	0.00	13.35	0.00	0.59	9.10		5.76	0.00	0.00	3.77	10.65	0.00	27.86	0.00	5.25	**76.33**
9-Mar-25	5.05	0.00	0.00	0.00	12.75	0.00	0.00	9.25		6.68	0.00	0.00	4.05	11.08	0.00	26.51	0.00	5.90	**81.27**
10-Mar-25	0.00	0.00	0.00	0.00	13.35	0.00	0.00	9.84		5.06	0.00	0.00	3.50	10.95	0.00	29.19	0.00	4.41	**76.30**
11-Mar-25	0.00	0.00	0.00	0.00	14.04	0.00	0.00	5.01	3.46	4.59	0.00	0.00	3.26	11.07	0.00	22.86	0.00	4.78	**69.07**
12-Mar-25	0.00	0.00	0.00	0.00	12.54	0.00	0.63	8.30		6.30	0.00	0.00	3.68	10.80	0.00	22.03	0.00	6.55	**70.83**
13-Mar-25	1.25	0.00	0.20	0.00	11.10	0.00	1.24	9.30		7.37	0.00	0.00	3.45	10.76	0.00	20.98	0.00	7.30	**72.95**
14-Mar-25	5.12	2.15	0.00	0.00	9.92	0.00	1.25	7.80		8.77	0.00	0.00	3.33	10.06	0.00	14.52	0.00	7.98	**70.90**
15-Mar-25	7.69	0.00	5.32	0.00	13.10	0.00	1.25	13.76		8.50	0.00	0.00	3.90	10.81	0.00	38.47	0.00	7.93	**110.73**
16-Mar-25	0.00	0.00	0.00	0.00	12.78	0.00	1.25	12.00		6.94	0.00	0.00	3.31	16.14	0.00	30.92	0.00	6.17	**89.51**
17-Mar-25	0.00	0.00	1.19	0.00	12.09	0.00	1.25	10.68		7.85	0.00	0.00	3.14	22.31	0.00	29.56	0.00	6.87	**94.94**
18-Mar-25	0.00	0.00	0.00	0.00	11.11	0.00	1.20	10.35		7.67	0.00	0.00	3.06	21.75	0.00	27.14	0.00	7.15	**89.43**
19-Mar-25	0.00	0.00	2.88	0.00	10.22	0.00	1.25	10.00		7.32	0.00	0.00	2.95	18.16	0.00	24.45	0.00	7.45	**84.68**
20-Mar-25	0.00	0.00	0.00	0.00	10.90	0.00	1.26	10.30		0.40	0.00	0.00	1.90	22.29	0.00	24.50	0.00	8.01	**79.56**
21-Mar-25	0.00	0.00	1.26	0.00	11.21	0.00	1.26	10.62		8.44	0.00	0.00	2.71	22.47	0.00	28.66	0.00	7.33	**93.96**
22-Mar-25	0.00	0.00	0.00	0.00	12.25	0.00	1.25	9.57		6.02	0.00	0.00	1.74	21.58	0.00	25.24	0.00	5.75	**83.40**
23-Mar-25	0.00	0.00	0.00	0.00	11.32	0.00	1.24	8.04		5.32	0.00	0.00	2.34	21.22	0.00	20.82	0.00	5.40	**75.70**
24-Mar-25	0.00	0.00	0.00	0.00	12.06	0.00	1.26	12.50		7.86	0.00	0.00	1.75	22.35	0.00	34.42	0.00	7.10	**99.30**
25-Mar-25	0.00	0.00	0.00	0.00	11.44	0.00	1.03	13.09		8.95	0.00	0.00	2.70	22.16	0.00	36.12	0.00	8.35	**103.84**
26-Mar-25	0.00	0.00	0.00	0.00	10.42	0.00	1.27	12.60		9.70	0.00	0.00	2.50	22.34	0.00	31.54	0.00	8.40	**98.77**
27-Mar-25	0.00	0.00	0.00	0.00	9.92	0.00	0.44	10.70		9.70	0.00	0.00	3.20	22.30	0.00	28.42	0.00	7.83	**92.51**
28-Mar-25	0.00	0.00	0.00	0.00	9.59	0.00	0.00	10.20		7.00	0.00	0.00	2.15	21.10	0.00	26.00	0.00	7.30	**83.34**
29-Mar-25	0.00	0.00	0.00	0.00	9.09	0.00	0.00	10.11		9.48	0.00	0.00	2.03	21.03	0.00	24.70	0.00	7.70	**84.14**
30-Mar-25	0.00	0.00	2.99	0.00	9.76	0.00	0.00	11.21		10.38	0.00	0.00	2.51	19.95	0.00	29.63	0.00	8.70	**95.13**
31-Mar-25	0.00	0.00	0.03	0.00	10.80	0.00	0.00	10.80		9.72	0.00	0.00	2.25	20.98	0.00	29.20	0.00	8.48	**92.26**
Total	**36.80**	**2.15**	**22.39**	**0.00**	**357.03**	**0.00**	**22.97**	**291.82**	**3.46**	**230.47**	**0.00**	**0.00**	**97.94**	**500.35**	**0.00**	**773.67**	**7.77**	**227.58**	**2574.40**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during March 2025

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	ER-NR 400 kV Biharshriff - Sahupuri D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Mar-25	7.95	10.38	6.76		10.56	0.62	0.00	4.08		1.84	0.39	0.46	0.00	0.00	0.00	3.12	3.76	**49.92**	0.00	**0.00**
2-Mar-25	6.90	9.99	5.25		9.73	0.18	0.00	3.61		2.35	0.00	0.25		0.00	0.00	2.75	3.38	**44.39**	0.00	**0.00**
3-Mar-25	8.16	12.14	4.74		11.60	0.10	0.00	4.56		2.45	0.00	0.48			0.00	3.43	3.57	**51.23**	0.00	**0.00**
4-Mar-25	6.55	6.73	4.16		11.79	0.00	0.00	4.32		2.20	0.16	0.10			0.00	3.39	2.22	**41.62**	0.00	**0.00**
5-Mar-25	5.31	5.84	3.25		10.46	0.00	0.00	3.42		2.38	0.00	0.10	0.00	0.00	0.00	3.16	0.95	**34.87**	0.00	**0.00**
6-Mar-25	7.55	13.39	5.15		13.15	0.00	0.00	5.09		2.38	0.15	0.48	0.00	0.00	0.00	4.07	4.15	**55.56**	0.00	**0.00**
7-Mar-25	8.35	11.79	7.36		13.71	1.88	0.00	5.94		2.19	0.10	0.50			0.00	4.00	3.24	**59.06**	0.00	**0.00**
8-Mar-25	8.66	12.03	7.34		14.44	3.22	0.00	6.85		1.77	0.00	0.46	0.00	0.00	0.00	4.38	3.99	**63.14**	0.00	**0.00**
9-Mar-25	7.25	12.65	6.29		13.29	1.12	0.00	5.60		2.29	0.00	0.25			0.00	3.97	3.60	**56.31**	0.00	**0.00**
10-Mar-25	8.05	11.60	7.30		14.26	1.57	0.00	6.79		2.21	0.20	0.40		0.00	0.00	4.27	3.85	**60.50**	0.00	**0.00**
11-Mar-25	8.83	10.87	7.78		13.47	0.57	0.00	5.20		2.06	0.11	0.50			0.00	4.03	4.01	**57.43**	0.00	**0.00**
12-Mar-25	7.41	10.36	6.36		12.30	1.12	0.00	4.77		2.28	0.00	0.24	0.00		0.00	3.72	3.07	**51.63**	0.00	**0.00**
13-Mar-25	5.57	5.78	5.32		11.97	0.00	0.00	4.71		2.32	0.07	0.20	0.00		0.00	3.46	2.58	**41.98**	0.00	**0.00**
14-Mar-25	2.45	0.49	2.59		8.31	0.00	0.00	3.46		2.38	0.00	0.48	4.80		0.00	2.21	0.58	**27.75**	0.00	**0.00**
15-Mar-25	2.96	1.59	2.14		7.47	2.35	0.00	3.78		2.30	0.00	0.06	0.00		0.00	1.91	0.65	**25.21**	0.00	**0.00**
16-Mar-25	4.75	4.03	3.55		8.44	0.00	0.00	4.15		2.00	0.30	0.13	0.00	0.00	0.00	2.53	2.15	**32.03**	0.00	**0.00**
17-Mar-25	5.31	6.06	4.35		11.03	0.00	0.00	4.85		1.92	0.26	0.21	0.00	0.00	0.00	3.09	2.10	**39.18**	0.00	**0.00**
18-Mar-25	5.74	5.40	5.35		10.81	0.00	0.00	4.26		1.94	0.35		0.48		0.00	3.11	2.78	**40.22**	0.00	**0.00**
19-Mar-25	4.14	0.51	4.07		8.10	0.00	0.00	2.81		2.29	0.05	0.00	0.00		0.00	2.10	0.72	**24.79**	0.00	**0.00**
20-Mar-25	6.60	4.70	4.72		10.20	0.00	0.00	4.28		1.85	0.62	0.21	0.00		0.00	2.90	3.31	**39.39**	0.00	**0.00**
21-Mar-25	8.16	10.72	6.77		11.99	0.23	0.00	5.43		2.01	0.21	0.97			0.00	3.78	4.08	**54.35**	0.00	**0.00**
22-Mar-25	9.85	13.18	8.71		15.71	3.55	0.20	5.95		1.41	0.80	1.17			0.00	4.90	5.20	**70.63**	0.00	**0.00**
23-Mar-25	8.52	12.69	7.71		13.56	4.29	0.85	5.43		1.55	0.85	0.95			0.00	4.14	5.42	**65.96**	0.00	**0.00**
24-Mar-25	7.50	8.91	7.10		9.81	1.11	0.00	4.15		2.04	0.20	0.65	0.00		0.00	1.65	3.52	**46.64**	0.00	**0.00**
25-Mar-25	5.17	4.96	5.83		8.46	0.00	0.00	3.24		2.51	0.00	0.48	0.00		0.00	2.08	1.76	**34.49**	0.00	**0.00**
26-Mar-25	4.40	0.25	4.61		5.72	0.00	0.00	2.16		2.60	0.00	0.03	0.00		0.00	1.27	0.00	**21.04**	0.00	**0.00**
27-Mar-25	3.90	0.00	4.47		6.40	0.00	0.00	2.42		2.94	0.00	0.60			0.00	1.50	0.00	**22.23**	0.00	**0.00**
28-Mar-25	3.09	0.00	1.13		7.25	0.00	0.00	1.96		2.78	0.00	0.30			0.00	1.69	0.00	**18.20**	0.00	**0.00**
29-Mar-25	3.58	0.00	3.36		6.94	0.00	0.00	1.95		2.85	0.00	0.00	0.00		0.00	1.53	0.00	**20.21**	0.00	**0.00**
30-Mar-25	1.42	0.00	2.75		6.31	0.00	0.00	1.84		2.67	0.00	0.00	0.00		0.00	2.31	0.00	**17.30**	0.00	**0.00**
31-Mar-25	1.73	0.00	3.49		7.25	0.00	0.00	2.65		2.60	0.00	0.00	0.00		0.00	1.80	0.00	**19.52**	0.00	**0.00**
Total	**185.81**	**207.04**	**159.76**	**0.00**	**324.49**	**21.91**	**1.05**	**129.71**	**0.00**	**69.36**	**4.82**	**10.66**	**5.28**	**0.00**	**0.00**	**92.25**	**74.64**	**1286.78**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during March 2025

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri Karamnasa	NR - ER 132 kV Rihand -Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	NR-ER 400 kV Sahupuri-Biharshariff D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Mar-25	0.00	0.00	0.00		0.00	0.00	0.95	0.00		0.00	0.00	0.00	0.00	0.09	0.70	0.00	0.00	1.74	17.14	17.14
2-Mar-25	0.00	0.00	0.00		0.00	0.00	1.01	0.00		0.00	0.16	0.00		0.08	0.71	0.00	0.00	1.96	16.65	16.65
3-Mar-25	0.00	0.00	0.00		0.00	0.00	0.99	0.00		0.00	0.07	0.00			0.71	0.00	0.00	1.77	17.07	17.07
4-Mar-25	0.00	0.00	0.00		0.00	1.30	2.61	0.00		0.00	0.00	0.00			0.72	0.00	0.00	4.63	16.67	16.67
5-Mar-25	0.00	0.00	0.00		0.00	2.69	3.40	0.00		0.00	0.13	0.00	0.00	0.07	0.51	0.00	0.00	6.80	16.68	16.68
6-Mar-25	0.00	0.00	0.00		0.00	0.40	1.40	0.00		0.00	0.00	0.00	0.00	0.09	0.59	0.00	0.00	2.48	16.42	16.42
7-Mar-25	0.00	0.00	0.00		0.00	0.00	0.68	0.00		0.00	0.00	0.00			0.30	0.00	0.00	0.98	16.42	16.42
8-Mar-25	0.00	0.00	0.00		0.00	0.00	0.45	0.00		0.00	0.15	0.00	0.00	0.14	0.28	0.00	0.00	1.02	16.33	16.33
9-Mar-25	0.00	0.00	0.00		0.00	0.00	1.62	0.00		0.00	0.07	0.00			0.55	0.00	0.00	2.24	17.33	17.33
10-Mar-25	0.00	0.00	0.00		0.00	0.00	1.74	0.00		0.00	0.00	0.00		0.09	0.60	0.00	0.00	2.43	16.67	16.67
11-Mar-25	0.00	0.00	0.00		0.00	0.00	1.74	0.00		0.00	0.00	0.00			0.57	0.00	0.00	2.31	17.12	17.12
12-Mar-25	0.00	0.00	0.00		0.00	0.00	2.51	0.00		0.00	0.11	0.00	0.00		0.61	0.00	0.00	3.23	16.68	16.68
13-Mar-25	0.00	0.00	0.00		0.00	1.11	2.91	0.00		0.00	0.00	0.00	0.00		0.61	0.00	0.00	4.63	17.45	17.45
14-Mar-25	0.00	0.00	0.00		0.00	1.36	3.81	0.00		0.00	0.10	0.00	0.00		0.63	0.00	0.00	5.90	16.75	16.75
15-Mar-25	0.00	0.00	0.00		0.00	0.00	5.43	0.00		0.00	0.10	0.00	0.00		0.63	0.00	0.00	6.16	16.07	16.07
16-Mar-25	0.00	0.00	0.00		0.00	1.37	4.09	0.00		0.00	0.00	0.00	0.00	0.11	0.63	0.00	0.00	6.20	16.82	16.82
17-Mar-25	0.00	0.00	0.00		0.00	1.50	4.27	0.00		0.00	0.00	0.00	0.00	0.09	0.61	0.00	0.00	6.47	16.85	16.85
18-Mar-25	0.00	0.00	0.00		0.00	2.19	3.48	0.00		0.00	0.00		0.00		0.62	0.00	0.61	6.90	16.78	16.78
19-Mar-25	0.00	0.00	0.00		0.00	4.59	5.12	0.00		0.00	0.00	0.18	0.00		0.62	0.00	0.00	10.51	19.69	19.69
20-Mar-25	0.00	0.00	0.00		0.00	1.97	3.50	0.00		0.00	0.00	0.00	0.00		0.43	0.00	0.64	6.54	24.29	24.29
21-Mar-25	0.00	0.00	0.00		0.00	0.00	1.87	0.00		0.00	0.00	0.00			0.30	0.00	0.00	2.17	23.25	23.25
22-Mar-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.36	0.00	0.00	0.36	24.20	24.20
23-Mar-25	0.00	0.00	0.00		0.00	0.00	0.00	0.00		0.00	0.00	0.00			0.44	0.00	0.00	0.44	24.17	24.17
24-Mar-25	0.00	0.00	0.00		0.00	0.00	1.07	0.00		0.00	0.00	0.00	0.00		0.64	0.00	0.00	1.71	23.72	23.72
25-Mar-25	0.00	0.00	0.00		0.00	0.87	2.54	0.00		0.00	0.30	0.00	0.00		0.64	0.00	0.00	4.35	23.95	23.95
26-Mar-25	0.00	0.00	0.00		0.00	2.68	3.75	0.00		0.00	0.33	0.00	0.00		0.61	0.00	1.68	9.05	24.07	24.07
27-Mar-25	0.00	2.11	0.00		0.00	3.25	4.42	0.00		0.00	0.50	0.00			0.61	0.00	6.30	17.19	24.25	24.25
28-Mar-25	0.00	6.51	0.00		0.00	5.11	6.27	0.00		0.00	0.58	0.00			0.66	0.00	1.39	20.52	23.98	23.98
29-Mar-25	0.00	5.07	0.00		0.00	5.82	6.85	0.00		0.00	0.48	0.48	0.00		0.66	0.00	1.65	21.01	23.74	23.74
30-Mar-25	0.00	4.81	0.00		0.00	5.54	6.42	0.00		0.00	0.50	0.15	0.00		0.65	0.00	1.96	20.03	23.65	23.65
31-Mar-25	0.00	3.87	0.00		0.00	4.21	5.70	0.00		0.00	0.36	0.48	0.48		0.64	0.00	0.90	16.64	25.60	25.60
Total	**0.00**	**22.37**	**0.00**	**0.00**	**0.00**	**45.96**	**90.60**	**0.00**	**0.00**	**0.00**	**3.94**	**1.29**	**0.48**	**0.76**	**17.84**	**0.00**	**15.13**	**198.37**	**610.46**	**610.46**
Disclaimer:-	Blank entry if the line under outage/shutdown on corrosponding day																			

15.3 Import and Export of ER with WR & NER during March 2025

Date	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Mar-25	1.1	11.5	0.0	0.1	0.0	0.5	0.0	**13.16**	11.3	1.2	22.0	3.7	12.2	0.3	1.5	**52.06**	0.65	0.26	0.00	**0.90**	0.98	2.29	0.71	**3.98**
2-Mar-25	0.4	8.7	0.0	0.0	0.0	0.5	0.0	**9.63**	14.2	1.6	14.9	5.9	11.9	0.2	1.3	**50.05**	0.00	0.00	0.00	**0.00**	2.25	4.66	1.29	**8.20**
3-Mar-25	0.0	8.4	0.0	0.0	0.0	0.5	0.0	**8.99**	16.0	1.7	14.7	6.3	11.8	0.1	1.2	**51.82**	0.09	0.00	0.00	**0.09**	1.89	3.86	1.06	**6.81**
4-Mar-25	0.6	14.3	0.0	0.2	0.0	1.4	0.0	**16.48**	14.1	0.9	14.3	4.7	9.5	0.0	1.3	**44.75**	0.01	0.00	0.00	**0.01**	1.87	3.59	1.06	**6.52**
5-Mar-25	0.2	11.7	0.0	0.0	0.0	1.0	0.0	**12.90**	13.9	1.7	14.3	4.6	9.9	0.0	1.4	**45.86**	0.20	0.04	0.00	**0.24**	1.59	3.12	0.95	**5.66**
6-Mar-25	0.2	1.9	0.0	0.0	0.0	0.4	0.0	**2.48**	15.4	4.7	17.2	5.4	14.3	0.4	2.0	**59.40**	0.13	0.00	0.00	**0.13**	1.76	3.66	0.87	**6.30**
7-Mar-25	0.1	0.8	0.0	0.0	0.0	0.8	0.0	**1.70**	13.6	5.3	16.5	4.6	13.8	0.3	1.7	**55.88**	0.63	0.38	0.00	**1.00**	1.37	2.86	0.82	**5.04**
8-Mar-25	0.0	4.1	0.0	0.0	0.0	0.4	0.0	**4.54**	18.1	3.1	15.5	5.6	11.8	0.4	2.1	**56.64**	0.67	0.42	0.00	**1.09**	1.92	3.67	0.94	**6.53**
9-Mar-25	0.9	5.6	0.0	0.2	0.0	0.3	0.0	**6.97**	16.4	6.1	13.7	5.5	10.4	0.7	2.5	**55.14**	0.75	0.54	0.00	**1.28**	1.91	3.67	0.99	**6.57**
10-Mar-25	0.9	3.2	0.0	0.1	0.0	0.2	0.0	**4.38**	9.8	6.0	13.7	4.0	12.2	0.6	2.3	**48.57**	0.45	0.13	0.01	**0.59**	1.46	3.20	0.82	**5.48**
11-Mar-25	1.1	4.7	0.0	0.3	0.0	0.2	0.0	**6.31**	7.3	2.9	12.6	2.9	13.3	0.8	2.0	**41.71**	0.82	0.53	0.06	**1.40**	1.94	3.89	0.83	**6.65**
12-Mar-25	0.2	2.5	0.0	0.0	0.0	0.3	0.0	**3.05**	11.1	3.4	14.0	4.0	12.3	0.8	2.5	**48.01**	0.84	0.75	0.03	**1.62**	2.25	4.29	0.92	**7.46**
13-Mar-25	2.2	2.7	0.0	0.5	0.0	0.5	0.0	**5.98**	10.4	4.9	15.0	3.9	10.8	0.4	2.3	**47.80**	1.13	1.16	0.16	**2.44**	2.62	4.61	1.02	**8.25**
14-Mar-25	1.9	7.5	0.0	0.4	0.0	0.6	0.0	**10.49**	9.8	2.1	14.5	3.6	9.4	0.7	2.2	**42.25**	0.02	0.00	0.00	**0.02**	2.47	4.56	1.14	**8.16**
15-Mar-25	2.8	5.3	0.0	0.1	0.0	0.0	0.0	**8.24**	9.5	3.7	15.9	3.6	13.3	1.9	2.3	**50.16**	0.41	0.27	0.00	**0.68**	3.19	5.35	1.56	**10.11**
16-Mar-25	4.3	7.8	0.0	0.6	0.0	0.0	0.0	**12.74**	6.6	0.4	15.2	3.8	15.2	2.3	2.1	**45.61**	0.12	0.07	0.00	**0.19**	3.14	5.01	1.77	**9.92**
17-Mar-25	1.3	8.4	0.0	0.0	0.0	0.0	0.0	**9.82**	8.2	3.2	14.8	4.0	13.2	2.1	2.1	**47.75**	0.00	0.00	0.00	**0.00**	3.45	5.28	1.72	**10.45**
18-Mar-25	1.4	7.5	0.0	0.1	0.0	0.0	0.0	**9.03**	8.4	0.8	14.7	4.0	13.0	3.1	1.4	**45.45**	0.00	0.00	0.00	**0.00**	2.83	4.57	1.65	**9.05**
19-Mar-25	2.5	6.4	0.0	0.3	0.0	0.4	0.0	**9.70**	6.2	1.9	14.2	3.1	10.0	1.6	0.8	**37.76**	0.44	0.96	0.00	**1.40**	2.32	3.98	1.30	**7.59**
20-Mar-25	1.2	3.5	0.0	0.1	0.0	0.1	0.0	**4.85**	8.0	2.2	14.7	4.2	12.5	1.4	1.2	**44.22**	0.16	0.26	0.00	**0.42**	3.03	5.53	1.73	**10.29**
21-Mar-25	0.0	2.6	0.0	0.0	0.0	0.1	0.0	**2.70**	12.9	7.3	17.1	6.6	13.0	1.5	2.2	**60.63**	0.30	0.46	0.00	**0.75**	2.99	5.03	1.81	**9.82**
22-Mar-25	0.5	9.0	0.0	0.0	0.0	0.1	0.0	**9.64**	17.4	5.7	24.2	6.5	12.9	1.1	2.4	**70.15**	0.12	0.17	0.00	**0.28**	3.42	5.80	1.97	**11.19**
23-Mar-25	0.3	5.6	0.0	0.0	0.0	0.0	0.0	**5.95**	16.8	3.1	27.5	5.7	13.2	1.6	2.6	**70.55**	0.00	0.00	0.00	**0.00**	4.13	7.77	2.01	**13.91**
24-Mar-25	0.4	2.9	0.0	0.0	0.0	0.0	0.0	**3.44**	16.8	5.9	29.4	5.6	13.5	1.5	2.5	**75.09**	0.03	0.00	0.00	**0.03**	3.54	6.25	1.94	**11.74**
25-Mar-25	1.3	3.6	0.0	0.2	0.0	0.2	0.0	**5.23**	13.1	3.7	26.8	4.7	12.8	1.3	2.2	**64.71**	0.17	0.01	0.00	**0.18**	3.10	5.57	1.67	**10.35**
26-Mar-25	4.5	4.3	0.0	0.4	0.0	0.0	0.0	**9.20**	9.9	2.7	26.1	3.7	12.6	1.1	1.8	**57.87**	0.32	0.10	0.00	**0.42**	2.94	5.31	1.24	**9.49**
27-Mar-25	6.3	7.6	0.0	0.8	0.0	0.1	0.0	**14.85**	4.0	3.0	23.8	2.4	12.2	0.9	1.9	**48.22**	0.33	0.25	0.01	**0.59**	2.76	4.73	1.05	**8.53**
28-Mar-25	10.5	16.3	0.0	1.7	0.0	0.1	0.1	**28.65**	1.7	3.1	20.1	1.0	10.9	1.1	0.9	**38.78**	0.92	0.71	0.08	**1.71**	2.15	3.68	0.74	**6.58**
29-Mar-25	10.4	19.5	0.0	1.2	0.0	0.0	0.1	**31.23**	1.6	1.0	20.0	1.0	10.6	2.0	0.5	**36.77**	0.89	0.39	0.01	**1.28**	2.14	3.57	0.75	**6.47**
30-Mar-25	9.6	17.4	0.0	1.2	0.0	0.3	0.1	**28.45**	1.9	0.5	19.2	1.3	11.3	0.6	0.7	**35.58**	0.12	0.07	0.00	**0.18**	2.08	3.65	0.90	**6.63**
31-Mar-25	7.9	23.0	0.0	1.2	0.0	0.3	0.1	**32.48**	0.8	0.5	18.0	0.9	9.3	0.3	1.0	**30.90**	0.00	0.00	0.00	**0.00**	3.59	6.02	1.29	**10.90**
Total	**75.10**	**238.44**	**0.00**	**9.76**	**0.02**	**9.58**	**0.35**	**333.25**	**325.15**	**94.20**	**554.73**	**127.00**	**373.30**	**31.00**	**54.78**	**1560.14**	**10.70**	**7.89**	**0.35**	**18.95**	**77.07**	**139.02**	**38.51**	**254.60**

15.4 Import and Export of SR with ER & WR during March 2025

Date	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)								
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Mar-25	6.52	38.15	60.86	**105.53**	0.00	0.00	0.00	**0.00**	20.26	15.35	49.49	0.00	87.02	2.39	0.00	50.83	**225.34**	0.00	1.33	0.00	18.14	0.00	0.00	0.00	0.00	**19.46**
2-Mar-25	7.41	35.64	57.12	**100.17**	0.00	0.00	0.00	**0.00**	23.61	14.85	46.28	0.00	87.93	2.10	0.00	46.93	**221.71**	0.00	1.82	0.00	17.72	0.00	0.00	0.00	0.00	**19.54**
3-Mar-25	12.57	43.39	58.19	**114.15**	0.00	0.00	0.00	**0.00**	21.32	16.21	46.45	0.00	93.26	2.46	0.00	49.11	**228.81**	0.00	0.87	0.00	14.39	0.00	0.00	0.00	0.00	**15.26**
4-Mar-25	16.43	45.23	60.08	**121.74**	0.00	0.00	0.00	**0.00**	21.59	25.63	56.62	0.06	110.02	2.11	0.00	55.47	**271.51**	0.00	1.44	0.00	11.57	0.00	0.00	0.00	0.00	**13.02**
5-Mar-25	15.45	46.69	57.66	**119.80**	0.00	0.00	0.00	**0.00**	22.74	21.19	52.36	0.00	128.59	2.57	0.00	52.18	**279.63**	0.00	1.57	0.00	12.59	0.00	0.00	0.00	0.00	**14.16**
6-Mar-25	12.67	45.98	59.55	**118.19**	0.00	0.00	0.00	**0.00**	22.83	14.62	51.20	0.00	114.23	2.57	0.01	48.32	**253.77**	0.00	0.71	0.00	17.77	0.00	0.00	0.00	0.00	**18.49**
7-Mar-25	15.11	48.13	58.66	**121.89**	0.00	0.00	0.00	**0.00**	23.11	15.24	45.96	0.00	120.26	2.26	0.00	49.88	**256.71**	0.00	1.41	0.00	18.53	0.00	0.00	0.00	0.00	**19.94**
8-Mar-25	17.58	42.72	56.81	**117.12**	0.00	0.00	0.00	**0.00**	23.42	14.31	50.67	0.00	118.49	2.55	0.01	49.64	**259.09**	0.00	2.49	0.00	18.08	0.00	0.00	0.00	0.00	**20.57**
9-Mar-25	17.58	38.58	49.63	**105.79**	0.00	0.00	0.00	**0.00**	23.56	9.03	41.09	0.00	86.05	2.47	0.01	39.62	**201.83**	0.00	7.01	0.27	23.35	0.00	0.00	0.00	0.14	**30.77**
10-Mar-25	16.44	39.84	49.36	**105.65**	0.00	0.00	0.00	**0.00**	20.11	5.06	36.10	0.00	55.84	2.56	0.00	38.63	**158.30**	0.00	6.61	0.00	27.19	0.00	0.00	0.00	0.00	**33.80**
11-Mar-25	15.95	41.92	51.36	**109.23**	0.00	0.00	0.00	**0.00**	20.80	4.58	39.64	0.00	70.78	2.46	0.00	41.45	**179.71**	0.00	4.77	0.00	30.20	0.00	0.00	0.00	0.00	**34.97**
12-Mar-25	8.95	39.36	54.55	**102.86**	0.00	0.00	0.00	**0.00**	13.68	9.92	45.35	0.00	98.26	2.62	0.00	46.67	**216.50**	0.00	4.32	0.00	26.04	0.00	0.00	0.00	0.00	**30.37**
13-Mar-25	7.51	42.27	55.30	**105.08**	0.00	0.00	0.00	**0.00**	18.97	8.25	41.79	0.00	114.73	2.64	0.00	45.31	**231.69**	0.00	4.25	0.00	25.79	0.00	0.00	0.00	0.00	**30.04**
14-Mar-25	10.48	37.67	62.66	**110.81**	0.00	0.00	0.00	**0.00**	23.56	25.16	56.26	0.00	120.62	1.98	0.00	60.16	**287.74**	0.00	0.00	0.00	15.69	0.00	0.00	0.00	0.00	**15.69**
15-Mar-25	16.86	31.22	60.03	**108.11**	0.00	0.00	0.00	**0.00**	23.08	12.64	47.33	0.00	129.42	2.27	0.01	50.71	**265.45**	0.00	2.86	0.00	21.46	0.00	0.00	0.00	0.00	**24.32**
16-Mar-25	16.65	44.69	59.79	**121.13**	0.00	0.00	0.00	**0.00**	22.58	10.09	45.79	0.00	81.88	2.39	0.00	47.79	**210.54**	0.00	1.46	0.00	22.18	0.00	0.00	0.00	0.00	**23.64**
17-Mar-25	16.25	43.77	60.87	**120.88**	0.00	0.00	0.00	**0.00**	20.46	13.33	49.50	0.00	126.37	2.35	0.00	51.59	**263.60**	0.00	2.16	0.00	19.93	0.00	0.00	0.00	0.00	**22.09**
18-Mar-25	16.25	40.49	63.53	**120.26**	0.00	0.00	0.00	**0.00**	21.38	17.11	52.93	0.00	117.20	2.35	0.00	56.25	**267.23**	0.00	0.04	0.00	18.41	0.00	0.00	0.00	0.00	**18.45**
19-Mar-25	15.13	44.74	60.13	**120.01**	0.00	0.00	0.00	**0.00**	22.94	15.50	48.51	0.00	116.59	2.35	0.00	52.32	**258.21**	0.00	0.20	0.00	19.21	0.00	0.00	0.00	0.00	**19.41**
20-Mar-25	12.56	48.09	57.60	**118.26**	0.00	0.00	0.00	**0.00**	23.10	11.59	46.05	0.00	107.36	2.31	0.00	45.47	**235.89**	0.00	0.69	0.00	20.01	0.00	0.00	0.00	0.00	**20.70**
21-Mar-25	13.21	48.10	61.06	**122.37**	0.00	0.00	0.00	**0.00**	23.54	14.51	51.04	0.00	132.69	2.39	0.00	50.07	**274.25**	0.00	1.05	0.00	18.38	0.00	0.00	0.00	0.00	**19.42**
22-Mar-25	16.17	48.09	65.07	**129.34**	0.00	0.00	0.00	**0.00**	23.42	14.64	49.61	0.00	108.51	2.22	0.00	50.33	**248.73**	0.00	2.10	0.00	17.89	0.00	0.00	0.00	0.00	**19.99**
23-Mar-25	17.43	25.64	60.83	**103.90**	0.00	0.00	0.00	**0.00**	23.36	8.37	45.71	0.00	117.15	2.10	0.00	46.11	**242.82**	0.00	1.63	0.00	21.14	0.00	0.00	0.00	0.00	**22.77**
24-Mar-25	17.44	24.23	60.47	**102.14**	0.00	0.00	0.00	**0.00**	23.41	9.11	46.89	0.00	129.85	2.22	0.00	47.41	**258.91**	0.00	2.14	0.00	19.48	0.00	0.00	0.00	0.00	**21.61**
25-Mar-25	17.42	24.22	59.62	**101.26**	0.00	0.00	0.00	**0.00**	23.33	8.71	46.34	0.00	132.64	2.26	0.01	45.42	**258.70**	0.00	1.97	0.00	21.57	0.00	0.00	0.00	0.00	**23.54**
26-Mar-25	17.41	24.22	59.42	**101.05**	0.00	0.00	0.00	**0.00**	22.93	13.94	46.39	0.00	118.34	2.33	0.00	49.14	**253.07**	0.00	0.49	0.00	19.33	0.00	0.00	0.00	0.00	**19.82**
27-Mar-25	17.40	24.21	60.49	**102.10**	0.00	0.00	0.00	**0.00**	23.00	16.53	47.25	0.00	111.92	2.32	0.01	49.68	**250.71**	0.00	0.57	0.00	19.52	0.00	0.00	0.00	0.00	**20.09**
28-Mar-25	11.18	44.44	59.69	**115.32**	0.00	0.00	0.00	**0.00**	21.74	14.68	45.37	0.00	124.83	2.33	0.01	52.05	**261.01**	0.00	2.41	0.00	20.69	0.00	0.00	0.00	0.00	**23.10**
29-Mar-25	12.90	48.11	61.78	**122.79**	0.00	0.00	0.00	**0.00**	19.77	15.13	50.83	0.00	115.03	2.45	0.61	52.85	**256.66**	0.00	1.24	0.00	16.71	0.00	0.00	0.00	0.00	**17.95**
30-Mar-25	12.78	43.26	58.64	**114.67**	0.00	0.00	0.00	**0.00**	20.07	8.40	47.70	0.00	106.17	2.33	0.49	48.47	**233.64**	0.00	2.23	0.00	20.88	0.00	0.00	0.00	0.00	**23.11**
31-Mar-25	11.41	45.60	59.50	**116.51**	0.00	0.00	0.00	**0.00**	23.02	12.11	48.15	0.00	101.96	2.38	0.00	46.60	**234.23**	0.00	1.90	0.00	18.36	0.00	0.00	0.00	0.00	**20.26**
TOTAL	**439.09**	**1238.70**	**1820.32**	**3498.11**	**0.00**	**0.00**	**0.00**	**0.00**	**680.67**	**415.80**	**1474.65**	**0.06**	**3384.00**	**73.10**	**1.22**	**1516.46**	**7545.96**	**0.00**	**63.72**	**0.27**	**612.19**	**0.00**	**0.00**	**0.01**	**0.14**	**676.34**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2024 **से मार्च** 2025 April 2024 to March 2025

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2024 APR'24	86.47	18.58	346.08	0.00	694.34	0.00	0.76	0.00
मई 2024 MAY'24	51.37	68.17	271.84	3.92	655.55	0.00	0.74	0.00
जून 2024 JUN'24	0.00	520.23	20.51	152.32	709.14	0.00	0.87	0.00
जुलाई 2024 JUL'24	0.00	1225.84	0.00	476.74	747.37	0.00	0.91	0.00
अगस्त 2024 AUG'24	0.00	1228.79	0.00	506.71	719.38	0.00	0.87	0.00
सितंबर 2024 SEP'24	0.00	1219.89	0.00	494.67	634.75	0.00	0.75	0.00
अक्तूबर 2024 OCT'24	0.00	918.96	0.00	283.29	695.63	0.00	0.80	0.00
नवंबर 2024 NOV'24	12.24	125.37	0.00	212.20	698.58	0.00	0.71	0.00
दिसम्बर 2024 DEC'24	187.39	0.00	58.60	1.56	521.28	0.00	0.72	0.00
जनवरी 2025 JAN'25	158.13	0.00	252.02	0.00	674.70	0.00	0.67	0.00
फ़रवरी 2025 FEB'25	216.70	0.00	328.10	0.00	635.20	0.00	0.56	0.00
मार्च 2025 MAR'25	147.08	0.00	356.99	0.00	732.35	0.00	0.65	0.00
कुल Total	859.38	5325.83	1634.12	2131.41	8118.27	0.00	9.01	0.00

* Based on daily operational data

16.2 Export to neighbouring countries during Mar 2025

(All figures in MU)

Date	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Mar-25	0.00	0.00	0.00	0.00	0.00	1.21	0.11	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-Mar-25	0.00	0.00	0.00	0.00	0.00	1.72	0.17	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-Mar-25	0.00	0.00	0.00	0.00	0.00	2.16	0.28	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-Mar-25	0.00	0.00	0.00	0.00	0.00	2.43	0.33	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-Mar-25	0.00	0.00	0.00	0.00	0.00	2.34	0.34	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-Mar-25	0.00	0.00	0.00	0.00	0.00	1.69	0.20	0.00	0.00	0.00	0.00	0.00	0.00	0.00
7-Mar-25	0.00	0.00	0.00	0.00	0.00	1.48	0.18	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-Mar-25	0.00	0.00	0.00	0.00	0.00	1.55	0.07	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-Mar-25	0.00	0.00	0.00	0.00	0.00	1.47	0.08	0.00	0.00	0.00	0.00	0.00	0.00	0.00
10-Mar-25	0.00	0.00	0.00	0.00	0.00	0.87	0.06	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Mar-25	0.00	0.00	0.00	0.00	0.00	0.62	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Mar-25	0.00	0.00	0.00	0.00	0.00	1.37	0.10	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-Mar-25	0.00	0.00	0.00	0.00	0.00	1.63	0.08	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-Mar-25	0.00	0.00	0.00	0.00	0.00	2.96	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-Mar-25	0.00	0.00	0.00	0.00	0.00	3.71	0.09	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-Mar-25	0.00	0.00	0.00	0.00	0.00	5.82	0.26	0.04	0.00	0.00	0.00	0.00	0.00	0.00
17-Mar-25	0.00	0.00	0.00	0.00	0.00	6.87	0.31	0.31	0.00	0.00	0.00	0.00	0.00	0.00
18-Mar-25	0.00	0.00	0.00	0.00	0.00	6.27	0.23	0.07	0.00	0.00	0.00	0.00	0.00	0.00
19-Mar-25	0.00	0.00	0.00	0.00	0.00	6.17	0.20	0.09	0.00	0.00	0.00	0.00	0.00	0.00
20-Mar-25	0.00	0.00	0.00	0.00	0.00	6.11	0.13	0.01	0.00	0.00	0.00	0.00	0.00	0.00
21-Mar-25	0.00	0.00	0.00	0.00	0.00	6.15	0.02	0.05	0.00	0.00	0.00	0.00	0.00	0.00
22-Mar-25	0.00	0.00	0.00	0.00	0.00	6.38	0.12	0.05	0.00	0.00	0.00	0.00	0.00	0.00
23-Mar-25	0.00	0.00	0.00	0.00	0.00	5.86	0.03	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-Mar-25	0.00	0.00	0.00	0.00	0.00	4.88	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-Mar-25	0.00	0.00	0.00	0.00	0.00	3.99	0.13	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-Mar-25	0.00	0.00	0.00	0.00	0.00	3.05	0.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00
27-Mar-25	0.00	0.00	0.00	0.00	0.00	4.07	0.17	0.00	0.00	0.00	0.00	0.00	0.00	0.00
28-Mar-25	0.00	0.00	0.00	0.00	0.00	4.36	0.18	0.00	0.00	0.00	0.00	0.00	0.00	0.00
29-Mar-25	0.00	0.00	0.00	0.00	0.00	3.49	0.13	0.00	0.00	0.00	0.00	0.00	0.00	0.00
30-Mar-25	0.00	0.00	0.00	0.00	0.00	4.48	0.22	0.00	0.00	0.00	0.00	0.00	0.00	0.00
31-Mar-25	0.00	0.00	0.00	0.00	0.00	4.58	0.26	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**109.74**	**4.49**	**0.62**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

16.2 Export to neighbouring countries during Mar 2025

(All figures in MU)

Date	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Mar-25	0.89	1.96	3.01	1.22	0.00	0.00	0.00	0.33	22.40	1.63	0.72	4.42	3.82	0.02
2-Mar-25	0.75	1.79	3.04	1.40	0.00	0.00	0.00	0.37	22.31	1.79	0.97	5.82	3.76	0.02
3-Mar-25	0.77	1.83	3.07	1.34	0.00	0.00	0.00	0.32	22.29	1.60	0.94	6.16	3.80	0.02
4-Mar-25	0.73	1.82	3.03	1.36	0.00	0.00	0.00	0.37	22.24	1.30	0.95	6.69	3.87	0.02
5-Mar-25	0.84	1.93	3.12	1.36	0.00	0.00	0.00	0.34	22.30	1.26	1.07	7.49	3.68	0.02
6-Mar-25	0.39	1.86	2.94	1.02	0.00	0.00	0.00	0.39	22.24	1.22	0.96	7.28	4.01	0.02
7-Mar-25	0.75	1.84	3.18	1.18	0.00	0.00	0.00	0.39	22.19	1.10	0.99	6.78	3.69	0.02
8-Mar-25	0.95	2.05	3.19	1.37	0.00	0.00	0.00	0.35	22.27	1.07	0.94	5.47	3.78	0.02
9-Mar-25	1.00	2.12	3.40	1.53	0.00	0.00	0.00	0.38	22.32	1.27	1.07	6.34	3.91	0.02
10-Mar-25	0.90	1.94	2.96	1.20	0.00	0.00	0.00	0.40	22.37	1.35	1.10	7.40	4.07	0.02
11-Mar-25	0.89	1.87	2.81	0.93	0.00	0.00	0.10	0.35	22.27	1.40	1.04	7.37	3.91	0.02
12-Mar-25	0.72	1.79	3.02	1.16	0.00	0.00	0.00	0.43	22.14	1.43	1.09	7.36	3.73	0.02
13-Mar-25	0.40	1.48	2.71	1.06	0.00	0.00	0.00	0.38	22.21	1.51	0.82	4.11	3.52	0.02
14-Mar-25	0.02	1.08	2.95	1.08	0.00	0.00	0.01	0.29	22.26	1.53	0.59	0.24	2.40	0.02
15-Mar-25	0.76	1.89	5.60	1.05	0.00	0.00	0.00	0.14	22.33	1.50	0.35	3.01	2.55	0.02
16-Mar-25	0.94	2.10	6.98	0.73	0.00	0.00	0.00	0.00	22.22	1.68	1.03	5.67	2.23	0.02
17-Mar-25	0.61	1.79	6.42	0.68	0.00	0.00	0.00	0.00	22.11	1.72	0.95	5.76	2.50	0.02
18-Mar-25	0.78	1.91	6.86	0.33	0.00	0.00	0.00	0.00	21.98	1.70	1.02	6.19	4.03	0.02
19-Mar-25	0.88	2.04	7.08	0.16	0.00	0.00	0.00	0.00	21.99	1.66	0.96	6.34	3.99	0.02
20-Mar-25	0.90	2.06	7.10	0.21	0.00	0.00	0.00	0.00	21.66	1.71	1.04	6.24	3.88	0.02
21-Mar-25	1.20	2.38	7.30	0.14	0.00	0.00	0.00	0.00	21.86	1.54	0.93	6.67	4.04	0.02
22-Mar-25	1.41	2.60	6.24	0.88	0.00	0.00	0.00	0.00	21.93	1.40	0.77	5.03	4.67	0.02
23-Mar-25	1.25	2.51	3.68	2.14	0.00	0.00	0.00	0.09	22.10	1.42	0.82	4.38	4.67	0.02
24-Mar-25	1.05	2.28	6.49	0.64	0.00	0.00	0.07	0.09	22.21	1.44	0.98	6.47	4.01	0.01
25-Mar-25	1.50	2.71	5.36	1.14	0.00	0.00	0.00	0.13	22.24	1.56	0.93	6.52	3.62	0.02
26-Mar-25	1.34	2.43	3.00	1.39	0.00	0.00	0.00	0.40	22.23	1.02	0.92	6.60	3.97	0.02
27-Mar-25	0.96	2.07	2.83	1.31	0.00	0.00	0.00	0.33	22.25	0.84	0.82	6.11	4.13	0.02
28-Mar-25	0.81	1.96	2.70	1.18	0.00	0.00	0.00	0.24	22.23	0.78	0.96	7.16	3.92	0.02
29-Mar-25	1.07	2.18	2.77	1.28	0.00	0.00	0.00	0.22	21.97	0.83	0.96	5.95	3.81	0.02
30-Mar-25	0.84	1.97	2.85	1.44	0.00	0.00	0.00	0.23	21.90	0.90	1.01	6.94	3.91	0.03
31-Mar-25	0.70	1.75	2.72	1.35	0.00	0.00	0.00	0.23	21.94	0.65	1.03	7.40	3.95	0.03
Total	**27.01**	**61.97**	**128.40**	**33.27**	**0.00**	**0.00**	**0.18**	**7.19**	**686.96**	**41.81**	**28.74**	**185.37**	**115.84**	**0.65**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – मार्च 2025

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - MARCH 2025

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

मार्च 2025 MARCH 2025			Apr'24- Mar'25	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	374	348	6949	27232
प.क्षे. WR	806	1035	5368	6799
द.क्षे. SR	287	2824	4279	13595
पू.क्षे. ER	484	386	4330	12792
पूर्वोत्तर क्षे. NER	97	96	1015	690
कुल TOTAL	2048	4689	21941	61106

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2024 Apr'24	9860	7128	1565	5921
मई 2024 May'24	497	8268	2258	7240
जून 2024 Jun'24	10971	8732	2329	8093
जुलाई 2024 Jul'24	11338	9378	1891	8626
अगस्त 2024 Aug'24	11648	9054	1930	8822
सितंबर 2024 Sep'24	11981	9212	1748	7572
अक्तूबर 2024 Oct'24	12567	8372	1511	2332
नवंबर 2024 Nov'24	11553	9432	1217	963
दिसम्बर 2024 Dec'24	12448	10602	1773	1468
जनवरी 2025 Jan'25	12932	9756	1984	2533
फ़रवरी 2025 Feb'25	11693	8852	1687	2848
मार्च 2025 Mar'25	13228	9832	2048	4689
कुल TOTAL	130716	108618	21941	61106

मासिक डी एस एम बिलिंग का ब्योरा* 2024-25
MONTHLY DSM BILLING DETAILS* 2024-25

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION ⟹ / सप्ताह WEEK ⇓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
03.03.25 to 09.03.25	168.70	247.24	36.76	244.14	61.80
10.03.25 to 16.03.25	193.14	259.72	24.58	199.27	54.99
17.03.25 to 23.03.25	173.96	245.27	31.40	211.63	74.49
24.03.25 to 30.03.25	271.40	275.38	24.49	294.74	85.81

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2025
EXCHANGES THROUGH POWER EXCHANGES -MARCH 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED	उत्तरी क्षेत्र NR	14.12	0.00
2	ADANI GREEN ENERGY TWENTY FIVE LIMITED		84.16	0.00
3	ADANI GREEN ENERGY TWENTY FIVE LIMITED_infirm		1.03	0.00
4	ADANI GREEN ENERGY TWENTY FOUR LIMITED		100.50	0.00
5	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		34.98	0.00
6	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		11.48	0.00
7	AMP Energy Green Four Private Limited		10.40	0.22
8	Adept Renewable Technologies Private Limited		28.92	0.00
9	Amp Energy Green Six Private Limited		26.97	0.00
10	Amplus Ages Private Limited		4.63	0.00
11	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		1.20	0.00
12	Chandigarh (UT)		35.87	3.70
13	Delhi		329.23	82.56
14	Government of Himachal Pradesh _ Chamera1HEP		14.92	1.68
15	Government of Himachal Pradesh _ Chamera3HEP		4.55	0.31
16	Government of Himachal Pradesh_ CHAMERA2HEP		7.04	0.55
17	Government of Himachal Pradesh_BairasuilHEP		7.83	0.63
18	Government of Himachal Pradesh_Koldam HEP		14.78	2.06
19	Government of Himachal Pradesh_NJHPS		26.30	0.60
20	Government of Himachal Pradesh_Parbati3HEP		2.58	0.24
21	Government of Himachal Pradesh_RampurHEP		7.81	0.18
22	Grian Energy Private Limited		8.16	0.00
23	Haryana		672.42	42.07
24	Himachal Pradesh		60.12	36.75
25	IGSTPS JHAJJAR		2.04	0.00
26	JUNIPER GREEN COSMIC PRIVATE LIMITED		11.89	0.00
27	JUNIPER NIRJARA ENERGY PRIVATE LIMITED		1.72	0.00
28	JUNIPER NIRJARA ENERGY PRIVATE LIMITED_Infirm		0.18	0.00
29	Jammu Kashmir		39.52	242.99
30	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		18.88	0.00
31	KHURJA STPP		0.83	0.00
32	NEA - UP STU		0.00	24.07
33	NEA Nepal Upper Chameliya Hydropower Project		0.40	0.00
34	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	17.76
35	NTPC Dadri Stage I		35.51	0.00
36	NTPC Dadri Stage II		7.75	0.00
37	NTPC Rihand stage I		8.49	0.00
38	NTPC Rihand stage II		6.91	0.00
39	NTPC Rihand stage III		9.14	0.00
40	NTPC Singrauli		20.23	0.00
41	NTPC Tanda Stage II		6.73	0.00
42	NTPC Unchahar Stage I		4.32	0.00
43	NTPC Unchahar Stage II		3.80	0.00
44	NTPC Unchahar Stage III		2.45	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2025
EXCHANGES THROUGH POWER EXCHANGES -MARCH 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	NTPC Unchahar Stage IV		7.62	0.00
46	North Central Railway Prayagraj		0.00	12.52
47	Onevolt Energy Private Limited		14.62	0.00
48	Punjab		5.74	1010.20
49	RENEW SURYA PRATAP PRIVATE LIMITED		47.56	0.00
50	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.56	0.00
51	Rajasthan		496.38	148.20
52	ReNew Surya Ravi Private Limited		48.37	0.00
53	SHREE CEMENT LIMITED TPS		30.21	0.00
54	Sainj HEP		5.90	0.00
55	Serentica Renewables India 4 Private Limited		2.85	0.00
56	Serentica Renewables India 5 Private Limited		31.38	0.00
57	Singoli Bhatwari HEP		13.73	0.00
58	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		6.98	0.00
59	TPSL 200MW TPTCL Banderwala		22.07	0.00
60	TPSL Banderwala SECI 100_INF		8.58	0.00
61	Transition Cleantech Services Private Limited		2.80	0.00
62	Transition Energy Services Private Limited		14.78	0.00
63	Transition Green Energy Private Limited		6.04	0.00
64	Transition Sustainable Energy Services One Private Limited		14.47	0.00
65	Uttar Pradesh		654.91	464.78
66	Uttarakhand		62.48	122.99
67	ACB (INDIA) LIMITED		28.53	0.28
68	ADANI GREEN ENERGY TWENTY FOUR LIMITED_PSS4		0.55	0.00
69	ADANI GREEN ENERGY TWENTY SIX A LIMITED_PSS-3		3.11	0.00
70	ADANI PORTS AND SPECIAL ECONOMIC ZONE LIMITED (PSS-3)		53.61	0.00
71	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS-3 (162.5 MW Hybrid Solar of 187.5MW HPD)		44.08	0.00
72	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.12	0.00
73	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		2.27	0.00
74	ADANI RENEWABLE ENERGY FIFTY SEVEN LIMITED_PSS13		31.72	0.00
75	ADANI RENEWABLE ENERGY FIFTY SEVEN LIMITED_PSS13_infirm		0.99	0.00
76	ADANI RENEWABLE ENERGY FIFTY SIX LIMITED_PSS4		4.85	0.00
77	ADANI RENEWABLE ENERGY FIFTY SIX LIMITED_PSS9		16.84	0.00
78	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS-3		48.38	0.00
79	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS13		17.51	0.00
80	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS4		0.39	0.00
81	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED_PSS-1		217.78	0.00
82	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		63.77	0.00
83	AMBUJA CEMENTS LIMITED_PSS3		12.94	0.00
84	AMBUJA CEMENTS LIMITED_PSS4_Hybrid Wind		0.78	0.00
85	Adani Green Energy Twenty Five A Limited_PSS-2		140.95	0.00
86	Adani Green Energy Twenty Five B Limited_PSS-2		165.52	0.00
87	Adani Green Energy Twenty Four A Limited_PSS-3		36.09	0.00
88	Adani Green Energy Twenty Six B Limited_PSS-2		46.16	0.00
89	Adani Ports and Special Economic Zone Limited_PSS4_Wind		0.21	0.00
90	Adani Power Limited - Raigarh TPP		125.99	1.14
91	Adani Power Limited-Raipur TPP		162.75	0.00
92	Adani Renewable Energy Forty Eight Limited (Wind)_PSS-9		25.17	0.00
93	ArcelorMittal Nippon Steel India Limited		0.00	126.79
94	BHARAT ALUMINIUM COMPANY LTD		49.93	0.00
95	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	1.00
96	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		3.42	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2025 EXCHANGES THROUGH POWER EXCHANGES -MARCH 2025				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
97	Chhattisgarh	पश्चिमी क्षेत्र WR	241.90	91.38
98	D B Power Limited		54.83	0.00
99	DHARIWAL STU OTH		0.28	0.00
100	Daman and Diu - Dadra and Nagar Haveli		2.74	68.56
101	Dhariwal ISTS		11.46	0.00
102	GMR Warora Energy Limited		5.57	0.00
103	Goa WR		23.49	6.94
104	Gujarat		109.14	838.04
105	Jaypee Nigrie Super Thermal Power Plant		199.87	0.00
106	Jhabua Power Limited		7.50	0.00
107	Jindal Power Limited, Stage-1		31.79	0.00
108	Jindal Power Limited, Stage-2		125.88	26.38
109	Jindal Steel & Power Ltd , DCPP		136.77	6.26
110	KSK MAHANADI POWER COMPANY LIMITED		22.31	0.00
111	LANCO AMARKANTAK POWER LIMITED		1.02	0.00
112	MAHAN ENERGEN LIMITED U#1		43.96	0.00
113	MAHAN ENERGEN LIMITED U#2		150.39	0.00
114	MB POWER (MADHYA PRADESH) LIMITED		74.74	8.11
115	Madhya Pradesh		417.38	76.19
116	Maharashtra		94.47	1319.43
117	Maruti Clean Coal and Power Limited		9.79	1.62
118	NREL-Dayapar Wind		6.02	0.00
119	NTPC Gadarwara		33.79	0.00
120	NTPC Jhanor Gandhar GPS		0.00	0.67
121	NTPC Kawas GPS		0.00	0.47
122	NTPC Korba Stage I &II		18.44	0.00
123	NTPC Korba Stage III		5.53	0.00
124	NTPC Lara Stage I		11.76	0.00
125	NTPC Mouda Stage I		23.44	0.00
126	NTPC Mouda Stage II		27.38	0.00
127	NTPC SAIL POWER COMPANY LIMITED		0.81	0.00
128	NTPC SOLAPUR SOLAR PV Station		0.00	0.00
129	NTPC Sipat Stage I		21.96	0.00
130	NTPC Sipat Stage II		7.23	0.00
131	NTPC Solapur		13.18	0.00
132	NTPC Vindhyachal Stage I		16.05	0.00
133	NTPC Vindhyachal Stage II		17.67	0.00
134	NTPC Vindhyachal Stage III		18.42	0.00
135	NTPC Vindhyachal Stage IV		19.67	0.00
136	NTPC Vindhyachal Stage V		8.96	0.00
137	NTPC khargone		18.09	0.00
138	R.K.M POWERGEN PRIVATE LIMITED		46.13	0.00
139	RENEW GREEN (MHS ONE) PRIVATE LIMITED_SOLAR_HYBRID		1.59	0.00
140	Ratnagiri Gas & Power Private Limited		0.00	3.40
141	SKS Power Generation Chhattisgarh Limited		12.31	14.65
142	Sasan Power Limited		22.27	0.00
143	TRN ENERGY PRIVATE LIMITED		22.20	0.00
144	The Tata Power Co Ltd (MTPS)		18.43	0.00
145	WIND FIVE RENERGY LIMITED		5.09	0.00
146	AM GREEN ENERGY PRIVATE LIMITED Solar		0.92	0.00
147	AM GREEN ENERGY PRIVATE LIMITED Wind		0.55	0.00
148	Andhra Pradesh		84.19	372.29

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2025 EXCHANGES THROUGH POWER EXCHANGES -MARCH 2025				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
149	COASTAL ENERGEN PRIVATE LIMITED	दक्षिणी क्षेत्र SR	38.39	2.03
150	Goa SR		0.21	7.54
151	IL&FS TAMIL NADU POWER COMPANY LIMITED		17.54	0.00
152	JINDAL POWER LIMITED SIMHAPURI		24.91	1.84
153	Karnataka		239.98	81.58
154	Kerala		9.38	211.02
155	MEENAKSHI ENERGY LIMITED		5.48	0.00
156	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		10.87	0.00
157	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		4.05	0.00
158	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.08	0.00
159	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		1.09	0.00
160	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		0.33	0.00
161	NLC Tamilnadu Power Limited		8.83	0.00
162	NTECL VALLUR		5.97	0.00
163	NTPC KUDGI		19.51	0.00
164	NTPC Ramagundam Stage I &II		15.16	0.00
165	NTPC Ramagundam Stage III		3.90	0.00
166	NTPC Simhadri Stage I		0.01	0.00
167	NTPC Simhadri Stage II		13.65	0.00
168	NTPC Talcher Super Thermal Power Station Stage II		22.74	0.00
169	NTPC Telangana		0.78	0.00
170	OSTRO KANNADA POWER PRIVATE LIMITED		8.98	0.00
171	Pondicherry UT		27.20	4.62
172	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		3.36	0.00
173	Ramagundam Floating solar		13.03	0.00
174	ReNew Surya Roshni Private Limited_Gadag		2.69	0.00
175	SEIL ENERGY INDIA LIMITED		38.24	0.00
176	SEIL Energy India Limited Project II		34.18	0.00
177	Serentica Renewables India 1 Private Limited		0.84	0.00
178	Simhadri FSP 15 MW		2.36	0.00
179	Tamil Nadu		318.97	332.03
180	Telangana		46.47	2096.23
181	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	1.91	0.00
182	Bihar		752.48	27.72
183	Chuzachen HEP		0.01	0.00
184	Damodar Valley Corporation		96.24	199.53
185	Dikchu Hydro Electric Project (Sneha Kinetic Power Projects Pvt. Ltd.)		4.16	0.00
186	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	195.74
187	GMR KAMALANGA ENERGY LTD-CTU		1.97	0.00
188	IND BARATH ENERGY UTKAL LIMITED		82.58	74.29
189	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.08	0.00
190	Jharkhand		68.34	53.19
191	Jindal India Power Limited		62.99	0.00
192	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		3.02	0.00
193	KANTI BIJLEE UTPADAN NIGAM LIMITED		16.28	0.00
194	MAITHON POWER LIMITED		5.06	0.00
195	NABINAGAR POWER GENERATING COMPANY LIMITED		30.33	0.00
196	NEA - Bihar STU		0.00	75.01
197	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	183.94
198	NTPC BARH Stage I		2.25	0.00
199	NTPC BARH Stage II		25.32	0.00
200	NTPC Darlipali		10.18	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL)				
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2025 EXCHANGES THROUGH POWER EXCHANGES -MARCH 2025				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
201	NTPC Farakka stage I		129.88	0.00
202	NTPC Farakka stage III		39.25	0.00
203	NTPC Kahalgaon stage I		13.97	0.00
204	NTPC Kahalgaon stage II		19.54	0.00
205	NTPC North Karanpura STPS		8.59	0.00
206	NTPC Talcher Stage I		4.42	0.00
207	NTPP BRBCL		35.48	0.00
208	Odisha		419.51	143.46
209	Sikkim		12.45	0.29
210	Tashiding HEP, Shiga Energy Private Limited		0.02	0.00
211	West Bengal		95.14	862.15
212	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	2.82	0.00
213	ASSAM GAS BASED POWER STATION		5.35	0.00
214	Arunachal Pradesh		5.66	8.46
215	Assam		163.87	14.62
216	Bongaigaon Thermal Power Station NTPC		3.26	0.00
217	KAMENG HYDRO POWER STATION		8.81	0.00
218	Manipur		2.84	0.00
219	Meghalaya		4.44	56.82
220	Mizoram		0.42	0.25
221	Nagaland		4.94	9.40
222	Palatana Plant		1.48	0.00
223	Tripura		6.49	11.15
	Total		9832	9832

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : MARCH 2025

RE Source & Unit wise break up (01.03.2025-31.03.2025)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	7	5	250	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1450	4	0	0
5	Small Hydro	14	1	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**1471**	**10**	**250**	**1**

RECs Issued (01.03.2025-31.03.2025)

Sr.No.	Non Solar	Solar	Total
1	711197	121049	832246

Redemption of REC (01.03.2025-31.03.2025)

Sr.No.	Non Solar	Solar	Total
1	2340754	194357	2535111

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : MARCH 2025

RE Source & Unit wise break up (Apr'24-Mar'25)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	385	25	342	13
2	Urban or Municipal Waste	0	0	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	3944	31	1268	23
5	Small Hydro	38	2	24	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	**4367**	**58**	**1646**	**38**

RECs Issued (Apr'24-Mar'25)

Sr.No.	Non Solar	Solar	Total
1	40839042	1208460	42047502

Redemption of REC (Apr'24-Mar'25)

Sr.No.	Non Solar	Solar	Total
1	29515447	557559	30073006

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

MONTH : MARCH 2025

RE Source & Unit wise break up Since Inception to Mar'25

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3345	542	3147	531
2	Urban or Municipal Waste	12	1	12	1
3	Solar Thermal	0	0	0	0
4	Solar PV	5541	597	2712	500
5	Small Hydro	883	44	881	45
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	**11010**	**1314**	**7516**	**1168**

RECs Issued since Inception to Mar'25

Sr.No.	Non Solar	Solar	Total
1	155944080	14748838	170692918

Redemption of REC since Inception to Mar'25

Sr.No.	Non Solar	Solar	Total
1	108019776	13006816	121026592

REC Closing balance as on 31.03.2024

Sr.No.	Non Solar	Solar	Total
1	36428153	1221112	37649265

Details of Grid Events during the Month of March 2025 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	Punjab	10-03-2025 14:32	10-03-2025 19:17	04:45	0	100	0.000	0.172	55015	58229	i)220kV Dasuya(PS) has double main bus scheme. ii)As reported at 14:32hrs, B-ph conductor of 220 KV Dasuya(PS)-Jalandhar(BB) Ckt-2 broken due to damage of insulator string and fell on 220kV bus-2. iii)As per PMU at Jalandhar(PG), B-N fault with delayed clearance of ~560msec is observed. iv)Fault was not cleared in time from Dasuya end. (Exact details w.r.t. bus bar protection at Dausya end yet to be received.) v)Line connected to 220kV Bus-2 i.e., 220 KV Dasuya(PS)-Jalandhar(PG) (PG) Ckt-1, 220 kV Sarna(PS)-Dasuya(PS) (PG) Ckt-2 and 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-2 tripped from remoted end. As reported, 220kV bus coupler at Dasuya(PS) also tripped. vi)As per SCADA, change in demand of approx. 100 MW is observed in Punjab control area.	1) 220 KV Dasuya(PS)-Jalandhar(BB) (BBMB) Ckt-2 2) 220 KV Dasuya(PS)-Jalandhar(PG) (PG) Ckt-1 3) 220 KV Sarna(PS)-Dasuya(PS) (PG) Ckt-2 4) 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-2
2	GI-2	Rajasthan	10-03-2025 07:14	10-03-2025 08:09	00:55	0	480	0.000	0.889	48596	54007	i)400/220KV Merta and Bikaner(RS) are connected to each other. Network diagram showing connectivity between Merta, Bikaner and VSLP plant is shown in attached in Annexure. ii)During antecedent condition, 220kV Merta-Makrana line was under open condition (as per instruction of SLDC-RS) and 220kV Merta-Jethana line was under tripped condition (line tripped on fault). 400/220kV 315 MVA ICT-1&2 at Bikaner(RS) and Merta(RS) were running at loading of 300MVA & 292MVA each respectively. 220/132kV Bikaner S/s was drawing power from VSLP generating station and 400/220kV Bikaner S/s (through D/C interconnector).iii)At 07:14 hrs, 135MW Unit-1 at VSLP tripped due to problem in PA fan. Due to this, the complete load of 220/132kV Bikaner S/s shifted on 220kV Bikaner(220kV)-Bikaner(400/220kV) interconnectors. Loading of interconnector-1&2 increased from 75MW & 31MW to 151MW & 68MW respectively. Eventually, 400/220kV 315MVA ICT-1&2 loading also increased (increased from 300MVA to 355MVA). iv)Due to increases in the loading of ICTs at Bikaner, SPS of ICTs at Bikaner operated and initiated tripping to 220kV Bikaner-Nokha which was carrying ~185MW. v)Further, load of Nokha shifted to 220kV Merta-Kuchera-Nokha after tripping of 220kV Bikaner-Nokha. This further led to overloading of 400/220kV 315MVA ICTs at Merta(RS). Loading of ICTs at Merta increased from 300MVA to 350MVA. vi)Further, 400/220kV 315MVA ICTs at Merta(RS) tripped due to ICT overcurrent protection operation due to overloading. At the same time, SPS of ICTs at Merta also operated and 220kV Merta-Kuchera line tipped. vii)As per PMU at Merta(RS), no fault in system is observed. viii)As per SCADA data change in Rajasthan demand of ~430MW is observed. However, as reported by SLDC-Rajasthan, load loss of ~480MW occurred in Rajasthan control area	1) 220kV Bikaner-Nokhra (RS) Ckt 2) 400/220 KV 315 MVA ICT 1 at Merta(RS) 3) 400/220 KV 315 MVA ICT 1 at Merta(RS) 4) 220kV Merta-Kuchera Ckt
3	GI-2	Rajasthan	11-03-2025 14:51	11-03-2025 16:08	01:17	275	0	0.493	0.000	55792	59426	i)Generation of 400kV Renew Surya Ravi (RSRPL) (IP) RE station evacuates through 400 KV Renew Surya Ravi SL_BKN_PG(RSRPL)-Bikaner(PG) Ckt via 400/33 kV 150 MVA ICT 1 and 2 at Renew Surya Ravi SL_BKN_PG (RSRPL). During antecedent condition, 400kV Renew Surya Ravi (RSRPL) (IP) RE station was generating approx. 275 MW (as per PMU). ii)As reported, at 14:51hrs, 400/33 kV 150 MVA ICT 1 at Renew Surya Ravi SL_BKN_PG (RSRPL) tripped due to maloperation of E/F relay (vector summation of current setting issue). As per DR/EL, E/F relay at ICT-1 operated. iii)During the same time, 400/33 kV 150 MVA ICT 2 at Renew Surya Ravi SL_BKN_PG (RSRPL) also tripped (exact reason and nature of protection operated yet to be shared). iv)Due to tripping of both 400/33 kV 150 MVA ICT 1 and 2 at Renew Surya Ravi SL_BKN_PG (RSRPL), 400kV Renew Surya Ravi (RSRPL) (IP) generation becomes zero due to loss of evacuation path. v)As per PMU, no fault is observed in the system. vi)As per PMU, solar generation loss of approx. 275 MW is observed at RSRPL(IP).	1) 400/33 kV 150 MVA ICT 1 at Renew SuryaRavi SL_BKN_PG (RSRPL) 2) 400/33 kV 150 MVA ICT 2 at Renew SuryaRavi SL_BKN_PG (RSRPL)
4	GD-1	Uttar Pradesh	12-03-2025 01:06	12-03-2025 09:20	08:14	0	40	0.000	0.087	40497	46132	i)220/132/33KV Baraut(UP) S/s has single main and transfer bus scheme in all voltage levels. ii)As reported at 01:06 hrs, R-ph CT of 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-1 got damaged which further led to bus bar protection operation at 220kV Baraut(UP). As a result, all the elements connected to 220KV Bus tripped and complete blackout occurred at 220/132/33kV Baraut(UP) S/s. iii)However, as per DR at Baghpat(PG) end of 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-1, R-N fault (Ir=~7.71kA) converted to R-Y-N fault (Ir=~14.48kA, Iy=~15.87kA) was observed in 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-1 and fault was cleared in zone-2 from Baghpat(PG) end with fault clearing time of =~440ms. iv)As per DR at Baghpat(PG) end of 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-2, R-N fault (Ir=~8.53kA) was observed in 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-2 and fault was sensed in zone-2 at Baghpat(PG) end with fault clearing time of =~240ms. v)As per SCADA SOE, 220 KV Baghpat(PG)-Shamli(UP) (UP) Ckt also tripped during the same time (exact reason of tripping yet to be shared). vi)As per PMU at Meerut(PG), R-N phase to ground fault converted to R-Y-N double phase to ground fault with delayed fault clearing time of 440ms was observed. vii)As per SCADA, change in demand of approx. 40MW is observed in Uttar Pradesh control area.	1) 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-1 2) 220 KV Baghpat(PG)-Baraut(UP) (UP) Ckt-2 3) 220 KV Nirpura-Baraut(UP) Ckt 4) 220 KV Muradnagar_new-Baraut(UP) Ckt 5) 220/132kV 200MVA ICT-1 at Baraut(UP) 6) 220/132kV 200MVA ICT-2 at Baraut(UP) 7) 220/132kV 200MVA ICT-3 at Baraut(UP)
5	GD-1	Delhi	14-03-2025 18:34	14-03-2025 20:32	01:58	0	30	0.000	0.075	39404	40233	i)220/66/33kV Delhi Rohtak Road(BB) S/s has double main bus arrangement at 220kV level. ii)During antecedent condition, incoming power at Delhi Rohtak Road(BB) through 220 KV Delhi RR(BB)-Narela(DV) (BBMB) D/C was approx. 17 MW each (as per SCADA) which was supplying load of Delhi Rohtak Road(BB) S/s. iii)As reported, at 18:34hrs, 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1 tripped on R-B phase to phase fault with following relay indications: fault distance of 1.185km and fault current of Ir=~2.587kA and Ib=~2.523kA from Delhi RR(BB) end and fault distance of 17.59 km and fault current of Ir=~3.841kA and Ib=~3.878kA from Narela(DV) end. During patrolling, a kite string was found tangled between R and B phases at tower loc. no. 1069A, which was later removed. iv)During the same time, 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-2 also tripped from Narela end only with following relay indications : fault distance of 17.59 km and fault current of Ir=~3.841kA and Ib=~3.878kA from Narela(DV) end (exact reason of fault yet not shared). During patrolling, nothing abnormal was found. v)Due to tripping of 220 KV Delhi RR(BB)-Narela(DV) (BBMB) D/C, complete blackout occurred at 220/66/33kV Delhi Rohtak Road(BB) S/s. vi)As per PMU at Mandaula(PG), R-B phase to phase fault with fault clearing time of 80 ms is observed. vii)As per SCADA, change in demand of approx. 30 MW is observed in Delhi control area.	1) 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1 2) 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-2

Details of Grid Events during the Month of March 2025 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
6	GI-2	Haryana	15-03-2025 17:19	15-03-2025 19:45	02:26	0	0	0.000	0.000	44153	42627	i)During antecedent condition, 800 kV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying approx. 250 MW each and hence total 1000 MW power was flowing from Champa to Kurukshetra. ii)As reported at 17:19 hrs, 800 kV HVDC Kurukshetra (PG) Pole-2 & 4 blocked due to commutation failure in Pole-2. (Exact reason of tripping need to be analyzed) iii)As 800 kV HVDC Kurukshetra(PG) Pole-2 and Pole-4 blocked, power flow of Pole-1 and Pole-2 shifted on Pole-3 and Pole-4. Hence, there was no reduction in power order. iv)As per PMU at Kurukshetra(PG), no fault was observed in the system. However, fluctuation in voltage was observed. v)As per SCADA, no change in demand of Haryana control area.	1) 800 kV HVDC Kurukshetra(PG) Pole-02 2) 800 kV HVDC Kurukshetra(PG) Pole-04
7	GD-1	Himachal Pradesh	16-03-2025 14:46	16-03-2025 16:45	01:59	0	0	0.000	0.000	48809	45884	i)Total generated power of Sainj HEP(HP), Parbati_2(NH) and Parbati_3(NH) evacuates through 400 kV Parbati_2(NH)- Banala(PG) (PKTCL) Ckt and 400 kV Parbati_3(NH)-Banala(PG) (PKTCL) Ckt via 400 KV Parbati_2(NH)-Sainj(HP) (PKTCL) Ckt and 400 KV Parbati_3(NH)-Sainj(HP) (PKTCL) Ckt. ii)During antecedent condition, no generation was there at 400kV Parbati_2(NH), 400kV Parbati_3(NH) and 400kV Sainj HEP(HP). iii)As reported, at 14:46hrs, 400 KV Parbati_3(NH)- Banala(PG) (PKTCL) Ckt tripped from Banala(PG) end only on R-N phase to earth fault with fault distance of 6.9km and fault current of 5.545kA from Banala(PG) end (exact reason of fault yet to be shared). iv)As further reported, 400 KV Parbati_2(NH)-Sainj(HP) (PKTCL) Ckt also tripped at the same time from Sainj end only (exact reason of tripping yet to be shared). v)Due to tripping of both 400 KV Parbati_3(NH)- Banala(PG) (PKTCL) Ckt and 400 KV Parbati_2(NH)-Sainj(HP) (PKTCL) Ckt, complete blackout occurred at 400kV Parbati_3(NH) and 400kV Sainj HEP(HP) S/s. vi)As per PMU at Nallagarh(PG), two consecutive R-N phase to earth fault is observed with delayed fault clearing time of 1240 ms and 1040 ms respectively. vii)As per SCADA, no generation loss is observed at 400kV Parbati_2(NH), 400kV Parbati_3(NH) and 400kV Sainj HEP(HP) as there was no generation at either of them.	1) 400 KV Parbati_2(NH)-Sainj(HP) (PKTCL) Ckt 2) 400 KV Parbati_3(NH)- Banala(PG) (PKTCL) Ckt
8	GD-1	Rajasthan	18-03-2025 10:00	18-03-2025 10:34	00:34	1035	0	1.757	0.000	58902	56730	i)Generation of 220kV Nokhra (IP) and 400kV AGE25L stations evacuate through 220 KV Nokhra SL_BHD2 (NTPC)-Bhadla_2 (PG) (NTPC_NOKHRA) Ckt and 400 KV AGE25L SL_BHD2_PG-Bhadla_2 (PG) (AGE25L) Ckt-1 respectively. ii)During antecedent condition, 220kV Nokhra (IP) and 400kV AGE25L were generating approx. 262 MW and 488 MW respectively (as per PMU). iii)As reported, at 09:59:46hrs Y-Phase CT of 405-52 bay at AGE25L RE station failed and it triggered Transformer Differential protection of main CB 404-52 and Tie CB 405-52 opened on Bus-Bar Zone-1 protection. iv)At 09:59:47 hrs, 400 KV AGE25L SL_BHD2_PG-Bhadla_2 (PG) (AGE25L) Ckt-1 tripped on R- Phase line differential protection. During inspection at site, spark in R-phase CVT was found and the same was replaced. v)As per PMU at 400kV Bhadla2(PG), Y-N fault cleared in 240msec followed by permanent R-N fault is observed is observed with fault clearing time of 80ms. vi)At the same time, 400/220kV 500MVA ICT-6 at Bhadla2(PG) and 220 KV NOKHRA SL_BHD2 (NTPC)-BHADLA_2 (PG) (NTPC_NOKHRA) CKT-1 also tripped. The reason for the same is yet to be received. vii)As per PMU, solar generation loss of approx. 487 MW at AGE25L(IP) and 262 MW at Nokra(IP) were observed. viii)As per SCADA, total Generation loss of 1035MW was observed in NR region.	1) 400/220 KV 500 MVA ICT 6 AT BHADLA_2 (PG) 2) 220 KV NOKHRA SL_BHD2 (NTPC)-BHADLA_2 (PG) (NOKHRA) CKT-1 3) 400 KV AGE25L SL_BHD2_PG-Bhadla_2 (PG) (AGE25L) Ckt-1
9	GI-2	Haryana	19-03-2025 19:13	19-03-2025 20:54	01:41	1035	0	2.094	0.000	49421	57326	i)During antecedent condition, 800kV HVDC Champa-Kurukshetra was carrying total 2578MW (Pole 01- 490 MW, Pole 02- 737MW, Pole 03- 716MW, Pole 04- 492MW). ii)As reported, at 19:13hrs Pole-2 and Pole-4 Tripped on T-Zone protection as Pole-2 protection was reading wrong values of DC current of parallel pole. Power shifted to remaining poles (Pole-1&3) and power order after the tripping were 1349 MW in Pole-1 and 1527 MW in Pole-3. iii)POWERGRID performed signal injection in control TB and affected lane was rebooted. The analog value of latched protection was found satisfactory. iv)As per PMU, fluctuation in voltage was observed. v) As per SCADA, no change in demand is observed in Haryana control area.	1) 800 KV HVDC KURUKSHETRA(PG) POLE-2 2) 800 KV HVDC KURUKSHETRA(PG) POLE-4
10	GD-1	Rajasthan	23-03-2025 09:34	23-03-2025 10:09	00:35	230	0	0.441	0.000	52157	53319	i)Generation of 220kV AEGPL(IP) stations evacuate through 220 KV BHADLA_2 (PG)-AEGPL_SL_BHD2_PG (AMP ENERGY GREEN PRIVATE LIMITED) CKT. ii)During antecedent condition, 220 KV BHADLA_2 (PG)-AEGPL_SL_BHD2_PG (AMP ENERGY GREEN PRIVATE LIMITED) CKT was generating approx. 230MW (as per PMU). iii)As reported, at 09:34hrs, 220 KV BHADLA_2 (PG)-AEGPL_SL_BHD2_PG (AMP ENERGY GREEN PRIVATE LIMITED) CKT tripped on B-N phase to earth fault. During the inspection it was found that there was cable failure in Feeder 5. iv)Due to tripping of 220 KV BHADLA_2 (PG)-AEGPL_SL_BHD2_PG (AMP ENERGY GREEN PRIVATE LIMITED) CKT , 220/33 KV, 150 MVA ICT-1 & 2 also tripped due to loss of evacuation path and 220KV AEGPL lost its connectivity from grid and blackout occurred in 220KV AEGPL S/s. v)As per PMU at 400kV Bhadla_2 S/s, no fault was observed. vi)As per PMU, solar generation loss of approx. 230 MW at AEGPL(IP) was observed.	1) 220 KV BHADLA_2 (PG)-AEGPL_SL_BHD2_PG (AMP ENERGY GREEN PRIVATE LIMITED) CKT

Details of Grid Events during the Month of March 2025 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
11	GD-1	Jammu & kashmir	26-03-2025 04:44	26-03-2025 06:26	01:42	6	21	0.014	0.045	42974	46931	i)220/66KV Leh has double main bus system. Nimmo Bazgo HEP is connected at 66kV level at 220/66kV Leh S/s. ii)During antecedent condition, 220 KV KHALSTI-LEH (PG) CKT-1 was carrying 12MW, while 220/66KV, 50MVA ICT-1 and ICT-2 were loaded 6 MW each. iii)As reported, at 04:44 hrs, 220KV Bus Bar protection operated due to flashover in GIS of Bus Coupler Bay resulting in outage of 220KV Khalsti-Leh Line & 220/66kV 50MVA ICT-1 at Leh (PG). Subsequently, 220KV Bus-2 and 220/66kV 50MVA ICT-2 also tripped (Details awaited). iv)Due to tripping of both the ICTs, the generator at Nimoo Bazgo HWP also tripped due to loss of evacuation path along with other 66KV feeders. This led to complete blackout of 220KV Leh substation. v)As per PMU, R-N phase to earth fault with fault clearance time of 120msec was observed. vi)As per SCADA, load loss of approx. 21 MW in J&K control area and generation loss of approx. 6 MW at Nimoo were observed.	i)220 KV LEH(JK) - BUS 1 ii)220/66 KV 50 MVA ICT 1 AT LEH(PG) iii)220 KV KHALSTI-LEH (PG) CKT-1
12	GD-1	HP & Haryana	26-03-2025 13:37	26-03-2025 16:02	02:25	0	113	0.000	0.224	57195	50427	i)220kV Pinjore(HR) and 220KV Baddi S/s has double main bus arrangement at 220kV side. ii)During antecedent condition, 220 KV Panchkula (PG)-Pinjore (HR) (HVPNL) Ckt-1 & Ckt-2 were carrying 136MW each, while 220KV Pinjore – Baddi Ckt1 & 2 were carrying 125MW each. (As per SCADA). Further, 220/66kV Baddi(HP) S/s was operating in split mode and load of 220/66kV was being fed from 220KV Pinjore – Baddi Ckt-1 & 2 iii)As reported, at 13:37 hrs, 220 KV Panchkula(PG)-Pinjore (HR) (HVPNL) Ckt-2 tripped on R-N phase to earth fault. The fault location was 30KM from Panchkula end, Z-2 distance protection operated. The fault current as reported by POWERGRID was 4.2KA but as per the DR submitted fault current was 3.8KA. It is pertinent to mention that due to tripping of Ckt-2 all the load shifted on 220 KV Panchkula(PG)-Pinjore (HR) (HVPNL) Ckt-1. iv)Further at 13:42 hrs, 220 KV Panchkula(PG)-Pinjore (HR) (HVPNL) Ckt-1 was manually hand tripped due to heavy sparking on Bus Isolator 20589 at Panchkula end. v)With the outage of 220kV Panchkula-Pinjore D/C, 220kV Pinjore station became dead and load of Baddi(HP) also got affected. vi)As per PMU at Panchkula(PG), R-N phase to earth fault is observed with delayed fault clearing time of 240msec. vii)As per SCADA, change in demand of approx. 113MW is observed in HP control area respectively. No change in demand of Haryana control area observed.	i)220 KV Panchkula(PG)-Pinjore (HR) (HVPNL) Ckt-2 ii)220 KV Panchkula(PG)-Pinjore (HR) (HVPNL) Ckt-1 iii)220 KV Pinjore(HR)-Baddi (HP) (HVPNL) Ckt-1 iv)220 KV Pinjore(HR)-Baddi (HP) (HVPNL) Ckt-2
13	GI-1	UK & HP	28-03-2025 07:31	28-03-2025 09:18	01:47	90	160	0.171	0.309	52576	51813	i)220 Khodri Sub station has double main Bus Bar system with 4 * 60MW generating units. ii)During antecedent condition, 220 KV KHODRI(UK)-MAJRI(HP) (UK) CKT-1 and CKT-2 were carrying 82MW load each, while 220 KV SAHARANPUR (UP) – KHODRI (UK) (UP) was carrying 19MW load (as per SCADA). iii)As reported, at 07:31 hrs, Bus Bar protection operated due to R phase CB blast of Unit 1 at Khodri. Due to bus bar protection operation, 220kV ..... As per DR of 220 KV KHODRI(UK)-MAJRI(HP) (UK) CKT-1 and Ckt2, R-N phase to earth fault can be observed along with Z-4 distance protection operation from Khodri end. iv)As per PMU, R-N phase to earth fault was observed in the system with delayed fault clearance of 240 msec observed. v)As per Disturbance short report submitted by UP SLDC, 220 KV SAHARANPUR(UP)-KHODRI(UK) (UP) CKT-1 tripped on R-N, transient earth fault, Z-3 and the fault current is 1.9KA . vi)220 KV SARSAWAN(UP)-KHODRI(UK) (UP) CKT-1 tripped on Z-1, R-N fault, fault distance: 85.22KM from Sarsawan(UP) end. The line did not open from Sarsawan end. vii)Due to tripping of 220kV Khodri-Majri D/C which were only feeding source at 220kV side at Majri (HP), load of 220/132kV Majri(HP) got affected. viii)As per SCADA, change in demand and generation of approx. 90 MW and 96 MW respectively in Himachal and Uttarakhand control area were observed. However, SLDC Uttarakhand and SLDC Himachal informed generation loss of 75MW and load loss of 160MW.	i)220 KV SAHARANPUR(UP)-KHODRI(UK) (UP) CKT-1 ii)220 KV SARSAWAN(UP)-KHODRI(UK) (UP) CKT-1 iii)220 KV KHODRI(UK)-MAJRI(HP) (UK) CKT-1 iv)220 KV KHODRI(UK)-MAJRI(HP) (UK) CKT-2
14	GD-1	Rajasthan	31-03-2025 13:43	31-03-2025 14:19	00:36	802	0	1.473	0.000	54433	43433	i)Generation of 220kV Azure Maple(IP) station evacuates through 220 KV Bhadla(PG)-Azure Maple PSS SL_BHD_PG (APMPL) (APMPL) Ckt-1 which was generating approx. 290 MW (as per PMU). Similarly, 220kV Azure 34(IP) station evacuates through 220 KV BHADLA(PG)-AZURE POWER 34 SOLAR(APTFL) (APTFL) CKT-1 which was generating 132MW (as per PMU). ii)As reported, at 13:43hrs, 220 KV Bhadla(PG)-Azure Maple PSS SL_BHD_PG (APMPL) (APMPL) Ckt-1 tripped on R-N phase to earth fault due to differential protection operation on account of tree fell on the line. At the same time 130 MVA 220/33KV ICT at 220kv Azure 34 also tripped on account of Differential relay protection (exact reason yet to be shared) iii)Due to tripping of 220 KV Bhadla(PG)-Azure Maple PSS SL_BHD_PG (APMPL) (APMPL) Ckt-1 and 130 MVA 220/33KV ICT1 at Azure34, Azure Maple(IP) and Azure 34 S/s lost its connectivity from grid and blackout occurred at 220kV Azure Maple(IP) and 220kV Azure 34(IP) S/s. iv)As per PMU at Bhadla(PG), R-N phase to earth fault (voltage dipped upto 0.95 p.u.) is observed with fault clearing time of 160ms. After the fault clearance voltage increased upto 1.04 p.u. v)As per PMU at Bassi(PG), a sharp drop in frequency is observed from 49.90 Hz to 49.82 Hz and frequency recovered to 49.91 Hz within 1 min. vi)As per SCADA, dip in NR total solar generation of approx. 802 MW is observed. vii)As per SCADA, solar generation loss of approx. 290MW at Azure Mapple, 132MW at Azure34, 115MW at TPREL and 115MW at AHEJ4L RE stations were observed. Drop in generation of TPREL and AHEJ4L is suspected due to LVRT non-compliance. Details is yet to be received from RE stations. viii)As per DR (Bhadla end) of 220 KV Bhadla(PG)-Azure Maple PSS SL_BHD_PG (APMPL) (APMPL) Ckt-1, R-N phase to earth fault (~7.3kA) with unsuccessful A/R operation is observed. 3-ph A/R was observed instead of 1-ph A/R.	i)220 KV Bhadla(PG)-Azure Maple PSS SL_BHD_PG (APMPL) Ckt-1 ii)220/33kV 130 MVA ICT1 at Azure 34

Details of Grid Events during the Month of March 2025 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	06-03-2025 06:47	06-03-2025 08:24	01:37	70	-	0.04%	-	74699	65838	At 06:47 hrs / 03-03-2025, 220 kV Bhuj-Chugger-1 tripped on Y-E fault from Chugger end only and autorecloser successful at Bhuj End. Due to loss of single evacuation transmission line 220 kV Chugger (SITAC) substation became dead. Generation loss of 70 MW occurred at Chugger (SITAC) Wind Power plant due to loss of evacuation path.	Tripping of following Elements: 1. 220 kV Bhuj-Chugger-1
2	GD-2	WR	12-03-2025 14:50	12-03-2025 20:00	05:10	2800	10000.00	3.70%	15.06%	75743	66419	On 12-03-2025, multiple events occurred in Central and South Gujarat. Complete loss of supply occurred at Eight(8) 400kV and forty two(42) 220kV substations in Central and South Gujarat system, leading to load loss of 3741 MW and generation loss of 2044 MW due to the multiple events **Event-1 (From 14:50 hrs to 15:00 hrs):** At 14:50 hrs / 12-03-2025, 400 kV Asoj-Kosamba-1 tripped on persistent Y-E fault, caused by a forest fire. This led to increased loading on parallel corridors from Central to South Gujarat. Simaltaneously, lines connected to 400 kV Gandhar and 400 kV Pirana(T) tripped unintendedly. 220 kV tie lines between Central and South Gujarat tripped on Over current protection.The cascade tripping of 400 kV & 220 kV transmission lines worsened the low voltage scenario in South Gujarat leading to tripping of major generation station in South Gujarat. **Event-2 (From 15:01 hrs to 15:35 hrs):**At 15:01 hrs / 12-03-2025, 400 kV Aurangabad(PG)-Boisar(PG)-1 line tripped on R-B phase-to-phase fault, due to snapping of R phase conductor. Subsequently, 220 kV TAPS(1&2)-Vapi(GJ)-1 and 220 kV Nashik-Navsari-1&2 tripped on over current protection operation. At 15:21Hrs, 400 kV Vav(GIS)-Navsari(PG)-1 line was manually tripped due to a fire in the wave trap at the Vav(GIS) end. As a consequence of these multiple trippings, the power supply to South Gujarat was solely dependent on the 400 kV Navsari(PG)-Jhanor-1 line. **Event-3 (From 15:35 hrs to 15:40 hrs):**At 15:35 hrs, an attempt was made to restore 400 kV Dehgam-Jhanor-1 from Jhanor end (to strengthen supply to South Gujarat). However, this line tripped again from Jhanor end shortly after being energized. The situation was further worsened by tripping of 400kV Navsari(PG)-Jhanor--1 (sole supply line) from Navsari(PG) end only (suspected unintended operation). The tripping of the 400 kV Navsari(PG)-Jhanor-1 line resulted in a complete power supply failure at several critical substations in South Gujarat, including Gandhar, Sugen, Vav(GIS), Ukai, and Kosamba. **Event-4 (From 15:40 hrs to 15:45 hrs):**At 15:40 Hrs, an attempt was made to restore power supply by closing the 400 kV Pirana(T)-Sugen-1 line from the Pirana(T) end as the line was closed from Sugen end. This action successfully extended the power supply to the previously affected substations Gandhar, Sugen, Vav(GIS), Ukai, and Kosamba. However, due to insufficient load demand in that area, the 400 kV Pirana(T)-Sugen-1 line tripped again. The tripping occurred due to overvoltage, triggered by the Direct Transfer (DT) signal received from Sugen end.	Complete loss of supply occurred at Eight(8) 400kV and forty two(42) 220kV substations in Central and South Gujarat system.Tripping of following Generating Units: 1. Ukai(H)-U#2 (75 MW) 2. KAPS-U#1 (220 MW) 3. SLPP-U#3 (125 MW) 4. KAPS-U#3 (700 MW) 5. KAPS-U#4 (700 MW) 6. SLPP-U#1 (125 MW) 7. SLPP-U#2 (125 MW) 8. Ukai(T)-U#4 (200 MW) 9. Ukai(T)-U#3 (200 MW) 10. Ukai(T)-U#6 (500 MW) 11. TAPS-U#3 (540 MW)
3	GD-1	WR	14-03-2025 18:08	14-03-2025 18:48	00:40	920	650.00	1.25%	1.12%	73840	57899	**Multiple Tripping Incidents in Korba(W)** At 16:01 hrs / 14-03-2025, Korba(W)-Unit-3 (210 MW) tripped on generator differential protection operation. Simaltaneously, 400/220 kV Korba(W)-ICT-1 tripped due to fire as reported by Chhattisgarh SLDC. Further, at 16:40 hrs / 14-03-2025, Korba(W)-Unit-4 (210 MW) tripped on generator differential protection operation and 400 kV Korba(W) Extension-Marwa-1 tripped due to fire as reported by Chhattisgarh SLDC. At, 18:06 hrs / 14-03-2025 Korba(W)-Unit-5 (210 MW) tripped due to fire as reported by Chhattisgarh SLDC and at 18:10 hrs 400 kV Korba(W) Extension-Bhilai-1 and 400 kV Korba(W)-Raita-1 tripped due to Bus bar protection operation. Due to these tripping 400/220 kV Korba(W) substation became dead resulting in Generation loss of 920 MW and load loss of 650 MW in downstream network.	Tripping of following Elements: 1. Korba(W)-Unit-3,4&5 (210 MW) 2. 400/220 kV Korba(W)-ICT-1 3. 400 kV Korba(W) Extension-Marwa-1 4. 400 kV Korba(W) Extension-Bhilai-1 5. 400 kV Korba(W)-Raita-1
4	GI-2	WR	15-03-2025 08:53	15-03-2025 10:11	01:18	1700	-	2.59%	-	65705	52637	At 08:53 hrs / 15-03-2025, while availing planned shutdown of 400 kV Khavda(KPS1)-Bus-1 for carrying out the HV test and bus bar stability, 400 kV Khavda(KPS1)-Bus-2, 400 kV Khavda(KPS1)-Khavda(KPSS1)-1, 400 kV Khavda(KPS1)-Khavda(KPSS2)-1, 400 kV Khavda(KPS1)-Khavda(KPSS3)-1 and 765/400kV Khavda(KPS1)-ICT-1, 2,&3 tripped. Ideally, in case of N-1 contingency of 400 kV Khavda(KPS1)-Bus-2, the three lines should have been in service through the three ICTs but the ICTs tripped on Backup Impedance relay operation. Due to loss of single evacuation transmission line 400 kV Khavda(KPSS1), 400 kV Khavda(KPSS2) and 400 kV Khavda(KPSS3) substations became dead, leading to around 1700 MW Generation loss.	Tripping of following Elements: 1. 400 kV Khavda(KPS1)-Bus-2, 2. 400 kV Khavda(KPS1)-Khavda(KPSS1)-1, 3. 400 kV Khavda(KPS1)-Khavda(KPSS2)-1, 4. 400 kV Khavda(KPS1)-Khavda(KPSS3)-1 5. 765/400kV Khavda(KPS1)-ICT-1, 2,&3
5	GD-1	WR	31-03-2025 10:54	31-03-2025 11:29	00:35	600	-	0.73%	-	81839	71392	At 10:54 hrs / 31-03-2025, 400 kV SKS-Kotra-1 tripped from SKS end only on B-E fault. Subsequently, at 10:56 hrs 400 kV SKS-Kotra-2 tripped on R-E fault from both ends. During inspection, internal flashover was observed in R phase wavetrap of 400 kV SKS-Kotra-2 at Kotra end. Due to loss of double circuit evacuation transmission lines 400 kV SKS thermal substation became dead. Generation loss of 600 MW occurred at 400 kV SKS thermal substation due to the event.	Tripping of following Elements: 1. 400 kV SKS-Kotra-1 2. SKS-Unit-1&2 (300 MW)

Details of Grid Events during the Month of March 2025 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	No GD-GI event in March 2025												

Details of Grid Events during the Month of March 2025 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA, TAMILNADU	03-03-2025 18:17	03-03-2025 19:14	00:57	0	240	0.00%	0.46%	46649.5	52397.33	Complete Outage of 230kV/110kV Hosur_TN SS of TANTRANSCO and de-energization of Bus-2 of 220kV/66kV Yerrandahalli SS of KPTCL: As per the reports submitted, 230kV Hosur_TN Hosur_PG line-1 and 2 tripped at 230kV Hosur_TN SS due to suspected maloperation of SPS at 230kV Hosur_TN SS which was envisaged during the radial assistance from 230kV Hosur_TN SS to 230kV Yerandahally SS during the shutdown period of 400kV Somanahally Mylasandra line. At the same time, tripping of 110kV feeders on operation of df/dt st-1 and st-2 at 230kV Hosur_TN SS were also reported. Subsequently, at 18:36hrs, YB-N fault was observed in 230kV Mettur_Auto Hosur line becuase of jumper cut at Loc No. 394. At both ends, zone-1 protection operated and the line tripped. Tripping of only connected source led to complete outage of 230kV/110kV Hosur_TN SS of TANTRANSCO and de-energization of Bus-2 of 220kV/66kV Yerrandahalli SS of KPTCL.	220KV-YERRAANDAHALLI-HOSUR-1, 230KV-METTURAUTO-HOSUR-1
2	GD - 1	KARNATAKA	04-03-2025 14:57	04-03-2025 16:42	01:45	0	124	0.00%	0.19%	51205.23	66970.73	Complete Outage of 220kV/66kV Chikkamangaluru SS: 220kV/66kV Chikkamangaluru is radially fed from 220kV MRS Shimoga Chikkamangaluru, 220kV Hassan_PG Chikkamanagaluru. As per the reports submitted,at 14:57hrs, the triggering incident was B-N fault in 220kV MRS Shimoga Chikkamangaluru and the line tripped. At 15:08hrs, YB-N fault was observed in 220kV Hassan_PG Chikkamanagaluru. At Hassan end, the fault was sensed in zone-1. Line was holding at Chikkamanagaluru end. Tripping of the only connected line led to complete outage of 220kV/66kV Chikkamangaluru SS.	220KV-HASSAN-CHIKKAMAGALURU-1, 220KV-CHIKKAMAGALURU-MRS SHIMOGA-1
3	GD - 1	KARNATAKA	05-03-2025 21:31	05-03-2025 22:19	00:48	0	190	0.00%	0.36%	44418.14	53485.98	Complete Outage of 220kV/110kV Puttur SS: The triggering incident was 110kV Bus fault at Puttur substation due to the failure of the clamp connecting 110kV Main Bus-1 and the extension bus, resulting in the snapping of the Y-phase bus extension jumper. The fault was being fed through 3 100MVA Puttur Transformers-1,2&7 which were fed from 220kV Puttur Kemar Line-1&2. Immediately, 100MVA Puttur Transformer-2 & 7 tripped due to the operation of the 110kV side Y-phase OCR high-set. Before the tripping of 100MVA Transformer-1, both 220kV Puttur Kemar Line-1&2 tripped at the Puttur end on Non directional Definite time Over current protection. This resulted in the de-energization of the 220kV Bus of 220kV/110kV Puttur SS and Complete Outage of 220kV/110kV Puttur SS.	220KV-PUTTUR-KEMAR-1, 220KV-PUTTUR-KEMAR-2
4	GD - 1	KARNATAKA	06-03-2025 13:10	06-03-2025 13:30	00:20	0	115	0.00%	0.18%	53027.09	65241.44	Complete Outage of 220kV/66kV Exora SS, 220kV/66kV Vikas Tech and 220kV Bus-1 Outage at 220kV/66kV Malur SS of KPTCL: 220kV Malur SS was operating with split bus condition with 220kV Hoody Malur line feeding 220kV Malur Bus-1. 220kV/66kV Exora and 220kV/66kV Vikas Tech Park were being radially fed from 220kV Malur Bus-1. As per the reports submitted, the triggering incident was RN fault in 220kV Hoody Malur line. Tripping of this line led to loss of power supply to 220kV Malur Bus-1 which intrun led to complete outage of 220kV Exora SS and 220kV Vikas Tech Park.	220KV-HOODY-MALUR-1
5	GD - 1	KARNATAKA	07-03-2025 13:10	07-03-2025 13:33	00:23	0	344	0.00%	0.51%	54018.5	67121.19	Complete outage of 220kV/66kV Naganathpura SS, 220kV/66kV HSR SS, 220kV/66kV Koramangala SS, 220kV/66kV Nimhans SS of KPTCL: During antecedent conditions, 220kV EDC Nimhans, 220kV HSR Hoody, 220kV HSR EPIP were under open condition. As per the reports submitted, the triggering incident was RY-N fault in 220kV HSR Mylasandra Line. At HSR end, the fault was sensed in zone-1 and the line tripped immediately. At Naganathpura end, the fault was pickedup in zone-3 and the line was holding. At the same time, 220kV Mylasandra HSR line-1 tripped on zone-1 at Mylasandra end. Subsequently, 220kV Mylasandra HSR Line-2 and 220kV Mylasandra Naganathpura lines tripped on zone-2 at Mylasansra end. Tripping of all these lines led to complete outage of 220kV/66kV Naganathpura SS, 220kV/66kV HSR SS, 220kV/66kV Koramangala SS, 220kV/66kV Nimhans SS.	220KV-MYLASANDRA-HSR-1, 220KV-HSR-MYLASANDRA-2, 220KV-NAGNATHPURA-MYLASANDRA-2
6	GD - 1	TELANGANA	10-03-2025 16:02	10-03-2025 16:23	00:21	0.15	0	0.00%	0.00%	57458.33	66259.78	Complete Outage of 400kV/11kV Medaram LIS: During antecedent condition, 400kV Ramadugu Medaram line-2 was under outage due to relay testing works. Triggering incident was tripping of 400kV Ramadugu Medaram line-1 only at Medaram end due to suspected maloperation. Tripping of the only connected line resulted in the complete outage of 400kV/11kV Medaram LIS. During this event there was no pump load.	400KV-MEDARAM_GIS-RAMADUGU-1
7	GD - 1	KARNATAKA	11-03-2025 13:43	11-03-2025 16:48	03:05	0	60	0.00%	0.10%	52941.12	62755.02	Complete Outage of 220kV/110kV MK Hubli SS of KPTCL: 220kV/110kV MK Hubli SS is radially fed from 400kV/220kV Narendra_PG SS. Triggering incident was RY fault in 220kV MK Hubli Narendra_PG line-1 and 2 at a distance of 4.8km from Narendra_PG end due to fire under tower no. 19 and 20. Tripping of both connected lines resulted in the complete outage of 220kV/110kV MK Hubli SS.	220KV-NARENDRA-M K HUBLI-2, 220KV-NARENDRA-M K HUBLI-1
8	GD - 1	TAMILNADU	12-03-2025 09:59	12-03-2025 18:59	09:00	0	0	0.00%	0.00%	55152.84	65325.77	Complete Outage of 230kV/110kV ETPS Generating Station of TANTRANSCO: 230kV ETPS Power house was dismantled and the the 230kV ETPS switch yard was being radially fed from 230kV ETPS Manali line. The 230kV ETPS Switch Yard consists of a 230kV/110kV ETPS Transformer and 4 no.s of 110kV feeders which are idle charged. As per the reports submitted, the triggering incident was an RY-N fault in 230kV ETPS Manali line at location no. 21&26\. At Manali end, the fault was sensed in zone-2 and line tripped after around 420ms. The line was holding at ETPS end. Tripping of the only connected line led to complete outage 230kV ETPS Power House.	230KV-ETPS-MANALI-1
9	GD - 1	TELANGANA	12-03-2025 10:21	12-03-2025 11:15	00:54	13	0	0.02%	0.00%	55531.66	65578.48	Complete Outage of 220kV Pulichintala PH of TGGENCO: As per the reports submitted, the LBB of 220kV bus mal operated at 220kV Pulichinthala PH. Immediately, all elements connected to the 220kV Bus tripped and this led to complete outage of 220kV Pulichinthala PH.	220KV-CHILLAKALLU-PULICHINTALA-1, 220KV-SITAPURAM-PULICHINTALA-1, PULICHINTALA - UNIT 2
10	GD - 1	KARNATAKA	14-03-2025 12:01	14-03-2025 12:29	00:28	0	408	0.00%	0.64%	51476.72	63895.46	Complete Outage of 220kV/66kV Yerrandahally SS, 220kV/66kV Jigani SS, 220kV/66kV Electronic City SS: The triggering incident was R-N fault in 220kV Somanahally Mylasandra Line-1 and the line tripped. After 3S, R-N fault was observed in 220kV Somanahally Electronic city line and the line tripped. Subsequently, 220kV Somanahlly Mylasandra Line-2 and 220kV Electronic city Shobha dreams lines tripped on over loading. Tripping of all these lines led to loss of power supply to 220kV/66kV Yerrandahally SS, 220kV/66kV Jigani SS, 220kV/66kV Electronic City SS.	220KV-SOMANAHALLI-ELECTRONIC_CITY-1, 220KV-SHOBHA_DREAMS-ELECTRONIC_CITY-1, 220KV-SOMANAHALLI-MYLASANDRA-1, 220KV-SOMANAHALLI-MYLASANDRA-2

Details of Grid Events during the Month of March 2025 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
11	GD - 1	KARNATAKA	15-03-2025 12:42	15-03-2025 12:54	00:12	0	457	0.00%	0.71%	52855.46	64594.85	Complete Outage of 220kV/66kV Yerrandahally SS, 220kV/66kV Jigani SS, 220kV/66kV Electronic City SS: 220 kV Somanahalli - Mylasandra line 1 & 2 tripped at 12:42 Hrs and 12:45 hrs respectively at both ends on distance protection. At the same time 220kV Somanahalli - Khodays and 220kV Somanahalli- Keonics City lines tripped on operation of distance protection. This resulted in complete outage of 220kV/66kV Yerrandahally SS, 220kV/66kV Jigani SS, 220kV/66kV Electronic City SS.	220KV-SOMANAHALLI-ELECTRONIC_CITY-1, 220KV-SHOBHA_DREAMS-ELECTRONIC_CITY-1, 220KV-SOMANAHALLI-MYLASANDRA-1, 220KV-SOMANAHALLI-MYLASANDRA-2
12	GD - 1	ANDHRA PRADESH	17-03-2025 11:45	17-03-2025 11:54	00:09	0	157	0.00%	0.23%	54555.45	68741.33	Complete Outage of 220/132kV Koduru and Rajampet: At 11:25 Hrs, the 220kV Cuddapah-Rajampet line tripped due to a B-N fault. Following the tripping of the 220kV Cuddapah-Rajampet line, the Koduru and Rajampet section became radially connected to Renigunta. At 11:45 Hrs, the 220 kV Renigunta-Koduru line tripped due to a Y-B fault, with the fault sensed only at Renigunta in Z2 resulting in a 3-phase trip at Renigunta. This caused the complete outage of the 220/132 kV Koduru and Rajampet substations.	220KV-CUDDAPAH-RAJAMPET-1, 220KV-RENIGUNTA-KODURU-1
13	GD - 1	KARNATAKA	19-03-2025 14:09	19-03-2025 14:25	00:16	0	126	0.00%	0.18%	53293.16	68849.46	Complete Outage of 220kV/66kV Exora SS, 220kV/66kV Vikas Tech and 220kV Bus-1 Outage at 220kV/66kV Malur SS of KPTCL: 220kV Malur SS was operating with split bus condition with 220kV Hoody Malur line feeding 220kV Malur Bus-1. 220kV/66kV Exora and 220kV/66kV Vikas Tech Park were being radially fed from 220kV Malur Bus-1. As per the reports submitted, the triggering incident was RN fault in 220kV Hoody Malur line. Tripping of this line led to loss of power supply to 220kV Malur Bus-1 which inturn led to complete outage of 220kV Exora SS and 220kV Vikas Tech Park.	220KV-HOODY-MALUR-1
14	GD - 1	TAMILNADU	19-03-2025 14:40	19-03-2025 14:55	00:15	0	161	0.00%	0.24%	52720.39	68053.5	Complete Outage of 230kV/110kV Veerapuram SS: During antecedent conditions, due to outage of 230kV Veerapuram SPKoil line and 230kV Veerapuram Cuddalore line 1& 2 on power regulation, 230kV/110kV Veerapuram SS was radially fed from 230kV Kalvindapattu Veerapuram line and 110kV Veerapuram SP Koil line-2. The triggering incident was RN fault in 230kV Kalvindapattu Veerapuram line and the line tripped. Subsequently, 110kV Veerapuram SP Koil line-2 tripped on overloadeing. Tripping of the only connected line resulted in complete loss of supply to 230kV/110kV Veerapuram SS.	230KV-KALVENDAPATTU-VEERAPURAM
15	GD - 1	KERALA	21-03-2025 20:08	21-03-2025 20:50	00:42	0	232	0.00%	0.43%	44566	53751	Complete Outage of 220kV/110kV Palakkad_KL SS of KSEB: As per the reports submitted, the triggering incident was Y-N fault in 220kV Madakathara Palakkad line. At both ends, fault was sensed in zone-1 and Y-pole opened. During A/R dead time, B-N fault was observed in 220kV Madakathara Palakkad line. During this fault DEF protection in 220kV Elapully Palakkad line-1,2&3 at Elupally end . DT was sent to Palakkad end and the lines tripped. Tripping of all these lines led to complete outage of 220kV/110kV Palakkad_KL SS.	220KV-ELAPULLY-PALAKKAD(KL)-2, 220KV-ELAPULLY-PALAKKAD(KL)-3, 220KV-ELAPULLY-PALAKKAD(KL)-1, 220KV-PALAKKAD-MADAKATHARA-1
16	GD - 1	TAMILNADU	23-03-2025 12:44	23-03-2025 16:06	03:22	285	0	0.57%	0.00%	49653.5	60201.42	Complete Outage of 400kV SEPC Generating Station: During antecedent conditions, 400kV SEPC Ottapidaram Line-1 was under emergency shutdown for R-phase CVT replacement. As per the reports submitted, while attending DC leakage in 400kV SEPC Ottapidaram line-1 at Ottapidaram end, DT was sent to SEPC(both in Main-1 and Main-2) end and the line tripped only at SEPC end. Tripping of the only connected line led to complete outage of 400kV SEPC Generating station. Subsequently, SEPC Generating Unit-1 tripped on loss of evcuation.	400KV-OTTAPIDARAM-SEPC-2, SEPC - 400KV - Bus 1, SEPC - 400KV - Bus 2, 400KV/21KV SEPC-GT-1, SEPC - UNIT 1
17	GD - 1	ANDHRA PRADESH	28-03-2025 17:07	28-03-2025 17:50	00:43	163	0	0.33%	0.00%	49644.09	65243.91	Complete Outage of 220kV Upper Sileru PH of APGENCO: As per the reports submitted, the triggering inicdent was LBB operation while deparalleling Upper Sileru Unit-1. Immedeately, all elements connected to 220kV Bus-1 and Bus-2 tripped. This led to complete outage of 220kV upper Sileru PH.	220KV-DONKARAYI-UPPER_SILERU-1, 220KV-PENDURTHI-UPPER_SILERU-1, UPPER_SILERU - 220KV - Bus 1, UPPER_SILERU - 220KV - Bus 2
18	GD - 1	KARNATAKA	28-03-2025 17:59	28-03-2025 18:22	00:23	0	131	0.00%	0.22%	48157	58781	Complete Outage of 220kV/66kV Nagnatpura SS of KPTCL: As per the reports submitted, the triggering incident was RYB fault in 66kV/11kV Transformer-1 of 220kV/66kV Nagnatpura SS. The fault was cleared by tripping of 220kV Nagnatpura Mylasandra line and 220kV Nagnatapura HSR line. Tripping of both lines led to comlplete outage of 220kV/66kV Nagnatpura SS.	220kV Nagnatpura Mylasandra line 220kV Nagnatapura HSR line.
19	GI-1	KARNATAKA	12-03-2025 07:26	12-03-2025 07:49	00:23	0	0	0.00%	0.00%	47861.32	61295.91	Tripping of 220kV Bus-2 of Narendra_PG SS: As per the reports submitted, the triggering incident was maloperation of LBB initiation in 211 bay (corresponds to 220kV Narendra MK Hubli-1) line due to auxillary relay maloperation. After 200ms, LBB trip operated and all elements connected to 220kV Narendra Bus-2 tripped.	220KV-NARENDRA-MAHALINGAPURA-2, 220KV-NARENDRA-M K HUBLI-1, 220KV-NARENDRA-GHATPRABHA-2, NARENDRA - 220KV - Bus 2, 400KV/220KV NARENDRA-ICT-1
20	GI-1	TAMILNADU	12-03-2025 10:32	12-03-2025 11:06	00:34	0	0	0.00%	0.00%	55331.02	65690.7	Tripping of 230kV Bus-1 and Bus-2 of 400kV/230kV SV Chatram SS of TANTRANSCO: As per the reports submitted, the triggering incident was B-phase CT failure in 230kV Bus coupler of 400kV/230kV SV Chatram SS. At SV Chatram, both 230kV Bus-1 and Bus-2 BBP operated and all elements connected to the 230kV Buses tripped except 400kV/230kV SV Chatram ICT-2 as 96 relay of the ICT-2 failed to operate. After around 500ms, 400kV/230kV SV Chatram ICT-2 tripped on operation of Bucholz relay. This led to loss of power supply to 230kV Bus-1 and Bus-2 of 400kV/230kV SV Chatram SS.	400KV/230KV SUNGAVARACHATRAM-ICT-1, 400KV/230KV SUNGAVARACHATRAM-ICT-2, 230KV-ORAGADAM-SUNGAVARACHATRAM-1, 230KV-ORAGADAM-SUNGAVARACHATRAM-2, 230KV-MAMBAKAM-SUNGAVARACHATRAM-1, 230KV-NOKIA-SUNGAVARACHATRAM-1
21	GI-1	KARNATAKA	18-03-2025 05:47	18-03-2025 06:28	00:41	0	82	0.00%	0.14%	43247.77	57217.73	Tripping of 220kV Bus-1 of 220kV/110kV Hubli SS: The triggering incident was B-ph jumper failure on the 220kV Hubli-Bidnal line-1 line between CT and wave trap which led to Z1 fault at Bidnal and a Z2 fault at Hubli end. The fault at Bidnal resulted in a 3-phase trip, while at Hubli, the absence of carrier signal led to a Z2 time trip. During the same time Bus-1 BBP tripped at Hubli, which led to the tripping of 220kV Bus-1 of 220kV/110kV Hubli SS.	220KV-HUBLI-BIDNAL-1, 220KV-NAGJHERI-HUBLI-1, 220KV-HUBLI-NARENDRA_KP-1

Details of Grid Events during the Month of March 2025 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Tezu and Namsai areas of Arunachal Pradesh Power System	10-03-2025 09:58	10-03-2025 10:49	00:51	0	3	0.00%	0.15%	1672	2065	Tezu and Namsai areas of Arunachal Pradesh Power System were connected with rest of NER Grid through 132 kV Roing – Tezu line. At 09:58 Hrs of 10-03-2025, 132 kV Roing – Tezu line tripped. Due to tripping of this element, Tezu and Namsai areas of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Roing – Tezu line at 10:49 Hrs of 10-03-2025.	132 kV Roing-Tezu Line
2	GD I	Tipaimukh area of Manipur Power System	13-03-2025 09:36	13-03-2025 10:40	01:04	0	1	0.00%	0.05%	1515	1824	Tipaimukh area of Manipur Power System was connected with rest of NER Grid through 132kV Aizawl-Tipaimukh and 132kV Jiribam-Tipaimukh lines. At 09:37 Hrs of 13-03-2025, 132 kV Aizawl-Tipaimukh and 132 kV Jiribam-Tipaimukh lines tripped. Due to tripping of these elements, Tipaimukh area of Manipur Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Tipaimukh area of Manipur Power System by charging 132kV Aizawl-Tipaimukh line at 10:40 Hrs of 13-03-2025.	132 kV Aizawl-Tipaimukh and 132 kV Jiribam-Tipaimukh lines
3	GD I	Tipaimukh area of Manipur Power System	15-03-2025 12:35	15-03-2025 14:03	01:28	0	1	0.00%	0.05%	1301	1903	Tipaimukh area of Manipur Power System was connected with rest of NER Grid through 132kV Aizawl-Tipaimukh and 132kV Jiribam-Tipaimukh lines. At 12:35 Hrs of 15-03-2025, 132 kV Aizawl-Tipaimukh and 132 kV Jiribam-Tipaimukh lines tripped. Due to tripping of these elements, Tipaimukh area of Manipur Power System got isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Tipaimukh area of Manipur Power System by charging 132 kV Aizawl-Tipaimukh line at 14:03 Hrs of 15-03-2025.	132 kV Aizawl-Tipaimukh and 132 kV Jiribam-Tipaimukh lines
4	GD I	Tezu and Namsai areas of Arunachal Pradesh Power System	18-03-2025 15:56	18-03-2025 21:14	05:18	0	8	0.00%	0.39%	1740	2047	Tezu and Namsai areas of Arunachal Pradesh Power System were connected with rest of NER Grid through 132 kV Roing – Tezu line. At 15:56 Hrs of 18-03-2025, 132 kV Roing – Tezu line tripped. Due to tripping of this element, Tezu and Namsai areas of Arunachal Pradesh Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Roing – Tezu line at 21:14 Hrs of 18-03-2025.	132 kV Roing – Tezu line
5	GD I	Tuirial S/S of NEEPCO & Kolasib and Bairabi areas of Mizoram Power system	20-03-2025 14:24	20-03-2025 15:26	01:02	0	6	0.00%	0.30%	1531	2026	Kolasib area of Mizoram Power System was connected with rest of NER Grid through 132 kV Kolasib-Badarpur and 132 kV Kolasib – Aizawl lines. Turial and Bairabi S/S are connected with Kolasib via 132 kV Kolasib – Turial line and 132 kV Kolasib – Bairabi line. At 14:24 Hrs of 20-03-2025, 132 kV Aizawl-Kolasib and 132kV Badarpur-Kolasib lines tripped. Due to tripping of these elements, Kolasib, Turial and Bairabi areas of Mizoram Power system got isolated from NER grid and collapsed due to no source available in these areas. Power supply was extended to Kolasib area by charging 132 kV Aizawl-Kolasib line at 15:26 Hrs of 20-03-2025.	132 kV Aizawl-Kolasib and 132kV Badarpur-Kolasib lines

Details of Grid Events during the Month of March 2025 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
6	GD I	132 kV Kameng S/S of NEEPCO & Khupi and Seppa areas of Arunachal Pradesh Power system	23-03-2025 18:18	23-03-2025 19:41	01:23	0	3	0.00%	0.11%	2794	2695	132 kV Kameng S/S of NEEPCO and Khupi and SEPPA areas of Arunachal Pradesh Power System were connected with rest of NER Grid through 132 kV Tenga-Khupi line and 132 kV Kameng-Khupi line and 400/132 kV ICT at Kameng. At 18:18 Hrs of 23.03.2025, 400/132 kV ICT at Kameng and 132 kV Tenga-Khupi line tripped. Due to these trippings, 132 kV Kameng S/S, Khupi and Seppa areas resulting in grid disturbance at 132 kV Kameng S/S of NEEPCO and Khupi & Seppa areas of Arunachal Pradesh got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was restored to Khupi area of Arunachal Pradesh Power System by charging 132kV Tenga-Khupi line at 19:41 Hrs of 23.03.2025.	400/132 kV ICT at Kameng and 132 kV Tenga-Khupi line
7	GD I	Mawlyndep area of Meghalaya Power System	23-03-2025 12:09	23-03-2025 12:32	00:23	0	12	0.00%	0.62%	1319	1946	Mawlyndep area of Meghalaya Power System was connected with rest of NER Grid through 132 kV NEHU-Mawlyndep & 132 kV Mawlyndep-Mustem lines. At 12:09 Hrs of 23-03-2025, 132 kV Mawlyndep-Mustem and 132 kV Mawlyndep-NEHU lines tripped. Due to tripping of these elements, Mawlyndep area of Meghalaya Power system got isolated from NER grid and collapsed due to no source available in this area. Power supply was extended to Mawlyndep area of Meghalaya Power System by charging 132 kV Mawlyndep-NEHU line at 12:32 Hrs of 23-02-2025.	132 kV Mawlyndep-Mustem and 132 kV Mawlyndep-NEHU lines
8	GD I	Loktak S/S of NHPC and radially connected Rengpang area of Manipur Power System	24-03-2025 11:38	24-03-2025 13:05	01:27	0	1	0.00%	0.05%	1369	2106	Loktak S/S of NHPC and Rengpang area of Manipur power system were connected with rest of NER grid through 132 kV Loktak-Jiribam, 132 kV Loktak-Imphal(PG), 132 kV Loktak-Ningthoukhong and 132 kV Loktak-Rengpang lines. Prior to the event, 132 kV Loktak-Imphal(PG) line was under planned shutdown and all units of Loktak were withdrawn as per schedule. Also, 132 kV Jiribam(MA)-Rengpang line was under outage since 17-11-2023. At 11:38 Hrs of 24.03.2025, 132 kV Loktak-Jiribam, 132 kV Loktak-Ningthoukhong and 132 kV Loktak-Rengpang lines tripped resulting in blackout of Loktak S/S of NHPC and Rengpang area of Manipur. Power supply was extended to Loktak by charging 132 kV Loktak – Jiribam line at 13:05 Hrs of 24-03-2025.	132 kV Loktak-Jiribam, 132 kV Loktak-Ningthoukhong and 132 kV Loktak-Rengpang lines
9	GD I	Gohpur area of Assam power system	26-03-2025 17:38	26-03-2025 18:52	01:14	0	0	0.00%	0.00%	2500	2890	Gohpur area of Assam power system was connected with the rest of the NER grid through 132 kV Gohpur-Nirjuli, 132 kV Gohpur-BNC(PG), 132 kV Gohpur-Itanagar, 132 kV Gohpur-North Lakhimpur D/C lines & 132 kV Gohpur-BNC(AS) D/C lines. Prior to the event, 132 kV BNC(PG) - Gohpur line was under emergency shutdown. Also, Assam requested for shutdown of 132 kV Bus section of Gohpur S/S, hence opening of following lines along with Bus Sectionalizer: 1. 132 kV Nirjuli- Gohpur Line 2. 132 kV Chimpu (Itanagar)- Gohpur Line (LILO) At 17:38 Hrs of 26.03.2025, 132 kV Gohpur Bus tripped during opening of the bus sectionalizer due to flashover in CB of bus sectionalizer resulting in tripping of 132 kV Gohpur-BNC(AS) D/C and 132 kV Gohpur-North Lakhimpur D/C lines. This led to blackout of 132 kV Gohpur S/S. Power supply was extended to Gohpur SS by charging 132 kV Gohpur -Nirjuli Line at 18:52 Hrs of 26-03-2025.	132 kV Gohpur-BNC(AS) D/C and 132 kV Gohpur-North Lakhimpur D/C lines
10	GD I	Rengpang area of Manipur power system	29-03-2025 10:52	29-03-2025 11:13	00:21	0	1	0.00%	0.04%	1369	2427	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132 kV Loktak-Rengpang line. Prior to the event,132 kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 10:52 Hrs of 29-03-2025, 132 kV Loktak-Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply is restored in Rengpang area of Manipur Power System by charging 132 kV Loktak-Rengpang line at 11:13 Hrs of 29-03-2025.	132 kV Loktak-Rengpang line
11	GD I	Thoubal(Old) area of Manipur power system	29-03-2025 14:27	29-03-2025 17:45	03:18	0	11	0.00%	0.44%	1484	2475	Thoubal(Old) area of Manipur power system was connected to rest of NER grid through 132 kV Thoubal(New)-Thoubal(Old) & 132 kV Thoubal(Old)-Kakching lines. At 14:27 Hrs 29-03-2025, due to wildfire near Thoubal S/S, 132 kV Thoubal(Old)-Kakching, 132 kV Thoubal(New) – Kongba I and 132 kV Thoubal(New) – Kakching lines tripped. Also, 400/132 kV ICT at Thoubal and 132 kV Thoubal(New) –Thoubal(Old) lines were hand tripped due to which blackout at Thoubal(old) S/S occurred. Power was extended to Thoubal(old) S/S by charging 400/132 kV ICT at Thoubal at 17:45 Hrs of 29-03-2025.	132 kV Thoubal(Old)-Kakching, 132 kV Thoubal(New) – Kongba I, 132 kV Thoubal(New) – Kakching lines, 400/132 kV ICT at Thoubal and 132 kV Thoubal(New) –Thoubal(Old) lines
12	GD I	Thoubal(Old) area of Manipur power system	29-03-2025 21:56	30-03-2025 00:31	02:35	0	8	0.00%	0.29%	2190	2775	Thoubal(Old) area of Manipur power system was connected to rest of NER grid through 132 kV Thoubal(New)-Thoubal(Old) & 132 kV Thoubal(Old)-Kakching lines. Prior to the event, 132 kV Thoubal(New) – Kongba I, 132 kV Thoubal(New) – Kakching I and 132 kV Thoubal(Old) - Kakching lines tripped at 14:27 Hrs of 29-03-2025. At 21:56 Hrs, 132 kV Thoubal (New) – Kongba II, 132 kV Thoubal (New) –Thoubal(Old) lines and 315 MVA, 400/132 kV ICT at Thoubal were hand tripped due to wildfire near the Thoubal S/S of Manipur Power system due to which blackout at Thoubal(old) S/S occurred. Power supply is restored in Thoubal(Old) area of Manipur Power System by charging 132 kV Thoubal (New) - Thoubal(Old) line at 00:31 Hrs of 30-03-2025.	132 kV Thoubal (New) – Kongba II, 132 kV Thoubal (New) –Thoubal(Old) lines and 315 MVA, 400/132 kV ICT at Thoubal

21. NEW ELEMENTS CHARGED IN MARCH 2025

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
ER	1	Barh, Bihar	NTPC BARH -UNIT 3(Stage-1)	3/Coal	660	1980	21.03.2025
	2	Chandwa, Jharkhand	NTPC NORTH KARANPURA - UNIT 3	3/Coal	660	1980	19.03.2025
	3	Patratu,Jharkhand	PVUNL-1	1/Coal	800	800	11.03.2025
	4	Dikchu, Sikkim	M/s Sneha Kinetic Power Projects Pvt. Ltd/ DIKCHU HEP-2	2/Hydro	48	96	05.03.2025
NR	5	Bhadla_2(PG)	Adani Green Energy Twenty Five Limited	Solar	72	500	04.03.2025
	6	Fatehgarh_2	Adani Green Energy Twenty Four Limited	Solar	71	500	05.03.2025
	7	Fatehgarh_2	Adani Green Energy Twenty Four Limited	Solar	24	500	05.03.2025
	8	Bhadla_2(PG)	Nokh Solar Power Plant NTPC Limited(NSPPNL)	Solar	245	735	11.03.2025
	9	Bhadla_2(PG)	Adani Green Energy Twenty Five Limited	Solar	71	500	12.03.2025
	10	Bhadla_2(PG)	GORBEA SOLAR PRIVATE LIMITED(GSPL)	Solar	100	300	22.03.2025
	11	Bikaner_2(PBTSL)	SJVN Green Energy Ltd	Solar	163.55	320	25.03.2025
	12	Bikaner_2(PBTSL)	SJVN Green Energy Ltd	Solar	92.44	320	27.03.2025
	13	Bikaner_2(PBTSL)	Karinsar Solar Plant NHPC Ltd(KSP_NHPC)	Solar	53.57	300	30.03.2025
	14	Bikaner_2(PBTSL)	Karinsar Solar Plant NHPC Ltd(KSP_NHPC)	Solar	43.21	300	31.03.2025
	15	Obra C S/S	UPRVUNL	Thermal	660	660	06.03.2025
	16	Jawaharpur TPS S/S	UPRVUNL	Thermal	660	660	13.03.2025
	17	Rawatbhata/ RAPP-D	NPCIL/ RAPP-7	Nuclear	700	2 X 700	17.03.2025
SR	18	230kV/33kV Dharapuram PSS	JSW NEO Energy Ltd. (JSW_270MW)	Wind/Lot-2	27	86.4	12.03.2025
	19	220/33KV RSPPL PSS GADAG	Renew Surya Power Private Limited (RSRPL)	Wind/Lot-4	33	178.2	11.03.2025
	20	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Wind/Lot-16	24.3	532	05.03.2025
	21	230kV/33kV VILATHIKULAM S/S	JSW Renew Energy Ltd (JSW_540MW)	Wind/Lot-15	5.4	537.4	07.03.2025
	22	400KV AMGEPL Solar Pooling Station	AMGEPL	Solar	12	352	11.03.2025
	23	400/220KV HIRIYUR PSS	Zentaris Renewable Energy Pvt. Ltd.	Wind/Lot-1	66	66	30.03.2025
	24	230kV/33kV Savalaperi S/S	JSW Renew Energy Ltd (JSW_540MW)	Wind/Lot-17	10.8	540	18.03.2025
	25	Nellore, Andhra Pradesh	Meenakshi Energy Limited (MEPL) - UNIT-3	UNIT-3	350	650	05.03.2025
	26	230kV/33kV Dharapuram PSS	JSW NEO Energy Ltd. (JSW_270MW)	Wind/Lot-3	43.2	129.6	19.03.2025
	27	220KV IRCON Solar PSS / PAVAGADA	IRCON Renewable Power Limited	Solar	25	225	11.03.2025
	28	400/33KV KURNOOL	AMGEPL	Wind/Lot-8	6.93	301.125	21.03.2025
	29	400/33KV KURNOOL	AMGEPL	Wind/Lot-9	6.765	307.89	28.03.2025
WR	30	400/33 kV Khavda PSS-4	Adani Green Energy Twenty Four Limited (AGE24L)	Wind	104	104/104	28.03.2025
	31	400/33 kV Khavda PSS-4	Adani Ports & Special Economic Zone (APSEZ)	Wind	52	52/52	06.03.2025
	32	400/33 kV Khavda PSS-13	Adani Renewable Energy Forty One Limited (ARE41L)	Wind	10.4	124.8/124.8	06.03.2025
	33	400/33 kV Khavda PSS-4	Ambuja Cements Limited (ACL)	Wind	98.8	98.8/156	11.03.2025
	34	220/33 kV Dayapar Inox	NTPC Renewable Energy Limited (NTPC REL)	Wind	90	140/150	28.03.2025
	35	400/33 kV Khavda PSS-4	Adani Renewable Energy Forty One Limited (ARE41L)	Wind	52	52/52	21.03.2025
	36	400/33 kV Khavda PSS-3	Adani Green Energy Twenty Four A Limited (AGE24AL)	Solar	200	400/400	13.03.2025
	37	400/33 kV Khavda PSS-4	Adani Renewable Energy Fifty Six Limited (ARE56L)	Solar	175	175/225	13.03.2025
	38	400/33 kV Khavda PSS-5	Adani Hybrid Energy Jaisalmer Five Limited (AHEJ5L)	Solar	145	145/570	24.03.2025
	39	400/33 kV Khavda PSS-13	Adani Renewable Energy Fifty Seven Limited (ARE57L)	Solar	300	300/1100	21.03.2025
	40	400/33 kV Khavda PSS-9	Adani Renewable Energy Fifty Six Limited (ARE56L)	Solar	100	150/400	19.03.2025
	41	400/33 kV Khavda PSS-5	Adani Renewable Energy Forty Five Limited (ARE45L)	Solar	50	50/250	19.03.2025
	42	400/33 kV Khavda PSS-10	Adani Renewable Energy Fifty Six Limited (ARE56L)	Solar	100	100/500	26.03.2025
				Toal Nuclear Generation addition	700		
				Total Coal/Thermal Generation addition	3790		
				Total Solar Generation addition	2043		
				Total Wind Generation addition	631		
				Total Hydro Generation addition	48		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
ER	1	SJVN Thermal Pvt Limited	400KV/220KV 500 MVA ICT 1 AT BUXAR TPP	ICT-1	400/220	500	15.03.2025
	2	SJVN Thermal Pvt Limited	400KV/220KV 500 MVA ICT 2 AT BUXAR TPP	ICT-2	400/220	500	21.03.2025
	3	BSPTCL	400KV/220KV 500 MVA ICT 1 AT BAKHTIYARPUR(BH)	ICT-1	400/220	500	06.03.2025
	4	BSPTCL	400KV/220KV 500 MVA ICT 2 AT BAKHTIYARPUR(BH)	ICT-2	400/220	500	06.03.2025
	5	PVUNL	400KV/11KV, 3X265 MVA GT 1 AT PVUNL	GT-1	400/11	795	11.03.2025
	6	Sneha Kinetic Power Projects Pvt. Ltd	132KV/11KV 75 MVA GT 2 AT DIKCHU HEP	GT-2	132/11	75	05.03.2025
NR	7	UPRVUNL	Obra_C_TPS(UP)	GT-2	765/22	825	06.03.2025
	8	NHPC	Parbati_2(NH)	GT-2	400/13.8	246	18.03.2025
	9	Gorbea_SPL	GSPL_SL_BHD2_PG	PT-1	220/33	160	20.03.2025
	10	Gorbea_SPL	GSPL_SL_BHD2_PG	PT-2	220/33	160	20.03.2025
	11	NHPC	Parbati_2(NH)	GT-3	400/13.8	246	21.03.2025
	12	SJVNGEL_BKN2	SJVN_GEL_SL_BKN2	PT-1	400/33/33	250	22.03.2025
	13	SJVNGEL_BKN2	SJVN_GEL_SL_BKN2	PT-3	400/33/33	250	22.03.2025
	14	SJVNGEL_BKN2	SJVN_GEL_SL_BKN2	PT-2	400/33/33	250	22.03.2025
	15	SJVNGEL_BKN2	SJVN_GEL_SL_BKN2	PT-4	400/33/33	250	22.03.2025
	16	RRVPNL	Jaisalmer(RS)	ICT-4	400/220/33	500	25.03.2025
	17	NHPC	Parbati_2(NH)	GT-1	400/13.8	246	28.03.2025
	18	NHPC	KSP_NHPC_LTD_SL_BKN2	PT-1	220/33	125	28.03.2025
	19	NHPC	KSP_NHPC_LTD_SL_BKN2	PT-2	220/33	125	28.03.2025
	20	NHPC	KSP_NHPC_LTD_SL_BKN2	PT-3	220/33	125	28.03.2025
	21	PBTSL	Bikaner_2 (PBTSL)	ICT-8	400/220/33	500	29.03.2025
	22	Renew Surya Jyoti Private Limited	RSJPL_SL_Ftg3(PG)	PT-1	220/33	210	30.03.2025
SR	23	APTRANSCO	400KV/220KV MARADAM SS	ICT-4	400/220KV/33	500	07.03.2025
	24	APTRANSCO	400KV/220KV NARNOOR SS	ICT-3	400/220KV/33	500	07.03.2025
	25	Zentaris Renewable Energy Pvt. Ltd.	220KV/33KV ZENATARIS PSS	ICT-1	220KV/33	160	22.03.2025
	26	APTRANSCO	400/220KV THALLAYAPALEM GIS	ICT-1	400/220KV/33	500	01.03.2025
	27	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-1	400/220/33	500	31.03.2025
	28	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-2	400/220/33	500	31.03.2025
	29	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-3	400/220/33	500	31.03.2025
	30	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-4	400/220/33	500	31.03.2025
	31	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-6	400/220/33	500	31.03.2025
	32	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-7	400/220/33	500	31.03.2025
	33	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-1	765/220/33	1500	30.03.2025
	34	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-2	765/220/33	1500	30.03.2025
	35	POWERGRID-SR1	765/400/220KV KURNOOL-III Pooling Station	ICT-3	765/220/33	1500	31.03.2025
WR	36	Rewa Ultra Mega Solar Limited	220/33 kV Surajpur	ICT-2	220/33	50	04.03.2025
	37	Rewa Ultra Mega Solar Limited	220/33 kV Surajpur	ICT-2	220/33	100	04.03.2025
	38	Adani Green Energy Limited	400/33 kV Khavda PSS5	ICT-5	400/33	330	04.03.2025
	39	Adani Green Energy Limited	400/33 kV Khavda PSS5	ICT-2	400/33	330	04.03.2025
	40	WRTS-2, POWERGRID	400/220 kV New Navsari	ICT-1	400/220	500	10.03.2025
	41	WRTS-2, POWERGRID	400/220 kV New Navsari	ICT-2	400/220	500	18.03.2025
	42	Adani Green Energy Limited	400/33 kV Khavda PSS4	ICT-2	400/33	330	30.03.2025
	43	POWERGRID Dharamjaigarh Transmission Limited	765/400/220 kV Durg	ICT-1	400/220	500	29.03.2025
	44	POWERGRID Dharamjaigarh Transmission Limited	765/400/220 kV Durg	ICT-2	400/220	500	30.03.2025
	45	Chhattisgarh State Power Transmission Corporation Limited	400/220 kV Kurud	ICT-3	400/220	315	28.03.2025
	46	POWERGRID Dharamjaigarh Transmission Limited	765/400/220 kV Durg	ICT-3	400/220	500	28.03.2025
	47	Reliance Industries Limited	400/220 kV RIL Jamnagar	ICT-7	400/220	500	26.03.2025

	48	Reliance Industries Limited	400/220 kV RIL Jamnagar	ICT-2	400/220	500	26.03.2025
	49	Adani Green Energy Limited	400/33 kV Khavda PS$10	ICT-4	400/33	330	25.03.2025
NER	50	AEGCL	BOKO (50 MVA ICT replaced with 160 MVA)	ICT-1	220/132/11	160	13.03.2025
	51	AEGCL	Rangia SS (100 MVA ICT replaced with 200 MVA)	ICT-1	220/132/33	200	27.03.2025
					Total (MVA)	**22143**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NR	1	Gorbea_SPL	220kV Bhadla_2 (PG)-GSPL_SL_BHD2_PG-1	6	AL59 Moose	19.03.2025
	2	SJVNGEL_BKN2	400kV SJVN_GEL_SL_BKN2-Bikaner_2 (PBTSL)-1	18	Quad Moose	21.03.2025
	3	NHPC	220kV KSP_NHPC_LTD_SL_BKN2-Bikaner_2 (PBTSL)-1	23	AL59 Moose	28.03.2025
	4	ReNew_SJPL	220kV RSJPL_SL_Ftg3(PG)-Fatehgarh_III(PG)-1	11	MOOSE	30.03.2025
	5	Neemba_SPRVPL	220kV Neemba_SPRVPL_SL-RSJPL_SL_Ftg3(PG)-1	2	MOOSE	31.03.2025
	6	PTCUL	220kV Jauljivi (PG)-Baram_Jauljibi GIS(UK)-2	13	ZEBRA	31.03.2025
SR	7	APTRANSCO	400 KV Vemagiri - Kamavarapu Kota (KV KOTA) feeder - I	100	ACSR Twin Moose	05.03.2025
	8	APTRANSCO	400 KV Vemagiri - Kamavarapu Kota (KV KOTA) feeder - II	100	ACSR Twin Moose	05.03.2025
	9	Zentaris Renewable Energy Pvt. Ltd.	220 KV Hiriyur-Zenataris_PSS-1	93	AL 59	22.03.2025
	10	POWERGRID SR-1	765kV Kurnool New SS-Kurnool-III Pooling Station Line-1	112	ACSR Hexa Zebra	30.03.2025
	11	POWERGRID SR-1	765kV Kurnool New SS-Kurnool-III Pooling Station Line-2	112	ACSR Hexa Zebra	30.03.2025
WR	12	Adani Green Energy Limited	765 kV KPS1 - Lakadiya line-1 (bypassing KPS2 as temporary arrangement)	198	AL 59 Zebra	01.03.2025
	13	Adani Green Energy Limited	765 kV KPS1 - Lakadiya line-2 (bypassing KPS2 as temporary arrangement)	198	AL 59 Zebra	04.03.2025
	14	Rewa Ultra Mega Solar Limited	220 kV Pachora SEZ - Surajpur RUMSL	67	ACSR Zebra	03.03.2025
	15	WRTS-2, POWERGRID	400 kV New Navsari - Magarwada - 1	96	HTLS Moose	04.03.2025
	16	WRTS-2, POWERGRID	400 kV New Navsari - Magarwada - 2	96	HTLS Moose	05.03.2025
			Total length (km)	**1244.2**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
NR	1	POWERGRID	400kV Kishenpur(PG)-Kishtwar(Sterlite) CKT-1 from Kishenpur(PG)	98	Quad Moose	28.03.2025
WR	2	POWERGRID ER-WR Transmission Ltd	400 kV Jagdalpur-Jeypore-2 (idle charging upto 32.24 km) through main bay 411 at Jagdalpur	68.8	Twin Moose	31.03.2025
	3	POWERGRID	400 kV Banaskantha-Sankhari-3 (idle charging upto 21.978 km from Banaskantha)	22.8	Twin Moose	29.03.2025
	4	POWERGRID	400 kV Banaskantha-Sankhari-4 (idle charging upto 21.978 km from Banaskantha)	22.8	Twin Moose	29.03.2025
	5	POWERGRID	400 kV Kala-New Navsari-1 (idle charging upto loc 67/3 from New Navsari)	87.2	Twin Moose	29.03.2025

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
ER	1	PGCIL	220 KV Dalkhola(PG)-Purnea(PG) D/C (Restored to its original state - earlier on ERS, bypassing Dalkhola (PG))	41	Single Zebra	28.03.2025
	2	WBSETCL	220 KV Dalkhola (PG)-Dalkhola(WB) D/C (Restored to its original state - earlier on ERS, bypassing Dalkhola (PG))	1	Single Zebra	27.03.2025
	3	PGCIL ODISHA PROJECT	400KV-ROURKELA-JHARSUGUD-1 {Reconductoring of Jharsuguda/Sundargarh (PG) – Rourkela (PG) with Twin HTLS conductor (with ampacity equivalent to single HTLS 1228 A at nominal voltage) with bay upgradation at Rourkela S/S.}	126	HTLS	29.03.2025
	4	PGCIL ODISHA PROJECT	400KV-JHARSUGUDA-ROURKEL-3 {Reconductoring of Jharsuguda/Sundargarh (PG) – Rourkela (PG) with Twin HTLS conductor (with ampacity equivalent to single HTLS 1228 A at nominal voltage) with bay upgradation at Rourkela S/S.}	126	HTLS	05.03.2025
	5	PGCIL	132KV-RANGPO-GANGTOK-2 (Reconductoring of 132 KV Rangpo-Gangtok-II (Conductor Type-Gapped Type HTLS, 26 KM) along with upgraded line Bay (Bay No-104))	26	HTLS	05.03.2025
NR	6	HVPNL	220kV Palwal(HV)-Harfali-1 (After LILO of 220kV Samaypur (BBMB) - Palwal (HVPNL) Ckt-2 at 220kV Harfali (HVPNL))	10.86	ZEBRA	07.03.2025
	7	HVPNL	220kV Samaypur(BB)-Harfali-1 (After LILO of 220kV Samaypur (BBMB) - Palwal (HVPNL) Ckt-2 at 220kV Harfali (HVPNL))	8.6	ZEBRA	07.03.2025
	8	TTL,UPPTCL	400kV Khurja STPP (TH)-Shamli(UP)-1(After LILO of 400 KV ALIGARH - SHAMLI CKT-I at KHURJA(THDC))	193.399	Twin Moose	10.03.2025
	9	TTL,UPPTCL	400kV Aligarh(UP)-Khurja STPP (TH)-1(After LILO of 400 KV ALIGARH - SHAMLI CKT-I at KHURJA(THDC))	71.125	Twin Moose	11.03.2025
WR	10	MSETCL	220 kV Solapur (PG) - Bale (MH)-1 (Termination removed from Osmanabad (MH) to Bale (MH) as per originally approved scheme)	13.37	0.4 ACSR Zebra	02.03.2025
	11	MSETCL	220 kV Solapur (PG) - Bale (MH)-2 (Termination removed from Osmanabad (MH) to Bale (MH) as per originally approved scheme)	13.37	0.4 ACSR Zebra	02.03.2025
	12	MSETCL	220 kV Tarapur-Kudus (LILO of 220 kV Tarapur-Borivali at Kudus)	91.69	AAAC 525 sq mm	29.03.2025
	13	MSETCL	220 kV Borivali-Kudus (LILO of 220 kV Tarapur-Borivali at Kudus)	66.29	AAAC 525 sq mm	29.03.2025
	14	CSPTCL	220 kV Borjhara-Raipur-2 (LILO of 220 kV Raipur-Urla)	13.00	ACSR	29.03.2025
NER	15	NERTS, POWERGRID	132 kV Khliehriat (MePTCL)- Khliehriat (POWERGRID)-1 (After upgradation of CTs at both ends)	7.80	HTLS ACCC	08.03.2025
	16	NERTS, POWERGRID	132 kV Imphal (POWERGRID)- Loktak (NHPC) line (After HTLS reconductoring and upgradation of CTs at NHPC end)	36.60	HTLS ACCC	29.03.2025

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
ER	1	BGCL	125MVAR 400KV B/R-1 AT JAKKANPUR(BH)	400	125	20.03.2025
	2	BGCL	125MVAR 400KV B/R-2 AT JAKKANPUR(BH)	400	125	20.03.2025
NR	3	RRVPNL	125 MVAR Bus Reactor 1 at GSS Pachpadra(RS)	400	125	12.03.2025
	4	POWERGRID	25 MVAR Bus Reactor 1 at Alusteng(PG)	220	25	16.03.2025
SR	5	POWERGRID SR-1	125 MVAR Bus Reactor 1 at 400KV KURNOOL_PG_III	400	125	31.03.2025
	6	POWERGRID SR-1	330 MVAR Bus Reactor 1 at 765KV KURNOOL_PG_III	765	110	30.03.2025
WR	7	WRTS-2, POWERGRID	125 MVAR, 400 kV Bus reactor at New Navsari	400	125	04.03.2025
	8	KPS1 Transmission Limited	125 MVAR, 400 kV Bus reactor-2 at KPS1	400	125	05.03.2025
	9	MSETCL	125 MVAR, 400 kV Bus reactor at Parli	400	125	29.03.2025
	10	MPPTCL	125 MVAR, 400 kV Bus reactor at Birsingpur	400	125	24.03.2025
				Total (MVAr)	**1135**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
NIL						

Voltage Profile

विद्युत विभव रूपरेखा माह - मार्च 2025 VOLTAGE PROFILE - March 2025

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	797	744	772
2		दारलिपली DARLIPALI	0%	100%	0%	0%	0	789	756	772
3		गया GAYA	0%	100%	0%	0%	0	779	746	765
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	787	739	764
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	1	801	763	782
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	796	746	769
7		राची RANCHI	0%	100%	0%	0%	0	795	765	780
8		सासाराम SASARAM	0%	100%	0%	0%	0	802	727	765
1		आगरा AGRA	0%	100%	0%	0%	0	800	756	783
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	797	747	778
3		अजमेर AJMER	0%	99%	1%	1%	8	806	749	785
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	797	752	780
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	784	758	770
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	780	754	765
7		अंता ANTA	0%	100%	0%	0%	0	804	760	782
8		बलिया BALLIA	0%	100%	0%	0%	0	785	747	769
9		बारा BARA	0%	100%	0%	0%	0	787	745	770
10		भाडला BHADLA	0%	100%	0%	0%	0	801	735	780
11		भाडला-2 BHADLA-2	0%	100%	0%	0%	0	802	742	780
12		भिवानी BHIWANI	0%	99%	1%	1%	8	804	727	786
13		बीकानेर BIKANER	0%	100%	0%	0%	0	797	695	781
14		बरेली BAREILLY	0%	100%	0%	0%	2	809	746	779
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	9	808	755	784
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	796	743	775
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	793	744	773
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	788	745	770
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	1	801	753	783
20		हापुड़ HAPUR	0%	100%	0%	0%	0	803	745	779
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	2	810	742	771
22		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	801	748	781
23		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	795	751	774
24		खेतरी KHETRI	0%	100%	0%	0%	0	803	746	781
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	799	750	777
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	773	743	760
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	796	747	771
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	792	736	768
29		मेरठ MEERUT	0%	98%	2%	2%	13	806	749	783
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	801	746	778
31		मोगा MOGA	0%	99%	1%	1%	5	803	743	780
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	778	750	763
33		उरई ORAI	0%	99%	1%	1%	8	804	769	789
34		फागी PHAGI	0%	100%	0%	0%	2	805	754	784
35		रामपुर RAMPUR	0%	96%	3%	3%	21	817	751	785
36		उन्नाव UNNAO	0%	100%	0%	0%	0	795	743	761
37		वाराणसी VARANASI	0%	100%	0%	0%	0	789	757	775
1		अकोला AKOLA	0%	100%	0%	0%	0	800	750	774
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	802	729	773
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	797	744	770
4		भुज BHUJ	0%	100%	0%	0%	1	802	755	782
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	796	750	779
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	782	749	764
7		बीना BINA	0%	100%	0%	0%	0	801	758	781
8		बनसकठा BANASKANTHA	0%	97%	3%	3%	24	806	751	787
9		चापा CHAMPA	0%	98%	2%	2%	15	807	763	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	795	746	770
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	785	754	768
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	795	759	777
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	795	742	769
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	800	757	780
15		ग्वालियर GWALIOR	0%	100%	0%	0%	3	804	765	785
16		इंदौर INDORE	0%	100%	0%	0%	0	794	747	769
17		जबलपुर JABALPUR	0%	100%	0%	0%	4	805	764	785
18	पश्चिमी क्षेत्र WR	खंडवा KHANDWA	0%	100%	0%	0%	0	795	747	770
19		कोरडी KORADI	0%	100%	0%	0%	0	789	754	769
20		लकाडिया LAKADIYA	0%	97%	3%	3%	20	808	710	789
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	793	765	779
22		पड़घे PADGHE	0%	100%	0%	0%	1	810	721	775
23		परली PARLI	0%	99%	1%	1%	4	808	756	779
24		पुणे PUNE	0%	100%	0%	0%	1	812	711	778
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	2	803	760	781
26		सासन SASAN	0%	100%	0%	0%	0	791	768	777
27		सतना SATNA	0%	100%	0%	0%	3	802	769	784
28		सिवनी SEONI	0%	100%	0%	0%	0	797	751	773
29		सीपत SIPAT	0%	100%	0%	0%	0	781	750	764
30		सोलापुर SOLAPUR	0%	99%	1%	1%	7	811	757	783
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	785	755	766
32		तामनार TAMNAR	0%	100%	0%	0%	0	791	764	778
33		वड़ोदरा VADODARA	0%	100%	0%	0%	2	805	751	776
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	794	770	780
35		वर्धा WARDHA	0%	100%	0%	0%	1	803	747	776
36		वरोरा WARORA	0%	100%	0%	0%	0	801	746	775
1		अरियलूर ARIYALUR	0%	100%	0%	0%	0	795	750	774
2		कड़पा CUDDAPAH	0%	100%	0%	0%	0	777	772	777
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	98%	2%	2%	12	808	751	778
4		कर्नूल KURNOOL	0%	100%	0%	0%	1	802	751	775
5		महेश्वरम MAHESWARAM	0%	96%	4%	4%	27	813	754	781
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	92%	8%	8%	58	813	743	781
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	796	754	772
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	2	807	753	778
9		रायचूर RAICHUR	0%	100%	0%	0%	1	802	755	777
10		श्रीकाकुलम SRIKAKULAM	0%	98%	2%	2%	13	813	738	776
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	1	803	749	773
12		वेमगिरी VEMAGIRI	0%	97%	3%	3%	24	811	753	781
13		वारंगल WARANGAL	0%	98%	2%	2%	14	811	748	778
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	416	376	401
2		बिस्वनाथ चरिआलि BISWANATH CHARIALI(400 kV)	0%	100%	0%	0%	0	416	376	401
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	415	397	407
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	416	399	408
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	416	390	403
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	416	393	406
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	418	392	403
8	पूर्वोत्तर क्षेत्र NER	अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	413	402	407
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	414	392	401
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	415	393	405
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	417	387	405
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	412	395	405
13		पबंकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	414	393	402
14		रंगानदी RANGANADI (400 kV)	0%	100%	0%	0%	0	420	393	404
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	396	406
16		सुर्ज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	412	394	400
17		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	411	386	398

All listed stations are 765 kV stations unless otherwise mentione
***Percentage is calculated w.r.t. Time of one month**

ALL TIME HIGHEST

31-03-2025

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	82312 23-07-2024	1990 18-06-2024	443 01-08-2023	86 07-08-2023	226 28-03-2025
WR	80000 08-02-2025	71512 11-03-2025	1690 11-03-2025	167 18-12-2014	310 28-05-2024	152.57 30-03-2025
SR	69942 21-03-2025	55925 28-03-2025	1460 19-03-2025	208 31-08-2018	323 26-07-2024	155.5 06-03-2025
ER	32531 10-06-2024	29695 29-05-2024	692 10-06-2024	157 14-09-2022	-	4 09-06-2024
NER	3905 19-09-2024	3787 19-09-2024	80 20-09-2024	43 27-06-2024	-	2 22-06-2022
All India	250070 30-05-2024	227354 29-05-2024	5466 30-05-2024	877 30-08-2022	619 28-05-2024	527 06-03-2025

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15980	29-06-2024	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	18985	12-02-2025	379.1	30-05-2024
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30032	13-06-2024	658.8	17-06-2024
	Uttarakhand	2863	14-06-2024	62.1	14-06-2024
	HP	2273	17-01-2025	41.3	20-12-2024
	J&K(UT) and Ladakh(UT)	3200	07-01-2025	70.3	04-02-2025
	Chandigarh	443	13-06-2024	9.1	18-06-2024
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6511	30-03-2025	151.2	28-03-2025
	Gujarat	25502	07-06-2024	514.2	07-06-2024
	MP	18888	20-12-2024	353.8	14-02-2025
	Maharashtra	30675	13-03-2025	685.0	13-03-2025
	Goa	810	13-03-2025	17.6	18-05-2024
	DD & DNH	1390	23-10-2024	32.6	16-10-2024
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	17162	20-03-2025	339.2	18-03-2025
	Karnataka	18395	07-03-2025	359.2	19-03-2025
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	530	31-05-2024	11.8	31-05-2024
ER	Bihar	8001	23-09-2024	172.8	30-07-2024
	DVC	3674	14-06-2024	81.2	22-04-2022
	Jharkhand	2351	09-07-2024	50.4	10-06-2024
	Odisha	7104	13-07-2023	148.5	19-04-2024
	West Bengal	12756	30-04-2024	264.0	30-04-2024
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	198	26-05-2024	3.9	18-06-2024
	Assam	2687	20-09-2024	55.8	20-09-2024
	Manipur	271	16-01-2025	4.2	10-01-2025
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	162	27-01-2024	2.6	02-03-2024
	Nagaland	188	22-07-2024	3.4	29-07-2024
	Tripura	386	04-05-2024	7.3	02-06-2024
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

Note: DVC has reported revised maximum demand met.

GRID CONTROLLER OF INDIA LIMITED

NATIONAL LOAD DESPATCH CENTRE

NEW DELHI

System Reliability Indices Report for the month of March 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
