ग्रिड-इंडिया
GRID-INDIA

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)
[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / National Load Despatch Centre

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 42785855

संदर्भ संख्या:- **GRID-INDIA/NLDC/MR/** दिनांक: **21.11.2025**

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – **अक्टूबर 2025**

महोदय,

आई०ई०जी०सी०-2023 की धारा-38 के अनुपालन में, **अक्टूबर 2025** माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

एस.सी. डंभारे
मुख्य महाप्रबन्धक
प्रणाली प्रचालन, रा.भा.प्रे.कें.

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची
Distribution List

1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली–110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building,36,Janpath,New Delhi-110001

2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली–110066
Chief Engineer (GM), CEA,Sewa Bhavan, R.K.Puram , New Delhi-110066

3 सदस्य सचिव, उ. क्षे. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Member Secretary, NRPC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

4 सदस्य सचिव, प. क्षे. वि. स., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Member Secretary, WRPC, F-3,MIDC Area, Andheri (East),Mumbai-400093

5 सदस्य सचिव, द. क्षे. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Member Secretary, SRPC, 29,Race Course Cross Road,Bangalore-560009

6 सदस्य सचिव, पू. क्षे. वि. स., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Member Secretary, ERPC, 14,Golf Club Road , Kolkata-700033

7 सदस्य सचिव,उ. पू. क्षे. वि. स.,मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नोंग्रिम हिल्स, शिलोंग – 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills , Shillong -793003

8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

9 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता – 700033
Executive Director, ERLDC,14, Golf Club Road , Kolkata-700033


10 कार्यपालक निदेशक, प. क्षे. भा. प्रे. के., एफ–3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई – 400093
Executive Director, WRLDC,F-3,MIDC Area, Andheri (East),Mumbai-400093

11 कार्यपालक निदेशक , उ.क्षे.भा.प्रे.के, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली – 110016
Executive Director, NRLDC,18/A,SJSS Marg, Katwaria Sarai, New Delhi-110016

12 कार्यपालक निदेशक, द. क्षे. भा. प्रे. के, 29, रेस कोर्स क्रॉस रोड, बंगलूरु – 560009
Executive Director, SRLDC, 29,Race Course Cross Road,Bangalore-560009

13 कार्यपालक निदेशक, पू. क्षे. भा. प्रे. के., डोंगतिएह, लोअर नोंग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006

ग्रिड-इंडिया
GRID-INDIA

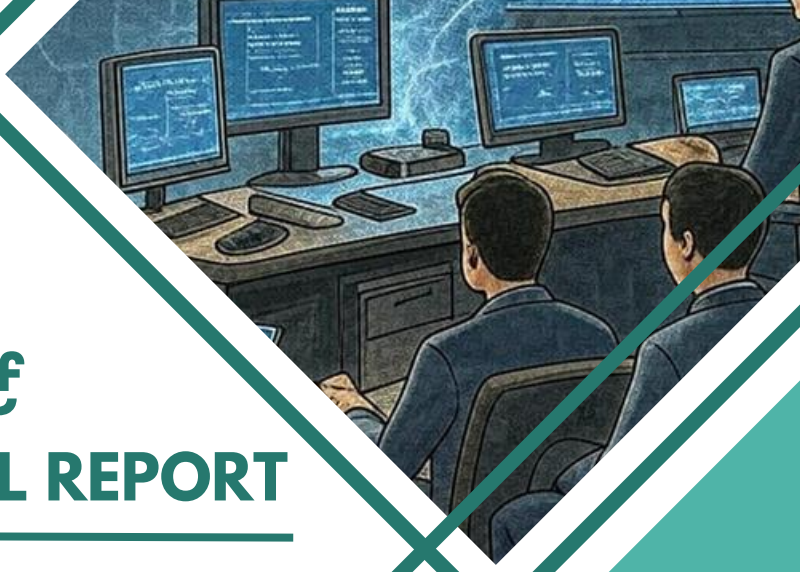

मासिक प्रचालन रिपोर्ट
MONTHLY OPERATIONAL REPORT

राष्ट्रीय भार प्रेषण केन्द्र
NATIONAL LOAD DESPATCH CENTRE

OCTOBER–2025

GRID CONTROLLER OF INDIA LIMITED
ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड





grid-india.in

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED
Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI

माह अक्टूबर 2025 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE MONTH OF OCTOBER-2025

पृष्ठसूची CONTENTS

1	माह अक्टूबर 2025 की सारांश रिपोर्ट Summary of report for the month of OCTOBER 2025	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति Evening Peak Hour Demand Met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	16 अक्टूबर के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 16-OCTOBER (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अक्टूबर 2024 से तुलना Energy requirement and met comparison with OCTOBER 2024	24


13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अक्टूबर 2024 से तुलना Peak demand requirement and met comparison with OCTOBER 2024	25
14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-38
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	39-41
17	एसटीओए (द्विपक्षीय एवं सामूहिक)एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	42
18	पावर मार्केट की सूचना Power market information	43-48
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	49-51
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	52-62
21	नए चार्ज किये गए तत्व New elements Charged	63
22	विभव रूपरेखा Voltage profile	64
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह अक्टूबर 2025 तक All Time Highest (Demand & Energy) figures: Till OCTOBER 2025	65
24	अक्टूबर 2025 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for OCTOBER 2025	66

1. SUMMARY OF REPORT FOR THE MONTH OF OCTOBER-2025

EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

Decreased by 7.90% as compared to Sep'25

Decreased by 5.48% as compared to 45596

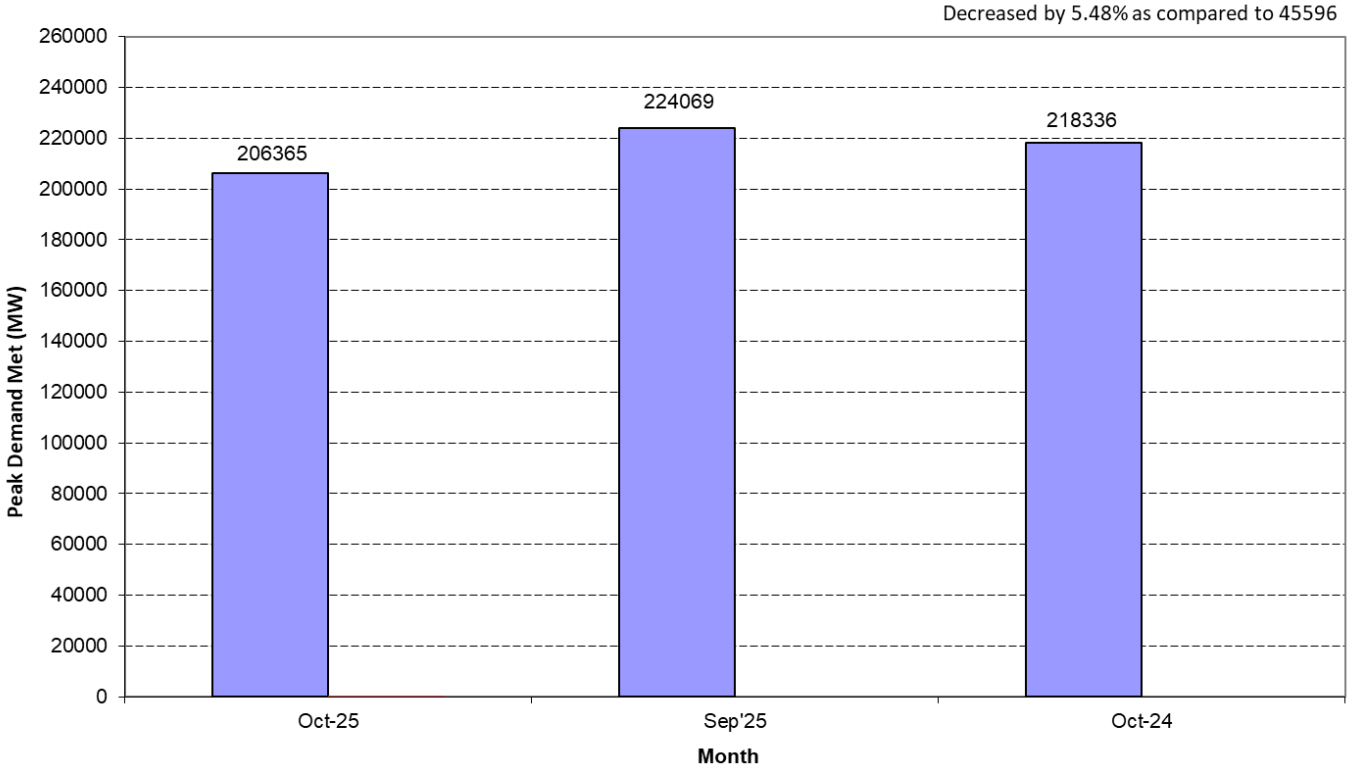


*Source: As per daily data furnished by states

Frequency within IEGC Band


Increased by 0.33% as compared to Sep'25

Decreased by 2.10% as compared to 45596

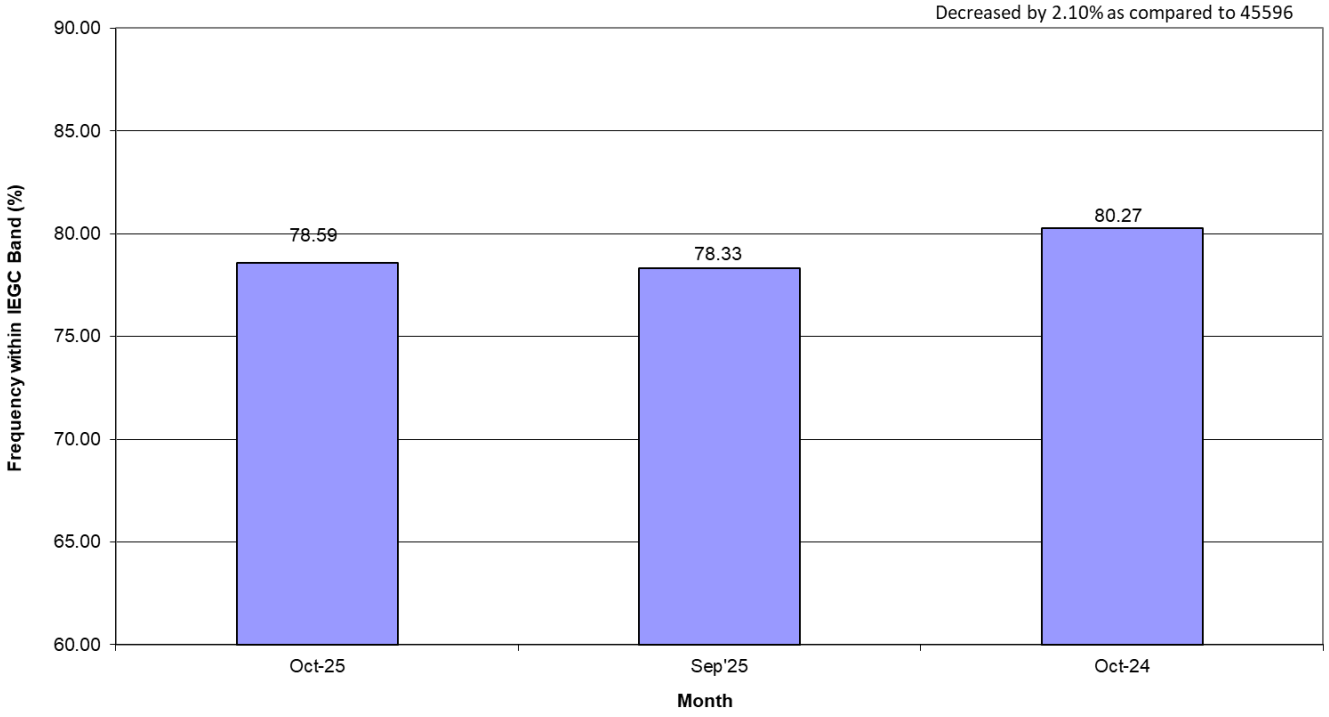


ENERGY MET AT NATIONAL LEVEL (MU)

Decreased by 9.54% as compared to Sep'25
Decreased by 6.03% as compared to 45596

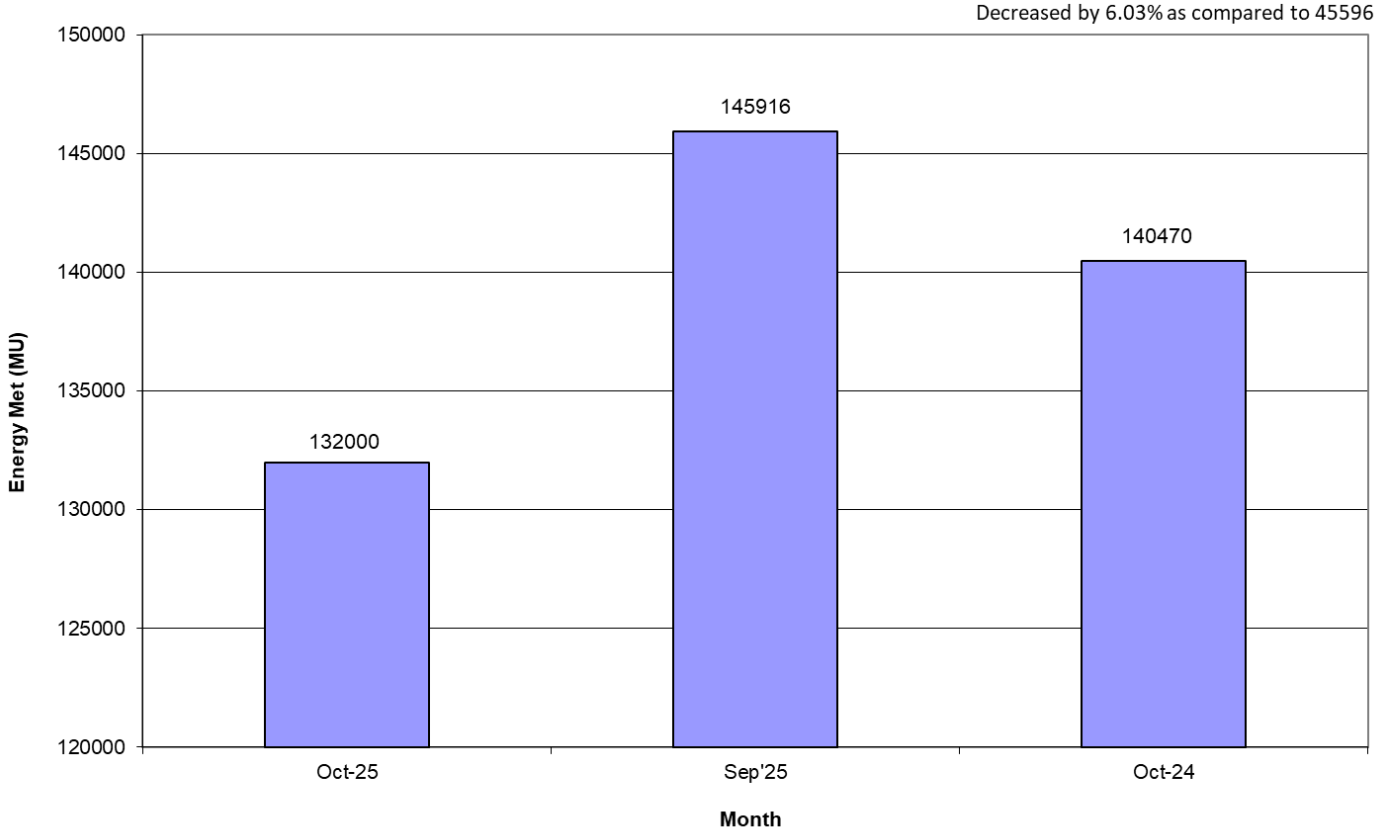


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

Decreased by 12.45% as compared to Sep'25
Decreased by 6.03% as compared to 45596

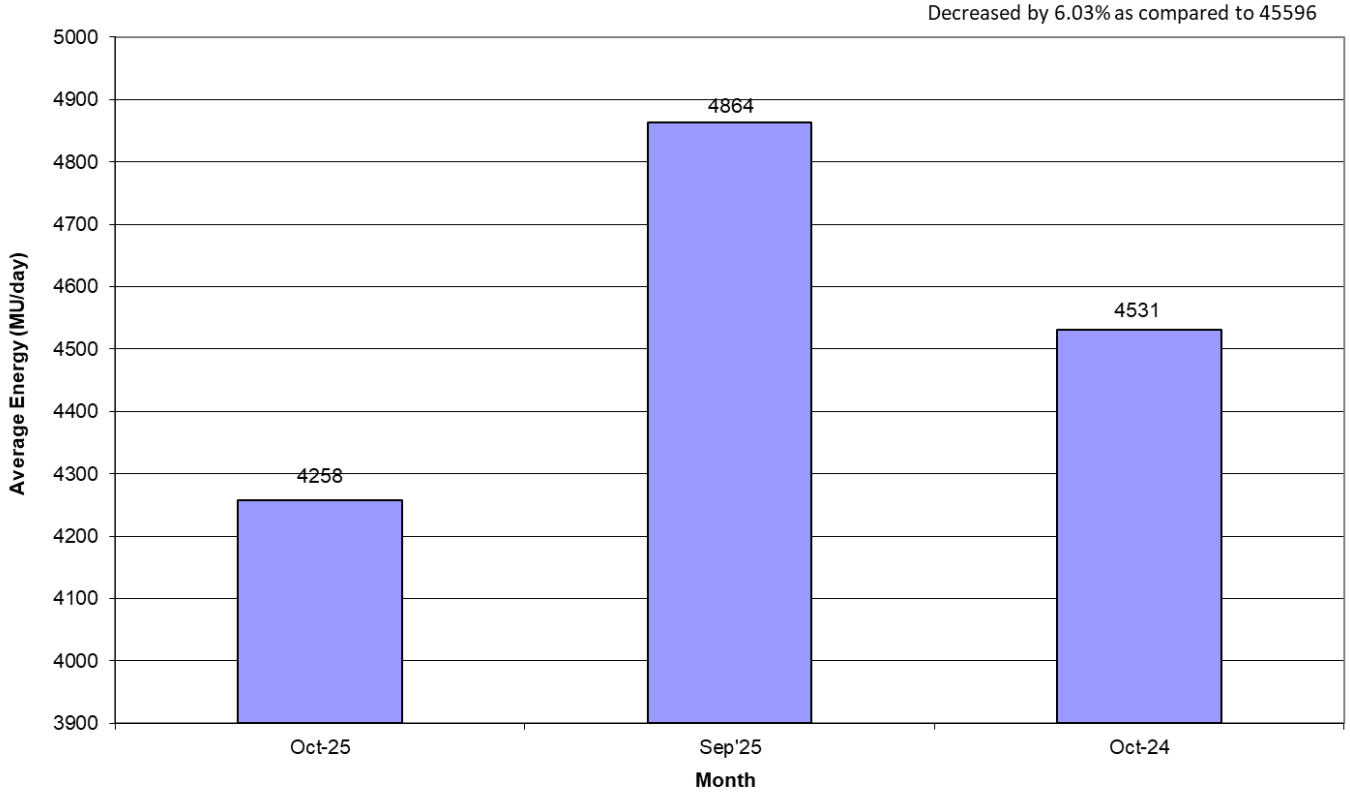


HYDRO GENERATION AT NATIONAL LEVEL (MU)

Decreased by 26.38% as compared to Sep'25
Increased by 11.80% as compared to 45596

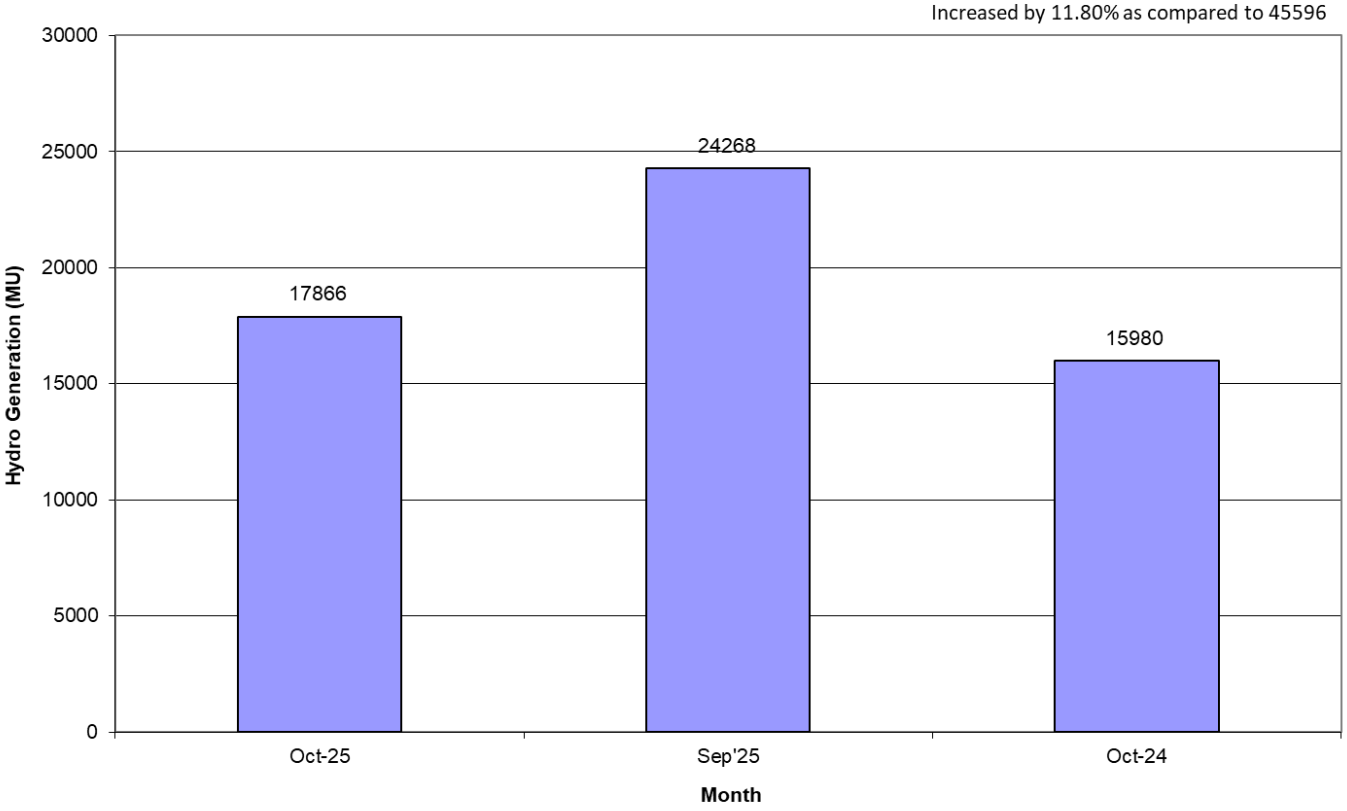

AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)


Decreased by 28.75% as compared to Sep'25
Increased by 11.80% as compared to 45596

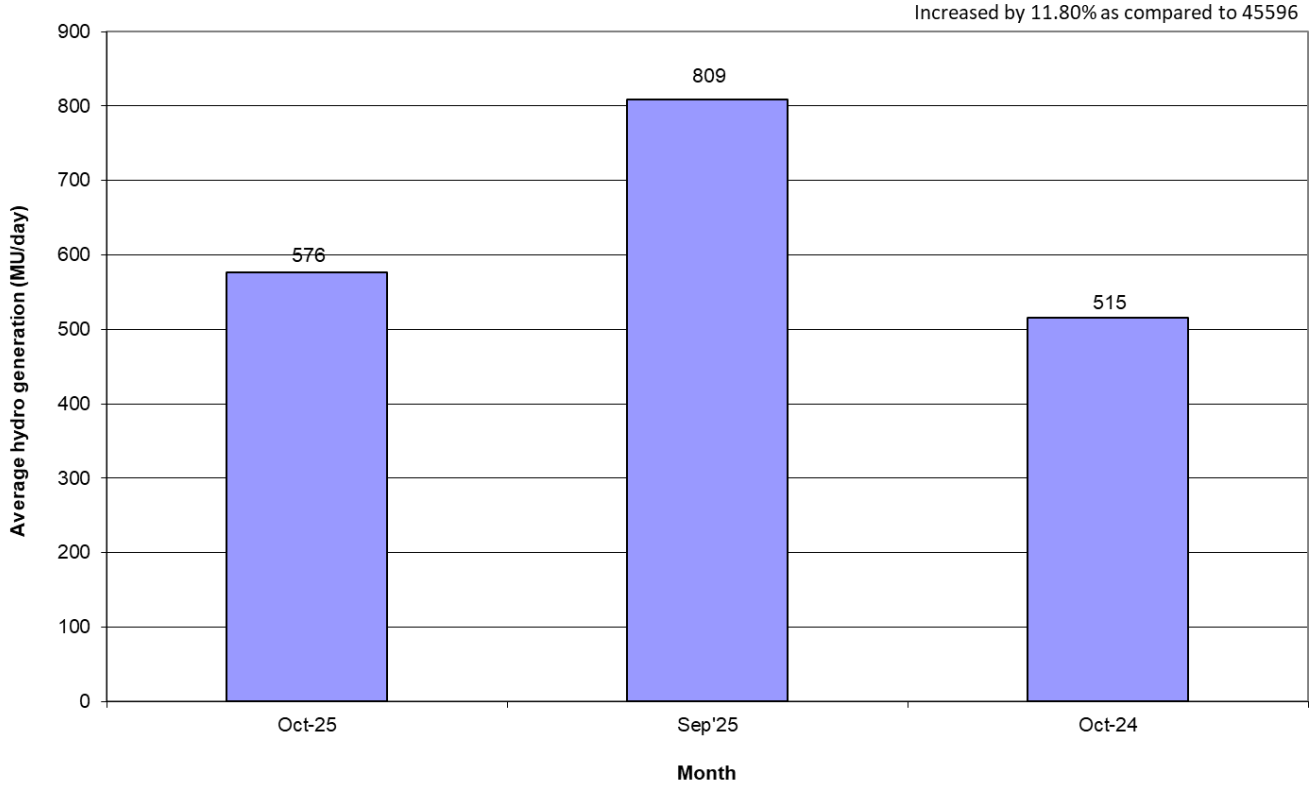

WIND GENERATION AT NATIONAL LEVEL (MU)

Decreased by 38.84% as compared to Sep'25


Increased by 112.07% as compared to 45596

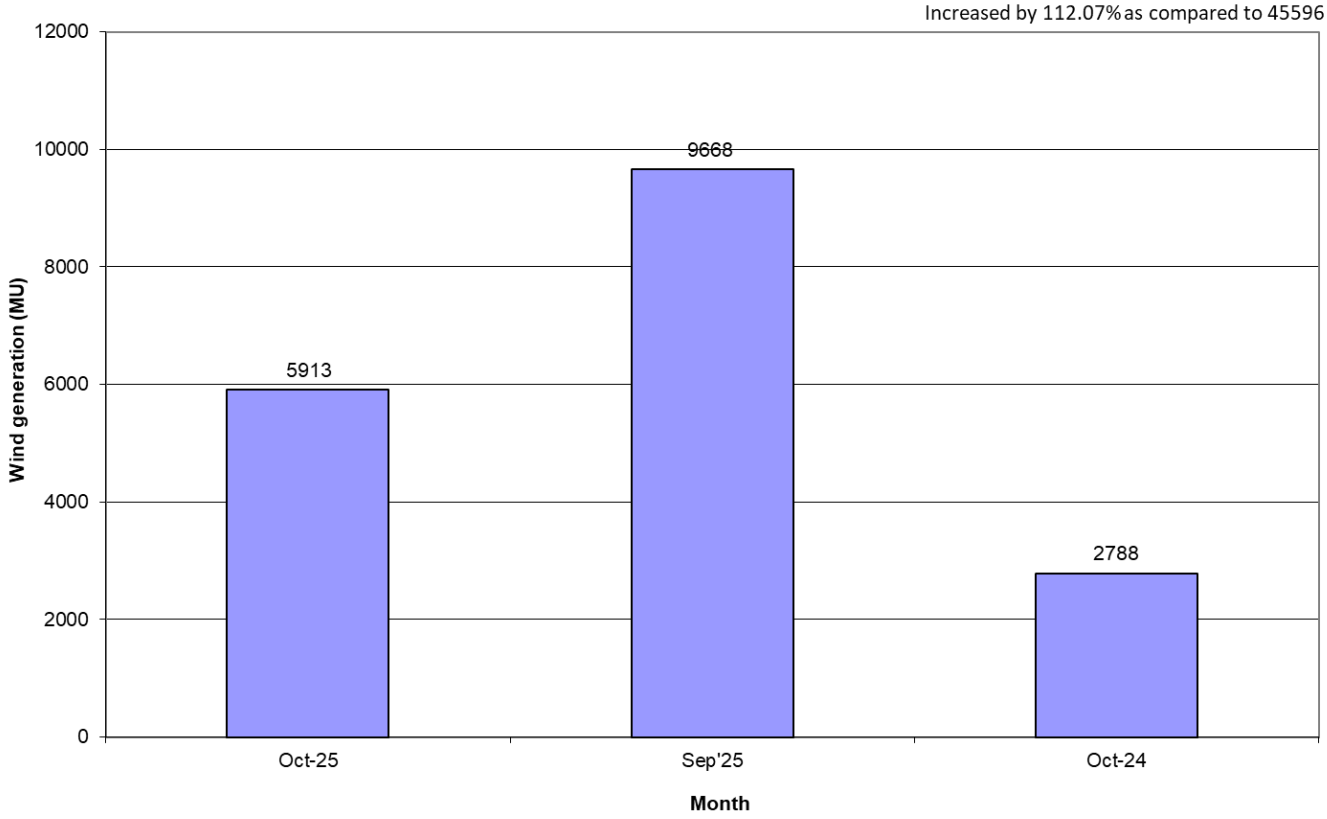

AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)


Decreased by 40.81% as compared to Sep'25

Increased by 112.07% as compared to 45596

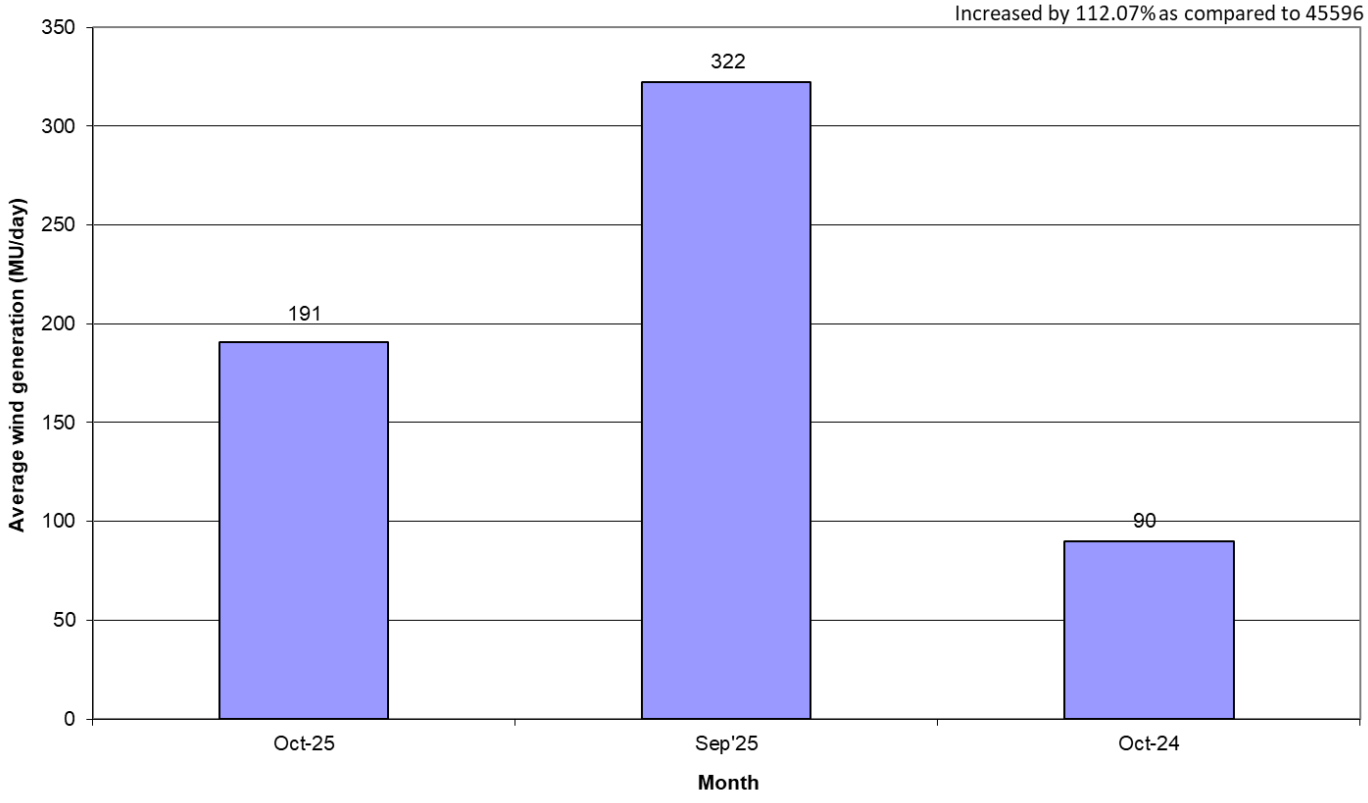


SOLAR GENERATION AT NATIONAL LEVEL (MU)

Decreased by 1.00% as compared to Sep'25
Increased by 13.56% as compared to 45596

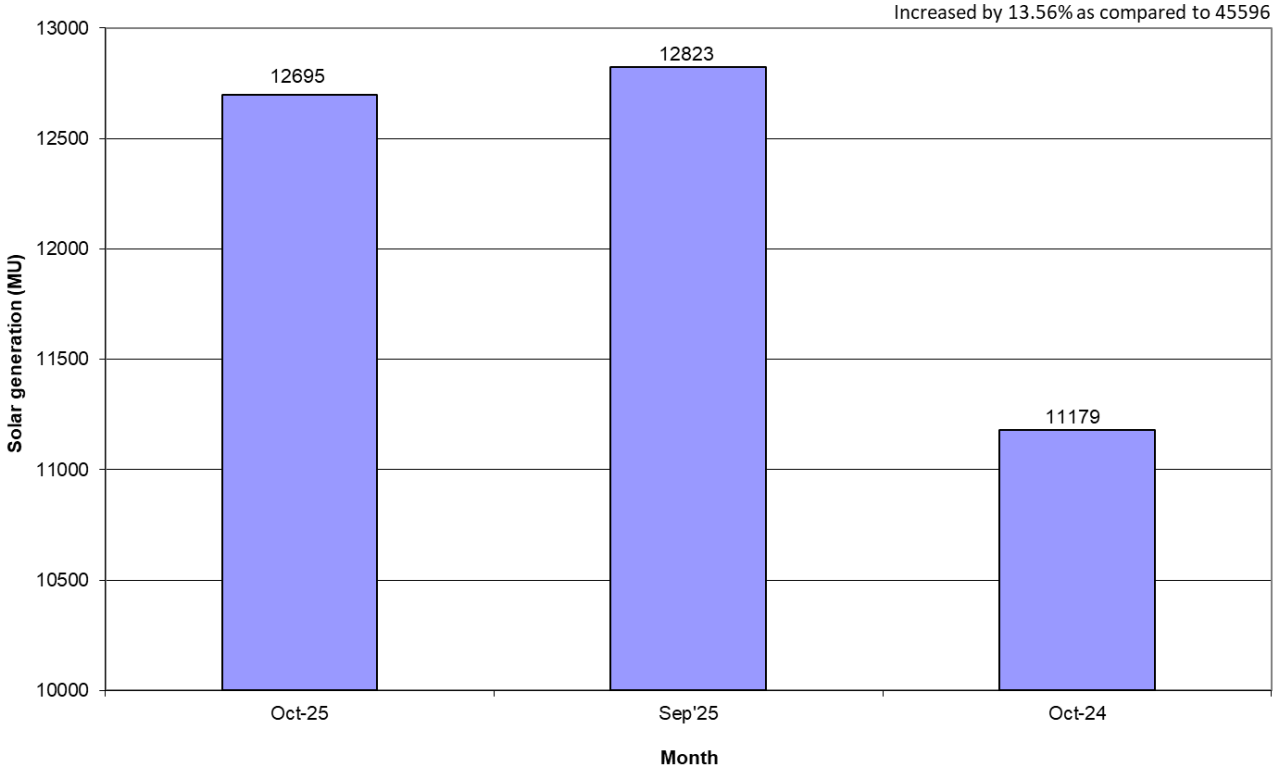

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

Decreased by 4.19% as compared to Sep'25
Increased by 13.56% as compared to 45596

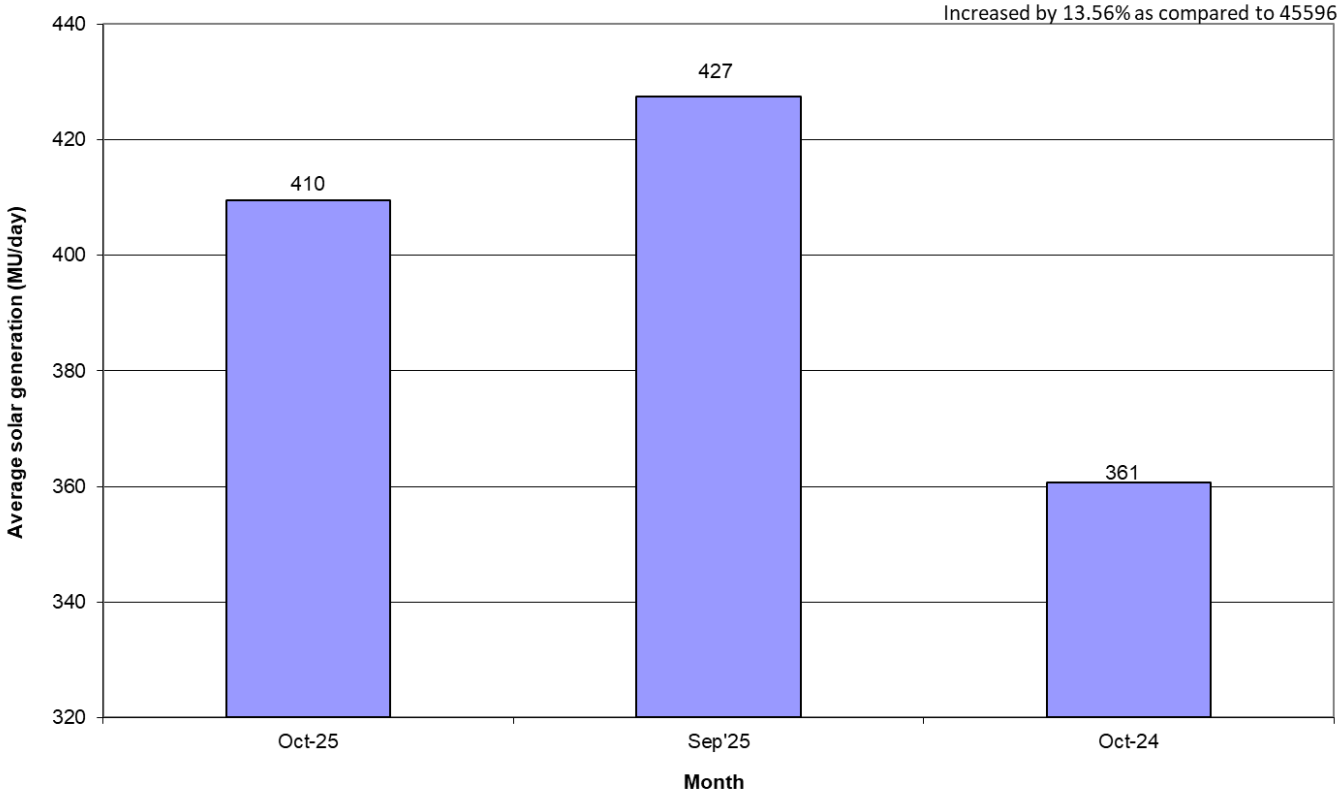

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.10.2025
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	61090	1580	5712	0	68382	2220	22239	55469	148310
2	WR	73548	1400	9399	0	84347	3240	7696	75780	171062
3	SR	51956	3640	3356	434	59385	3320	13607	65568	141881
4	ER	30895	0	0	0	30895	0	4862	2664	38421
5	NER	770	0	1665	36	2471	0	1944	771	5186
6	ISLANDS	0	0	0	120	120	0	0	43	163
	ALL INDIA	218258	6620	20132	589	245600	8780	50348	200295	505023

Source: Central Electricity Authority

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर अवधि की विद्युत मांग पूर्ति
EVENING PEAK HOUR (at 20:00hrs) DEMAND MET AT NATIONAL LEVEL


माह: अक्टूबर 2025 MONTH:- OCTOBER 2025

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	अखिल भारतीय All India
1-Oct-25	74215	59087	42776	23625	2892	202595
2-Oct-25	61780	53773	41818	21802	2674	181847
3-Oct-25	68754	62146	47889	23056	3309	205154
4-Oct-25	69705	63584	47069	22555	3452	206365
5-Oct-25	64258	59512	43232	23194	2807	193003
6-Oct-25	56905	62018	49064	25318	3220	196525
7-Oct-25	56078	63765	49961	26276	3486	199566
8-Oct-25	58261	63926	49565	26936	3451	202139
9-Oct-25	58028	64522	48945	27577	3524	202596
10-Oct-25	55813	63471	48103	26576	3458	197421
11-Oct-25	56837	63789	47731	26136	3357	197850
12-Oct-25	54082	61243	43875	25878	3266	188344
13-Oct-25	57539	65401	49006	26173	3471	201590
14-Oct-25	58559	66135	48047	26641	3635	203017
15-Oct-25	59155	65106	48176	26677	3583	202697
16-Oct-25	59841	66044	47788	27119	3618	204410
17-Oct-25	59410	66246	46722	27124	3567	203069
18-Oct-25	57685	63786	45852	27229	3474	198026
19-Oct-25	54031	59824	41074	26683	3257	184869
20-Oct-25	47860	52742	36368	25837	3166	165973
21-Oct-25	48698	49880	39161	27296	3283	168318
22-Oct-25	50785	52223	42221	27857	3449	176535
23-Oct-25	53652	55011	43800	27294	3400	183157
24-Oct-25	56107	58140	44466	27621	3326	189660
25-Oct-25	55686	58256	44743	27228	3325	189238
26-Oct-25	52004	55129	41423	26526	3110	178192
27-Oct-25	50318	55641	43570	26707	3296	179532
28-Oct-25	51128	57113	41314	24631	3310	177496
29-Oct-25	53157	57642	43497	24103	3249	181648
30-Oct-25	51610	56384	46602	23346	3072	181014
31-Oct-25	53304	57059	47962	23559	2985	184869
उच्चतम MAXIMUM	74215	66246	49961	27857	3635	206365
निम्नतम MINIMUM	47860	49880	36368	21802	2674	165973
औसत AVERAGE	56943	59955	45220	25761	3306	191184
अब तक का उच्चतम All Time Max.	84151	71713	55925	31898	4065	232191
दिनांक Date	14.06.25	24.04.25	28.03.25	14.05.25	23.07.25	09.06.25

Source: As per daily data furnished by states

EVENING PEAK HOUR DEMAND(at 2000hrs) MET DURING THE MONTH OF OCTOBER 2025

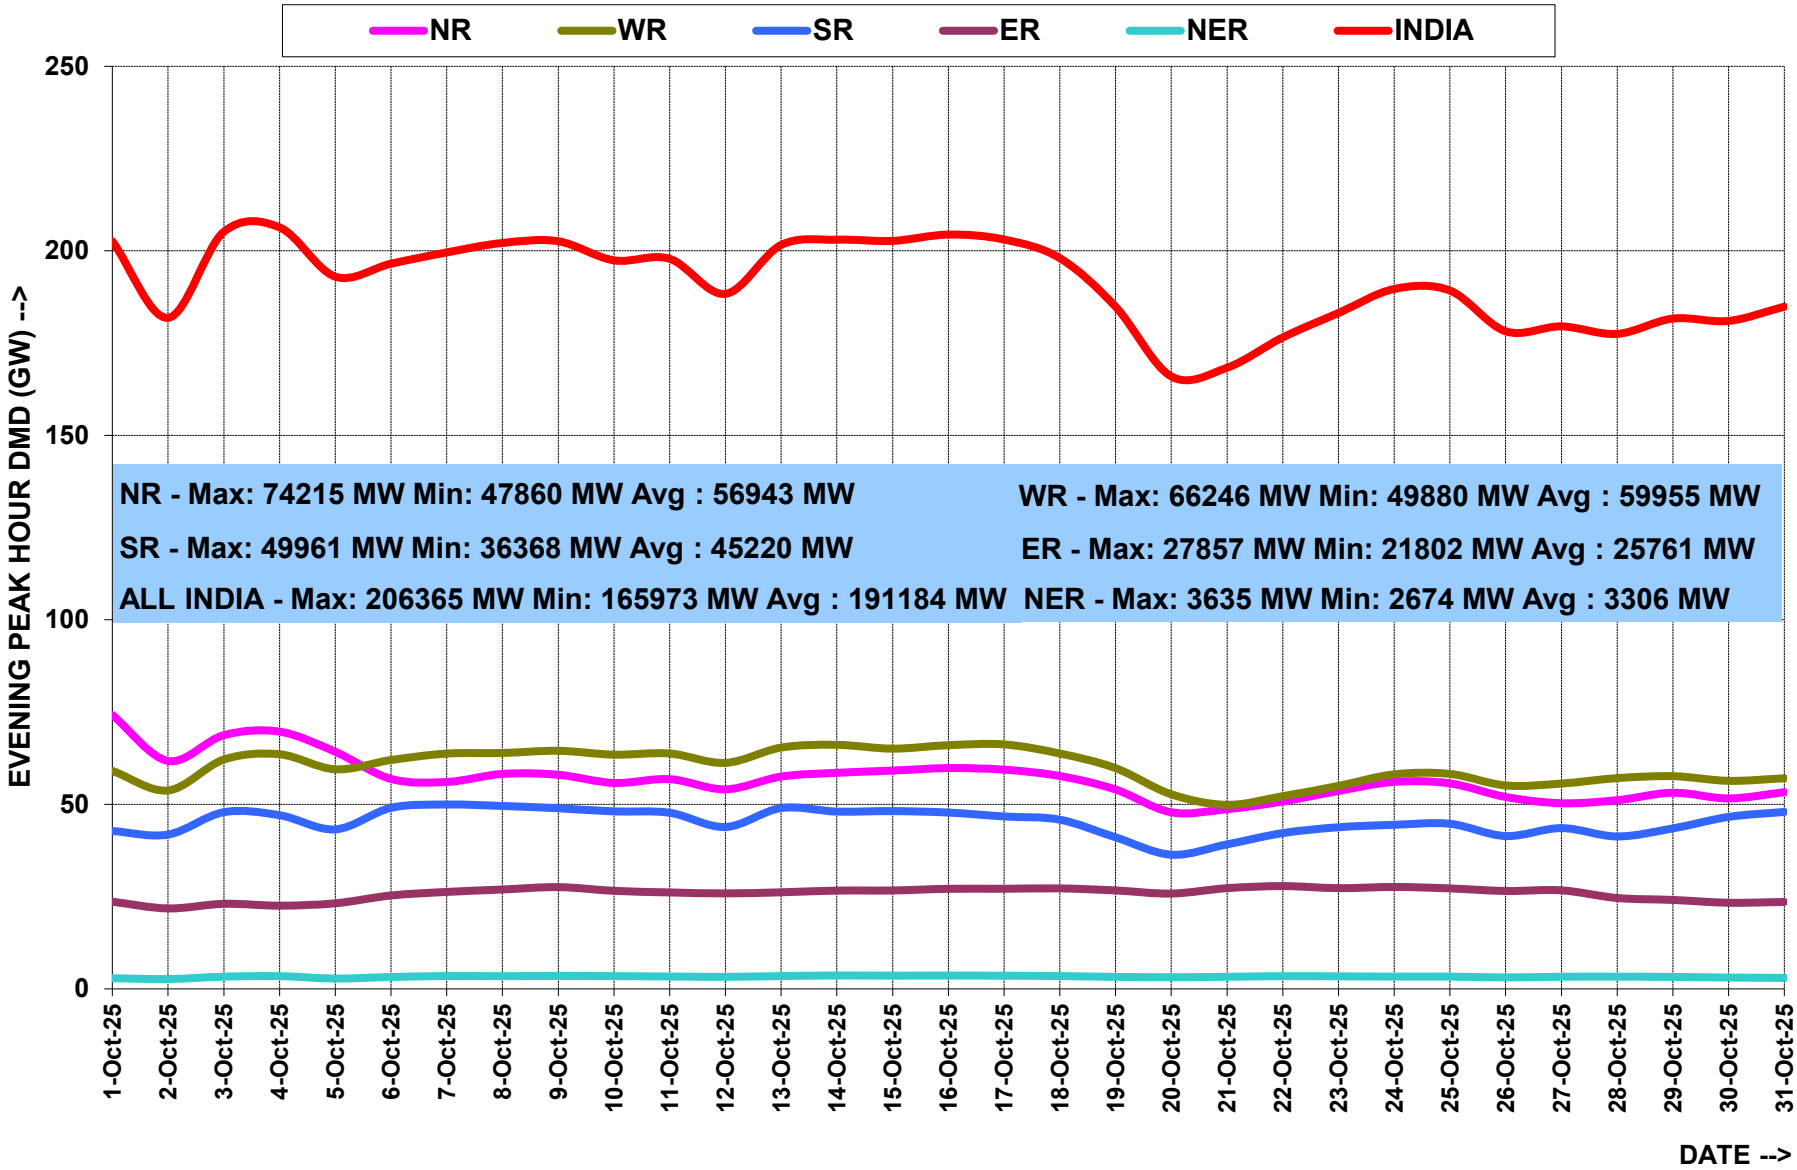


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: अक्टूबर 2025 MONTH:- OCTOBER 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	अखिल भारतीय All India
01-Oct-25	1595	1314	1057	571	55	4593
02-Oct-25	1460	1231	1026	499	54	4270
03-Oct-25	1483	1308	1134	505	61	4491
04-Oct-25	1480	1364	1144	499	66	4552
05-Oct-25	1362	1340	1072	496	59	4329
06-Oct-25	1255	1356	1121	526	60	4317
07-Oct-25	1157	1378	1158	558	66	4317
08-Oct-25	1177	1381	1188	572	66	4384
09-Oct-25	1177	1399	1155	586	67	4384
10-Oct-25	1193	1403	1135	582	68	4381
11-Oct-25	1193	1394	1121	568	64	4340
12-Oct-25	1167	1363	1058	554	62	4205
13-Oct-25	1226	1428	1115	569	65	4403
14-Oct-25	1250	1459	1131	567	68	4476
15-Oct-25	1267	1462	1119	564	71	4483
16-Oct-25	1271	1483	1119	562	69	4505
17-Oct-25	1287	1494	1115	576	68	4540
18-Oct-25	1280	1477	1098	581	68	4505
19-Oct-25	1225	1399	1002	573	64	4264
20-Oct-25	1120	1287	924	573	61	3965
21-Oct-25	1085	1208	927	582	61	3862
22-Oct-25	1128	1197	948	591	64	3928
23-Oct-25	1177	1265	980	581	66	4068
24-Oct-25	1226	1345	997	579	65	4211
25-Oct-25	1225	1361	985	587	64	4221
26-Oct-25	1182	1287	933	575	60	4037
27-Oct-25	1173	1277	999	571	61	4081
28-Oct-25	1139	1266	946	550	63	3963
29-Oct-25	1146	1271	933	524	62	3937
30-Oct-25	1144	1271	991	506	63	3974
31-Oct-25	1146	1257	1053	502	56	4014
कुल TOTAL	38394	41722	32687	17231	1967	132000
उच्चतम MAXIMUM	1595	1494	1188	591	71	4593
निम्नतम MINIMUM	1085	1197	924	496	54	3862
औसत AVERAGE	1239	1346	1054	556	63	4258
संचयी 2025-26 Cumulative 2025-26	326600	311226	246689	129703	13995	1028212
अब तक का उच्चतम All Time Max.	2023	1742	1458	704	82	5466
दिनांक Date	12.06.25	25.04.25	28.03.25	23.07.25	24.07.25	30.05.24

ENERGY MET DURING THE MONTH OF OCTOBER' 2025

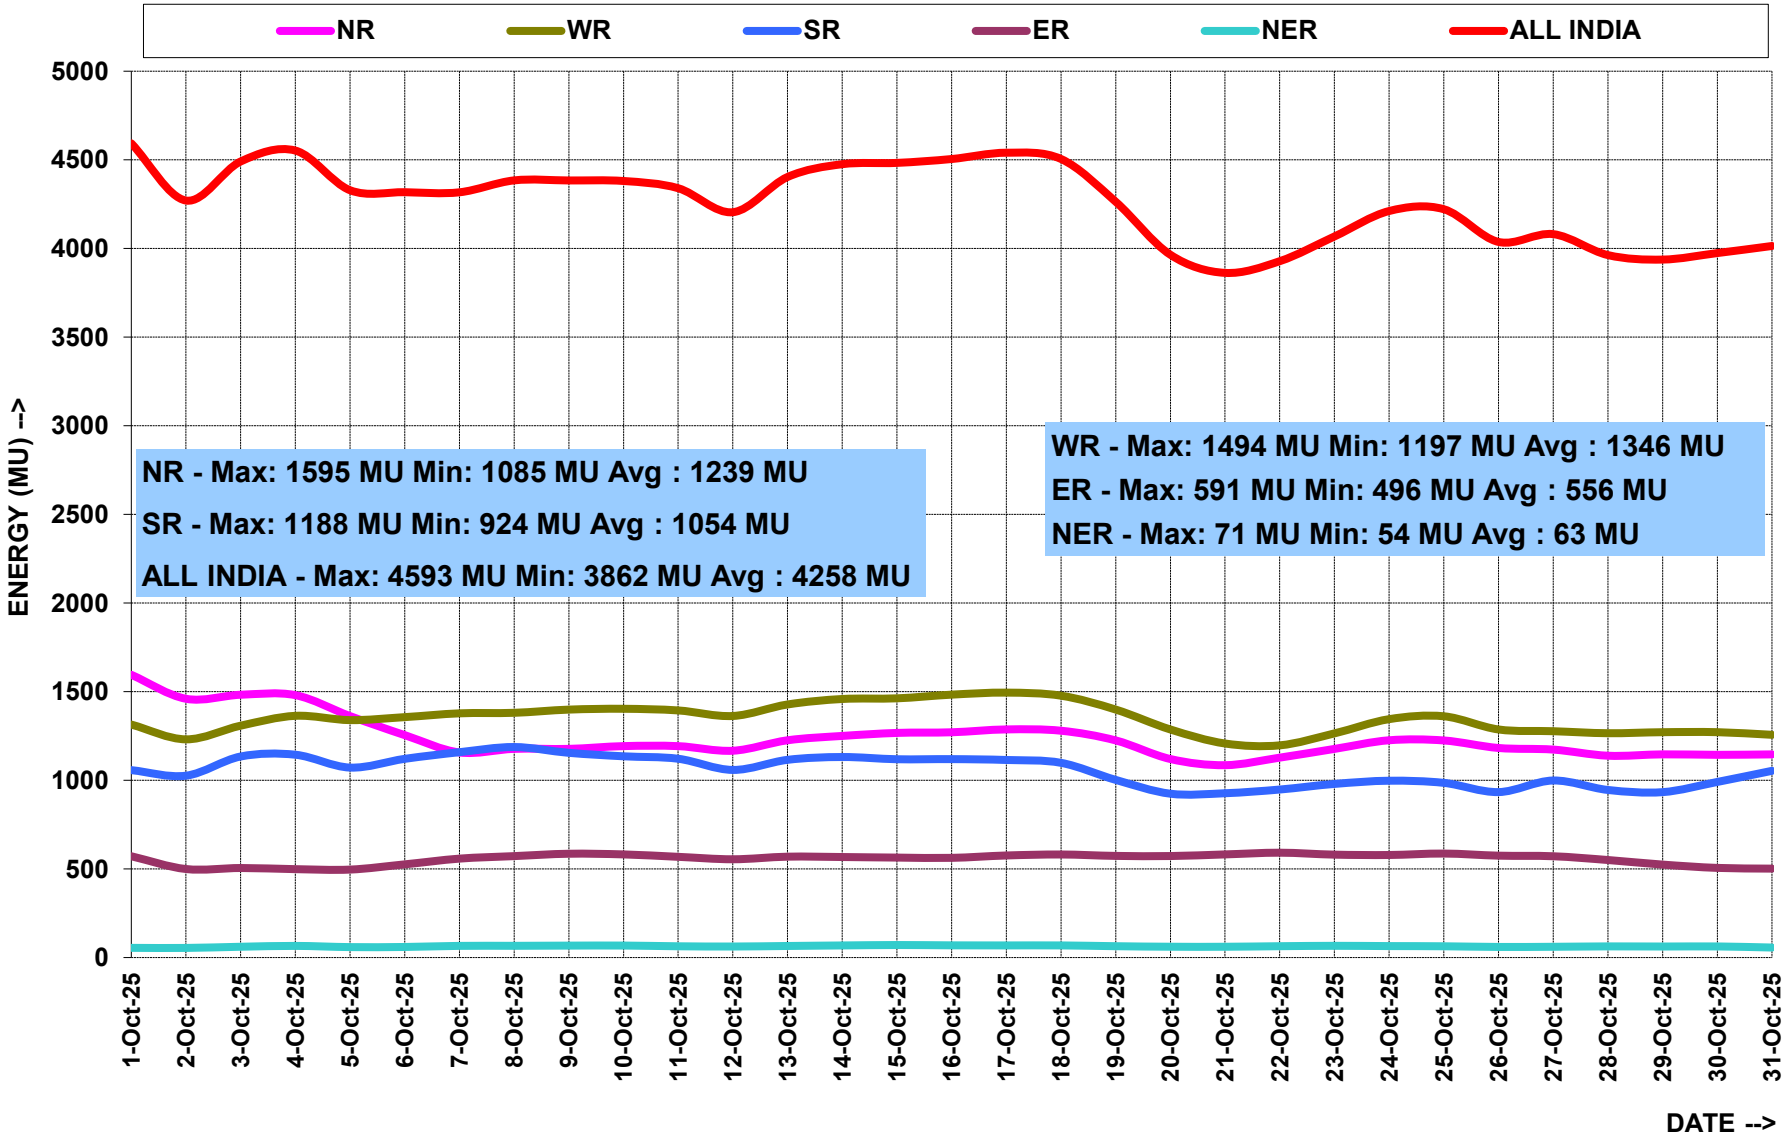

5. वर्ष 2025-26 के लिए आवृत्ति रूपरेखा
FREQUENCY PROFILE FOR YEAR 2025-26

राष्ट्रीय ग्रिड NATIONAL GRID							
आवृत्ति रूपरेखा (Hz) Frequency		<49.9	49.9-50.05	>50.05	उच्चतम आवृत्ति Max. Frequency	निम्नतम आवृत्ति Min. Frequency	औसत आवृत्ति Avg. Frequency
% समय % Time	Apr-25	5.16	75.64	19.20	50.49	49.42	50.00
	May-25	3.60	73.30	23.11	50.49	49.59	50.02
	Jun-25	7.56	71.85	20.60	50.27	49.74	50.00
	Jul-25	6.65	72.89	20.46	50.40	49.50	50.00
	Aug-25	6.63	76.22	17.16	50.35	49.46	50.00
	Sep-25	6.02	78.33	15.65	50.41	49.41	50.00
	Oct-25	6.60	78.59	14.81	50.31	49.42	49.99
	2025-26 (upto Oct)	**6.03**	**75.26**	**18.71**	**50.49**	**49.41**	**50.00**

5.1 अक्तूबर 2025 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR OCTOBER 2025

आवृत्ति रूपरेखा (Hz) Frequency Profile(Hz)		<49.9	49.9-50.05	>50.05	उच्चतम आवृत्ति Max. Frequency	निम्नतम आवृत्ति Min. Frequency	औसत आवृत्ति Avg. Frequency	एफ़.वी.आई. FVI
% समय % Time	01-Oct-25	7.99	67.06	24.95	50.30	49.75	50.00	0.07
	02-Oct-25	8.23	67.20	24.57	50.30	49.72	50.01	0.06
	03-Oct-25	11.44	79.86	8.70	50.13	49.65	49.98	0.04
	04-Oct-25	12.92	79.92	7.16	50.21	49.55	49.97	0.07
	05-Oct-25	7.69	71.11	21.20	50.30	49.77	50.00	0.05
	06-Oct-25	5.87	66.06	28.07	50.31	49.81	50.02	0.08
	07-Oct-25	7.89	76.61	15.50	50.26	49.82	49.99	0.04
	08-Oct-25	1.98	80.59	17.43	50.19	49.83	50.00	0.03
	09-Oct-25	4.86	84.64	10.50	50.17	49.80	49.99	0.03
	10-Oct-25	5.71	85.72	8.58	50.16	49.72	49.98	0.03
	11-Oct-25	4.50	83.24	12.26	50.24	49.80	49.99	0.04
	12-Oct-25	4.28	84.05	11.67	50.18	49.73	49.99	0.03
	13-Oct-25	6.18	77.77	16.05	50.29	49.64	50.00	0.04
	14-Oct-25	6.89	75.66	17.45	50.20	49.72	50.00	0.04
	15-Oct-25	2.92	85.54	11.54	50.25	49.79	50.00	0.02
	16-Oct-25	5.51	83.82	10.67	50.18	49.74	49.99	0.03
	17-Oct-25	5.60	82.70	11.70	50.23	49.75	50.00	0.03
	18-Oct-25	9.81	81.67	8.52	50.16	49.77	49.98	0.04
	19-Oct-25	8.58	79.40	12.03	50.14	49.67	49.99	0.04
	20-Oct-25	5.78	78.24	15.98	50.19	49.75	49.99	0.03
	21-Oct-25	5.63	76.85	17.52	50.16	49.75	50.00	0.03
	22-Oct-25	5.01	79.84	15.15	50.20	49.74	50.00	0.03
	23-Oct-25	6.90	82.03	11.08	50.21	49.76	49.99	0.03
	24-Oct-25	6.82	82.34	10.84	50.21	49.75	49.98	0.04
	25-Oct-25	2.52	81.33	16.15	50.24	49.78	50.00	0.03
	26-Oct-25	4.35	83.07	12.58	50.19	49.79	49.99	0.03
	27-Oct-25	0.74	86.89	12.37	50.16	49.87	50.00	0.02
	28-Oct-25	7.77	65.87	26.37	50.27	49.66	50.00	0.06
	29-Oct-25	6.84	80.21	12.95	50.28	49.75	49.99	0.04
	30-Oct-25	13.87	70.44	15.69	50.24	49.63	49.98	0.06
	31-Oct-25	9.44	76.60	13.96	50.26	49.42	49.99	0.09


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: अक्टूबर 2025 MONTH:- OCTOBER 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	अखिल भारतीय All India
01-Oct-25	325	104	159	106	32	726
02-Oct-25	312	108	157	103	34	714
03-Oct-25	303	113	173	111	36	736
04-Oct-25	305	114	170	120	39	747
05-Oct-25	291	107	162	93	38	692
06-Oct-25	269	107	163	71	39	648
07-Oct-25	289	110	172	89	36	697
08-Oct-25	280	116	171	98	35	700
09-Oct-25	268	114	167	104	36	689
10-Oct-25	249	112	171	107	36	675
11-Oct-25	235	106	168	104	36	650
12-Oct-25	225	95	158	97	35	609
13-Oct-25	219	93	164	96	32	603
14-Oct-25	220	77	164	88	33	582
15-Oct-25	222	71	176	81	33	582
16-Oct-25	213	66	163	83	31	555
17-Oct-25	208	46	164	83	30	530
18-Oct-25	203	41	152	77	29	502
19-Oct-25	200	37	154	74	28	492
20-Oct-25	193	39	138	71	28	469
21-Oct-25	191	33	145	69	27	465
22-Oct-25	195	33	133	71	26	457
23-Oct-25	186	35	141	66	27	454
24-Oct-25	175	39	178	62	26	481
25-Oct-25	172	36	148	66	26	448
26-Oct-25	161	38	154	63	26	442
27-Oct-25	170	57	170	59	25	482
28-Oct-25	168	77	161	62	26	494
29-Oct-25	166	85	163	58	24	496
30-Oct-25	163	87	175	57	26	508
31-Oct-25	158	85	196	78	25	541
कुल TOTAL	6932	2378	5030	2567	959	17866
उच्चतम MAXIMUM	325	116	196	120	39	747
निम्नतम MINIMUM	158	33	133	57	24	442
औसत AVERAGE	224	77	162	83	31	576
संचयी 2025-26 Cumulative 2025-26	66926	15121	29751	16139	6350	134288
अब तक का उच्चतम All Time Max.	443	167	208	157	46	892
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	15.08.25	21.08.25

HYDRO ENERGY DURING THE MONTH OF OCTOBER' 2025

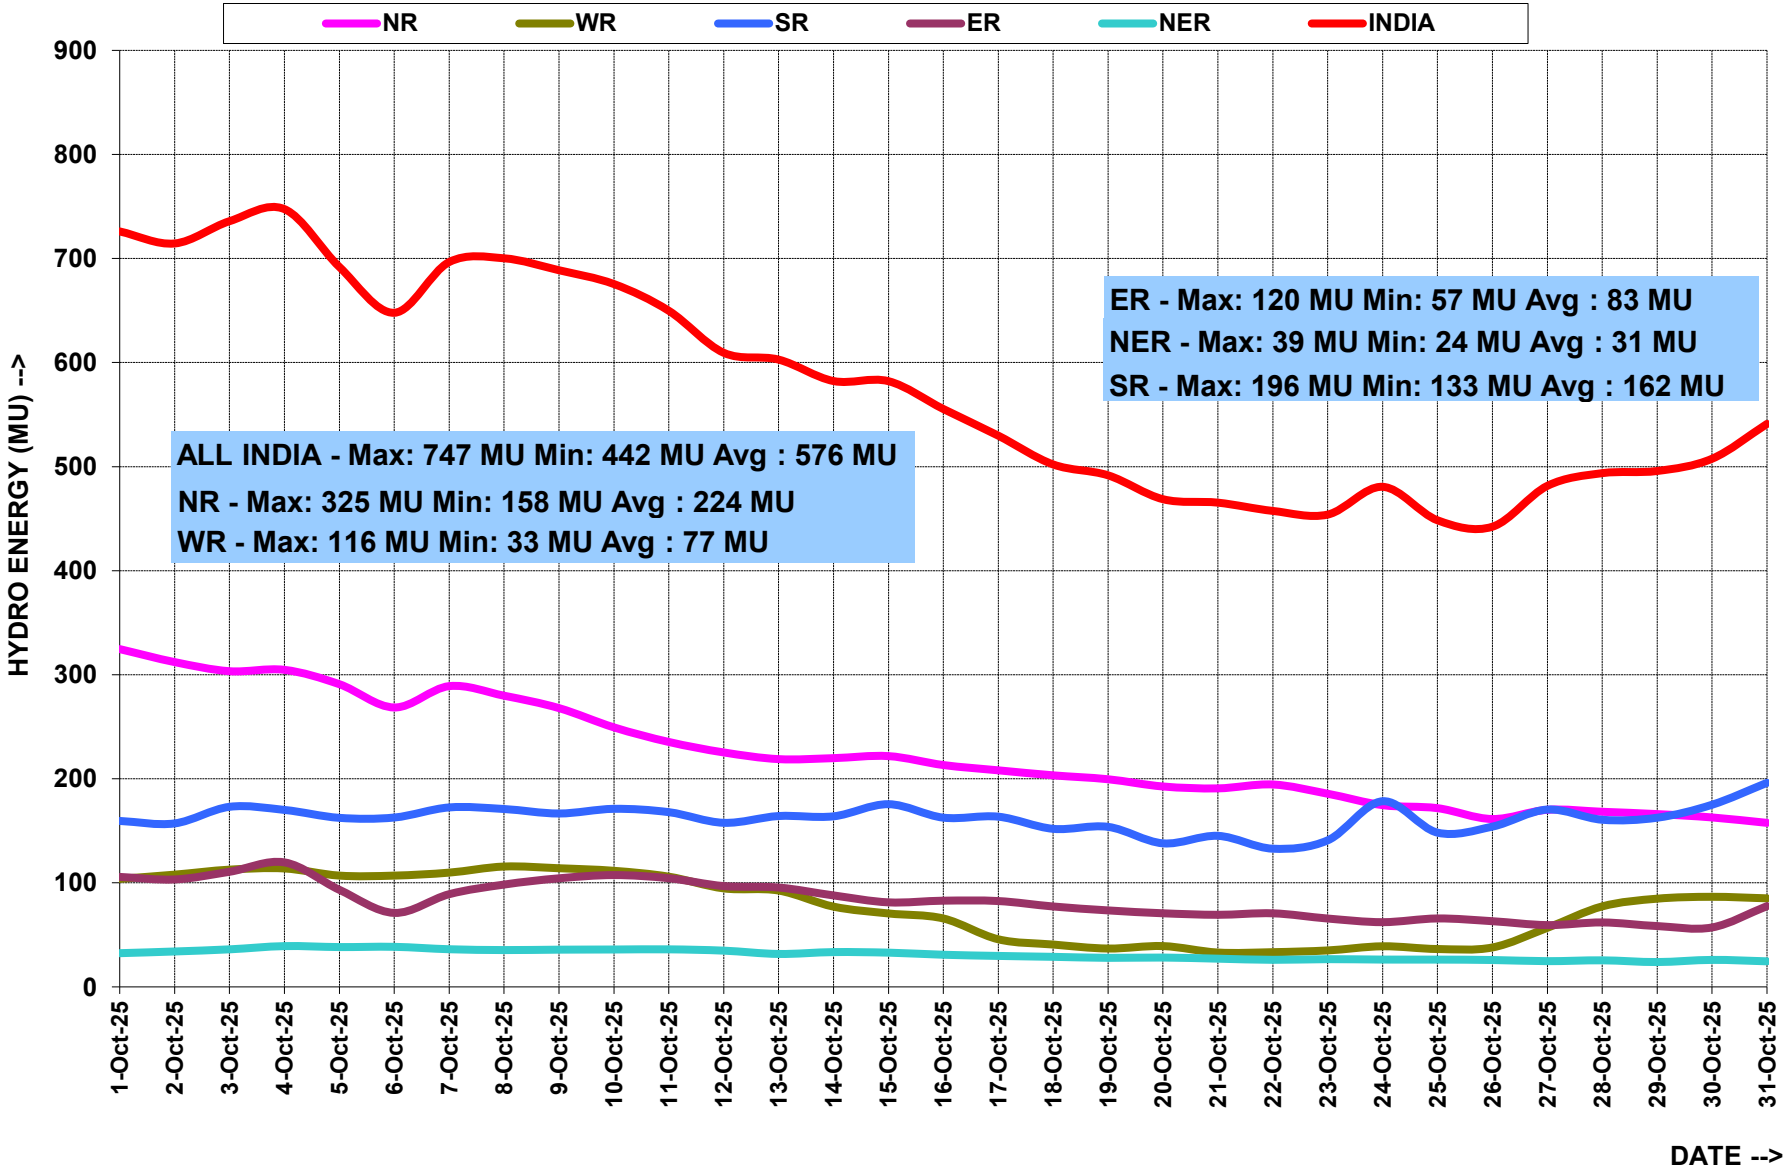

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: अक्टूबर 2025 MONTH:- OCTOBER 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	अखिल भारतीय All India
01-Oct-25	4	148	215	----------	----------	367
02-Oct-25	5	133	182	----------	----------	320
03-Oct-25	6	124	96	----------	----------	225
04-Oct-25	13	97	68	----------	----------	178
05-Oct-25	36	120	66	----------	----------	222
06-Oct-25	49	151	65	----------	----------	265
07-Oct-25	11	80	47	----------	----------	139
08-Oct-25	7	29	27	----------	----------	63
09-Oct-25	6	28	28	----------	----------	63
10-Oct-25	7	32	27	----------	----------	66
11-Oct-25	3	34	34	----------	----------	72
12-Oct-25	3	47	35	----------	----------	85
13-Oct-25	3	39	35	----------	----------	77
14-Oct-25	2	51	42	----------	----------	96
15-Oct-25	4	53	53	----------	----------	110
16-Oct-25	5	59	75	----------	----------	138
17-Oct-25	4	60	93	----------	----------	157
18-Oct-25	5	53	52	----------	----------	110
19-Oct-25	6	47	44	----------	----------	97
20-Oct-25	7	59	49	----------	----------	115
21-Oct-25	10	78	46	----------	----------	134
22-Oct-25	15	125	88	----------	----------	228
23-Oct-25	7	135	67	----------	----------	210
24-Oct-25	10	134	41	----------	----------	185
25-Oct-25	13	149	56	----------	----------	218
26-Oct-25	31	137	60	----------	----------	228
27-Oct-25	37	168	116	----------	----------	321
28-Oct-25	55	177	201	----------	----------	433
29-Oct-25	37	184	217	----------	----------	438
30-Oct-25	38	149	166	----------	----------	353
31-Oct-25	8	119	71	----------	----------	198
कुल TOTAL	448	2999	2466	----------	----------	5913
उच्चतम MAXIMUM	55	184	217	----------	----------	438
निम्नतम MINIMUM	2	28	27	----------	----------	63
औसत AVERAGE	14	97	80	----------	----------	191
संचयी 2025-26 Cumulative 2025-26	5246	29838	34542	----------	----------	69625
अब तक का उच्चतम All Time Max.	86	319	342	----------	----------	673
दिनांक Date	07.08.23	29.07.25	26.07.25	----------	----------	29.07.25

*__Source:__ As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: अक्टूबर 2025 MONTH:- OCTOBER 2025

सभी आंकड़े मिलियन यूनिट मे All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	अखिल भारतीय All India
01-Oct-25	145	92	135	3.2	0.4	376
02-Oct-25	122	83	123	1.2	0.7	331
03-Oct-25	152	116	144	1.3	1.0	414
04-Oct-25	182	127	119	2.1	1.0	431
05-Oct-25	152	115	125	2.2	0.8	396
06-Oct-25	127	113	131	3.2	0.8	376
07-Oct-25	137	131	128	3.0	0.9	400
08-Oct-25	159	143	120	3.3	0.7	426
09-Oct-25	166	143	124	2.9	0.9	436
10-Oct-25	174	140	121	3.2	0.9	440
11-Oct-25	173	140	134	3.4	0.7	450
12-Oct-25	150	132	144	2.6	0.9	430
13-Oct-25	193	150	128	3.3	1.0	476
14-Oct-25	203	152	112	3.8	1.0	472
15-Oct-25	205	152	114	4.0	1.1	475
16-Oct-25	204	153	101	3.6	1.2	463
17-Oct-25	200	153	111	3.7	1.1	468
18-Oct-25	203	150	119	3.8	1.2	476
19-Oct-25	190	155	120	2.5	1.2	469
20-Oct-25	173	144	95	2.7	1.2	416
21-Oct-25	173	134	73	3.5	1.1	384
22-Oct-25	158	125	86	3.3	1.1	373
23-Oct-25	171	135	94	3.3	1.1	405
24-Oct-25	184	132	82	3.5	1.1	403
25-Oct-25	188	118	127	3.4	1.1	438
26-Oct-25	180	87	124	3.3	1.0	395
27-Oct-25	167	81	87	2.5	1.1	338
28-Oct-25	148	76	66	1.9	1.1	293
29-Oct-25	142	64	106	1.9	0.6	314
30-Oct-25	140	51	144	2.0	0.5	337
31-Oct-25	154	86	152	1.8	0.6	394
कुल TOTAL	5216	3772	3589	89	29	12695
उच्चतम MAXIMUM	205	155	152	4.0	1.2	476
निम्नतम MINIMUM	122	51	66	1.2	0.4	293
औसत AVERAGE	168	122	116	2.9	0.9	410
संचयी 2025-26 Cumulative 2025-26	39179	25614	25855	647	185.9	91481
अब तक का उच्चतम All Time Max.	228	160	156	5.7	3.5	534
दिनांक Date	22.04.25	24.04.25	06.03.25	18.03.25	08.09.24	23.04.25

*__Source__: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग आपूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: अक्टूबर 2025 MONTH:- OCTOBER 2025

सभी आंकड़े मेगावाट मे All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	अखिल भारतीय All India	विभिन्नता फ़ैक्टर Diversity Factor*
01-Oct-25	74696	60672	49555	27995	2958	205145	1.052
02-Oct-25	68441	55087	49164	23700	2785	185917	1.071
03-Oct-25	69376	63811	54743	23532	3333	208698	1.029
04-Oct-25	69428	64719	53499	22924	3475	207987	1.029
05-Oct-25	64873	60519	49654	23431	2834	195611	1.029
06-Oct-25	59720	64363	52380	25513	3326	201569	1.019
07-Oct-25	57302	65820	53254	26638	3547	204523	1.010
08-Oct-25	58959	65652	55489	27194	3531	206129	1.023
09-Oct-25	59081	66712	52298	27813	3636	207280	1.011
10-Oct-25	58701	66267	51544	26941	3523	205917	1.005
11-Oct-25	59073	66395	51266	28826	3447	206278	1.013
12-Oct-25	56751	63599	46798	26462	3348	194447	1.013
13-Oct-25	60894	67998	50834	27175	3640	209433	1.005
14-Oct-25	60387	68533	51571	27150	3739	209109	1.011
15-Oct-25	61585	67007	52122	27190	3777	209062	1.013
16-Oct-25	61262	68277	52235	27518	3712	210710	1.011
17-Oct-25	61619	68252	52541	27547	3718	209673	1.019
18-Oct-25	61619	68252	52541	27547	3718	209673	1.019
19-Oct-25	56918	61849	47766	27343	3368	191639	1.029
20-Oct-25	53030	57254	43996	26692	3335	180140	1.023
21-Oct-25	50534	54588	46432	27739	3440	176506	1.035
22-Oct-25	53410	53070	44584	28505	3606	182216	1.005
23-Oct-25	55970	56904	46858	27394	3653	190183	1.003
24-Oct-25	58700	60671	47143	27900	3557	197085	1.004
25-Oct-25	59162	62294	47146	27750	3526	198249	1.008
26-Oct-25	55553	57986	43278	26476	3240	185956	1.003
27-Oct-25	57009	58918	47016	27170	3479	189372	1.022
28-Oct-25	55400	60692	45283	25625	3528	188905	1.009
29-Oct-25	57148	60230	46182	25142	3452	191246	1.005
30-Oct-25	56023	59198	49136	24154	3323	191290	1.003
31-Oct-25	56016	59301	49555	24017	3164	191223	1.004
उच्चतम MAXIMUM	74696	68533	55489	28826	3777	210710	1.071
निम्नतम MINIMUM	50534	53070	43278	22924	2785	176506	1.003
औसत AVERAGE	59634	62416	49544	26484	3442	198102	1.017
अब तक का उच्चतम All Time Max.	91215	80000	69942	33452	4159	250070	
दिनांक Date	19.06.24	08.02.25	21.03.25	23.07.25	26.09.25	30.05.24	


* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।


Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

10. DEMAND AND GENERATION PLOTS FOR 16th OCTOBER (MAXIMUM DEMAND MET)

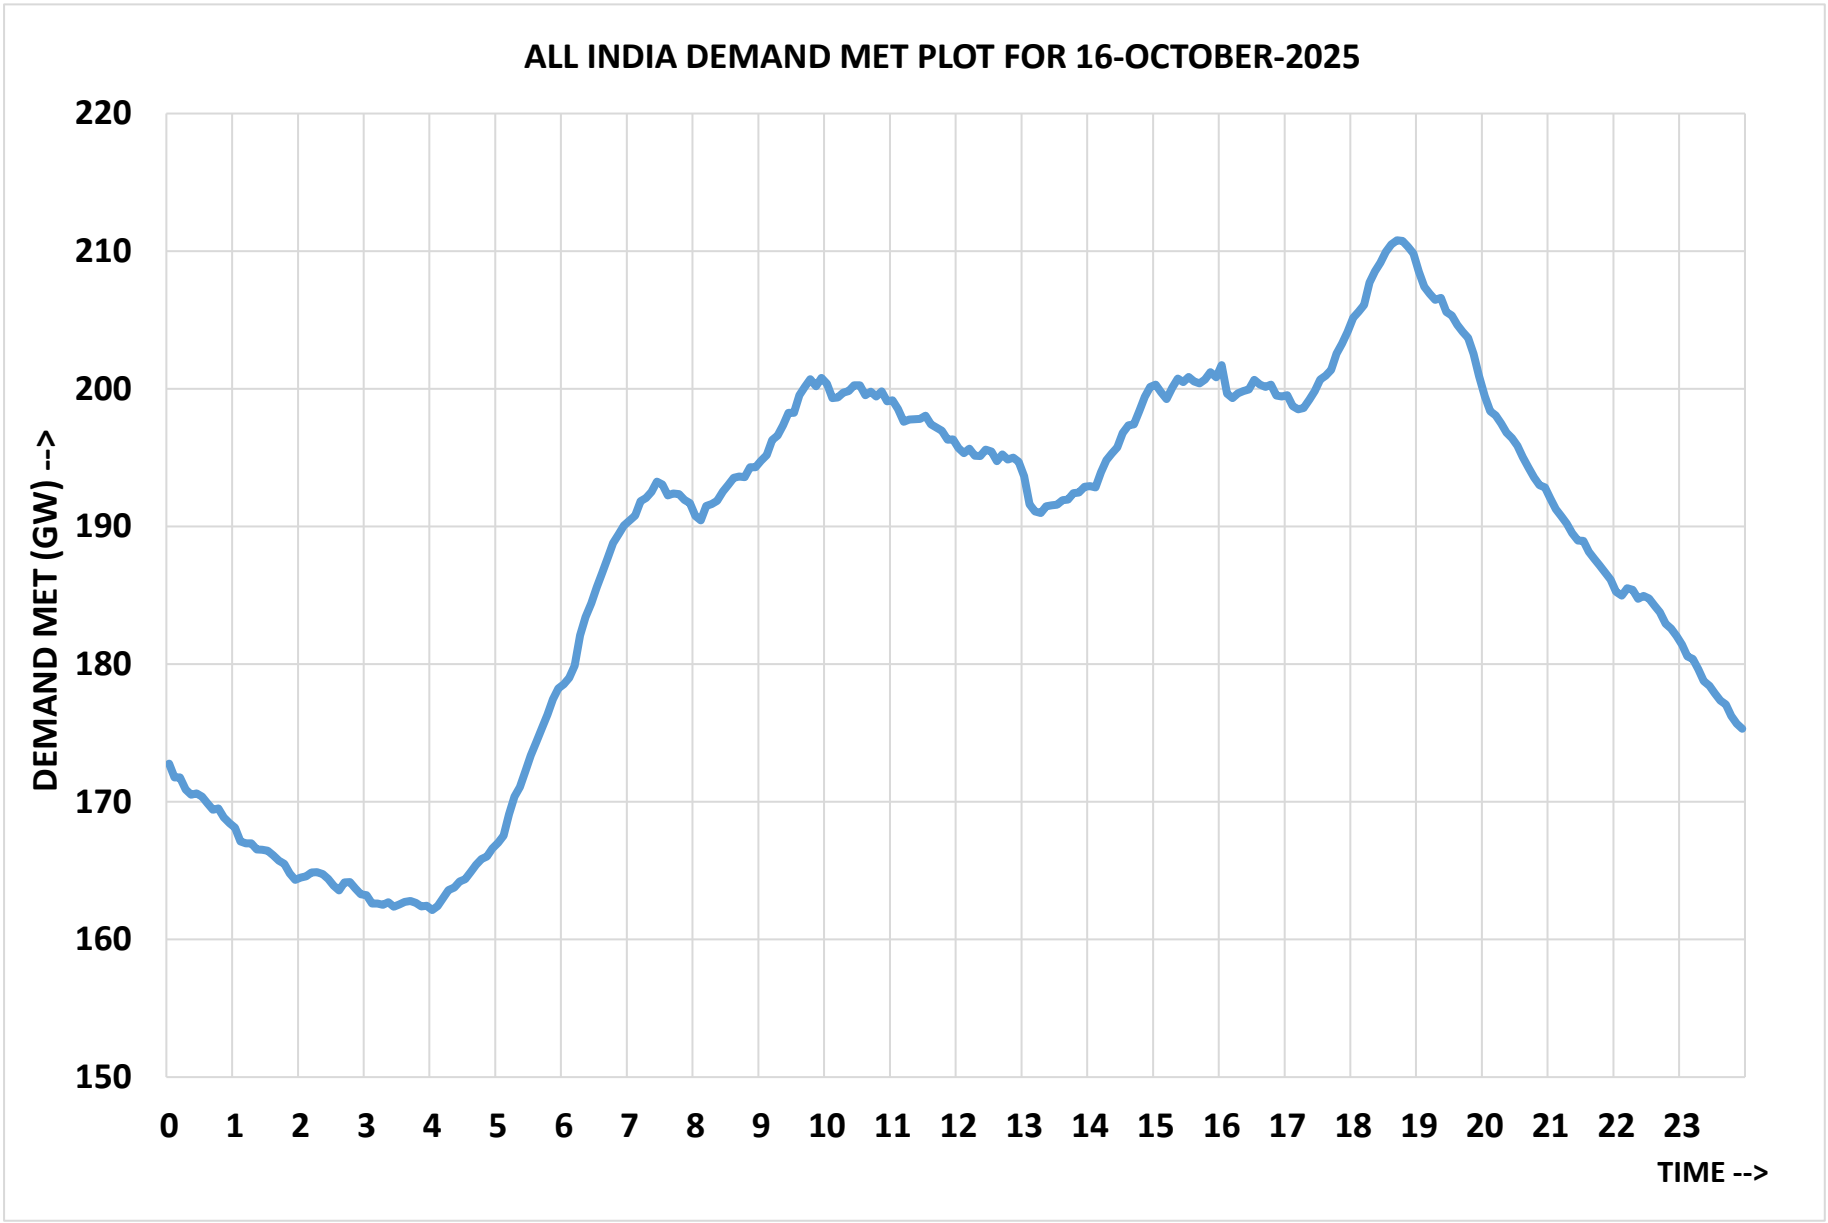

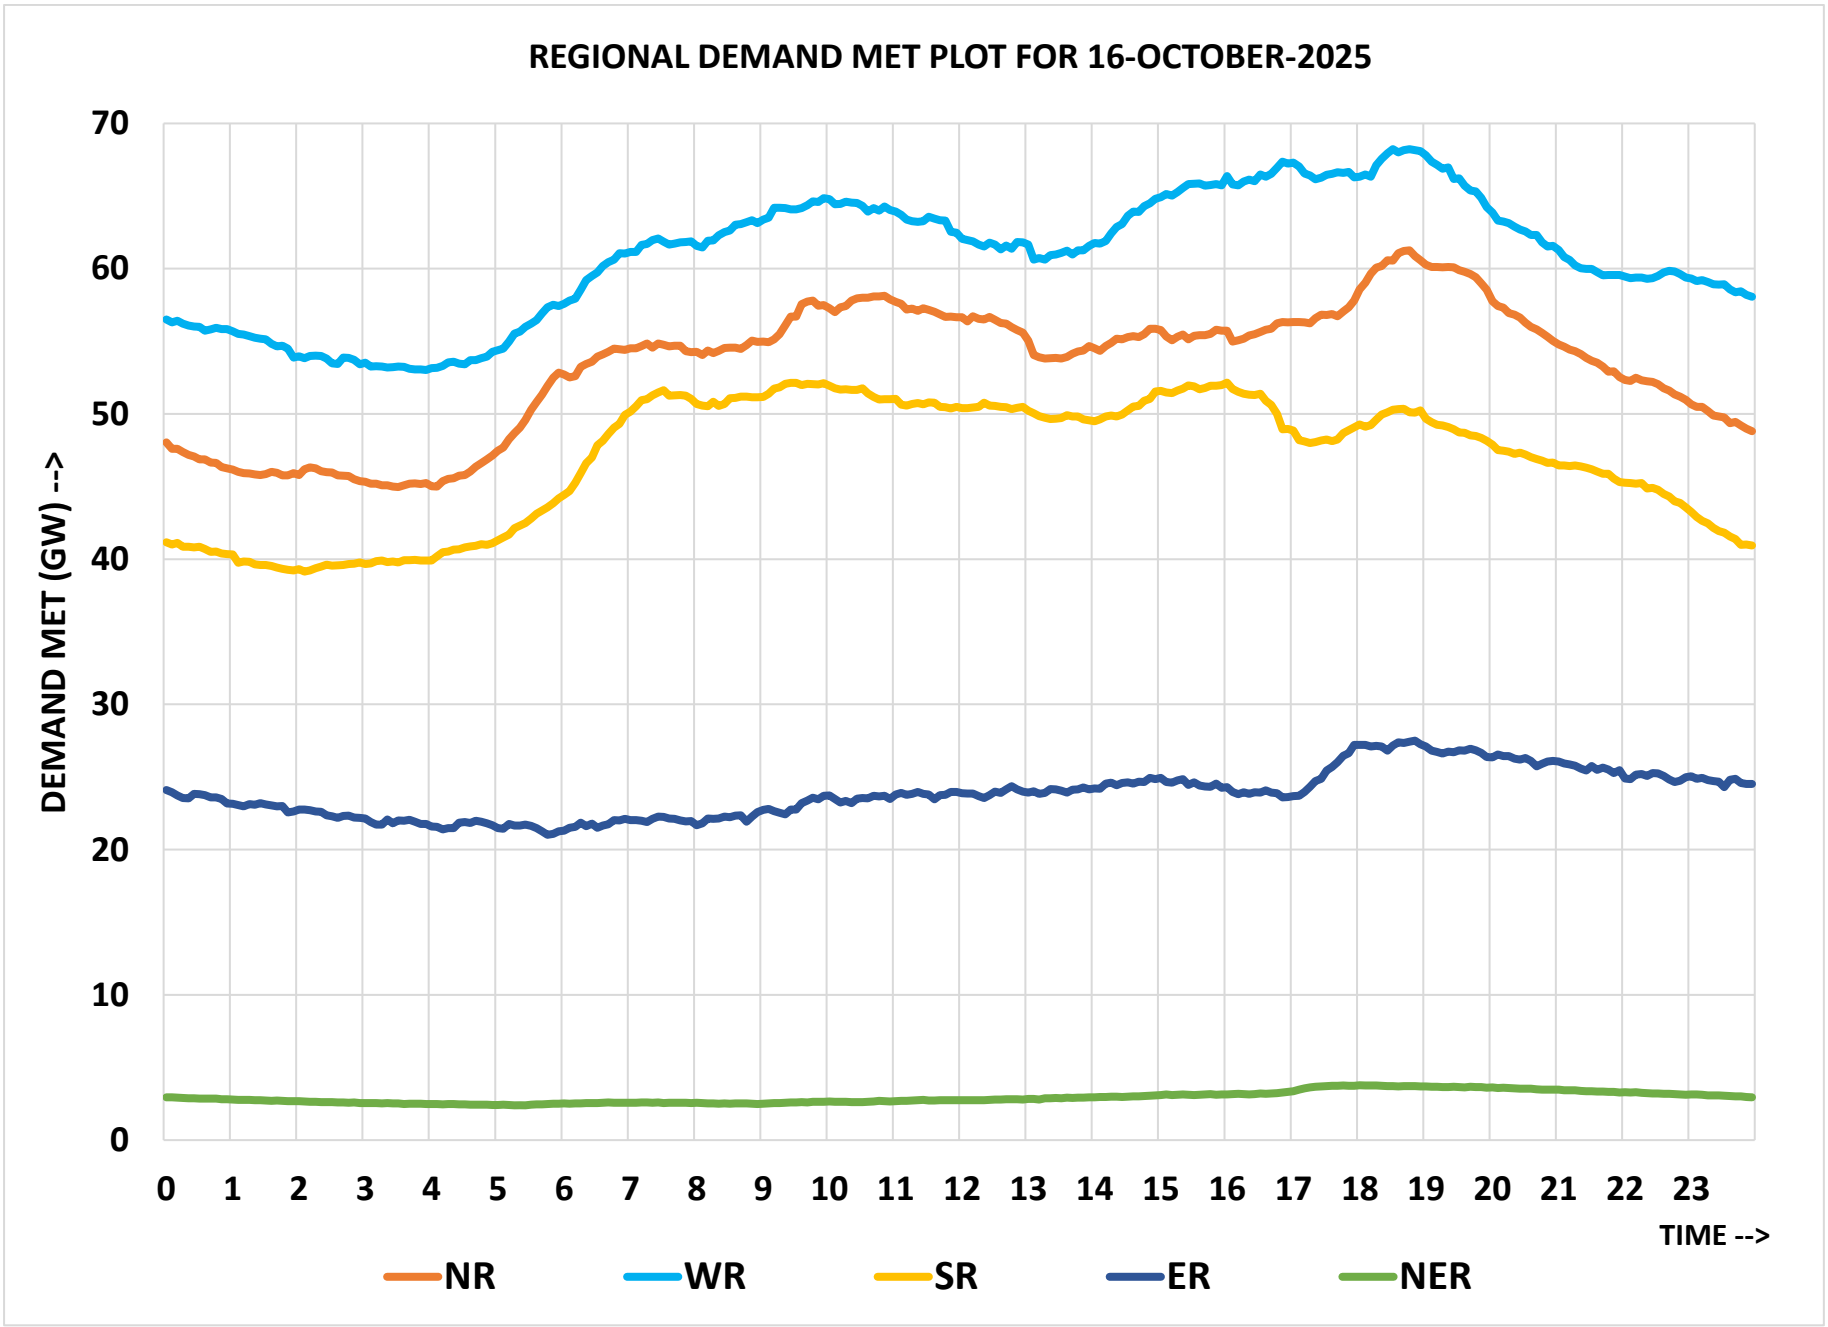
REGIONAL DEMAND MET PLOT FOR 16-OCTOBER-2025
DEMAND MET (GW) -->
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
NR
WR
SR
ER
NER

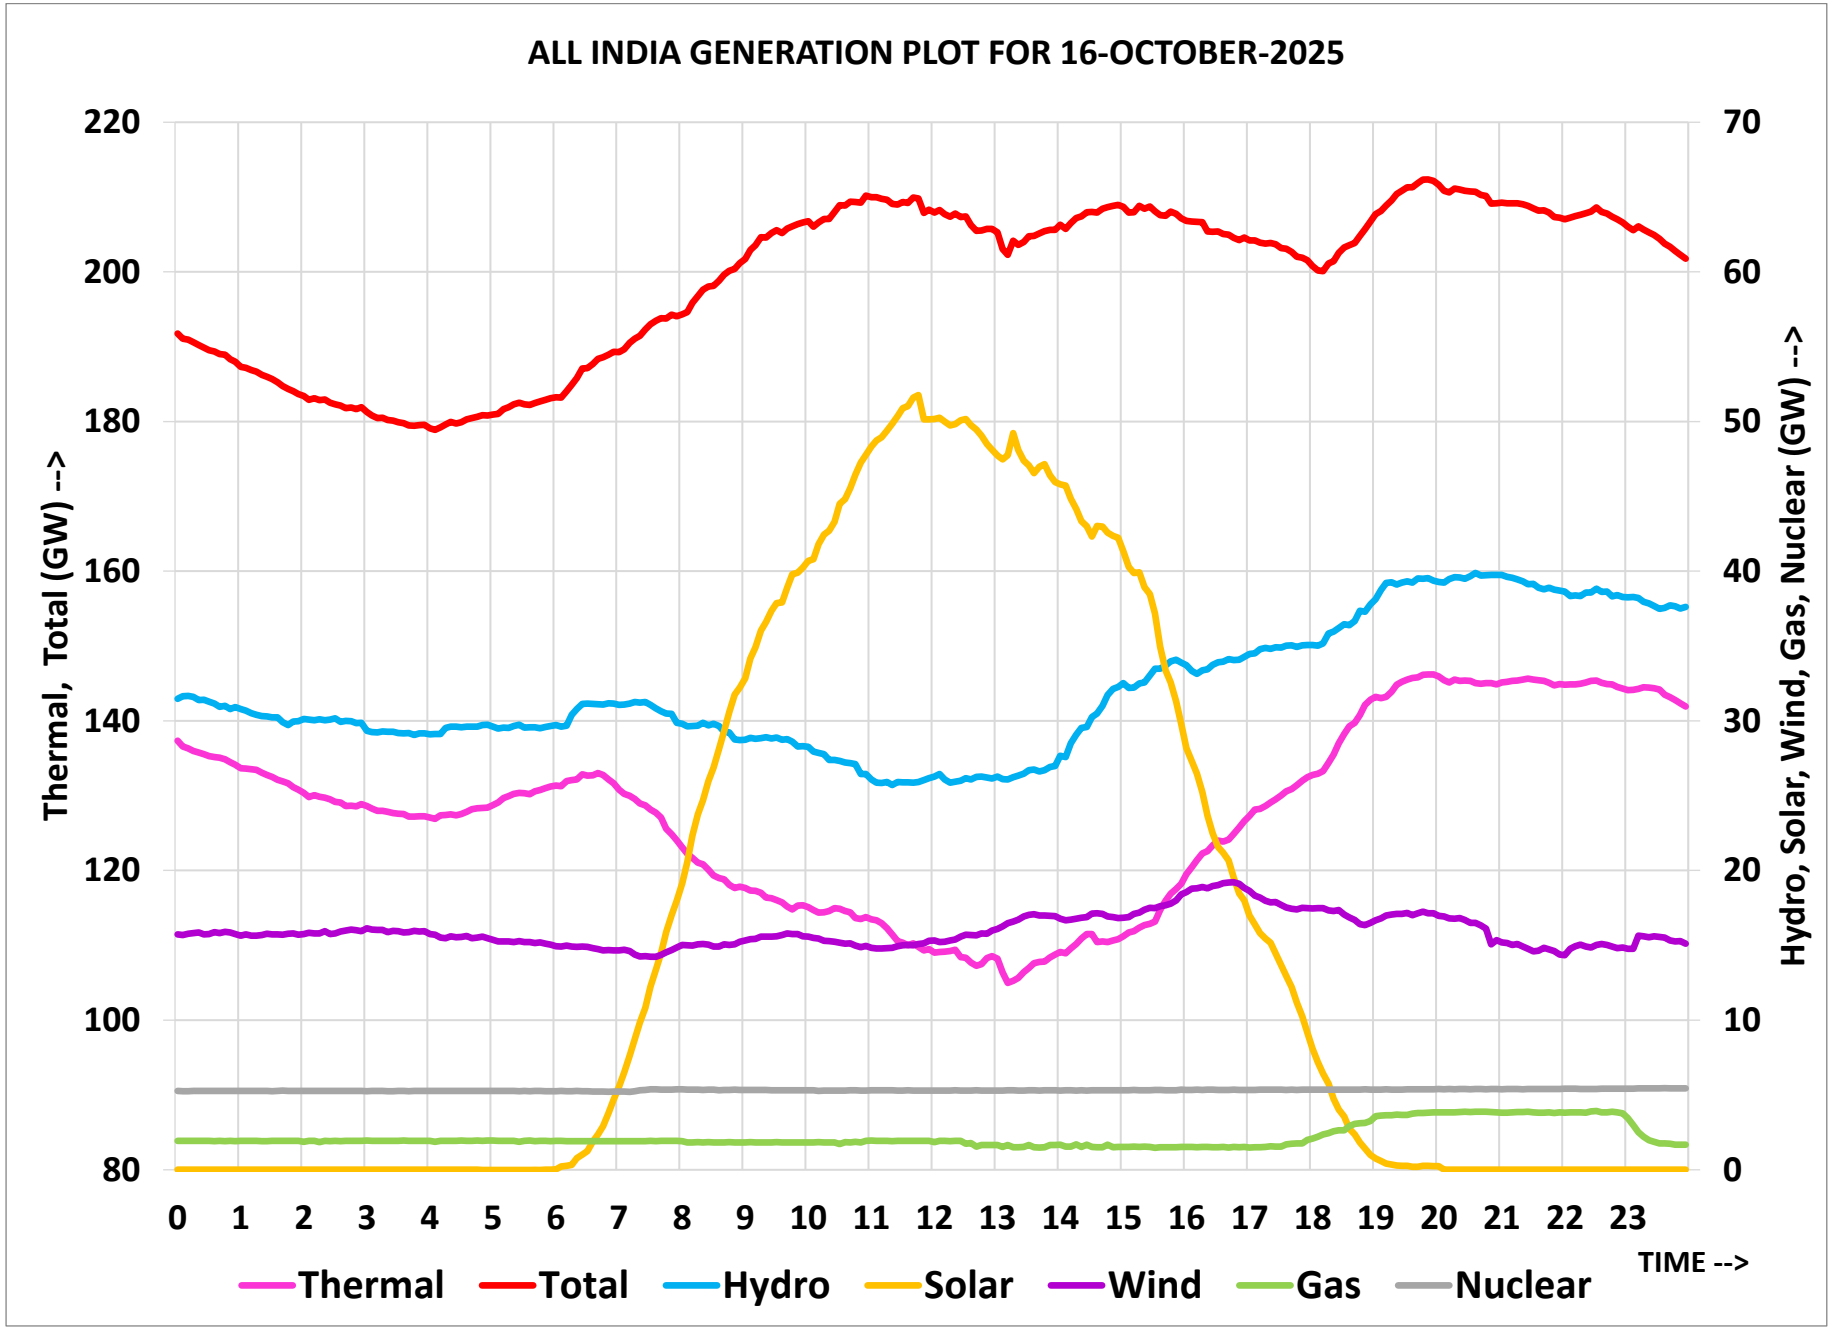
ALL INDIA GENERATION PLOT FOR 16-OCTOBER-2025
Thermal, Total (GW) -->
Hydro, Solar, Wind, Gas, Nuclear (GW) -->
220
200
180
160
140
120
100
80
70
60
50
40
30
20
10
0
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
TIME -->
Thermal
Total
Hydro
Solar
Wind
Gas
Nuclear

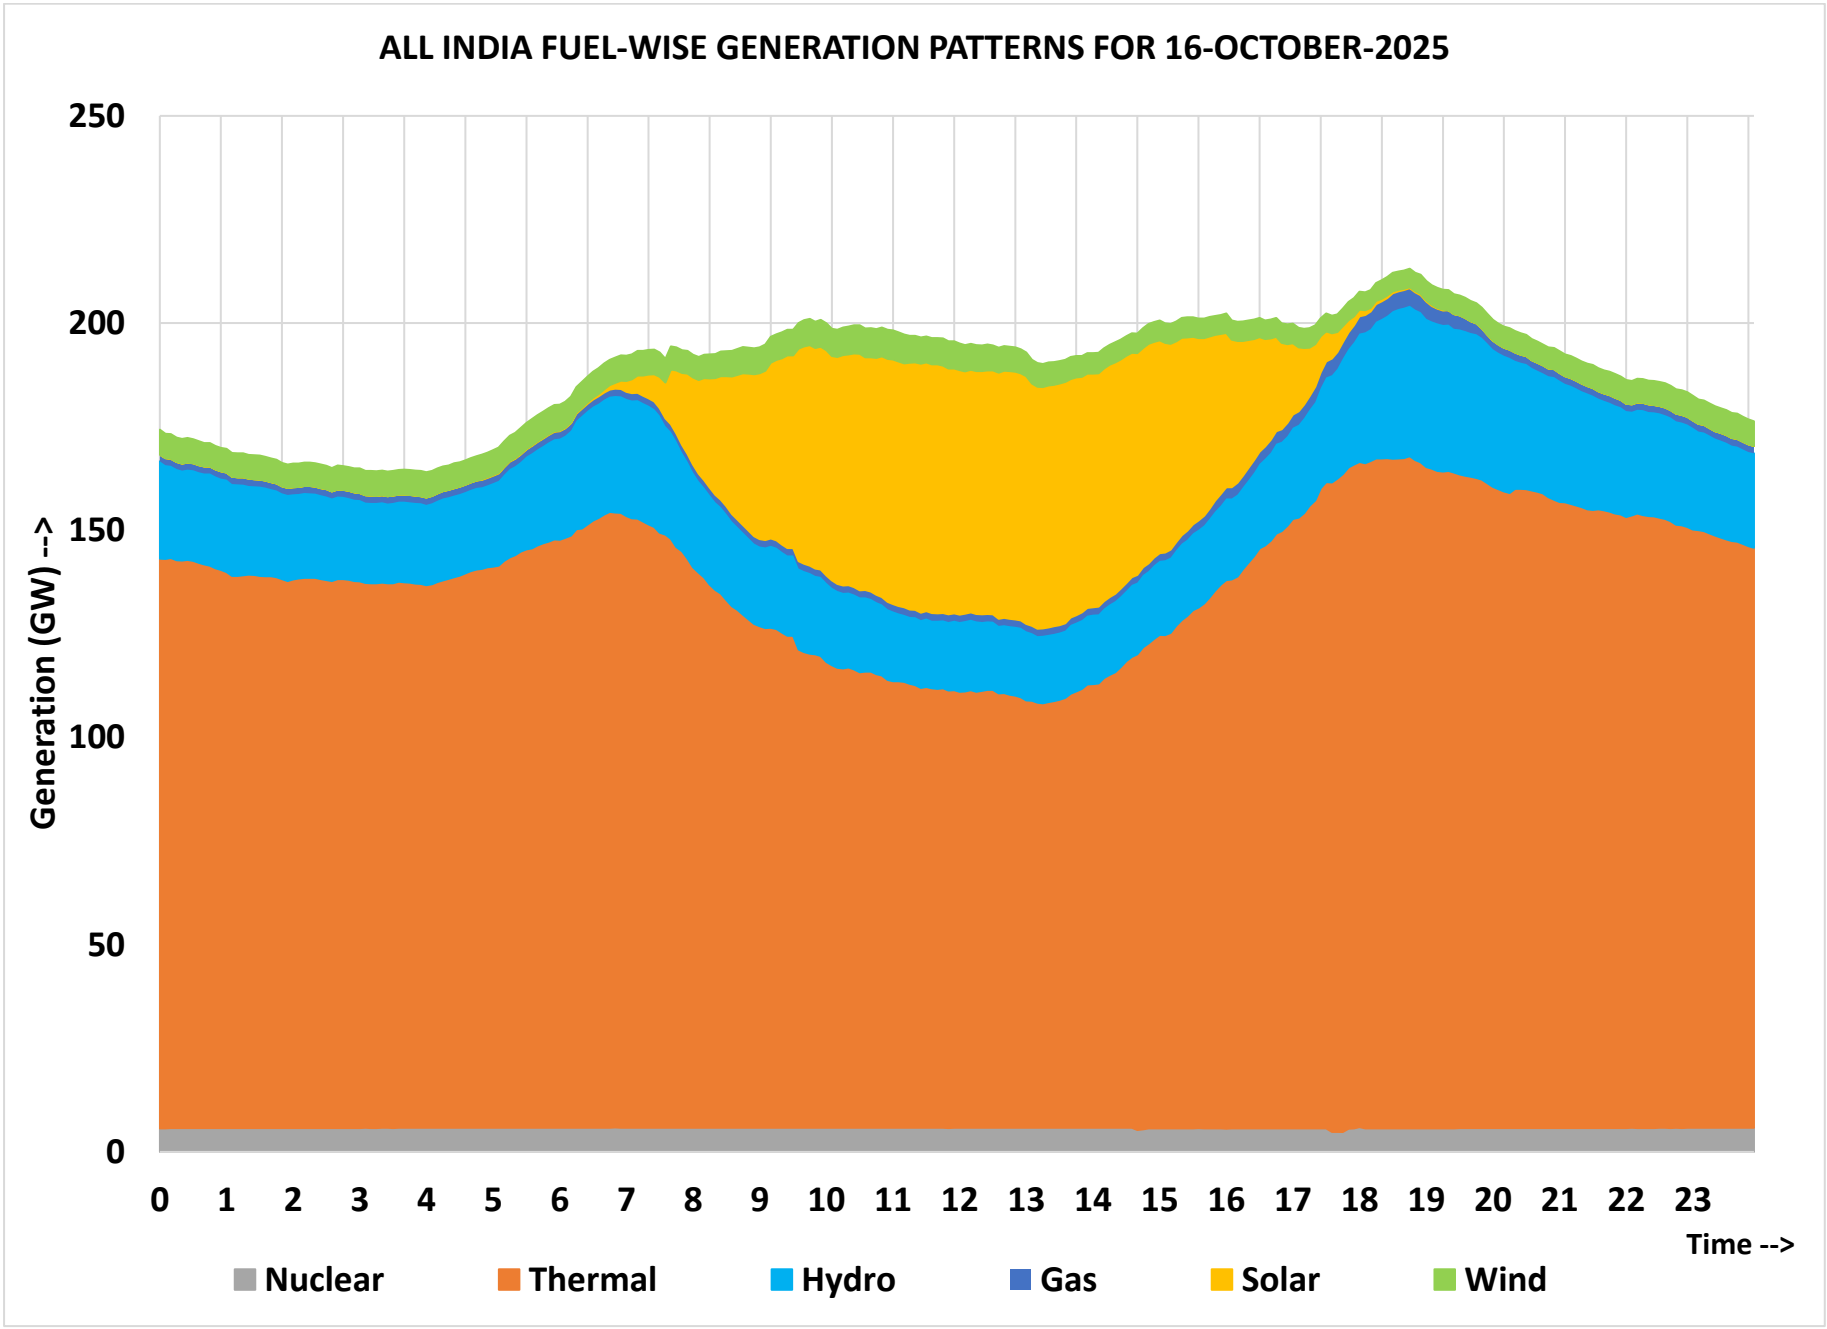
ALL INDIA FUEL-WISE GENERATION PATTERNS FOR 16-OCTOBER-2025
250
200
150
100
50
0
Generation (GW) -->
0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23
Time -->
Nuclear
Thermal
Hydro
Gas
Solar
Wind

16 अक्टूबर 2025 (अधिकतम माँग*) की अखिल भारतीय माँग आपूर्ति
ALL INDIA DEMAND MET FOR 16 OCTOBER 2025 (MAXIMUM DEMAND*)

समय Time	अखिल भारतीय माँग आपूर्ति (मे.वा.) All India Demand Met(MW)		समय Time	अखिल भारतीय माँग आपूर्ति (मे.वा.) All India Demand Met(MW)
00:05	171779		12:05	195334
00:20	170522		12:20	195117
00:35	169897		12:35	194755
00:50	168856		12:50	194997
01:05	167120		13:05	191607
01:20	166547		13:20	191469
01:35	166124		13:35	191913
01:50	164798		13:50	192474
02:05	164577		14:05	192834
02:20	164742		14:20	195296
02:35	163555		14:35	197347
02:50	163704		14:50	199417
03:05	162611		15:05	199736
03:20	162706		15:20	200757
03:35	162737		15:35	200543
03:50	162398		15:50	201216
04:05	162423		16:05	199647
04:20	163778		16:20	199848
04:35	164882		16:35	200314
04:50	166039		16:50	199504
05:05	167547		17:05	198750
05:20	171075		17:20	199208
05:35	174333		17:35	200954
05:50	177448		17:50	203273
06:05	178994		18:05	205617
06:20	183431		18:20	208545
06:35	186635		18:35	210481
06:50	189421		18:50	210332
07:05	190793		19:05	207427
07:20	192507		19:20	206597
07:35	192262		19:35	204643
07:50	191923		19:50	202531
08:05	190452		20:05	198382
08:20	191868		20:20	196815
08:35	193531		20:35	195015
08:50	194294		20:50	193009
09:05	195184		21:05	191267
09:20	197343		21:20	189517
09:35	199540		21:35	188174
09:50	200185		21:50	186646
10:05	199317		22:05	184984
10:20	199829		22:20	184737
10:35	199532		22:35	184252
10:50	199826		22:50	182595
11:05	198547		23:05	180553
11:20	197793		23:20	178773
11:35	197427		23:35	177343
11:50	196314		23:50	175683

अधिकतम 210710 मेगावॉट माँग की आपूर्ति 18:40 बजे की गई (1-मिनट SCADA डेटा के अनुसार)

Maximum Demand of 210710 MW met@ 18:40 hrs (from 1 min. interval SCADA DATA)

* 15 minute interval SCADA DATA of instanteneous demand

11. विद्युत आपूर्ति की वास्तविक स्थिति - अक्टूबर 2025

11. ACTUAL POWER SUPPLY POSITION - OCTOBER 2025

क्षेत्र REGION	राज्य STATE	दैनिक ऊर्जा आवश्यकता एवं आपूर्ति (मि.यू./दिन) Energy Requirement & Met (MU/Day)			ऊर्जा आवश्यकता एवं आपूर्ति (मि.यू.) Energy Requirement & Met (MU)				अधिकतम माँग/अधिकतम माँग आपूर्ति (मेगावॉट) Peak Demand/Peak Demand Met in MW			
		ऊर्जा आवश्यकता Energy Requirement	ऊर्जा आपूर्ति Energy met	अतिरिक्त (+) / अभाव (-) Surplus(+)/ Deficit(-)	ऊर्जा आवश्यकता Energy Requirement	ऊर्जा आपूर्ति Energy met	अतिरिक्त (+) / अभाव (-) Surplus(+)/ Deficit(-)	% अभाव % Shortage	अधिकतम मांग Peak Demand	अधिकतम माँग आपूर्ति Peak Demand Met	अतिरिक्त (+) / अभाव (-) Surplus(+)/ Deficit(-)	% अभाव % Shortage
उ०क्षे० NR	चंडीगढ़ Chandigarh	4	4	0.0	132	132	0	0.0	323	323	0	0.0
	दिल्ली Delhi	92	92	0.0	2849	2849	0	0.0	5956	5956	0	0.0
	हरियाणा Haryana	176	176	0.0	5459	5459	0	0.0	11372	11372	0	0.0
	हिमाचल प्रदेश Himachal Pradesh	32	32	0.0	981	981	0	0.0	2003	2003	0	0.0
	जम्मू और कश्मीर एवं लद्दाख J&K(UT) and Ladakh(UT)	51	51	0.0	1586	1586	0	0.0	2723	2723	0	0.0
	पंजाब Punjab	176	176	0.0	5442	5442	0	0.0	12989	12989	0	0.0
	राजस्थान Rajasthan	259	259	0.0	8024	8024	0	0.0	14165	14165	0	0.0
	उत्तर प्रदेश Uttar Pradesh	405	405	-0.2	12552	12546	-6	0.0	26269	26269	0	0.0
	उत्तराखंड Uttarakhand	40	40	0.0	1240	1239	-1	-0.1	2466	2466	0	0.0
	रेलवे_उ.क्षे.अ.रा.प्र.प्र. Railway_NR ISTS	4	4	0.0	137	137	0	0.0	239	239	0	0.0
	एन.एफ.एल. NFL	0	0	0.0	2	2	0	0.0	4	4	0	0.0
	कुल TOTAL	1239	1239	-0.2	38402	38396	-6	0.0	74215	74215	0	0.0
प०क्षे० WR	गुजरात Gujarat	396	396	0.0	12270	12270	0	0.0	21822	21822	0	0.0
	मध्य प्रदेश Madhya Pradesh	241	241	0.0	7466	7466	0	0.0	13518	13518	0	0.0
	छत्तीसगढ़ Chhattisgarh	106	106	0.0	3280	3280	0	0.0	5288	5279	-9	-0.2
	महाराष्ट्र Maharashtra	523	523	0.0	16206	16206	0	0.0	27286	27286	0	0.0
	गोवा Goa	15	15	0.0	450	450	0	0.0	750	750	0	0.0
	दादरा और नगर हवेली एवं दमन और दीव DNHDDPDCL	29	29	0.0	903	903	0	0.0	1394	1394	0	0.0
	आ.मि.नि.स्.इं.लि. AMNSIL	18	18	0.0	567	567	0	0.0	954	954	0	0.0
	भा.ए.कं.लि. BALCO	13	13	0.0	406	406	0	0.0	562	562	0	0.0
	रि.इं.लि. जामनगर RIL JAMNAGAR	6	6	0.0	174	174	0	0.0	257	257	0	0.0
	कुल TOTAL	1346	1346	0.0	41723	41723	0	0.0	68618	68498	-120	-0.2
द०क्षे० SR	आंध्र प्रदेश Andhra Pradesh	198	198	0.0	6129	6129	0	0.0	10851	10851	0	0.0
	तेलंगाना Telangana	215	215	0.0	6660	6660	0	0.0	12998	12998	0	0.0
	कर्नाटक Karnataka	223	223	-0.1	6910	6908	-2	0.0	14508	14508	0	0.0
	केरल Kerala	84	84	0.0	2617	2617	0	0.0	4596	4596	0	0.0
	तमिलनाडु Tamil Nadu	325	325	0.0	10087	10087	0	0.0	17887	17887	0	0.0
	पुदुच्चेरी Puducherry	9	9	0.0	286	286	0	0.0	477	477	0	0.0
	कुल TOTAL	1054	1054	-0.1	32689	32687	-2	0.0	55483	55483	0	0.0
पू०क्षे० ER	बिहार Bihar	128	128	0.0	3954	3954	0	0.0	7676	7676	0	0.0
	झारखंड Jharkhand	42	42	-0.1	1302	1300	-2	-0.2	2262	2262	0	0.0
	दा.घा.नि. DVC	66	66	0.0	2035	2035	0	0.0	3246	3246	0	0.0
	ओडिशा Odisha	121	121	0.0	3753	3753	0	0.0	6313	6313	0	0.0
	पश्चिम बंगाल West Bengal	203	203	0.0	6306	6306	0	0.0	10306	10306	0	0.0
	सिक्किम Sikkim	1	1	0.0	34	34	0	0.0	91	91	0	0.0
	रेलवे_पू.क्षे.अ.रा.प्र.प्र. Railways_ER ISTS	0	0	0.0	4	4	0	0.0	26	26	0	0.0
	कुल TOTAL	561	561	-0.1	17389	17387	-2	0.0	28231	28231	0	0.0
उ०पू०क्षे० NER	अरुणाचल प्रदेश Arunachal Pradesh	3	3	0.0	96	96	0	0.0	200	200	0	0.0
	असम Assam	41	41	0.0	1262	1262	0	0.0	2412	2412	0	0.0
	मणिपुर Manipur	3	3	0.0	96	96	0	0.0	235	235	0	0.0
	मेघालय Meghalaya	6	6	0.0	173	173	0	0.0	343	343	0	0.0
	मिजोरम Mizoram	2	2	0.0	63	63	0	0.0	141	141	0	0.0
	नागालैंड Nagaland	3	3	0.0	90	90	0	0.0	188	188	0	0.0
	त्रिपुरा Tripura	6	6	0.0	187	187	0	0.0	347	347	0	0.0
	कुल TOTAL	63	63	0.0	1967	1967	0	0.0	3746	3746	0	0.0
अखिल भारतीय ALL INDIA		4264	4263	-0.3	132169	132159	-10	0.0				

नोट: इकाइयों द्वारा प्रस्तुत किए गए आँकड़ों पर आधारित
NOTE: BASED ON THE DATA FURNISHED BY ENTITIES

12. अक्तूबर 2025 और अक्तूबर 2024 की ऊर्जा तुलना

12. ENERGY COMPARISON OF OCTOBER 2025 vs OCTOBER 2024

क्षेत्र REGION	राज्य STATE	ऊर्जा आवश्यकता (मि.यू.) Energy Requirement (MU)					ऊर्जा आपूर्ति (मि.यू.) Energy Met (MU)				
		अक्तूबर-24 October-24	अक्तूबर-25 October-25	अंतर Difference	%परिवर्तन % Change	दैनिक औसत मि.यू.-अक्तूबर-25 Average MU/day for October-25	अक्तूबर-24 October-24	अक्तूबर-25 October-25	अंतर Difference	%परिवर्तन % Change	दैनिक औसत मि.यू.-अक्तूबर-25 Average MU/day for October-25
उ०क्षे० NR	चंडीगढ़ Chandigarh	145	132	-14	-9	4	145	132	-14	-9	4
	दिल्ली Delhi	3250	2849	-401	-12	92	3250	2849	-401	-12	92
	हरियाणा Haryana	6162	5459	-703	-11	176	6162	5459	-703	-11	176
	हिमाचल प्रदेश Himachal Pradesh	1067	981	-86	-8	32	1067	981	-86	-8	32
	जम्मू और कश्मीर एवं लद्दाख J&K(UT) and Ladakh(UT)	1558	1586	28	2	51	1546	1586	39	3	51
	पंजाब Punjab	6338	5442	-896	-14	176	6338	5442	-896	-14	176
	राजस्थान Rajasthan	9845	8024	-1821	-18	259	9845	8024	-1821	-18	259
	उत्तर प्रदेश Uttar Pradesh	14230	12552	-1678	-12	405	14229	12546	-1683	-12	405
	उत्तराखंड Uttarakhand	1370	1240	-130	-9	40	1369	1239	-130	-10	40
	रेलवे_उ.क्षे.अ.रा.प्र.प्र./एन.एफ.एल. Railway_NR ISTS/NFL	135	139	4	3	4	135	139	4	3	4
	कुल TOTAL	44099	38402	-5697	-13	1239	44086	38396	-5690	-13	1239
प०क्षे० WR	गुजरात Gujarat	13185	12270	-915	-7	396	13185	12270	-915	-7	396
	मध्य प्रदेश Madhya Pradesh	8024	7466	-559	-7	241	8024	7466	-559	-7	241
	छत्तीसगढ़ Chhattisgarh	3853	3280	-573	-15	106	3852	3280	-572	-15	106
	महाराष्ट्र Maharashtra	16873	16206	-666	-4	523	16871	16206	-665	-4	523
	गोवा Goa	455	450	-5	-1	15	455	450	-5	-1	15
	दादरा और नगर हवेली एवं दमन और दीव DNHDDPDCL	938	903	-35	-4	29	938	903	-35	-4	29
	आ.मि.नि.स्.इं.लि. AMNSIL	575	567	-7	-1	18	575	567	-7	-1	18
	भा.ए.कं.लि. BALCO	392	406	15	4	13	392	406	15	4	13
	रि.इं.लि. जामनगर RIL JAMNAGAR	-	174	-	-	-	-	174	-	-	-
	कुल TOTAL	44294	41723	-2572	-6	1346	44292	41723	-2569	-6	1346
द०क्षे० SR	आंध्र प्रदेश Andhra Pradesh	6399	6129	-270	-4	198	6382	6129	-253	-4	198
	तेलंगाना Telangana	7270	6660	-610	-8	215	7250	6660	-591	-8	215
	कर्नाटक Karnataka	6408	6910	502	8	223	6386	6908	522	8	223
	केरल Kerala	2567	2617	50	2	84	2560	2617	57	2	84
	तमिलनाडु Tamil Nadu	10267	10087	-181	-2	325	10241	10087	-154	-2	325
	पुदुच्चेरी Puducherry	301	286	-14	-5	9	300	286	-13	-4	9
	कुल TOTAL	33212	32689	-523	-2	1054	33119	32687	-432	-1	1054
पू०क्षे० ER	बिहार Bihar	4047	3954	-93	-2	128	4044	3954	-90	-2	128
	झारखंड Jharkhand	1305	1302	-3	0	42	1304	1300	-4	0	42
	दा.घा.नि. DVC	2181	2035	-145	-7	66	2181	2035	-145	-7	66
	ओडिशा Odisha	3916	3753	-163	-4	121	3916	3753	-163	-4	121
	पश्चिम बंगाल West Bengal	5967	6306	339	6	203	5967	6306	339	6	203
	सिक्किम Sikkim	39	34	-5	-12	1	39	34	-5	-12	1
	रेलवे_पू.क्षे.अ.रा.प्र.प्र. Railways_ER ISTS	5	4	-1	-15	0	5	4	-1	-15	0
	कुल TOTAL	17459	17389	-70	0	561	17456	17387	-69	0	561
उ०पू०क्षे० NER	अरुणाचल प्रदेश Arunachal Pradesh	86	96	10	12	3	86	96	10	12	3
	असम Assam	1072	1262	191	18	41	1072	1262	191	18	41
	मणिपुर Manipur	81	96	15	19	3	81	96	15	19	3
	मेघालय Meghalaya	155	173	18	11	6	155	173	18	11	6
	मिजोरम Mizoram	57	63	6	11	2	57	63	6	11	2
	नागालैंड Nagaland	77	90	13	17	3	77	90	13	17	3
	त्रिपुरा Tripura	171	187	16	9	6	171	187	16	9	6
	कुल TOTAL	1698	1967	269	16	63	1698	1967	269	16	63
अखिल भारतीय ALL INDIA		140761	132169	-8592	-6	4264	140650	132159	-8491	-6	4263

13. अक्तूबर 2025 और अक्तूबर 2024 की अधिकतम मांग की तुलना

13. PEAK DEMAND COMPARISON OF OCTOBER 2025 vs OCTOBER 2024

क्षेत्र REGION	राज्य STATE	अधिकतम मांग (मेगावाट) Peak Demand (MW)				अधिकतम मांग आपूर्ति (मेगावाट) Peak Demand Met (MW)			
		अक्तूबर-24 October-24	अक्तूबर-25 October-25	अंतर Difference	%परिवर्तन % Change	अक्तूबर-24 October-24	अक्तूबर-25 October-25	अंतर Difference	%परिवर्तन % Change
उ०क्षे० NR	चंडीगढ़ Chandigarh	298	323	25	8.4	298	323	25	8.4
	दिल्ली Delhi	6161	5956	-205	-3.3	6161	5956	-205	-3.3
	हरियाणा Haryana	11087	11372	285	2.6	11087	11372	285	2.6
	हिमाचल प्रदेश Himachal Pradesh	1947	2003	56	2.9	1947	2003	56	2.9
	जम्मू और कश्मीर एवं लद्दाख J&K(UT) and Ladakh(UT)	3068	2723	-345	-11.2	2742	2723	-19	-0.7
	पंजाब Punjab	14311	12989	-1322	-9.2	14311	12989	-1322	-9.2
	राजस्थान Rajasthan	16206	14165	-2041	-12.6	16206	14165	-2041	-12.6
	उत्तर प्रदेश Uttar Pradesh	26756	26269	-487	-1.8	26756	26269	-487	-1.8
	उत्तराखंड Uttarakhand	2412	2466	54	2.2	2412	2466	54	2.2
	रेलवे_उ.क्षे.अ.रा.प्र.प्र./एन.एफ.एल. Railway_NR ISTS/NFL	243	243	0	0.1	243	243	0	0.1
प०क्षे० WR	गुजरात Gujarat	22092	21822	-270	-1	22092	21822	-270	-1.2
	मध्य प्रदेश Madhya Pradesh	13603	13518	-85	-1	13563	13518	-45	-0.3
	छत्तीसगढ़ Chhattisgarh	5916	5288	-628	-11	5916	5279	-637	-10.8
	महाराष्ट्र Maharashtra	26632	27286	654	2	26613	27286	673	2.5
	गोवा Goa	741	750	9	1	741	750	9	1.2
	दादरा और नगर हवेली एवं दमन और दीव DNHDDPDCL	1390	1394	4	0.3	1390	1394	4	0.3
	आ.मि.नि.स्.इं.लि. AMNSIL	907	954	47	5.2	907	954	47	5.2
	भा.ए.कं.लि. BALCO	534	562	28	5.2	534	562	28	5.2
	रि.इं.लि. जामनगर RIL JAMNAGAR	-	257	-	-	-	257	-	-
द०क्षे० SR	आंध्र प्रदेश Andhra Pradesh	11545	10851	-694	-6.0	11545	10851	-694	-6.0
	तेलंगाना Telangana	14003	12998	-1005	-7.2	14003	12998	-1005	-7.2
	कर्नाटक Karnataka	12850	14508	1658	12.9	12850	14508	1658	12.9
	केरल Kerala	4455	4596	141	3.2	4455	4596	141	3.2
	तमिलनाडु Tamil Nadu	18113	17887	-226	-1.2	18113	17887	-226	-1.2
	पुदुच्चेरी Puducherry	517	477	-40	-7.8	517	477	-40	-7.7
पू०क्षे० ER	बिहार Bihar	7204	7676	472	6.6	7204	7676	472	6.6
	झारखंड Jharkhand	2229	2262	33	1.5	2229	2262	33	1.5
	दा.घा.नि. DVC	3453	3246	-207	-6.0	3453	3246	-207	-6.0
	ओडिशा Odisha	6388	6313	-75	-1.2	6388	6313	-75	-1.2
	पश्चिम बंगाल West Bengal	11227	10306	-921	-8.2	11227	10306	-921	-8.2
	सिक्किम Sikkim	99	91	-8	-8.1	99	91	-8	-8.1
	रेलवे_पू.क्षे.अ.रा.प्र.प्र. Railways_ER ISTS	25	26	1	4.0	25	26	1	4.0
उ०पू०क्षे० NER	अरुणाचल प्रदेश Arunachal Pradesh	170	200	30	17.6	170	200	30	17.6
	असम Assam	2262	2412	150	6.6	2262	2412	150	6.6
	मणिपुर Manipur	226	235	9	4.0	226	235	9	4.0
	मेघालय Meghalaya	354	343	-11	-3.1	354	343	-11	-3.1
	मिजोरम Mizoram	136	141	5	3.7	136	141	5	3.7
	नागालैंड Nagaland	176	188	12	6.8	176	188	12	6.8
	त्रिपुरा Tripura	333	347	14	4.2	333	347	14	4.2

14. राज्यों/घटकों के शेड्यूल ड्रॉअल एवं ऐक्चुअल ड्रॉअल - अक्तूबर 2025

14. SCHEDULE DRAWAL & ACTUAL DRAWAL OF CONSTITUENTS - OCTOBER 2025

क्षेत्र REGION	राज्य STATE	शेड्यूल ड्रॉअल (मि.यू.) Schedule Drawal (MU)	ऐक्चुअल ड्रॉअल (मि.यू.) Actual Drawal (MU)	ओवरड्रॉअल(+)/ अंडरड्रॉअल(-) (मि०यू०) Over drawal(+)/ Under Drawal(-) (MU)	% ओ. ड्रॉ. / अं. ड्रॉ. % OD / UD	शेड्यूल ड्रॉअल (मि.यू./दिन) Schedule Drawal (MU/DAY)	ऐक्चुअल ड्रॉअल (मि.यू./दिन) Actual Drawal (MU/DAY)	ओवरड्रॉअल(+)/ अंडरड्रॉअल(-) (मि.यू./दिन) Over drawal(+)/ Under Drawal(-) (MU/DAY)
उ०क्षे० NR	चंडीगढ़ Chandigarh	129.67	131.61	1.94	1.50	4.18	4.25	0.06
	दिल्ली Delhi	2761.30	2756.55	-4.75	-0.17	89.07	88.92	-0.15
	हरियाणा Haryana	4480.33	4443.39	-36.94	-0.82	144.53	143.34	-1.19
	हिमाचल प्रदेश Himachal Pradesh	311.05	288.56	-22.49	-7.23	10.03	9.31	-0.73
	जम्मू और कश्मीर एवं लद्दाख J&K(UT) and Ladakh(UT)	1187.95	1190.03	2.08	0.18	38.32	38.39	0.07
	पंजाब Punjab	2729.83	2704.72	-25.11	-0.92	88.06	87.25	-0.81
	राजस्थान Rajasthan	2510.00	2387.83	-122.17	-4.87	80.97	77.03	-3.94
	उत्तर प्रदेश Uttar Pradesh	4497.08	4448.74	-48.34	-1.07	145.07	143.51	-1.56
	उत्तराखंड Uttarakhand	733.95	740.95	7.00	0.95	23.68	23.90	0.23
	रेलवे_उ.क्षे.अ.रा.प्र.प्र. Railway_NR ISTS	121.87	137.00	15.13	12.42	3.93	4.42	0.49
	एन.एफ.एल. NFL	1.60	2.17	0.57	35.63	0.05	0.07	0.02
	कुल TOTAL	19464.63	19231.55	-233.08	-1.20	627.89	620.37	-7.52
प०क्षे० WR	गुजरात Gujarat	6235.45	6119.24	-116.21	-1.86	201.14	197.39	-3.75
	मध्य प्रदेश Madhya Pradesh	4261.68	4261.28	-0.40	-0.01	137.47	137.46	-0.01
	छत्तीसगढ़ Chhattisgarh	1673.92	1661.37	-12.55	-0.75	54.00	53.59	-0.40
	महाराष्ट्र Maharashtra	5849.38	5779.76	-69.62	-1.19	188.69	186.44	-2.25
	गोवा Goa	378.76	375.74	-3.02	-0.80	12.22	12.12	-0.10
	दादरा और नगर हवेली एवं दमन और दीव DNHDDPDCL	900.36	902.61	2.25	0.25	29.04	29.12	0.07
	आ.मि.नि.स.इं.लि. AMNSIL	352.61	361.66	9.05	2.57	11.37	11.67	0.29
	भा.ए.कं.लि. BALCO	407.94	406.26	-1.68	-0.41	13.16	13.11	-0.05
	रि.इं.लि. जामनगर RIL JAMNAGAR	177.26	174.13	-3.13	-1.77	5.72	5.62	-0.10
	कुल TOTAL	20237.36	20042.04	-195.32	-0.97	652.82	646.52	-6.30
द०क्षे० SR	आंध्र प्रदेश Andhra Pradesh	1723.66	1700.34	-23.32	-1.35	55.60	54.85	-0.75
	तेलंगाना Telangana	2711.09	2711.81	0.72	0.03	87.45	87.48	0.02
	कर्नाटक Karnataka	1824.47	1799.50	-24.97	-1.37	58.85	58.05	-0.81
	केरल Kerala	1599.91	1590.92	-8.99	-0.56	51.61	51.32	-0.29
	तमिलनाडु Tamil Nadu	5442.06	5361.28	-80.78	-1.48	175.55	172.94	-2.61
	पुदुच्चेरी Puducherry	272.08	266.49	-5.59	-2.05	8.78	8.60	-0.18
	Goa (SR)	58.85	60.02	1.17	1.99	1.90	1.94	0.04
	कुल TOTAL	13632.12	13490.36	-141.76	-1.04	439.75	435.17	-4.57
पू०क्षे० ER	बिहार Bihar	3545.99	3522.25	-23.74	-0.67	114.39	113.62	-0.77
	झारखंड Jharkhand	952.22	935.99	-16.24	-1.71	30.72	30.19	-0.52
	दा.घा.नि. DVC	-937.00	-934.79	2.21	-0.24	-30.23	-30.15	0.07
	ओडिशा Odisha	1146.16	1093.43	-52.72	-4.60	36.97	35.27	-1.70
	पश्चिम बंगाल West Bengal	2129.93	2052.85	-77.08	-3.62	68.71	66.22	-2.49
	सिक्किम Sikkim	36.62	34.49	-2.13	-5.82	1.18	1.11	-0.07
	रेलवे_पू.क्षे.अ.रा.प.प्र. Railways_ER ISTS	3.92	3.91	-0.01	-0.34	0.13	0.13	0.00
	कुल TOTAL	6877.84	6708.13	-169.71	-2.47	221.87	216.39	-5.47
उ०पू०क्षे० NER	अरुणाचल प्रदेश Arunachal Pradesh	93.28	85.86	-7.42	-7.95	3.01	2.77	-0.24
	असम Assam	1016.89	1030.61	13.72	1.35	32.80	33.25	0.44
	मणिपुर Manipur	95.81	96.05	0.24	0.25	3.09	3.10	0.01
	मेघालय Meghalaya	73.04	68.81	-4.23	-5.79	2.36	2.22	-0.14
	मिजोरम Mizoram	25.00	18.18	-6.82	-27.28	0.81	0.59	-0.22
	नागालैंड Nagaland	81.58	78.94	-2.64	-3.24	2.63	2.55	-0.09
	त्रिपुरा Tripura	180.03	184.05	4.02	2.23	5.81	5.94	0.13
	कुल TOTAL	1565.63	1562.50	-3.13	-0.20	50.50	50.40	-0.10
अखिल भारतीय ALL INDIA		61777.58	61034.58	-742.99	-1.20	1992.83	1968.86	-23.97

15. INTER REGIONAL EXCHANGES 2025-26

(All figures in MU)

	Apr'25	May'25	June'25	July'25	Aug'25	Sep'25	Oct'25	Fin. Year 2025-26
Name of Line								
Import of NR from WR (WR-NR)								
WR - NR HVDC Champa- Kurukshetra	1382.87	2023.40	2254.66	2061.89	1829.09	2053.57	1244.76	**12850.24**
WR - NR HVDC Vindhyachal	16.65	119.23	79.22	18.92	164.94	92.04	40.67	**531.67**
WR - NR HVDC Mundra - M'garh	896.71	1001.79	1174.93	1092.67	831.89	805.61	554.73	**6358.33**
WR - NR 765 kV Gwalior - Agra 2xS/C	375.96	961.14	1365.69	1177.97	940.04	887.52	691.87	**6400.19**
WR - NR 765 kV Gwalior-Phagi 2xS/C	119.97	290.73	572.46	579.83	608.04	473.33	622.60	**3266.96**
WR - NR 765 kV Jabalpur- Orai D/C	317.58	813.58	1229.16	1149.27	1049.23	912.28	782.75	**6253.85**
WR - NR 765 kV Satna- Orai	506.38	537.61	607.95	563.33	531.25	477.32	497.14	**3720.98**
WR - NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
WR - NR 765 kV Banaskata - Chittorgarh D/C	17.73	226.09	478.26	143.44	77.35	14.43	8.75	**966.05**
WR - NR 765 kV Vindhyachal - Varanasi	1245.55	1708.13	1914.58	1711.26	1541.75	1624.58	980.42	**10726.27**
WR - NR 765 kV Neemach - Chittorgarh D/C	0.00	36.24	165.77	169.30	173.42	143.45	41.50	**729.68**
WR - NR 400 kV Zerda- Kankroli	0.50	20.28	53.83	17.88	14.03	0.00	0.00	**106.52**
WR - NR 400 kV Zerda- Bhinmal	0.00	70.94	17.08	0.00	0.00	0.00	0.00	**88.02**
WR - NR 400 kV Shujalpur - RAPP C D/C	0.00	32.33	133.09	110.88	82.50	70.69	17.81	**447.30**
WR - NR 400 KV Vindhyachal - Rihand D/C	0.00	0.00	0.00	0.65	0.00	0.00	0.00	**0.65**
WR - NR 220 kV Bhanpura - Ranpur	62.23	62.87	60.21	66.31	71.88	65.21	51.26	**439.97**
WR - NR 220 kV Bhanpura - Modak	70.83	86.49	84.28	81.56	84.82	84.32	53.37	**545.67**
WR - NR 220 kV Malanpur / Mehgaon - Auraiya	0.00	1.18	4.39	5.14	0.07	2.71	2.54	**16.03**
Total WR - NR	**5012.96**	**7992.03**	**10195.56**	**8950.30**	**8000.30**	**7707.06**	**5590.17**	**53448.38**

	Apr'25	May'25	June'25	July'25	Aug'25	Sep'25	Oct'25	Fin. Year 2025-26
Name of Line								
Export of NR to WR (NR-WR)								
NR - WR HVDC Kurukshetra - Champa	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR HVDC Vindhyachal	43.26	29.26	39.61	74.13	2.31	59.21	78.10	**325.88**
NR - WR HVDC M'garh - Mundra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Agra - Gwalior 2xS/C	6.16	0.00	0.00	0.00	0.00	0.00	0.00	**6.16**
NR - WR 765 kV Phagi - Gwalior 2xS/C	11.05	2.35	1.79	0.00	0.00	5.52	0.00	**20.71**
NR - WR 765 kV Orai - Jabalpur D/C	8.98	0.00	0.00	0.00	0.00	0.00	0.00	**8.98**
NR - WR 765 kV Orai - Satna	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Orai - Gwalior	345.16	292.43	286.32	309.34	374.51	363.92	399.65	**2371.33**
NR - WR 765 kV Chittorgarh - Banaskata D/C	330.62	27.29	9.25	136.12	298.85	364.43	658.78	**1825.34**
NR - WR 765 kV Varanasi - Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 765 kV Chittorgarh - Neemach D/C	192.85	53.22	5.93	1.84	3.89	11.32	21.60	**290.65**
NR - WR 400 kV Kankroli - Zerda	180.27	34.58	15.88	63.75	123.14	177.30	278.83	**873.75**
NR - WR 400 kV Bhinmal - Zerda	0.00	1.60	16.53	0.00	0.00	6.79	0.00	**24.92**
NR - WR 400 kV RAPP C - Shujalpur D/C	179.68	68.92	11.81	5.23	23.87	87.68	51.12	**428.31**
NR - WR 400 KV Rihand - Vindhyachal D/C	627.94	529.60	0.00	0.00	0.00	0.00	0.00	**1157.54**
NR - WR 220 kV Ranpur - Bhanpura	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Modak - Bhanpura	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	66.11	28.64	11.28	14.79	26.16	31.53	32.23	**210.74**
Total NR - WR	**1992.08**	**1067.89**	**398.40**	**605.20**	**852.73**	**1107.70**	**1520.31**	**7544.31**

	Apr'25	May'25	June'25	July'25	Aug'25	Sep'25	Oct'25	Fin. Year 2025-26
Name of Line								
Import of NR from ER (ER-NR)								
ER - NR HVDC Alipurduar - Agra	0.43	0.00	207.46	294.66	391.71	270.52	176.94	**1341.72**
ER - NR 765 kV Sasaram - Fatehpur	77.99	33.39	58.92	63.66	96.60	57.23	136.90	**524.69**
ER - NR 765 kV Gaya - Varanasi 2*S/C	65.04	56.80	78.50	137.65	170.12	116.54	244.29	**868.94**
ER - NR 765 kV Gaya - Balia	186.58	263.25	335.15	365.65	353.77	349.57	281.72	**2135.69**
ER - NR 400 kV Patna - Balia D/C	193.76	203.41	224.63	246.91	311.71	380.81	250.46	**1811.69**
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	11.63	113.13	212.77	291.02	309.09	325.30	327.03	**1589.97**
ER - NR 400 kV Biharshariff - Balia D/C	0.00	12.52	32.71	23.23	43.79	50.49	33.03	**195.77**
ER - NR 400 kV Motihari - Gorakhpur D/C	62.83	123.33	143.14	160.46	172.75	187.28	204.79	**1054.58**
ER - NR 400 kV Biharshariff - Varanasi D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
ER - NR 400 kV Sasaram - Varanasi	60.82	64.18	68.81	62.53	52.97	56.91	51.58	**417.80**
ER - NR 400 kV Sasaram - Allahabad	10.62	8.32	10.59	18.44	18.83	15.41	20.03	**102.24**
ER - NR 400 kV Naubatpur - Balia D/C	45.33	47.32	50.15	56.33	78.05	99.48	64.57	**441.23**
ER - NR 400 kV Biharshriff - Sahupuri D/C	25.32	33.43	58.54	83.15	80.91	63.23	77.20	**421.78**
ER - NR 220 kV Sahupuri - Karamnasa	5.66	46.35	66.77	50.47	32.36	40.97	42.29	**284.87**
ER - NR 132 kV Sahupuri - Karamnasa	0.96	0.48	0.96	1.28	2.50	0.00	0.48	**6.66**
ER - NR 132 kV Nagar Untari - Rihand	0.05	0.00	0.12	0.00	0.00	0.11	0.25	**0.53**
ER - NR 132 kV Garhwa - Rihand	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
Total ER-NR	**747.02**	**1005.91**	**1549.22**	**1855.44**	**2115.16**	**2013.85**	**1911.56**	**11198.16**
Import of NR from NER (NER-NR)								
NER - NR HVDC Biswanath Chariali - Agra	0.00	22.96	306.84	257.24	242.18	297.13	355.81	**1482.16**
Total NER - NR	**0.00**	**22.96**	**306.84**	**257.24**	**242.18**	**297.13**	**355.81**	**1482.16**

	Apr'25	May'25	June'25	July'25	Aug'25	Sep'25	Oct'25	Fin. Year 2025-26
Name of Line								
Export of NR to ER (NR-ER)								
NR - ER HVDC Agra - Alipurduar	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 765 kV Fatehpur - Sasaram	6.26	34.48	24.77	11.38	10.78	36.92	2.17	**126.76**
NR - ER 765 kV Varanasi - Gaya 2*S/C	56.47	106.17	77.38	18.92	21.86	76.19	0.24	**357.23**
NR - ER 765 kV Balia - Gaya	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Balia - Patna D/C	1.06	0.00	0.89	0.00	0.00	0.00	0.00	**1.95**
NR - ER 400 kV Gorakhpur - Muzaffarpur D/C	99.75	29.83	3.10	0.00	0.00	0.00	0.00	**132.68**
NR - ER 400 kV Balia - Biharshariff D/C	162.65	104.51	75.25	33.58	4.97	14.20	59.59	**454.75**
NR - ER 400 kV Gorakhpur - Motihari D/C	4.85	0.05	1.51	0.00	0.21	0.00	0.00	**6.62**
NR - ER 400 kV Varanasi - Biharshariff D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Varanasi - Sasaram	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
NR - ER 400 kV Allahabad - Sasaram	2.99	6.52	11.90	1.71	1.64	4.73	0.38	**29.87**
NR - ER 400 kV Balia - Naubatpur D/C	1.90	4.36	6.54	0.19	0.00	0.00	2.68	**15.67**
NR - ER 400 kV Sahupuri - Biharshriff D/C	25.78	30.77	8.13	1.25	3.79	26.15	1.76	**97.63**
NR - ER 220 kV Karamnasa - Sahupuri	7.75	1.36	0.00	0.00	0.00	0.00	0.00	**9.11**
NR - ER 132 kV Karamnasa - Sahupuri	0.20	0.39	0.00	0.00	0.00	0.00	0.00	**0.59**
NR - ER 132 kV Rihand - Nagar Untari	0.98	0.10	0.46	0.44	0.87	0.75	0.10	**3.70**
NR - ER 132 kV Rihand - Garhwa	14.20	15.51	17.81	17.36	18.67	16.94	17.66	**118.15**
Total NR - ER	**384.84**	**334.05**	**227.74**	**84.83**	**62.79**	**175.88**	**84.58**	**1354.71**
Export of NR to NER (NER-NR)								
NR - NER HVDC Agra - Biswanath Chariali	587.35	339.01	0.00	0.00	0.00	0.00	0.00	**926.36**
Total NR - NER	**587.35**	**339.01**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**926.36**

	Apr'25	May'25	June'25	July'25	Aug'25	Sep'25	Oct'25	Fin. Year 2025-26
Name of Line								
Export of WR to ER (WR-ER)								
WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	361.32	847.34	1120.57	894.90	833.15	838.94	440.49	**5336.71**
WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	302.38	152.33	213.61	378.95	368.81	318.40	170.38	**1904.86**
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	8.48	22.27	14.44	17.80	20.78	3.54	**87.31**
WR - ER 400 kV Sipat - Ranchi D/C	44.41	165.08	241.40	199.46	143.96	169.04	83.22	**1046.57**
WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	0.04	36.04	100.65	98.86	81.72	82.40	65.37	**465.07**
WR - ER 400 kV Jeypore - Jagdalpur D/C			28.61	18.98	89.69	104.51	36.80	**278.60**
WR - ER 220 kV Korba - Budhipadar D/C	12.35	33.58	45.82	18.61	8.06	25.44	29.96	**173.82**
WR - ER 220 kV Raigarh - Budhipadar	0.10	11.59	9.61	10.21	1.74	3.37	4.57	**41.20**
Total WR - ER	**720.61**	**1254.44**	**1782.54**	**1634.41**	**1544.93**	**1562.87**	**834.34**	**9334.13**
Import of WR from ER (ER - WR)								
ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	79.61	7.39	0.39	14.42	18.50	11.03	38.43	**169.76**
ER - WR 765 kV Dharamjaygarh - Jharsuguda D/C	160.09	253.52	323.63	135.13	105.77	155.76	198.84	**1332.74**
ER - WR 765 kV Durg - Jharsuguda D/C	503.09	232.42	113.50	100.38	193.02	126.25	287.38	**1556.03**
ER - WR 400 kV Sipat - Ranchi D/C	55.76	5.53	1.02	6.80	14.63	7.55	19.16	**110.45**
ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	325.72	102.70	16.71	33.89	72.87	51.48	93.18	**696.55**
ER - WR 400 kV Jeypore - Jagdalpur D/C			53.82	147.11	92.47	72.65	76.88	**442.93**
ER - WR 220 kV Korba - Budhipadar D/C	25.22	2.91	1.56	17.04	41.57	9.36	14.27	**111.94**
ER - WR 220 kV Raigarh - Budhipadar	50.11	13.49	7.03	13.79	49.50	27.15	39.41	**200.47**
Total ER - WR	**1199.60**	**617.96**	**517.65**	**468.56**	**588.32**	**461.23**	**767.55**	**4620.87**
Export of ER to NER (ER - NER)								
ER - NER 400 kV Binaguri - Bongaigaon D/C	23.81	14.14	102.25	105.97	56.38	78.60	144.63	**525.76**
ER - NER 400 kV Alipurduar - Bongaigaon D/C	28.02	45.27	273.90	304.64	183.77	258.09	300.88	**1394.58**
ER - NER 220 kV Birpara - Salakati D/C	3.15	4.51	41.91	53.28	41.36	49.41	52.02	**245.65**
Total ER - NER	**54.98**	**63.92**	**418.06**	**463.89**	**281.52**	**386.09**	**497.53**	**2165.99**
Import of ER from NER (NER - ER)								
NER - ER 400 kV Binaguri - Bongaigaon D/C	86.91	101.88	20.90	9.45	23.01	19.23	13.87	**275.26**
NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	133.68	82.82	6.53	0.61	5.90	3.97	0.36	**233.86**
NER - ER 220 kV Birpara - Salakati D/C	30.05	24.26	2.60	0.29	1.15	0.91	0.25	**59.51**
Total NER - ER	**250.64**	**208.96**	**30.02**	**10.35**	**30.06**	**24.10**	**14.49**	**568.63**

	Apr'25	May'25	June'25	July'25	Aug'25	Sep'25	Oct'25	Fin. Year 2025-26
Name of Line								
Export of ER to SR (ER - SR)								
ER - SR HVDC Gazuwaka	64.45	47.26	1.00	31.46	173.49	232.48	210.73	**760.88**
ER - SR HVDC Talchar -Kolar	1338.63	1181.86	1012.66	904.97	1101.75	886.78	1133.78	**7560.42**
ER - SR 765 kV Angul- Srikakulam D/C	1591.65	1274.48	977.07	1020.33	924.64	881.85	1361.95	**8031.99**
Total ER - SR	**2994.74**	**2503.60**	**1990.73**	**1956.76**	**2199.88**	**2001.12**	**2706.46**	**16353.29**
Import of ER from SR (SR - ER)								
SR - ER HVDC Gazuwaka	44.04	138.20	218.83	234.55	142.35	128.35	35.50	**941.83**
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	1.05	0.00	1.45	0.87	0.00	**3.37**
Total SR - ER	**44.04**	**138.20**	**219.88**	**234.55**	**143.80**	**129.21**	**35.50**	**945.19**
Export of WR to SR (WR-SR)								
WR - SR HVDC Bhadrawati	644.61	220.50	0.00	51.48	146.62	112.09	244.35	**1419.64**
WR - SR 765 kV Sholapur - Raichur 2xS/C	206.88	115.39	44.74	31.44	63.88	40.95	87.78	**591.07**
WR - SR 765 kV Wardha - Nizamabad D/C	983.94	603.84	465.00	551.34	510.01	483.80	736.29	**4334.21**
WR - SR 400KV Kolhapur-Kudgi D/C	0.02	0.00	0.00	0.00	0.00	0.13	0.00	**0.15**
WR - SR HVDC Raigarh-Pugalur	2564.04	1621.30	873.08	571.53	630.46	794.65	1313.84	**8368.90**
WR - SR 220kV Xeldem - Ambewadi S/C	71.04	74.18	57.52	61.31	63.95	55.66	59.02	**442.68**
WR - SR 220kV Ponda - Ambewadi S/C	0.79	0.09	0.08	0.10	0.09	0.04	0.07	**1.27**
WR - SR 765 kV Warora - Warangal D/C	1140.34	750.16	469.61	486.50	442.05	401.88	657.65	**4348.20**
Total WR - SR	**5611.68**	**3385.46**	**1910.04**	**1753.70**	**1857.05**	**1889.20**	**3099.00**	**19506.12**
Import of WR from SR (SR - WR)								
SR - WR HVDC Bhadrawati	0.00	206.01	506.97	447.98	236.20	269.21	92.02	**1758.39**
SR - WR 765 kV Raichur - Sholapur 2xS/C	134.40	376.02	834.64	997.37	844.87	702.51	332.79	**4222.60**
SR - WR 765 kV Wardha - Nizamabad D/C	0.24	25.72	110.14	75.83	147.29	103.32	6.45	**468.99**
SR - WR 400KV Kolhapur-Kudgi D/C	657.02	869.48	956.40	1149.16	979.17	980.65	963.55	**6555.43**
SR - WR HVDC Pugalur-Raigarh	0.00	0.00	11.69	219.49	374.18	274.39	64.99	**944.75**
SR - WR 220kV Xeldem - Ambewadi S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	**0.00**
SR - WR 220kV Ponda - Ambewadi S/C	0.01	0.01	0.01	0.00	0.01	0.01	0.01	**0.06**
SR - WR 765 kV Warangal - Warora D/C	0.02	17.52	122.79	74.60	133.02	52.49	4.99	**405.42**
Total SR - WR	**791.68**	**1494.76**	**2542.64**	**2964.44**	**2714.74**	**2382.58**	**1464.80**	**14355.64**
TOTAL ALL INDIA	**20392**	**20429**	**22089**	**21240**	**20633**	**20138**	**18882**	**143804**

***In case of mutiple ckt / DC pole year corres. to the commissioning of final element**

Date	15.1 Import-Export of NR with WR during October 2025																		
	Import of NR from WR (WR-NR)																		
	WR - NR HVDC Champa-Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR HVDC Mundra - M'garh	WR - NR 765 kV Gwalior - Agra 2xS/C	WR - NR 765 kV Gwalior-Phagi 2xS/C	WR - NR 765 kV Jabalpur-Orai D/C	WR - NR 765 kV Satna-Orai	WR - NR 765 kV Gwalior-Orai	WR - NR 765 kV Banaskata - Chittorgarh D/C	WR - NR 765 kV Vindhyachal - Varanasi	WR - NR 765 kV Neemach - Chittorgarh D/C	WR - NR 400 kV Zerda-Kankroli	WR - NR 400 kV Zerda-Bhinmal	WR - NR 400 kV Shujalpur - RAPP C D/C	WR - NR 400 KV Vindhyachal - Rihand D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Malanpur / Mehgaon - Auraiya	Total WR - NR
1-Oct-25	78.31	5.90	29.24	44.54	27.45	44.89	20.10	0.00	0.00	57.10	7.65	0.00		4.23		2.41	1.95	0.46	**324.23**
2-Oct-25	50.96	3.51	7.55	39.97	28.78	42.50	20.10	0.00	2.08	43.83	7.08	0.00		4.12		2.23	1.96	0.00	**254.67**
3-Oct-25	48.40	2.43	7.00	36.25	29.25	37.45	20.63	0.00	0.00	32.70	5.62	0.00		2.85		2.30	2.07	0.00	**226.95**
4-Oct-25	64.25	6.00	9.39	25.90	27.07	30.12	19.72	0.00	0.00	16.97	3.95	0.00		0.81		2.58	2.06	0.00	**208.82**
5-Oct-25	70.05	6.02	14.59	17.36	21.19	24.72	15.29	0.00	0.00	28.49	1.73	0.00		0.14		2.10	2.04	0.00	**203.72**
6-Oct-25	68.89	3.83	18.02	14.20	11.04	16.90	12.69	0.00	0.00	32.37	0.00	0.00		0.00		1.60	1.77	0.00	**181.31**
7-Oct-25	34.96	1.22	12.18	12.53	14.02	14.73	12.21	0.00	0.00	31.34	0.85	0.00		0.00		1.60	1.88	0.00	**137.52**
8-Oct-25	34.82	1.22	17.71	4.91	14.09	9.81	11.80	0.00	0.00	26.21	0.00	0.00		0.00		2.13	1.91	0.00	**124.61**
9-Oct-25	34.99	1.22	26.69	5.98	16.45	13.82	11.92	0.00	0.00	19.57	0.66	0.00		0.00		1.60	2.25	0.00	**135.15**
10-Oct-25	38.35	1.21	26.23	10.70	19.80	17.47	13.43	0.00	0.00	14.75	0.62	0.00		0.00		1.65	1.65	0.00	**145.86**
11-Oct-25	32.11	1.22	36.32	17.85	25.24	20.93	14.11	0.00	0.00	21.56	2.17	0.00		0.00		1.61	1.84	0.00	**174.96**
12-Oct-25	24.14	1.22	37.89	20.20	28.42	25.54	16.51	0.00	0.00	24.90	4.39	0.00		2.10		1.56	1.73	0.00	**188.60**
13-Oct-25	35.89	1.20	23.68	21.86	23.70	22.12	14.99	0.00	0.00	23.28	1.33	0.00		0.00		1.97	1.60	0.00	**171.62**
14-Oct-25	46.70	1.22	31.18	12.92	20.92	20.65	14.59	0.00	0.00	14.67	0.00	0.00		0.00		2.08	1.35	0.00	**166.28**
15-Oct-25	46.59	1.22	24.21	15.03	21.33	22.17	17.44	0.00	0.00	21.69	0.00	0.00		0.00		2.13	2.25	0.00	**174.06**
16-Oct-25	47.20	1.22	20.40	14.55	22.85	22.10	17.62	0.00	0.00	24.72	0.00	0.00		0.00		2.06	2.65	0.00	**175.37**
17-Oct-25	46.56	0.81	23.45	18.38	23.85	21.50	18.58	0.00	0.00	25.46	0.00	0.00		0.00		1.60	2.66	0.00	**182.85**
18-Oct-25	47.42	0.00	24.07	16.26	19.34	22.48	16.60	0.00	0.00	24.82	0.00	0.00		0.00		1.62	2.14	0.00	**174.75**
19-Oct-25	42.08	0.00	12.18	18.40	17.03	27.17	15.43	0.00	0.00	25.69	0.00	0.00		0.00		1.75	1.47	0.00	**161.20**
20-Oct-25	29.17	0.00	12.19	18.15	18.01	23.62	12.90	0.00	0.00	25.32	0.00	0.00		0.01		1.15	0.80	0.00	**141.32**
21-Oct-25	33.46	0.00	11.71	17.44	13.49	18.46	11.79	0.00	0.00	33.06	0.00	0.00		0.00		1.54	0.69	0.00	**141.64**
22-Oct-25	37.92	0.00	9.78	21.12	13.29	20.89	12.25	0.00	0.00	40.89	0.00	0.00		0.00		1.28	0.89	0.00	**158.31**
23-Oct-25	21.15	0.00	9.78	24.83	19.45	23.76	14.94	0.00	0.00	42.56	0.65	0.00		0.00		1.21	1.15	0.00	**159.48**
24-Oct-25	23.00	0.00	17.04	25.56	22.26	24.79	16.07	0.00	0.00	39.01	0.00	0.00		0.00		1.16	1.47	0.00	**170.36**
25-Oct-25	23.20	0.00	19.51	26.09	19.77	26.69	17.00	0.00	0.00	39.21	0.00	0.00		0.00		1.31	1.68	0.00	**174.46**
26-Oct-25	23.13	0.00	9.45	26.26	17.85	30.09	17.26	0.00	0.00	41.60	0.00	0.00		0.00		1.35	1.87	0.00	**168.86**
27-Oct-25	23.05	0.00	9.35	28.73	15.33	28.63	17.51	0.00	0.00	44.90	0.00	0.00		0.00		1.29	1.48	0.26	**170.53**
28-Oct-25	24.10	0.00	9.76	38.98	16.85	32.73	17.81	0.00	2.50	49.58	1.11	0.00		1.06		1.17	1.38	1.07	**198.10**
29-Oct-25	24.87	0.00	11.74	39.21	17.70	36.50	19.46	0.00	4.17	45.97	1.99	0.00		1.50		1.02	1.45	0.75	**206.33**
30-Oct-25	32.21	0.00	13.74	34.57	20.42	36.22	19.73	0.00	0.00	39.12	1.70	0.00		0.99		0.97	1.70	0.00	**201.37**
31-Oct-25	56.83	0.00	18.70	23.14	16.36	23.30	16.66	0.00	0.00	29.08	0.00	0.00		0.00		1.23	1.58	0.00	**186.88**
Total	**1244.76**	**40.67**	**554.73**	**691.87**	**622.60**	**782.75**	**497.14**	**0.00**	**8.75**	**980.42**	**41.50**	**0.00**	**0.00**	**17.81**	**0.00**	**51.26**	**53.37**	**2.54**	**5590.17**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

Date	15.1 Import-Export of NR with WR during October 2025																		
	Export of NR to WR (NR- WR)																		
	NR - WR HVDC Kurukshetra - Champa	NR - WR HVDC Vindhyachal	NR - WR HVDC M'garh - Mundra	NR - WR 765 kV Agra - Gwalior 2xS/C	NR - WR 765 kV Phagi - Gwalior 2xS/C	NR - WR 765 kV Orai - Jabalpur D/C	NR - WR 765 kV Orai - Satna	NR - WR 765 kV Orai - Gwalior	NR - WR 765 kV Chittorgarh - Banaskata D/C	NR - WR 765 kV Varanasi - Vindhyachal	NR - WR 765 kV Chittorgarh - Neemach D/C	NR - WR 400 kV Kankroli - Zerda	NR - WR 400 kV Bhinmal - Zerda	NR - WR 400 kV RAPP C - Shujalpur D/C	NR - WR 400 KV Rihand - Vindhyachal D/C	NR - WR 220 kV Ranpur - Bhanpura	NR - WR 220 kV Modak - Bhanpura	NR - WR 220 kV Auraiya - Malanpur/Mehgaon	Total NR - WR
1-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.98	1.53	0.00	0.00	2.86		0.00		0.00	0.00	0.00	**16.37**
2-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.51	0.00	0.00	0.00	0.76		0.00		0.00	0.00	0.24	**14.51**
3-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.25	4.27	0.00	0.00	2.75		0.00		0.00	0.00	0.94	**23.21**
4-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.60	16.02	0.00	0.00	7.56		0.00		0.00	0.00	1.58	**40.76**
5-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.70	17.49	0.00	0.00	8.24		0.00		0.00	0.00	1.49	**40.92**
6-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.23	10.32	0.00	1.25	7.60		3.00		0.00	0.00	1.29	**34.69**
7-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.42	24.43	0.00	0.00	9.99		2.87		0.00	0.00	1.35	**52.06**
8-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.86	37.94	0.00	0.30	14.08		4.20		0.00	0.00	2.03	**71.41**
9-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.28	43.09	0.00	0.00	15.43		3.34		0.00	0.00	1.95	**76.09**
10-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.49	42.10	0.00	0.00	14.40		2.40		0.00	0.00	1.90	**74.29**
11-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.53	44.00	0.00	0.00	14.20		0.39		0.00	0.00	1.55	**76.67**
12-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	18.88	34.40	0.00	0.00	11.89		0.00		0.00	0.00	1.26	**66.43**
13-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.46	33.79	0.00	0.00	12.50		0.65		0.00	0.00	1.63	**66.03**
14-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.63	36.42	0.00	1.33	13.54		3.11		0.00	0.00	1.78	**68.81**
15-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.21	36.31	0.00	2.05	13.61		3.40		0.00	0.00	1.63	**68.21**
16-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.65	36.40	0.00	2.02	13.65		3.85		0.00	0.00	1.65	**69.22**
17-Oct-25	0.00	0.81	0.00	0.00	0.00	0.00	0.00	11.82	34.65	0.00	2.10	13.70		3.89		0.00	0.00	1.25	**68.22**
18-Oct-25	0.00	2.48	0.00	0.00	0.00	0.00	0.00	11.51	35.57	0.00	2.36	13.45		4.12		0.00	0.00	1.28	**70.77**
19-Oct-25	0.00	2.43	0.00	0.00	0.00	0.00	0.00	12.03	26.01	0.00	1.17	11.04		2.89		0.00	0.00	1.07	**56.64**
20-Oct-25	0.00	10.51	0.00	0.00	0.00	0.00	0.00	13.63	28.54	0.00	0.35	11.56		2.73		0.00	0.00	1.15	**68.47**
21-Oct-25	0.00	12.18	0.00	0.00	0.00	0.00	0.00	12.97	21.30	0.00	1.26	9.43		2.51		0.00	0.00	0.85	**60.50**
22-Oct-25	0.00	5.89	0.00	0.00	0.00	0.00	0.00	13.84	8.41	0.00	0.39	4.95		1.20		0.00	0.00	0.88	**35.56**
23-Oct-25	0.00	4.86	0.00	0.00	0.00	0.00	0.00	14.93	10.29	0.00	0.00	5.18		0.28		0.00	0.00	0.61	**36.15**
24-Oct-25	0.00	4.87	0.00	0.00	0.00	0.00	0.00	15.76	14.42	0.00	0.81	5.77		0.72		0.00	0.00	0.89	**43.24**
25-Oct-25	0.00	4.86	0.00	0.00	0.00	0.00	0.00	13.14	7.92	0.00	1.97	6.22		1.45		0.00	0.00	0.64	**36.20**
26-Oct-25	0.00	4.86	0.00	0.00	0.00	0.00	0.00	11.03	11.06	0.00	1.41	7.55		0.94		0.00	0.00	0.41	**37.26**
27-Oct-25	0.00	4.85	0.00	0.00	0.00	0.00	0.00	9.02	7.00	0.00	1.57	6.04		0.98		0.00	0.00	0.00	**29.46**
28-Oct-25	0.00	4.85	0.00	0.00	0.00	0.00	0.00	9.68	0.00	0.00	0.00	3.69		0.00		0.00	0.00	0.00	**18.22**
29-Oct-25	0.00	4.87	0.00	0.00	0.00	0.00	0.00	8.17	0.00	0.00	0.00	2.17		0.00		0.00	0.00	0.00	**15.21**
30-Oct-25	0.00	4.86	0.00	0.00	0.00	0.00	0.00	9.89	18.78	0.00	0.00	8.02		0.00		0.00	0.00	0.43	**41.98**
31-Oct-25	0.00	4.92	0.00	0.00	0.00	0.00	0.00	10.55	16.32	0.00	1.26	7.00		2.20		0.00	0.00	0.50	**42.75**
Total	**0.00**	**78.10**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**399.65**	**658.78**	**0.00**	**21.60**	**278.83**	**0.00**	**51.12**	**0.00**	**0.00**	**0.00**	**32.23**	**1520.31**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during October 2025

Date	Import of NR from ER (ER-NR)																		Import of NR from NER (NER-NR)	
	ER - NR HVDC Alipurduar - Agra	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*S/C	ER - NR 765 kV Gaya - Balia	ER - NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER - NR 400 kV Sasaram - Varanasi	ER - NR 400 kV Sasaram - Allahabad	ER - NR 400 kV Naubatpur - Balia D/C	ER - NR 400 kV Biharshriff - Sahupuri D/C	ER - NR 220 kV Sahupuri - Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Nagar Untari - Rihand	ER - NR 132 kV Garhwa - Rihand	Total ER -NR	NER - NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Oct-25	5.75	4.10	5.95	14.49	12.90	21.98	4.90	10.89		1.33	0.98	3.95	4.76	2.35			0.00	**94.33**	12.05	**12.05**
2-Oct-25		7.85	12.57	11.83	11.61	22.76	6.05	11.26		0.97	1.38	3.74	6.85	2.80			0.00	**99.67**	12.05	**12.05**
3-Oct-25		9.41	16.75	11.15	11.45	23.10	7.05	11.22		0.65	1.73	4.00	6.00	2.10			0.00	**104.61**	10.80	**10.80**
4-Oct-25		12.65	18.96	7.94	10.85	22.35	5.03	13.07		0.42	1.40	3.65	6.40	1.71		0.00	0.00	**104.43**	10.05	**10.05**
5-Oct-25		6.46	9.18	8.85	5.95	14.73	1.71	8.93		1.62	0.70	1.82	3.14	1.22			0.00	**64.31**	12.32	**12.32**
6-Oct-25		2.89	3.54	7.43	3.28	9.34	0.00	3.52		1.74	0.54	1.14	1.40	1.09			0.00	**35.91**	16.10	**16.10**
7-Oct-25	2.20	2.93	1.50	5.94	3.79	8.54	0.00	4.36		1.40	0.13	0.95	0.57	1.13	0.48		0.00	**33.92**	14.63	**14.63**
8-Oct-25	7.00	2.82	3.50	6.57	7.92	9.10	0.00	5.09		2.29	0.04	2.42	1.24	1.41			0.00	**49.40**	9.43	**9.43**
9-Oct-25	8.00	4.19	6.94	6.84	9.40	9.81	0.00	5.80		2.21	0.21	2.80	2.15	1.12	0.00		0.00	**59.47**	9.63	**9.63**
10-Oct-25	7.00	5.45	11.45	8.10	11.54	11.82	0.00	7.50		1.95	0.45	3.50	3.25	1.38			0.00	**73.39**	9.40	**9.40**
11-Oct-25	7.80	5.50	10.30	8.00	10.33	13.48	1.16	8.03		1.52	0.84	2.85	3.71	1.40		0.10	0.00	**75.02**	9.63	**9.63**
12-Oct-25	6.15	5.80	12.83	9.76	10.60	14.19	0.92	8.25		1.30	1.13	2.64	3.20	1.19			0.00	**77.96**	9.63	**9.63**
13-Oct-25	7.81	5.82	9.88	9.56	9.74	10.30	0.13	7.26		1.80	1.05	2.31	3.30	0.68			0.00	**69.64**	9.20	**9.20**
14-Oct-25	7.00	5.65	11.35	9.40	9.37	10.17	0.00	6.33		2.30	0.26	2.20	2.27	0.74	0.00		0.00	**67.04**	9.43	**9.43**
15-Oct-25	7.01	6.13	11.75	10.23	10.03	11.22	0.24	7.30		1.50	0.68	2.50	2.90	1.02	0.00		0.00	**72.51**	9.64	**9.64**
16-Oct-25	6.96	5.61	13.59	10.70	9.73	11.15	0.00	7.14		1.72	0.67	2.44	3.49	1.05			0.00	**74.25**	9.14	**9.14**
17-Oct-25	7.65	5.56	12.65	10.04	8.15	10.60	0.00	6.91		1.95	0.45	1.70	3.11	0.85			0.00	**69.62**	9.64	**9.64**
18-Oct-25	6.11	4.95	12.53	10.60	7.32	10.23	0.00	6.60		2.17	0.30	1.72	3.26	1.02			0.00	**66.81**	5.52	**5.52**
19-Oct-25	7.01	4.02	10.58	10.84	8.54	9.56	0.00	6.52		2.11	0.25	2.03	2.65	0.97	0.00		0.00	**65.08**	9.64	**9.64**
20-Oct-25	7.10	1.86	7.73	9.43	7.31	8.39	0.00	5.70		2.08	0.36	1.59	1.42	0.68			0.00	**53.65**	9.65	**9.65**
21-Oct-25	6.90	0.00	2.91	8.36	6.02	6.00	0.00	4.55		2.25	0.10	0.94	0.00	0.64			0.00	**38.67**	9.64	**9.64**
22-Oct-25	7.23	0.00	0.00	8.66	5.15	3.07	0.00	3.43		2.50	0.00	0.59	0.00	0.73	0.00		0.00	**31.36**	13.79	**13.79**
23-Oct-25	6.92	1.39	3.10	9.48	6.68	5.52	0.00	5.27		2.37	0.09	1.11	0.70	1.34			0.00	**43.97**	14.02	**14.02**
24-Oct-25	6.92	4.54	7.97	9.34	6.44	7.02	0.00	6.56		1.79	0.08	1.62	2.13	2.32			0.00	**56.73**	14.02	**14.02**
25-Oct-25	7.10	2.92	6.12	9.65	6.66	5.30	0.00	5.21		1.93	0.29	1.46	1.66	2.15			0.00	**50.45**	14.44	**14.44**
26-Oct-25	7.08	1.35	3.41	9.00	3.00	4.89	0.00	3.73		1.95	0.18	0.01	0.52	1.70	0.00		0.00	**36.82**	14.46	**14.46**
27-Oct-25	7.11	1.02	1.61	8.41	2.90	4.34	0.00	3.54		2.20	0.04	0.07	0.00	0.53	0.00		0.00	**31.77**	14.01	**14.01**
28-Oct-25	7.20	0.76	0.00	6.96	1.63	2.77	0.00	2.81		1.32	1.04	0.00	0.00	1.33		0.10	0.00	**25.92**	12.58	**12.58**
29-Oct-25	7.01	2.18	3.88	7.39	6.67	4.29	0.00	4.60		0.89	1.44	0.00	1.16	1.46		0.05	0.00	**41.02**	14.40	**14.40**
30-Oct-25	6.42	6.61	6.61	8.77	10.51	8.22	0.54	6.33		0.56	1.77	4.62	2.92	2.48			0.00	**66.36**	14.47	**14.47**
31-Oct-25	6.50	6.48	5.15	8.00	14.99	12.79	5.30	7.08		0.79	1.45	4.20	3.04	1.70			0.00	**77.47**	12.40	**12.40**
Total	**176.94**	**136.90**	**244.29**	**281.72**	**250.46**	**327.03**	**33.03**	**204.79**	**0.00**	**51.58**	**20.03**	**64.57**	**77.20**	**42.29**	**0.48**	**0.25**	**0.00**	**1911.56**	**355.81**	**355.81**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.2 Import-Export of NR with ER & NER during October 2025

Date	Export of NR to ER (NR- ER)																		Export of NR to NER (NR-NER)	
	NR - ER HVDC Agra - Alipurduar	NR - ER 765 kV Fatehpur - Sasaram	NR - ER 765 kV Varanasi - Gaya 2*S/C	NR - ER 765 kV Balia - Gaya	NR - ER 400 kV Balia - Patna D/C	NR - ER 400 kV Gorakhpur - Muzaffarpur D/C	NR - ER 400 kV Balia - Biharshariff D/C	NR - ER 400 kV Gorakhpur - Motihari D/C	NR - ER 400 kV Varanasi - Biharshariff D/C	NR - ER 400 kV Varanasi - Sasaram	NR - ER 400 kV Allahabad - Sasaram	NR - ER 400 kV Balia - Naubatpur D/C	NR - ER 400 kV Sahupuri - Biharshriff D/C	NR - ER 220 kV Karamnasa - Sahupuri	NR - ER 132 kV Karamnasa - Sahupuri	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	Total NR -ER	NR - NER HVDC Agra - Biswanath Chariali	Total NR-NER
1-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.60	**0.60**	0.00	**0.00**
2-Oct-25		0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.56	**0.56**	0.00	**0.00**
3-Oct-25		0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.35	**0.35**	0.00	**0.00**
4-Oct-25		0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00		0.10	0.38	**0.48**	0.00	**0.00**
5-Oct-25		0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.60	**0.60**	0.00	**0.00**
6-Oct-25		0.00	0.00	0.00	0.00	0.00	1.45	0.00		0.00	0.00	0.00	0.00	0.00			0.60	**2.05**	0.00	**0.00**
7-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	3.35	0.00		0.00	0.00	0.00	0.00	0.00	0.00		0.55	**3.90**	0.00	**0.00**
8-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	2.03	0.00		0.00	0.00	0.00	0.00	0.00			0.70	**2.73**	0.00	**0.00**
9-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	1.38	0.00		0.00	0.00	0.00	0.00	0.00	0.00		0.55	**1.93**	0.00	**0.00**
10-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.13	0.00		0.00	0.00	0.00	0.00	0.00			0.64	**0.77**	0.00	**0.00**
11-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00		0.00	0.66	**0.66**	0.00	**0.00**
12-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.57	**0.57**	0.00	**0.00**
13-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.68	**0.68**	0.00	**0.00**
14-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.52	0.00		0.00	0.00	0.00	0.00	0.00	0.00		0.60	**1.12**	0.00	**0.00**
15-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00		0.59	**0.59**	0.00	**0.00**
16-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.34	0.00		0.00	0.00	0.00	0.00	0.00			0.61	**0.95**	0.00	**0.00**
17-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	1.76	0.00		0.00	0.00	0.00	0.00	0.00			0.55	**2.31**	0.00	**0.00**
18-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.94	0.00		0.00	0.00	0.00	0.00	0.00			0.66	**1.60**	0.00	**0.00**
19-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	1.81	0.00		0.00	0.00	0.00	0.00	0.00	0.00		0.76	**2.57**	0.00	**0.00**
20-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	2.23	0.00		0.00	0.00	0.00	0.00	0.00			0.76	**2.99**	0.00	**0.00**
21-Oct-25	0.00	0.59	0.00	0.00	0.00	0.00	4.10	0.00		0.00	0.00	0.00	0.17	0.00			0.70	**5.56**	0.00	**0.00**
22-Oct-25	0.00	1.58	0.13	0.00	0.00	0.00	5.44	0.00		0.00	0.38	0.00	0.94	0.00	0.00		0.67	**9.14**	0.00	**0.00**
23-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	5.08	0.00		0.00	0.00	0.00	0.00	0.00			0.74	**5.82**	0.00	**0.00**
24-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	5.72	0.00		0.00	0.00	0.00	0.00	0.00			0.63	**6.35**	0.00	**0.00**
25-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	5.30	0.00		0.00	0.00	0.00	0.00	0.00			0.71	**6.01**	0.00	**0.00**
26-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	5.29	0.00		0.00	0.00	0.00	0.00	0.00	0.00		0.68	**5.97**	0.00	**0.00**
27-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	5.78	0.00		0.00	0.00	0.00	0.15	0.00	0.00		0.50	**6.43**	0.00	**0.00**
28-Oct-25	0.00	0.00	0.11	0.00	0.00	0.00	5.96	0.00		0.00	0.00	0.36	0.50	0.00		0.00	0.46	**7.39**	0.00	**0.00**
29-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.98	0.00		0.00	0.00	2.32	0.00	0.00		0.00	0.29	**3.59**	0.00	**0.00**
30-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.18	**0.18**	0.00	**0.00**
31-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00			0.13	**0.13**	0.00	**0.00**
Total	**0.00**	**2.17**	**0.24**	**0.00**	**0.00**	**0.00**	**59.59**	**0.00**	**0.00**	**0.00**	**0.38**	**2.68**	**1.76**	**0.00**	**0.00**	**0.10**	**17.66**	**84.58**	**0.00**	**0.00**

Disclaimer:- Blank entry if the line under outage/shutdown on corrosponding day

15.3 Import and Export of ER with WR & NER during October 2025

Date	Export of WR to ER (WR-ER)									Import of WR from ER (ER - WR)									Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xD/C	WR - ER 400 kV Jeypore - Jagdalpur D/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 400 kV Jeypore - Jagdalpur D/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Oct-25	25.9	8.4	0.9	4.8	1.2	0.5	0.8	0.1	**42.57**	0.0	2.5	4.9	0.0	2.6	5.2	0.3	1.5	**17.00**	0.24	5.83	0.75	**6.82**	1.78	0.00	0.00	**1.78**
2-Oct-25	17.1	9.5	0.7	3.4	1.0	0.8	1.1	0.2	**33.90**	0.0	3.8	5.5	0.1	2.6	4.8	0.2	1.2	**18.22**	0.00	5.31	0.45	**5.76**	3.18	0.00	0.01	**3.19**
3-Oct-25	8.9	2.5	0.0	1.8	0.6	0.1	0.5	0.0	**14.48**	3.3	12.9	10.1	1.6	5.2	6.3	0.8	2.0	**42.16**	0.42	6.23	0.95	**7.60**	2.73	0.04	0.09	**2.86**
4-Oct-25	2.6	1.9	0.0	0.6	1.0	0.2	0.7	0.0	**7.10**	5.2	12.4	11.4	2.1	5.7	3.7	0.9	1.9	**43.37**	0.44	7.37	1.07	**8.88**	2.30	0.00	0.00	**2.30**
5-Oct-25	7.1	1.8	0.0	1.9	1.3	0.7	1.2	0.0	**14.13**	1.7	12.2	9.2	0.7	4.6	1.0	0.4	1.6	**31.25**	0.81	4.56	0.46	**5.84**	1.31	0.00	0.02	**1.34**
6-Oct-25	9.5	2.9	0.0	2.3	1.4	2.1	1.1	0.0	**19.29**	1.1	10.7	9.0	0.3	3.7	0.5	0.2	1.5	**26.94**	2.84	6.22	0.97	**10.04**	0.42	0.29	0.10	**0.81**
7-Oct-25	15.7	8.4	0.0	3.1	1.3	1.4	1.1	0.1	**31.09**	0.3	7.6	8.7	0.1	4.5	0.2	0.4	1.5	**23.28**	4.04	8.67	1.63	**14.34**	0.04	0.00	0.00	**0.04**
8-Oct-25	9.7	6.9	0.0	1.7	0.9	0.4	1.0	0.0	**20.67**	2.1	8.8	10.5	0.8	5.9	1.6	0.6	1.8	**32.05**	2.55	6.78	1.38	**10.71**	0.06	0.03	0.00	**0.09**
9-Oct-25	11.2	5.8	0.1	2.1	1.1	0.3	1.2	0.3	**22.20**	1.1	9.0	9.6	0.5	5.4	1.9	0.3	1.2	**29.08**	2.20	7.58	1.32	**11.10**	0.56	0.00	0.00	**0.56**
10-Oct-25	7.1	3.9	0.0	1.2	0.7	0.2	1.2	0.2	**14.38**	2.3	8.1	10.2	1.4	7.0	3.4	0.5	1.2	**34.11**	1.98	8.81	1.37	**12.16**	0.35	0.00	0.00	**0.35**
11-Oct-25	9.8	7.0	0.0	1.7	1.0	1.8	1.3	0.1	**22.65**	1.3	5.7	9.6	0.8	5.9	1.5	0.2	1.1	**25.98**	1.00	6.30	0.89	**8.19**	0.33	0.00	0.00	**0.33**
12-Oct-25	9.5	8.1	0.1	1.5	0.9	0.5	1.2	0.3	**22.11**	1.1	2.6	9.9	0.6	5.4	1.2	0.2	1.0	**22.09**	1.53	6.16	1.00	**8.69**	0.50	0.00	0.02	**0.53**
13-Oct-25	8.1	5.8	0.0	1.4	1.1	0.1	1.0	0.0	**17.54**	1.8	1.3	12.4	1.1	5.6	2.9	0.4	1.7	**27.15**	3.32	8.65	1.54	**13.50**	0.24	0.00	0.00	**0.24**
14-Oct-25	6.0	3.3	0.0	1.1	0.8	0.4	1.0	0.0	**12.62**	1.7	4.1	9.9	1.3	6.1	2.4	0.6	1.6	**27.61**	4.08	9.69	1.76	**15.53**	0.00	0.00	0.00	**0.00**
15-Oct-25	4.8	4.0	0.0	0.6	1.8	3.1	0.8	0.1	**15.18**	2.6	5.9	10.6	1.4	3.3	1.0	1.2	1.5	**27.34**	4.98	10.64	2.01	**17.63**	0.00	0.00	0.00	**0.00**
16-Oct-25	4.6	2.5	0.0	0.4	1.5	1.4	0.9	0.1	**11.36**	4.1	10.1	12.3	1.1	3.6	2.4	1.0	1.6	**36.33**	5.78	11.51	2.10	**19.39**	0.00	0.00	0.00	**0.00**
17-Oct-25	8.3	2.8	0.0	1.5	2.6	1.2	0.8	0.2	**17.32**	4.0	8.7	11.1	1.6	1.5	4.1	0.6	1.5	**33.14**	5.07	12.92	2.31	**20.29**	0.00	0.00	0.00	**0.00**
18-Oct-25	8.6	3.0	0.0	1.5	3.0	0.6	0.6	0.1	**17.47**	2.3	7.6	10.5	0.9	1.0	3.6	0.3	1.4	**27.75**	6.56	11.88	2.10	**20.54**	0.00	0.00	0.00	**0.00**
19-Oct-25	12.7	1.3	0.0	2.0	2.5	1.9	0.9	0.1	**21.47**	0.7	10.9	11.0	0.7	2.1	4.2	0.4	0.8	**30.81**	5.83	10.48	1.81	**18.11**	0.00	0.00	0.00	**0.00**
20-Oct-25	18.0	4.6	0.2	3.3	2.9	1.7	1.3	0.3	**32.19**	0.7	6.6	9.9	0.6	2.6	2.8	0.3	1.0	**24.49**	4.74	8.39	1.46	**14.58**	0.00	0.00	0.00	**0.00**
21-Oct-25	21.3	7.0	0.1	3.8	3.4	0.9	1.3	0.3	**38.03**	0.2	3.4	8.8	0.2	0.9	1.3	0.2	0.7	**15.77**	5.39	9.11	1.72	**16.22**	0.00	0.00	0.00	**0.00**
22-Oct-25	24.8	7.1	0.3	4.3	3.0	1.9	1.2	0.4	**42.96**	0.0	3.9	8.2	0.1	1.1	1.3	0.4	0.6	**15.51**	8.32	13.65	2.56	**24.53**	0.00	0.00	0.00	**0.00**
23-Oct-25	19.9	9.0	0.1	3.4	2.5	2.3	1.0	0.2	**38.27**	0.0	2.8	9.2	0.2	1.4	0.7	0.4	0.8	**15.52**	9.07	14.58	2.65	**26.30**	0.00	0.00	0.00	**0.00**
24-Oct-25	16.9	3.7	0.0	2.9	1.9	2.5	0.8	0.0	**28.66**	0.4	6.2	11.3	0.3	1.5	0.8	0.4	1.2	**22.17**	8.58	13.52	2.47	**24.58**	0.00	0.00	0.00	**0.00**
25-Oct-25	17.6	10.1	0.0	3.4	3.6	1.5	0.8	0.1	**37.10**	0.3	3.0	8.1	0.2	0.4	1.1	0.3	1.2	**14.63**	8.44	13.07	2.36	**23.87**	0.00	0.00	0.00	**0.00**
26-Oct-25	21.6	11.8	0.5	4.7	4.4	2.4	1.1	0.2	**46.77**	0.0	2.8	6.8	0.0	0.3	0.6	0.2	1.2	**11.76**	7.84	12.11	2.15	**22.11**	0.00	0.00	0.00	**0.00**
27-Oct-25	23.1	8.7	0.0	5.4	4.1	1.5	1.1	0.2	**44.10**	0.1	5.5	8.0	0.1	0.5	0.4	0.1	1.1	**15.92**	8.41	12.61	2.30	**23.32**	0.00	0.00	0.00	**0.00**
28-Oct-25	30.2	9.0	0.2	6.2	4.8	0.0	1.0	0.2	**51.72**	0.0	4.6	5.9	0.0	0.4	4.4	0.3	0.8	**16.27**	8.57	12.58	2.23	**23.38**	0.00	0.00	0.00	**0.00**
29-Oct-25	25.8	4.5	0.2	4.9	3.2	0.0	0.5	0.2	**39.24**	0.0	4.7	6.3	0.1	1.5	6.0	0.9	1.2	**20.76**	9.14	13.40	2.30	**24.84**	0.00	0.00	0.00	**0.00**
30-Oct-25	20.5	2.2	0.0	3.6	2.6	0.5	0.4	0.2	**30.01**	0.0	4.7	8.6	0.0	0.6	5.5	1.0	1.1	**21.54**	8.12	12.48	2.26	**22.85**	0.00	0.00	0.00	**0.00**
31-Oct-25	13.8	2.8	0.0	2.6	3.4	4.0	0.8	0.3	**27.76**	0.1	5.6	10.0	0.3	0.4	0.0	0.3	0.9	**17.57**	4.35	9.82	1.69	**15.86**	0.07	0.00	0.00	**0.07**
Total	**440.49**	**170.38**	**3.54**	**83.22**	**65.37**	**36.80**	**29.96**	**4.57**	**834.34**	**38.43**	**198.84**	**287.38**	**19.16**	**93.18**	**76.88**	**14.27**	**39.41**	**767.55**	**144.63**	**300.88**	**52.02**	**497.53**	**13.87**	**0.36**	**0.25**	**14.49**

Note- 400 kV Jeypore - Jagdalpur Ckt-1&2 included from 07.06.2025

Date	15.4 Import and Export of SR with ER & WR during October 2025																								
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)									Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar - Kolar	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	SR - WR 220kV Xeldem - Ambewadi S/C	SR - WR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Oct-25	0.00	21.24	40.50	**61.74**	11.05	0.00	0.00	**11.05**	0.00	2.93	21.53	0.00	2.38	1.89	0.00	15.74	**44.47**	15.20	13.08	1.55	36.06	42.40	0.00	0.00	1.10	**109.39**
2-Oct-25	0.00	36.39	38.70	**75.09**	9.72	0.00	0.00	**9.72**	0.00	2.30	22.80	0.00	0.00	1.86	0.00	16.22	**43.19**	10.15	7.31	0.04	28.92	15.27	0.00	0.00	0.13	**61.83**
3-Oct-25	0.42	35.32	50.72	**86.46**	5.24	0.00	0.00	**5.24**	0.00	6.02	30.87	0.00	34.86	2.03	0.00	23.07	**96.85**	7.23	0.99	0.00	26.79	1.04	0.00	0.00	0.00	**36.06**
4-Oct-25	6.71	34.39	51.14	**92.25**	0.00	0.00	0.00	**0.00**	0.00	9.52	35.22	0.00	62.33	2.00	0.00	25.82	**134.90**	7.23	1.61	0.00	28.68	0.00	0.00	0.00	0.00	**37.52**
5-Oct-25	12.62	31.55	39.36	**83.53**	0.00	0.00	0.00	**0.00**	0.00	3.69	24.11	0.00	57.11	1.46	0.00	17.86	**104.23**	7.23	9.98	0.00	31.10	0.00	0.00	0.00	0.00	**48.32**
6-Oct-25	12.67	36.94	40.11	**89.71**	0.00	0.00	0.00	**0.00**	0.00	3.24	25.53	0.00	71.95	1.89	0.00	19.58	**122.18**	7.23	5.62	0.00	27.70	0.00	0.00	0.00	0.00	**40.55**
7-Oct-25	12.65	43.83	42.94	**99.41**	0.00	0.00	0.00	**0.00**	0.00	6.62	27.37	0.00	65.51	1.84	0.00	21.60	**122.95**	7.25	4.45	0.00	30.65	0.00	0.00	0.00	0.00	**42.34**
8-Oct-25	10.72	37.73	46.78	**95.23**	0.00	0.00	0.00	**0.00**	15.74	8.22	27.93	0.00	89.22	1.79	0.00	23.25	**166.16**	2.12	3.88	0.00	32.12	0.00	0.00	0.00	0.00	**38.12**
9-Oct-25	9.63	33.58	45.19	**88.40**	0.00	0.00	0.00	**0.00**	12.13	5.27	24.20	0.00	80.18	1.73	0.00	20.64	**144.15**	0.00	7.10	0.00	33.60	0.00	0.00	0.00	0.00	**40.70**
10-Oct-25	7.39	35.30	45.96	**88.64**	0.00	0.00	0.00	**0.00**	7.32	2.45	26.09	0.00	83.53	1.91	0.00	20.72	**142.02**	0.00	5.90	0.00	34.62	0.00	0.00	0.00	0.00	**40.52**
11-Oct-25	13.24	40.93	44.63	**98.81**	0.00	0.00	0.00	**0.00**	10.62	0.66	23.68	0.00	67.29	0.10	0.00	18.53	**120.88**	0.00	9.18	0.03	38.04	0.00	0.00	0.00	0.00	**47.25**
12-Oct-25	9.54	39.54	44.89	**93.98**	0.00	0.00	0.00	**0.00**	9.96	0.41	22.87	0.00	40.55	2.04	0.00	17.34	**93.17**	0.00	12.56	0.03	38.71	0.00	0.00	0.00	0.03	**51.34**
13-Oct-25	7.41	39.86	46.36	**93.63**	0.00	0.00	0.00	**0.00**	14.84	1.31	26.42	0.00	51.23	2.28	0.00	19.28	**115.37**	0.00	9.15	0.00	35.72	0.00	0.00	0.00	0.00	**44.87**
14-Oct-25	9.05	40.21	43.56	**92.82**	0.00	0.00	0.00	**0.00**	20.12	0.85	23.91	0.00	57.39	2.04	0.00	16.77	**121.08**	0.00	14.84	0.00	33.84	0.00	0.00	0.00	0.00	**48.67**
15-Oct-25	12.58	48.15	46.07	**106.80**	0.00	0.00	0.00	**0.00**	20.95	1.19	25.38	0.00	35.41	2.38	0.00	17.93	**103.25**	0.00	15.44	0.00	34.95	0.00	0.00	0.00	0.00	**50.39**
16-Oct-25	6.58	40.54	51.26	**98.39**	0.00	0.00	0.00	**0.00**	14.83	3.16	29.88	0.00	43.58	2.09	0.00	20.20	**113.74**	0.00	11.48	0.00	36.69	0.00	0.00	0.00	0.00	**48.17**
17-Oct-25	1.26	45.14	49.07	**95.47**	0.00	0.00	0.00	**0.00**	7.14	1.22	25.62	0.00	47.16	0.79	0.00	18.04	**99.97**	0.00	14.81	0.00	40.02	0.00	0.00	0.00	0.00	**54.83**
18-Oct-25	1.27	43.87	48.08	**93.22**	0.00	0.00	0.00	**0.00**	7.31	1.13	21.79	0.00	40.69	2.22	0.00	28.24	**101.36**	0.00	14.41	0.00	35.99	0.00	0.00	0.00	0.00	**50.39**
19-Oct-25	2.54	36.72	42.61	**81.88**	0.00	0.00	0.00	**0.00**	7.31	0.05	15.80	0.00	30.46	1.92	0.00	21.59	**77.13**	0.00	16.82	0.00	35.20	0.00	0.00	0.00	0.00	**52.02**
20-Oct-25	4.58	34.41	41.90	**80.90**	0.00	0.00	0.00	**0.00**	7.32	0.89	19.08	0.00	22.20	1.66	0.00	24.00	**75.15**	0.00	10.79	0.00	26.22	0.00	0.00	0.00	0.00	**37.01**
21-Oct-25	7.17	37.30	43.33	**87.80**	0.00	0.00	0.00	**0.00**	6.55	3.88	27.36	0.00	22.49	1.86	0.00	30.08	**92.23**	0.00	5.33	0.00	22.56	0.00	0.00	0.00	0.00	**27.89**
22-Oct-25	7.48	35.35	38.04	**80.88**	0.00	0.00	0.00	**0.00**	8.19	2.04	22.01	0.00	14.60	2.16	0.00	24.75	**73.75**	0.00	8.14	0.00	25.98	0.00	0.00	0.00	0.00	**34.12**
23-Oct-25	7.56	40.97	43.38	**91.92**	0.00	0.00	0.00	**0.00**	12.26	3.84	26.21	0.00	25.07	2.01	0.00	30.06	**99.44**	0.00	4.96	0.00	21.92	0.00	0.00	0.00	0.00	**26.88**
24-Oct-25	7.54	39.84	49.47	**96.85**	0.00	0.00	0.00	**0.00**	16.55	2.13	27.46	0.00	48.47	2.15	0.00	31.94	**128.71**	0.00	5.93	0.00	21.68	0.00	0.00	0.00	0.00	**27.61**
25-Oct-25	7.54	35.40	44.94	**87.88**	0.00	0.00	0.00	**0.00**	11.63	1.09	21.07	0.00	34.77	2.14	0.00	25.78	**96.49**	0.00	11.95	0.08	25.10	0.00	0.00	0.00	0.00	**37.13**
26-Oct-25	7.54	28.94	37.72	**74.20**	0.00	0.00	0.00	**0.00**	11.57	0.47	17.34	0.00	24.20	2.07	0.00	20.92	**76.57**	0.00	16.06	1.96	25.64	0.00	0.00	0.00	1.46	**45.12**
27-Oct-25	7.58	35.07	40.98	**83.63**	0.00	0.00	0.00	**0.00**	11.47	0.92	20.39	0.00	34.70	2.12	0.00	23.52	**93.11**	0.00	13.53	0.00	26.02	0.00	0.00	0.00	0.00	**39.55**
28-Oct-25	2.25	27.14	34.50	**63.89**	0.84	0.00	0.00	**0.84**	7.32	0.28	14.64	0.00	14.91	2.19	0.00	15.95	**55.29**	0.00	22.08	0.29	31.41	0.00	0.00	0.00	0.29	**54.07**
29-Oct-25	0.00	25.19	34.69	**59.88**	2.63	0.00	0.00	**2.63**	3.22	0.07	12.80	0.00	18.51	2.13	0.01	11.08	**47.80**	9.29	28.98	1.44	38.52	0.00	0.00	0.00	1.74	**79.97**
30-Oct-25	3.64	35.72	47.04	**86.39**	6.02	0.00	0.00	**6.02**	0.00	2.38	19.50	0.00	32.39	2.12	0.00	14.42	**70.81**	11.86	18.68	0.90	34.17	6.26	0.00	0.00	0.22	**72.10**
31-Oct-25	11.55	37.23	48.02	**96.80**	0.00	0.00	0.00	**0.00**	0.00	9.58	27.43	0.00	60.69	2.16	0.00	22.71	**122.58**	7.24	7.76	0.13	24.93	0.00	0.00	0.00	0.01	**40.07**
TOTAL	**210.73**	**1133.78**	**1361.95**	**2706.46**	**35.50**	**0.00**	**0.00**	**35.50**	**244.35**	**87.78**	**736.29**	**0.00**	**1313.84**	**59.02**	**0.07**	**657.65**	**3099.00**	**92.02**	**332.79**	**6.45**	**963.55**	**64.99**	**0.00**	**0.01**	**4.99**	**1464.80**

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय
INTERNATIONAL EXCHANGE WITH BHUTAN, NEPAL BANGLADESH AND MYANMAR

अप्रैल 2025 से मार्च 2026 April 2025 to March 2026

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/ 'को आयात']
Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2025 APR'25	72.61	27.18	365.47	0.00	684.92	0.00	0.70	0.00
मई 2025 MAY'25	0.00	553.50	203.10	9.50	707.90	0.00	0.74	0.00
जून 2025 JUN'25	0.00	1148.30	21.70	248.80	646.50	0.00	0.74	0.00
जुलाई 2025 JUL'25	0.00	1522.80	0.00	484.01	709.78	0.00	0.71	0.00
अगस्त 2025 AUG'25	0.00	1610.50	0.00	551.22	712.95	0.00	0.77	0.00
सितंबर 2025 SEP'25	0.00	1593.64	0.00	634.40	722.43	0.00	0.69	0.00
अक्तूबर 2025 OCT'25	0.00	938.40	0.00	741.80	749.20	0.00	0.73	0.00
कुल Total	**72.61**	**7394.32**	**590.27**	**2669.73**	**4933.68**	**0.00**	**5.08**	**0.00**

* Based on daily operational data

16.1 सीमावर्ती देशों से आयात (अक्तूबर 2025)

16.1 Import from neighbouring countries during October 2025

(सभी आंकड़े मि.यू.में) (All figures in MU)

दिनांक Date	भूटान से आयात Import from Bhutan								बांग्लादेश से आयात Import from Bangladesh		नेपाल से आयात Import from Nepal				म्यांमार से आयात Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	From UP Source	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Oct-25	16.97	4.41	1.70	0.00	13.01	21.27	0.69	0.41	0.00	0.00	0.38	0.00	20.01	3.92	0.00
2-Oct-25	17.23	4.56	1.62	0.00	12.94	21.09	0.95	0.23	0.00	0.00	1.09	0.00	18.84	4.00	0.00
3-Oct-25	17.14	4.51	1.66	0.00	12.41	20.40	1.21	0.24	0.00	0.00	1.34	0.00	20.38	3.84	0.00
4-Oct-25	15.65	4.05	1.68	0.00	13.22	21.21	1.15	0.22	0.00	0.00	1.33	0.00	18.26	3.28	0.00
5-Oct-25	8.91	1.03	0.39	0.00	5.83	13.69	0.96	0.05	0.00	0.00	1.01	0.00	11.08	1.72	0.00
6-Oct-25	1.51	0.00	0.37	0.00	0.00	10.23	0.89	0.00	0.00	0.00	0.73	0.00	18.39	3.84	0.00
7-Oct-25	9.88	3.61	1.42	0.51	0.00	13.12	1.10	0.00	0.00	0.00	1.22	0.00	19.16	3.95	0.00
8-Oct-25	8.51	3.02	1.69	0.00	0.00	19.78	1.15	0.08	0.00	0.00	1.19	0.00	18.83	3.78	0.00
9-Oct-25	7.21	2.42	1.50	0.00	3.09	23.56	1.16	0.19	0.00	0.00	1.42	0.00	18.36	3.71	0.00
10-Oct-25	11.23	3.14	1.34	0.00	12.04	18.95	1.14	0.00	0.00	0.00	1.49	0.00	18.42	4.15	0.00
11-Oct-25	11.90	2.77	1.12	0.00	10.88	16.91	1.03	0.00	0.00	0.00	1.50	0.00	19.36	3.83	0.00
12-Oct-25	11.33	2.59	0.90	0.00	10.03	15.37	0.95	0.00	0.00	0.00	1.45	0.00	18.58	4.01	0.00
13-Oct-25	10.49	2.28	0.83	0.00	9.21	14.00	0.91	0.00	0.00	0.00	1.48	0.00	18.60	3.81	0.00
14-Oct-25	8.89	1.74	0.74	0.00	8.64	13.02	0.54	0.00	0.00	0.00	1.36	0.00	18.68	3.99	0.00
15-Oct-25	11.71	0.54	0.59	0.00	8.28	12.26	0.55	0.00	0.00	0.00	1.48	0.00	18.69	3.96	0.00
16-Oct-25	10.47	2.18	0.62	0.00	7.73	11.36	0.70	0.00	0.00	0.00	1.44	0.00	18.33	3.84	0.00
17-Oct-25	10.60	2.17	0.64	0.00	7.35	10.96	0.66	0.00	0.00	0.00	1.49	0.00	18.36	3.92	0.00
18-Oct-25	9.69	1.86	0.39	0.00	7.68	8.95	0.56	0.00	0.00	0.00	1.40	0.00	18.25	3.90	0.00
19-Oct-25	9.32	1.28	0.00	0.00	6.57	9.38	0.40	0.00	0.00	0.00	1.45	0.00	18.53	4.02	0.00
20-Oct-25	8.31	1.43	0.00	0.00	6.11	8.55	0.40	0.00	0.00	0.00	1.49	0.00	19.61	3.99	0.00
21-Oct-25	8.11	1.36	0.00	0.00	5.71	7.85	0.22	0.00	0.00	0.00	1.52	0.00	19.78	4.15	0.00
22-Oct-25	7.25	1.02	0.00	0.00	5.57	7.62	0.29	0.00	0.00	0.00	1.47	0.00	19.05	4.37	0.00
23-Oct-25	6.20	0.98	0.00	0.00	5.31	7.05	0.22	0.00	0.00	0.00	1.52	0.00	19.60	4.33	0.00
24-Oct-25	6.58	0.75	0.00	0.00	5.13	6.62	0.07	0.00	0.00	0.00	1.49	0.00	19.14	4.21	0.00
25-Oct-25	5.49	0.90	0.00	0.00	5.46	5.77	0.00	0.00	0.00	0.00	0.75	0.00	18.61	4.20	0.00
26-Oct-25	4.95	1.02	0.00	0.00	5.38	5.65	0.00	0.00	0.00	0.00	0.35	0.00	18.97	4.05	0.00
27-Oct-25	4.44	0.76	0.00	0.00	4.90	4.97	0.00	0.00	0.00	0.00	0.37	0.00	19.22	4.12	0.00
28-Oct-25	4.53	0.77	0.00	0.00	4.77	4.45	0.00	0.00	0.00	0.00	0.41	0.00	19.18	4.23	0.00
29-Oct-25	4.56	0.80	0.00	0.00	4.07	4.56	0.55	0.00	0.00	0.00	0.85	0.00	18.92	4.21	0.00
30-Oct-25	7.06	1.64	0.00	0.00	4.42	5.56	0.54	0.00	0.00	0.00	1.51	0.00	20.53	3.96	0.00
31-Oct-25	14.04	3.25	0.00	0.00	7.71	11.94	0.68	0.00	0.00	0.00	1.53	0.00	21.98	4.01	0.00
Total	**290.15**	**62.82**	**19.18**	**0.51**	**213.48**	**376.09**	**19.67**	**1.43**	**0.00**	**0.00**	**37.51**	**0.00**	**583.68**	**121.32**	**0.00**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

16.2 सीमावर्ती देशों को निर्यात (अक्तूबर 2025)

16.2 Export to neighbouring countries during October 2025

(सभी आंकड़े मि.यू.में) (All figures in MU)

दिनांक Date	भूटान को निर्यात Export to Bhutan								बांग्लादेश को निर्यात Export to Bangladesh		नेपाल को निर्यात Export to Nepal				म्यांमार को निर्यात Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwar D/C*	400 kV Jigmeling-Alipurdwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	From UP Source	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Oct-25	0.00	0.00	0.00	0.33	0.00	0.00	0.00	0.00	22.20	0.84	0.00	0.00	0.00	0.00	0.02
2-Oct-25	0.00	0.00	0.00	0.52	0.00	0.00	0.00	0.00	21.58	0.88	0.00	0.00	0.00	0.00	0.03
3-Oct-25	0.00	0.00	0.00	0.41	0.00	0.00	0.00	0.00	19.91	0.94	0.00	0.00	0.00	0.00	0.02
4-Oct-25	0.00	0.00	0.00	0.41	0.00	0.00	0.00	0.00	21.49	1.00	0.00	0.00	0.00	0.00	0.03
5-Oct-25	0.00	0.00	0.00	1.73	0.00	0.00	0.00	0.00	21.28	0.91	0.00	0.00	0.00	0.00	0.03
6-Oct-25	0.00	0.39	0.00	0.63	0.00	0.00	0.00	0.12	21.54	0.85	0.00	0.00	0.00	0.00	0.03
7-Oct-25	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.02	22.05	1.33	0.00	0.00	0.00	0.00	0.03
8-Oct-25	0.00	0.00	0.00	0.06	0.00	0.00	0.00	0.00	21.09	1.63	0.00	0.00	0.00	0.00	0.02
9-Oct-25	0.00	0.00	0.00	0.35	0.00	0.00	0.00	0.00	22.78	1.61	0.00	0.00	0.00	0.00	0.02
10-Oct-25	0.00	0.00	0.00	0.18	0.00	0.00	0.00	0.00	23.21	1.57	0.00	0.00	0.00	0.00	0.02
11-Oct-25	0.00	0.00	0.00	0.27	0.00	0.00	0.00	0.15	22.84	1.49	0.00	0.00	0.00	0.00	0.01
12-Oct-25	0.00	0.00	0.00	0.44	0.00	0.00	0.00	0.24	22.92	1.56	0.00	0.00	0.00	0.00	0.02
13-Oct-25	0.00	0.00	0.00	0.40	0.00	0.00	0.00	0.22	22.67	1.57	0.00	0.00	0.00	0.00	0.02
14-Oct-25	0.00	0.00	0.00	0.46	0.00	0.00	0.00	0.21	22.67	1.62	0.00	0.00	0.00	0.00	0.03
15-Oct-25	0.00	0.00	0.00	0.63	0.00	0.00	0.00	0.25	22.78	1.72	0.00	0.00	0.00	0.00	0.03
16-Oct-25	0.00	0.00	0.00	0.13	0.00	0.00	0.00	0.40	22.77	1.80	0.00	0.00	0.00	0.00	0.03
17-Oct-25	0.00	0.00	0.00	0.11	0.00	0.00	0.00	0.21	22.23	1.62	0.00	0.00	0.00	0.00	0.02
18-Oct-25	0.00	0.00	0.00	0.20	0.00	0.00	0.00	0.34	22.22	1.51	0.00	0.00	0.00	0.00	0.02
19-Oct-25	0.00	0.00	0.12	0.45	0.00	0.00	0.00	0.52	22.22	1.82	0.00	0.00	0.00	0.00	0.02
20-Oct-25	0.00	0.00	0.28	0.61	0.00	0.00	0.00	0.70	22.72	1.99	0.00	0.00	0.00	0.00	0.02
21-Oct-25	0.00	0.00	0.54	0.70	0.00	0.00	0.00	0.74	23.35	2.06	0.00	0.00	0.00	0.00	0.02
22-Oct-25	0.00	0.00	0.71	0.63	0.00	0.00	0.00	0.63	23.60	2.05	0.00	0.00	0.00	0.00	0.03
23-Oct-25	0.00	0.00	0.86	0.59	0.00	0.00	0.00	0.68	23.58	1.94	0.00	0.00	0.00	0.00	0.03
24-Oct-25	0.00	0.00	0.86	0.61	0.00	0.00	0.00	0.36	22.97	1.86	0.00	0.00	0.00	0.00	0.02
25-Oct-25	0.00	0.00	0.91	0.53	0.00	0.00	0.40	0.20	22.68	1.80	0.00	0.00	0.00	0.00	0.03
26-Oct-25	0.00	0.00	1.06	0.57	0.00	0.00	0.43	0.25	22.53	1.86	0.00	0.00	0.00	0.00	0.03
27-Oct-25	0.00	0.00	1.27	0.62	0.00	0.00	0.57	0.25	22.98	1.77	0.00	0.00	0.00	0.00	0.02
28-Oct-25	0.00	0.00	1.32	0.53	0.00	0.00	0.17	0.34	22.97	1.71	0.00	0.00	0.00	0.00	0.03
29-Oct-25	0.00	0.00	1.32	0.44	0.00	0.00	0.00	0.45	23.34	1.71	0.00	0.00	0.00	0.00	0.03
30-Oct-25	0.00	0.00	0.80	0.53	0.00	0.00	0.00	0.42	23.18	1.79	0.00	0.00	0.00	0.00	0.02
31-Oct-25	0.00	0.00	0.26	0.56	0.00	0.00	0.00	0.29	22.93	1.74	0.00	0.00	0.00	0.00	0.01
Total	**0.00**	**0.39**	**10.32**	**14.61**	**0.00**	**0.00**	**1.57**	**7.98**	**697.28**	**48.55**	**0.00**	**0.00**	**0.00**	**0.00**	**0.73**

Based on SEM/Energy meter data for links where available (*Mangdechu generation reciept at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – अक्तूबर 2025

17. STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - OCTOBER 2025

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

अक्तूबर 2025 October 2025			Apr'25- Mar'26	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	1095	1662	12196	26538
प.क्षे. WR	957	560	6984	5449
द.क्षे. SR	898	556	6272	10455
पू.क्षे. ER	1072	852	4988	9988
पूर्वोत्तर क्षे. NER	118	155	886	2279
कुल TOTAL	4140	3785	31326	54709

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2025 Apr'25	13712	9041	2804	7138
मई 2025 May'25	14344	9129	3472	7546
जून 2025 Jun'25	14456	9860	4621	8890
जुलाई 2025 Jul'25	15157	11649	5344	9965
अगस्त 2025 Aug'25	15809	10883	5218	9425
सितंबर 2025 Sep'25	15509	10023	5727	7960
अक्तूबर 2025 Oct'25	15944	10342	4140	3785
कुल TOTAL	104931	70927	31326	54709

मासिक डी एस एम बिलिंग का ब्योरा* 2025-26
MONTHLY DSM BILLING DETAILS* 2025-26

अनंतिम आँकड़े
Provisional data subject to change

करोड़ रु. मे (RS. IN CRORES)

क्षेत्र REGION → / सप्ताह WEEK ↓	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
29.09.25 to 05.10.25	34.40	236.54	30.92	156.65	32.39
06.10.25 to 12.10.25	184.33	182.55	30.32	151.83	27.17
13.10.25 to 19.10.25	120.52	185.95	38.43	156.47	29.40
20.10.25 to 26.10.25	109.01	167.65	23.23	122.57	29.87
27.10.25 to 02.11.25	63.42	230.40	34.02	157.27	32.91

* Amount shown is Payble to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2025
EXCHANGES THROUGH POWER EXCHANGES -OCTOBER 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED		43.47	0.00
2	ADANI GREEN ENERGY TWENTY FIVE LIMITED		25.13	0.00
3	ADANI GREEN ENERGY TWENTY FOUR LIMITED		48.56	0.00
4	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		22.50	0.00
5	ADANI SOLAR ENERGY JODHPUR SIX PRIVATE LIMITED_50MW		7.92	0.00
6	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		9.10	0.00
7	AMBUJA CEMENTS LIMITED_Essel Park RJ		29.08	0.00
8	AMP Energy Green Four Private Limited		3.66	0.00
9	Adept Renewable Technologies Private Limited		16.83	0.00
10	Amp Energy Green Six Private Limited		16.52	0.00
11	Amplus Ages Private Limited		1.02	0.00
12	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		3.35	0.00
13	Chandigarh (UT)		34.14	12.82
14	Delhi		17.33	571.12
15	Eden Renewable Alma Private Limited		13.35	0.00
16	Government of Himachal Pradesh _ Chamera1HEP		12.82	2.18
17	Government of Himachal Pradesh _ Chamera3HEP		3.31	0.73
18	Government of Himachal Pradesh_ CHAMERA2HEP		10.23	2.67
19	Government of Himachal Pradesh_BairasuilHEP		5.32	0.80
20	Government of Himachal Pradesh_Koldam HEP		22.42	2.69
21	Government of Himachal Pradesh_NJHPS		39.24	4.44
22	Government of Himachal Pradesh_Parbati2HEP		11.68	2.29
23	Government of Himachal Pradesh_Parbati3HEP		7.80	1.74
24	Government of Himachal Pradesh_RampurHEP		12.37	1.29
25	Grian Energy Private Limited		0.97	0.00
26	Haryana		279.94	110.06
27	Himachal Pradesh		232.90	31.02
28	IGSTPS JHAJJAR		19.52	0.00
29	JUNIPER GREEN COSMIC PRIVATE LIMITED		5.64	0.00
30	JUNIPER NIRJARA ENERGY PRIVATE LIMITED		3.29	0.00
31	Jammu Kashmir		364.09	14.69
32	Juna Renewable Energy Private Limited		22.44	0.00
33	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		36.23	0.00
34	Khidrat Renewable Energy Private Limited		41.60	0.00
35	NEA Nepal Upper Chameliya Hydropower Project	उत्तरी क्षेत्र NR	19.74	0.00
36	NEA Nepal Upper Kalangagad Hydropower Project new		17.45	0.00
37	NTPC Dadri Stage I		22.84	0.00
38	NTPC Dadri Stage II		3.85	0.00
39	NTPC Rihand stage I		12.08	0.00
40	NTPC Rihand stage II		13.94	0.00
41	NTPC Rihand stage III		15.18	0.00
42	NTPC Singrauli		25.29	0.00
43	NTPC Tanda Stage II		1.57	0.00
44	NTPC Unchahar Stage I		1.16	0.00
45	NTPC Unchahar Stage II		7.28	0.00
46	NTPC Unchahar Stage III		3.30	0.00
47	NTPC Unchahar Stage IV		2.77	0.00
48	North Central Railway Prayagraj		0.00	42.29
49	Onevolt Energy Private Limited		2.09	0.00
50	Punjab		101.47	786.30

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2025
EXCHANGES THROUGH POWER EXCHANGES -OCTOBER 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
51	RENEW SURYA PRATAP PRIVATE LIMITED		39.99	0.00
52	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		0.33	0.00
53	Rajasthan		309.27	147.05
54	ReNew Surya Ravi Private Limited		19.82	0.00
55	Renew Surya Jyoti Private Limited		5.11	0.00
56	SHREE CEMENT LIMITED TPS		19.07	7.08
57	Serentica Renewables India 4 Private Limited		2.57	0.00
58	Serentica Renewables India 5 Private Limited		6.93	0.00
59	Singoli Bhatwari HEP		38.76	0.09
60	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		15.82	0.00
61	TPSL 200MW TPTCL Banderwala		0.29	0.00
62	TPSL Banderwala SECI 100_INF		0.03	0.00
63	Transition Cleantech Services Private Limited		0.83	0.00
64	Transition Energy Services Private Limited		5.08	0.00
65	Transition Green Energy Private Limited		0.34	0.00
66	Transition Sustainable Energy Services One Private Limited		7.99	0.00
67	Transition Sustainable Energy Services Private Limited		0.12	0.00
68	Uttar Pradesh		138.60	649.05
69	Uttarakhand		57.84	165.93
70	2X600 VEDANTA LIMITED Chhattisgarh Power Plant		53.05	29.10
71	ACB (INDIA) LIMITED		23.72	0.53
72	ADANI GREEN ENERGY TWENTY FOUR LIMITED_PSS4		20.43	0.00
73	ADANI GREEN ENERGY TWENTY SIX A LIMITED_PSS-3		1.97	0.00
74	ADANI HYBRID ENERGY JAISALMER FIVE LIMITED_PSS4		12.41	0.00
75	ADANI HYBRID ENERGY JAISALMER FIVE LIMITED_PSS5_Solar		7.02	0.00
76	ADANI PORTS AND SPECIAL ECONOMIC ZONE LIMITED (PSS-3)		23.29	0.00
77	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS-3 (162.5 MW Hybrid Solar of 187.5MW HPD)		26.74	0.00
78	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (20.8 MW Hybrid Wind of 25 MW of 187.5MW HPD)		0.09	0.00
79	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_PSS3 (25 MW Hybrid Solar of 25 MW of 187.5MW HPD)		0.11	0.00
80	ADANI RENEWABLE ENERGY FIFTY SEVEN LIMITED_PSS13		118.27	0.00
81	ADANI RENEWABLE ENERGY FIFTY SIX LIMITED_PSS4		38.15	0.00
82	ADANI RENEWABLE ENERGY FIFTY SIX LIMITED_PSS9		68.59	0.00
83	ADANI RENEWABLE ENERGY FORTY FIVE LIMITED_PSS5		41.79	0.00
84	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS-3		58.81	0.00
85	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS13		24.62	0.00
86	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS4		10.41	0.00
87	ADANI RENEWABLE ENERGY FORTY ONE LIMITED_PSS8		18.72	0.00
88	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED_PSS-1		92.01	0.00
89	ADANI RENEWABLE ENERGY THREE LIMITED_PSS8_Hybrid Solar		4.28	0.00
90	ADANI RENEWABLE ENERGY THREE LIMITED_PSS8_Hybrid Wind		5.84	0.00
91	ADANI SOLAR ENERGY JODHPUR SIX PRIVATE LIMITED_PSS8_Hybrid Solar		6.02	0.00
92	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		78.90	0.00
93	AMBUJA CEMENTS LIMITED_PSS3		4.88	0.00
94	AMBUJA CEMENTS LIMITED_PSS4_Hybrid Solar		2.76	0.00
95	AMBUJA CEMENTS LIMITED_PSS4_Hybrid Wind		3.68	0.00
96	Adani Green Energy Twenty Five A Limited_PSS-2		30.06	0.00
97	Adani Green Energy Twenty Five B Limited(Hybrid Solar)_PSS9		16.86	0.00
98	Adani Green Energy Twenty Five B Limited(Wind)_PSS9		20.72	0.00
99	Adani Green Energy Twenty Five B Limited_PSS-2		99.27	0.00
100	Adani Green Energy Twenty Four A Limited_PSS-3		65.74	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2025
EXCHANGES THROUGH POWER EXCHANGES -OCTOBER 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
101	Adani Green Energy Twenty Six B Limited_Hybrid Solar_PSS10		10.18	0.00
102	Adani Green Energy Twenty Six B Limited_Hybrid Wind_PSS10		24.64	0.00
103	Adani Green Energy Twenty Six B Limited_PSS-2		28.71	0.00
104	Adani Hybrid Energy Jaisalmer Five Limited_Solar_PSS8		7.20	0.00
105	Adani Hybrid Energy Jaisalmer Five Limited_Wind_PSS8		3.46	0.00
106	Adani Ports and Special Economic Zone Limited_PSS4_Wind		6.27	0.00
107	Adani Power Limited - Raigarh TPP		137.18	7.38
108	Adani Power Limited-Raipur TPP		138.59	3.17
109	Adani Renewable Energy Fifty Six Limited_PSS10		69.51	0.00
110	ArcelorMittal Nippon Steel India Private Limited		0.00	156.02
111	Ayana Renewable Power Four Private Limited_Hybrid_Solar		5.52	0.00
112	Ayana Renewable Power Four Private Limited_Solar		2.66	0.00
113	Ayana Renewable Power Four Private limited_Hybrid_WindPower		2.28	0.00
114	BHARAT ALUMINIUM COMPANY LTD		18.99	0.00
115	Blue Leaf Energy Renewables Private Limited_Hybrid_Solar		15.67	0.00
116	Blue Leaf Energy Renewables Private Limited_Hybrid_Wind		19.56	0.00
117	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		0.48	0.00
118	Chhattisgarh		143.47	3.10
119	D B Power Limited		51.77	0.57
120	DHARIWAL STU OTH		0.60	0.00
121	Daman and Diu - Dadra and Nagar Haveli		0.04	73.99
122	Dhariwal ISTS	पश्चिमी क्षेत्र WR	5.31	0.00
123	GMR Warora Energy Limited		4.85	0.00
124	Goa WR		20.27	1.00
125	Gujarat		22.73	1727.12
126	Jaypee Nigrie Super Thermal Power Plant		70.24	0.63
127	Jhabua Power Limited		2.03	0.63
128	Jindal Power Limited, Stage-1		211.23	0.60
129	Jindal Power Limited, Stage-2		396.97	26.42
130	Jindal Steel & Power Ltd , DCPP		62.45	2.59
131	KSK MAHANADI POWER COMPANY LIMITED		182.49	0.00
132	LANCO AMARKANTAK POWER LIMITED		4.62	0.00
133	MAHAN ENERGEN LIMITED U#1		70.54	0.00
134	MAHAN ENERGEN LIMITED U#2		81.96	1.84
135	MB POWER (MADHYA PRADESH) LIMITED		25.35	25.27
136	Madhya Pradesh		462.42	114.63
137	Maharashtra		104.37	780.36
138	Maruti Clean Coal and Power Limited		11.74	0.26
139	NTPC Gadarwara		19.55	0.00
140	NTPC Jhanor Gandhar GPS		0.00	1.11
141	NTPC Kawas GPS		0.00	0.73
142	NTPC Korba Stage I &II		47.84	0.00
143	NTPC Korba Stage III		12.36	0.00
144	NTPC Lara Stage I		28.12	0.00
145	NTPC Mouda Stage I		7.04	0.00
146	NTPC Mouda Stage II		9.81	0.00
147	NTPC SAIL POWER COMPANY LIMITED		1.02	0.00
148	NTPC SOLAPUR SOLAR PV Station		1.73	0.00
149	NTPC Sipat Stage I		43.50	0.00
150	NTPC Sipat Stage II		24.36	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2025
EXCHANGES THROUGH POWER EXCHANGES -OCTOBER 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
151	NTPC Solapur		4.35	0.00
152	NTPC Vindhyachal Stage I		16.17	0.00
153	NTPC Vindhyachal Stage II		12.38	0.00
154	NTPC Vindhyachal Stage III		12.39	0.00
155	NTPC Vindhyachal Stage IV		11.79	0.00
156	NTPC Vindhyachal Stage V		7.55	0.00
157	NTPC khargone		6.45	0.00
158	Nani Virani Wind Energy Private Limited		1.45	0.00
159	O2 RENEWABLE ENERGY III PRIVATE LIMITED(Teq green X1_merchant)		1.41	0.00
160	R.K.M POWERGEN PRIVATE LIMITED		1.93	0.00
161	RENEW GREEN (MHP ONE) PRIVATE LIMITED		19.99	0.00
162	RENEW GREEN (MHS ONE) PRIVATE LIMITED_SOLAR_HYBRID		1.36	0.00
163	RENEW GREEN (MHS ONE) PRIVATE LIMITED_WIND_HYBRID		6.03	0.00
164	RENEW GREEN (MHS THREE) PRIVATE LIMITED_HYBRID_SOLAR		19.95	0.00
165	RENEW GREEN (TN THREE) PRIVATE LIMITED		0.45	0.00
166	RENEW SURYA ROSHNI PRIVATE LIMITED Kallam PS		1.74	0.00
167	Ratnagiri Gas & Power Private Limited		0.00	3.53
168	SKS Power Generation Chhattisgarh Limited		31.95	0.53
169	Sasan Power Limited		71.17	0.00
170	TEQ GREEN POWER XI PRIVATE LIMITED_C&I(Hybrid_solar)		0.00	0.00
171	TEQ GREEN POWER XI PRIVATE LIMITED_C&I(Hybrid_wind)		2.61	0.00
172	TRN ENERGY PRIVATE LIMITED		21.25	0.00
173	The Tata Power Co Ltd (MTPS)		0.00	8.34
174	WIND FIVE RENERGY LIMITED		7.34	0.00
175	AM GREEN ENERGY PRIVATE LIMITED Solar		5.27	0.00
176	Andhra Pradesh		97.62	408.60
177	COASTAL ENERGEN PRIVATE LIMITED		13.48	1.32
178	GREENKO AP01 IREP PRIVATE LIMITED_INFIRM_Drawee		0.00	16.28
179	GREENKO AP01 IREP PRIVATE LIMITED_Infirm_Injectee		36.86	0.00
180	Goa SR		0.22	1.35
181	Greenko AP01 IREP Private Limited_Drawee		0.00	33.51
182	Greenko AP01 IREP Private Limited_Injectee		62.67	0.00
183	Greenko AP01 IREP Private Limited_Start UP		0.00	0.08
184	IL&FS TAMIL NADU POWER COMPANY LIMITED		0.75	0.00
185	JINDAL POWER LIMITED SIMHAPURI		11.01	2.64
186	KLEIO SOLAR POWER PRIVATE LIMITED (Solar)		16.14	0.00
187	KLEIO SOLAR POWER PRIVATE LIMITED (Wind)		18.89	0.00
188	Karnataka		237.84	106.59
189	Kerala		11.66	227.62
190	MEENAKSHI ENERGY LIMITED		0.85	161.50
191	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		2.45	0.00
192	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		3.55	0.00
193	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		3.19	0.00
194	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		5.36	0.00
195	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		7.94	0.00
196	NLC Tamilnadu Power Limited		11.46	0.00
197	NTECL VALLUR	दक्षिणी क्षेत्र SR	0.20	0.00
198	NTPC KUDGI		5.91	0.00
199	NTPC Ramagundam Stage I &II		1.42	0.00
200	NTPC Ramagundam Stage III		0.75	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2025
EXCHANGES THROUGH POWER EXCHANGES -OCTOBER 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
201	NTPC Simhadri Stage I		1.34	0.00
202	NTPC Simhadri Stage II		0.07	0.00
203	NTPC Talcher Super Thermal Power Station Stage II		14.18	0.00
204	NTPC Telangana		5.35	0.00
205	OSTRO KANNADA POWER PRIVATE LIMITED		11.03	0.00
206	Pondicherry UT		15.39	2.44
207	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		0.33	0.00
208	Ramagundam Floating solar		8.22	0.00
209	ReNew Surya Roshni Private Limited_Gadag		7.27	0.00
210	SEIL ENERGY INDIA LIMITED		10.04	0.00
211	SEIL Energy India Limited Project II		16.99	0.00
212	Serentica Renewables India 1 Private Limited		0.09	0.00
213	Serentica Renewables India 3 Private Limited (Wind)		7.75	0.00
214	Simhadri FSP 15 MW		1.42	0.00
215	Simhadri Floating solar (10 MW)		1.10	0.00
216	Sprng Akshaya Urja Private Limited		0.21	0.00
217	Tamil Nadu		519.44	568.16
218	Telangana		180.40	1101.83
219	Zenataris Renewable Energy Private Limited		5.07	0.00
220	ADHUNIK POWER & NATURAL RESOURCES LIMITED		2.10	0.00
221	Basochhu Hydropower Plant Bhutan		23.12	0.00
222	Bihar		712.67	40.35
223	Chuzachen HEP		0.04	0.00
224	Damodar Valley Corporation		12.95	272.52
225	Dikchu Hydro Electric Project (Sneha Kinetic Power Projects Pvt. Ltd.)		31.94	0.00
226	GMR KAMALANGA ENERGY LTD-CTU		19.82	0.00
227	JORETHANG LOOP HEP, DANS ENERGY PRIVATE LIMITED		0.10	0.00
228	JSW ENERGY (UTKAL) LIMITED		147.33	6.89
229	Jharkhand		82.88	52.13
230	Jindal India Power Limited		47.20	0.00
231	KALI GANDAKI NEPAL ELECTRICITY AUTHORITY		92.39	0.00
232	KANTI BIJLEE UTPADAN NIGAM LIMITED		4.68	0.00
233	Kabeli B-1 Hydro Power Project NEPAL ELECTRICITY AUTHORITY		0.66	0.00
234	LIKHU-iV NEA		36.08	0.00
235	Lower Modi Hydro Power Project NEPAL ELECTRICITY AUTHORITY		0.54	0.00
236	MAITHON POWER LIMITED		3.23	0.00
237	MARSYANGDI NEPAL ELECTRICITY AUTHORITY		47.73	0.00
238	NABINAGAR POWER GENERATING COMPANY LIMITED		31.42	0.00
239	NEA Nepal Upper Balephi A Hydropower Project1	पूर्वी क्षेत्र ER	0.96	0.00
240	NEA Nepal Upper Dordi A Hydropower Project		0.68	0.00
241	NEPAL ELECTRICITY AUTHORITY-MIDDLE MARSYANGDI		48.46	0.00
242	NTPC BARH Stage I		5.50	0.00
243	NTPC BARH Stage II		4.22	0.00
244	NTPC Darlipali		30.15	0.00
245	NTPC Farakka stage I		12.63	0.00
246	NTPC Farakka stage III		5.94	0.00
247	NTPC Kahalgaon stage I		4.31	0.00
248	NTPC Kahalgaon stage II		18.51	0.00
249	NTPC North Karanpura STPS		34.54	0.00
250	NTPC Talcher Stage I		20.29	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)

पावर एक्स्चेंज के माध्यम से विनिमय – माह:- अक्तूबर 2025
EXCHANGES THROUGH POWER EXCHANGES -OCTOBER 2025

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
251	NTPP BRBCL		3.85	0.00
252	Nikachhu Hydropower Project		13.92	0.00
253	Odisha		712.49	455.71
254	Rongnichu HEP		39.62	0.00
255	Sikkim		19.35	0.57
256	Solu Hydropower Project NEPAL ELECTRICITY AUTHORITY		16.07	0.00
257	Suchhu HEP		0.18	0.00
258	Tashiding HEP, Shiga Energy Private Limited		0.23	0.00
259	West Bengal		62.93	1198.21
260	AGARTALA GAS BASED POWER STATION	पूर्वोतर क्षेत्र NER	0.18	0.00
261	ASSAM GAS BASED POWER STATION		1.00	0.00
262	Arunachal Pradesh		32.62	0.64
263	Assam		137.55	59.24
264	Bongaigaon Thermal Power Station NTPC		5.28	0.00
265	KAMENG HYDRO POWER STATION		113.31	0.00
266	Manipur		1.90	26.83
267	Meghalaya		56.80	30.57
268	Mizoram		31.82	0.00
269	Nagaland		18.34	3.14
270	Palatana Plant		23.73	0.00
271	Tripura		3.56	37.63
	Total		**10342**	**10342**

19. अक्षय ऊर्जा प्रमाणपत्र तंत्र संबंधी विवरण

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

माह : अक्तूबर 2025

MONTH : OCTOBER 2025

नवीकरणीय स्रोत एवं इकाई-वार विवरण (01.10.2025-31.10.2025)

RE Source & Unit wise break up (01.10.2025-31.10.2025)

क्रमांक Sr.No	स्रोत-वार Source Wise	मान्यता Accreditation		पंजीकरण Registration	
		क्षमता (मेगावाट) Capacity (MW)	इकाई Unit	क्षमता (मेगावाट) Capacity (MW)	इकाई Unit
1	पवन Wind	106	8	158	6
2	शहरी या नगरपालिका अपशिष्ट Urban or Municipal Waste	0	0	0	0
3	सौर तापीय Solar Thermal	0	0	0	0
4	सौर पीवी Solar PV	25	1	0	0
5	लघु जलविद्युत Small Hydro	0	0	0	0
6	अन्य Others	0	0	0	0
7	भू-तापीय Geothermal	0	0	0	0
8	जैव ईंधन स्रोत Biomass	0	0	0	0
9	जैव ईंधन सह-उत्पादन Bio-fuel cogeneration	0	0	0	0
	कुल Total	**131**	**9**	**158**	**6**

01.10.2025 से 31.10.2025 के दौरान जारी किए गए अक्षय ऊर्जा प्रमाणपत्र
RECs Issued (01.10.2025-31.10.2025)

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	1252839		1252839

01.10.2025 से 31.10.2025 के दौरान अक्षय ऊर्जा प्रमाणपत्रों का मोचन
Redemption of REC (01.10.2025-31.10.2025)

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	2128063		21,28,063

19. अक्षय ऊर्जा प्रमाणपत्र तंत्र संबंधी विवरण

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

माह : अक्तूबर 2025

नवीकरणीय स्रोत एवं इकाई-वार विवरण (अप्रैल 2025 - मार्च 2026)
RE Source & Unit wise break up (Apr'25-Mar'26)

क्रमांक Sr.No	स्रोत-वार Source Wise	मान्यता Accreditation		पंजीकरण Registration	
		क्षमता (मेगावाट) Capacity (MW)	इकाई Unit	क्षमता (मेगावाट) Capacity (MW)	इकाई Unit
1	पवन Wind	470	15	457	22
2	शहरी या नगरपालिका अपशिष्ट Urban or Municipal Waste	0	0	0	0
3	सौर तापीय Solar Thermal	0	0	0	0
4	सौर पीवी Solar PV	4174	21	4388	15
5	लघु जलविद्युत Small Hydro	113	1	97	2
6	अन्य Others	0	0	0	0
7	भू-तापीय Geothermal	0	0	0	0
8	जैव ईंधन स्रोत Biomass	0	0	0	0
9	जैव ईंधन सह-उत्पादन Bio-fuel cogeneration	0	0	0	0
	कुल Total	**4757**	**37**	**4942**	**39**

अप्रैल 2025 - मार्च 2026 के दौरान जारी किए गए अक्षय ऊर्जा प्रमाणपत्र
RECs Issued (Apr'25-Mar'26)

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	26181598		2,61,81,598

अप्रैल 2025 - मार्च 2026 के दौरान अक्षय ऊर्जा प्रमाणपत्रों का मोचन
Redemption of REC (Apr'25-Mar'26)

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	29656068		2,96,56,068

19. अक्षय ऊर्जा प्रमाणपत्र तंत्र संबंधी विवरण

19. INFORMATION ABOUT RENEWABLE ENERGY CERTIFICATE MECHANISM

माह : अक्तूबर 2025

नवीकरणीय स्रोत एवं इकाई वार विवरण प्रारंभ से – अक्तूबर 2025
RE Source & Unit wise break up Since Inception to October'25

क्रमांक Sr.No	स्रोत-वार Source Wise	मान्यता Accreditation		पंजीकरण Registration	
		क्षमता (मेगावाट) Capacity (MW)	इकाई Unit	क्षमता (मेगावाट) Capacity (MW)	इकाई Unit
1	पवन Wind	3803	554	3519	547
2	शहरी या नगरपालिका अपशिष्ट Urban or Municipal Waste	12	1	12	1
3	सौर तापीय Solar Thermal	0	0	0	0
4	सौर पीवी Solar PV	9677	580	7100	515
5	लघु जलविद्युत Small Hydro	1653	52	1533	52
6	अन्य Others	5	2	3	1
7	भू-तापीय Geothermal	0	0	0	0
8	जैव ईंधन स्रोत Biomass	403	37	378	35
9	जैव ईंधन सह-उत्पादन Bio-fuel cogeneration	825	91	383	55
	कुल Total	**16378**	**1317**	**12928**	**1206**

प्रारंभ से अक्तूबर 2025 के दौरान जारी किए गए अक्षय ऊर्जा प्रमाणपत्र
RECs Issued since Inception to October'25

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	198485534		198485534

प्रारंभ से अक्तूबर 2025 के दौरान अक्षय ऊर्जा प्रमाणपत्रों का मोचन
Redemption of REC since Inception to Oct'25

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	154031364		15,40,31,364

अक्षय ऊर्जा प्रमाणपत्र का समापन शेष दिनांक 31.10.2025 तक
REC Closing balance as on 31.10.2025

Sr.No.	गैर-सौर Non Solar	सौर Solar	कुल Total
1	33316363		33316363

20. Important events/disturbances

Details of Grid Events during the Month of October 2025 in Northern Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Uttarakhand	02-10-2025 04:59	02-10-2025 05:39	00:40	196	55	0.454	0.090	43210	60986	i) 220KV Khodri(UK) and 220kV Chhibro(UK) generating station have 4 generating units each of 30MW and 60MW respectively and have double main bus scheme. ii) During antecedent condition, 30 MW Unit-1, 3 & 4 at Khodri(UK) were in running condition and were generating approx. 23 MW, 22 MW and 21 MW respectively. Also, 60 MW Unit-1, 2, 3 & 4 at Chhibro(UK) were in running condition and were generating approx. 45 MW, 43 MW and 42 MW respectively (as per SCADA) . iii) As reported, at 04:59 hrs, standby earth fault (51N) initiated on generator protection relays of 30 MW Unit-1, 3 & 4 at Khodri(UK) (exact reason, location and nature of fault yet to be shared) . iv) CB of Unit-3 opened correctly on standby earth fault protection operation. But Unit-1 and 4 experienced delayed opening of CB due to which LBB protection operated (as also confirmed from DR) . v) LBB protection issued tripping commands to all the 220kV feeders and 220/132 kV 100 MVA ICT at Khodri(UK) to isolate the fault and complete blackout occurred at 220kV Khodri(UK) . vi) On this fault, 220 KV Saharanpur(UP) - Saharanpur(PG) Ckt also tripped sensing the fault in zone-2 at Shaharanpur(UP) end with fault distance of 9.7 km (105.6%) from Shaharanpur(UP) . vii) Due to tripping of both 220 KV Khodri - Chhibro (UK) Ckt-1 & 2, 60 MW Unit-1, 2, 3 & 4 at Chhibro(UK) tripped on loss of evacuation path and complete blackout occurred 220kV Chhibro(UK) . viii) As per SCADA SOE, 132 KV Giri-KalaAmb (HP) Ckt also tripped during the same time (exact reason of tripping yet to be shared) . ix) As per PMU at Dehradun(PG) , Y-N phase to earth fault with fault clearing time of 440 ms was observed. x) As per SCADA, generation loss of approx. 196 MW and change in demand of approx. 55 MW was observed in Uttarakhand control area.	1) 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-1 2) 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 3) 220 KV Khodri - Chhibro (UK) Ckt-1 4) 220 KV Khodri - Chhibro (UK) Ckt-2 5) 220 KV Sarsawan(UP)-Khodri(UK) (UP) Ckt 6) 220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt 7) 220 KV Jhajra-Khodri (UK) Ckt 8) 220/132 kV 100 MVA ICT at Khodri(UK) 9) 30 MW Unit-1 at Khodri(UK) 10) 30 MW Unit-3 at Khodri(UK) 11) 30 MW Unit-4 at Khodri(UK) 12) 60 MW Unit-1 at Chhibro(UK) 13) 60 MW Unit-2 at Chhibro(UK) 14) 60 MW Unit-3 at Chhibro(UK) 15) 220 KV Saharanpur(UP)- Saharanpur(PG) Ckt
2	GD-1	Rajasthan	03-10-2025 12:53	03-10-2025 13:29	00:36	70	0	0.132	0.000	53228	65347	i) Generation of 220kV AHEJ4L PSS2 (ASPS2) (IP) station evacuates through 220 KV Adani Renew Park SL_FGARH_FBTL (AREPRL) -AHEJ4L PSS2 HB_FGRAH_FBTL (AHEJ4L) (AREPRL) Ckt which is further connected to 220/33 kV 150 MVA ICT 1, 2 & 3 at AHEJ4L PSS2 HB_FGRAH_FBTL (AHEJ4L) . ii) During antecedent condition, 220kV AHEJ4L PSS2 (ASPS2) (IP) station was generating approx. 70 MW (as per SCADA) . iii) As reported, at 12:53hrs, 220/33 kV 150 MVA ICT 1, 2 & 3 at AHEJ4L PSS2 HB_FGRAH_FBTL (AHEJ4L) tripped on over-flux protection operation (exact reason of tripping yet to be shared) which led to complete blackout out of 220kV AHEJ4L PSS2 (ASPS2) (IP) S/s. iv) As per PMU at Fatehgarh(IP) , no fault was observed in the system. v) As per SCADA, NR solar generation loss of approx. 70 MW was observed at AHEJ4L PSS2 (ASPS2) (IP) .	1) 220/33 kV 150 MVA ICT 1 at AHEJ4L PSS2 HB_FGRAH_FBTL (AHEJ4L) 2) 220/33 kV 150 MVA ICT 2 at AHEJ4L PSS2 HB_FGRAH_FBTL (AHEJ4L) 3) 220/33 kV 150 MVA ICT 3 at AHEJ4L PSS2 HB_FGRAH_FBTL (AHEJ4L)
3	GD-1	Uttarakhand	03-10-2025 19:00	03-10-2025 21:31	02:31	342	105	0.628	0.152	54420	69252	i) Power of 33*3MW Singoli Bhatwari HEP evacuates through 220 KV Singoli Bhatwari (Singoli(LTUHP)) (end) -Srinagar(UK) (PTCUL) Ckt-1 & 2. ii) During antecedent condition, 82.5 MW Unit-2, 3 & 4 at Alaknanda GVK (UPC) and 33MW unit-1, 2 & 3 at Singoli Bhatwari HEP were in running condition and generating approx. 85 MW, 83 MW, 84 MW, 35 MW, 28 MW and 27 MW respectively. 400 KV Alaknanda GVK(UPC) -Srinagar(UK) (UK) Ckt-2 was not in service. iii) As reported, at 19:00 hrs, 400 KV Alaknanda GVK(UPC) -Srinagar(UK) (UK) Ckt-1 tripped on Y-B-N double phase to earth fault with fault distance of 14.25 km from Alaknanda end. As per DR, fault current was Iy= ~5.45kA and Ib=~5.23kA from Alaknanda; fault sensed in Z-2 at Alaknanda end. 400/220 kV 315 MVA ICT 2 at Srinagar(UK) also tripped due to tripping of 400 KV Alaknanda GVK(UPC) -Srinagar(UK) (UK) Ckt-1. iv) During the same time, 82.5 MW Alaknanda GVK (UPC) Unit-2, 3 & 4 also tripped (exact reason and nature of protection operated yet to be shared) . v) As further reported, 220 KV Singoli Bhatwari(Singoli(LTUHP)) -Srinagar(UK) (PTCUL) Ckt-1 & 2 also tripped due to DT received at Singoli Bhatwari end (exact reason yet to be shared) . vi) Due to tripping of 220 KV Singoli Bhatwari(Singoli(LTUHP)) -Srinagar(UK) (PTCUL) Ckt-1 & 2, 33 MW Singoli Bhatwari(Singoli (LTUHP)) HPS - UNIT 1, 2 & 3 tripped due to unavailability of power evacuating path. As per DR, over-frequency protection operated at all three units of Singoli Bhatwari HEP. vii) Due to this event, complete blackout occurred at 220kV Singoli Bhatwari HEP(Singoli(LTUHP)) S/s. viii) As per PMU at Rishikesh(UP) , Y-B-N double phase to earth fault with fault clearance time of 120 ms is observed. ix) As per SCADA, change in demand of approx. 105 MW in Uttarakhand control area and generation loss of approx. 252 MW and 90 MW at Alaknanda HEP and Singoli Bhatwari HEP respectively were observed.	1) 400 KV Alaknanda GVK(UPC)-Srinagar(UK) (UK) Ckt-1 2) 400/220 kV 315 MVA ICT 2 at Srinagar(UK) 3) 82.5 MW Alaknanda GVK (UPC) Unit-2 4) 82.5 MW Alaknanda GVK (UPC) Unit-3 5) 82.5 MW Alaknanda GVK (UPC) Unit-4 6) 220 KV Singoli Bhatwari (Singoli(LTUHP)) (end)-Srinagar(UK) (PTCUL) Ckt-1 7) 220 KV Singoli Bhatwari (Singoli(LTUHP)) (end)-Srinagar(UK) (PTCUL) Ckt-2 8) 33 MW Singoli Bhatwari (Singoli(LTUHP)) HPS - UNIT 1 9) 33 MW Singoli Bhatwari (Singoli(LTUHP)) HPS - UNIT 2 10) 33 MW Singoli Bhatwari (Singoli(LTUHP)) HPS - UNIT 3
4	GD-1	Uttar Pradesh	08-10-2025 13:54	08-10-2025 15:17	01:23	250	0	0.522	0.000	47878	48006	i) Power of 82.5*4 MW Alaknanda HEP evacuates through 400 KV Alaknanda GVK (UPC) -Muzaffarnagar(UP) Ckt and 400 KV Alaknanda GVK(UPC) - Vishnuprayag(UP) (UP) Ckt. ii) During antecedent condition, 82.5 MW Unit-2, 3 & 4 at Alaknanda GVK (UPC) were in running condition and generating approx. 83 MW, 84 MW and 83 MW respectively. 400 KV Alaknanda GVK(UPC) - Vishnuprayag(UP) (UP) Ckt was already under emergency shutdown for re-adjustment of conductor sag and 82.5 MW Alaknanda GVK (UPC) Unit-1 was under shutdown due to low availability of water. iii) As reported, at 13:54 hrs, 400 KV Alaknanda GVK(UPC) - Muzaffarnagar (UP) Ckt tripped on B-N phase to earth fault with fault distance of 20.27 km from Alaknanda end. iv) As per DR, fault current was Ib= ~2.42kA from Alaknanda end and Ib=~3.37kA from Muzaffarnagar end; fault sensed in Z-1 at both ends; unsuccessful A/R was observed at both ends with different A/R dead time (~700ms at Muzaffarnagar end and ~1s at Alaknanda end) . v) Due to tripping of 400 KV Alaknanda GVK(UPC) - Muzaffarnagar (UP) Ckt, 82.5 MW Alaknanda GVK (UPC) Unit-2, 3 & 4 tripped due to loss of power evacuating path. vi) Due to this event, complete blackout occurred at 400kV Alaknanda GVK(UPC) S/s. vii) As per PMU at Muzaffarnagar(UP) , B-N phase to earth fault with unsuccessful A/R and fault clearance time of 80 ms is observed. viii) As per SCADA, generation loss of approx. 250 MW was observed at Alaknanda HEP.	1) 400 KV Alaknanda GVK(UPC)- Muzaffarnagar (UP) Ckt 2) 82.5 MW Alaknanda GVK (UPC) Unit-2 3) 82.5 MW Alaknanda GVK (UPC) Unit-3 4) 82.5 MW Alaknanda GVK (UPC) Unit-4

Details of Grid Events during the Month of October 2025 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
5	GI-1	Uttarakhand	08-10-2025 15:45	08-10-2025 16:02	00:17	105	0	0.213	0.000	49407	48229	i) During antecedent condition, 31.4 MW Tanakpur(NH) Unit-1, 2 & 3 were in running condition and generating approx. 35 MW, 36 MW and 34 MW respectively. ii) To attend to a hotspot in the 220kV Bus-2 isolator of the bus coupler bay at Tanakpur(NH) , shutdown of Bus-2 was required for which all elements connected to Bus-2 were being transferred to Bus-1. iii) As reported, 220 KV Tanakpur(NH) -Sitarganj(PG) (PG) Ckt was successfully transferred from Bus-2 to Bus-1. At 15:45 hrs, during the transfer of 31.4 MW Tanakpur(NH) Unit-2 from Bus-2 to Bus-1, busbar differential (zone-A) protection operated and tripped all elements connected to 220kV Bus-2 at Tanakpur(NH) . iv) As per DR, Busbar differential current of ~300A was present before the event (persisting Id alarm) which matched the load current of 220 KV Tanakpur(NH) -Sitarganj(PG) (PG) Ckt. After investigation, it was found that feedback status of the Bus-1 isolator for 220 KV Tanakpur(NH) -Sitarganj(PG) (PG) Ckt was missing. As a result, the relay treated the load current of ~300 A as differential current in all three phases as per existing relay configuration. v) Similarly, the feedback status of the Bus-2 isolator for Unit-2 was also missing. Hence, during the shifting of Unit-2 (carrying ~90 A) from Bus-2 to Bus-1, the differential current in all three phases increased to around 390 A which exceeded the permissible pickup threshold for the busbar protection relay, which was set at 360 A. vi) Due to the non-availability of the feedback status of the Bus-1 isolator and the Bus-2 isolator status being in the OFF condition for 220 KV Tanakpur(NH) -Sitarganj(PG) (PG) Ckt, the relay did not consider the line as an active element connected to Bus-1. Accordingly, as per the existing relay configuration, no trip command was initiated and the line didn't trip. Hence, though busbar differential (zone-A) protection operated, 220KV Bus-1 at Tanakpur(NH) remained charged through 220 KV Tanakpur(NH) -Sitarganj(PG) (PG) Ckt. vii) As per PMU at CB Ganj(UP) , no fault was observed in the system. viii) As per SCADA, generation loss of approx. 105 MW was observed at Tanakpur HEP(NH) . ix) As remedial action taken, the feedback status of bus isolators of 220 KV Tanakpur(NH) -Sitarganj(PG) (PG) Ckt & 31.4 MW Tanakpur(NH) Unit-2 has been rectified.	1) 220 KV Tanakpur(NH)-CBGanj(UP) (PG) Ckt 2) 132 KV Mahendra Nagar(NP)-Tanakpur(NH) (PG) Ckt 3) 31.4 MW Tanakpur(NH) Unit-1 4) 31.4 MW Tanakpur(NH) Unit-2 5) 31.4 MW Tanakpur(NH) Unit-3
6	GD-1	Rajasthan	15-10-2025 13:15	15-10-2025 15:17	02:02	282	0	0.525	0.000	53668	54101	i) Generation of 220kV AHEJ2L(IP) station evacuates through 220 KV Fatehgarh_II(PG) -AHEJ2L PSS HB_FGRAH_PG (AHEJ2L) (AHEJ2L) Ckt which is further connected to 220/33 kV 150 MVA ICT 1 & 2 at AHEJ2L(IP) . ii) During antecedent condition, 220kV AHEJ2L(IP) station was generating approx. 282 MW (as per PMU) . iii) As reported, at 13:15hrs, 220 KV Fatehgarh_II(PG) -AHEJ2L PSS HB_FGRAH_PG (AHEJ2L) (AHEJ2L) Ckt tripped on R-Y phase to phase fault (exact nature, location and reason of fault yet to be shared) which led to complete blackout out of 220kV AHEJ2L(IP) S/s. iv) As per PMU at Fatehgarh2(PG) , R-Y phase to phase fault was observed with fault clearing time of 120ms. Voltage dipped upto 0.788 pu during fault. v) As per PMU, solar generation loss of approx. 282 MW was observed at AHEJ2L(IP) .	1) 220 KV Fatehgarh_II(PG)-AHEJ2L PSS HB_FGRAH_PG (AHEJ2L) (AHEJ2L) Ckt
7	GD-1	Rajasthan	15-10-2025 12:11	15-10-2025 12:48	00:37	1855	0	3.378	0.000	54915	56880	i) Generation of 220kV Clean Solar Power Jodhpur (CSPJP) (IP) and 220kV Saurya Urja(IP) station evacuates respectively through 220 KV Bhadla(PG) -CS_Jodhpur SL_BHD_PG (CSPJP) (Cleansolar_Jodhpur) Ckt and 220 KV Bhadla(PG) -Saurya Urja Solar(SU) (Saurya Urja) Ckt-1 & 2. ii) During antecedent condition, 220kV Clean Solar Power Jodhpur (CSPJP) (IP) and 220kV Saurya Urja(IP) station were generating approx. 246 MW and 463 MW (Ckt-1 carrying 190 MW and Ckt-2 carrying 273 MW) respectively (as per PMU) . iii) As reported, at 12:11hrs, 220 KV Bhadla(PG) -CS_Jodhpur SL_BHD_PG (CSPJP) (Cleansolar_Jodhpur) Ckt tripped on Y-B Phase to phase fault due to snapping of jumper (exact location yet to be shared) . As per DR at Bhadla(PG) end, line differential protection operated in Main-2 relay with fault current of Iy=~28.22kA, Ib=~28.30kA from Bhadla(PG) end; fault sensed in zone-1 in main-1 relay; fault clearing time was ~56 ms. iv) During the same time, 220 KV Bhadla(PG) -Saurya Urja Solar(SU) (Saurya Urja) Ckt-2 also tripped from Saurya Urja(IP) end only (exact reason and nature of protection operated yet to be shared) . v) As per PMU at Bhadla(PG) , Y-B Phase to phase fault was observed with fault clearing time of ~120ms. Voltage dipped upto 0.775 pu. Frequency decreased from 50.023 Hz to 49.833 Hz (max change in frequency=~0.19 Hz) . vi) As per PMU at CSPJP(IP) and Saurya Urja(IP) , solar generation loss of approx. 246 MW and 273 MW were observed at CSPJP(IP) and Saurya Urja(IP) respectively. vii) As per SCADA, change in NR total Solar generation of approx. 1855 MW was observed among which dip in Rajasthan solar generation was approx. 295 MW.	1) 220 KV Bhadla(PG)-CS_Jodhpur SL_BHD_PG (CSPJP) (Cleansolar_Jodhpur) Ckt 2) 220 KV Bhadla(PG)-Saurya Urja Solar(SU) (Saurya Urja) Ckt-2
8	GD-1	Uttar Pradesh	15-10-2025 11:58	15-10-2025 12:08	00:10	0	230	0.000	0.400	54865	57521	i) 220/132kV Nehtaur(UP) S/s has main and transfer bus scheme at both 220kV and 132kV level. During antecedent condition, 220 KV Amroha- Morabadbad Ckt had already tripped (at 10:30 Hrs) , hence no supply feed was present from 220 KV Amroha. ii) As reported, at 11:58 hrs, Y-N fault appeared in 220 KV Meerut(PG) -Nehtaur(UP) (UP) Ckt and line auto-reclosed successfully. But Y-N phase to earth fault again appeared within reclaim time and finally the line tripped. As per DR at Nehtaur(UP) , fault current was 1.8kA and fault distance was 22.7km (31.0 %) from Nehtaur(UP) end; zone-1 distance protection operated at Nehtaur(UP) end. iii) As no supply feed was present from 220 KV Amroha, supply fail occurred at 220/132kV Nehtaur(UP) . 220 KV Amroha-Nehtaur (UP) Ckt was hand tripped for safety purpose and complete blackout occurred at 220/132kV Nehtaur(UP) S/s. iv) As per PMU at Meerut(PG) , three consecutive Y-N, R-N and Y-N Phase to earth faults were observed with fault clearing time of 120 ms each. v) As per SCADA, change in demand of approx. 230 MW was observed in UP control area.	1) 220 KV Meerut(PG)-Nehtaur(UP) (UP) Ckt 2) 220 KV Amroha-Nehtaur (UP) Ckt
9	GI-1	Uttarakhand	18-10-2025 12:09	18-10-2025 13:09	01:00	0	65	0.000	0.111	56489	58823	i) 220KV Khodri(UK) generating station have 4 generating units each of 30MW and have double main bus scheme. ii) During antecedent condition, only 30 MW Unit-3 at Khodri(UK) was in running condition and was generating approx. 22 MW (as per SCADA) . iii) As reported, at 12:09 hrs, during the synchronisation of 30 MW Unit-2 at Khodri(UK) , restricted earth fault protection of UAT operated (exact reason, location and nature of fault yet to be shared) . However, due to delayed opening of CB of Unit-2, LBB protection operated. iv) LBB protection issued tripping commands to 220 KV Khodri(UK) -Majri(HP) (UK) Ckt-2, 220 KV Khodri - Chhibro (UK) Ckt-2, 220 KV Saharanpur(UP) -Khodri(UK) (UP) Ckt and 220/132 kV 100 MVA ICT at Khodri(UK) to isolate the fault. v) As per PMU at Saharanpur(PG) , three phase to earth fault with fault clearing time of 280 ms was observed. vi) As per SCADA, change in demand of approx. 65 MW was observed in Uttarakhand control area.	1) 220 KV Khodri(UK)-Majri(HP) (UK) Ckt-2 2) 220 KV Khodri - Chhibro (UK) Ckt-2 3) 220 KV Saharanpur(UP)-Khodri(UK) (UP) Ckt 4) 220/132 kV 100 MVA ICT at Khodri(UK)

Details of Grid Events during the Month of October 2025 in Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
10	GI-2	Uttar Pradesh	21-10-2025 19:16	21-10-2025 20:03	00:47	0	109	0.000	0.221	42847	49218	i) 400/220kV Agra(UP) S/s has double main and transfer bus scheme at both 400kV & 220kV level and double bus scheme at 132kV level. During antecedent condition, 400/220kV 500MVA ICT-2, 315 MVA ICT-3, 220kV feeder to IOCL-I, Agra220kV-I, Gokul-I & 220/132kV ICT-6 were connected to 220kV Bus-1 and rest of the elements were connected to 220kV Bus-2 at Agra(UP) . ii) As reported, at 19:16 hrs, R & Y phase CT of 220kV Agra-IOCL line-1 at Agra end damaged. Distance protection at Agra end operated in Z-1 however, due to delay in decay of complete fault current, LBB protection operated. Current more than 200 Amp persisted for more than 200msec. iii) Due to LBB protection operation, all the elements connected to 220kV Bus-1 i.e., 400/220kV 500MVA ICT-2, 315 MVA ICT-3, 220kV feeder to IOCL-I, Agra220kV-I, Gokul-I & 220/132kV ICT-6 at Agra(UP) tripped. iv) At the same time, due to tripping of 500 MVA ICT-2 and 315 MVA ICT-3, case-5 of SPS of transformers at Agra(UP) operated. 220kV feeder to Agra220kV-II, IOCL-II and 132kV feeders to Foundry Nagar, Sadabad, Agra Taj, Dayalbagh-I & Bhimnagri tripped on SPS operation. 220kV feeder to Shamsabad and Mitai didn't trip on SPS. During inspection, it was found that CB status of both the feeders was not showing in SPS system. v) Further, at 19:16:16 hrs, 400/220kV 500 MVA ICT-1 at Agra(UP) also tripped on differential protection operation. As reported, no fault was found during inspection. vi) As per PMU at Agra765(PG) , R-N & Y-N fault at 19:16:14 hrs with delayed clearance of ~200 msec followed by R-N fault at 19:16:16 hrs is observed. vii) As per SCADA change in demand of ~100 MW is observed in UP control area.	1) 220kV Agra-IOCL line-I 2) 220kV Bus-1 at Agra(UP) 3) 400/220kV 500 MVA ICT-2 at Agra(UP) 4) 400/220kV 315 MVA ICT-3 at Agra(UP) 5) 220kV Agra-Agra220kV line-I 6) 220kV Agra-Gokul line 7) 220/132kV 160 MVA ICT-6 at Agra(UP) 8) 220kV Agra-Agra220kV line-II 9) 220kV Agra-IOCL line-II 10) 400/220kV 500 MVA ICT-1 at Agra(UP)
11	GD-1	Punjab	29-10-2025 14:59	29-10-2025 15:18	00:19	590	35	1.313	0.069	44939	51069	i) 220/132kV GGSTPS (Ropar TPS) has 3 main bus and 1 reserve bus. During antecedent condition, 220kV Bus-I&II were already under shutdown for ongoing construction work in switchyard. 220kV feeders to Ghulal, Jadla-I&II, Ropar400-I&III, Khara, 210 MW Unit-3 & 6, ST-3 & 4 and 100MVA ICT-1&2 were connected to 220kV Reserve bus and remaining feeders and 210 MW Unit-4 & 5 were connected to 220kV Bus-2. 210 MW Unit-1&2 were under shutdown and 220kV Gobindgarh-I feeder was also taken under shutdown to attend air leakage from the compressor. ii) During antecedent condition, 210 MW Unit-3,4,5&6 at GGSTPS were running and generating ~146 MW, ~147 MW, ~142 MW & ~153 MW respectively. iii) As reported, at 14:59 hrs, while hanging earth stick on 220kV Gobindgarh-I feeder, the earth stick inadvertently got induction voltage from the nearby live feeder of Interlinking 220/132kV 100MVA Transformer-2 and created bus fault. iv) On this fault, bus bar protection of 220kV Reserve bus (bus bar Z-4) operated leading to tripping of all the elements connected to 220kV Reserve bus. v) At the same time, 210 MW Unit-4 & 5 which were connected to 220kV Bus-3 also tripped due to tripping of allied auxiliaries running on ST-3 and ST-4. vi) As per PMU at Nallagarh(PG) , R-N fault which cleared within 100msec is observed. vii) As per SCADA change in demand of approx. 35 MW in Punjab control area and generation loss of approx. 590 MW at GGSTPS (Ropar TPS) is observed.	1) 220kV Reserve Bus (Bus-4) at GGSTPS(PS) 2) 220kV GGSTPS-Ghulal (PS) line 3) 220kV GGSTPS-Jadla (PS) line-I 4) 220kV GGSTPS-Jadla (PS) line-II 5) 220kV GGSTPS-Kharar (PS) line-I 6) 220kV GGSTPS- Ropar400 (PS) line-I 7) 220kV GGSTPS- Ropar400 (PS) line-III 8) 220/132kV 100 MVA ICT-1 at GGSTPS (PS) 9) 220/132kV 100 MVA ICT-2 at GGSTPS (PS) 10) 210 MW GGSTPS (Ropar) - UNIT 3 11) 210 MW GGSTPS (Ropar) - UNIT 6 12) 220kV ST-3 13) 220kV ST-4 14) 210 MW GGSTPS (Ropar) - UNIT 4 15) 210 MW GGSTPS (Ropar) - UNIT 5
12	GI-2	Punjab	30-10-2025 12:58	30-10-2025 14:17	01:19	0	245	0.000	0.479	44554	51164	i) 400/220kV Ludhiana(PG) has one & half breaker scheme at 400kV level and double main & transfer bus scheme at 220kV level. ii) During antecedent condition, 400/220kV ICT-1, 2, 3 & 4 were carrying ~181 MW, 169 MW, 111 MW & 168 MW respectively. iii) As reported, at 12:58 hrs, flashover occurred in R & Y phase bus isolators of 206 bay (ICT-4 bay) . This happened during onload operation of 86B isolator of 206 bay (ICT-4 bay) . iv) On this fault bus bar protection of both the 220kV Bus-1&2 operated leading to tripping of all the elements connected to 220kV bus-1&2 at Ludhiana(PG) . v) From the event logger record, it was observed that prior to BB tripping, condition of Zone Merge was formed which has resulted in extending tripping in both Busbars. At 12:49:51:149, DC earth fault in source-1 is observed in event list. vi) As per PMU at Ludhiana(PG) , R-Y double phase fault which cleared within 120msec is observed. vii) As per SCADA change in demand of approx. 245 MW in Punjab control area is observed. viii) As a precautionary measure, AC & DC supply of all 220kV isolators has been kept OFF. Further investigation is under progress. Suspected cause of tripping is currently attributable to 206 Schnieder make BCU i.e., maloperation of BO card)	1) 220kV Bus-1 at Ludhiana(PG) 2) 220kV Bus-1 at Ludhiana(PG) 3) 400/220kV 500 MVA ICT-1 at Ludhiana(PG) 4) 400/220kV 500 MVA ICT-2 at Ludhiana(PG) 5) 400/220kV 315 MVA ICT-3 at Ludhiana(PG) 6) 400/220kV 500 MVA ICT-4 at Ludhiana(PG) 7) 220kV Ludhiana(PG)-Laltokalan line-I 8) 220kV Ludhiana(PG)-Laltokalan line-II 9) 220kV Ludhiana(PG)-Sahnewal line-I 10) 220kV Ludhiana(PG)-Sahnewal line-II 11) 220kV Ludhiana(PG)-Dandhari line-II 12) 220kV Ludhiana(PG)-Jagraon line 13) 220kV Ludhiana(PG)-Doraha line 14) 220kV Ludhiana(PG)-Pakhowal line
13	GI-2	Haryana	31-10-2025 06:02	31-10-2025 07:12	01:10	0	440	0.000	0.962	34273	45736	i) 400/220kV Daulatabad(HR) has one & half breaker scheme at 400kV level and double main bus scheme at 220kV level. ii) During antecedent condition, 400/220kV ICT-1, 2, 3 & 4 were carrying 83 MW, 82 MW, 82 MW & 84 MW respectively. iii) As reported, at 06:02 hrs, B-ph CT of 220kV bus coupler burst resulting into 220kV bus fault. iv) As bus bar protection was not in working condition due to issue in cables, bus bar protection didn't operate and fault cleared with the tripping of all four 400/220kV 315 MVA ICTs at Daulatabad(HR) . v) As per PMU at Gurgaon(PG) , B-N fault with delayed clearance of 660 msec is observed. vi) As per SCADA change in demand of approx. 440 MW in Haryana control area is observed. vii) As reported by Daulatabad(HR) , issues with the bus bar protection has already been taken up with the relay OEM.	1) 400/220kV 315 MVA ICT-1 at Daulatabad(HR) 2) 400/220kV 315 MVA ICT-2 at Daulatabad(HR) 3) 400/220kV 315 MVA ICT-3 at Daulatabad(HR) 4) 400/220kV 315 MVA ICT-4 at Daulatabad(HR)

Details of Grid Events during the Month of October 2025 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	02-10-2025 16:45	02-10-2025 18:21	01:36	145	-	0.26%	-	55554	50705	Complete outage of 220 kV Baranda S/S:At 16:45Hrs/02-10-2025, 220kV Bhuj- Baranda(Avikiran) S/c tripped on R-E fault. Generation loss of around 145 MW occurred due to loss of evacuation path.	1. 220 kV Baranda-Bhuj S/C
2	GI-1	WR	06-10-2025 11:10	06-10-2025 13:02	01:52	254	-	0.41%	-	62411	56138	Complete outage of 220 kV SSP(CHPH) S/S:At 11:11 hrs / 06-10-2025, 220 kV SSP(CHPH)-SSP(RBPH)1&2 tripped on B-E differential protection operation. 220kV SSP(CHPH)-Unit-1,2,3,4&5 tripped due to loss of evacuation path. Generation loss of around 254 MW occurred at SSP Hydro Power Plant during the event.	1 220 kV SSP(CHPH)-SSP(RBPH)-1 2 220 kV SSP(CHPH)-SSP(RBPH)-2 3 400/220 kV SSP(RBPH)-ICT-1 4 400/220 kV SSP(RBPH)- ICT-2 5 SSP(CHPH)-Unit-1 (50 MW) 6 SSP(CHPH)-Unit-2 (50 MW) 7 SSP(CHPH)-Unit-3 (50 MW) 8 SSP(CHPH)-Unit-4 (50 MW) 9 SSP(CHPH)-Unit-5 (50 MW)
3	GD-1	WR	07-10-2025 16:14	07-10-2025 19:21	03:07	528	-	0.77%	-	68298	58573	Complete outage of 220 kV KhavdaPSS13 S/S: At 16:14 hrs / 07-10-2025, 400 kV Khavda-PSS13–Khavda-PS1-1 tripped due to false DT signal sent from Khavda-PSS13. On inspection it was found that the DT signal triggered by a faulty control cable at Khavda-PSS13. Generation loss of 528 MW Occurred at Khavda-PSS13 (Adani) Wind Power Plant due to loss of evacuation path.	1 400 kV Khavda-PSS13–Khavda-PS1-
4	GD-1	WR	08-10-2025 11:13	08-10-2025 13:41	02:28	-	-	-	-	63239	54793	Complete outage of 220 kV Baranda S/S: At 11:13 Hrs/ 08-10-2025, 220 kV Baranda-Bhuj S/C tripped on B-E fault during auto recloser reclaim time. As seen from PMU plot, 220 kV Baranda-Bhuj S/C A/R successfully at 11:13:43 Hrs. As informed by ASIPL, No Generation at the time of tripping.	1. 220 kV Bhuj-Baranda
5	GI-1	WR	09-10-2025 17:37	09-10-2025 18:06	00:29	9	58	0.01%	0.09%	71131	63500	Partial outage of 220 kV Halkarni S/S: At 17:37 Hrs/ 09-10-2025, Both 220kV Mumewadi–Halkarni Line-I and Line-II tripped on distance protection operation. The Line-I tripped from Halkarni end, while Auto Reclose (A/R) was successful at Mumewadi end. The Line-II tripped from Mumewadi end with A/R lockout, and no tripping was observed at Halkarni end. These trippings resulted in zero power in 220kV Halkarni-Mahalaxmi & 220kV Halkarni-Tillari lines, 220kV Mahalaxmi-Amona & 220kV Tillari-Amona lines. Stormy weather with lightning reported at the time of event. Due to above event, Generation loss of 9 MW occurred at Maharashtra & Load loss of 13 MW & 45 MW occurred in Maharashtra and Goa respectively.	1 220kV Halkarni-Mumewadi-1 2 220kV Halkarni-Mumewadi-2
6	GD-1	WR	09-10-2025 21:02	10-10-2025 00:07	03:05	-	200	-	0.33%	67679	59738	Partial outage of 220kV Siltara S/S: At 21:02 Hrs/ 09-10-2025, 220 kV Siltara Bus bar protection operated due to B-E fault suspected due to lightning strike & 220 kV Siltara s/s went into dark (220 kV Single Main & Transfer Bus scheme) along with associated 132KV Substations (132 KV Kachna, 132 KV Siltara Phase 2, 132 KV Maindirhasusad & 132 KV Kuhera). As reported by SLDC CG, load loss of 200 MW occurred.	1 220 kV Siltara-JNIL 2 220 kV Siltara- Raipur(PG) 3 220 kV Siltara- Raita 4 220 kV Siltara- Urla 5 220 kV Siltara- Dardehi 6 220/132 kV 160 MVA Siltara ICT 1 7 220/132 kV 160 MVA Siltara ICT 2 8 220/132 kV 160 MVA Siltara ICT 3
7	GD-1	WR	13-10-2025 23:26	14-10-2025 13:22	13:56	153.4	-	0.24%	-	65253	57141	Complete outage of 220 kV Tuljapur S/S: At 23:36 hrs/13-10-2025, the 400 kV Tuljapur-Konhali line tripped due to 87L protection relay general pickup operated at Tuljapur. Line is holding from Konhali. This resulted in a generation loss of approximately 30 MW due to loss of the evacuation path.	1 400kV Tuljapur-Konhali line-1 2 200 MVA 400/33kV Tuljapur ICT-1

Details of Grid Events during the Month of October 2025 in Western Region

Sl No.	Category of Grid Event (GI 1or GI 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD-1	WR	16-10-2025 21:39	17-10-2025 01:12	03:33	-	-	-	-	68278	59632	Complete outage of 220 kV Baranda S/S: At 21:39 hrs/16-10-2025, 220KV Baranda-Bhuj line tripped in B Phase to Earth fault. Foreign material string was found on B phase at tower no. AP -06 during patrolling. No Generation loss occurred at Avikiran Baranda due to the event.	1. 220 kV Bhuj-Baranda-1
9	GI-2	WR	19-10-2025 00:26	19-10-2025 02:44	02:18	15	-	0.02%	-	63968	56547	Partial outage of 400 kV Khavda PS2 S/S: At 26:57 Hrs/19.10.2025, 765/400 kV Khavda PS2 ICT 4 tripped on Differential (B-E fault) protection operation. • At 00:27:01 Hrs, 220 kV Dedhiya Bus coupler tripped on Over Voltage protection operation. Due to Bus coupler tripping, 220/33 kV Dedhiya ICT 2 along with 220 kV Dedhiya Bus 1 became dead. Tripping of 220 kV Dedhiya Bus coupler on Over Voltage protection operation is undesirable and settings needs to be reviewed. • At 00:27:02 Hrs (after 5 seconds of 765/400 kV Khavda PS2 ICT 4 tripping), 765 kV Bhuj- Khavda PS1 ckt 2 & 765 kV Lakadiya- Ahmedabad 1 (anti-theft charged from Lakadiya end upto 56 km) tripped on Over Voltage Stage I protection operation at Khavda PS1 & Lakadiya ends respectively. • As seen from PMU plot, Voltage of 765 kV Bhuj- Khavda PS1 ckt 2 at Khavda PS1 end increased from 782 kV to 828 kV (108%) and resulted in Over Voltage protection operation and receipt of DT at Bhuj end. Generation loss of 15 MW occurred at 220 kV Dedhiya WPP due to Bus coupler tripping.	1 765/400 kV Khavda PS2 ICT 4 2 765 kV Bhuj- Khavda PS1 ckt 2 3 765 kV Lakadiya- Ahmedabad 1 4 220 kV Dehdiya Bus coupler 5 220 kV Dehdiya Bus 1 6 220/33 kV Dedhiya ICT 2
10	GD-1	WR	20-10-2025 21:51	21-10-2025 04:15	06:24	1.2	-	0.00%	-	54407	47271	Complete outage of 220 kV Gadsisa S/S: At 21:51 Hrs/20-10-2025, 220kV Bhuj–Gadhsisa line tripped due to B phase to ground fault (CT jumper opened at Bhuj end), fault current- 23.8KA, 1.01 km from Bhuj end.	1 220kV Bhuj-Gadhsisa S/C 2 220kV Gadhsisa Bus-1 3 220kV Gadhsisa Bus-2 4 220/33 kV 160MVA Gadhsisa ICT-1
11	GD-1	WR	21-10-2025 03:58	21-10-2025 04:29	00:31	-	-	-	-	51637	44133	Partial outage of 400 kV Nicol S/S: At 03:58 hrs/21-10-2025, The 400 kV PIRANA–NICOL-II–1 and 400 kV RANCHODPURA–NICOL-II–1 lines tripped on overvoltage. Subsequently, for load changeover at Nicol, the 400/132 kV ICTs were manually opened by the station, resulting in the 400 kV bus at Nicol becoming dead.	1 400 kV PIRANA–NICOL-II–1 2 400 kV RANCHODPURA–NICOL-II–1 3 400/132 KV ICT 1 4 400/132 KV ICT 2 5 400/132 KV ICT 3
12	GI-2	WR	21-10-2025 20:03	21-10-2025 21:14	01:11	726	-	1.11%	-	65530	52355	Partial outage of 400 kV Chandrapur S/S: 1. At 20:03 hrs. Disturbance occurred in Chandrapur, Dhariwal & Bhadrawati: Y phase IPS tube (bus isolator to CB) of 400 kV Chandrapur-II-Chandrapur Switching ckt-2 fell down at Chandrapur II end and created Y-E fault. As the fault was not cleared by primary protection (600 ms delay observed), multiple lines connected to 400kV Chandrapur-II tripped from the respective remote ends on Zone 2 DPR operation. 2. During this event at Bhadrawati HVDC, three AC lines on the west side tripped due to overvoltage (464kV as per PMU). The auxiliary supply was disturbed, resulting in tripping of both HVDC poles. 3. Chandrapur Unit 8 & 9 (500 MW each), Dhariwal Units 1 & 2 (300 MW each) tripped. With the tripping of units, multiple lines at Chandrapur & Dhariwal tripped on Over Voltage protection operation. 4. 400kV Chandrapur switching station has become dead due to tripping of respective lines and units. 5. Generation loss of 1150 MW occurred in Maharashtra control area and No load loss reported.	1 400 kV-Chandrapur-Chandrapur-II-1 & 2 2 400 kV-Chandrapur II-Bus-1 3 400 kV Dhariwal-Chandrapur-II-1 & 2 4 400 kV Dhariwal-Parli(PG)-1 5 400 kV Chandrapur-II-Warora-1 & 2 6 400 kV Bhadrawati-Raipur-1 & 3 7 400 kV Bhadrawati-Chandrapur-II-1 8 400 kV Bhadrawati-GMR Warora-1 9 400 kV Bhilai-Bhadrawati-1 10 400 kV Chandrapur-II-Nanded-1 & 2 11 400 kV Chandrapur-Khaperkheda-1 12 400 kV Chandrapur-Parli line 13 HVDC-Bhadrawati-Pole-1 & 2 14 Chandrapur Unit 8 & 9 (500 MW each) 15 Dhariwal Unit 1 &2 (300 MW each)
13	GD-1	WR	22-10-2025 23:17	28-10-2025 01:00	121:43	37	-	0.06%	-	59438	48866	Complete outage of 220 kV Gadsisa S/S: At 23:17 Hrs/22-10 2025, 220kV Bhuj–Gadhsisa line tripped due to B phase to ground fault. Indications at Gadsisa end, 31 km, 0.8 kA. At Bhuj end, 38.7 km, 4.94 kA. Generation loss of 37 MW occurred due to loss of evacuation. After patrolling, tower collapse is observed in tower no. 21/4 and 21/5.	1. 220kV Bhuj-Gadhsisa S/C 2. 220kV Gadhsisa Bus-1 3. 220kV Gadhsisa Bus-2 4. 220/33 kV 160MVA Gadhsisa ICT-1
14	GD-1	WR	29-10-2025 04:41	29-10-2025 06:58	02:17	18	-	0.03%	-	55579	46822	Complete outage of 220 kV Teq Green S/S: At 04:41 Hrs/29-10-2025, 220kV Kallam–TEQ_GREEN line tripped due to B phase to ground fault. Generation loss of 18 MW occurred due to loss of evacuation path.	1 220kV Kallam–TEQ_GREEN

Details of Grid Events during the Month of October 2025 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD - 1	KARNATAKA	03-10-2025 15:55	03-10-2025 16:09	00:14	0	208	0.0 %	0.0 %	48620.7	54371.57	Complete outage of 220kV TATAGUNI, KIADB-HAROHALLI and KANKAPURA and Tripping of Bus-A1 of SOMANAHALLI station. The triggering incident is the Y-G bus fault occurred in Somanahally-Harohally line bay due to failure of Y phase cross bus insulator string before the CT of the line (can be confirmed from the DR of Somanahally-Harohally line at Somanahally). Since the BBP is in disabled condition and BBP protection in not available, multiple lines tripped on Z4 and 500MVA Somanahally ICT-1 tripped on OC protection operation and led to the Complete outage of KIADB-HAROHALLI and KANKAPURA station. The even led to the Complete outage of 220kV TATAGUNI, KIADB-HAROHALLI and KANKAPURA and Tripping of Bus-A1 of SOMANAHALLI station.	220KV-HAROHALLI-SOMANAHALLI-1, 220KV-TATAGUNI-SOMANAHALLI-1, 220KV-SOMANAHALLI-ELECTRONIC_CITY-1, 400KV/220KV SOMANAHALLI-ICT-1, 220KV-TATAGUNI-VRISHABHAVATHI_VALLEY-1
2	GD - 1	KARNATAKA	04-10-2025 08:49	04-10-2025 09:50	01:01	0	460	0.0 %	0.01 %	43534.31	51544.15	Tripping of 220kV Mylasandra Bus-2 of 400kV Mylasandra SS, Complete Outage of 220kV Koramangala, 220kV Nimhans, 220kV Nagnathapura.of KPTCL. During antecedent conditions, 220kV Koramangala, 220kV Nimhans, 220kV Nagnathapura were being radially fed from 220kV Mylasandra Bu-2. As per the reports submitted, the triggering incident was the operation of the bus zone gas trip in LCC (86ZT2) due to spurious initiation from one of the bus-side gas density monitors, suspected to be caused by DC grounding in the 220 kV Bus-2 of the 400 kV Mylasandra SS. Immediately, all elements connected to the 220 kV Bus-2 tripped. This led to loss of power supply to 220kV Mylasandra Bus-2 which in turn led to loss of power supply to 220kV Koramangala, 220kV Nimhans, 220kV Nagnathapura.	MYLASANDRA - 220KV - Bus 2, 220KV-HSR-MYLASANDRA-2, 220KV-MYLASANDRA-HSR-1, 220KV-NAGNATHPURA-MYLASANDRA-2, 400KV/220KV MYLASANDRA-ICT-1, 400KV/220KV MYLASANDRA-ICT-2, 400KV/220KV MYLASANDRA-ICT-3
3	GD - 1	PRADESH , TA	04-10-2025 19:29	04-10-2025 20:32	01:03	0	200	0.0 %	0.0 %	43079.69	47892.73	Complete Outage of 230kV ARS, Kamachi, Cauvery, Thervoi Kandigai, Mychelin, Suryadev and Gummidipoondi SS 230kV ARS, Kamachi, Cauvery, Thervoi Kandigai, Mychelin, Suryadev were radially connected to Gummidipoondi. The triggering incident is the Y-B fault in 230kV NCTPS-Gummidipoondi line and 110kV connected line tripped after around 29s and due to which 230kV Sullurpet-Gummidipoondi also tripped due to wrong bus CVT selection. With the tripping of both 230kV NCTPS-Gummidipoondi and 230kV Sullurpet-Gummidipoondi lines led to the complete outage of 230kV ARS, Kamachi, Cauvery, Thervoi Kandigai, Mychelin, Suryadev and Gummidipoondi SS.	220KV-SULURPET-GUMMIDIPOONDI-1, 230KV-GUMMIDIPOONDI-NCTPS-1
4	GD - 1	TAMILNADU	06-10-2025 11:02	06-10-2025 11:22	00:20	415	60	0.01 %	0.0 %	49711.64	51529.41	Complete Outage of 230kV Tondiarpet SS, 230kV Athipattu SS of TANTRANSCO and 230kv NCTPS Generating station of TNPGL As per the reports submitted, the triggering incident was R-N fault in 230kV NCTPS Tondiarpet Line-2. At NCTPS end, the fault was sensed in zone-2 and carrier was received. At Thondiarpet end, the fault was sensed in zone-1. However, the breaker failed to open making LBB to operate. Immediately all elements to 230kV Bus tripped leading to complete outage of 230kV Tondiarpet SS. Subsequently, other 230kV lines connected to 230kV NCTPS tripped on different faults. Tripping of all these lines led to running of NCTPS Units on house load of 38MW. Since, 230kV Athipattu was being radially fed from 230kV NCTPS, loss of power supply to 230kV NCTPS led to complete outage of 230kV Athipattu SS.	230KV-GUMMIDIPOONDI-NCTPS-1, 230KV-NCTPS-KILPAUK-1, 230KV-NCTPS-SRIPERUMBADUR_TN-1, 230KV-NCTPS-TONDIARPET-2, 230KV-BASIN_BRIDGE-TONDIARPET-1, 230KV-NCTPS-TONDIARPET-1, 230KV-BASIN_BRIDGE-TONDIARPET-1, 230KV-ETPS-TONDIARPET-1
5	GD - 1	ANDHRA PRADESH , TAMILNADU	06-10-2025 12:24	06-10-2025 12:50	00:26	0	175	0.0 %	0.0 %	48495.78	51245.31	Complete Outage of 230kV ARS, Kamachi, Cauvery, Thervoi Kandigai, Mychelin, Suryadev and Gummidipoondi SS In the antecedent conditions, ARS, Kamachi, Cauvery, Thervoi Kandigai, Mychelin, Suryadev were radially connected to Gummidipoondi and is radially being fed from 230kV Sullurpet-Gummidipoondi. The triggering incident is the B-G fault in the line. Tripping of the only line connected to Gummidipoondi led to the Complete Outage of 230kV ARS, Kamachi, Cauvery, Thervoi Kandigai, Mychelin, Suryadev and Gummidipoondi SS	220KV-SULURPET-GUMMIDIPOONDI-1
6	GD - 1	TAMILNADU	08-10-2025 12:12	08-10-2025 13:35	01:23	0	0	0.0 %	0.0 %	50049.75	55153.73	Complete Outage of 230kV Karur_JSW_Dharapuram_2, TP Vardaman and Tripping of 230kV Bus-1 &2 at Karur PS JSW_Dharapuram_1, JSW_Dharapuram_2 and TP Vardaman are radially connected to Karur PS which is inturn connected to 400kV via 400/230kV ICT-1&2 Karur PS. In the antecedent conditions 230kV Karur_JSW_Dharapuram_1 was under shutdown and 400/230kV Karur PS ICT-2 was under shut down condition. The triggering incident is the R-B phase Bus fault (as per PMU) in Bus-1 due to human error (as per user FIR) leading to Bus-1 BBP operation and tripping of all the elements connected to Bus-1 including the Bus Coupler. Bus-2 did not have any evacuation led tripping the Bus-2 at Karur PS. This led to the Complete Outage of Karur_JSW_Dharapuram_2, TP Vardaman and Tripping of 220kV Bus-1 &2 at Karur PS.	230KV-KARUR_PS-KARUR_JSW_Dharapuram_1-2, KARUR_JSW_Dharapuram_1 - 230KV
7	GD - 1	ANDHRA PRADESH , TELANGANA	08-10-2025 21:36	08-10-2025 21:46	00:10	0	15	0.0 %	0.0 %	41202.15	48443.41	Complete Outage of 220kV Chalakurthy SS, 220kV Puttamgandi SS, 220kV Puliyantanda SS of TGTRANSCO 220V PuliyantandaSS and 220kV Puttamgandi SS are being radially fed from 220kV Chalakurthy SS. 220kV Chalakurthy SS is operating with Single bus configuration. As per the reports submitted, the triggering incident was R-N fault in 220kV Chalakurthy KM Palli Line-1 while charging the line from Chalakurthy end due to R-phase discs flashover and conductor fallen on Y-phase cross arm in the line. At Chalakurthy end, the fault was sensed in zone-1 & SOTF operated and the line tripped. At the same time, 220kV Chalakurthy BB operated on suspected CT saturation in 220kV Chalakurthy KM Palli Line-1. All elements connected to 220kV Chalakurthy Bus tripped leading complete outage of 220kV Chalakurthy SS which inturn led to complete outage of 220kV Puliyantanda SS and 220kV Puttamgandi SS.	220KV-CHALAKURTHY-KONDAMALLEPALLY-1, 220KV-NAGARJUNASAGAR_AP-CHALAKURTHY-1, 220KV-CHALAKURTHY-KONDAMALLEPALLY-2, 220KV-CHALAKURTHY-PULIYATHANDA-1, 220KV-CHALAKURTHY-PUTTAMGANDI-1

Details of Grid Events during the Month of October 2025 in Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD - 1	KARNATAKA	12-10-2025 13:13	12-10-2025 13:30	00:17	0	85	0.0 %	0.0 %	47811.27	45128.47	Complete Outage of 220kV Ranebennur SS of KPTCL During antecedent conditions, 220kV Ranebennur Shiralkoppa line was under open condition and 220kV Ranebenur SS was being radially fed from 220kV Guttur SS. As per the reports submitted, the triggering incident was B-N fault in 220kV Guttur Ranebennur line and the line tripped. Tripping of the only connected line led to complete outage of 220kV Ranebennur SS.	220KV-GUTTUR-RANEBENNUR-1, 400KV/220KV GUTTUR-ICT-1
9	GD - 1	KERALA	16-10-2025 14:18	16-10-2025 14:28	00:10	0	140	0.0 %	0.0 %	46590.58	50017.13	Complete Outage of 220kV Orkattery SS, 220kV Kanhirode SS, 220kV Thalaserry SS, 220kV Taliparamba SS, 220kV Ambalathara SS and 220kV Mylatty SS of KSEB 220kV Orkattery SS, 220kV Kanhirode SS, 220kV Thalaserry SS, 220kV Taliparamba SS, 220kV Ambalathara SS, 220kV Mylatty SS are being radially fed from 220kV Areakode Orkattery line and 220kV Areakode Kanhirode lines. As per the reports submitted, the triggering incident was YN fault in 220kV Areakode Orkattery line . A/R operated and the line was holding. Subsequently, YB-N fault was observed in 220kV Areakode Orkattery line and 220kV Areakode Kanhirode lines tripped. Tripping of both connected lines led to complete outage of radial connected stations.	220KV-KANHIRODE-ORKKATTERY-1, 220KV-AREACODE-KANHIRODE-1
10	GD - 1	TAMILNADU	17-10-2025 03:31	17-10-2025 04:05	00:34	0	0	0.0 %	0.0 %	35792.89	39889.71	Complete Outage of 400kV Thappukundu SS of TANTRANSCO During antecedent conditions, 400kV Thappukundu SS was being radially fed through 400kV Thappukundu Anaikadavu Line-1. As per the reports submitted, the triggering incident was RY fault in 400kV Thappukundu Anaikadavu Line1 and the line tripped. Tripping of the only connected line led to complete outage of 400kV Thappukundu SS	400KV-ANAIKADAVU-THAPPUKUNDU-1
11	GD - 1	TAMILNADU	17-10-2025 04:47	17-10-2025 11:49	07:02	0	0	0.0 %	0.0 %	36550.92	41246.46	Complete Outage of 400kV Thappukundu SS of TANTRANSCO During antecedent conditions, 400kV Thappukundu SS was being radially fed through 400kV Thappukundu Anaikadavu Line-1. As per the reports submitted, the triggering incident was RY fault in 400kV Thappukundu Anaikadavu Line-1 and the line tripped. Tripping of the only connected line led to complete outage of 400kV Thappukundu SS	400KV-ANAIKADAVU-THAPPUKUNDU-2
12	GD - 1	KARNATAKA	18-10-2025 17:12	18-10-2025 17:24	00:12	560	495	0.01 %	0.01 %	42463.57	48762.76	Complete Outage 400kV UPCL Generating Station of Adani, 220kV Kavoor SS, 220kV Kemar SS, 220kV Puttur SS and 220kV MSEZ SS of KPTCL . As per the reports submitted, 400kV UPCL Hebbanahalli Line-1&2 tripped on B-N fault at 16:27hrs. Subsequently, 220kV Kemar Varahi Line-1&2 tripped on YB-N fault at 17:09hrs and 220kV Kemar Heggunje line tripped on RYB-N fault at 17:13hrs. Tripping of all these lines led to complete outage of 400kV UPCL Generating Station, 220kV Kavoor SS, 220kV Kemar SS, 220kV Puttur SS and 220kV MSEZ SS	400KV-HEBBANAHALLI-UPCL-1, UPCL - UNIT 1, UPCL - UNIT 2, 400KV-HEBBANAHALLI-UPCL-2, 220KV-HEGGUNJE-KEMAR-3, 220KV-VARAHI-KEMAR-1, 220KV-VARAHI-KEMAR-2
13	GD - 1	KARNATAKA , KERALA	19-10-2025 17:14	19-10-2025 17:24	00:10	0	60	0.0 %	0.0 %	37833.51	40211.17	Complete Outage of 220kV Kaniyampetta SS of KSEB During antecedent conditions, 220kV Kaniyampetta Kunnamangalam was under outage. 220kV Kaniyampetta SS was being radially fed from 220kV Kunnamangalam Kadakola line. As per the reports submitted, the triggering incident was Y-G fault in 220kV Kunnamangalam Kadakola line and the line tripped. Tripping of the only connected line led to complete outage of 220kV Kaniyampetta SS	220KV-KADAKOLA-KANIYAMPETTA
14	GD - 1	KERALA	19-10-2025 19:31	19-10-2025 19:55	00:24	0	43	0.0 %	0.0 %	39054.77	41579.27	Complete Outage of 220kV Kaniyampetta SS of KSEB During antecedent conditions, 220kV Kaniyampetta Kadakola was under outage. 220kV Kaniyampetta SS was being radially fed from 220kV Kunnamangalam Kaniyampetta line. As per the reports submitted, the triggering incident was YB-G fault in 220kV Kunnamangalam Kaniyampetta line and the line tripped. Tripping of the only connected line led to complete outage of 220kV Kaniyampetta SS	220KV-KANIYAMPETTA-KUNAMANGALAM-1
15	GD - 1	ANDHRA PRADESH	21-10-2025 02:53	21-10-2025 04:03	01:10	0	0	0.0 %	0.0 %	29493.62	31832.8	Complete Outage 220kV Naidupeta of APTRANSCO 220V Naidupeta SS was being radially from 220kV Rachagunneri Naidupeta Line-1&2\. As per the reports submitted, the triggering incident was B-N fault in 220kV Rachagunneri Naidupeta Line-2 at 02:46hrs At both ends, the fault was sensed in zone-1. A/R operated and the line tripped on persistent fault. At the same time, the same fault was sensed in zone-1 and R-pole opened at Naidupeta end in 220kV Rachagunneri Naidupeta Line-1. After around 1.5seconds other two poles opened on suspected PD relay. Tripping of both lines at Naidupeta end led to complete outage of 220kV Naidupeta SS.	220KV-RACHAGUNNERI-NAIDUPETA-1, 220KV-RACHAGUNNERI-NAIDUPETA-2, NAIDUPETA - 220KV
16	GD - 1	ANDHRA PRADESH	22-10-2025 00:30	22-10-2025 01:58	01:28	0	0	0.0 %	0.0 %	31563.17	33341.99	Complete Outage of 220kV Peddapuram SS of APTRANSCO As per the reports submitted, the triggering incident was failure in CT in 220kV Peddapuram Relaince Line-1 at 220kv Peddapuram SS. The scattered parts of CT caused Y-N fault in 220kV Bus-1 and B-N fault in 220kV Bus-2. Both Bus-1 and Bus-2 BBP operated causing complete outage of 220kV Peddapuram SS.	PEDDAPURAM - 220KV, 220KV-PEDDAPURAM-RELIANCE-2, 220KV-PEDDAPURAM-RELIANCE-1, 220KV-VEMAGIRI_AP-PEDDAPURAM-2, 220KV-BOMMUR-PEDDAPURAM-1, 220KV-VEMAGIRI_AP-PEDDAPURAM-1, 220KV-KAKINADA-PEDDAPURAM-1
17	GD - 1	ANDHRA PRADESH	25-10-2025 17:10	25-10-2025 17:57	00:47	0	0	0.0 %	0.0 %	39331.0	43468.23	Complete Outage of 220kV Setipali SS of APTRANSCO As per the reports submitted, the triggering incident was CT cable issue in 220kV Setipali RTSS Veludurthy feeder causing BBP to maloperate at 220kV Setipali end. Immediately all elements connected to 220kV Bus tripped. Since 220kV Setipali is operating with SIngle bus configuration this led to complete outage of 220kV Setipali SS.	SETIPALI - 220KV, 220KV-KRISHNAGIRI-SETIPALI-1, 220KV-KRISHNAGIRI-SETIPALI-2
18	GD - 1	ANDHRA PRADESH	29-10-2025 00:55	29-10-2025 01:40	00:45	0	20	0.0 %	0.0 %	35582.96	32251.75	Complete Outage of 220kV Markapur SS of APTRANSCO As per the reports submitted, the triggering incident was B-N fault in 220kV Srisailam RB Markapur Line-1. At Markapur end, breaker failed to open causing LBB to operate. All elements connected to 220kV Markapur Bus tripped . This led to complete outage of 220kV Markapur SS.	220KV-SRISAILAM_RIGHT_BANK-MARKAPUR-1, MARKAPUR - 220KV

Details of Grid Events during the Month of October 2025 in Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	IBTPS(OPTCL)	21.10.2025 17:25	21.10.2025 18:08	00:43	176	0	0.58%	0.00%	30142	25587	Prior to the disturbance IBTPS unit #2 was generating around 176 MW (Unit #1 was under outage condition) evacuating through 220kV IBTPS-Budhipadar 1,2,3 & 4 line. At 17:25 hrs., 220 kV IBTPS–Budhipadar 1, 2, 3 & 4 lines tripped on Z-4 protection due to puncture of B-phase Bus-1 side isolator of 220 kV IBTPS–Budhipadar-4 line at Budhipadar end. Consequently, 220kV IBTPS became dead and generation loss of 176 MW reported at IBTPS.	220KV-IBTPS-BUDHIPADAR- 1 220KV-IBTPS-BUDHIPADAR- 2 220KV-IBTPS-BUDHIPADAR- 3 220KV-IBTPS-BUDHIPADAR- 4 IB TPS UNIT -2
2	GD-1	CHATRA(JUSNL)	23.10.2025 18:22	23.10.2025 19:15	00:53	0	95	0.00%	0.35%	34636	27082	Prior to the disturbance, 220 kV Chatra S/s of Jharkhand Power System was connected with rest of ER grid through 220kV Chatra-Daltongunj line and 220kV Chatra-Latehar line. At 18:22 Hrs, 220kV Chatra-Latehar line tripped on Y-B-Earth fault, simultaneously 220kV Chatra-Daltongunj line also got tripped from Daltongunj end. Consequently, 220kV Chatra S/s became dead, resulting in a load loss of 95 MW at Chatra S/s. Power supply was restored through the 220kV Chatra-Daltongunj line at 19:15 Hrs.	220kV Latehar-Chatra line 220kV Daltongunj-Chatra line
3	GD-1	KESINGA(OPTCL)	29.10.2025 16:42	29.10.2025 17:08	00:26	0	70	0.00%	0.32%	27843	21867	Prior to the disturbance 220kV Kesinga connected through 220kV Bolangir New (OPTCL) and 220kV Bolangir(PG) S/s. At 16:42 Hrs a Y-B-Earth fault occurred in 132kV Kesinga-Saintala feeder which was not cleared from Kesinga end due to faulty trip coil. Fault persisted for around 1.8 seconds and was cleared by tripping of 220 kV Bolangir (PG)-Kesinga line and 220 kV Bolangir (New)-Kesinga line. Consequently, 220/132 kV Kesinga S/s became dead. Total load loss of 70 MW reported in Kesinga S/s.	220 kV Bolangir (PG)-Kesinga line 220 kV Bolangir (New)-Kesinga line

Details of Grid Events during the Month of October 2025 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Kohima, Zhadima & Chiephbozou areas of Nagaland Power System and Karong area of Manipur power system	02-10-2025 22:09	02-10-2025 22:55	00:46	21	20	0.69%	0.77%	3043	2582	Kohima, Zhadima & Chiephbozou areas of Nagaland Power System were connected with rest of NER Grid through 132kV Kohima-Karong line. (132 kV Dimapur – Kohima line under tripped condition since 17:14 Hrs of 02-10-2025 & 132 kV Wokha – Chiephobozou lines were in tripped condition since 13:26 Hrs of 30-09-2025). Karong area of Manipur power system was connected with the rest of the NER Grid through 132 kV Karong-Kohima line and 132 kV Yurembam – Karong line. At 22:09 Hrs of 02-10-2025, 132 kV Karong-Kohima and 132 kV Yurembam – Karong lines tripped. Due to tripping of these line, Kohima, Zhadima & Chiephbozou areas of Nagaland Power and Karong area of Manipur power system were isolated from NER Grid. Power supply was restored to Karong and Kohima areas by charging 132 kV Imphal-Karong line at 22:25 hrs & 132 kV Karong-Kohima line at 22:55 hrs of 02-10-2025.	132 kV Karong-Kohima and 132 kV Yurembam – Karong lines
2	GD I	Along area of Arunachal Pradesh power system	03-10-2025 11:05	03-10-2025 11:20	00:15	0	5	0.00%	3.88%	2434	2422	Along area of Arunachal Pradesh Power System was connected with rest of NER Grid through 132 kV Along-Pasighat line. 132 kV Along-Basar was under planned shutdown since 25-08-2025 due to which Along area was radially fed from pasighat end. At 11:05 Hrs of 03-10-2025, 132 kV Along-Pasighat line tripped. Due to tripping of this element, Along area of Arunachal Pradesh Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Along area by charging 132 kV Along –Pasighat line at 11:20 Hrs of 03-10-2025.	132 kV Along-Pasighat line
3	GD I	Leshka HEP of Meghalaya Power System	05-10-2025 13:27	05-10-2025 14:01	00:34	114	0	4.03%	0.00%	2826	2311	Leshka HEP of Meghalaya Power System was connected with rest of NER Grid via 132 kV Mynkre-Leshka D/C lines. At 13:27 Hrs of 05-10-2025, grid disturbance occurred at 132 kV Leshka HEP due to tripping of 132 kV Leshka-Mynkre D/C lines.	132 kV Leshka-Mynkre D/C lines
4	GD I	Dimapur(NA) area of Nagaland Power System	06-10-2025 06:44	06-10-2025 09:46	03:02	0	78	0.00%	3.55%	2795	2198	Dimapur area of Nagaland Power System was connected with rest of NER Grid through 132 kV Dimapur (PG)-Dimapur(NA) D/C lines. At 06:44 hrs of 06.10.2025, 132 kV Dimapur (PG)-Dimapur D/C lines tripped resulting in grid disturbance at Dimapur(Nagarjan) area of Nagaland Power System. Power supply was restored to Dimapur(Nagarjan) area by charging 132 kV Dimapur (PG)-Dimapur D/C line at 09:46 hrs of 06-10-2025.	132 kV Dimapur (PG)-Dimapur D/C lines
5	GD I	Tuirial HEP of NEEPCO Power System	07-10-2025 10:53	07-10-2025 11:01	00:08	0	58	0.00%	2.25%	2351	2578	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 10:53 Hrs of 07.10.2025, 132 kV Tuirial - Kolasib line tripped due to which Tuirial HEP of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 11:01 Hrs of 07.10.2025.	132 kV Tuirial - Kolasib line
6	GD I	Tuirial HEP of NEEPCO Power System	08-10-2025 00:23	08-10-2025 00:41	00:18	0	58	0.00%	2.15%	2720	2694	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 00:23 Hrs of 08.10.2025, 132 kV Tuirial - Kolasib line tripped due to which Tuirial HEP of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 00:41 Hrs of 08.10.2025.	132 kV Tuirial - Kolasib line
7	GD I	Sanis & Wokha areas of Nagaland power system	08-10-2025 14:20	08-10-2025 14:57:00 (Sanis) 08-10-2025 17:46:00 (Wokha)	37 min (Sanis) 3 Hr 26 min (Wokha)	0	3	0.00%	0.11%	2457	2687	Sanis and Wokha areas of Nagaland Power System are connected with rest of NER Grid through 132kV Chiephbozou-Wokha line and 132kV Doyang-Sanis line. At 14:20 Hrs of 08-10-2025, 132 kV Doyang-Sanis line and 132kV Sanis-Wokha line tripped. Due to tripping of these lines, Sanis and Wokha areas of Nagaland Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Sanis by energizing the 132kV Doyang–Sanis line at 14:57 hrs on 08-10-2025. Subsequently, power supply to Wokha was restored at 17:46 hrs on 08-10-2025 by charging the 132kV Sanis–Wokha line, following line patrolling and the removal of a broken tree branch that had fallen on the line.	132 kV Doyang-Sanis line and 132kV Sanis-Wokha line

Details of Grid Events during the Month of October 2025 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD I	Kohima, Meluri, Zhadima, Chiephbozou areas & LHEP generating station of Nagaland Power System & Karong area of Manipur power system	08-10-2025 21:32	08-10-2025 23:30	01:58	19	25	0.63%	0.80%	2993	3121	Kohima, Meluri, Zhadima, Chiephbozou areas & LHEP generating station of Nagaland Power System were connected with rest of NER Grid through 132kV Kohima-Karong line. (132 kV Wokha – Chiephobozou & 132 kV Dimapur-Kohima lines were in tripped condition) At 21:32 hrs of 08-10-2025, 132 kV Yurembam-Karong line tripped. And due to tripping of this line, Kohima, Meluri, Zhadima, Chiephbozou areas & LHEP generating station of Nagaland Power and Karong area of Manipur power system were isolated from NER Grid. Power supply was extended to Karong and Kohima areas by charging 132 kV Imphal (MA)-Karong line at 22:43 hrs. However, The Imphal (MA)- Karong TL tripped again at 22:47 hrs while charging of 132 kV Dimapur (PG)-Kohima TL. The 132 kV Dimapur (PG)-Kohima TL is found faulty. Finally, Power supply is restored to Karong and Kohima areas by charging of 132 kV Imphal (MA)-Karong line at 23:14 hrs & 132 kV Karong-Kohima line at 23:30 hrs of 08-10-2025.	132 kV Yurembam-Karong line
9	GD I	Rengpang area of Manipur Power System	10-10-2025 11:14	10-10-2025 21:34	10:20	0	1	3.07%	0.04%	2479	2624	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132kV Loktak Rengpang line. The 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 11:14 Hrs of 10-10-2025, 132kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 21:34 Hrs of 10-10-2025.	132kV Loktak - Rengpang line
10	GD I	Lekhi area of Arunachal Pradesh power system	10-10-2025 17:08	11-10-2025 22:04	28:56	0	17	0.00%	0.54%	2784	3166	Lekhi area of Arunachal Power System was connected with rest of NER Grid through 132kV Panyor-Lekhi, 132kV Nirjuli-Lekhi and 132kV Chimpu-Lekhi lines. 132 kV Lekhi - Chimpu line was under long outage since 06:11 Hrs of 30.05.2025. At 17:09 Hrs of 10-10-2025, 132kV Panyor-Lekhi and 132kV Nirjuli-Lekhi lines tripped. Due to tripping of these lines, Lekhi area of Arunachal Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Lekhi area by energizing the 132kV Nirjuli-Lekhi line at 22:04 hrs on 11-10-2025.	132kV Panyor-Lekhi and 132kV Nirjuli-Lekhi lines
11	GD I	Tipaimukh area of Manipur Power System	10-10-2025 21:01	10-10-2025 22:03	01:02	0	1	0.00%	1.03%	3071	3195	Tipaimukh area of Manipur Power System was connected with rest of NER Grid through 132 kV Aizawl - Tipaimukh Line and 132 kV Jiribam - Tipaimukh Line. At 21:01 Hrs of 10-10-2025, 132 kV Aizawl - Tipaimukh Line and 132 kV Jiribam - Tipaimukh Line tripped. Due to tripping of this element, Tipaimukh area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Tipaimukh area by charging 132 kV Aizawl-Tipaimukh line at 22:03 Hrs of 10-10-2025.	132 kV Aizawl - Tipaimukh Line and 132 kV Jiribam - Tipaimukh Line
12	GD I	Tuirial HEP of NEEPCO Power System	14-10-2025 05:47	14-10-2025 05:56	00:09	58	0	2.24%	0.00%	2589	2353	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 05:47 Hrs of 14.10.2025, 132 kV Tuirial - Kolasib line tripped due to which Tuirial HEP of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 05:56 Hrs of 14.10.2025.	132 kV Tuirial - Kolasib line
13	GD I	Tuirial HEP of NEEPCO Power System	14-10-2025 07:34	14-10-2025 07:39	00:05	58	0	2.27%	0.00%	2554	2492	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 07:34 Hrs of 14.10.2025, 132 kV Tuirial - Kolasib line tripped due to which Tuirial HEP of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 07:39 Hrs of 14.10.2025.	132 kV Tuirial - Kolasib line
14	GD I	Tuirial HEP of NEEPCO Power System	14-10-2025 08:09	14-10-2025 08:24	00:15	0	0	0.00%	0.00%	2439	2452	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 08:09 Hrs of 14.10.2025, 132 kV Tuirial - Kolasib line tripped due to which Tuirial HEP of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 08:24 Hrs of 14.10.2025.	132 kV Tuirial - Kolasib line

Details of Grid Events during the Month of October 2025 in North Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
15	GD I	Rangia, Nalbari, Nathkuchi, part load of Bornagar, part load Shishugram, Tangla, Amingaon, Kamalpur and Hajo areas of Assam Power System	14-10-2025 13:01	14-10-2025 13:21	00:20	0	191	0.00%	7.19%	2370	2658	Rangia S/S, Nalbari, Nathkuchi, part load of Bornagar, part load Shishugram, Tangla, Amingaon, Kamalpur and Hajo areas of Assam Power System were connected with rest of the NER Grid by 220kV BTPS- Rangia line 2. Prior to the event, 220 kV BTPS-Rangia ckt 1 was under planned shutdown. At 13:01 Hrs of 14-10-2025, 220 kV BTPS- Rangia line 2 tripped. Consequently, 132 kV Rangia - Rangia I & II, 132 kV Rangia-Kamalpur I & II and 132 kV Rangia – Tangla lines tripped due to SPS operation. As a result, 220kV Rangia S/S, Nalbari, Nathkuchi, part load of Bornagar, part load Shishugram, Tangla, Amingaon, Kamalpur and Hajo areas of Assam Power System got isolated from NER Grid and collapsed due to no source available in these areas. Power supply was extended to 220 kV Rangia S/S, Nalbari, Nathkuchi, part load of Bornagar, part load Shishugram, Sipajhar, Tangla, Amingaon, Kamalpur and Hajo areas of Assam Power System by charging 220kV BTPS- Rangia II at 13:21 Hrs of 14.10.2025.	220 kV BTPS- Rangia line 2
16	GD I	Umrangsho area of Assam power system	14-10-2025 17:08	14-10-2025 17:44	00:36	0	1.37	0.00%	0.04%	2849	3244	Umrangsho area of Assam Power System was connected with rest of NER Grid through 132 kV Haflong-Umrangsho & 132 kV-Khandong-Umrangsho lines. At 17:08 hrs of 14.10.2025, 132 kV Haflong-Umrangsho & 132 kV-Khandong-Umrangsho lines tripped resulting in grid disturbance at Umrangsho area of Assam Power System. Power supply was extended to Umrangsho area of Assam Power System by charging 132 kV Haflong-Umrangsho & 132 kV-Khandong-Umrangsho lines at 17:44 hrs of 14.10.2025.	132 kV Haflong-Umrangsho & 132 kV-Khandong-Umrangsho lines
17	GD I	Karong area of Manipur Power System	16-10-2025 14:30	16-10-2025 15:08	00:38	0	1	0.00%	0.03%	2313	2901	Karong area of Manipur Power System is connected to the rest of NER Grid via 132 kV Kohima–Karong line. Prior to the event, 132 kV Gamphajol-Karong line was under outage since 19:33 Hrs of 10.10.2025. At 14:30 Hrs of 16-10-2025, 132 kV Kohima–Karong line tripped. Due to tripping of this element, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Karong area by charging 132 kV Kohima-Karong line at 15:08 Hrs of 16-10-2025.	132 kV Kohima–Karong line
18	GD I	Rengpang area of Manipur Power System	16-10-2025 13:58	16-10-2025 16:48	02:50	0	39	0.00%	1.36%	2357	2859	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132kV Loktak Rengpang line. The 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 13:58 Hrs of 16-10-2025, 132kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 16:48 Hrs of 16-10-2025.	132kV Loktak - Rengpang line
19	GD I	Tuirial HEP of NEEPCO Power System	17-10-2025 19:04	18-10-2025 11:33	16:29	58	0	1.74%	0.00%	3327	3613	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 19:04 Hrs of 17.10.2025, 132 kV Tuirial - Kolasib line tripped due to which Tuirial HEP of Mizoram Power System was isolated from NER Grid and collapsed due to loss of evacuation path. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 11:33 Hrs of 18.10.2025.	132 kV Tuirial - Kolasib line
20	GD I	Tuirial HEP of NEEPCO Power System	23-10-2025 02:17	23-10-2025 11:22	09:05	58	0	2.54%	0.00%	2287	2372	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 02:17 Hrs of 23-10-2025, 132 kV Kolasib – Turial line tripped resulted into grid disturbance in Turial HEP due to load-generation mismatch in this area. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 11:22 Hrs of 23.10.2025.	132 kV Kolasib – Turial line
21	GD I	Rengpang area of Manipur Power System	23-10-2025 13:04	23-10-2025 15:42	02:38	0	1	0.00%	0.04%	2076	2679	Rengpang area of Manipur Power System was connected with rest of NER Grid through 132kV Loktak Rengpang line. The 132kV-Jiribam-Rengpang line was under long outage since 18:18 Hrs of 17.11.2023. At 13:04 Hrs of 23-10-2025, 132 kV Loktak - Rengpang line tripped. Due to tripping of this element, Rengpang area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Rengpang area by charging 132 kV Loktak-Rengpang line at 15:42 Hrs of 23-10-2025.	132 kV Loktak - Rengpang line
22	GD I	Tuirial HEP of NEEPCO Power System	23-10-2025 13:08	23-10-2025 13:16	00:08	58	0	2.88%	0.00%	2013	2692	Tuirial HEP of Mizoram Power System was connected NER Power system via 132 kV Tuirial - Kolasib line. At 13:08 Hrs of 23-10-2025, 132 kV Kolasib – Turial line tripped resulted into grid disturbance in Turial HEP due to load-generation mismatch in this area. Power was extended to Tuirial area by charging 132 kV Tuirial - Kolasib line at 13:16 Hrs of 23.10.2025.	132 kV Kolasib – Turial line

21. NEW ELEMENTS CHARGED IN OCTOBER 2025

GENERATING UNITS

REGION	S. NO.	Location	Owner/Unit Name	Unit No/Source	Capacity added (MW)	Total/Installed Capacity (MW)	DATE
WR	1	220/33 kV ARP4PL Devsar	Ayana Renewable Power Four Private Limited (ARP4PL)	Wind	6.6	92.4/150	24.10.2025
	2	400/33 kV AGEL Khavda PSS-5	Adani Hybrid Energy Jaisalmer Five Limited (AHEJ5L) PSS5	Wind	31.2	526.2/772.8	14.10.2025
	3	400/33 kV AGEL Khavda PSS-5	Adani Hybrid Energy Jaisalmer Five Limited (AHEJ5L) PSS5	Wind	72.8	599/772.8	16.10.2025
	4	400/33 kV GIPCL Khavda PSS-1	Gujarat Industries Power Company Limited (GIPCL)	Solar	123.2	369.6/600	09.10.2025
	5	400/33 kV NTPC REL Khavda PSS-2	NTPC REL Khavda PSS2	Solar	53.04	937/1555	01.10.2025
	6	400/33 kV NTPC REL Khavda PSS-2	NTPC REL Khavda PSS2	Solar	70.72	1008/1555	06.10.2025
	7	220/33 kV Gahtnandur RSRPL	Renew Surya Roshni Private Limited (RSRPL)	Wind	16.5	115.5/300	08.10.2025
	8	220/33 kV Patoda RGMOPL	Renew Green (MHP One) Private Limited RGMOPL	Wind	13.2	128.7/148.5	17.10.2025
	9	400/33 kV AGEL Khavda PSS-5	Adani Hybrid Energy Jaisalmer Five Limited (AHEJ5L) PSS5	Solar	75	674/772.8	28.10.2025
	10	400/33 kV SRPL Khavda PSS-10	Adani Renewable Energy Fifty Six Limited (ARE56L) PSS10	Solar	75	500/500	28.10.2025
	11	400/33 kV AGEL Khavda PSS-8	Adani Renewable Energy Forty One Limited (ARE41L) PSS8	Wind	5.2	130/130	28.10.2025
	12	400/33 kV AGEL Khavda PSS-8	Adani Hybrid Energy Jaisalmer Five Limited (AHEJ5L) PSS8	Wind	10.4	41.6/67.6	28.10.2025
	13	400/33 kV AGEL Khavda PSS-8	Adani Hybrid Energy Jaisalmer Five Limited (AHEJ5L) PSS8	Wind	20.8	62.4/67.6	28.10.2025
SR	14	Gadag PS	M/s Serentica Renewables India 3 Private Limited (Gadag)	Wind	34.65	470	08.10.2025
	15	Karur PS	M/s TP VARDHAMAN SURYA LIMITED (KARUR)	Wind	50	198	11.10.2025
	16	Karur PS	M/s TP VARDHAMAN SURYA LIMITED (KARUR)	Wind	50	198	15.10.2025
	17	Gadag PS	M/s Renew Surya Roshini Pvt Ltd (Gadag)	Wind	6.6	300	24.10.2025
NR	18	Fatehgarh_III	Energizent Power Private Limited	Solar	69	250	29.10.2025
			Total Thermal Generation addition		**0**		
			Total Hydro Generation addition		**0**		
			Total Solar Generation addition		**466**		
			Total Wind Generation addition		**318**		

Interconnecting/Generator/Station Transformers

REGION	S.NO.	Agency/Owner	Sub-Station	ICT No.	Voltage Level (kV)	Capacity (MVA)	DATE
ER	1	JSL(Jindal steel Limited)	Angul Captive Power Plant-II	ST-1	400/11	80	25.10.2025
SR	2	M/s SAEL SOLAR MHP2 PRIVATE LIMITED	SAEL SOLAR MHP2	ICT-1	220/33/33	160	30.10.2025
	3	M/s SAEL SOLAR MHP2 PRIVATE LIMITED	SAEL SOLAR MHP2	ICT-2	220/33/33	160	30.10.2025
	4	M/s Powergrid	Kurnool III Pooling Station	ICT-5	400 /220 /33	500	10.10.2025
NR	5	PNTL	Narela(PNTL)	ICT-1	765/400/33	1500	01.10.2025
	6	PNTL	Narela(PNTL)	ICT-2	765/400/33	1500	02.10.2025
	7	PNTL	Narela(PNTL)	ICT-3	756/400/33	1500	02.10.2025
	8	PSTCL	Dhanansu(PS)	ICT-2	400/220	500	15.10.2025
	9	PRTL	Fatehgarh_III(PG)	ICT-6	400/220/33	500	17.10.2025
	10	PSTCL	Nakodar(PSG)	ICT-1	400/220/33	315	17.10.2025
	11	Energizent_PPL	Energizent_PPL_FTG3	ICT-1	220/33	160	18.10.2025
	12	Energizent_PPL	Energizent_PPL_FTG3	ICT-2	220/33	160	18.10.2025
	13	PB_DAUSA_TL	DAUSA(PBDTL)	ICT-1	765/400/33	1500	18.10.2025
	14	NPCIL	RAPS_D(NP)	GT-8	400/21	855	24.10.2025
	15	POWERGRID	Bawana(DV)	ICT-3	400/220/33	500	27.10.2025
					Total (MVA)	**9890**	

NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
ER	1	JSL(Jindal steel Limited)	400KV-JSPL-ACPP II-1	4.7	Twin ACSR Moose	25.10.2025
	2	JSL(Jindal steel Limited)	400KV-JSPL-ACPP II-2	4.7	Twin ACSR Moose	25.10.2025
SR	3	SAEL SOLAR MHP1 PRIVATE LIMITED	220kV SAEL MHP2-Kurnool(PG)-3	26.5	AL-59 Moose	30.10.2025
	4	TGTRANSCO	400kV Choutuppal-YTPP-1	92.4	ACSR Moose	27.10.2025
	5	TGTRANSCO	400kV Choutuppal-YTPP-2	92.4	ACSR Moose	27.10.2025
NR	6	Energizent_PPL	220kV Energizent_PPL_FTG3-Fatehgarh_III(PG)-1	10.4	HTLS	17.10.2025
			Total length (km)	**231.1**		

ANTI-THEFT CHARGING OF NEW TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name	Length (KM)	Conductor Type	DATE
ER	1	SJVN	400KV-BUXAR-NAUBATPUR-1	125.45	Moose conductor	45947.68889
NR	2	POWERGRID	400kV Kishenpur(PG)-Kishtwar(GIS)-1	120.634	Quad Moose	45947
WR	3	POWERGRID Khavda II B Transmission Limited	765 kV Ahmadabad-Lakadiya-1	56	AL59 Zebra 85C	18.10.2025
			Total length (km)	**302.1**		

LILO/RE-ARRANGEMENT OF EXISTING TRANSMISSION LINES

REGION	S.NO.	Agency/Owner	Line Name/LILO at	Length (KM)	Conductor Type	DATE
SR	1	M/s KPTCL	220 KV Hassan (PG)-Dudda Line-1 (After LILO of 220 kV Hassan (PG)-Shivamoga Line-1 at 220 kV Dudda)	21.16	Drake	30.10.2025
ER	2	PGCIL ER-I	400KV-FSTPP-GOKARNA (New Purnea bypass temporarily)	299.5	Snow Birds	02.10.2025
NR	3	PNTL	765kV Bhiwani(PG)-Narela(PNTL)-1(After LILO of 765kV Meerut-Bhiwani at Narela(PNTL))	122.34	Hexa Zebra	01.10.2025
	4	POWERGRID	765kV Meerut(PG)-Narela(PNTL)-1 (After LILO of 765kV Meerut-Bhiwani at Narela(PNTL))	124.34	Hexa Zebra	01.10.2025
	5	HVPNL	220kV Sonipat(PG)-Mohana(HV)-3 (After LILO of 220kV Mohana - Samalkha Ckt-1&2 at 400kV Sonipat PG)	3.5	MOOSE	29.10.2025
	6	HVPNL	220kV Sonipat(PG)-Mohana(HV)-4 (After LILO of 220kV Mohana - Samalkha ckt-1&2 at 400kV Sonipat PG)	3.5	MOOSE	29.10.2025
	7	HVPNL	220kV Sonipat(PG)-Samalakha(HV)-1 (After LILO of 220kV Mohana - Samalkha ckt-1&2 at 400kV Sonipat PG)	31	MOOSE	29.10.2025

BUS/LINE REACTORS

REGION	S.NO.	Agency/Owner	Element Name	Voltage Level (kV)	Rating (MVAr)	DATE
SR	1	M/s Tamilnadu	125 MVAR, B/R-2 at Udangudi STPP	420	125	45947
WR	2	POWERGRID KPS2 Transmission System Limited	125 MVAR, B/R at 765/400 kV Khavda PS2	400	125	13.10.2025
	3	POWERGRID KPS2 B Transmission Limited	240 MVAR, L/R of 765 kV Lakadiya-Ahmedabad-2 at Ahmedabad	765	240	16.10.2025
NR	4	PNTL	765kV, 330 MVAR Bus Reactor 1 at Narela(PNTL)	765	330	01.10.2025
	5	POWERGRID	400kV, 125 MVAR Bus Reactor at Mandola(PG)	400	125	01.10.2025
	6	PNTL	400kV, 125 MVAR Bus Reactor 1 at Narela(PNTL)	400	125	03.10.2025
	7	PNTL	765kV, 330 MVAR Bus Reactor 2 at Narela(PNTL)	765	330	03.10.2025
	8	PKATL	400kV, 125 MVAR Bus Reactor 125 MVAR Bus-Reactor-3 at Kala Amb(PKTL)	400	125	19.10.2025
	9	PB_DAUSA_TL	400kV, 125 MVAR Bus Reactor 2 at DAUSA(PBDTL)	400	125	29.10.2025
	10	PB_DAUSA_TL	400kV, 125 MVAR Bus Reactor 1 at DAUSA(PBDTL)	400	125	29.10.2025
	11	POWERGRID	50 MVAR Non-Switchable Convertable LINE_REACTOR of 400 KV Ballabgarh-Manipuri-2	400	50	17.10.2025
				Total (MVAr)	**1825**	

HVDC /AC Filter bank / FACTS DEVICE associated System

REGION	S.NO.	Agency/Owner	Element Name	SUB-STATION	Voltage Level (kV)	DATE
		Nil				

22. Voltage Profile

विद्युत विभव रूपरेखा माह - अक्टूबर 2025 Voltage Profile - October 2025

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1		अंगुल ANGUL	0%	100%	0%	0%	0	790	741	768
2		दार्लिपली DARLIPALI	0%	100%	0%	0%	0	788	756	773
3		गया GAYA	0%	100%	0%	0%	0	788	749	771
4	पूर्वी क्षेत्र ER	जीरत JEERAT	0%	100%	0%	0%	0	787	738	763
5		झारसुगुड़ा JHARSUGUDA	0%	100%	0%	0%	0	798	761	780
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	787	746	769
7		राची RANCHI	0%	100%	0%	0%	0	792	760	778
8		सासाराम SASARAM	0%	100%	0%	0%	0	788	746	772
1		आगरा AGRA	0%	100%	0%	0%	0	800	748	781
2		आगरा (फ़तेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	767	767	767
3		अजमेर AJMER	0%	96%	4%	4%	28	808	760	789
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	795	745	777
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	785	757	772
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	781	752	768
7		अंता ANTA	0%	100%	0%	0%	0	799	767	785
8		बलिया BALLIA	0%	100%	0%	0%	0	795	743	771
9		बारा BARA	0%	100%	0%	0%	0	786	754	773
10		भाडला BHADLA	0%	100%	0%	0%	1	802	762	787
11		भाडला-2 BHADLA-2	0%	100%	0%	0%	1	803	754	787
12		भिवानी BHIWANI	0%	100%	0%	0%	3	803	741	783
13		बीकानेर BIKANER	0%	100%	0%	0%	3	804	750	787
14		बरेली BAREILLY	0%	100%	0%	0%	0	798	742	779
15		चित्तौडगढ़ CHITTORGARH	0%	98%	2%	2%	14	810	751	784
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	816	751	783
17		फ़तेहपुर FATEHPUR	0%	100%	0%	0%	0	795	736	773
18	उत्तरी क्षेत्र NR	घाटमपुर GHATAMPUR	0%	100%	0%	0%	0	784	741	770
19		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	0	799	748	780
20		हापड़ HAPUR	0%	100%	0%	0%	0	799	740	777
21		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	788	739	770
22		झटिकरा JHATIKARA	0%	100%	0%	0%	0	801	741	780
23		कानपर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	797	741	775
24		खेतरी KHETRI	0%	94%	6%	6%	43	806	742	786
25		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	2	807	736	771
26		ललितपुर LALITPUR	0%	100%	0%	0%	0	771	738	760
27		लखनऊ LUCKNOW	0%	100%	0%	0%	0	793	740	773
28		मैनपुरी MAINPURI	0%	100%	0%	0%	0	784	734	766
29		मेरठ MEERUT	0%	100%	0%	0%	1	803	740	777
30		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	797	739	775
31		मोगा MOGA	0%	99%	1%	1%	8	805	738	784
32		ओबरा सी OBRA C	0%	100%	0%	0%	0	777	749	765
33		उरई ORAI	0%	98%	2%	2%	18	809	757	785
34		फागी PHAGI	0%	99%	1%	1%	7	805	758	786
35		रामपुर RAMPUR	0%	100%	0%	0%	0	797	754	778
36		उन्नाव UNNAO	0%	100%	0%	0%	0	788	740	769
37		वाराणसी VARANASI	0%	100%	0%	0%	0	796	754	778
1		अकोला AKOLA	0%	100%	0%	0%	0	800	736	772
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	1	804	739	775
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	798	732	771
4		भुज BHUJ	0%	100%	0%	0%	0	799	743	775
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	797	739	773
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	786	749	769
7		बीना BINA	0%	100%	0%	0%	3	805	749	780
8		बनसकंठा BANASKANTHA	0%	99%	1%	1%	7	808	746	782
9		चापा CHAMPA	0%	93%	7%	7%	55	806	761	788
10		धले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	800	739	774
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	784	753	770
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	793	754	777
13		एकतनी EKTUNI	0%	100%	0%	0%	0	800	736	771
14		गदरवाड़ा GADARWARA	0%	99%	1%	1%	9	805	759	784
15		ग्वालियर GWALIOR	0%	99%	1%	1%	4	805	750	782
16		इंदौर INDORE	0%	100%	0%	0%	0	799	737	771
17		जबलपुर JABALPUR	0%	97%	3%	3%	26	807	757	785
18	पश्चिमी क्षेत्र WR	खडवा KHANDWA	0%	100%	0%	0%	0	801	742	774
19		कोरडी KORADI	0%	100%	0%	0%	0	788	745	769
20		लकाडिया LAKADIYA	0%	98%	2%	2%	11	806	751	784
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	796	762	782
22		पड़घे PADGHE	0%	100%	0%	0%	2	805	738	775
23		परली PARLI	0%	99%	1%	1%	5	805	755	783
24		पणे PUNE	0%	99%	1%	1%	9	809	741	779
25		राजनन्दगाँव RAJNANDGAON	0%	97%	3%	3%	25	807	758	785
26		सासन SASAN	0%	100%	0%	0%	0	797	764	782
27		सतना SATNA	0%	97%	3%	3%	25	805	762	786
28		सिवनी SEONI	0%	100%	0%	0%	1	803	749	779
29		सीपत SIPAT	0%	100%	0%	0%	0	785	752	770
30		सोलापर SOLAPUR	0%	100%	0%	0%	2	803	752	781
31		तिरोड़ा TIRORA	0%	100%	0%	0%	0	783	748	766
32		तामनार TAMNAR	0%	100%	0%	0%	0	794	762	780
33		वड़ोदरा VADODARA	0%	99%	1%	1%	9	805	744	782
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	800	765	784
35		वर्धा WARDHA	0%	99%	1%	1%	10	809	748	782
36		वरोरा WARORA	0%	100%	0%	0%	3	803	741	782
1		अरियलर ARIYALUR	0%	98%	2%	2%	13	805	753	785
2		कड़पा CUDDAPAH	0%	89%	11%	11%	79	810	755	786
3		चिल्कलूरीपेट CHILAKALURIPETA	0%	100%	0%	0%	0	801	738	778
4		कर्नल KURNOOL	0%	100%	0%	0%	0	799	753	778
5		महेश्वरम MAHESWARAM	0%	99%	1%	1%	7	804	751	782
6	दक्षिणी क्षेत्र SR	निज़ामाबाद NIZAMABAD	0%	92%	8%	8%	59	808	758	789
7		नेल्लर पलिंग NELLORE PS	0%	100%	0%	0%	0	795	756	776
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	100%	0%	0%	0	799	739	777
9		रायचर RAICHUR	0%	100%	0%	0%	0	800	700	780
10		श्रीकाकलम SRIKAKULAM	0%	99%	1%	1%	4	805	742	778
11		तिरुवलम THIRUVALEM	0%	100%	0%	0%	0	797	742	774
12		वेमगिरी VEMAGIRI	0%	100%	0%	0%	0	800	745	778
13		वारगल WARANGAL	0%	100%	0%	0%	0	796	754	768
1		बालिपारा BALIPARA (400 kV)	0%	100%	0%	0%	0	412	395	403
2		बिस्वनाथ चरिआलि BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	413	394	401
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	416	400	407
4		बोंगाईगाव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	418	401	409
5		इम्फ़ाल IMPHAL (400 kV)	0%	100%	0%	0%	0	414	393	403
6		बर्निहाट BYRNIHAT (400 kV)	0%	100%	0%	0%	0	419	398	409
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	414	395	403
8	पूर्वोत्तर क्षेत्र NER	अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	410	400	406
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	412	393	402
10		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	414	395	404
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	415	392	404
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	414	401	407
13		पुर्बकंचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	413	394	403
14		रंगानदी RANGANADI (400 kV)	0%	100%	0%	0%	0	418	397	406
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	416	398	407
16		सुर्ज्यामणिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	412	392	402
17		थौबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	412	385	401

All listed stations are 765 kV stations unless otherwise mentioned

***Percentage is calculated w.r.t. Time of one month.**

23. ALL TIME HIGHEST

31-10-2025

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	91215 19-06-2024	84151 14-06-2025	2023 12-06-2025	443 01-08-2023	86 07-08-2023	228 22-04-2025
WR	80000 08-02-2025	71713 24-04-2025	1742 25-04-2025	167 18-12-2014	319 29-07-2025	160.2 24-04-2025
SR	69942 21-03-2025	55925 28-03-2025	1458 28-03-2025	208 31-08-2018	342 26-07-2025	155.5 06-03-2025
ER	33452 23-07-2025	31508 22-07-2025	704 23-07-2025	157 14-09-2022	-	4.76 02-05-2025
NER	4159 26-09-2025	4065 23-07-2025	82 24-07-2025	46 15-08-2025	-	2.4 22-06-2022
All India	250070 30-05-2024	232191 09-06-2025	5466 30-05-2024	892 21-08-2025	673 29-07-2025	534 23-04-2025

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	17171	05-07-2025	366.8	21-07-2024
	Haryana	14524	31-07-2024	293.4	19-06-2024
	Rajasthan	18985	12-02-2025	388.0	11-06-2025
	Delhi	8568	18-06-2024	177.7	18-06-2024
	UP	30632	11-06-2025	658.8	17-06-2024
	Uttarakhand	2910	11-06-2025	62.4	12-06-2025
	HP	2273	17-01-2025	42.6	11-06-2025
	J&K(UT) and Ladakh(UT)	3200	07-01-2025	70.3	04-02-2025
	Chandigarh	460	12-06-2025	9.3	12-06-2025
	Railways_NR_ISTS	-	-	-	-
WR	Chhattisgarh	6798	25-04-2025	153.3	25-04-2025
	Gujarat	26457	14-06-2025	529.8	13-06-2025
	MP	18888	20-12-2024	353.8	14-02-2025
	Maharashtra	30675	13-03-2025	689.0	24-04-2025
	Goa	864	14-05-2025	18.4	06-05-2025
	DD & DNH	1411	22-07-2025	32.7	18-07-2025
	AMNSIL	1083	10-01-2024	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13712	04-05-2024	263.8	16-06-2023
	Telangana*	17162	20-03-2025	339.2	18-03-2025
	Karnataka	18395	07-03-2025	359.2	19-03-2025
	Kerala	5797	02-05-2024	116.1	03-05-2024
	Tamil Nadu	20830	02-05-2024	443.6	30-04-2024
	Pondy	548	14-07-2025	11.8	31-05-2024
ER	Bihar	8752	23-07-2025	186.8	24-07-2025
	DVC	3674	14-06-2024	81.2	22-04-2022
	Jharkhand	2406	13-06-2025	52.5	14-06-2025
	Odisha	7302	12-08-2025	148.5	19-04-2024
	West Bengal	13108	14-06-2025	268.2	14-06-2025
	Sikkim	137	11-01-2024	2.5	28-01-2020
	Railways_ER_ISTS	-	-	-	-
NER	Arunachal Pradesh	223	30-07-2025	4.3	23-07-2025
	Assam	2812	26-09-2025	57.8	24-07-2025
	Manipur	269	28-12-2024	4.2	10-01-2025
	Meghalaya	405	29-01-2024	7.8	31-01-2022
	Mizoram	168	29-01-2025	3.0	10-06-2025
	Nagaland	204	24-07-2025	4.0	18-07-2025
	Tripura	386	04-05-2024	7.4	22-07-2025
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

24. System Reliability Indices Report for the month of Oct 2025

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	20	5.00	0.80
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.
